

Zone 2A


Zone 2B & 2C

Activity ID	Activity Name	Dur	Baseline Start	Baseline Finish	Forecast/Actual Start	Forecast/Actual Finish	2021											
							August					September			October			
							25	01	08	15	22	29	05	12	19	26	03	10

Piling for Integrated Basement and U/G Road in Zone 2B & 2C						
Contract Period						
00	Contract Commencement of the Works	0	23-Jul-21		23-Jul-21	
Access / Return Dates						
AC030	Late Access Date of Portion B5-B7,B13-B15, B19-B21, B27, B28, B30-B32 (30 days after Commencement)	0	22-Aug-21		22-Aug-21	
AC060	Late Access Date of Portion B36,B40 (60 days after Commencement)	0	21-Sep-21		21-Sep-21	
AC070	Late Access Date of Portion B4,B11(70 days after Commencement)	0	01-Oct-21		01-Oct-21	
AC090	Latest Access Date of Portion B22-B26,B29,B38,B39 (90 days after Commencement)	0	21-Oct-21		21-Oct-21	
Access Date of Site Portion (Non-optional Works)						
ACB05	Access to Site Portion B05	0	22-Aug-21		22-Aug-21	
ACB06	Access to Site Portion B06	0	22-Aug-21		22-Aug-21	
ACB07	Access to Site Portion B07	0	22-Aug-21		22-Aug-21	
ACB13	Access to Site Portion B13	0	22-Aug-21		22-Aug-21	
ACB14	Access to Site Portion B14	0	22-Aug-21		22-Aug-21	
ACB15	Access to Site Portion B15	0	22-Aug-21		22-Aug-21	
ACB19	Access to Site Portion B19	0	22-Aug-21		22-Aug-21	
ACB20	Access to Site Portion B20	0	22-Aug-21		22-Aug-21	
ACB21	Access to Site Portion B21	0	22-Aug-21		22-Aug-21	
ACB27	Access to Site Portion B27	0	22-Aug-21		22-Aug-21	
ACB28	Access to Site Portion B28	0	22-Aug-21		22-Aug-21	
ACB29	Access to Site Portion B29	0	22-Aug-21		22-Aug-21	
ACB30	Access to Site Portion B30	0	22-Aug-21		22-Aug-21	
ACB31	Access to Site Portion B31	0	22-Aug-21		22-Aug-21	
ACB32	Access to Site Portion B32	0	22-Aug-21		22-Aug-21	
ACB35	Access to Site Portion B35 (To be agreed with the Zone 2A contractor)	0	22-Aug-21		22-Aug-21	
ACB36	Access to Site Portion B36	0	21-Sep-21		21-Sep-21	
ACB40	Access to Site Portion B40	0	21-Sep-21		21-Sep-21	
ACB11	Access to Site Portion B11	0	01-Oct-21		01-Oct-21	
ACB04	Access to Site Portion B04	0	01-Oct-21		01-Oct-21	
ACB22	Access to Site Portion B22	0	21-Oct-21		21-Oct-21	
ACB23	Access to Site Portion B23	0	21-Oct-21		21-Oct-21	
ACB38	Access to Site Portion B38	0	21-Oct-21		21-Oct-21	
ACB39	Access to Site Portion B39	0	21-Oct-21		21-Oct-21	
Access Date of Site Portion (only applicable if Optional Works Item No. 3 is instructed)						
ACB05a	Access to Site Portion B05a	0	22-Aug-21		22-Aug-21	
ACB06a	Access to Site Portion B06a	0	22-Aug-21		22-Aug-21	
ACB07a	Access to Site Portion B07a	0	22-Aug-21		22-Aug-21	
ACB30a	Access to Site Portion B30a	0	22-Aug-21		22-Aug-21	
ACB31a	Access to Site Portion B31a	0	22-Aug-21		22-Aug-21	
ACB32a	Access to Site Portion B32a	0	22-Aug-21		22-Aug-21	
ACB36a	Access to Site Portion B36a	0	21-Sep-21		21-Sep-21	
ACB40a	Access to Site Portion B40a	0	21-Sep-21		21-Sep-21	
ACB04a	Access to Site Portion B04a	0	01-Oct-21		01-Oct-21	



Mobilization Stage						
General Submission						
25	Pre-construction Condition Survey (50m from Site Boundary)	91	23-Jul-21	21-Oct-21	23-Jul-21A	21-Oct-21
29	Public Relations Plan Submission	91	23-Jul-21	21-Oct-21	23-Jul-21A	21-Oct-21
28	Construction Noise Permit (CNP)	91	23-Jul-21	21-Oct-21	23-Jul-21A	21-Oct-21
26	CCTV Inspection of Surrounding Pipelines/Drain	91	23-Jul-21	21-Oct-21	23-Jul-21	21-Oct-21
30	Submission of Site Supervision Plan (SSP) for Foundation Works	91	23-Jul-21	21-Oct-21	23-Jul-21A	21-Oct-21
31	C&D Disposal Billing Account	91	23-Jul-21	21-Oct-21	23-Jul-21A	21-Oct-21
34	Submission of Environmental Management Plan and Approval of BEAM PLUS Coordinator	91	23-Jul-21	21-Oct-21	23-Jul-21A	21-Oct-21
33	Coordination with Zone 2A and Zone 3 Contractor	0	23-Jul-21	21-Oct-21	29-Jul-21A	29-Jul-21A
27	Underground Utilities Detection	78	23-Jul-21	21-Oct-21	05-Aug-21A	21-Oct-21
32	Submission of Method Statement to MTR for Approval	91	23-Jul-21	21-Oct-21	23-Jul-21	21-Oct-21
37	Submission of Method Statement for Bored Pile Works to CA for Approval	91	23-Jul-21	21-Oct-21	23-Jul-21A	21-Oct-21
34.1	Submission of Environmental Management Plan (EMP) and Waste Management Plan (WMP) for Approval	91	23-Jul-21	21-Oct-21	23-Jul-21A	21-Oct-21
30.1	Submission of Site Supervision Plan (SSP) for GI Works	21	23-Jul-21	21-Oct-21	10-Aug-21A	30-Aug-21
25.1	Submission of Method Statement for Pre-condition Condition Survey (Seawall) for Approval	39	23-Jul-21	21-Oct-21	23-Jul-21A	30-Aug-21
35	Submission of Baseline Work (1)	4	02-Aug-21	05-Aug-21	02-Aug-21A	05-Aug-21A
36	Submission of Baseline Work (2)	39	06-Aug-21	30-Sep-21	06-Aug-21A	13-Sep-21
25.2	Carrying Out Pre-condition Condition Survey (Seawall)	52	31-Aug-21	21-Oct-21	31-Aug-21	21-Oct-21
37.1	Submission of Method Statement for Socket H-Pile Works to CA for Approval	42	20-Sep-21	31-Oct-21	20-Sep-21	31-Oct-21
BD Submissions						
40	Obtain BD 1st Approval for Foundation Plan	0	23-Jul-21		23-Jul-21	
41	Bored Pile & Socket H-Pile Consent application	28	23-Jul-21	19-Aug-21	23-Jul-21	19-Aug-21
42	Submission of BA10 for Bored Pile & Socket H-Pile Works	7	13-Aug-21	19-Aug-21	13-Aug-21	19-Aug-21
Site Preparation Works						
50	Site Office Set Up	21	22-Aug-21	11-Sep-21	22-Aug-21	11-Sep-21
48	Initial Site Setting Out	14	22-Aug-21	04-Sep-21	22-Aug-21	04-Sep-21
49	General Site Clearance	21	22-Aug-21	11-Sep-21	22-Aug-21	11-Sep-21

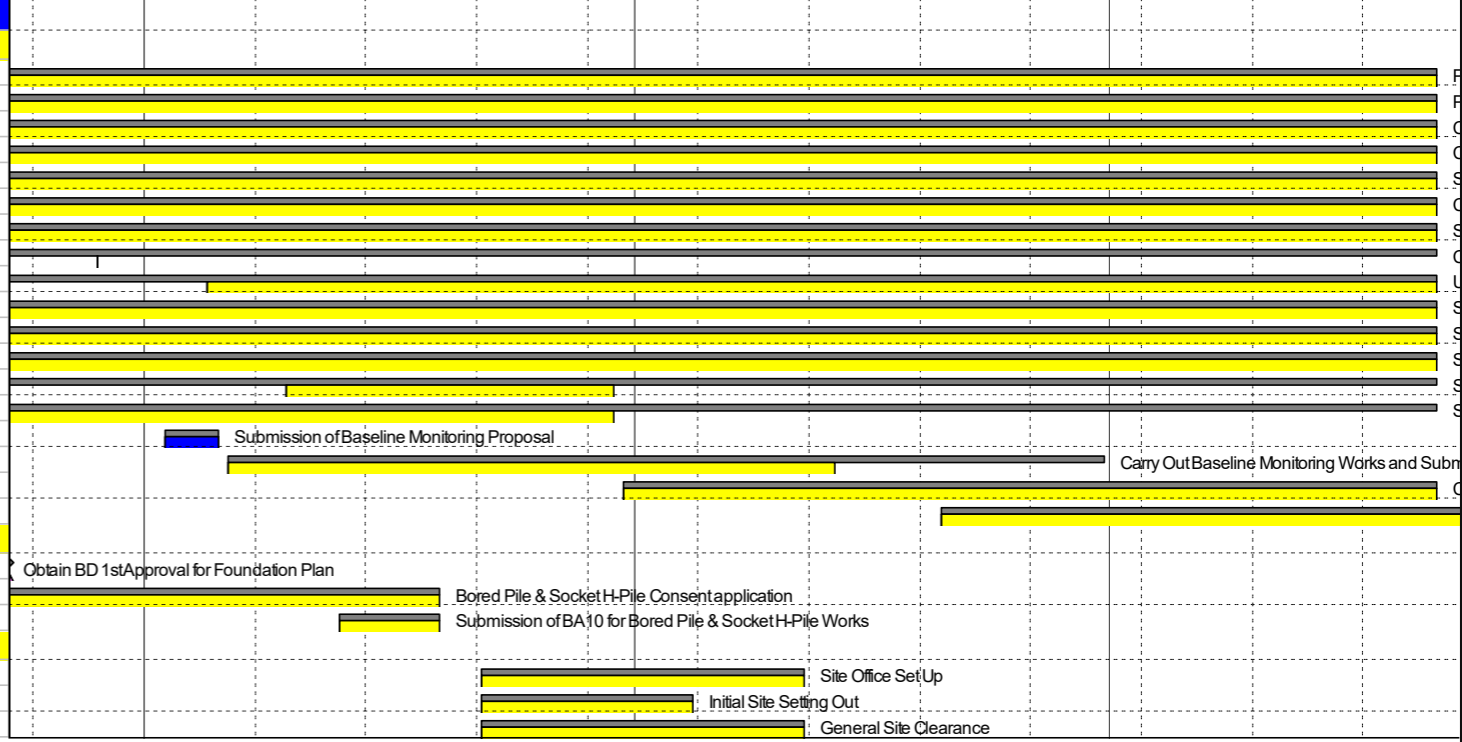

ID: 2B2C	BL MS	▲ Actual MS
Data Date: 23-Jul-21	▲ Critical Remaining Work	▲ Critical MS
Print Date: 23-Aug-21_19:09	■ Baseline	■ Remaining Work
Page 1 of 2	▲ MS	■ Actual Work(%Comp)

West Kowloon Cultural District District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
Three Month Rolling Programme (Rev.a)



Date	Revision	Check...	Approved
23-Aug-21	Rev a		

Activity ID	Activity Name	Dur	Baseline Start	Baseline Finish	Forecast/Actual Start	Forecast/Actual Finish	2021																	
							August				September				October									
							25	01	08	15	22	29	05	12	19	26	03	10	17					
51	Demarcate MTR Zone on Site	21	22-Aug-21	11-Sep-21	22-Aug-21	11-Sep-21																		
Monitoring Works																								
54	Apply XP or liaise with other parties for installation of monitoring outside site boundary	75	23-Jul-21	05-Oct-21	23-Jul-21	05-Oct-21																		
56	Carry Out MTR Condition Survey	30	23-Jul-21	21-Aug-21	23-Jul-21	21-Aug-21																		
53	Install monitoring Checkpoints	30	22-Aug-21	20-Sep-21	22-Aug-21	20-Sep-21																		
57	Install Monitoring Checkpoints within MTR Premises	28	22-Aug-21	18-Sep-21	22-Aug-21	18-Sep-21																		
55	Install Monitoring Checkpoint outside site boundary	14	06-Oct-21	19-Oct-21	06-Oct-21	19-Oct-21																		
58	Take Initial Reading of BD Monitoring Points	0	20-Oct-21		20-Oct-21																			
Hoarding Works																								
60	Hoarding Erection / Modification (Stage 1)	30	21-Aug-21	19-Sep-21	21-Aug-21	19-Sep-21																		
61	Hoarding Erection / Modification (Stage 2)	30	21-Oct-21	19-Nov-21	21-Oct-21	19-Nov-21																		
Construction Stage																								
Section 1 Works																								
KD01 (Stage 1-1) Bored Pile (Northern Part of East Access Road- 6 nos. 2m dia & 10 nos. 3m dia)																								
69	Predrilling	71	30-Sep-21	09-Dec-21	21-Sep-21	09-Dec-21																		
Section 3 Works																								
KD03 (Stage 3-1) Bored Pile (Northern Part of West Access Road- 4 nos. 2m dia & 12 nos. 3m dia)																								
111	Predrilling	11	21-Oct-21	31-Oct-21	21-Oct-21	31-Oct-21																		
Section 4 Works																								
KD04 (Stage 4-1) Bored Pile (Southern Part of West Access Road- 12 nos. 3m dia)																								
136	Predrilling	10	21-Oct-21	30-Oct-21	21-Oct-21	30-Oct-21																		
KD04 Socketed H Pile Works (80 nos.)																								
142	Predrilling	50	16-Oct-21	04-Dec-21	16-Oct-21	04-Dec-21																		

◆	◆	▲	▲
◆	◆	▲	▲
◆	◆	▲	▲
◆	◆	▲	▲

◆ BL MS ◆ Actual MS
 ■ Critical Remaining Work ▲ Critical MS
 ■ Baseline ■ Remaining Work
 ▲ MS ■ Actual Work(%Comp)

West Kowloon Cultural District District Authority
 Piling for Integrated Basement and U/G Road in Zone 2B 2C
Three Month Rolling Programme (Rev.a)



Date	Revision	Check...	Approved
23-Aug-21	Rev a		
