

Zone 2A

Project Name: Foundation and ELS Works for Integrated Basement and Underground Road in Zone 2A of the West Kowloon Cultural District

3-Month Rolling Programme

Activity Description	Duration (Cal. Day)	Start Date	Finish Date	2021				2022															
				December				January				February											
				10 W83	17 W84	24 W85	31 W86	7 W87	14 W88	21 W89	28 W90	4 W91	11 W92	18 W93	25 W94								
Zone 2A-1 Foundation, ELS Works and Blinding to Formation (KD01)																							
ELS (Stage 1) - Grouting / Pipe Pile Works																							
King Post (8/64 Nos Completed) & Erection of Steel Column for Working Platform (13/41 Nos completed)	342	15-May-21	21-Apr-22																				
Socketed H-Pile Works																							
Remaining Socketed H-Pile Works (27/53 Nos completed)	218	16-Jun-21	19-Jan-22																				
Zone 2A-2 Foundation, ELS Works and Blinding to Formation (KD02)																							
Bored Pile Works																							
Additional Bored Pile Construction (Total 16 Nos.) BP15Y, BP16TA, BP13U, BP14Y, BP12M, BP12T, BP20XA, BP12Y, BP13Y, BP16WA, BP12K, BP13W, BP12P, BP12JA, BP12E, BP17Y (14 Nos. Cast; 1 Nos. completed RCD)	290	23-Mar-21	6-Jan-22																				
ELS (Stage 1) - Grouting / Pipe Pile Works																							
King Post (0/86 Nos Completed) & Erection of Steel Column for Working Platform (0/65 Nos Completed)	208	18-Dec-21	13-Jul-22																				
Stage 1a & 1b grouting (915/940 Nos Completed)	478	22-Oct-20	11-Feb-22																				
Pipe Pile Construction (411/457 Nos Completed)	591	17-Nov-20	30-Jun-22																				

- Actual
- Remaining Works
- Critical Remaining Works

Zone 2B & 2C

Activity ID	Activity Name	CMWP 4th Draft Start	CMWP 4th Draft Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	December				January				February				March			
									-1				1				2				3			
									03	10	17	24	31	07	14	21	28	04	11	18	25	04	11	18

Piling for Integrated Basement and U/G Road in Zone 2B & 2C

Contract Dates

Key Dates

KD for Zone 2C

Activity ID	Activity Name	CMWP 4th Draft Start	CMWP 4th Draft Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete
KD02	KD02 (Stage 5-1) - 200 days after Commencement (7 Feb 2022)		06-Feb-22	0		18-Feb-22*	-11	0%

Access Dates of Site Portion

120 days after Commencement

Activity ID	Activity Name	CMWP 4th Draft Start	CMWP 4th Draft Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete
ACB02	Access to Site Portion B02	19-Nov-21		0	03-Dec-21 A			100%
ACB08	Access to Site Portion B08	19-Nov-21		0	02-Dec-21 A			100%
ACB09	Access to Site Portion B09	19-Nov-21		0	03-Dec-21 A			100%
ACB10	Access to Site Portion B10	19-Nov-21		0	01-Jan-22		39	0%
ACB37	Access to Site Portion B37	19-Nov-21		0	03-Dec-21 A			100%

150 days after Commencement

Activity ID	Activity Name	CMWP 4th Draft Start	CMWP 4th Draft Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete
ACB34	Access to Site Portion B34	19-Dec-21		0	01-Jan-22		82	0%

Mobilization Stage

Temporary Services and Site Facilities Installation Dates

Activity ID	Activity Name	CMWP 4th Draft Start	CMWP 4th Draft Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete
MOBP.04.1100	Water Meter Application (WSD)	23-Jul-21	30-Nov-21	162	23-Jul-21 A	01-Jan-22	107	100%
MOBP.04.1120	Electrical Meter Application (CLP Group)	23-Jul-21	30-Nov-21	162	23-Jul-21 A	01-Jan-22	107	100%

Major Construction Information and Drawings Requirement Dates

Activity ID	Activity Name	CMWP 4th Draft Start	CMWP 4th Draft Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete
MOBP.05.1100	Approval of Foundation Plan (1st Amendment)	20-Nov-21	17-Dec-21	45	23-Nov-21 A	07-Jan-22	142	77.23%

Statutory Procedures and Consents

EPD



Activity ID	Activity Name	CMWP 4th Draft Start	CMWP 4th Draft Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	December				January				February				March			
									-1				1				2				3			
									03	10	17	24	31	07	14	21	28	04	11	18	25	04	11	18

MOBP.06.1100	Application and Approval of Construction Noise Permit	26-Jul-21	30-Nov-21	159	26-Jul-21 A	01-Jan-22	102	100%
--------------	---	-----------	-----------	-----	-------------	-----------	-----	------

Major Resources Procurement for the Early Works

MOBP.07.1080	Steel Rebar Delivery (1st Batch), Testing of Rebar and Approval of Rebar	05-Oct-21	18-Nov-21	88	05-Oct-21 A	01-Jan-22	87	100%
MOBP.07.1120	Preparation and Submission of Structural Steel H-Pile for Socketed H-Piling Works	23-Jul-21	18-Oct-21	162	23-Jul-21 A	01-Jan-22	57	100%

Pre-construction Submission for Mobilization

General Submission

MOBP.08.1140	Approval of Site Management Plan	22-Aug-21	04-Oct-21	132	22-Aug-21 A	01-Jan-22	47	100%
--------------	----------------------------------	-----------	-----------	-----	-------------	-----------	----	------

Method Statement of Site Works

MOBP.08.1660	Approval of Method Statement for Large Diameter Bored Pile Construction (MTR Protection Zone)	28-Jul-21	04-Oct-21	157	28-Jul-21 A	01-Jan-22	47	100%
--------------	---	-----------	-----------	-----	-------------	-----------	----	------

Site Mobilization Works

Pre-Construction Works before Piling Commencement

MOBP.10.1120	Site Clearance	23-Jul-21	30-Apr-22	303	23-Jul-21 A	21-May-22	117	50%
MOBP.10.1200	Installation of Monitoring Check Points (Stage 2) [33 nos.]	20-Nov-21	08-Dec-21	19	01-Jan-22	19-Jan-22	89	0%
MOBP.10.1220	Installation of Monitoring Check Points (Extensometer)	11-Oct-21	13-Nov-21	55	20-Nov-21 A	13-Jan-22	76	50%
MOBP.10.1260	Erection of Hoardings (Stage 2)	20-Dec-21	31-Jan-22	38	01-Jan-22	07-Feb-22	130	0%
MOBP.10.1300	Trial Pit for Drillholes & Removal of Existing Substructures / Ground Slab [503 nos]	19-Aug-21	30-Apr-22	255	19-Aug-21 A	30-Apr-22	137	65%

Construction Stage


Pile Construction

Initial Mobilization

	Planned Bar		Milestone
	Critical Bar		Critical MS
	Baseline		Baseline MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 31 Dec 2021
Based on CMWP 4th Draft

Date	Revision	Checked	Approved
06-Aug-21	1st Draft	KL	N
29-Sep-21	2nd Draft	KL	N
25-Oct-21	3rd Draft	KL	C
26-Nov-21	4th Draft	KL	



Activity ID	Activity Name	CMWP 4th Draft Start	CMWP 4th Draft Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	December				January				February				March			
									-1				1				2				3			
									03	10	17	24	31	07	14	21	28	04	11	18	25	04	11	18

MO.1010	Initial Mobilization for Predrilling of BP (CCD / KD05 / KD01)	23-Jul-21	07-Sep-21	174	23-Jul-21 A	21-Feb-22	68	80%	
MO.1020	Initial Mobilization for Predrilling of BP (CCE / KD06)	23-Jul-21	07-Sep-21	174	23-Jul-21 A	21-Feb-22	202	50%	
MO.1030	Initial Mobilization for Predrilling of BP (CCF / KD07 / KD03)	23-Jul-21	07-Sep-21	174	23-Jul-21 A	21-Feb-22	152	85%	
MO.1040	Initial Mobilization for Predrilling of BP (CCG / KD08 / KD04)	23-Jul-21	07-Sep-21	134	23-Jul-21 A	03-Jan-22	192	90%	
MO.1050	Initial Mobilization for Predrilling of BP (CCH / KD09 / KD02)	23-Jul-21	07-Sep-21	144	23-Jul-21 A	13-Jan-22	18	60%	

Predrilling

PD.1000	Predrilling for BP in KD01 [8 nos.]	30-Sep-21	30-Mar-22	148	30-Sep-21 A	30-Mar-22	24	87%	
PD.1020	Predrilling for BP in KD02 [4 nos.]	19-Nov-21	23-Dec-21	36	30-Nov-21 A	13-Jan-22	18	75%	
PD.1040	Predrilling for BP in KD03 [5 nos.]	20-Oct-21	06-May-22	160	20-Oct-21 A	06-May-22	93	80%	
PD.1060	Predrilling for BP in KD04 [3 nos.] incl. 1 additional no.	30-Sep-21	30-Mar-22	143	30-Sep-21 A	31-Mar-22	113	66%	
PD.1080	Predrilling for BP in KD05 [76 nos.]	30-Sep-21	30-Mar-22	149	30-Sep-21 A	31-Mar-22	29	55%	
PD.1100	Predrilling for BP in KD06 [95 nos.] incl. 5 additional nos.	30-Sep-21	23-May-22	187	30-Sep-21 A	23-May-22	119	40%	
PD.1120	Predrilling for BP in KD07 [90 nos.] incl. 2 additional nos.	30-Sep-21	23-May-22	188	30-Sep-21 A	24-May-22	210	71%	
PD.1140	Predrilling for BP in KD08 [74 nos.] incl. 1 additional no.	30-Sep-21	30-Mar-22	148	30-Sep-21 A	31-Mar-22	142	95%	
PD.1160	Predrilling for BP in KD09 [149 nos.] incl. 4 additional nos.	30-Sep-21	30-Mar-22	149	30-Sep-21 A	30-Mar-22	157	48%	
PD.1170	Predrilling for SSHP [12 nos.]	30-Sep-21	22-Oct-21	37	01-Dec-21 A	31-Jan-22 A		100%	

KD01 (Stage 1-1)

Bored Piles									
CD01									
02									
P23-BP22.20	BP - RCD Drilling	23-Dec-21	17-Jan-22	17	27-Nov-21 A	17-Dec-21 A		100%	
P23-BP22.30	BP - Airlift, Cage Install and Concrete	18-Jan-22	26-Jan-22	17	18-Dec-21 A	10-Jan-22	101	12.5%	
CD07									
01									
CBA-BPC41K.10	BP - Excavation	19-Jan-22	25-Jan-22	6	19-Jan-22	25-Jan-22	14	0%	

ID: 2B2C-20211231_bw
 Data Date: 01-Jan-22
 Print Date: 03-Jan-22_14:19
 Page 3 of 20

- Planned Bar
- Critical Bar
- Baseline
- Milestone
- Critical MS
- Baseline MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 31 Dec 2021
 Based on CMWP 4th Draft



Date	Revision	Checked	Approved
06-Aug-21	1st Draft	KL	N
29-Sep-21	2nd Draft	KL	N
25-Oct-21	3rd Draft	KL	C
26-Nov-21	4th Draft	KL	

Activity ID	Activity Name	CMWP 4th Draft Start	CMWP 4th Draft Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	December				January				February				March			
									-1				1				2				3			
									03	10	17	24	31	07	14	21	28	04	11	18	25	04	11	18

01									
P23-BP76.10	BP - Excavation	03-Dec-21	09-Dec-21	11	24-Dec-21 A	08-Jan-22	-10	0%	
P23-BP76.20	BP - RCD Drilling	10-Dec-21	30-Dec-21	16	10-Jan-22	27-Jan-22	-10	0%	
P23-BP76.30	BP - Airlift, Cage Install and Concrete	31-Dec-21	10-Jan-22	8	28-Jan-22	09-Feb-22	-10	0%	

02									
P23-BP87.10	BP - Excavation	03-Dec-21	09-Dec-21	6	03-Jan-22	08-Jan-22	-10	0%	
P23-BP87.20	BP - RCD Drilling	10-Dec-21	10-Jan-22	24	10-Jan-22	09-Feb-22	-10	0%	
P23-BP87.30	BP - Airlift, Cage Install and Concrete	11-Jan-22	19-Jan-22	8	10-Feb-22	18-Feb-22	-10	0%	

03									
P23-BP117.10	BP - Excavation	03-Dec-21	09-Dec-21	6	03-Jan-22	08-Jan-22	-10	0%	
P23-BP117.20	BP - RCD Drilling	10-Dec-21	10-Jan-22	24	10-Jan-22	09-Feb-22	-10	0%	
P23-BP117.30	BP - Airlift, Cage Install and Concrete	20-Jan-22	28-Jan-22	8	10-Feb-22	18-Feb-22	-10	0%	

KD03 (Stage 3-1)

KD03.BP.0040	Review and Confirmation of Rockhead and Founding Level of Pile by CA	14-Nov-21	27-Nov-21	14	01-Jan-22	14-Jan-22	4	0%	
--------------	--	-----------	-----------	----	-----------	-----------	---	----	--

Bored Piles

VD02									
03									
P28&29-BP08.10	BP - Excavation	18-Mar-22	24-Mar-22	6	18-Mar-22	24-Mar-22	37	0%	
P28&29-BP08.20	BP - RCD Drilling	25-Mar-22	12-Apr-22	15	25-Mar-22	12-Apr-22	37	0%	


VD06									
01									
P28&29-BP29.10	BP - Excavation	19-Jan-22	25-Jan-22	6	19-Jan-22	25-Jan-22	0	0%	
P28&29-BP29.20	BP - RCD Drilling	26-Jan-22	15-Feb-22	15	26-Jan-22	15-Feb-22	0	0%	
P28&29-BP29.30	BP - Airlift, Cage Install and Concrete	16-Feb-22	23-Feb-22	7	16-Feb-22	23-Feb-22	80	0%	

VD09									
01									
CBA-BPC54Jb.10	BP - Excavation	26-Feb-22	04-Mar-22	6	26-Feb-22	04-Mar-22	0	0%	
CBA-BPC54Jb.20	BP - RCD Drilling	05-Mar-22	11-Apr-22	31	05-Mar-22	11-Apr-22	0	0%	

KD04 (Stage 4-1)

KD04.BP.0040	Review and Confirmation of Rockhead and Founding Level of Pile by CA	03-Nov-21	16-Nov-21	77	30-Oct-21 A	14-Jan-22	83	0%	
--------------	--	-----------	-----------	----	-------------	-----------	----	----	--

KD05 (Section 1)

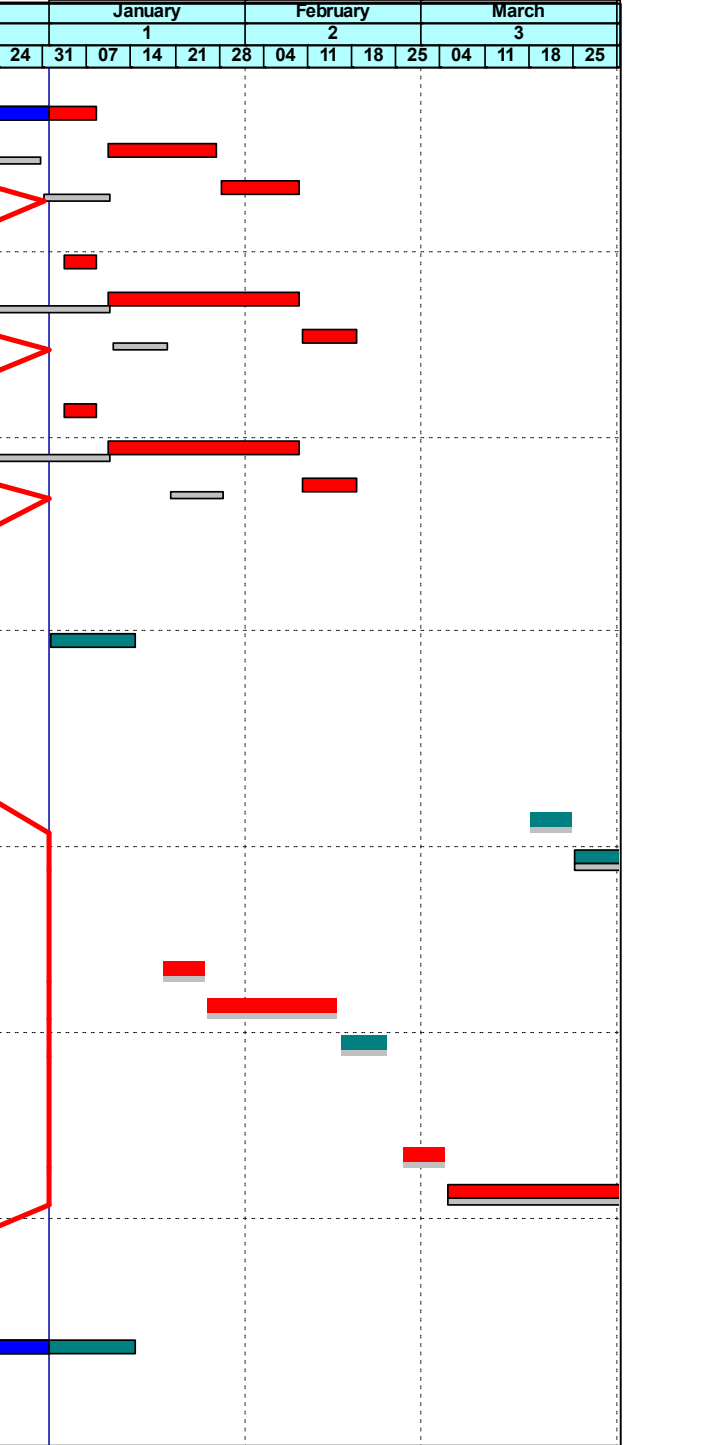

	Planned Bar		Milestone
	Critical Bar		Critical MS
	Baseline		Baseline MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 31 Dec 2021
Based on CMWP 4th Draft

Date	Revision	Checked	Approved
06-Aug-21	1st Draft	KL	N
29-Sep-21	2nd Draft	KL	N
25-Oct-21	3rd Draft	KL	C
26-Nov-21	4th Draft	KL	

Activity ID	Activity Name	CMWP 4th Draft Start	CMWP 4th Draft Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	December				January				February				March			
									-1				1				2				3			
									03	10	17	24	31	07	14	21	28	04	11	18	25	04	11	18


MO.1060	Initial Mobilization for BP (CCD / KD05 / KD01)	15-Sep-21	15-Nov-21	75	22-Oct-21 A	20-Jan-22	281	80%
---------	---	-----------	-----------	----	-------------	-----------	-----	-----

Trial Pile (P23-BP11 (Regular Pile))

CD03								
01								
P23-BP11.20	BP - RCD Drilling	01-Dec-21	22-Dec-21	11	25-Nov-21 A	08-Dec-21 A		100%
P23-BP11.30	BP - Airlift, Cage Install and Concrete	23-Dec-21	04-Jan-22	12	09-Dec-21 A	23-Dec-21 A		100%

Bored Piles

CD01								
01								
P23-BP30.10	BP - Excavation	29-Nov-21	04-Dec-21	33	03-Nov-21 A	11-Dec-21 A		100%
P23-BP30.20	BP - RCD Drilling	06-Dec-21	22-Dec-21	30	13-Dec-21 A	19-Jan-22	198	0%
P23-BP30.30	BP - Airlift, Cage Install and Concrete	23-Dec-21	03-Jan-22	7	20-Jan-22	27-Jan-22	198	0%
03								
P23-BP20.10	BP - Excavation	11-Jan-22	17-Jan-22	6	03-Jan-22	08-Jan-22	56	0%
P23-BP20.20	BP - RCD Drilling	18-Jan-22	07-Feb-22	15	10-Jan-22	26-Jan-22	56	0%
P23-BP20.30	BP - Airlift, Cage Install and Concrete	08-Feb-22	15-Feb-22	7	27-Jan-22	07-Feb-22	192	0%
07								
P23-BP19.10	BP - Excavation	12-Mar-22	18-Mar-22	6	05-Mar-22	11-Mar-22	55	0%
P23-BP19.20	BP - RCD Drilling	19-Mar-22	11-Apr-22	19	12-Mar-22	02-Apr-22	55	0%
08								
P23-BP32.10	BP - Excavation	04-Apr-22	11-Apr-22	6	28-Mar-22	02-Apr-22	55	0%
CD07								
02								
CBA-BPC43K.10	BP - Excavation	31-Jan-22	09-Feb-22	6	31-Jan-22	09-Feb-22	14	0%
CBA-BPC43K.20	BP - RCD Drilling	10-Feb-22	21-Feb-22	10	10-Feb-22	21-Feb-22	14	0%
CBA-BPC43K.30	BP - Airlift, Cage Install and Concrete	22-Feb-22	26-Feb-22	5	22-Feb-22	26-Feb-22	42	0%
03								
CBA-BPC44Jb.10	BP - Excavation	14-Feb-22	21-Feb-22	17	18-Dec-21 A	10-Jan-22	33	0%
CBA-BPC44Jb.20	BP - RCD Drilling	22-Feb-22	09-Mar-22	14	11-Jan-22	26-Jan-22	33	0%
CBA-BPC44Jb.30	BP - Airlift, Cage Install and Concrete	10-Mar-22	16-Mar-22	6	27-Jan-22	05-Feb-22	193	0%
04								
CBA-BPC40Ja.10	BP - Excavation	03-Mar-22	09-Mar-22	6	15-Feb-22	21-Feb-22	14	0%
CBA-BPC40Ja.20	BP - RCD Drilling	10-Mar-22	21-Mar-22	10	22-Feb-22	04-Mar-22	14	0%
CBA-BPC40Ja.30	BP - Airlift, Cage Install and Concrete	22-Mar-22	26-Mar-22	5	05-Mar-22	10-Mar-22	37	0%

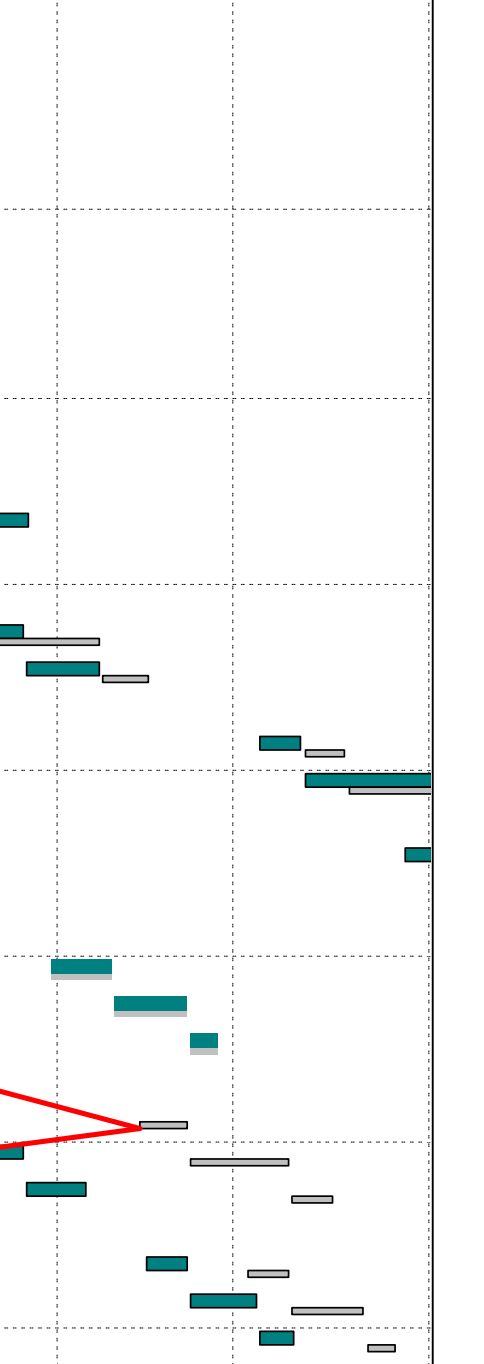

ID: 2B2C-20211231_bw
 Data Date: 01-Jan-22
 Print Date: 03-Jan-22_14:19
 Page 6 of 20

	Planned Bar		Milestone
	Critical Bar		Critical MS
	Baseline		Baseline MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 31 Dec 2021
 Based on CMWP 4th Draft

	Date	Revision	Checked	Approved
	06-Aug-21	1st Draft	KL	N
	29-Sep-21	2nd Draft	KL	N
	25-Oct-21	3rd Draft	KL	C
	26-Nov-21	4th Draft	KL	


Activity ID	Activity Name	CMWP 4th Draft Start	CMWP 4th Draft Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	December				January				February				March				
									-1				1				2				3				
									03	10	17	24	31	07	14	21	28	04	11	18	25	04	11	18	25
05																									
CBA-BPC42K.10	BP - Excavation	15-Mar-22	21-Mar-22	6	26-Feb-22	04-Mar-22	14	0%																	
CBA-BPC42K.20	BP - RCD Drilling	22-Mar-22	01-Apr-22	10	05-Mar-22	16-Mar-22	14	0%																	
CBA-BPC42K.30	BP - Airlift, Cage Install and Concrete	02-Apr-22	08-Apr-22	5	17-Mar-22	22-Mar-22	32	0%																	
06																									
CBA-BPC44K.10	BP - Excavation	25-Mar-22	01-Apr-22	7	09-Mar-22	16-Mar-22	14	0%																	
CBA-BPC44K.20	BP - RCD Drilling	02-Apr-22	22-Apr-22	14	17-Mar-22	01-Apr-22	14	0%																	
13																									
CBA-BP01.10	BP - Excavation	25-Mar-22	01-Apr-22	7	09-Mar-22	16-Mar-22	14	0%																	
CBA-BP01.20	BP - RCD Drilling	02-Apr-22	22-Apr-22	14	17-Mar-22	01-Apr-22	14	0%																	
CD05																									
01																									
P22&P19-BP04.10	BP - Excavation	19-Nov-21	25-Nov-21	6	03-Jan-22	08-Jan-22	187	0%																	
P22&P19-BP04.20	BP - RCD Drilling	26-Nov-21	17-Dec-21	19	10-Jan-22	31-Jan-22	187	0%																	
P22&P19-BP04.30	BP - Airlift, Cage Install and Concrete	18-Dec-21	29-Dec-21	8	04-Feb-22	12-Feb-22	187	0%																	
02																									
P22&P19-BP05.10	BP - Excavation	11-Dec-21	17-Dec-21	7	09-Dec-21 A	17-Dec-21 A		100%																	
P22&P19-BP05.20	BP - RCD Drilling	18-Dec-21	12-Jan-22	29	18-Dec-21 A	24-Jan-22	9	0%																	
P22&P19-BP05.30	BP - Airlift, Cage Install and Concrete	13-Jan-22	21-Jan-22	8	25-Jan-22	05-Feb-22	42	0%																	
03																									
P17-BP05.10	BP - Excavation	06-Jan-22	12-Jan-22	6	18-Jan-22	24-Jan-22	9	0%																	
P17-BP05.20	BP - RCD Drilling	13-Jan-22	29-Jan-22	15	25-Jan-22	14-Feb-22	9	0%																	
P17-BP05.30	BP - Airlift, Cage Install and Concrete	31-Jan-22	10-Feb-22	7	15-Feb-22	22-Feb-22	35	0%																	
06																									
P22&P19-BP15.10	BP - Excavation	12-Mar-22	18-Mar-22	6	02-Mar-22	08-Mar-22	9	0%																	
P22&P19-BP15.20	BP - RCD Drilling	19-Mar-22	11-Apr-22	19	09-Mar-22	30-Mar-22	9	0%																	
11																									
P22&P19-BP26.10	BP - Excavation	06-Jan-22	12-Jan-22	6	18-Jan-22	24-Jan-22	88	0%																	
P22&P19-BP26.20	BP - RCD Drilling	13-Jan-22	18-Feb-22	29	25-Jan-22	02-Mar-22	88	0%																	
P22&P19-BP26.30	BP - Airlift, Cage Install and Concrete	19-Feb-22	28-Feb-22	8	03-Mar-22	11-Mar-22	132	0%																	
13																									
P22&P19-BP25.10	BP - Excavation	07-Mar-22	12-Mar-22	6	18-Mar-22	24-Mar-22	88	0%																	
P22&P19-BP25.20	BP - RCD Drilling	14-Mar-22	04-Apr-22	19	25-Mar-22	20-Apr-22	88	0%																	
CD04																									
01																									
P17-BP03.10	BP - Excavation	24-Nov-21	30-Nov-21	6	03-Jan-22	08-Jan-22	38	0%																	
P17-BP03.20	BP - RCD Drilling	01-Dec-21	17-Dec-21	15	10-Jan-22	26-Jan-22	38	0%																	

Planned Bar	Milestone
Critical Bar	Critical MS
Baseline	Baseline MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 31 Dec 2021
 Based on CMWP 4th Draft



Date	Revision	Checked	Approved
06-Aug-21	1st Draft	KL	N
29-Sep-21	2nd Draft	KL	N
25-Oct-21	3rd Draft	KL	C
26-Nov-21	4th Draft	KL	

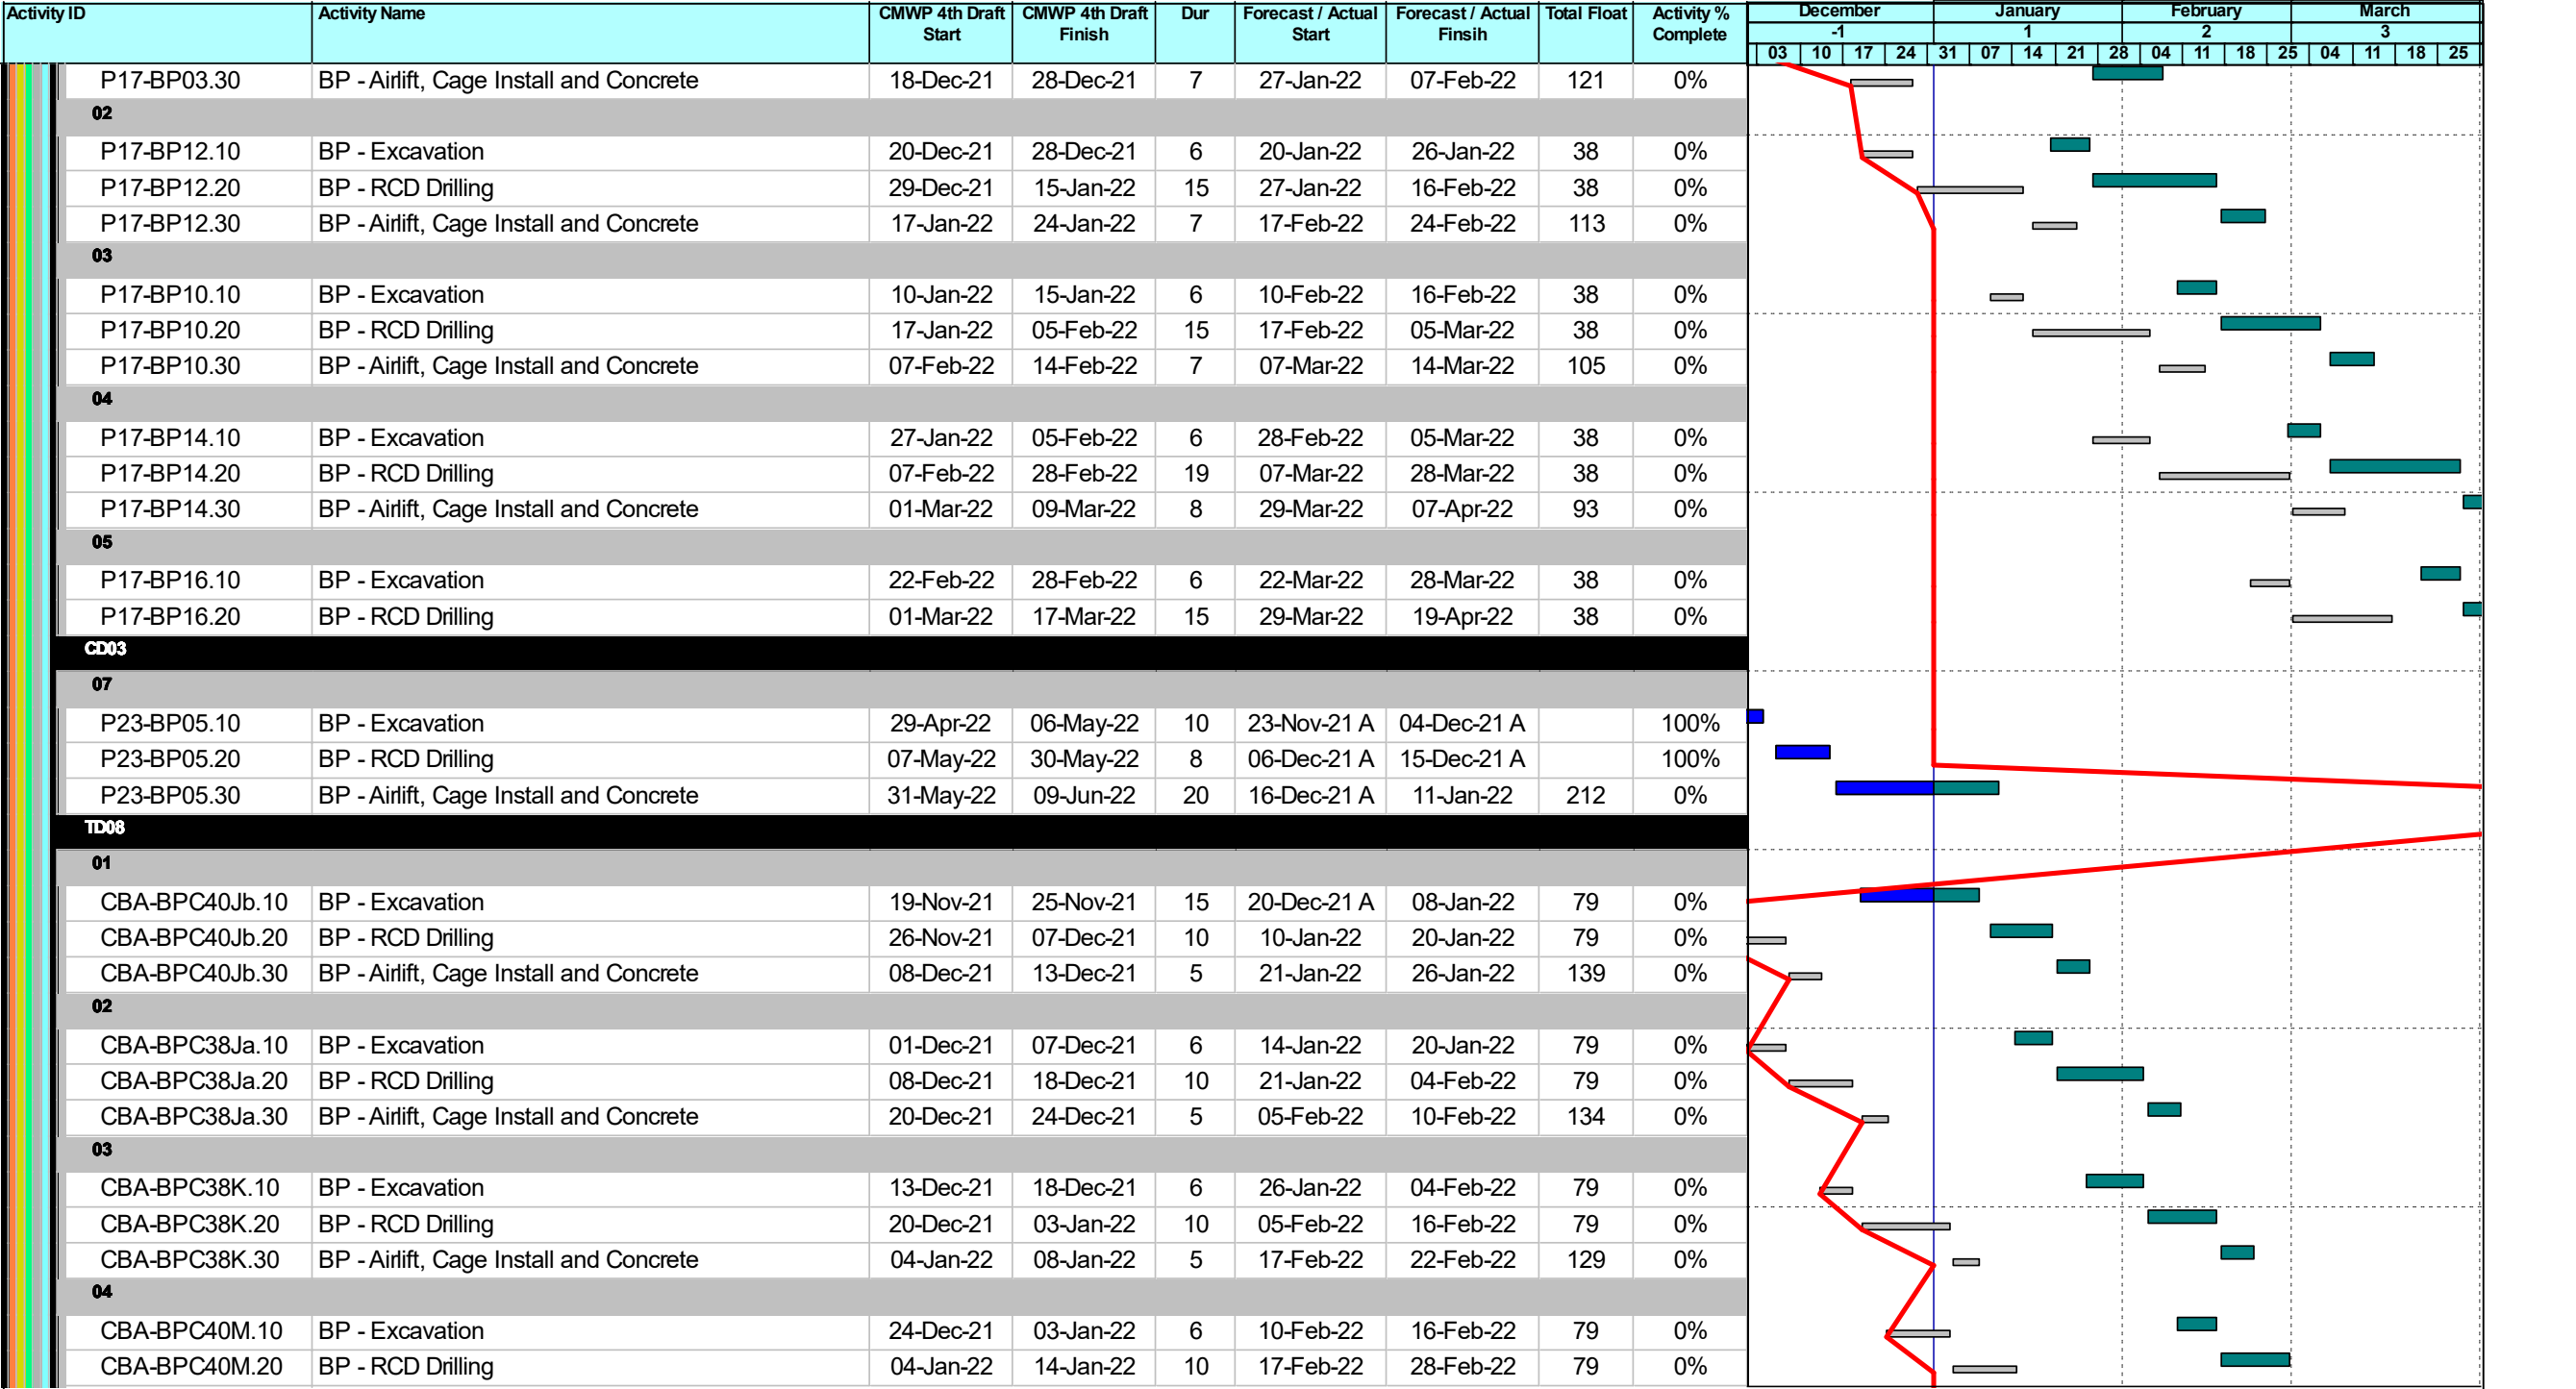


	Planned Bar		Milestone
	Critical Bar		Critical MS
	Baseline		Baseline MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 31 Dec 2021
Based on CMWP 4th Draft



Date	Revision	Checked	Approved
06-Aug-21	1st Draft	KL	N
29-Sep-21	2nd Draft	KL	N
25-Oct-21	3rd Draft	KL	C
26-Nov-21	4th Draft	KL	

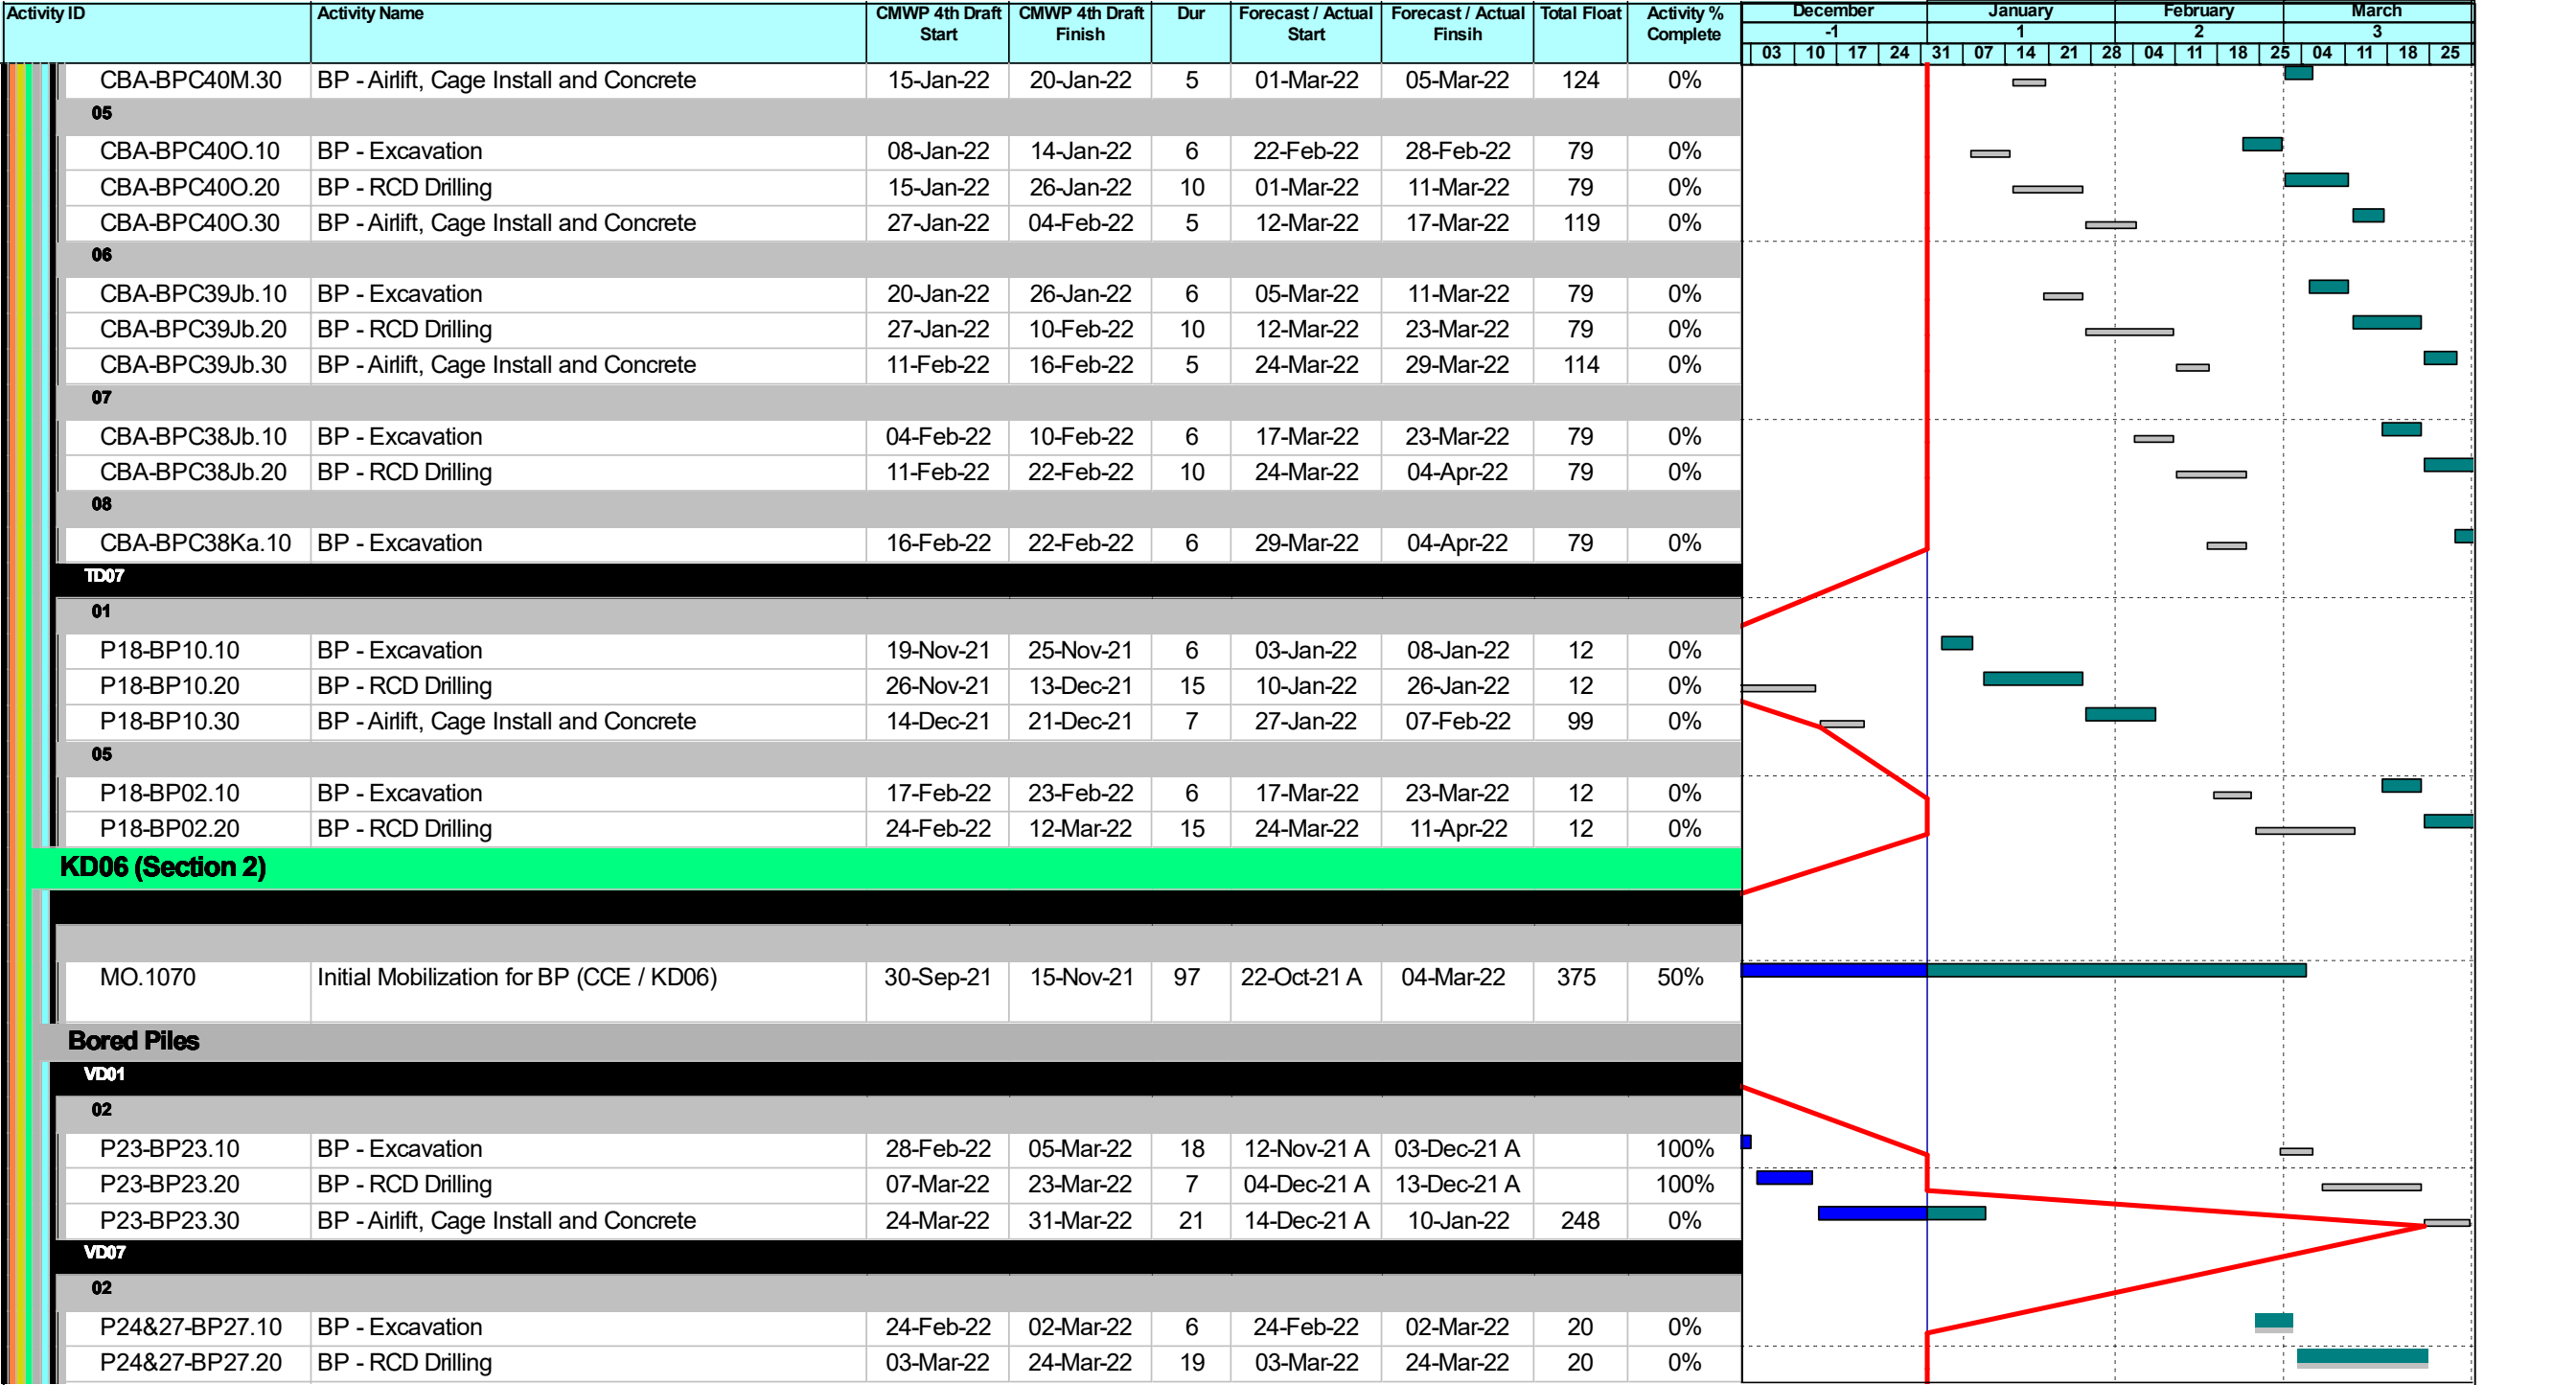


	Planned Bar		Milestone
	Critical Bar		Critical MS
	Baseline		Baseline MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 31 Dec 2021
 Based on CMWP 4th Draft



Date	Revision	Checked	Approved
06-Aug-21	1st Draft	KL	N
29-Sep-21	2nd Draft	KL	N
25-Oct-21	3rd Draft	KL	C
26-Nov-21	4th Draft	KL	

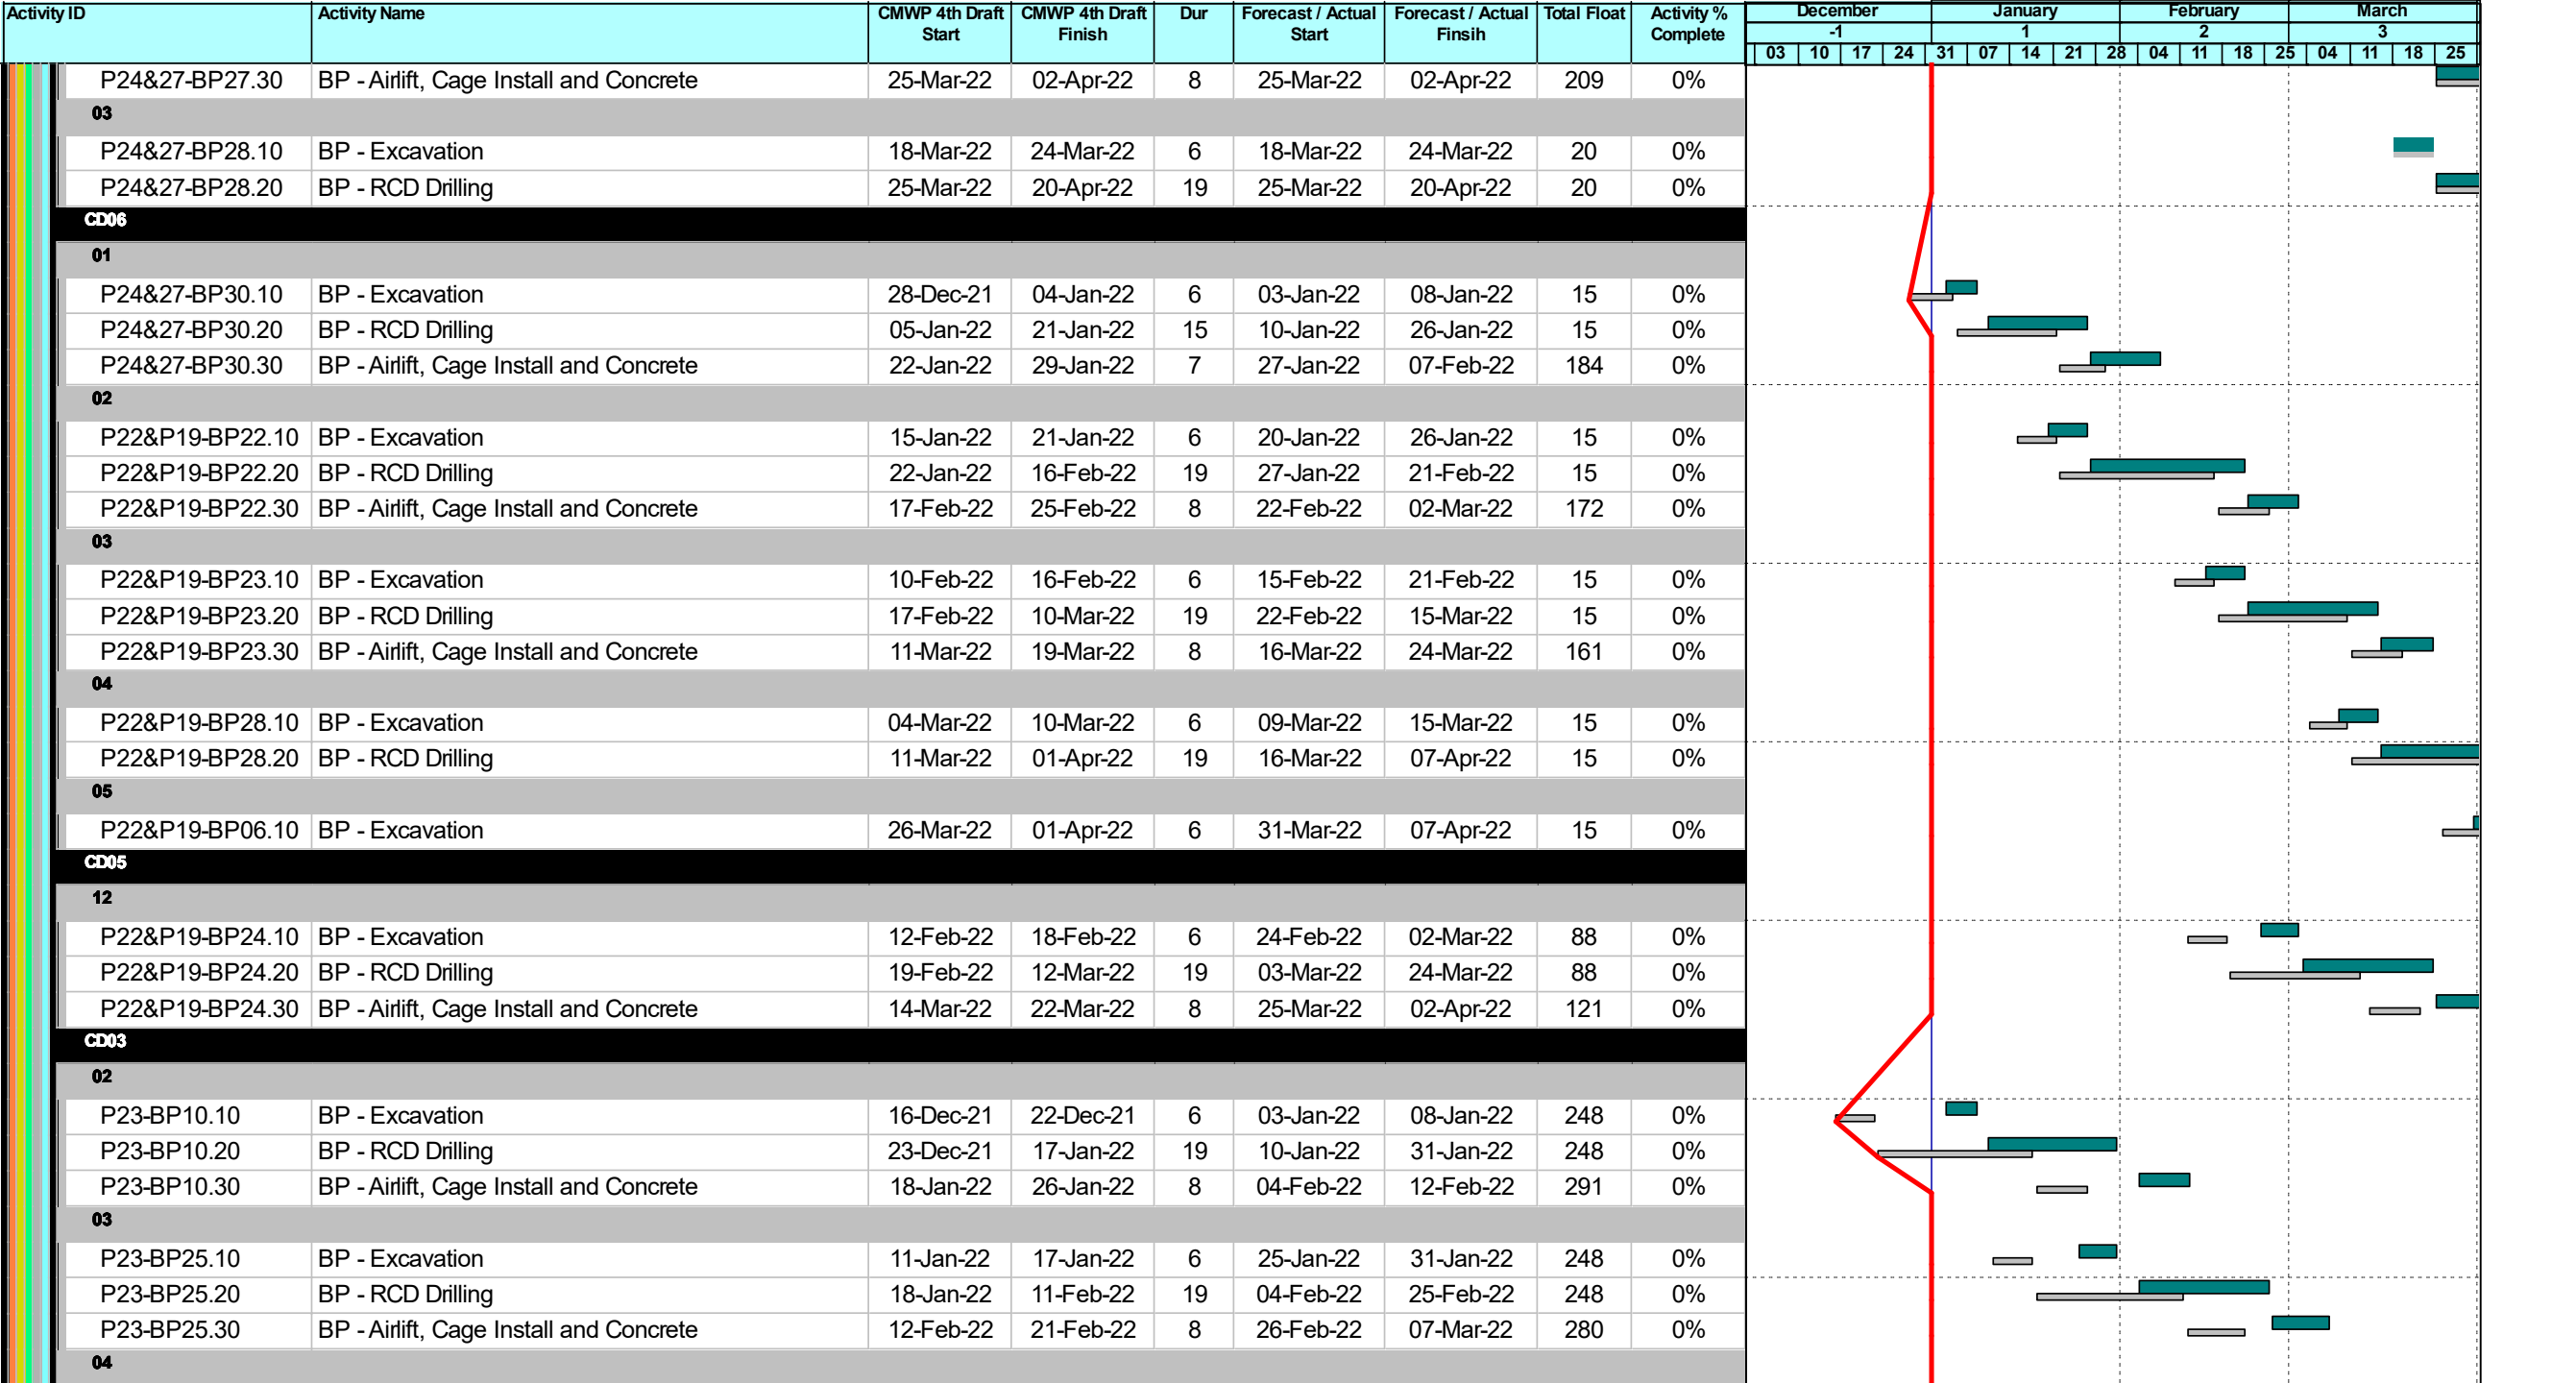

	Planned Bar		Milestone
	Critical Bar		Critical MS
	Baseline		Baseline MS

West Kowloon Cultural District Authority
Piling for Retained Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 31 Dec 2021
 Based on CMWP 4th Draft

Date	Revision	Checked	Approved
06-Aug-21	1st Draft	KL	N
29-Sep-21	2nd Draft	KL	N
25-Oct-21	3rd Draft	KL	C
26-Nov-21	4th Draft	KL	

Activity ID	Activity Name	CMWP 4th Draft Start	CMWP 4th Draft Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	December				January				February				March			
									-1				1				2				3			
									03	10	17	24	31	07	14	21	28	04	11	18	25	04	11	18

01									
P24&27-BP34.10	BP (Trial Pile for Schedule 2) - Excavation	18-Jan-22	24-Jan-22	6	18-Jan-22	24-Jan-22	13	0%	
P24&27-BP34.20	BP (Trial Pile for Schedule 2) - RCD Drilling	25-Jan-22	18-Feb-22	19	25-Jan-22	18-Feb-22	13	0%	
P24&27-BP34.30	BP (Trial Pile for Schedule 2) - Airlift, Cage Install and Concrete	19-Feb-22	28-Feb-22	8	19-Feb-22	28-Feb-22	13	0%	

KD07.BP.0060	Review and Confirmation of Rockhead and Founding Level of Pile by CA	23-Oct-21	05-Nov-21	49	13-Nov-21 A	01-Jan-22	2	100%	
--------------	--	-----------	-----------	----	-------------	-----------	---	------	--

Bored Piles

VD01

03									
P26-BP08.10	BP - Excavation	17-Mar-22	23-Mar-22	36	25-Nov-21 A	08-Jan-22	79	0%	
P26-BP08.20	BP - RCD Drilling	24-Mar-22	19-Apr-22	19	10-Jan-22	31-Jan-22	79	0%	
P26-BP08.30	BP - Airlift, Cage Install and Concrete	20-Apr-22	28-Apr-22	8	04-Feb-22	12-Feb-22	230	0%	

05									
P26-BP11.10	BP - Excavation	19-May-22	25-May-22	6	03-Mar-22	09-Mar-22	79	0%	
P26-BP11.20	BP - RCD Drilling	26-May-22	17-Jun-22	19	10-Mar-22	31-Mar-22	79	0%	

VD02

02									
P24&27-BP08.10	BP - Excavation	12-Feb-22	18-Feb-22	6	12-Feb-22	18-Feb-22	37	0%	
P24&27-BP08.20	BP - RCD Drilling	19-Feb-22	24-Mar-22	29	19-Feb-22	24-Mar-22	37	0%	
P24&27-BP08.30	BP - Airlift, Cage Install and Concrete	25-Mar-22	02-Apr-22	8	25-Mar-22	02-Apr-22	110	0%	

08									
P24&27-BP02.10	BP - Excavation	02-Sep-22	08-Sep-22	17	17-Dec-21 A	08-Jan-22	338	0%	
P24&27-BP02.20	BP - RCD Drilling	09-Sep-22	15-Oct-22	29	10-Jan-22	15-Feb-22	338	0%	
P24&27-BP02.30	BP - Airlift, Cage Install and Concrete	17-Oct-22	25-Oct-22	8	16-Feb-22	24-Feb-22	375	0%	


VD03

02									
P30-BP59.10	BP - Excavation	23-Feb-22	01-Mar-22	6	26-Feb-22	04-Mar-22	0	0%	
P30-BP59.20	BP - RCD Drilling	02-Mar-22	04-Apr-22	29	05-Mar-22	08-Apr-22	0	0%	

VD04

04									
P30-BP66.10	BP - Excavation	21-Mar-22	26-Mar-22	6	21-Mar-22	26-Mar-22	0	0%	
P30-BP66.20	BP - RCD Drilling	28-Mar-22	14-Apr-22	15	28-Mar-22	14-Apr-22	0	0%	


VD06

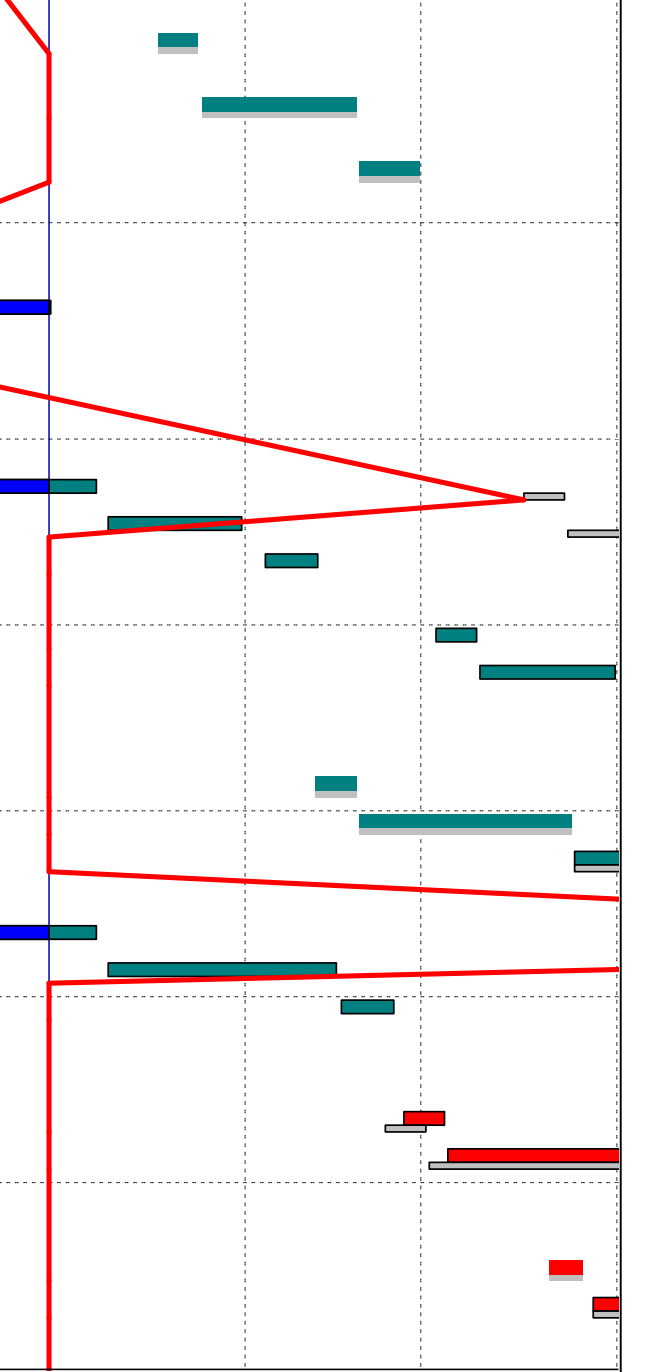

	Planned Bar		Milestone
	Critical Bar		Critical MS
	Baseline		Baseline MS

West Kowloon Cultural District Authority
Piling for Retained Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 31 Dec 2021
Based on CMWP 4th Draft

Date	Revision	Checked	Approved
06-Aug-21	1st Draft	KL	N
29-Sep-21	2nd Draft	KL	N
25-Oct-21	3rd Draft	KL	C
26-Nov-21	4th Draft	KL	



Activity ID	Activity Name	CMWP 4th Draft Start	CMWP 4th Draft Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	December				January				February				March			
									-1				1				2				3			
									03	10	17	24	31	07	14	21	28	04	11	18	25	04	11	18

02									
P28&29-BP11.10	BP - Excavation	09-Feb-22	15-Feb-22	6	09-Feb-22	15-Feb-22	0	0%	
P28&29-BP11.20	BP - RCD Drilling	16-Feb-22	04-Mar-22	15	16-Feb-22	04-Mar-22	0	0%	
P28&29-BP11.30	BP - Airlift, Cage Install and Concrete	05-Mar-22	12-Mar-22	7	05-Mar-22	12-Mar-22	72	0%	

03									
P28&29-BP03.10	BP - Excavation	26-Feb-22	04-Mar-22	6	26-Feb-22	04-Mar-22	0	0%	
P28&29-BP03.20	BP - RCD Drilling	05-Mar-22	22-Mar-22	15	05-Mar-22	22-Mar-22	0	0%	
P28&29-BP03.30	BP - Airlift, Cage Install and Concrete	23-Mar-22	30-Mar-22	7	23-Mar-22	30-Mar-22	64	0%	

04									
P28&29-BP01.10	BP - Excavation	16-Mar-22	22-Mar-22	6	16-Mar-22	22-Mar-22	0	0%	
P28&29-BP01.20	BP - RCD Drilling	23-Mar-22	09-Apr-22	15	23-Mar-22	09-Apr-22	0	0%	

VD07									
01									
P24&27-BP25.10	BP - Excavation	18-Jan-22	24-Jan-22	6	18-Jan-22	24-Jan-22	20	0%	
P24&27-BP25.20	BP - RCD Drilling	25-Jan-22	02-Mar-22	29	25-Jan-22	02-Mar-22	20	0%	
P24&27-BP25.30	BP - Airlift, Cage Install and Concrete	03-Mar-22	11-Mar-22	8	03-Mar-22	11-Mar-22	220	0%	

KD08 (Section 4)

Trial Pile (P30-BP15)


TD01									
04									
P30-BP15.10	BP (Trial Pile for Schedule 3) - Excavation	28-Mar-22	02-Apr-22	6	04-Feb-22	10-Feb-22	55	0%	
P30-BP15.20	BP (Trial Pile for Schedule 3) - RCD Drilling	04-Apr-22	25-Apr-22	15	11-Feb-22	28-Feb-22	55	0%	
P30-BP15.30	BP (Trial Pile for Schedule 3) - Airlift, Cage Install and Concrete	26-Apr-22	04-May-22	7	01-Mar-22	08-Mar-22	55	0%	

MO.1090	Initial Mobilization for BP (CCG / KD08 / KD04)	15-Sep-21	15-Nov-21	97	05-Nov-21 A	04-Mar-22	359	90%	
---------	---	-----------	-----------	----	-------------	-----------	-----	-----	--

Bored Piles

VD01									
04									
P26-BP12.10	BP - Excavation	09-Apr-22	19-Apr-22	6	25-Jan-22	31-Jan-22	79	0%	
P26-BP12.20	BP - RCD Drilling	20-Apr-22	25-May-22	29	04-Feb-22	09-Mar-22	79	0%	
P26-BP12.30	BP - Airlift, Cage Install and Concrete	26-May-22	04-Jun-22	8	10-Mar-22	18-Mar-22	209	0%	

VD04

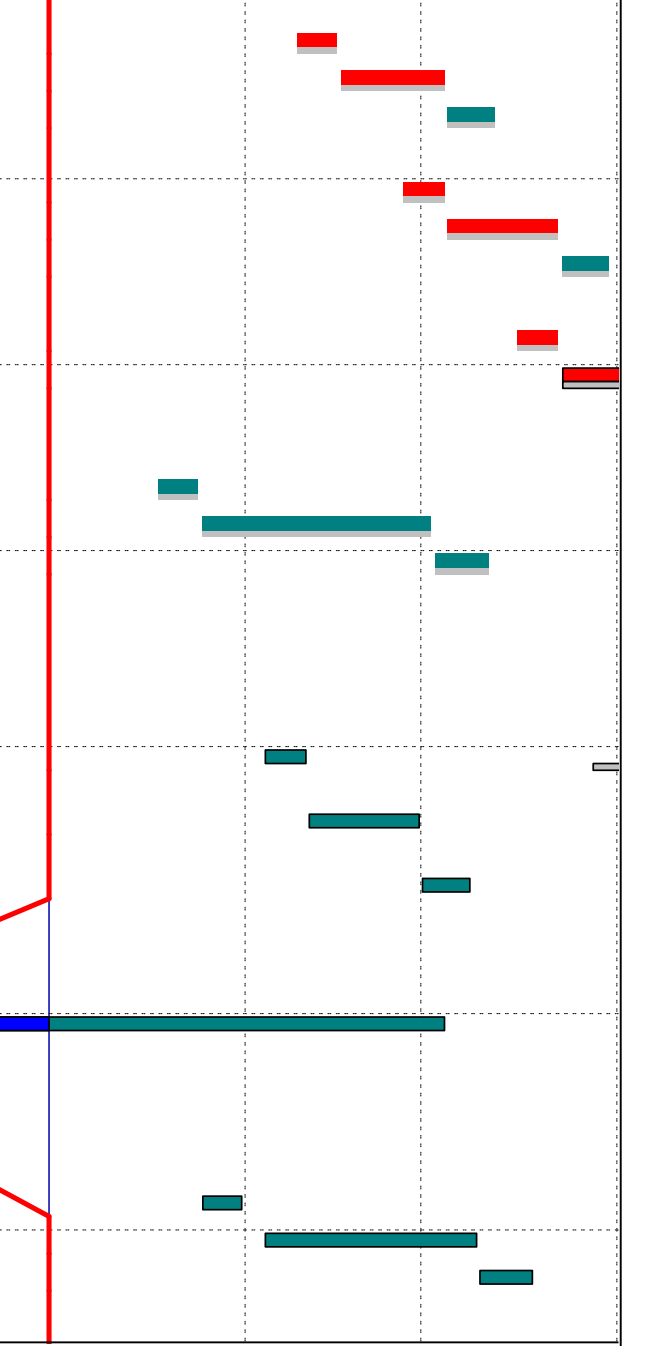

	Planned Bar		Milestone
	Critical Bar		Critical MS
	Baseline		Baseline MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 31 Dec 2021
 Based on CMWP 4th Draft


Date	Revision	Checked	Approved
06-Aug-21	1st Draft	KL	N
29-Sep-21	2nd Draft	KL	N
25-Oct-21	3rd Draft	KL	C
26-Nov-21	4th Draft	KL	

Activity ID	Activity Name	CMWP 4th Draft Start	CMWP 4th Draft Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	December				January				February				March			
									-1				1				2				3			
									03	10	17	24	31	07	14	21	28	04	11	18	25	04	11	18

01									
P30-BP41.10	BP - Excavation	19-Jan-22	25-Jan-22	6	19-Jan-22	25-Jan-22	0	0%	
P30-BP41.20	BP - RCD Drilling	26-Jan-22	15-Feb-22	15	26-Jan-22	15-Feb-22	0	0%	
P30-BP41.30	BP - Airlift, Cage Install and Concrete	16-Feb-22	23-Feb-22	7	16-Feb-22	23-Feb-22	159	0%	
02									
P30-BP47.10	BP - Excavation	09-Feb-22	15-Feb-22	6	09-Feb-22	15-Feb-22	0	0%	
P30-BP47.20	BP - RCD Drilling	16-Feb-22	04-Mar-22	15	16-Feb-22	04-Mar-22	0	0%	
P30-BP47.30	BP - Airlift, Cage Install and Concrete	05-Mar-22	12-Mar-22	7	05-Mar-22	12-Mar-22	151	0%	
03									
P30-BP58.10	BP - Excavation	26-Feb-22	04-Mar-22	6	26-Feb-22	04-Mar-22	0	0%	
P30-BP58.20	BP - RCD Drilling	05-Mar-22	26-Mar-22	19	05-Mar-22	26-Mar-22	0	0%	
P30-BP58.30	BP - Airlift, Cage Install and Concrete	28-Mar-22	06-Apr-22	8	28-Mar-22	06-Apr-22	139	0%	

VD05									
01									
P30-BP20.10	BP - Excavation	29-Nov-21	04-Dec-21	12	01-Dec-21 A	15-Dec-21 A		100%	
P30-BP20.20	BP - RCD Drilling	06-Dec-21	22-Dec-21	7	16-Dec-21 A	24-Dec-21 A		100%	
P30-BP20.30	BP - Airlift, Cage Install and Concrete	23-Dec-21	03-Jan-22	11	28-Dec-21 A	10-Jan-22	220	0%	
02									
P30-BP19.10	BP - Excavation	16-Dec-21	22-Dec-21	6	03-Jan-22	08-Jan-22	41	0%	
P30-BP19.20	BP - RCD Drilling	23-Dec-21	28-Jan-22	29	10-Jan-22	15-Feb-22	41	0%	
P30-BP19.30	BP - Airlift, Cage Install and Concrete	29-Jan-22	10-Feb-22	8	16-Feb-22	24-Feb-22	192	0%	
03									
P30-BP24.10	BP - Excavation	22-Jan-22	28-Jan-22	6	09-Feb-22	15-Feb-22	41	0%	
P30-BP24.20	BP - RCD Drilling	29-Jan-22	23-Feb-22	19	16-Feb-22	09-Mar-22	41	0%	
P30-BP24.30	BP - Airlift, Cage Install and Concrete	24-Feb-22	04-Mar-22	8	10-Mar-22	18-Mar-22	181	0%	
04									
P30-BP31.10	BP - Excavation	17-Feb-22	23-Feb-22	6	03-Mar-22	09-Mar-22	41	0%	
P30-BP31.20	BP - RCD Drilling	24-Feb-22	29-Mar-22	29	10-Mar-22	13-Apr-22	41	0%	
12									
P30-BP39.10	BP - Excavation	25-Aug-22	31-Aug-22	23	10-Dec-21 A	08-Jan-22	304	0%	
P30-BP39.20	BP - RCD Drilling	01-Sep-22	19-Sep-22	15	10-Jan-22	26-Jan-22	304	0%	
P30-BP39.30	BP - Airlift, Cage Install and Concrete	20-Sep-22	27-Sep-22	7	27-Jan-22	07-Feb-22	304	0%	

TD01									
01									
P30-BP01.30	BP - Airlift, Cage Install and Concrete	23-Feb-22	02-Mar-22	15	28-Nov-21 A	16-Dec-21 A		100%	
02									
P30-BP05.10	BP - Excavation	16-Feb-22	22-Feb-22	29	08-Nov-21 A	11-Dec-21 A		100%	

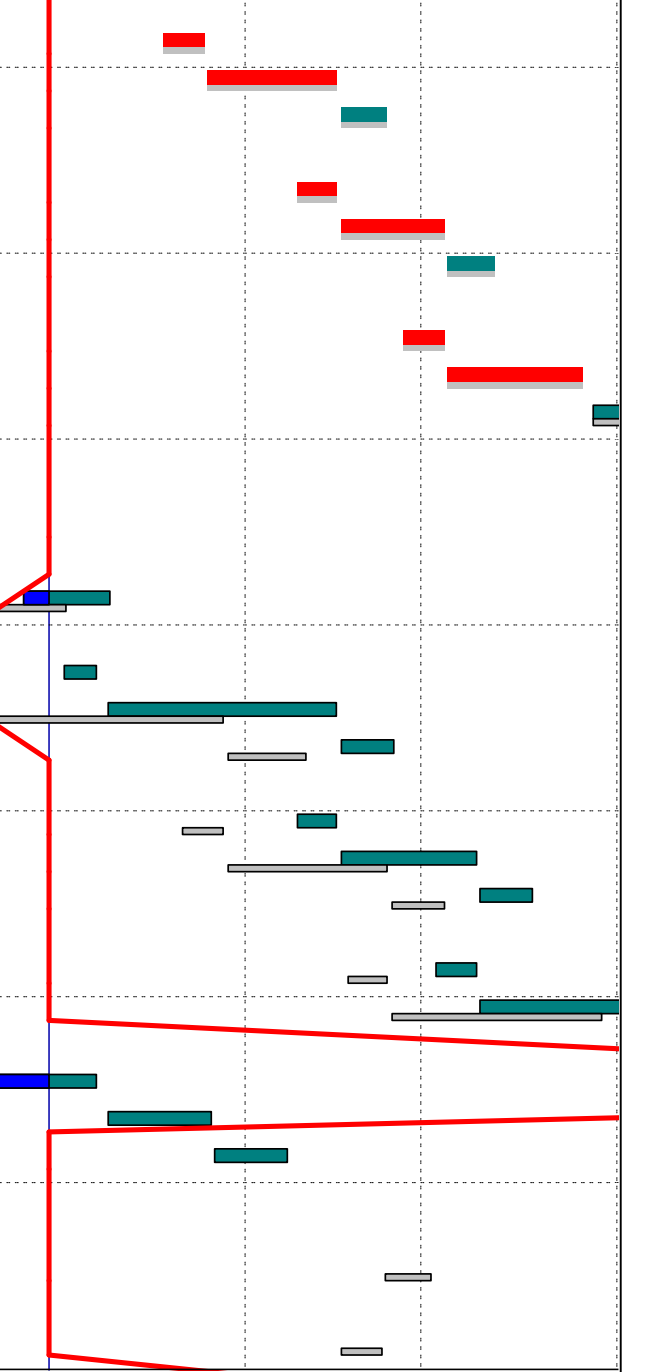


	Planned Bar		Milestone
	Critical Bar		Critical MS
	Baseline		Baseline MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 31 Dec 2021
 Based on CMWP 4th Draft

Date	Revision	Checked	Approved
06-Aug-21	1st Draft	KL	N
29-Sep-21	2nd Draft	KL	N
25-Oct-21	3rd Draft	KL	C
26-Nov-21	4th Draft	KL	



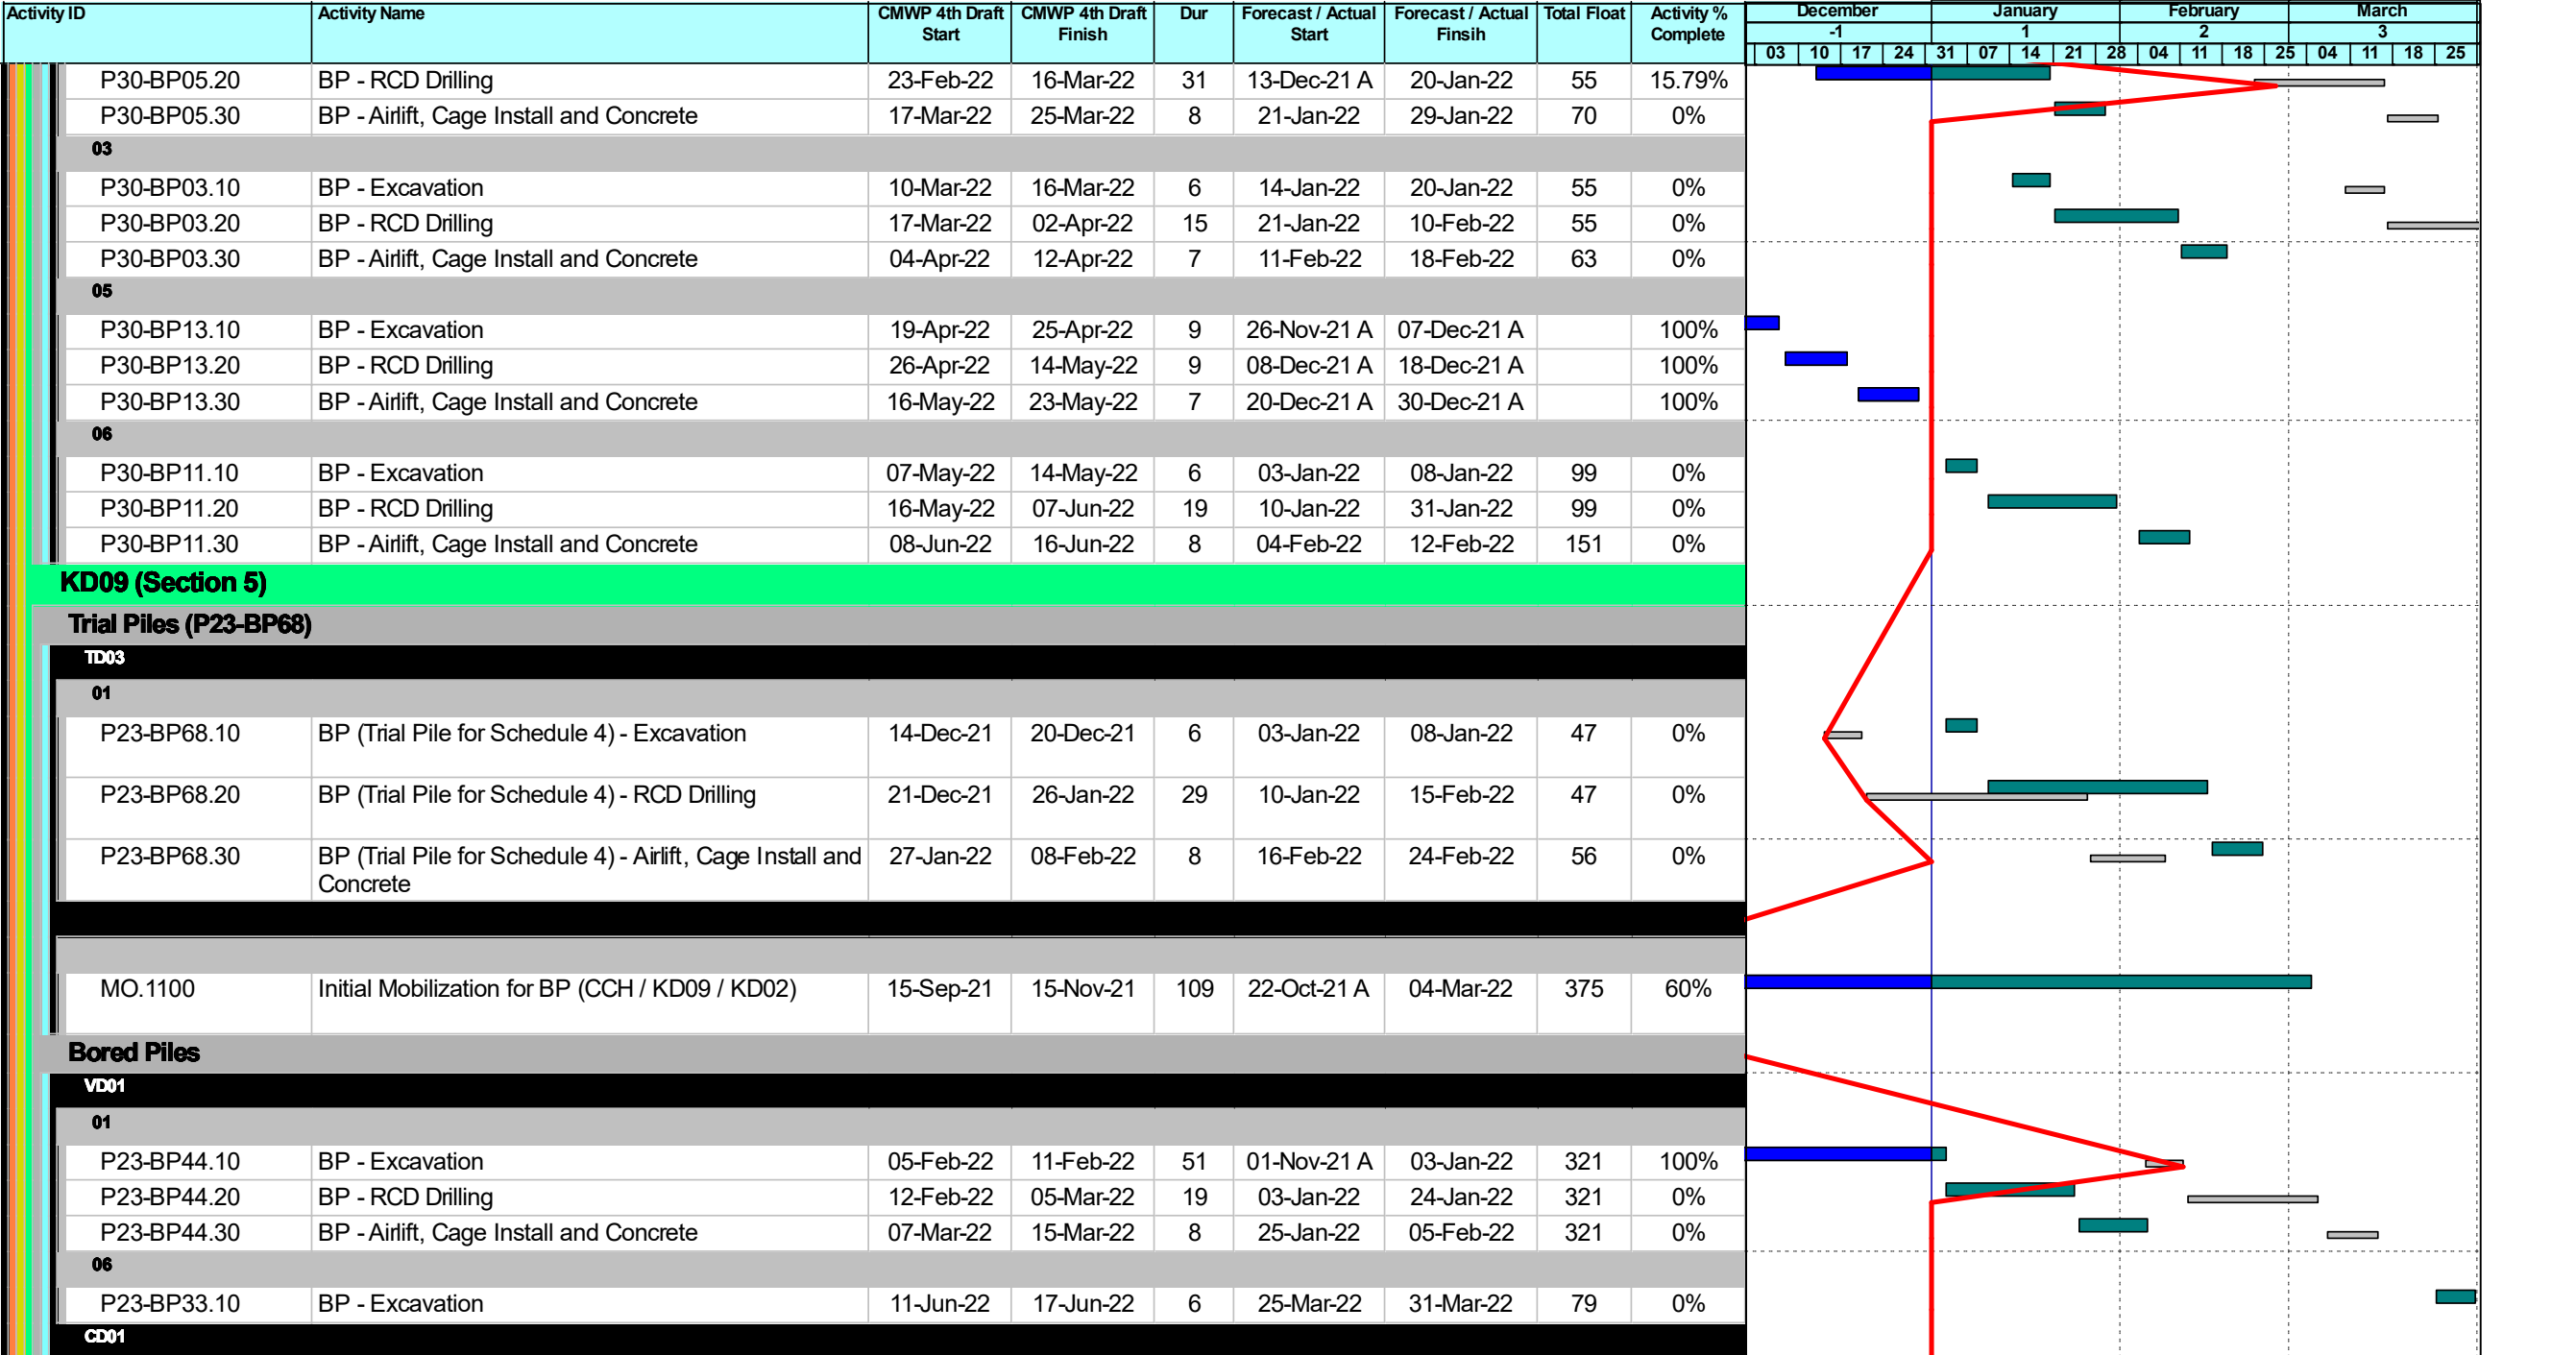



ID: 2B2C-20211231_bw
 Data Date: 01-Jan-22
 Print Date: 03-Jan-22_14:19
 Page 15 of 20



West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 31 Dec 2021
 Based on CMWP 4th Draft

Date	Revision	Checked	Approved
06-Aug-21	1st Draft	KL	N
29-Sep-21	2nd Draft	KL	N
25-Oct-21	3rd Draft	KL	C
26-Nov-21	4th Draft	KL	



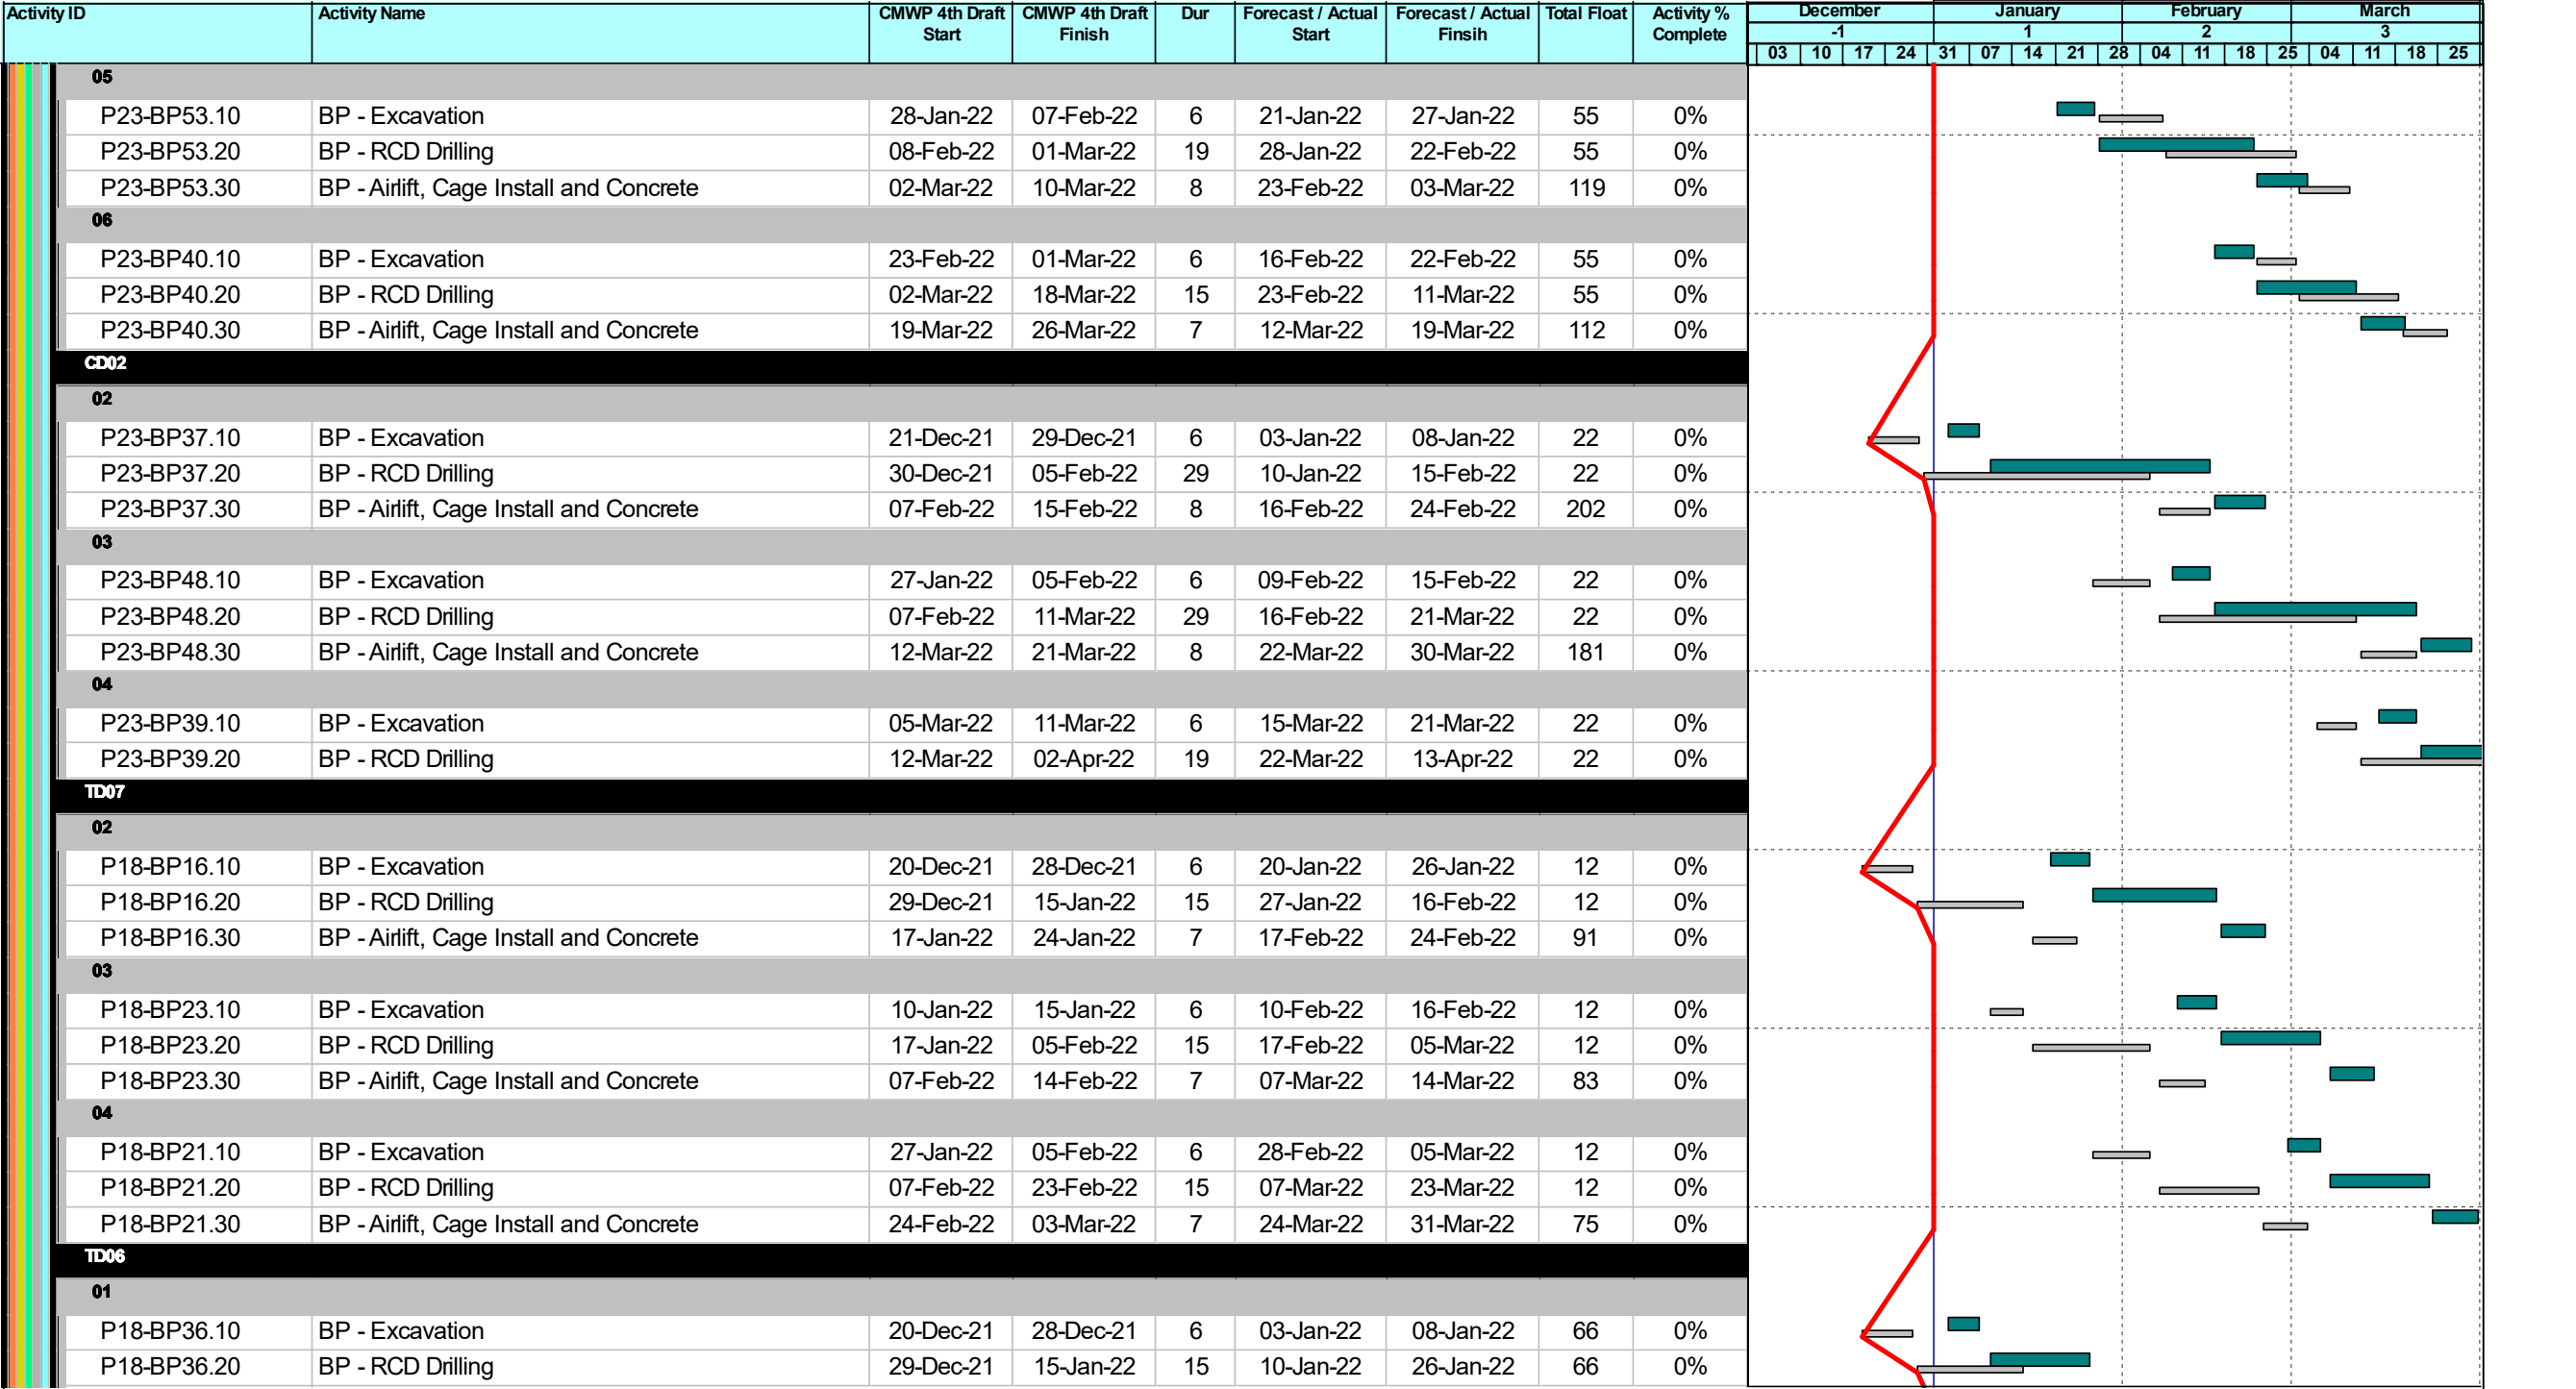

	Planned Bar		Milestone
	Critical Bar		Critical MS
	Baseline		Baseline MS


West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 31 Dec 2021
 Based on CMWP 4th Draft



Date	Revision	Checked	Approved
06-Aug-21	1st Draft	KL	N
29-Sep-21	2nd Draft	KL	N
25-Oct-21	3rd Draft	KL	C
26-Nov-21	4th Draft	KL	

Activity ID	Activity Name	CMWP 4th Draft Start	CMWP 4th Draft Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	December				January				February				March			
									-1				1				2				3			
									03	10	17	24	31	07	14	21	28	04	11	18	25	04	11	18

02	P18-BP36.30	BP - Airlift, Cage Install and Concrete	17-Jan-22	24-Jan-22	7	27-Jan-22	07-Feb-22	208	0%
	P18-BP40.10	BP - Excavation	10-Jan-22	15-Jan-22	6	20-Jan-22	26-Jan-22	66	0%
	P18-BP40.20	BP - RCD Drilling	17-Jan-22	05-Feb-22	15	27-Jan-22	16-Feb-22	66	0%
	P18-BP40.30	BP - Airlift, Cage Install and Concrete	07-Feb-22	14-Feb-22	7	17-Feb-22	24-Feb-22	200	0%
03	P18-BP38.10	BP - Excavation	27-Jan-22	05-Feb-22	6	10-Feb-22	16-Feb-22	66	0%
	P18-BP38.20	BP - RCD Drilling	07-Feb-22	28-Feb-22	19	17-Feb-22	10-Mar-22	66	0%
	P18-BP38.30	BP - Airlift, Cage Install and Concrete	01-Mar-22	09-Mar-22	8	11-Mar-22	19-Mar-22	188	0%
04	P18-BP33.10	BP - Excavation	22-Feb-22	28-Feb-22	6	04-Mar-22	10-Mar-22	66	0%
	P18-BP33.20	BP - RCD Drilling	01-Mar-22	17-Mar-22	15	11-Mar-22	28-Mar-22	66	0%
	P18-BP33.30	BP - Airlift, Cage Install and Concrete	18-Mar-22	25-Mar-22	7	29-Mar-22	06-Apr-22	181	0%
05	P18-BP28.10	BP - Excavation	11-Mar-22	17-Mar-22	6	22-Mar-22	28-Mar-22	66	0%
	P18-BP28.20	BP - RCD Drilling	18-Mar-22	04-Apr-22	15	29-Mar-22	19-Apr-22	66	0%
TD05									
01	P18-BP48.10	BP - Excavation	20-Dec-21	28-Dec-21	6	03-Jan-22	08-Jan-22	95	0%
	P18-BP48.20	BP - RCD Drilling	29-Dec-21	15-Jan-22	15	10-Jan-22	26-Jan-22	95	0%
	P18-BP48.30	BP - Airlift, Cage Install and Concrete	17-Jan-22	24-Jan-22	7	27-Jan-22	07-Feb-22	225	0%
02	P18-BP60.10	BP - Excavation	10-Jan-22	15-Jan-22	6	20-Jan-22	26-Jan-22	95	0%
	P18-BP60.20	BP - RCD Drilling	17-Jan-22	10-Feb-22	19	27-Jan-22	21-Feb-22	95	0%
	P18-BP60.30	BP - Airlift, Cage Install and Concrete	11-Feb-22	19-Feb-22	8	22-Feb-22	02-Mar-22	213	0%
03	P18-BP63.10	BP - Excavation	04-Feb-22	10-Feb-22	6	15-Feb-22	21-Feb-22	95	0%
	P18-BP63.20	BP - RCD Drilling	11-Feb-22	04-Mar-22	19	22-Feb-22	15-Mar-22	95	0%
	P18-BP63.30	BP - Airlift, Cage Install and Concrete	05-Mar-22	14-Mar-22	8	16-Mar-22	24-Mar-22	202	0%
04	P18-BP62.10	BP - Excavation	26-Feb-22	04-Mar-22	6	09-Mar-22	15-Mar-22	95	0%
	P18-BP62.20	BP - RCD Drilling	05-Mar-22	26-Mar-22	19	16-Mar-22	07-Apr-22	95	0%
05	P18-BP61.10	BP - Excavation	21-Mar-22	26-Mar-22	6	31-Mar-22	07-Apr-22	95	0%
TD04									
04	P23-BP107.10	BP - Excavation	04-Jan-22	10-Jan-22	6	31-Jan-22	09-Feb-22	176	0%

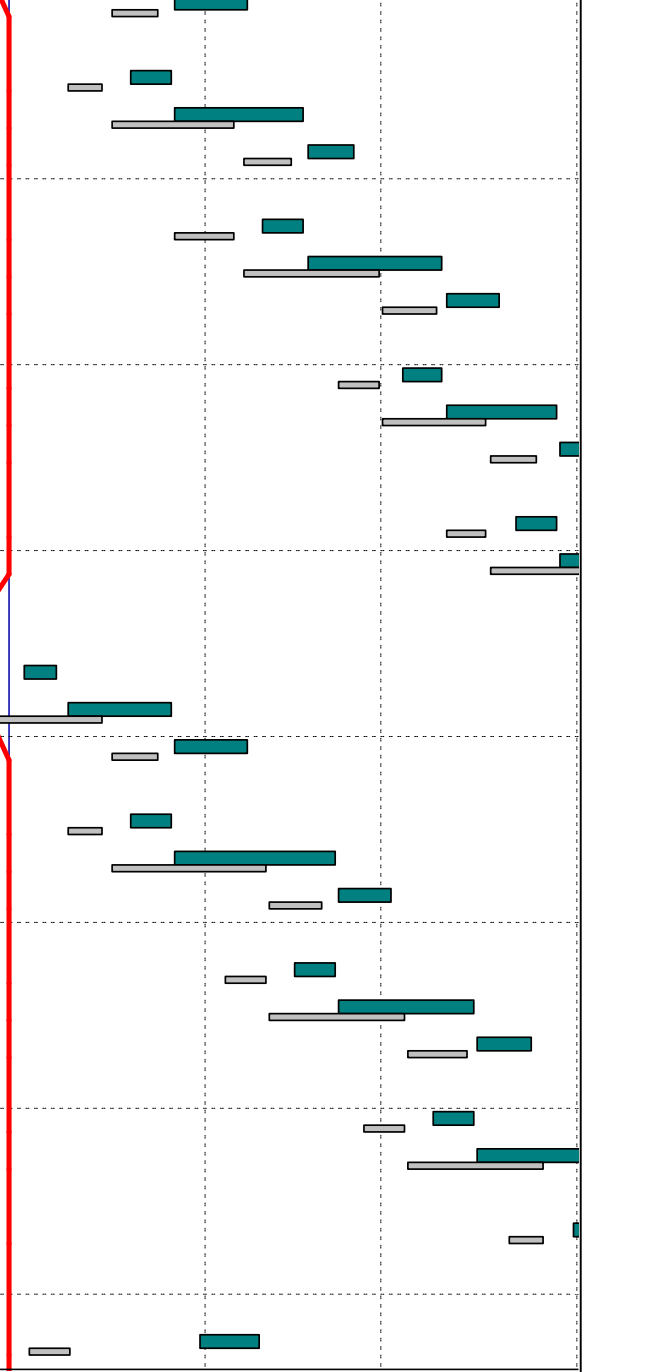

Planned Bar	Critical Bar	Baseline	Milestone	Critical MS	Baseline MS
-------------	--------------	----------	-----------	-------------	-------------



Date	Revision	Checked	Approved
06-Aug-21	1st Draft	KL	N
29-Sep-21	2nd Draft	KL	N
25-Oct-21	3rd Draft	KL	C
26-Nov-21	4th Draft	KL	

Activity ID	Activity Name	CMWP 4th Draft Start	CMWP 4th Draft Finish	Dur	Forecast / Actual Start	Forecast / Actual Finish	Total Float	Activity % Complete	December				January				February				March					
									-1				1				2				3					
									03	10	17	24	31	07	14	21	28	04	11	18	25	04	11	18	25	
P23-BP107.20	BP - RCD Drilling	11-Jan-22	04-Feb-22	19	10-Feb-22	03-Mar-22	176	0%																		
P23-BP107.30	BP - Airlift, Cage Install and Concrete	05-Feb-22	14-Feb-22	8	04-Mar-22	12-Mar-22	251	0%																		
05																										
P23-BP75.10	BP - Excavation	26-Jan-22	04-Feb-22	6	25-Feb-22	03-Mar-22	176	0%																		
P23-BP75.20	BP - RCD Drilling	05-Feb-22	26-Feb-22	19	04-Mar-22	25-Mar-22	176	0%																		
P23-BP75.30	BP - Airlift, Cage Install and Concrete	28-Feb-22	08-Mar-22	8	26-Mar-22	04-Apr-22	240	0%																		
06																										
P23-BP73.10	BP - Excavation	21-Feb-22	26-Feb-22	6	19-Mar-22	25-Mar-22	176	0%																		
P23-BP73.20	BP - RCD Drilling	28-Feb-22	21-Mar-22	19	26-Mar-22	21-Apr-22	176	0%																		
10																										
P23-BP115.10	BP - Excavation	04-Jan-22	10-Jan-22	6	31-Jan-22	09-Feb-22	99	0%																		
P23-BP115.20	BP - RCD Drilling	11-Jan-22	04-Feb-22	19	10-Feb-22	03-Mar-22	99	0%																		
P23-BP115.30	BP - Airlift, Cage Install and Concrete	05-Feb-22	14-Feb-22	8	04-Mar-22	12-Mar-22	227	0%																		
11																										
P23-BP108.10	BP - Excavation	26-Jan-22	04-Feb-22	6	25-Feb-22	03-Mar-22	99	0%																		
P23-BP108.20	BP - RCD Drilling	05-Feb-22	10-Mar-22	29	04-Mar-22	07-Apr-22	99	0%																		
12																										
P23-BP74.10	BP - Excavation	04-Mar-22	10-Mar-22	6	31-Mar-22	07-Apr-22	99	0%																		
TD03																										
02																										
P23-BP101.10	BP - Excavation	20-Jan-22	26-Jan-22	6	09-Feb-22	15-Feb-22	47	0%																		
P23-BP101.20	BP - RCD Drilling	27-Jan-22	21-Feb-22	19	16-Feb-22	09-Mar-22	47	0%																		
P23-BP101.30	BP - Airlift, Cage Install and Concrete	22-Feb-22	02-Mar-22	8	10-Mar-22	18-Mar-22	198	0%																		
03																										
P23-BP110.10	BP - Excavation	15-Feb-22	21-Feb-22	6	03-Mar-22	09-Mar-22	47	0%																		
P23-BP110.20	BP - RCD Drilling	22-Feb-22	15-Mar-22	19	10-Mar-22	31-Mar-22	47	0%																		
04																										
P23-BP109.10	BP - Excavation	09-Mar-22	15-Mar-22	6	25-Mar-22	31-Mar-22	47	0%																		
14																										
P23-BP90.10	BP - Excavation	27-Apr-22	04-May-22	18	16-Dec-21 A	08-Jan-22	181	0%																		
P23-BP90.20	BP - RCD Drilling	05-May-22	09-Jun-22	29	10-Jan-22	15-Feb-22	181	0%																		
P23-BP90.30	BP - Airlift, Cage Install and Concrete	10-Jun-22	18-Jun-22	8	16-Feb-22	24-Feb-22	257	0%																		
TD02																										
01																										
P23-BP81.10	BP - Excavation	20-Dec-21	28-Dec-21	26	12-Nov-21 A	13-Dec-21 A		100%																		
P23-BP81.20	BP - RCD Drilling	29-Dec-21	04-Feb-22	4	14-Dec-21 A	18-Dec-21 A		100%																		
P23-BP81.30	BP - Airlift, Cage Install and Concrete	05-Feb-22	14-Feb-22	17	20-Dec-21 A	11-Jan-22	275	0%																		

	Planned Bar		Milestone
	Critical Bar		Critical MS
	Baseline		Baseline MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 31 Dec 2021
 Based on CMWP 4th Draft



Date	Revision	Checked	Approved
06-Aug-21	1st Draft	KL	N
29-Sep-21	2nd Draft	KL	N
25-Oct-21	3rd Draft	KL	C
26-Nov-21	4th Draft	KL	


Activity ID	Activity Name	CMWP 4th Draft Start	CMWP 4th Draft Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	December				January				February				March			
									-1				1				2				3			
									03	10	17	24	31	07	14	21	28	04	11	18	25	04	11	18
02																								
P23-BP59.10	BP - Excavation	26-Jan-22	04-Feb-22	21	03-Dec-21 A	30-Dec-21 A		100%																
P23-BP59.20	BP - RCD Drilling	05-Feb-22	10-Mar-22	30	31-Dec-21 A	08-Feb-22	112	0%																
P23-BP59.30	BP - Airlift, Cage Install and Concrete	11-Mar-22	19-Mar-22	8	09-Feb-22	17-Feb-22	254	0%																
03																								
P23-BP71.10	BP - Excavation	04-Mar-22	10-Mar-22	6	29-Jan-22	08-Feb-22	112	0%																
P23-BP71.20	BP - RCD Drilling	11-Mar-22	14-Apr-22	29	09-Feb-22	14-Mar-22	112	0%																
P23-BP71.30	BP - Airlift, Cage Install and Concrete	19-Apr-22	27-Apr-22	8	15-Mar-22	23-Mar-22	233	0%																
04																								
P23-BP83.10	BP - Excavation	08-Apr-22	14-Apr-22	6	08-Mar-22	14-Mar-22	112	0%																
P23-BP83.20	BP - RCD Drilling	19-Apr-22	24-May-22	29	15-Mar-22	21-Apr-22	112	0%																
10																								
P23-BP94.10	BP - Excavation	26-Jan-22	04-Feb-22	6	03-Jan-22	08-Jan-22	55	0%																
P23-BP94.20	BP - RCD Drilling	05-Feb-22	10-Mar-22	29	10-Jan-22	15-Feb-22	55	0%																
P23-BP94.30	BP - Airlift, Cage Install and Concrete	11-Mar-22	19-Mar-22	8	16-Feb-22	24-Feb-22	225	0%																
11																								
P23-BP113.10	BP - Excavation	04-Mar-22	10-Mar-22	6	09-Feb-22	15-Feb-22	55	0%																
P23-BP113.20	BP - RCD Drilling	11-Mar-22	01-Apr-22	19	16-Feb-22	09-Mar-22	55	0%																
P23-BP113.30	BP - Airlift, Cage Install and Concrete	02-Apr-22	12-Apr-22	8	10-Mar-22	18-Mar-22	214	0%																
12																								
P23-BP111.10	BP - Excavation	26-Mar-22	01-Apr-22	6	03-Mar-22	09-Mar-22	55	0%																
P23-BP111.20	BP - RCD Drilling	02-Apr-22	28-Apr-22	19	10-Mar-22	31-Mar-22	55	0%																
13																								
P23-BP92.10	BP - Excavation	22-Apr-22	28-Apr-22	6	25-Mar-22	31-Mar-22	55	0%																
Socketed Steel H- Piles																								
Trial Pile																								
KD09.SSHP.0000	Test Installation of Pile (SHP-C52Xa-P6)	17-Jan-22	26-Jan-22	9	17-Jan-22	26-Jan-22	19	0%																
KD09.SSHP.0020	Submission and Approval of Installation Report by BD	27-Jan-22	02-Feb-22	7	27-Jan-22	02-Feb-22	26	0%																
Socketed Steel H- Pile Construction																								
SHP-BW-52Y1b-P	Socketed Steel H-Piling	04-Feb-22	12-Feb-22	8	04-Feb-22	12-Feb-22	93	0%																
SHP-BW-52Y1b-P:	Socketed Steel H-Piling	08-Feb-22	16-Feb-22	8	08-Feb-22	16-Feb-22	93	0%																

	Planned Bar		Milestone
	Critical Bar		Critical MS
	Baseline		Baseline MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 31 Dec 2021
Based on CMWP 4th Draft

	Date	Revision	Checked	Approved
	06-Aug-21	1st Draft	KL	N
	29-Sep-21	2nd Draft	KL	N
	25-Oct-21	3rd Draft	KL	C
	26-Nov-21	4th Draft	KL	

Activity ID	Activity Name	CMWP 4th Draft Start	CMWP 4th Draft Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	December				January				February				March				
									-1				1				2				3				
									03	10	17	24	31	07	14	21	28	04	11	18	25	04	11	18	25
	SHP-C52W-P1	Socketed Steel H-Piling	11-Feb-22	19-Feb-22	8	11-Feb-22	19-Feb-22	93	0%																
	SHP-C52W-P2	Socketed Steel H-Piling	15-Feb-22	23-Feb-22	8	15-Feb-22	23-Feb-22	93	0%																
	SHP-C52W-P3	Socketed Steel H-Piling	18-Feb-22	26-Feb-22	8	18-Feb-22	26-Feb-22	93	0%																
	SHP-C52W-P4	Socketed Steel H-Piling	22-Feb-22	02-Mar-22	8	22-Feb-22	02-Mar-22	93	0%																
	SHP-C52W-P5	Socketed Steel H-Piling	25-Feb-22	05-Mar-22	8	25-Feb-22	05-Mar-22	93	0%																
	SHP-C52W-P6	Socketed Steel H-Piling	01-Mar-22	09-Mar-22	8	01-Mar-22	09-Mar-22	93	0%																
	SHP-C52X-P1	Socketed Steel H-Piling	04-Mar-22	12-Mar-22	8	04-Mar-22	12-Mar-22	93	0%																
	SHP-C52X-P2	Socketed Steel H-Piling	08-Mar-22	16-Mar-22	8	08-Mar-22	16-Mar-22	93	0%																
	SHP-C52X-P3	Socketed Steel H-Piling	11-Mar-22	19-Mar-22	8	11-Mar-22	19-Mar-22	93	0%																
	SHP-C52X-P4	Socketed Steel H-Piling	15-Mar-22	23-Mar-22	8	15-Mar-22	23-Mar-22	93	0%																
	SHP-C52X-P5	Socketed Steel H-Piling	18-Mar-22	26-Mar-22	8	18-Mar-22	26-Mar-22	93	0%																
	SHP-C52X-P6	Socketed Steel H-Piling	22-Mar-22	30-Mar-22	8	22-Mar-22	30-Mar-22	93	0%																
	SHP-C52Xa-P1	Socketed Steel H-Piling	25-Mar-22	02-Apr-22	8	25-Mar-22	02-Apr-22	93	0%																
	SHP-C52Xa-P2	Socketed Steel H-Piling	29-Mar-22	07-Apr-22	8	29-Mar-22	07-Apr-22	93	0%																



	Planned Bar		Milestone
	Critical Bar		Critical MS
	Baseline		Baseline MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 31 Dec 2021
Based on CMWP 4th Draft



Date	Revision	Checked	Approved
06-Aug-21	1st Draft	KL	N
29-Sep-21	2nd Draft	KL	N
25-Oct-21	3rd Draft	KL	C
26-Nov-21	4th Draft	KL	
