

Zone 2A

Project Name: Foundation and ELS Works for Integrated Basement and Underground Road in Zone 2A of the West Kowloon Cultural District

3-Month Rolling Programme


Activity Description	Duration (Cal. Day)	Start Date	Finish Date	2022											
				January				February				March			
				7	14	21	28	4	11	18	25	4	11	18	25
W87	W88	W89	W90	W91	W92	W93	W94	W95	W96	W97	W98				
Zone 2A-1 Foundation, ELS Works and Blinding to Formation (KD01)															
ELS (Stage 1) - Grouting / Pipe Pile Works															
King Post (8/64 Nos Completed) & Erection of Steel Column for Working Platform (13/41 Nos completed)	356	15-May-21	5-May-22												
Socketed H-Pile Works															
Remaining Socketed H-Pile Works (53/53 Nos completed)	210	16-Jun-21	11-Jan-22												
Zone 2A-2 Foundation, ELS Works and Blinding to Formation (KD02)															
ELS (Stage 1) - Grouting / Pipe Pile Works															
King Post (0/86 Nos Completed) & Erection of Steel Column for Working Platform (0/65 Nos Completed)	193	15-Jan-22	26-Jul-22												
Stage 1a & 1b grouting (930/940 Nos Completed)	490	22-Oct-20	23-Feb-22												
Pipe Pile Construction (412/457 Nos Completed)	543	17-Nov-20	13-May-22												

- Actual
- Remaining Works
- Critical Remaining Works

Zone 2B & 2C


Activity ID	Activity Name	CMWP 4th Draft Start	CMWP 4th Draft Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	January				February				March				April			
									1				2				3				4			
									31	07	14	21	28	04	11	18	25	04	11	18	25	01	08	15

Piling for Integrated Basement and U/G Road in Zone 2B & 2C

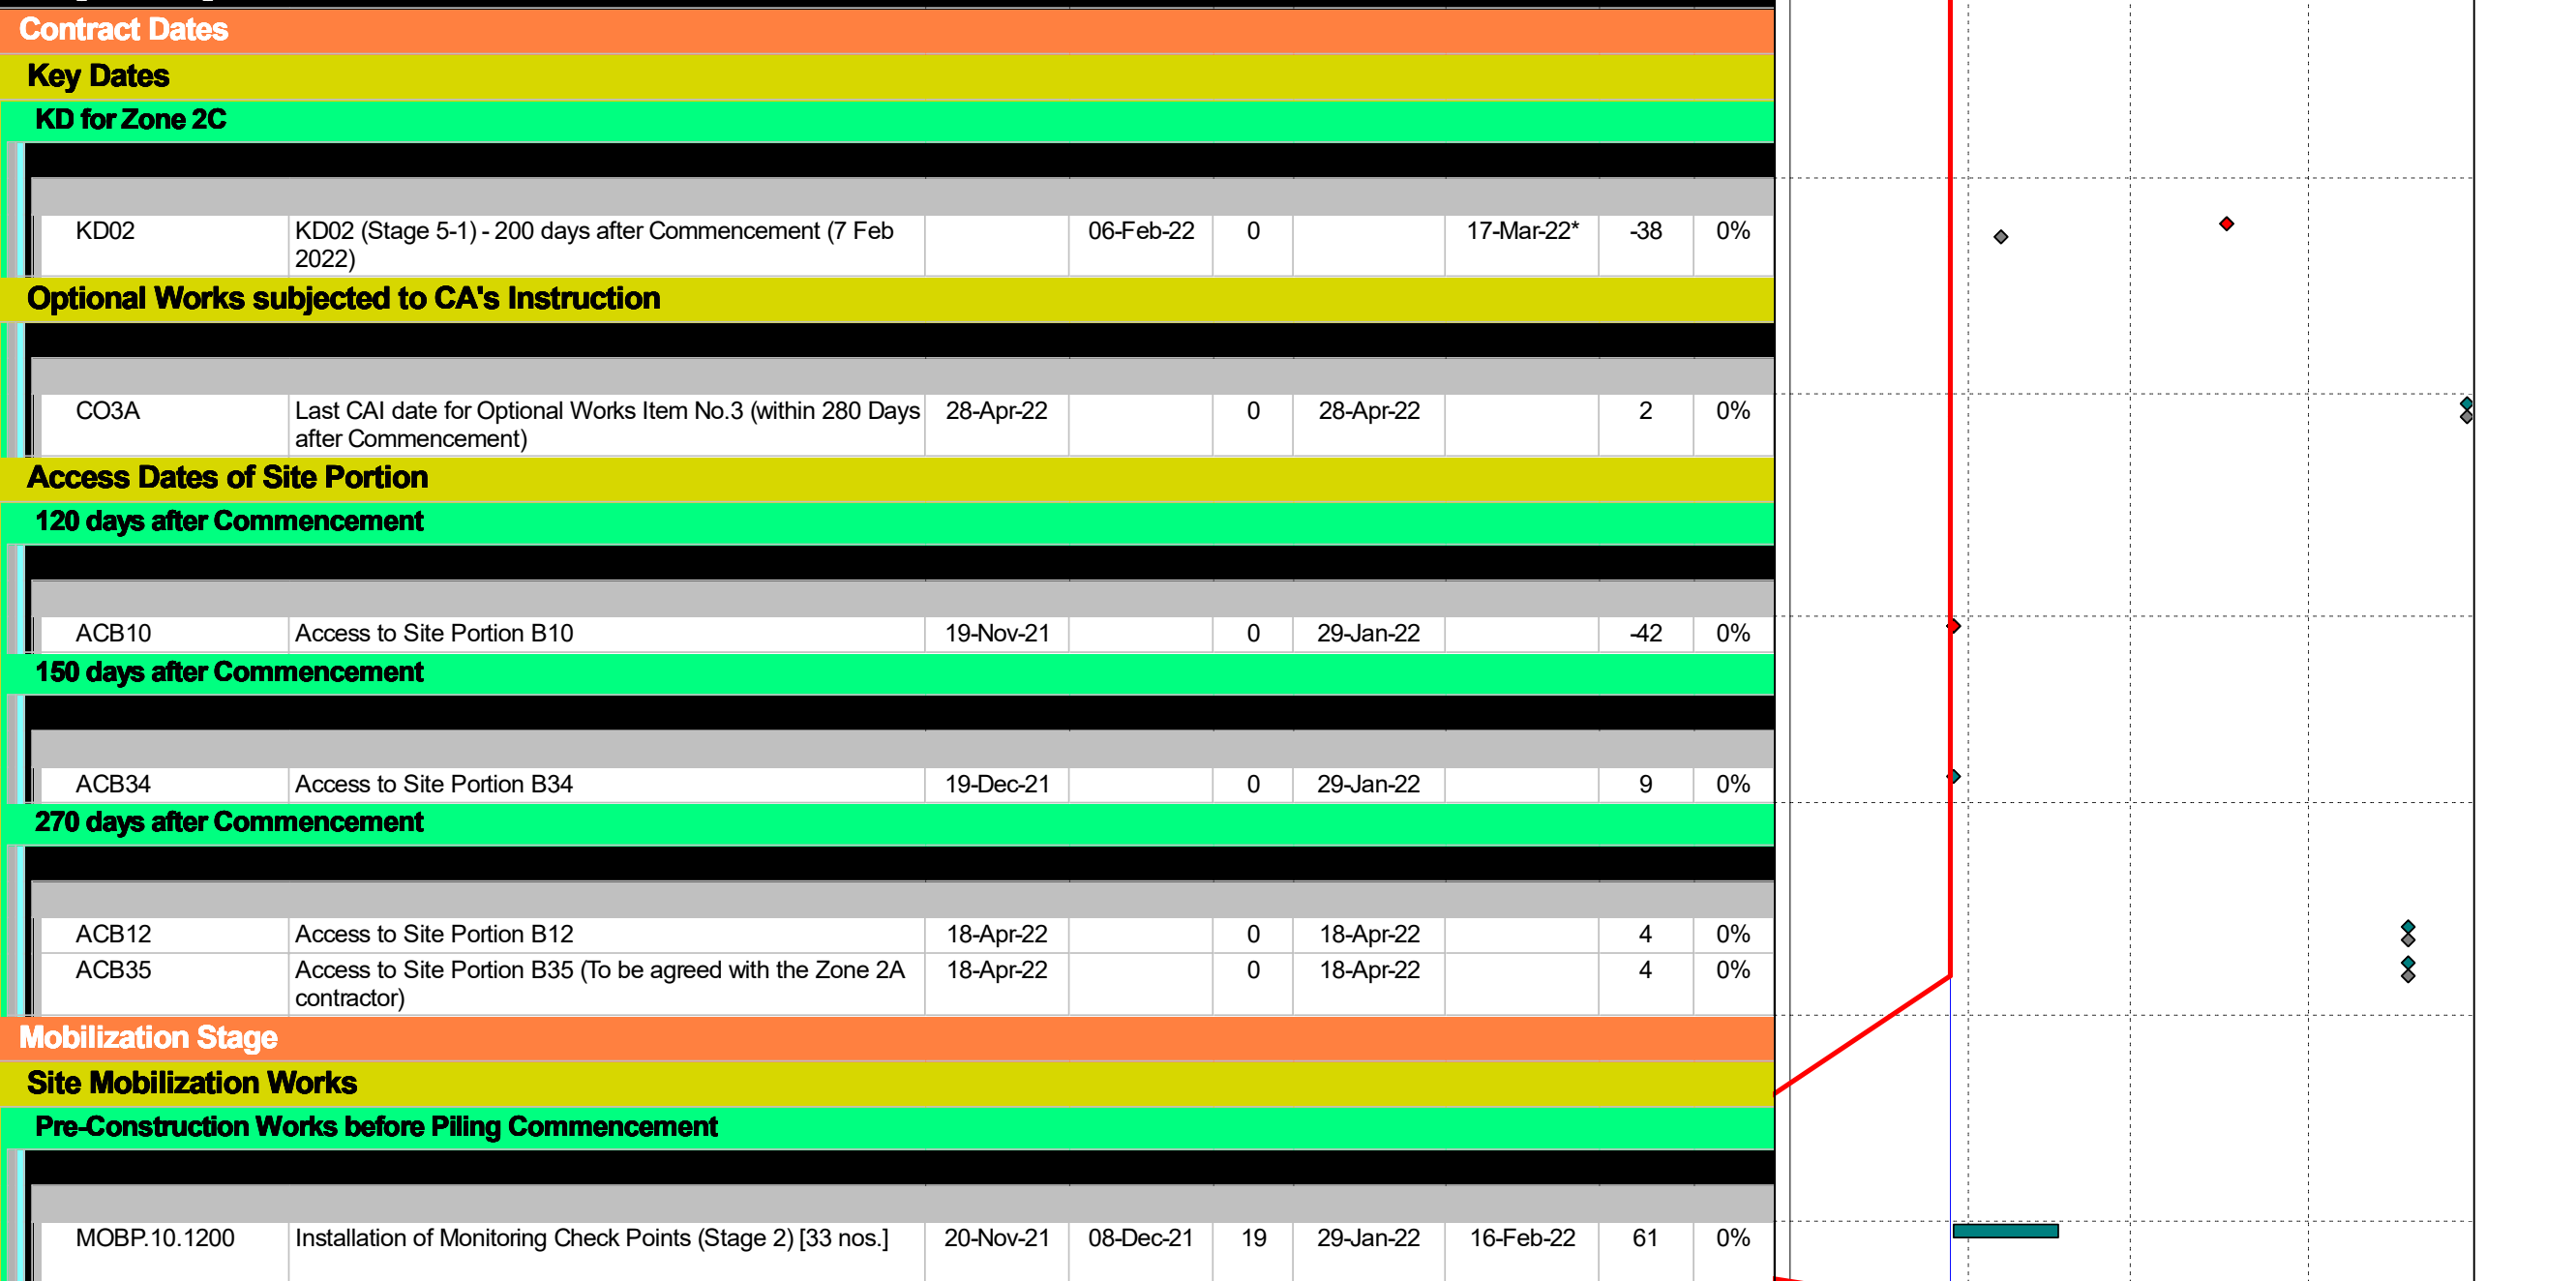

	Planned Bar		Milestone
	Critical Bar		Critical MS
	Baseline		Baseline MS

Date	Revision	Checked	Approved
06-Aug-21	1st Draft	KL	N
29-Sep-21	2nd Draft	KL	N
25-Oct-21	3rd Draft	KL	C
26-Nov-21	4th Draft	KL	B



Activity ID	Activity Name	CMWP 4th Draft Start	CMWP 4th Draft Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	January				February				March				April			
									1				2				3				4			
									31	07	14	21	28	04	11	18	25	04	11	18	25	01	08	15
MOBP.10.1220	Installation of Monitoring Check Points (Extensometer)	11-Oct-21	13-Nov-21	48	20-Nov-21 A	07-Jan-22 A		100%																
MOBP.10.1260	Erection of Hoardings (Stage 2)	20-Dec-21	31-Jan-22	29	08-Jan-22 A	05-Feb-22	132	80%																
MOBP.10.1300	Trial Pit for Drillholes & Removal of Existing Substructures / Ground Slab [503 nos]	19-Aug-21	30-Apr-22	262	19-Aug-21 A	07-May-22	130	69%																

Construction Stage

Pile Construction

Predrilling

PD.1000	Predrilling for BP in KD01 [8 nos.]	30-Sep-21	30-Mar-22	148	30-Sep-21 A	30-Mar-22	36	87%
PD.1020	Predrilling for BP in KD02 [4 nos.]	19-Nov-21	23-Dec-21	30	30-Nov-21 A	07-Jan-22 A		100%
PD.1040	Predrilling for BP in KD03 [5 nos.]	20-Oct-21	06-May-22	161	20-Oct-21 A	07-May-22	92	80%
PD.1060	Predrilling for BP in KD04 [3 nos.] incl. 1 additional no.	30-Sep-21	30-Mar-22	86	23-Sep-21 A	21-Jan-22 A		100%
PD.1080	Predrilling for BP in KD05 [76 nos.]	30-Sep-21	30-Mar-22	149	30-Sep-21 A	31-Mar-22	41	58%
PD.1100	Predrilling for BP in KD06 [95 nos.] incl. 5 additional nos.	30-Sep-21	23-May-22	187	30-Sep-21 A	23-May-22	130	41%
PD.1120	Predrilling for BP in KD07 [90 nos.] incl. 2 additional nos.	30-Sep-21	23-May-22	188	30-Sep-21 A	24-May-22	221	71%
PD.1140	Predrilling for BP in KD08 [74 nos.] incl. 1 additional no.	30-Sep-21	30-Mar-22	92	30-Sep-21 A	21-Jan-22 A		100%
PD.1160	Predrilling for BP in KD09 [149 nos.] incl. 4 additional nos.	30-Sep-21	30-Mar-22	150	30-Sep-21 A	31-Mar-22	169	48%
PD.1170	Predrilling for SSHP [12 nos.]	30-Sep-21	22-Oct-21	12	01-Dec-21 A	31-Dec-21 A		100%


KD01 (Stage 1-1)

Bored Piles

CD01									
02									
P23-BP22.30	BP - Airlift, Cage Install and Concrete	18-Jan-22	26-Jan-22	14	18-Dec-21 A	07-Jan-22 A			100%

CD07									
01									
CBA-BPC41K.10	BP - Excavation	19-Jan-22	25-Jan-22	6	29-Jan-22	08-Feb-22	5		0%
CBA-BPC41K.20	BP - RCD Drilling	26-Jan-22	09-Feb-22	10	09-Feb-22	19-Feb-22	5		0%
CBA-BPC41K.30	BP - Airlift, Cage Install and Concrete	10-Feb-22	15-Feb-22	5	21-Feb-22	25-Feb-22	38		0%

07									
CBA-BPC41Jb.10	BP - Excavation	13-Apr-22	22-Apr-22	6	07-Apr-22	13-Apr-22	10		0%
CBA-BPC41Jb.20	BP - RCD Drilling	23-Apr-22	05-May-22	10	14-Apr-22	28-Apr-22	10		0%

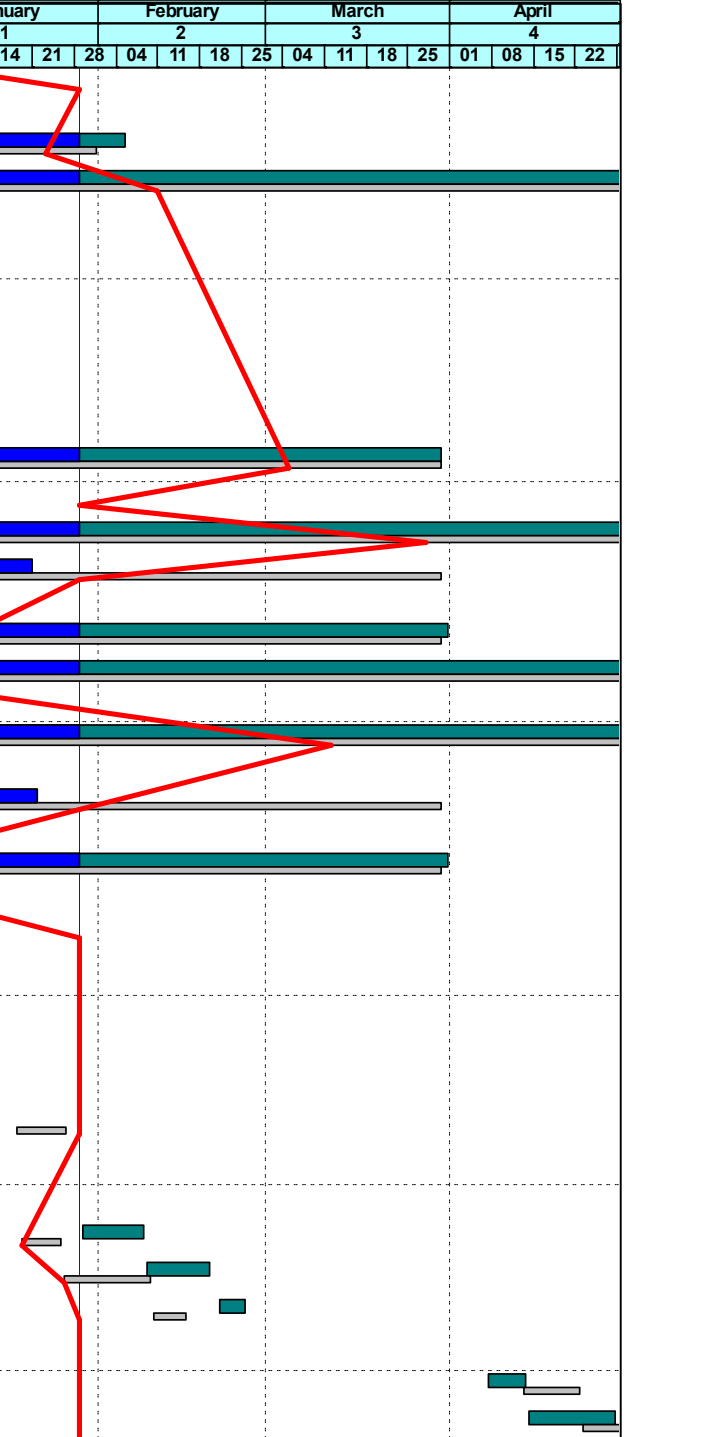

Planned Bar	Milestone
Critical Bar	Critical MS
Baseline	Baseline MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 28 Jan 2022
Based on CMWP 4th Draft

Date	Revision	Checked	Approved
06-Aug-21	1st Draft	KL	N
29-Sep-21	2nd Draft	KL	N
25-Oct-21	3rd Draft	KL	C
26-Nov-21	4th Draft	KL	B

Activity ID	Activity Name	CMWP 4th Draft Start	CMWP 4th Draft Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	January				February				March				April			
									1				2				3				4			
									31	07	14	21	28	04	11	18	25	04	11	18	25	01	08	15

14									
CBA-BP04.10	BP - Excavation	12-Apr-22	22-Apr-22	7	06-Apr-22	13-Apr-22	5	0%	
CBA-BP04.20	BP - RCD Drilling	23-Apr-22	11-May-22	14	14-Apr-22	04-May-22	5	0%	

CD05									
04									
P22&P19-BP11.10	BP - Excavation	24-Jan-22	29-Jan-22	6	19-Feb-22	25-Feb-22	18	0%	
P22&P19-BP11.20	BP - RCD Drilling	31-Jan-22	24-Feb-22	19	26-Feb-22	19-Mar-22	18	0%	
P22&P19-BP11.30	BP - Airlift, Cage Install and Concrete	25-Feb-22	05-Mar-22	8	21-Mar-22	29-Mar-22	29	0%	

05									
P22&P19-BP21.10	BP - Excavation	18-Feb-22	24-Feb-22	6	14-Mar-22	19-Mar-22	18	0%	
P22&P19-BP21.20	BP - RCD Drilling	25-Feb-22	18-Mar-22	19	21-Mar-22	12-Apr-22	18	0%	
P22&P19-BP21.30	BP - Airlift, Cage Install and Concrete	19-Mar-22	28-Mar-22	8	13-Apr-22	25-Apr-22	18	0%	

07									
P22&P19-BP29.10	BP - Excavation	04-Apr-22	11-Apr-22	12	22-Jan-22 A	08-Feb-22	52	0%	
P22&P19-BP29.20	BP - RCD Drilling	12-Apr-22	07-May-22	19	09-Feb-22	02-Mar-22	52	0%	
P22&P19-BP29.30	BP - Airlift, Cage Install and Concrete	10-May-22	18-May-22	8	03-Mar-22	11-Mar-22	52	0%	

CD03									
06									
P23-BP06.10	BP - Excavation	02-Apr-22	09-Apr-22	34	24-Dec-21 A	08-Feb-22	52	0%	
P23-BP06.20	BP - RCD Drilling	11-Apr-22	06-May-22	19	09-Feb-22	02-Mar-22	52	0%	
P23-BP06.30	BP - Airlift, Cage Install and Concrete	07-May-22	17-May-22	8	03-Mar-22	11-Mar-22	52	0%	


KD02 (Stage 5-1)

KD02.BP.0040	Review and Confirmation of Rockhead and Founding Level of the 1st Pile by CA	19-Nov-21	02-Dec-21	63	03-Dec-21 A	03-Feb-22	-42	57.14%	
--------------	--	-----------	-----------	----	-------------	-----------	-----	--------	--

Bored Piles

CD01									
04									
P23-BP43.10	BP - Excavation	03-Dec-21	09-Dec-21	9	21-Dec-21 A	04-Jan-22 A		100%	
P23-BP43.20	BP - RCD Drilling	10-Dec-21	30-Dec-21	13	05-Jan-22 A	20-Jan-22 A		100%	
P23-BP43.30	BP - Airlift, Cage Install and Concrete	31-Dec-21	10-Jan-22	17	21-Jan-22 A	12-Feb-22	-5	0%	

TD04									
01									
P23-BP76.10	BP - Excavation	03-Dec-21	09-Dec-21	34	24-Dec-21 A	08-Feb-22	-33	0%	
P23-BP76.20	BP - RCD Drilling	10-Dec-21	30-Dec-21	16	09-Feb-22	26-Feb-22	-33	0%	
P23-BP76.30	BP - Airlift, Cage Install and Concrete	31-Dec-21	10-Jan-22	8	28-Feb-22	08-Mar-22	-33	0%	

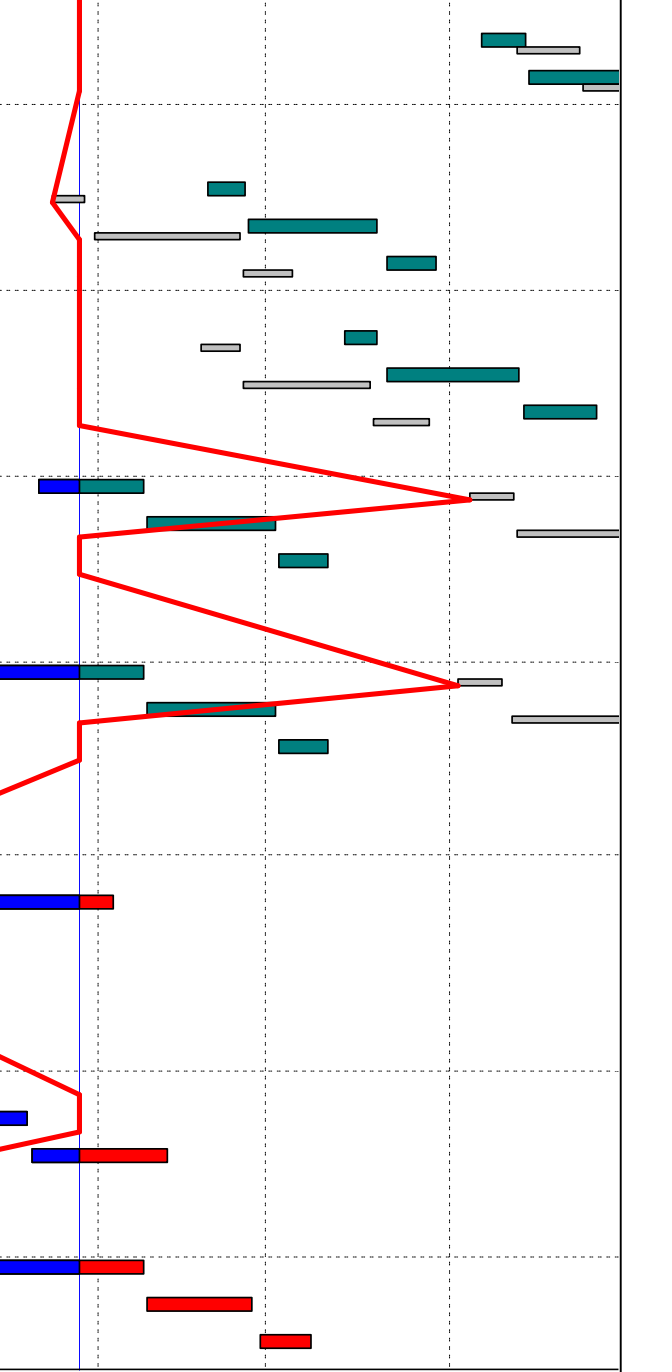


Planned Bar	Milestone
Critical Bar	Critical MS
Baseline	Baseline MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 28 Jan 2022
 Based on CMWP 4th Draft

Date	Revision	Checked	Approved
06-Aug-21	1st Draft	KL	N
29-Sep-21	2nd Draft	KL	N
25-Oct-21	3rd Draft	KL	C
26-Nov-21	4th Draft	KL	B



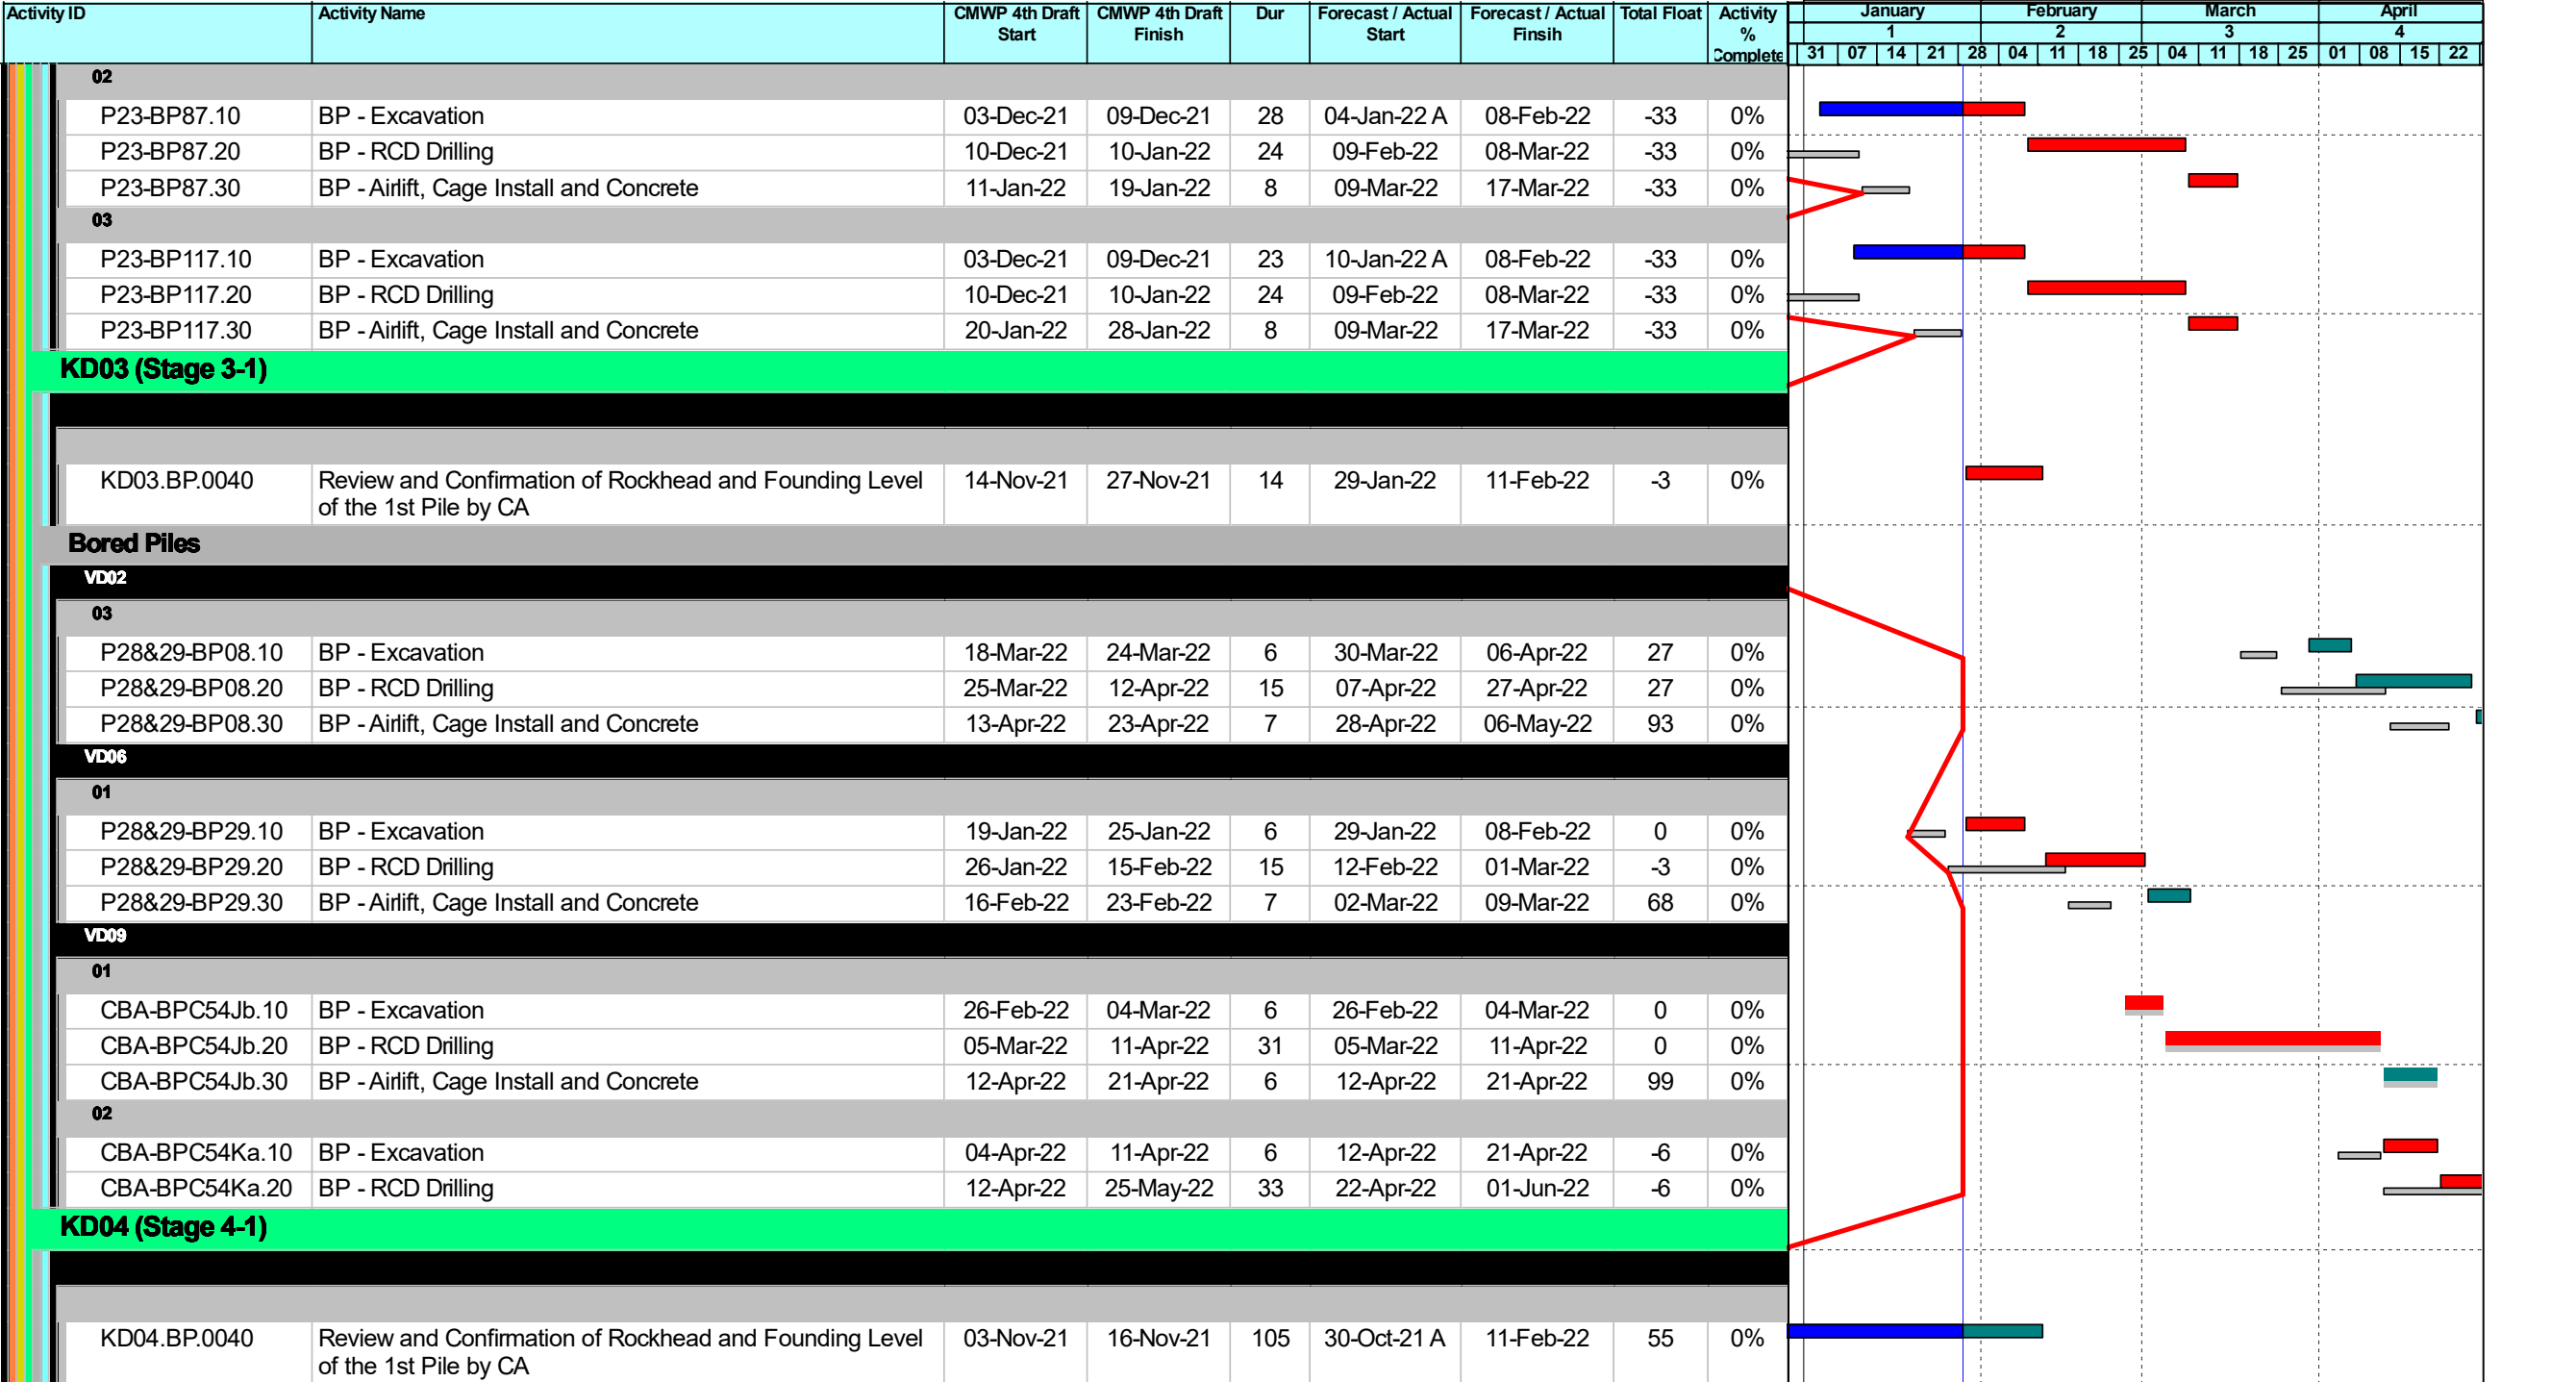

	Planned Bar		Milestone
	Critical Bar		Critical MS
	Baseline		Baseline MS

West Kowloon Cultural District Authority
Piling for Retained Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 28 Jan 2022
 Based on CMWP 4th Draft


	Date	Revision	Checked	Approved
	06-Aug-21	1st Draft	KL	N
	29-Sep-21	2nd Draft	KL	N
	25-Oct-21	3rd Draft	KL	C
	26-Nov-21	4th Draft	KL	B

Activity ID	Activity Name	CMWP 4th Draft Start	CMWP 4th Draft Finish	Dur	Forecast / Actual Start	Forecast / Actual Finish	Total Float	Activity % Complete	January				February				March				April			
									1				2				3				4			
									31	07	14	21	28	04	11	18	25	04	11	18	25	01	08	15

Bored Piles									
TD09									
01									
CBA-BPC54V.10	BP - Excavation	08-Apr-22	14-Apr-22	6	08-Apr-22	14-Apr-22	0	0%	
CBA-BPC54V.20	BP - RCD Drilling	19-Apr-22	29-Apr-22	10	19-Apr-22	29-Apr-22	0	0%	

KD05 (Section 1)

Bored Piles									
CD01									
01									
P23-BP30.20	BP - RCD Drilling	06-Dec-21	22-Dec-21	16	13-Dec-21 A	04-Jan-22 A		100%	
P23-BP30.30	BP - Airlift, Cage Install and Concrete	23-Dec-21	03-Jan-22	12	05-Jan-22 A	19-Jan-22 A		100%	
03									
P23-BP20.10	BP - Excavation	11-Jan-22	17-Jan-22	6	29-Jan-22	08-Feb-22	67	0%	
P23-BP20.20	BP - RCD Drilling	18-Jan-22	07-Feb-22	15	09-Feb-22	25-Feb-22	67	0%	
P23-BP20.30	BP - Airlift, Cage Install and Concrete	08-Feb-22	15-Feb-22	7	26-Feb-22	05-Mar-22	169	0%	
07									
P23-BP19.10	BP - Excavation	12-Mar-22	18-Mar-22	14	20-Jan-22 A	08-Feb-22	164	0%	
P23-BP19.20	BP - RCD Drilling	19-Mar-22	11-Apr-22	19	09-Feb-22	02-Mar-22	164	0%	
P23-BP19.30	BP - Airlift, Cage Install and Concrete	12-Apr-22	23-Apr-22	8	03-Mar-22	11-Mar-22	164	0%	
08									
P23-BP32.10	BP - Excavation	04-Apr-22	11-Apr-22	8	13-Jan-22 A	22-Jan-22 A		100%	
P23-BP32.20	BP - RCD Drilling	12-Apr-22	03-May-22	20	24-Jan-22 A	18-Feb-22	175	0%	
P23-BP32.30	BP - Airlift, Cage Install and Concrete	04-May-22	12-May-22	7	19-Feb-22	26-Feb-22	175	0%	
16									
P23-BP31.10	BP - Excavation	13-Jun-22	18-Jun-22	6	18-Mar-22	24-Mar-22	131	0%	
P23-BP31.20	BP - RCD Drilling	20-Jun-22	07-Jul-22	15	25-Mar-22	12-Apr-22	131	0%	
P23-BP31.30	BP - Airlift, Cage Install and Concrete	08-Jul-22	15-Jul-22	7	13-Apr-22	23-Apr-22	131	0%	
CD07									
02									
CBA-BPC43K.10	BP - Excavation	31-Jan-22	09-Feb-22	6	14-Feb-22	19-Feb-22	5	0%	
CBA-BPC43K.20	BP - RCD Drilling	10-Feb-22	21-Feb-22	10	21-Feb-22	03-Mar-22	5	0%	
CBA-BPC43K.30	BP - Airlift, Cage Install and Concrete	22-Feb-22	26-Feb-22	5	04-Mar-22	09-Mar-22	33	0%	
03									
CBA-BPC44Jb.10	BP - Excavation	14-Feb-22	21-Feb-22	40	18-Dec-21 A	09-Feb-22	10	0%	
CBA-BPC44Jb.20	BP - RCD Drilling	22-Feb-22	09-Mar-22	14	10-Feb-22	25-Feb-22	10	0%	
CBA-BPC44Jb.30	BP - Airlift, Cage Install and Concrete	10-Mar-22	16-Mar-22	6	26-Feb-22	04-Mar-22	170	0%	

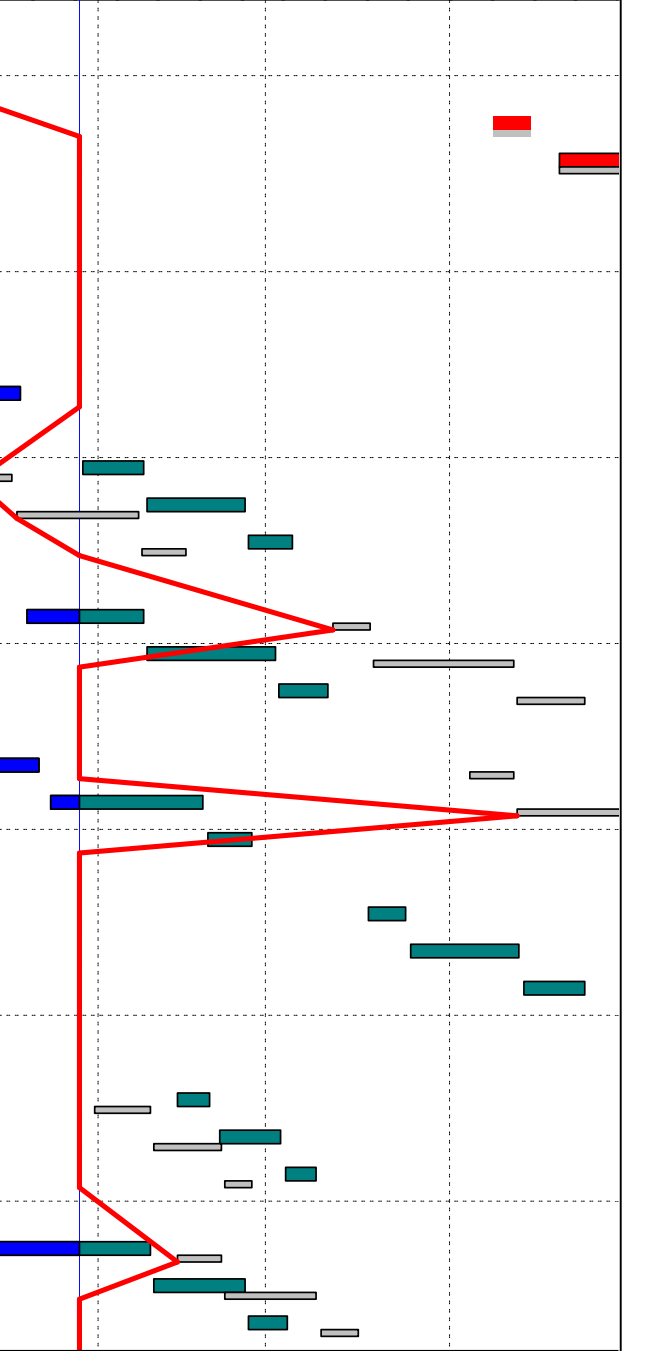


	Planned Bar		Milestone
	Critical Bar		Critical MS
	Baseline		Baseline MS

West Kowloon Cultural District Authority
Piling for Retained Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 28 Jan 2022
 Based on CMWP 4th Draft



Date	Revision	Checked	Approved
06-Aug-21	1st Draft	KL	N
29-Sep-21	2nd Draft	KL	N
25-Oct-21	3rd Draft	KL	C
26-Nov-21	4th Draft	KL	B

Activity ID	Activity Name	CMWP 4th Draft Start	CMWP 4th Draft Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	January				February				March				April			
									1				2				3				4			
									31	07	14	21	28	04	11	18	25	04	11	18	25	01	08	15


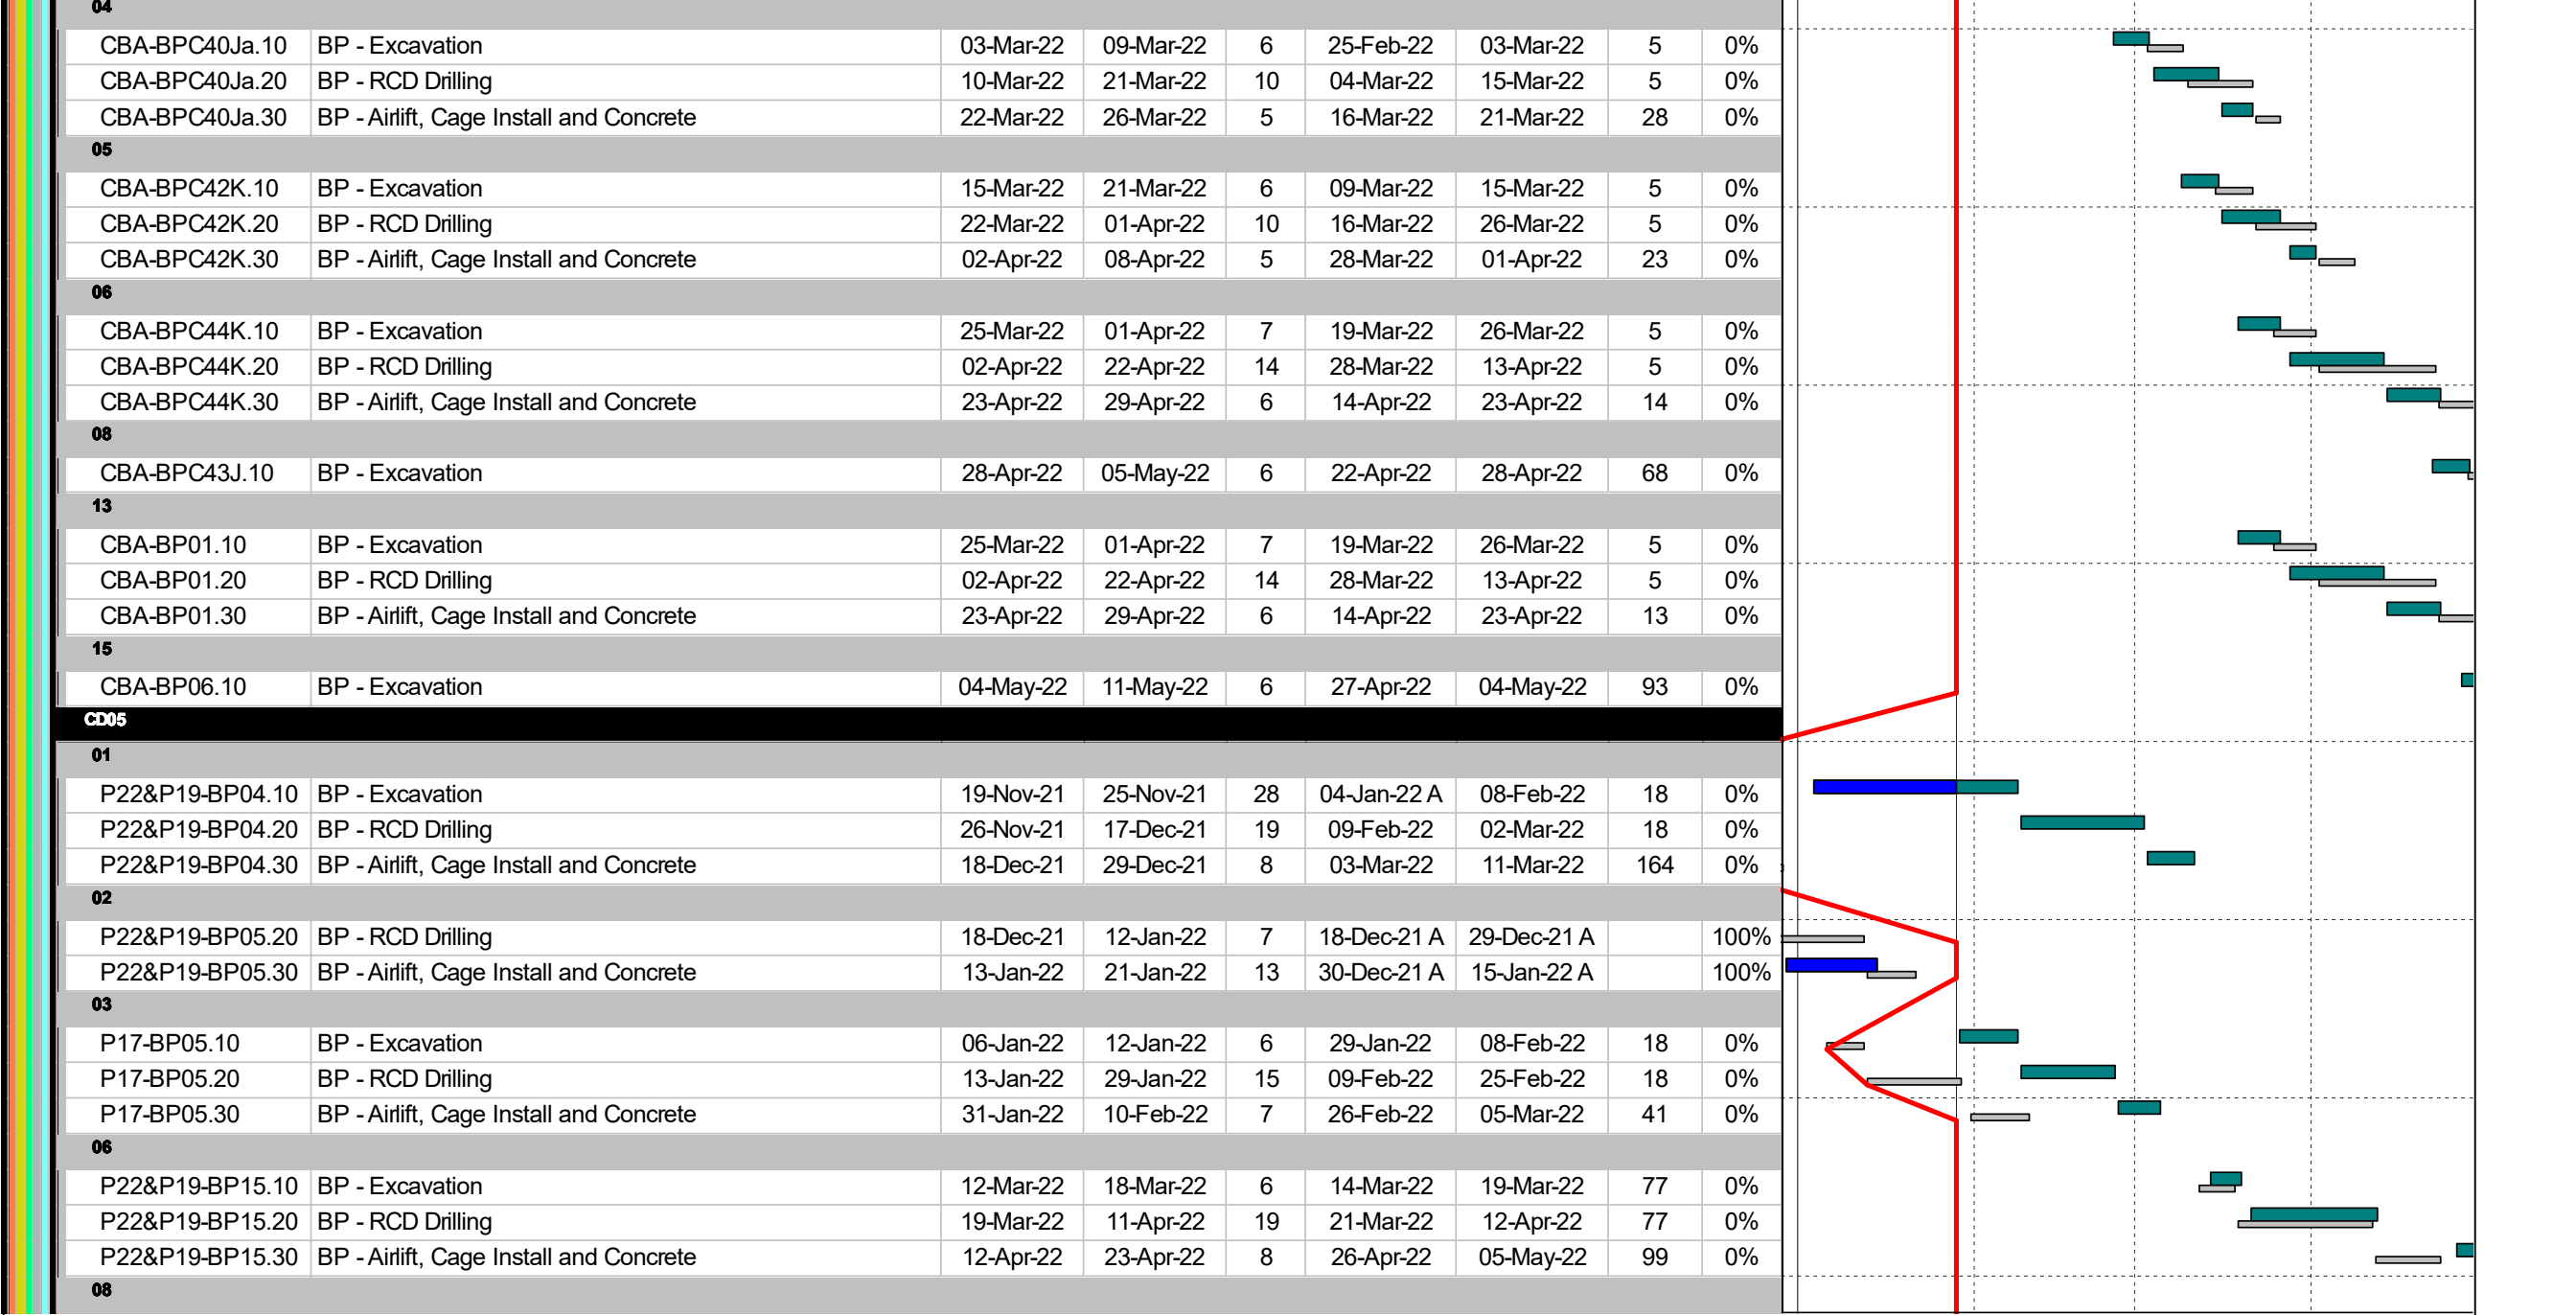


	Planned Bar		Milestone
	Critical Bar		Critical MS
	Baseline		Baseline MS

West Kowloon Cultural District Authority
Piling for Retaining Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 28 Jan 2022
Based on CMWP 4th Draft





Date	Revision	Checked	Approved
06-Aug-21	1st Draft	KL	N
29-Sep-21	2nd Draft	KL	N
25-Oct-21	3rd Draft	KL	C
26-Nov-21	4th Draft	KL	B

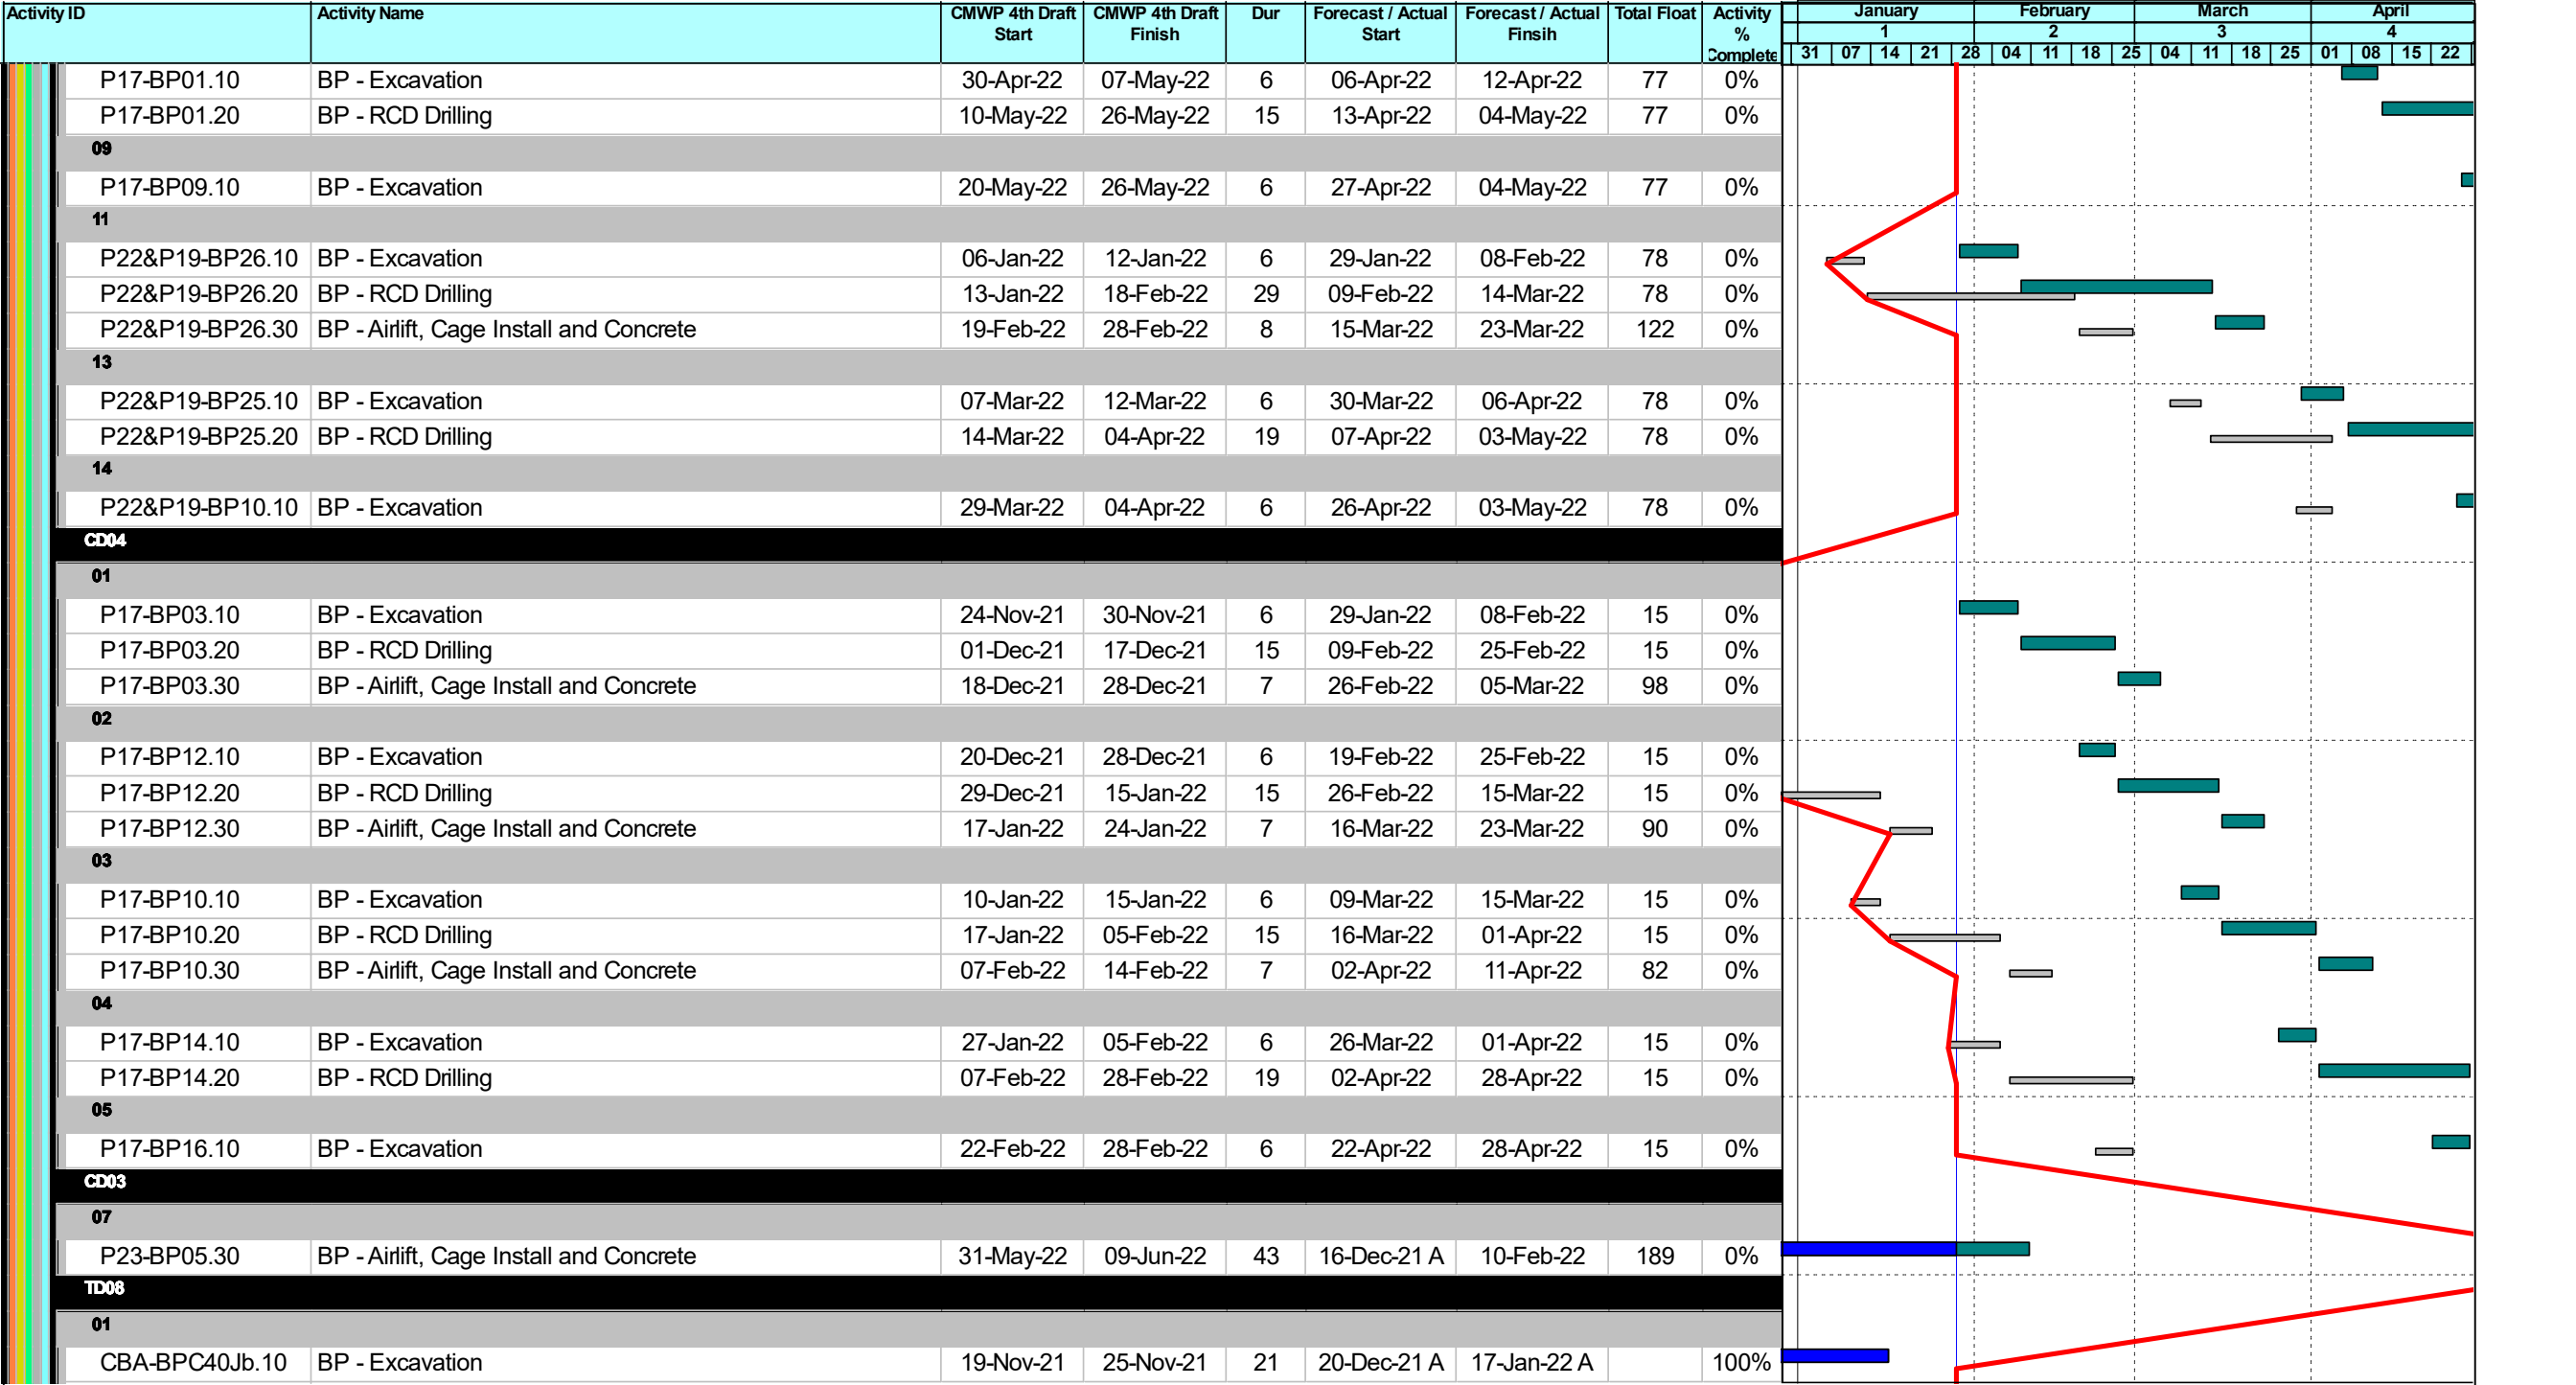

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 28 Jan 2022
Based on CMWP 4th Draft




Date	Revision	Checked	Approved
06-Aug-21	1st Draft	KL	N
29-Sep-21	2nd Draft	KL	N
25-Oct-21	3rd Draft	KL	C
26-Nov-21	4th Draft	KL	B

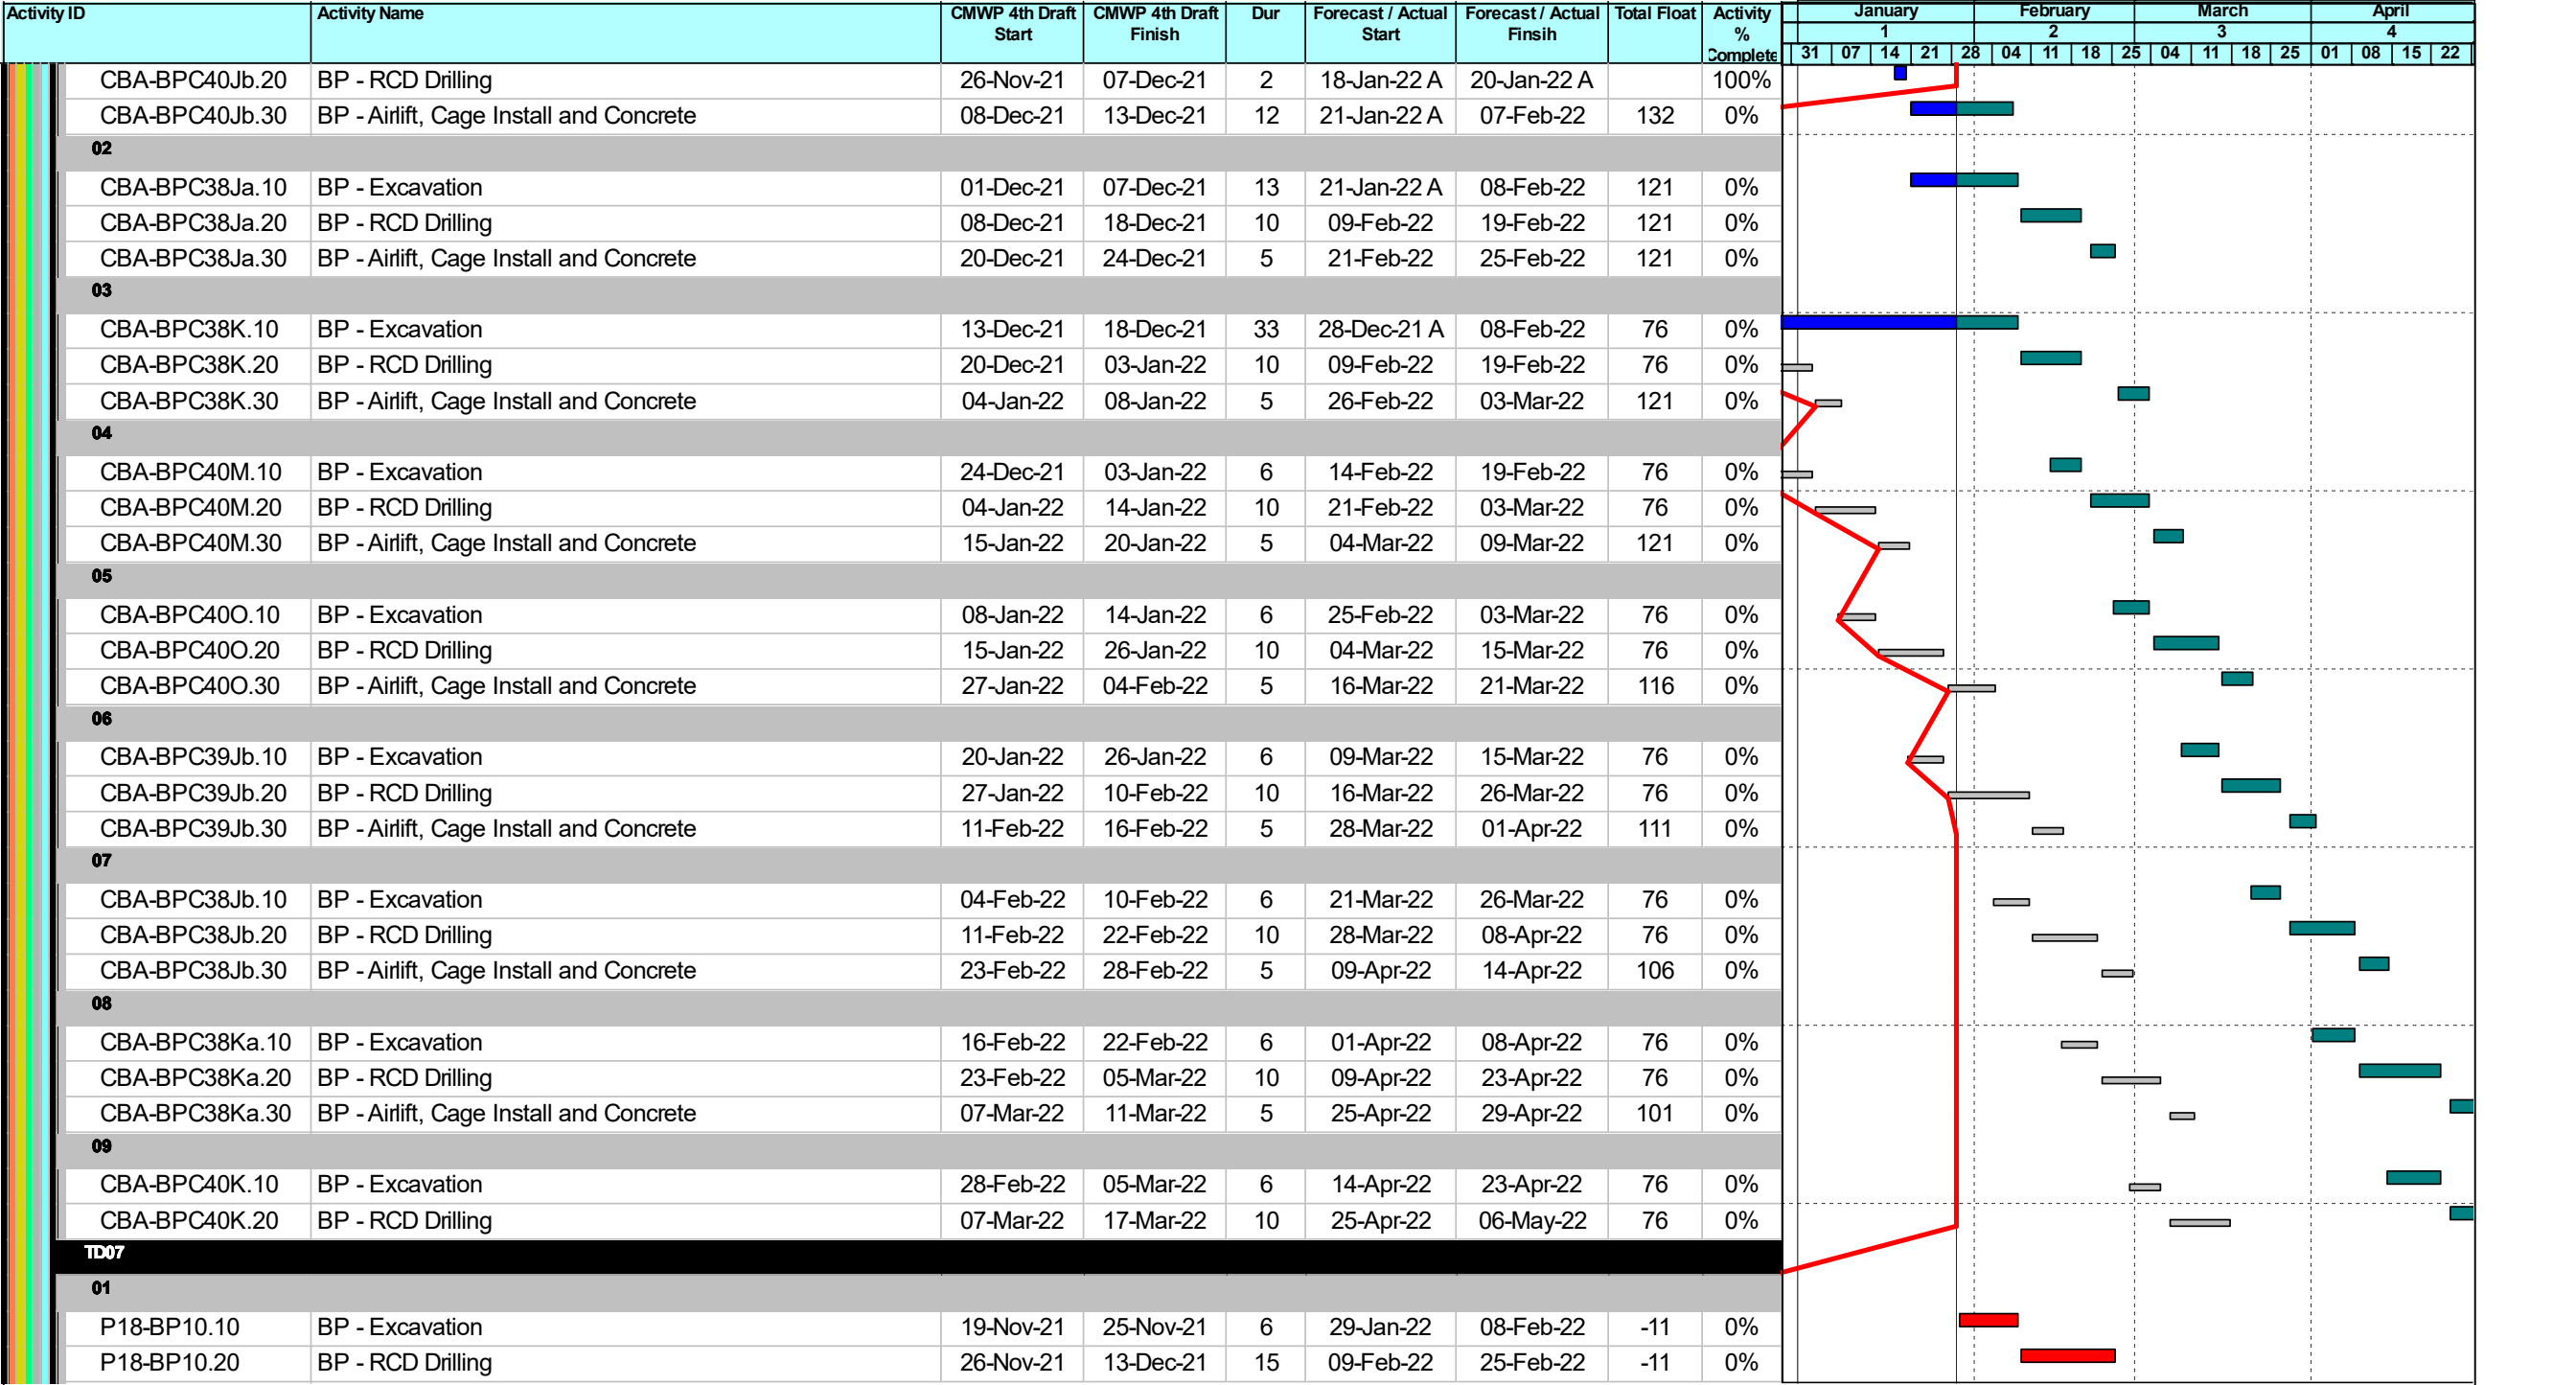

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 28 Jan 2022
 Based on CMWP 4th Draft



Date	Revision	Checked	Approved
06-Aug-21	1st Draft	KL	N
29-Sep-21	2nd Draft	KL	N
25-Oct-21	3rd Draft	KL	C
26-Nov-21	4th Draft	KL	B

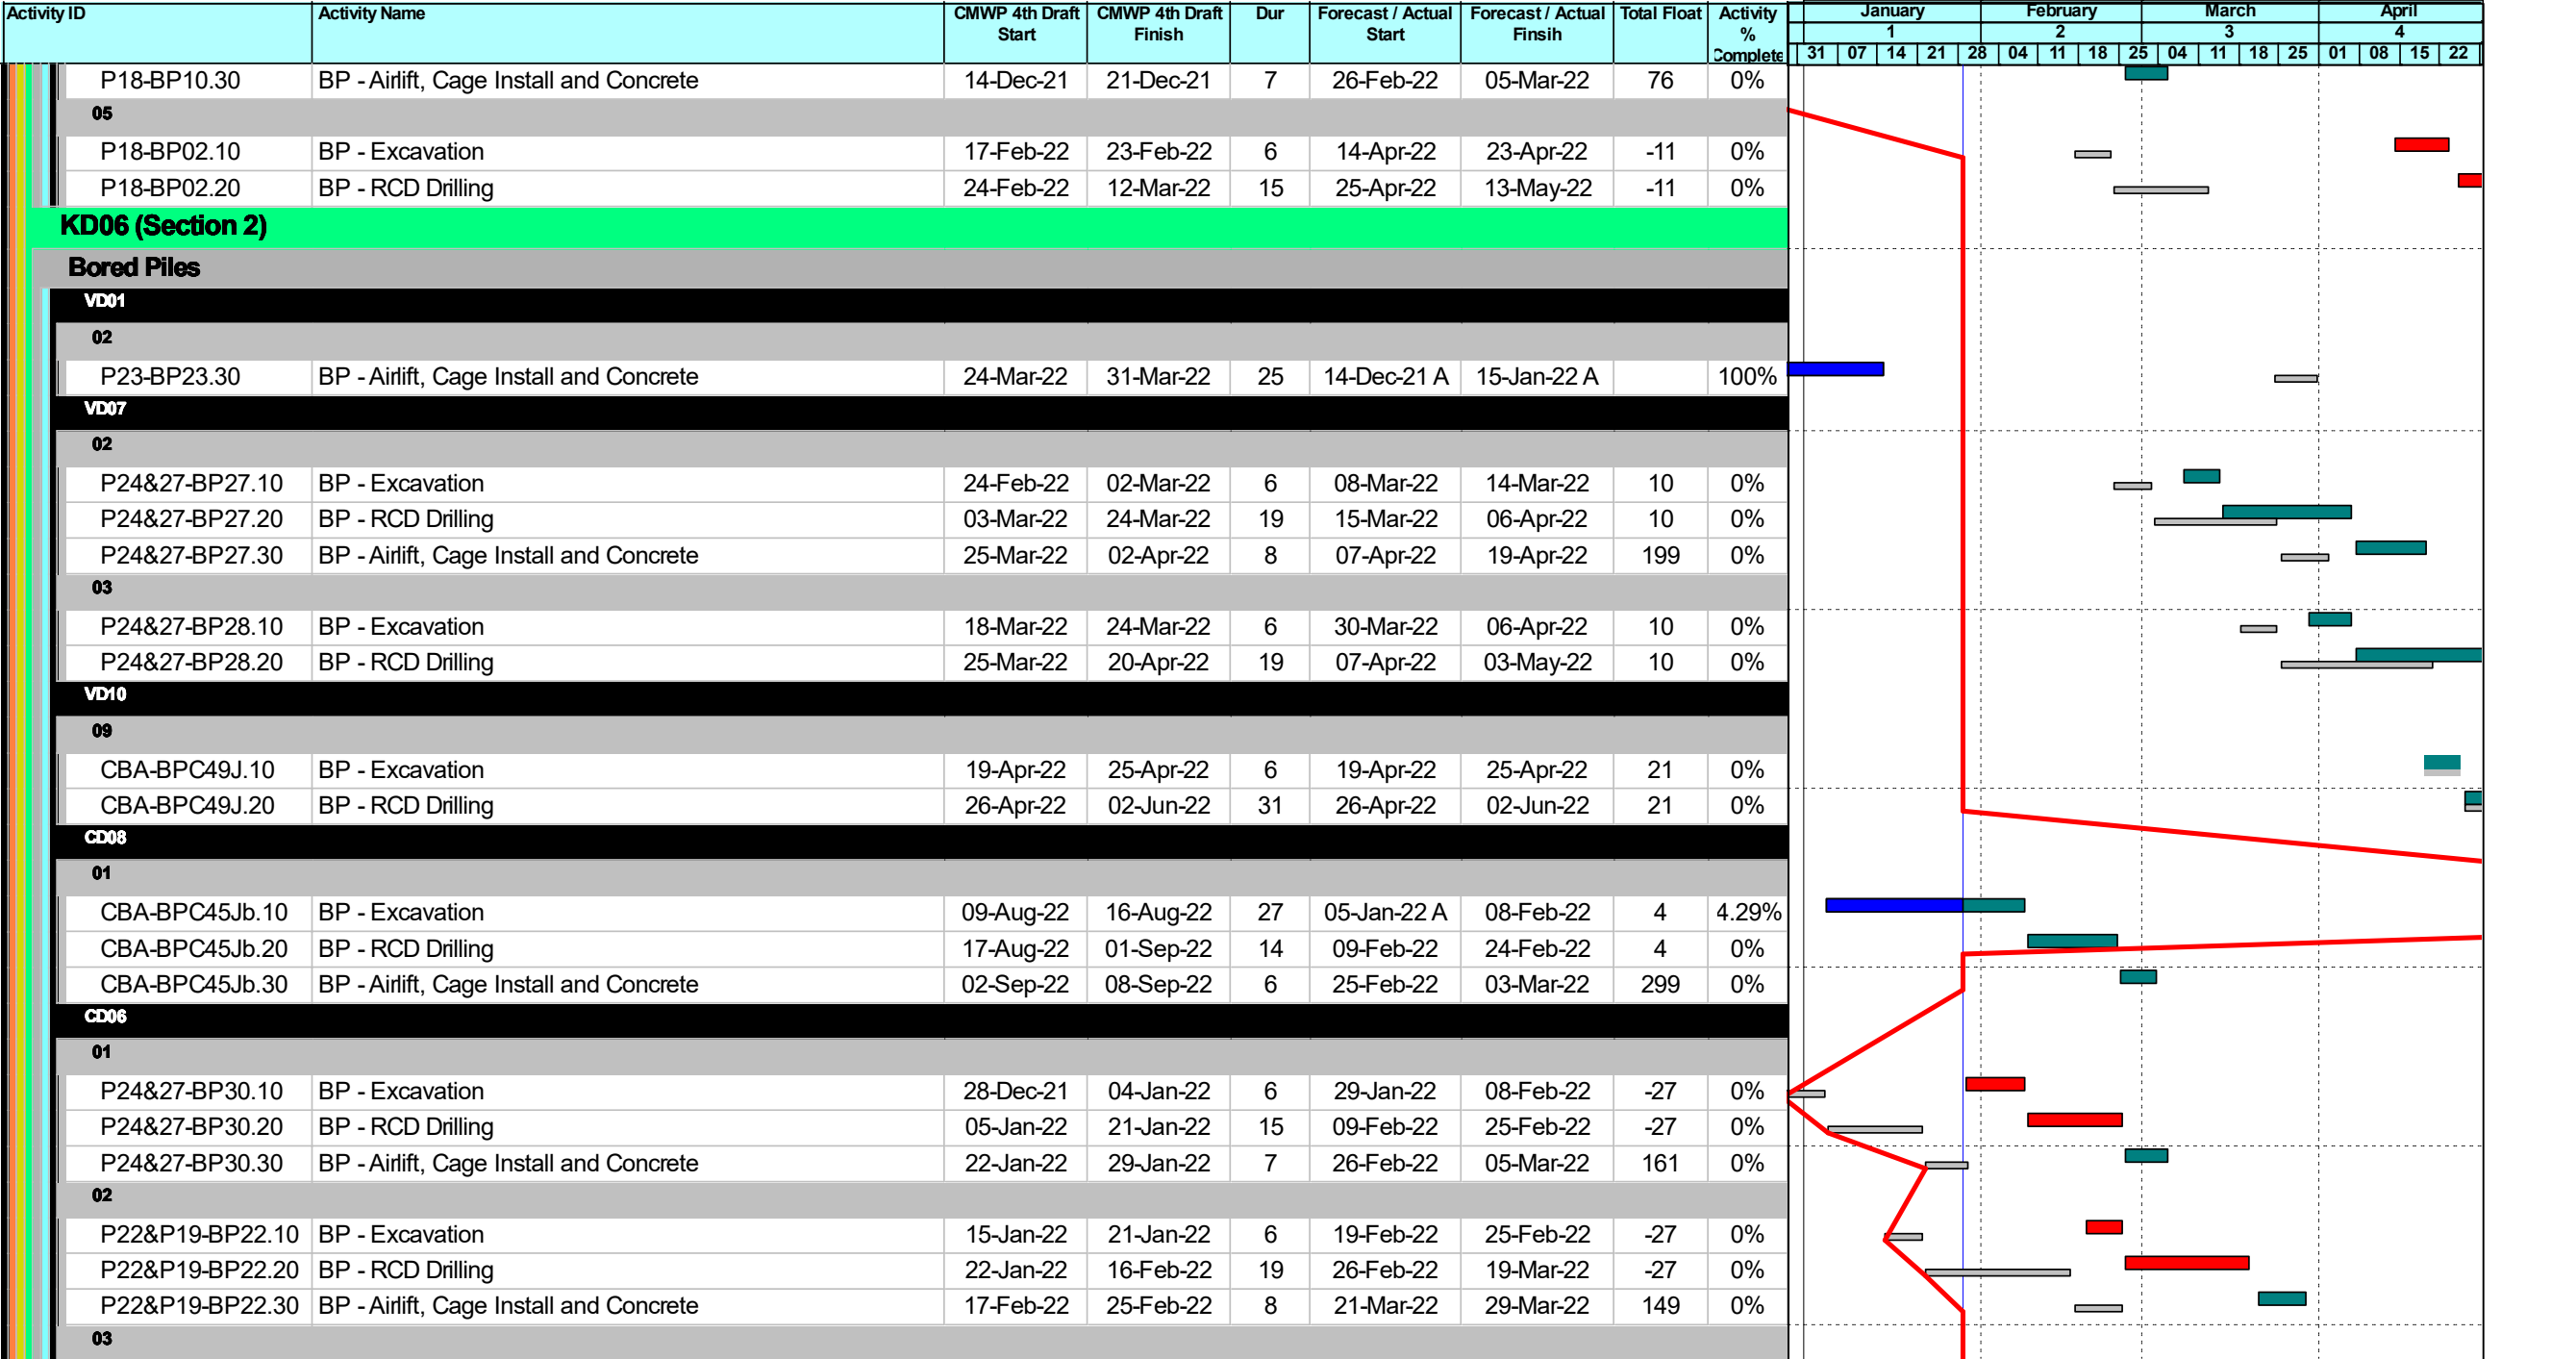


- Planned Bar
- Critical Bar
- Baseline
- ◆ Milestone
- ◆ Critical MS
- ◆ Baseline MS

West Kowloon Cultural District Authority
Piling for Retaining Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 28 Jan 2022
 Based on CMWP 4th Draft




Date	Revision	Checked	Approved
06-Aug-21	1st Draft	KL	N
29-Sep-21	2nd Draft	KL	N
25-Oct-21	3rd Draft	KL	C
26-Nov-21	4th Draft	KL	B

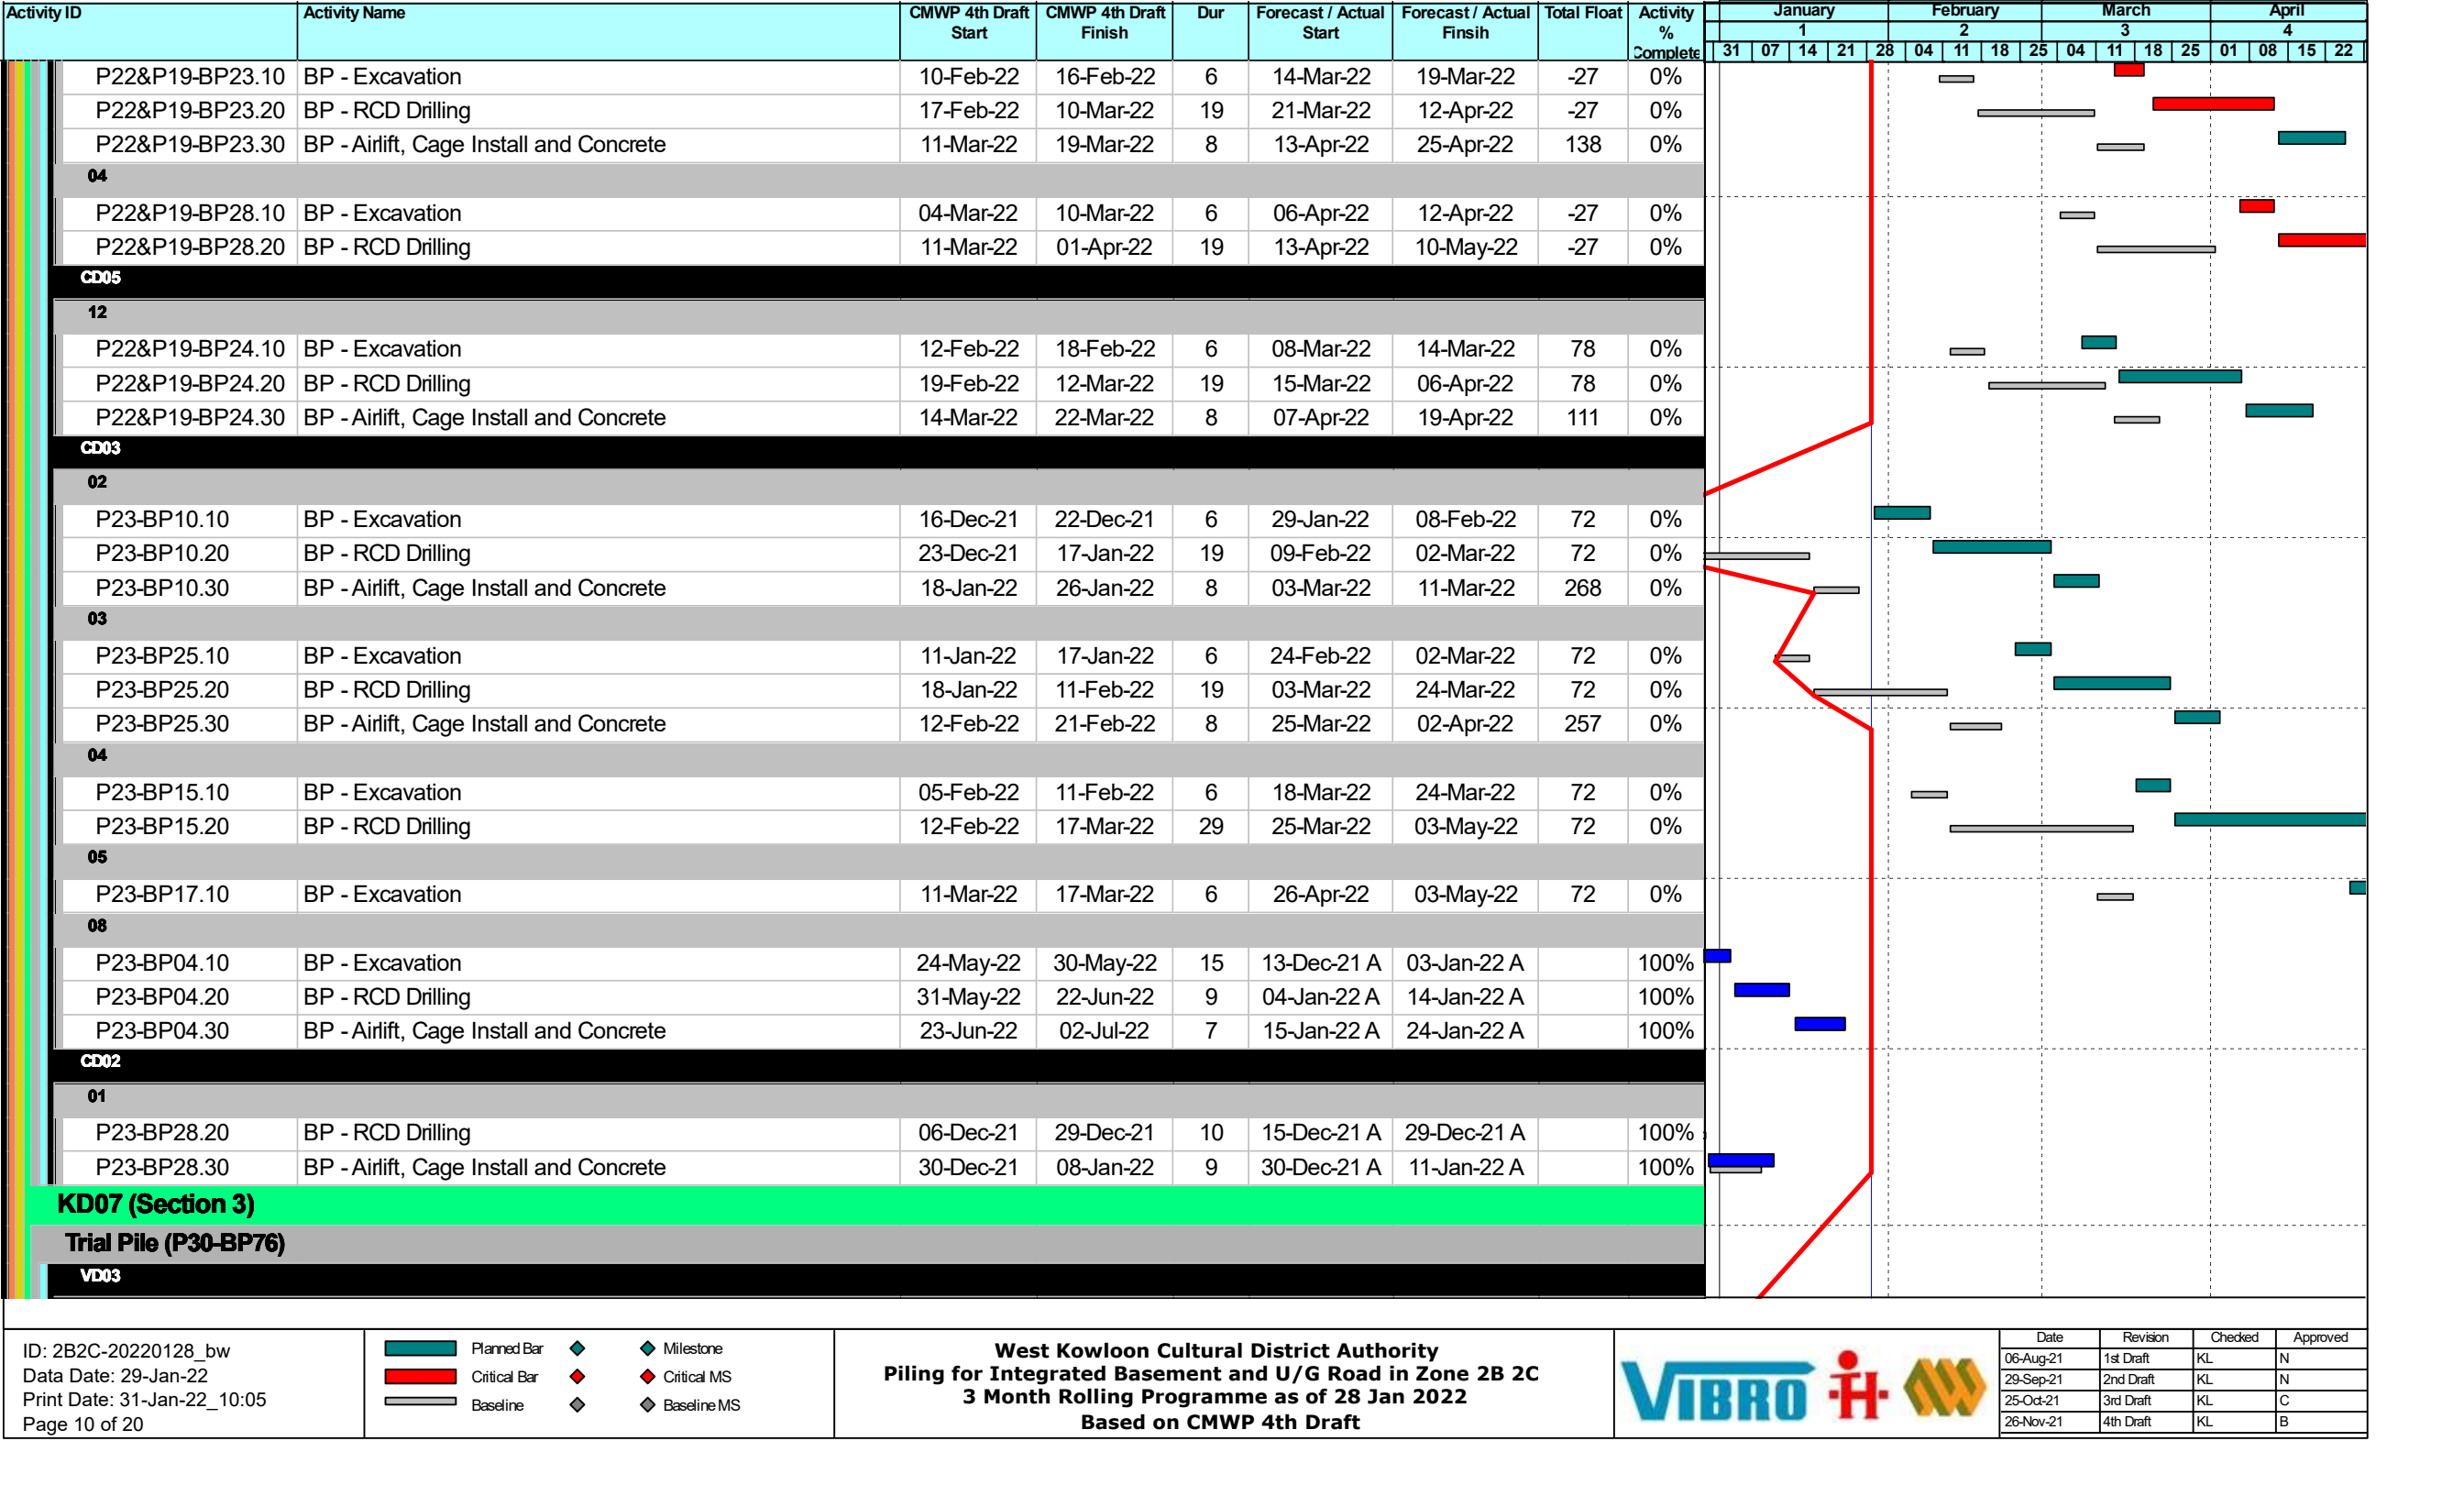

 Planned Bar
  Milestone
 Critical Bar
  Critical MS
 Baseline
  Baseline MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 28 Jan 2022
Based on CMWP 4th Draft





Date	Revision	Checked	Approved
06-Aug-21	1st Draft	KL	N
29-Sep-21	2nd Draft	KL	N
25-Oct-21	3rd Draft	KL	C
26-Nov-21	4th Draft	KL	B

Activity ID	Activity Name	CMWP 4th Draft Start	CMWP 4th Draft Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	January				February				March				April			
									1				2				3				4			
									31	07	14	21	28	04	11	18	25	04	11	18	25	01	08	15

01									
P30-BP76.10	BP (Trial Pile for Schedule 1) - Excavation	29-Dec-21	05-Jan-22	16	17-Jan-22 A	07-Feb-22	-6	6.67%	
P30-BP76.20	BP (Trial Pile for Schedule 1) - RCD Drilling	06-Jan-22	01-Mar-22	44	08-Feb-22	30-Mar-22	-6	0%	
P30-BP76.30	BP (Trial Pile for Schedule 1) - Airlift, Cage Install and Concrete	02-Mar-22	11-Mar-22	9	31-Mar-22	11-Apr-22	-6	0%	

VD02									
KD07.BP.0020	Review and Confirmation of Rockhead and Founding Level of the 1st Pile by CA	14-Nov-21	27-Nov-21	77	13-Nov-21 A	29-Jan-22	-7	100%	

Trial Pile (P24&P27-BP34)

VD02									
01									
P24&27-BP34.10	BP (Trial Pile for Schedule 2) - Excavation	18-Jan-22	24-Jan-22	15	19-Jan-22 A	08-Feb-22	3	0%	
P24&27-BP34.20	BP (Trial Pile for Schedule 2) - RCD Drilling	25-Jan-22	18-Feb-22	19	09-Feb-22	02-Mar-22	3	0%	
P24&27-BP34.30	BP (Trial Pile for Schedule 2) - Airlift, Cage Install and Concrete	19-Feb-22	28-Feb-22	8	03-Mar-22	11-Mar-22	3	0%	

VD02									
KD07.BP.0060	Review and Confirmation of Rockhead and Founding Level of the 1st Pile by CA	23-Oct-21	05-Nov-21	77	13-Nov-21 A	29-Jan-22	-7	100%	


Bored Piles

VD01									
03									
P26-BP08.10	BP - Excavation	17-Mar-22	23-Mar-22	75	25-Nov-21 A	26-Feb-22	40	0%	
P26-BP08.20	BP - RCD Drilling	24-Mar-22	19-Apr-22	19	28-Feb-22	21-Mar-22	40	0%	
P26-BP08.30	BP - Airlift, Cage Install and Concrete	20-Apr-22	28-Apr-22	8	22-Mar-22	30-Mar-22	191	0%	
05									
P26-BP11.10	BP - Excavation	19-May-22	25-May-22	6	22-Apr-22	28-Apr-22	40	0%	

VD02									
02									
P24&27-BP08.10	BP - Excavation	12-Feb-22	18-Feb-22	6	24-Feb-22	02-Mar-22	27	0%	
P24&27-BP08.20	BP - RCD Drilling	19-Feb-22	24-Mar-22	29	03-Mar-22	06-Apr-22	27	0%	
P24&27-BP08.30	BP - Airlift, Cage Install and Concrete	25-Mar-22	02-Apr-22	8	07-Apr-22	19-Apr-22	100	0%	

04									
P26-BP03.10	BP - Excavation	06-Apr-22	12-Apr-22	6	21-Apr-22	27-Apr-22	27	0%	
P26-BP03.20	BP - RCD Drilling	13-Apr-22	21-May-22	29	28-Apr-22	02-Jun-22	27	0%	

08									
P24&27-BP02.10	BP - Excavation	02-Sep-22	08-Sep-22	40	17-Dec-21 A	08-Feb-22	315	0%	

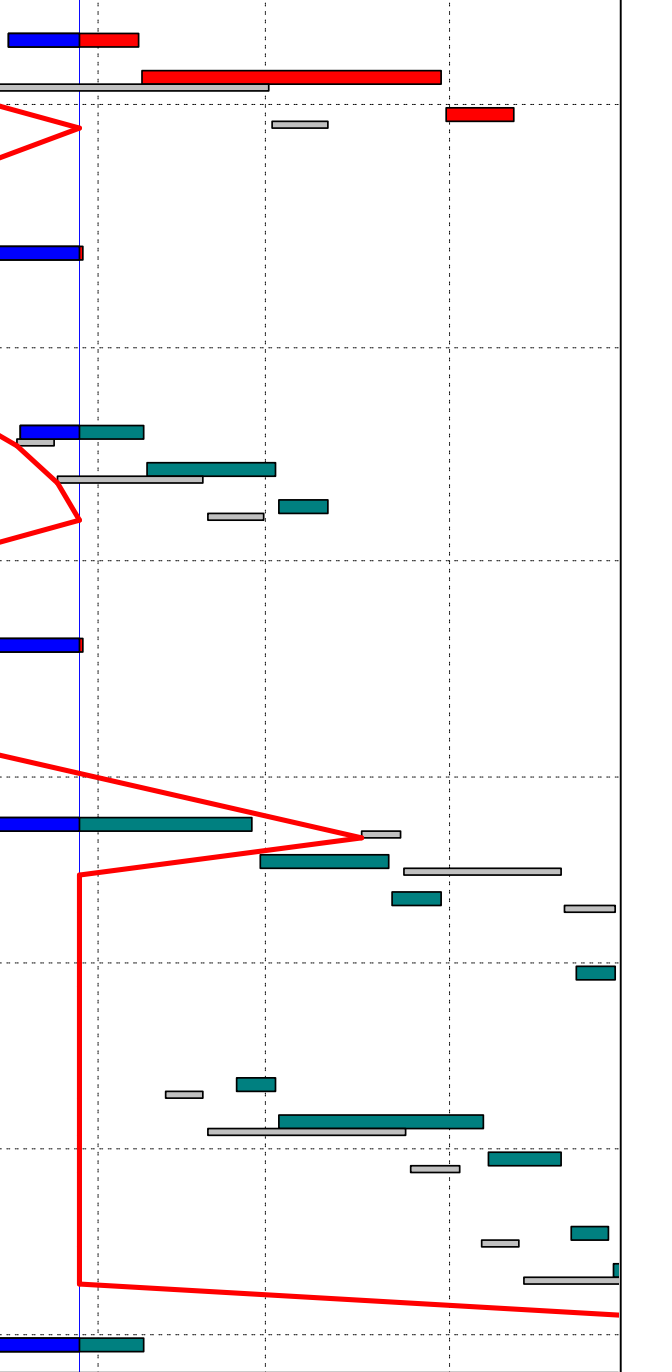


	Planned Bar		Milestone
	Critical Bar		Critical MS
	Baseline		Baseline MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 28 Jan 2022
Based on CMWP 4th Draft



Date	Revision	Checked	Approved
06-Aug-21	1st Draft	KL	N
29-Sep-21	2nd Draft	KL	N
25-Oct-21	3rd Draft	KL	C
26-Nov-21	4th Draft	KL	B

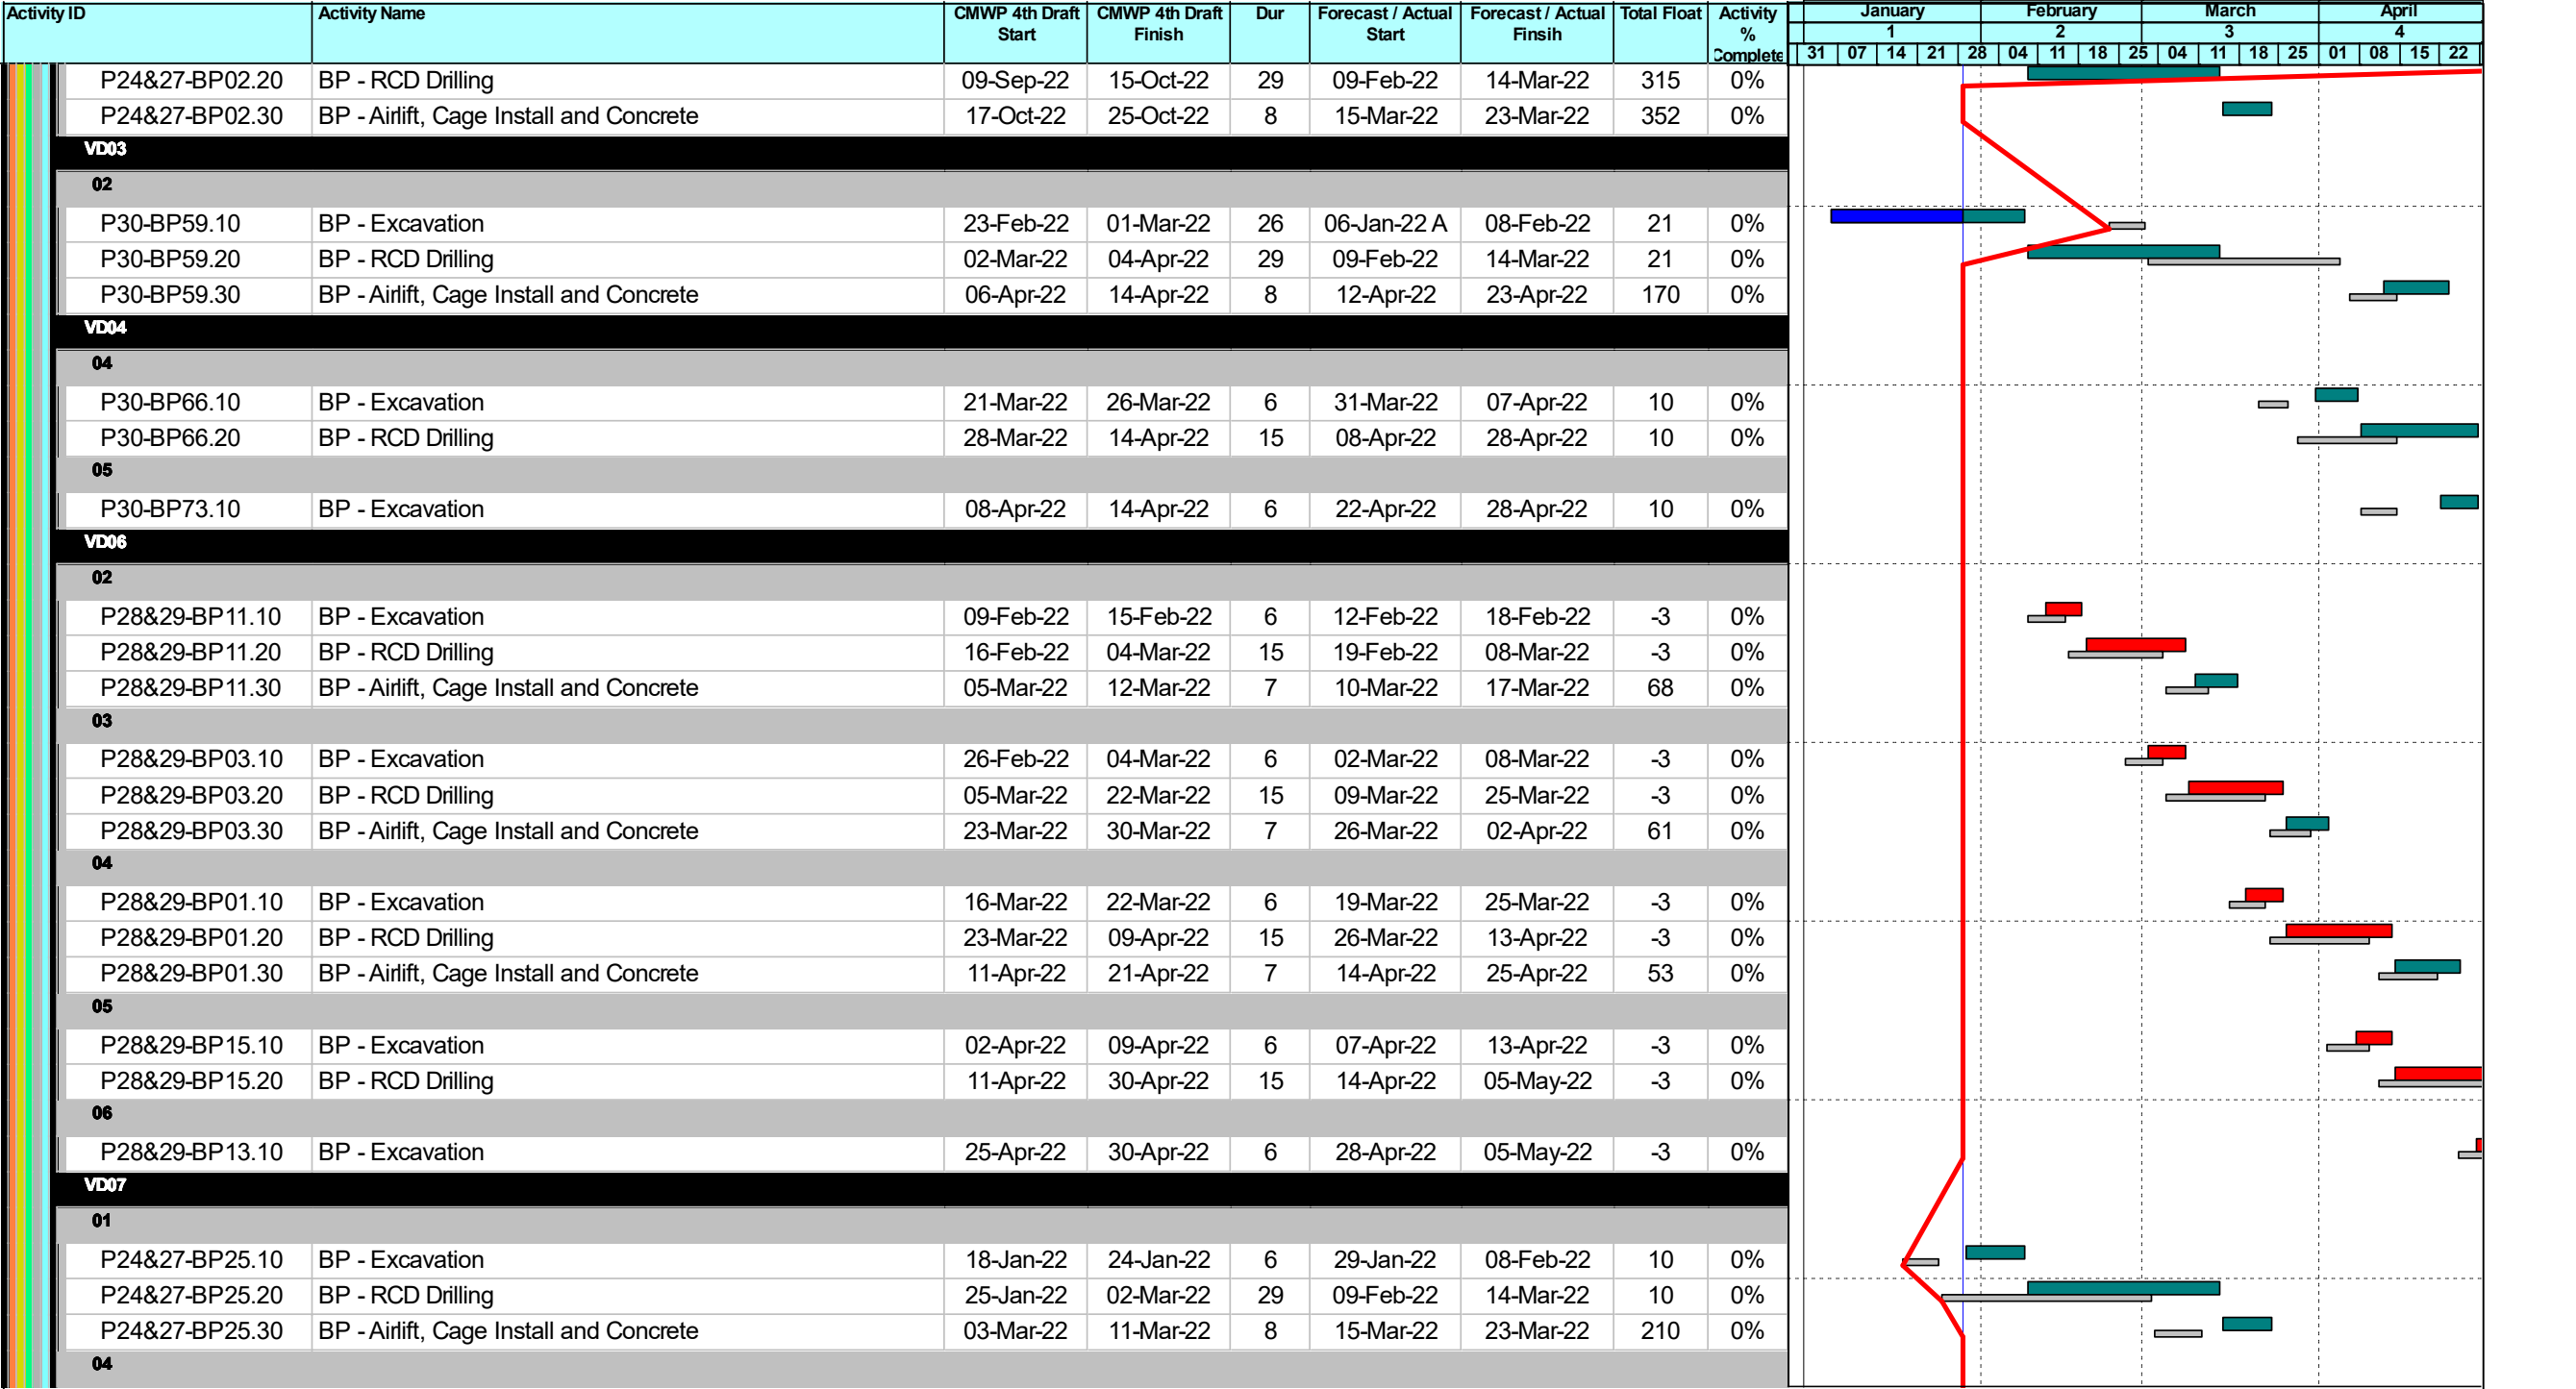


	Planned Bar		Milestone
	Critical Bar		Critical MS
	Baseline		Baseline MS

West Kowloon Cultural District Authority
Piling for Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 28 Jan 2022
 Based on CMWP 4th Draft



Date	Revision	Checked	Approved
06-Aug-21	1st Draft	KL	N
29-Sep-21	2nd Draft	KL	N
25-Oct-21	3rd Draft	KL	C
26-Nov-21	4th Draft	KL	B

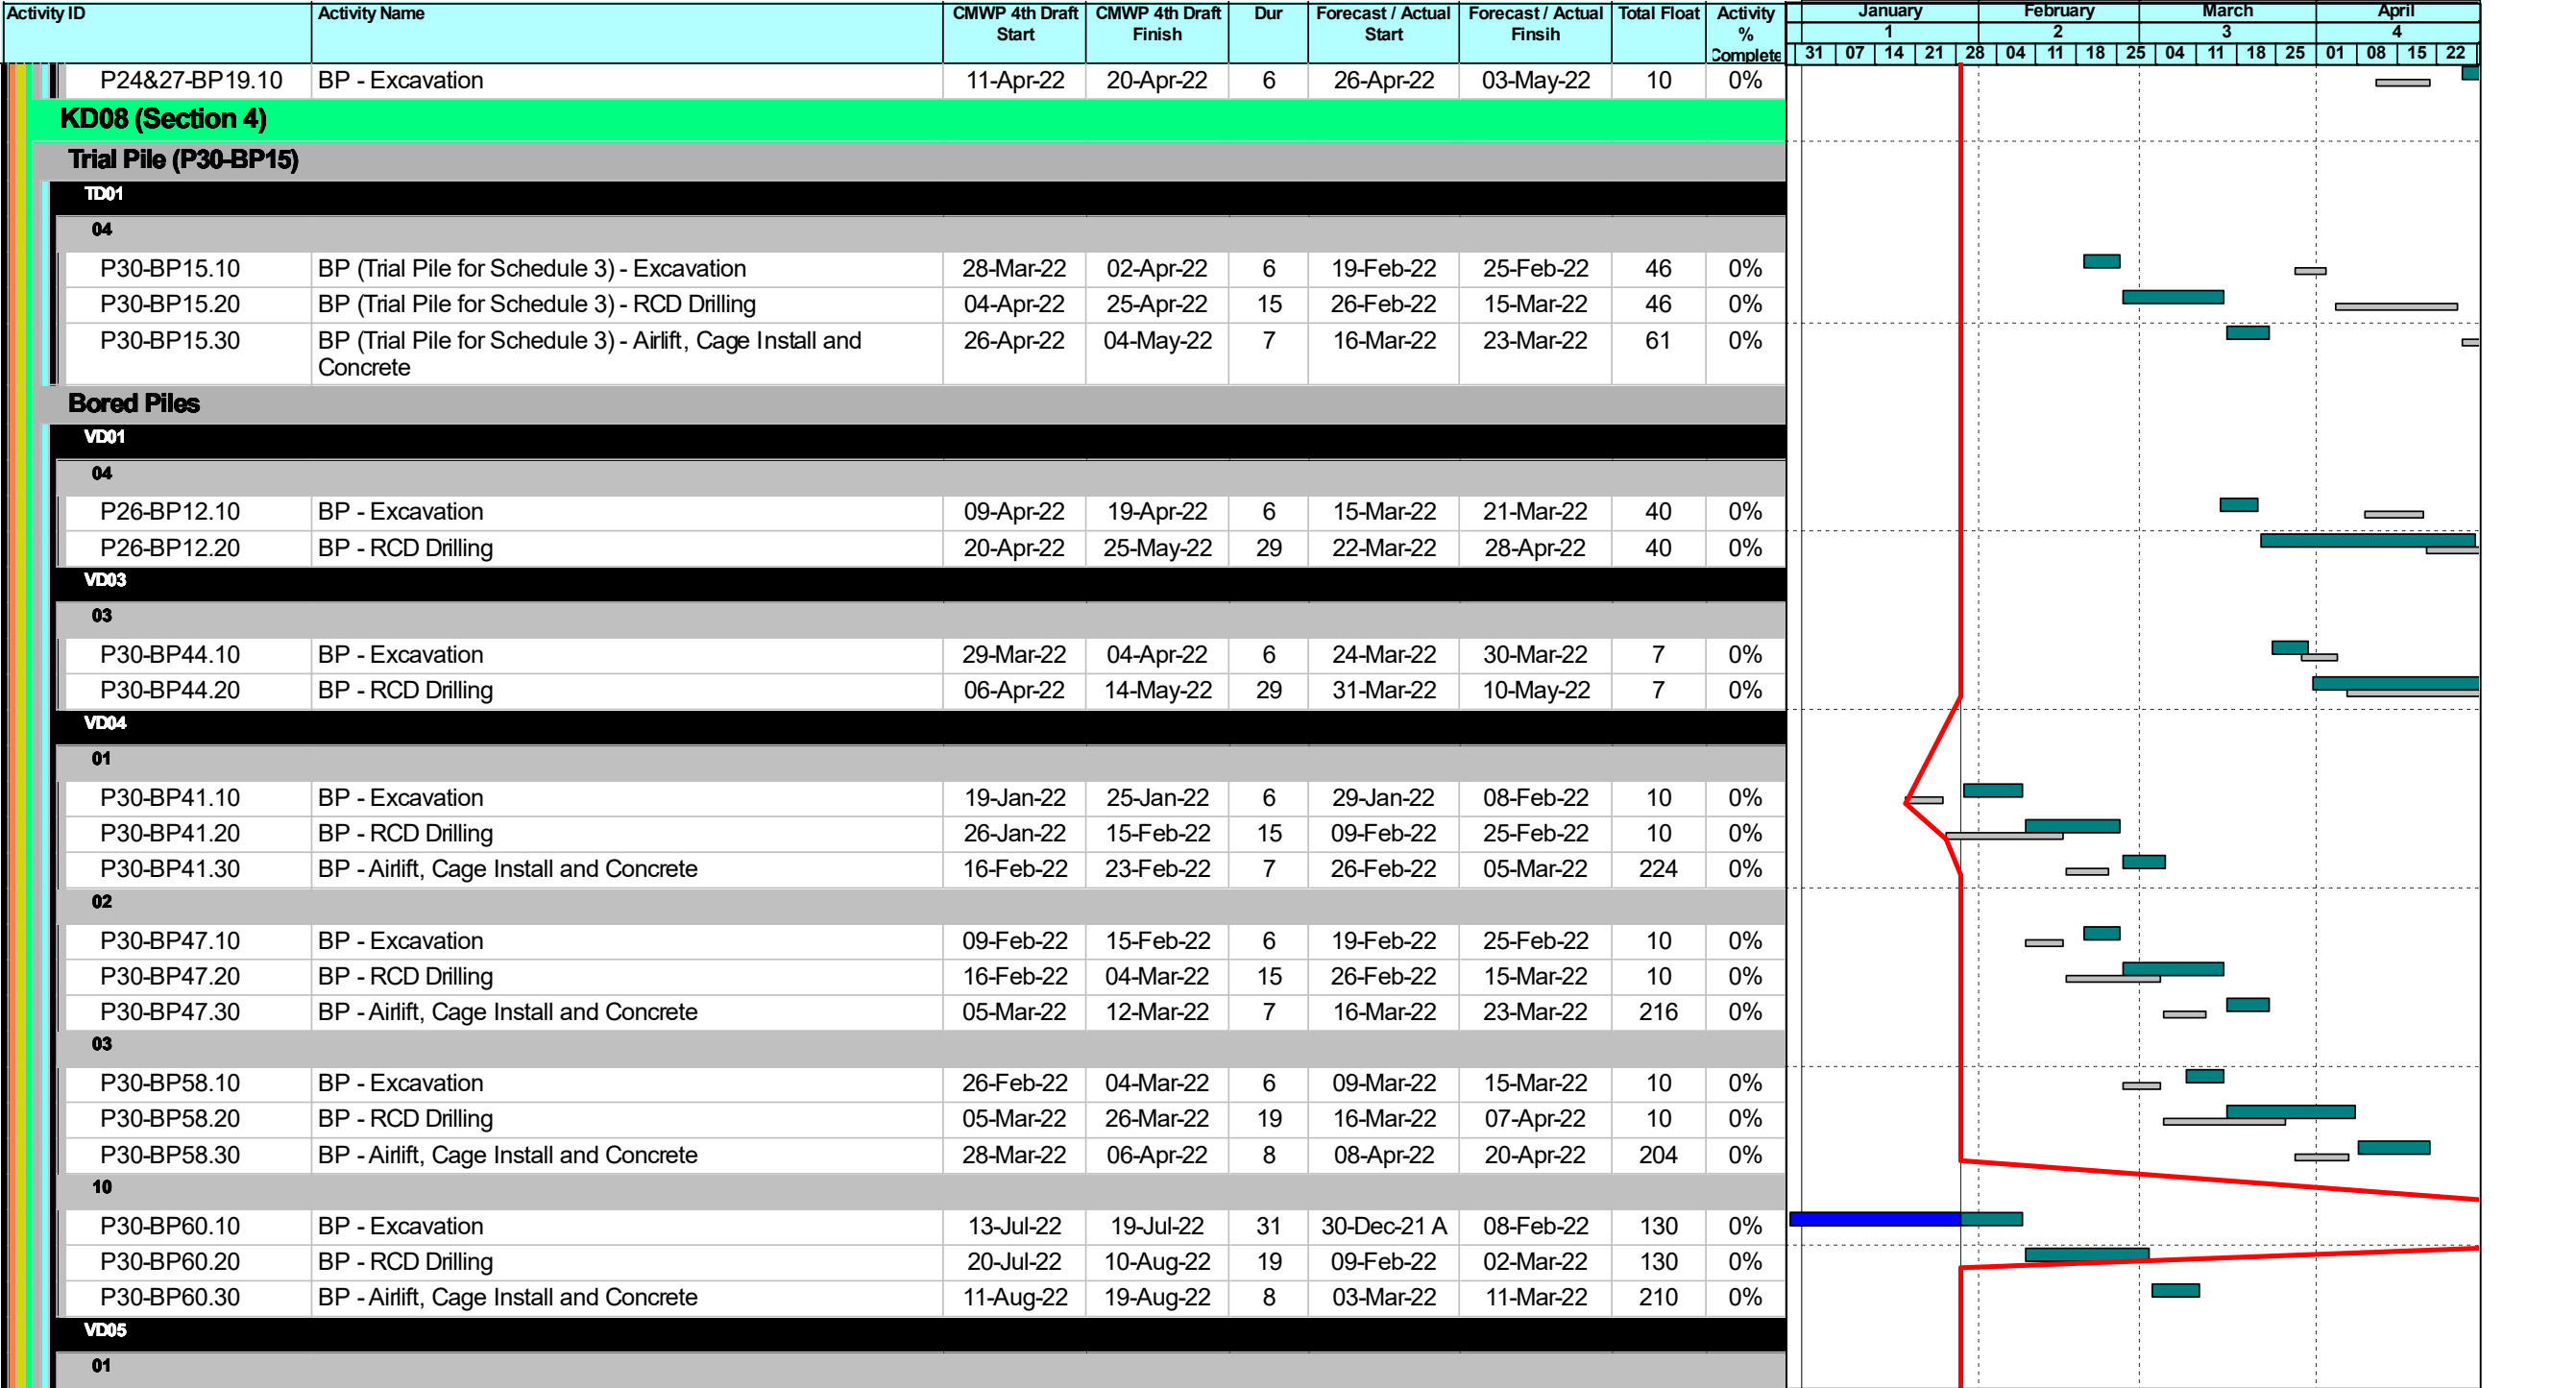







Planned Bar	Milestone
Critical Bar	Critical MS
Baseline	Baseline MS

West Kowloon Cultural District Authority
Piling for Retained Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 28 Jan 2022
 Based on CMWP 4th Draft

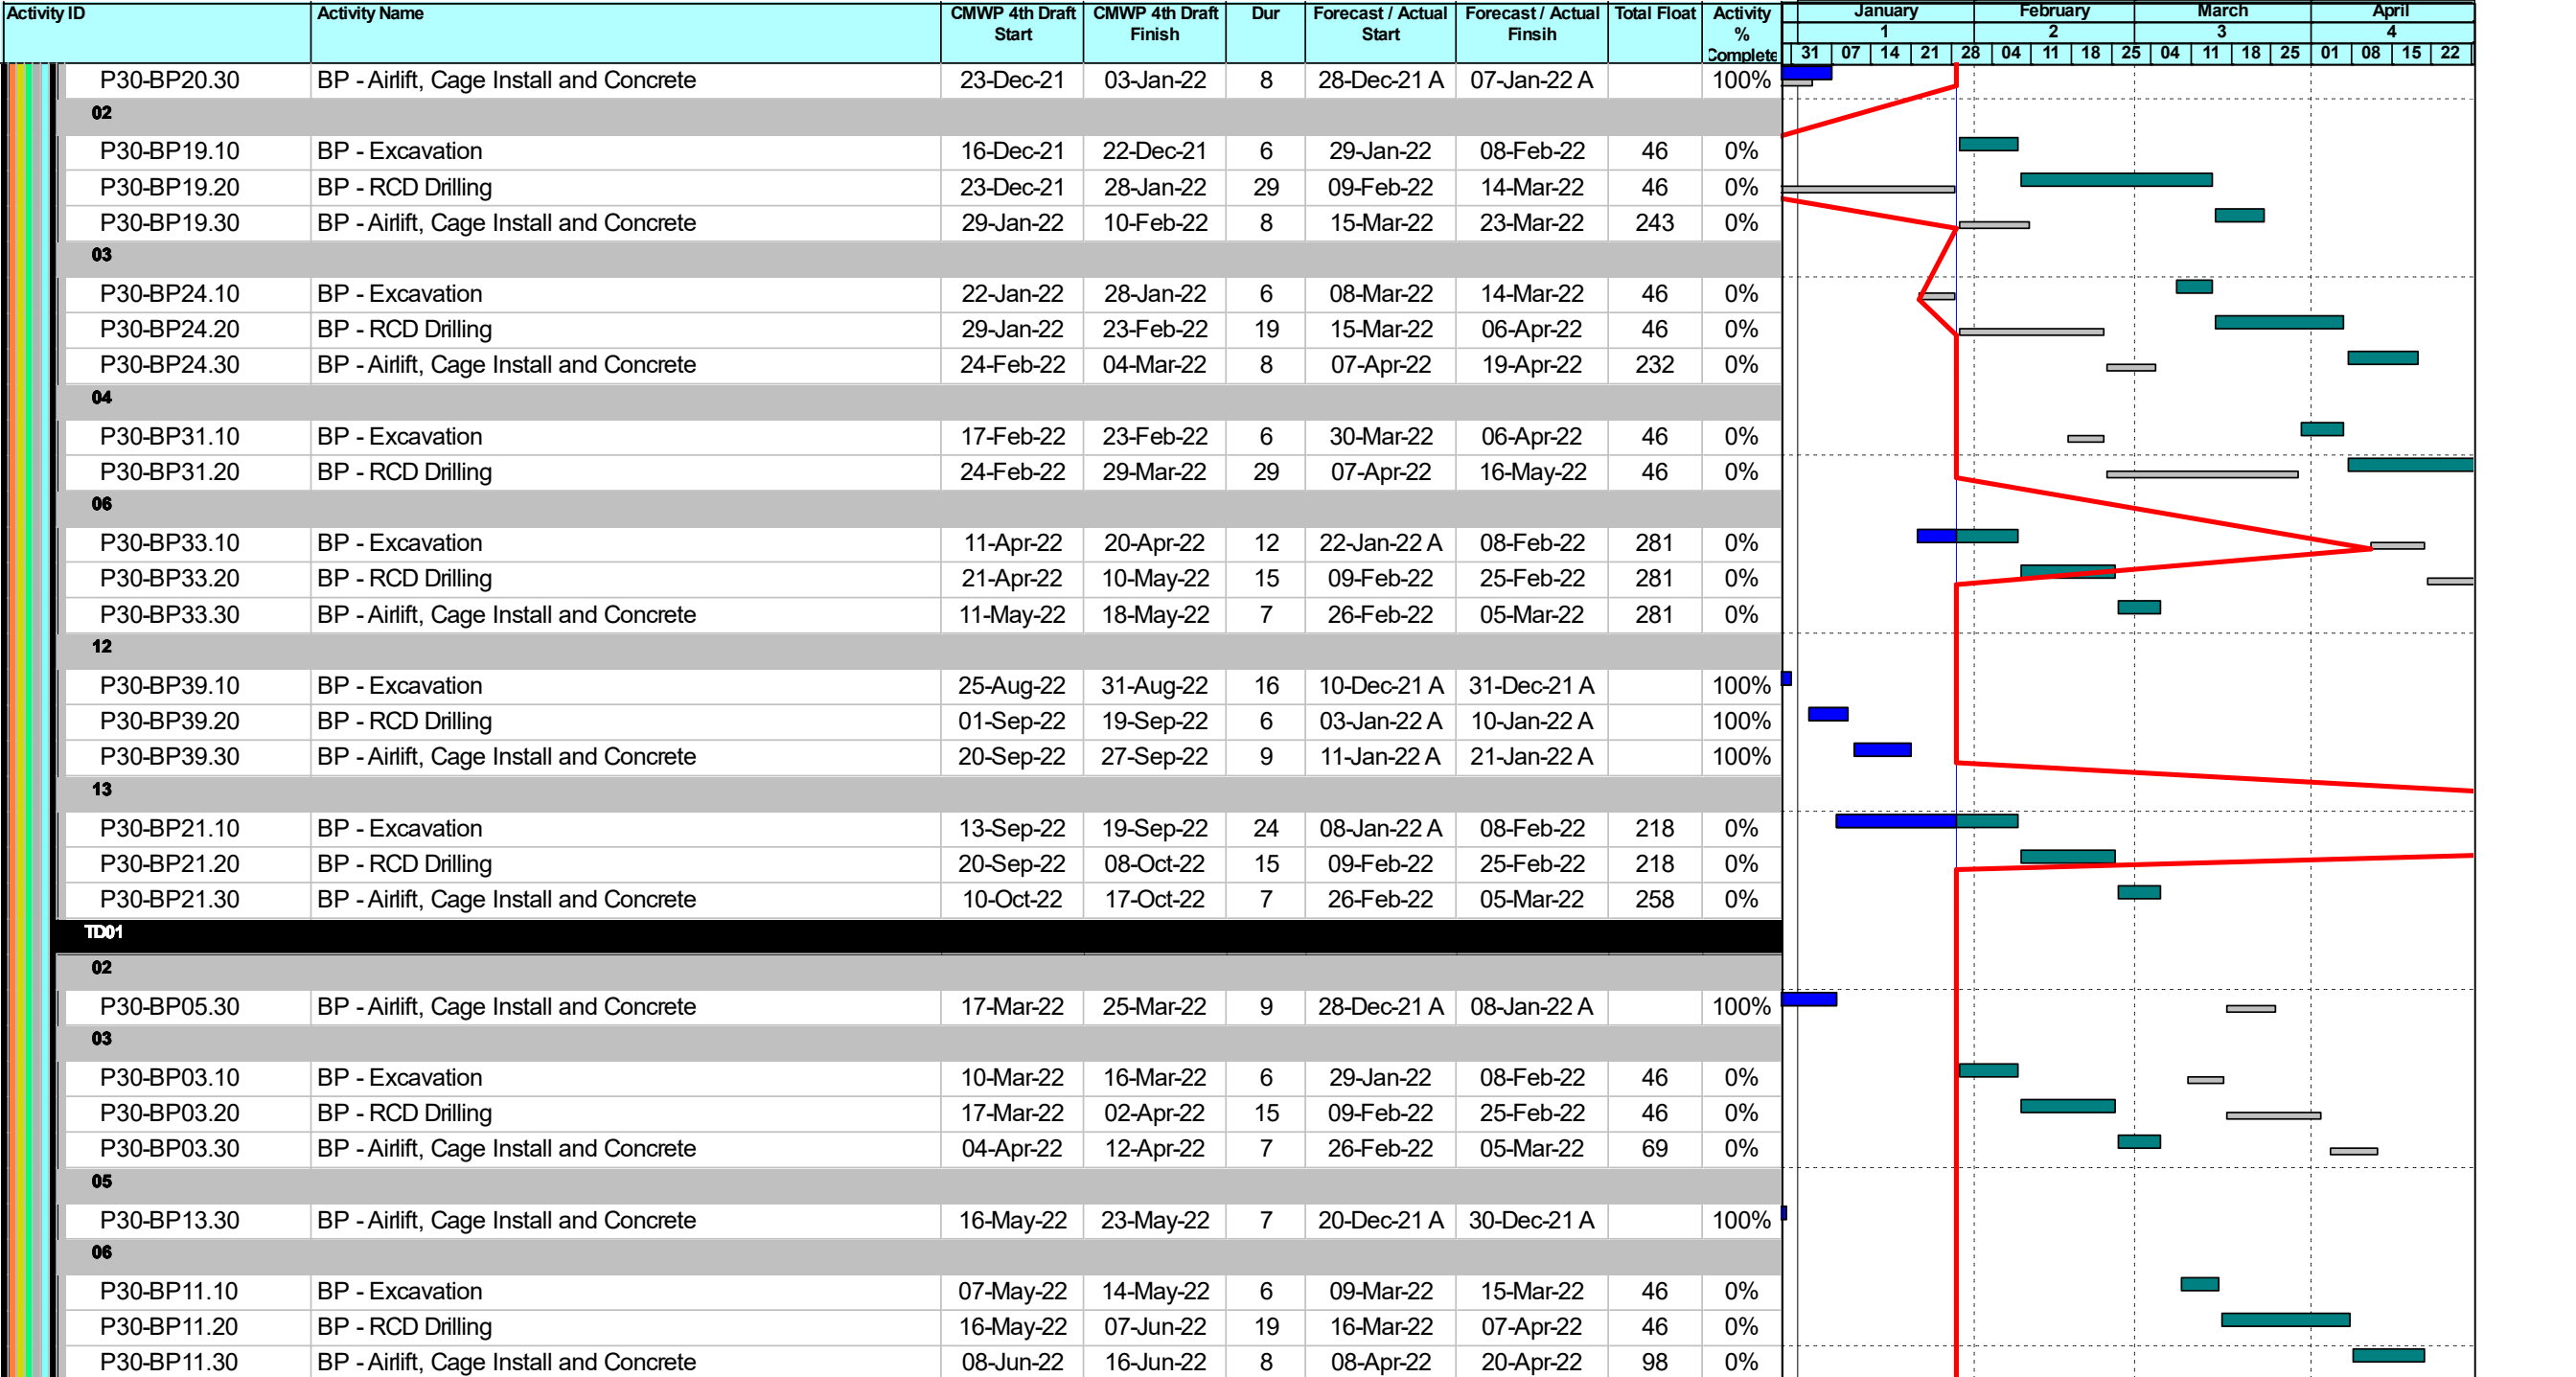

Date	Revision	Checked	Approved
06-Aug-21	1st Draft	KL	N
29-Sep-21	2nd Draft	KL	N
25-Oct-21	3rd Draft	KL	C
26-Nov-21	4th Draft	KL	B



	Planned Bar		Milestone
	Critical Bar		Critical MS
	Baseline		Baseline MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 28 Jan 2022
 Based on CMWP 4th Draft



Date	Revision	Checked	Approved
06-Aug-21	1st Draft	KL	N
29-Sep-21	2nd Draft	KL	N
25-Oct-21	3rd Draft	KL	C
26-Nov-21	4th Draft	KL	B

Activity ID	Activity Name	CMWP 4th Draft Start	CMWP 4th Draft Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	January				February				March				April			
									1				2				3				4			
									31	07	14	21	28	04	11	18	25	04	11	18	25	01	08	15

TD09									
02									
CBA-BPC52Va.10	BP - Excavation	23-Apr-22	29-Apr-22	6	23-Apr-22	29-Apr-22	0	0%	

KD09 (Section 5)

Trial Piles (P23-BP68)

TD08									
01									
P23-BP68.10	BP (Trial Pile for Schedule 4) - Excavation	14-Dec-21	20-Dec-21	11	24-Jan-22 A	08-Feb-22	24	0%	
P23-BP68.20	BP (Trial Pile for Schedule 4) - RCD Drilling	21-Dec-21	26-Jan-22	29	09-Feb-22	14-Mar-22	24	0%	
P23-BP68.30	BP (Trial Pile for Schedule 4) - Airlift, Cage Install and Concrete	27-Jan-22	08-Feb-22	8	15-Mar-22	23-Mar-22	52	0%	

Bored Piles

VD01									
01									
P23-BP44.10	BP - Excavation	05-Feb-22	11-Feb-22	77	01-Nov-21 A	05-Feb-22	40	100%	
P23-BP44.20	BP - RCD Drilling	12-Feb-22	05-Mar-22	19	05-Feb-22	26-Feb-22	40	0%	
P23-BP44.30	BP - Airlift, Cage Install and Concrete	07-Mar-22	15-Mar-22	8	28-Feb-22	08-Mar-22	202	0%	

CD01									
05									
P23-BP53.10	BP - Excavation	28-Jan-22	07-Feb-22	6	19-Feb-22	25-Feb-22	67	0%	
P23-BP53.20	BP - RCD Drilling	08-Feb-22	01-Mar-22	19	26-Feb-22	19-Mar-22	67	0%	
P23-BP53.30	BP - Airlift, Cage Install and Concrete	02-Mar-22	10-Mar-22	8	21-Mar-22	29-Mar-22	270	0%	


06									
P23-BP40.10	BP - Excavation	23-Feb-22	01-Mar-22	6	14-Mar-22	19-Mar-22	67	0%	
P23-BP40.20	BP - RCD Drilling	02-Mar-22	18-Mar-22	15	21-Mar-22	07-Apr-22	67	0%	
P23-BP40.30	BP - Airlift, Cage Install and Concrete	19-Mar-22	26-Mar-22	7	08-Apr-22	19-Apr-22	263	0%	

09									
P23-BP64.10	BP - Excavation	26-Apr-22	03-May-22	6	31-Mar-22	07-Apr-22	67	0%	
P23-BP64.20	BP - RCD Drilling	04-May-22	26-May-22	19	08-Apr-22	04-May-22	67	0%	

10									
P23-BP62.10	BP - Excavation	20-May-22	26-May-22	6	27-Apr-22	04-May-22	67	0%	

14									
P23-BP63.10	BP - Excavation	26-Apr-22	03-May-22	16	18-Jan-22 A	08-Feb-22	131	0%	
P23-BP63.20	BP - RCD Drilling	04-May-22	26-May-22	19	09-Feb-22	02-Mar-22	131	0%	
P23-BP63.30	BP - Airlift, Cage Install and Concrete	27-May-22	06-Jun-22	8	03-Mar-22	11-Mar-22	149	0%	

15									
P23-BP52.10	BP - Excavation	20-May-22	26-May-22	6	24-Feb-22	02-Mar-22	131	0%	

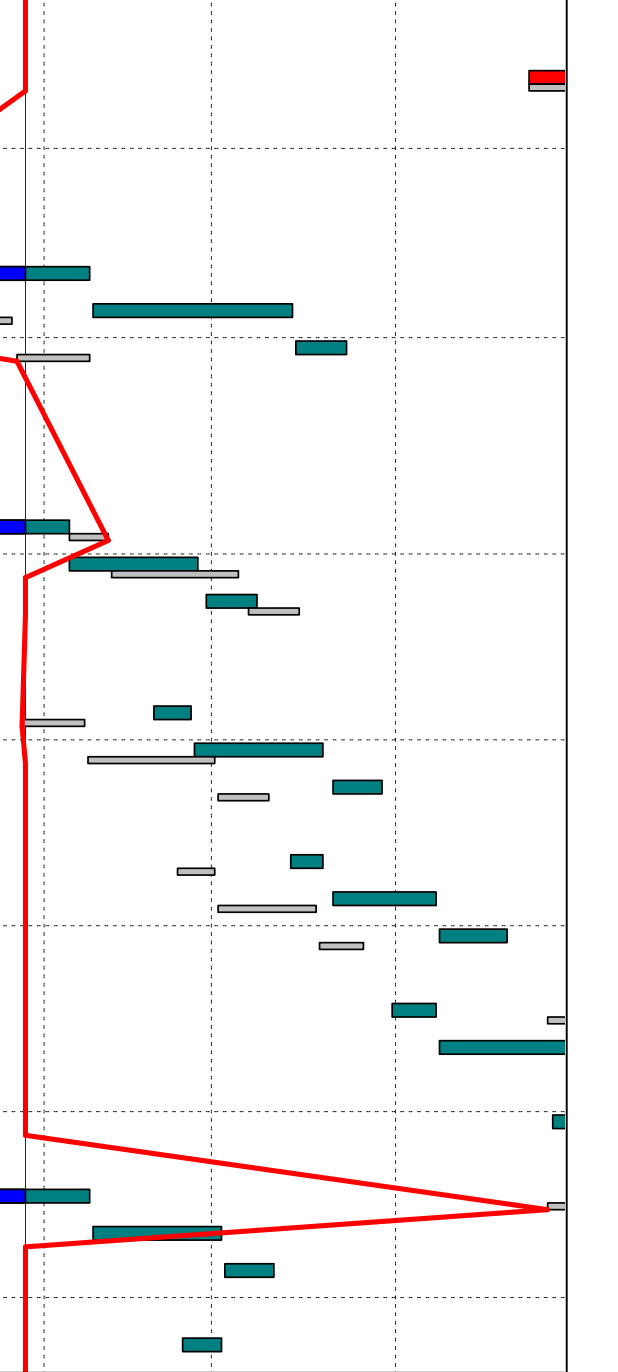

	Planned Bar		Milestone
	Critical Bar		Critical MS
	Baseline		Baseline MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 28 Jan 2022
 Based on CMWP 4th Draft

	Date	Revision	Checked	Approved
	06-Aug-21	1st Draft	KL	N
	29-Sep-21	2nd Draft	KL	N
	25-Oct-21	3rd Draft	KL	C
	26-Nov-21	4th Draft	KL	B

Activity ID	Activity Name	CMWP 4th Draft Start	CMWP 4th Draft Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	January				February				March				April			
									1				2				3				4			
									31	07	14	21	28	04	11	18	25	04	11	18	25	01	08	15
P23-BP52.20	BP - RCD Drilling	27-May-22	18-Jun-22	19	03-Mar-22	24-Mar-22	131	0%																
P23-BP52.30	BP - Airlift, Cage Install and Concrete	20-Jun-22	28-Jun-22	8	25-Mar-22	02-Apr-22	138	0%																
17																								
P23-BP42.10	BP - Excavation	30-Jun-22	07-Jul-22	6	06-Apr-22	12-Apr-22	244	0%																
P23-BP42.20	BP - RCD Drilling	08-Jul-22	25-Jul-22	15	13-Apr-22	04-May-22	244	0%																
CD02																								
02																								
P23-BP37.10	BP - Excavation	21-Dec-21	29-Dec-21	6	29-Jan-22	08-Feb-22	18	0%																
P23-BP37.20	BP - RCD Drilling	30-Dec-21	05-Feb-22	29	09-Feb-22	14-Mar-22	18	0%																
P23-BP37.30	BP - Airlift, Cage Install and Concrete	07-Feb-22	15-Feb-22	8	15-Mar-22	23-Mar-22	242	0%																
03																								
P23-BP48.10	BP - Excavation	27-Jan-22	05-Feb-22	6	08-Mar-22	14-Mar-22	18	0%																
P23-BP48.20	BP - RCD Drilling	07-Feb-22	11-Mar-22	29	15-Mar-22	21-Apr-22	18	0%																
P23-BP48.30	BP - Airlift, Cage Install and Concrete	12-Mar-22	21-Mar-22	8	22-Apr-22	30-Apr-22	221	0%																
04																								
P23-BP39.10	BP - Excavation	05-Mar-22	11-Mar-22	6	12-Apr-22	21-Apr-22	18	0%																
P23-BP39.20	BP - RCD Drilling	12-Mar-22	02-Apr-22	19	22-Apr-22	16-May-22	18	0%																
08																								
P23-BP51.10	BP - Excavation	22-Jun-22	28-Jun-22	23	10-Jan-22 A	08-Feb-22	143	0%																
P23-BP51.20	BP - RCD Drilling	29-Jun-22	21-Jul-22	19	09-Feb-22	02-Mar-22	143	0%																
P23-BP51.30	BP - Airlift, Cage Install and Concrete	22-Jul-22	30-Jul-22	8	03-Mar-22	11-Mar-22	292	0%																
TD07																								
02																								
P18-BP16.10	BP - Excavation	20-Dec-21	28-Dec-21	6	19-Feb-22	25-Feb-22	-11	0%																
P18-BP16.20	BP - RCD Drilling	29-Dec-21	15-Jan-22	15	26-Feb-22	15-Mar-22	-11	0%																
P18-BP16.30	BP - Airlift, Cage Install and Concrete	17-Jan-22	24-Jan-22	7	16-Mar-22	23-Mar-22	68	0%																
03																								
P18-BP23.10	BP - Excavation	10-Jan-22	15-Jan-22	6	09-Mar-22	15-Mar-22	-11	0%																
P18-BP23.20	BP - RCD Drilling	17-Jan-22	05-Feb-22	15	16-Mar-22	01-Apr-22	-11	0%																
P18-BP23.30	BP - Airlift, Cage Install and Concrete	07-Feb-22	14-Feb-22	7	02-Apr-22	11-Apr-22	60	0%																
04																								
P18-BP21.10	BP - Excavation	27-Jan-22	05-Feb-22	6	26-Mar-22	01-Apr-22	-11	0%																
P18-BP21.20	BP - RCD Drilling	07-Feb-22	23-Feb-22	15	02-Apr-22	23-Apr-22	-11	0%																
P18-BP21.30	BP - Airlift, Cage Install and Concrete	24-Feb-22	03-Mar-22	7	25-Apr-22	03-May-22	52	0%																
TD06																								
01																								
P18-BP36.10	BP - Excavation	20-Dec-21	28-Dec-21	6	29-Jan-22	08-Feb-22	43	0%																

	Planned Bar		Milestone
	Critical Bar		Critical MS
	Baseline		Baseline MS

West Kowloon Cultural District Authority
Piling for Retaining Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 28 Jan 2022
 Based on CMWP 4th Draft

	Date	Revision	Checked	Approved
	06-Aug-21	1st Draft	KL	N
	29-Sep-21	2nd Draft	KL	N
	25-Oct-21	3rd Draft	KL	C
	26-Nov-21	4th Draft	KL	B


Activity ID	Activity Name	CMWP 4th Draft Start	CMWP 4th Draft Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	January				February				March				April			
									1				2				3				4			
									31	07	14	21	28	04	11	18	25	04	11	18	25	01	08	15
P18-BP36.20	BP - RCD Drilling	29-Dec-21	15-Jan-22	15	09-Feb-22	25-Feb-22	43	0%																
P18-BP36.30	BP - Airlift, Cage Install and Concrete	17-Jan-22	24-Jan-22	7	26-Feb-22	05-Mar-22	185	0%																
02																								
P18-BP40.10	BP - Excavation	10-Jan-22	15-Jan-22	6	19-Feb-22	25-Feb-22	43	0%																
P18-BP40.20	BP - RCD Drilling	17-Jan-22	05-Feb-22	15	26-Feb-22	15-Mar-22	43	0%																
P18-BP40.30	BP - Airlift, Cage Install and Concrete	07-Feb-22	14-Feb-22	7	16-Mar-22	23-Mar-22	177	0%																
03																								
P18-BP38.10	BP - Excavation	27-Jan-22	05-Feb-22	6	09-Mar-22	15-Mar-22	43	0%																
P18-BP38.20	BP - RCD Drilling	07-Feb-22	28-Feb-22	19	16-Mar-22	07-Apr-22	43	0%																
P18-BP38.30	BP - Airlift, Cage Install and Concrete	01-Mar-22	09-Mar-22	8	08-Apr-22	20-Apr-22	165	0%																
04																								
P18-BP33.10	BP - Excavation	22-Feb-22	28-Feb-22	6	31-Mar-22	07-Apr-22	43	0%																
P18-BP33.20	BP - RCD Drilling	01-Mar-22	17-Mar-22	15	08-Apr-22	28-Apr-22	43	0%																
05																								
P18-BP28.10	BP - Excavation	11-Mar-22	17-Mar-22	6	22-Apr-22	28-Apr-22	43	0%																
TD05																								
01																								
P18-BP48.10	BP - Excavation	20-Dec-21	28-Dec-21	6	29-Jan-22	08-Feb-22	72	0%																
P18-BP48.20	BP - RCD Drilling	29-Dec-21	15-Jan-22	15	09-Feb-22	25-Feb-22	72	0%																
P18-BP48.30	BP - Airlift, Cage Install and Concrete	17-Jan-22	24-Jan-22	7	26-Feb-22	05-Mar-22	202	0%																
02																								
P18-BP60.10	BP - Excavation	10-Jan-22	15-Jan-22	6	19-Feb-22	25-Feb-22	72	0%																
P18-BP60.20	BP - RCD Drilling	17-Jan-22	10-Feb-22	19	26-Feb-22	19-Mar-22	72	0%																
P18-BP60.30	BP - Airlift, Cage Install and Concrete	11-Feb-22	19-Feb-22	8	21-Mar-22	29-Mar-22	190	0%																
03																								
P18-BP63.10	BP - Excavation	04-Feb-22	10-Feb-22	6	14-Mar-22	19-Mar-22	72	0%																
P18-BP63.20	BP - RCD Drilling	11-Feb-22	04-Mar-22	19	21-Mar-22	12-Apr-22	72	0%																
P18-BP63.30	BP - Airlift, Cage Install and Concrete	05-Mar-22	14-Mar-22	8	13-Apr-22	25-Apr-22	179	0%																
04																								
P18-BP62.10	BP - Excavation	26-Feb-22	04-Mar-22	6	06-Apr-22	12-Apr-22	72	0%																
P18-BP62.20	BP - RCD Drilling	05-Mar-22	26-Mar-22	19	13-Apr-22	10-May-22	72	0%																
TD04																								
04																								
P23-BP107.10	BP - Excavation	04-Jan-22	10-Jan-22	6	02-Mar-22	08-Mar-22	153	0%																
P23-BP107.20	BP - RCD Drilling	11-Jan-22	04-Feb-22	19	09-Mar-22	30-Mar-22	153	0%																
P23-BP107.30	BP - Airlift, Cage Install and Concrete	05-Feb-22	14-Feb-22	8	31-Mar-22	09-Apr-22	228	0%																
05																								

	Planned Bar		Milestone
	Critical Bar		Critical MS
	Baseline		Baseline MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 28 Jan 2022
Based on CMWP 4th Draft



Date	Revision	Checked	Approved
06-Aug-21	1st Draft	KL	N
29-Sep-21	2nd Draft	KL	N
25-Oct-21	3rd Draft	KL	C
26-Nov-21	4th Draft	KL	B

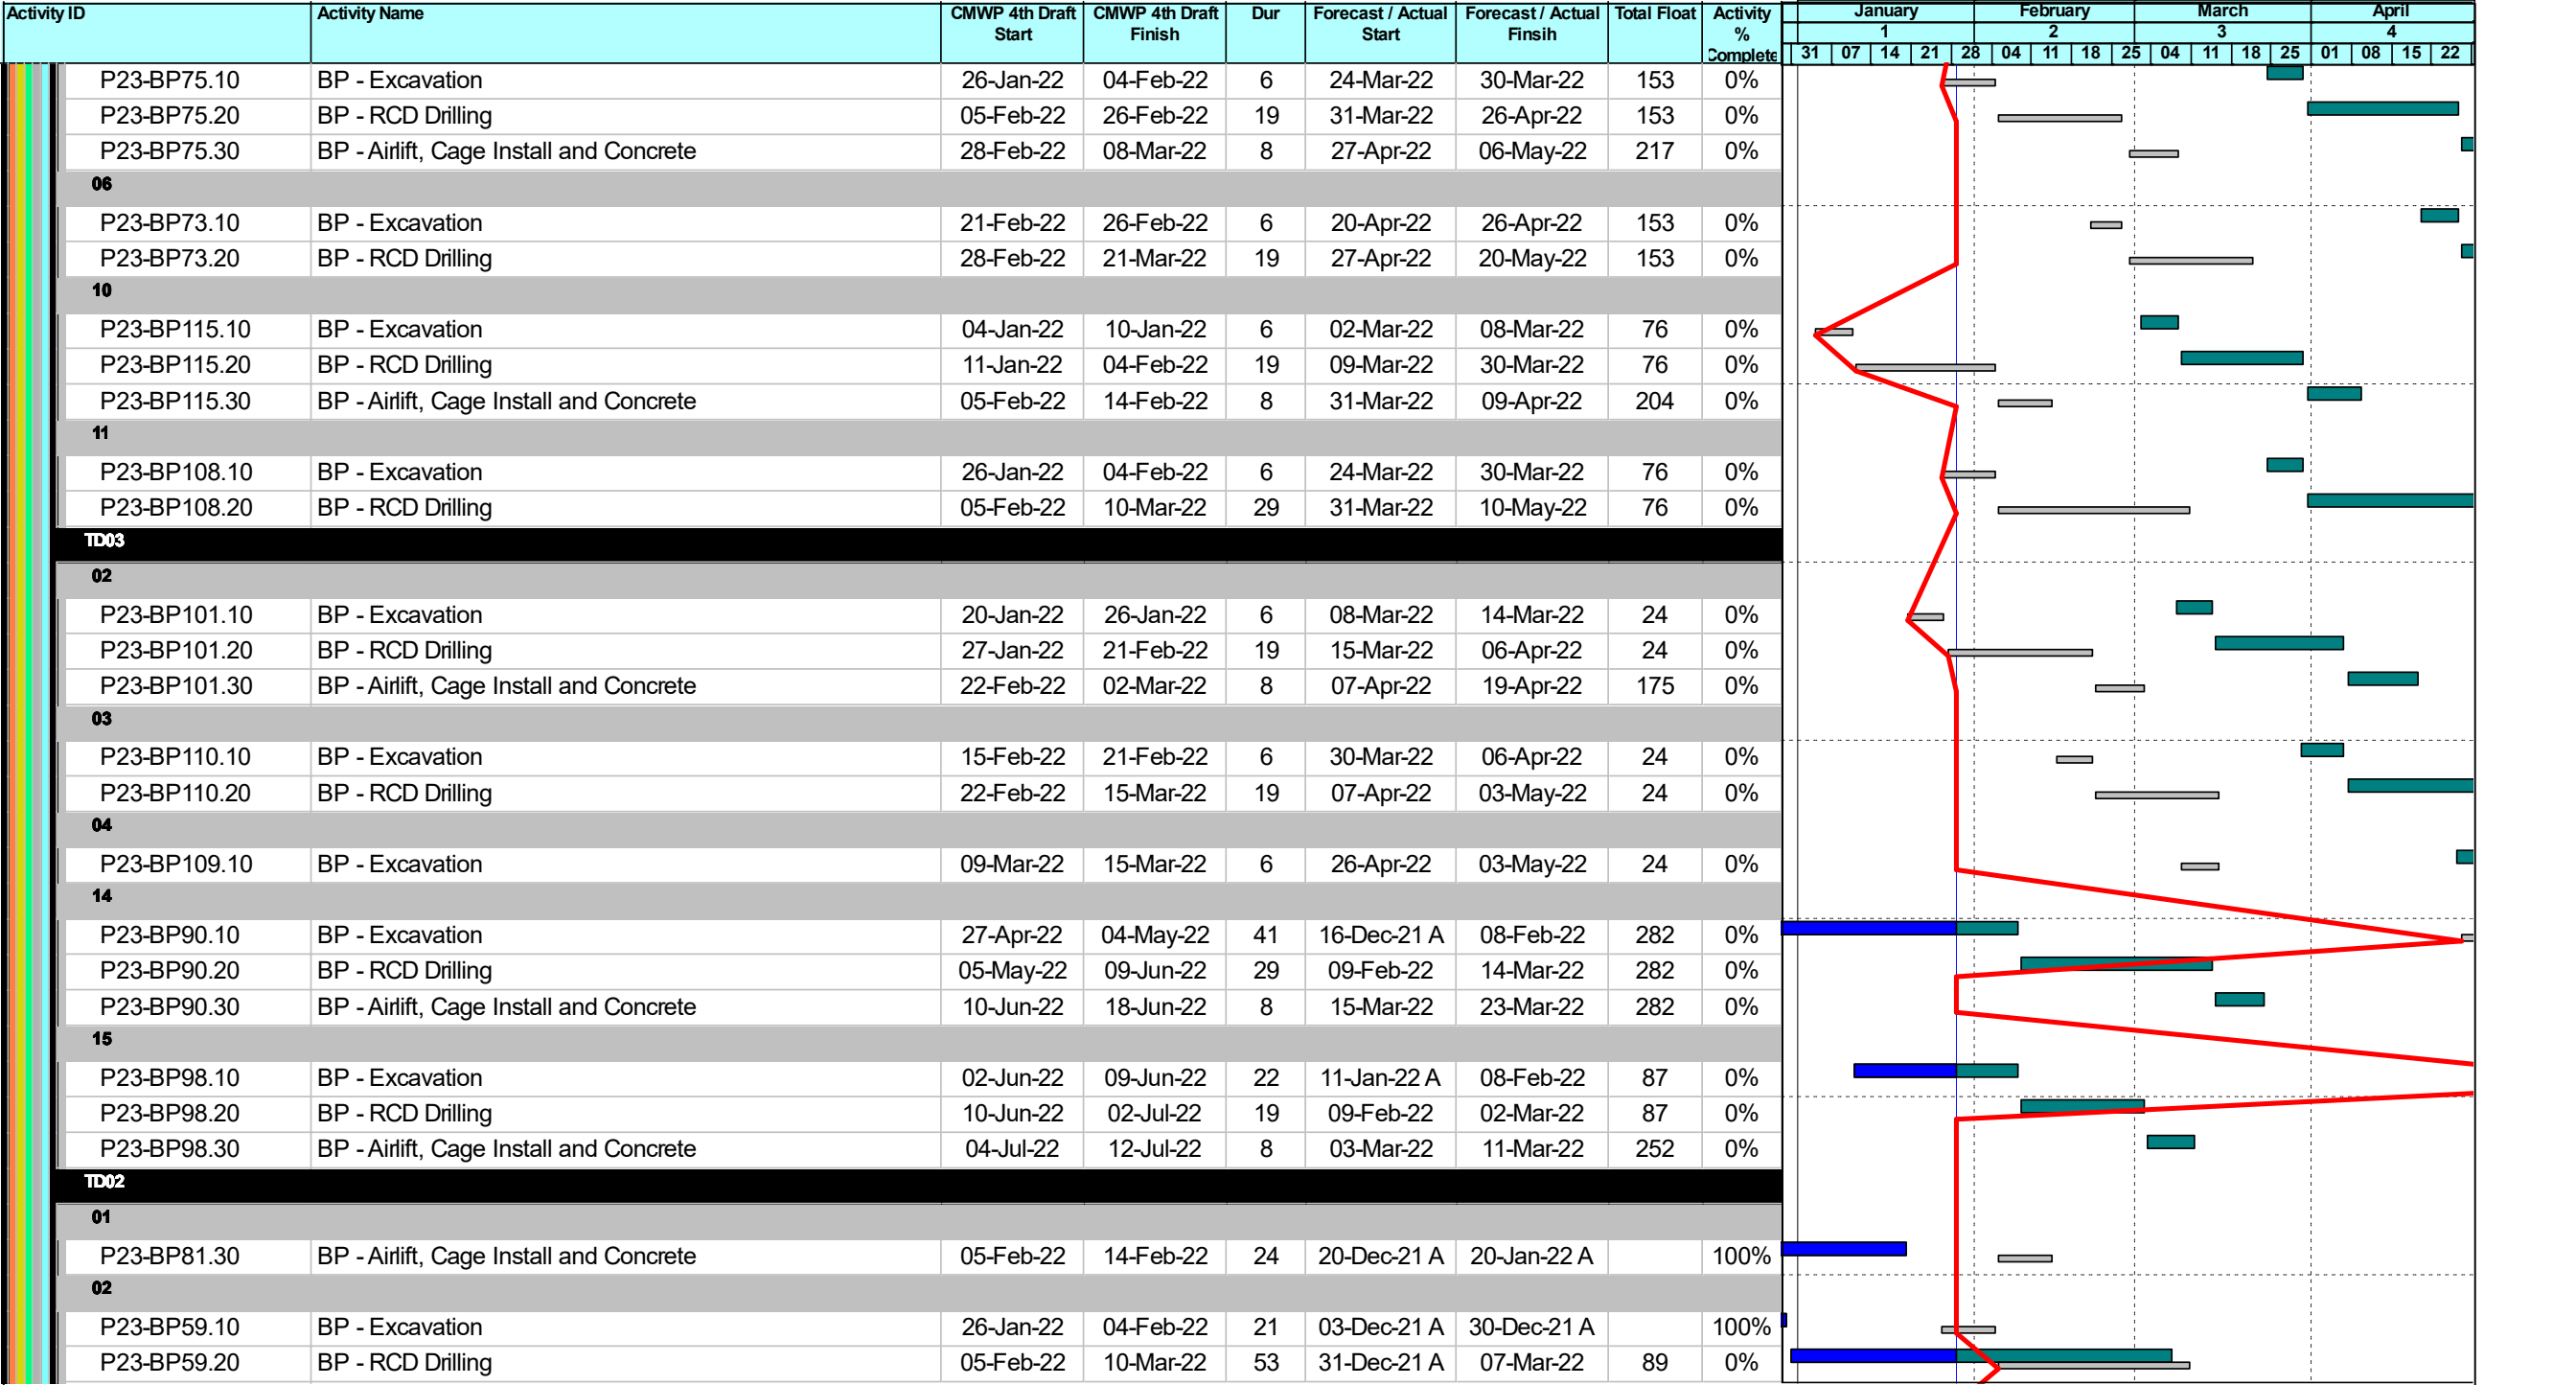


	Planned Bar		Milestone
	Critical Bar		Critical MS
	Baseline		Baseline MS

West Kowloon Cultural District Authority
Piling for Retained Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 28 Jan 2022
Based on CMWP 4th Draft



Date	Revision	Checked	Approved
06-Aug-21	1st Draft	KL	N
29-Sep-21	2nd Draft	KL	N
25-Oct-21	3rd Draft	KL	C
26-Nov-21	4th Draft	KL	B

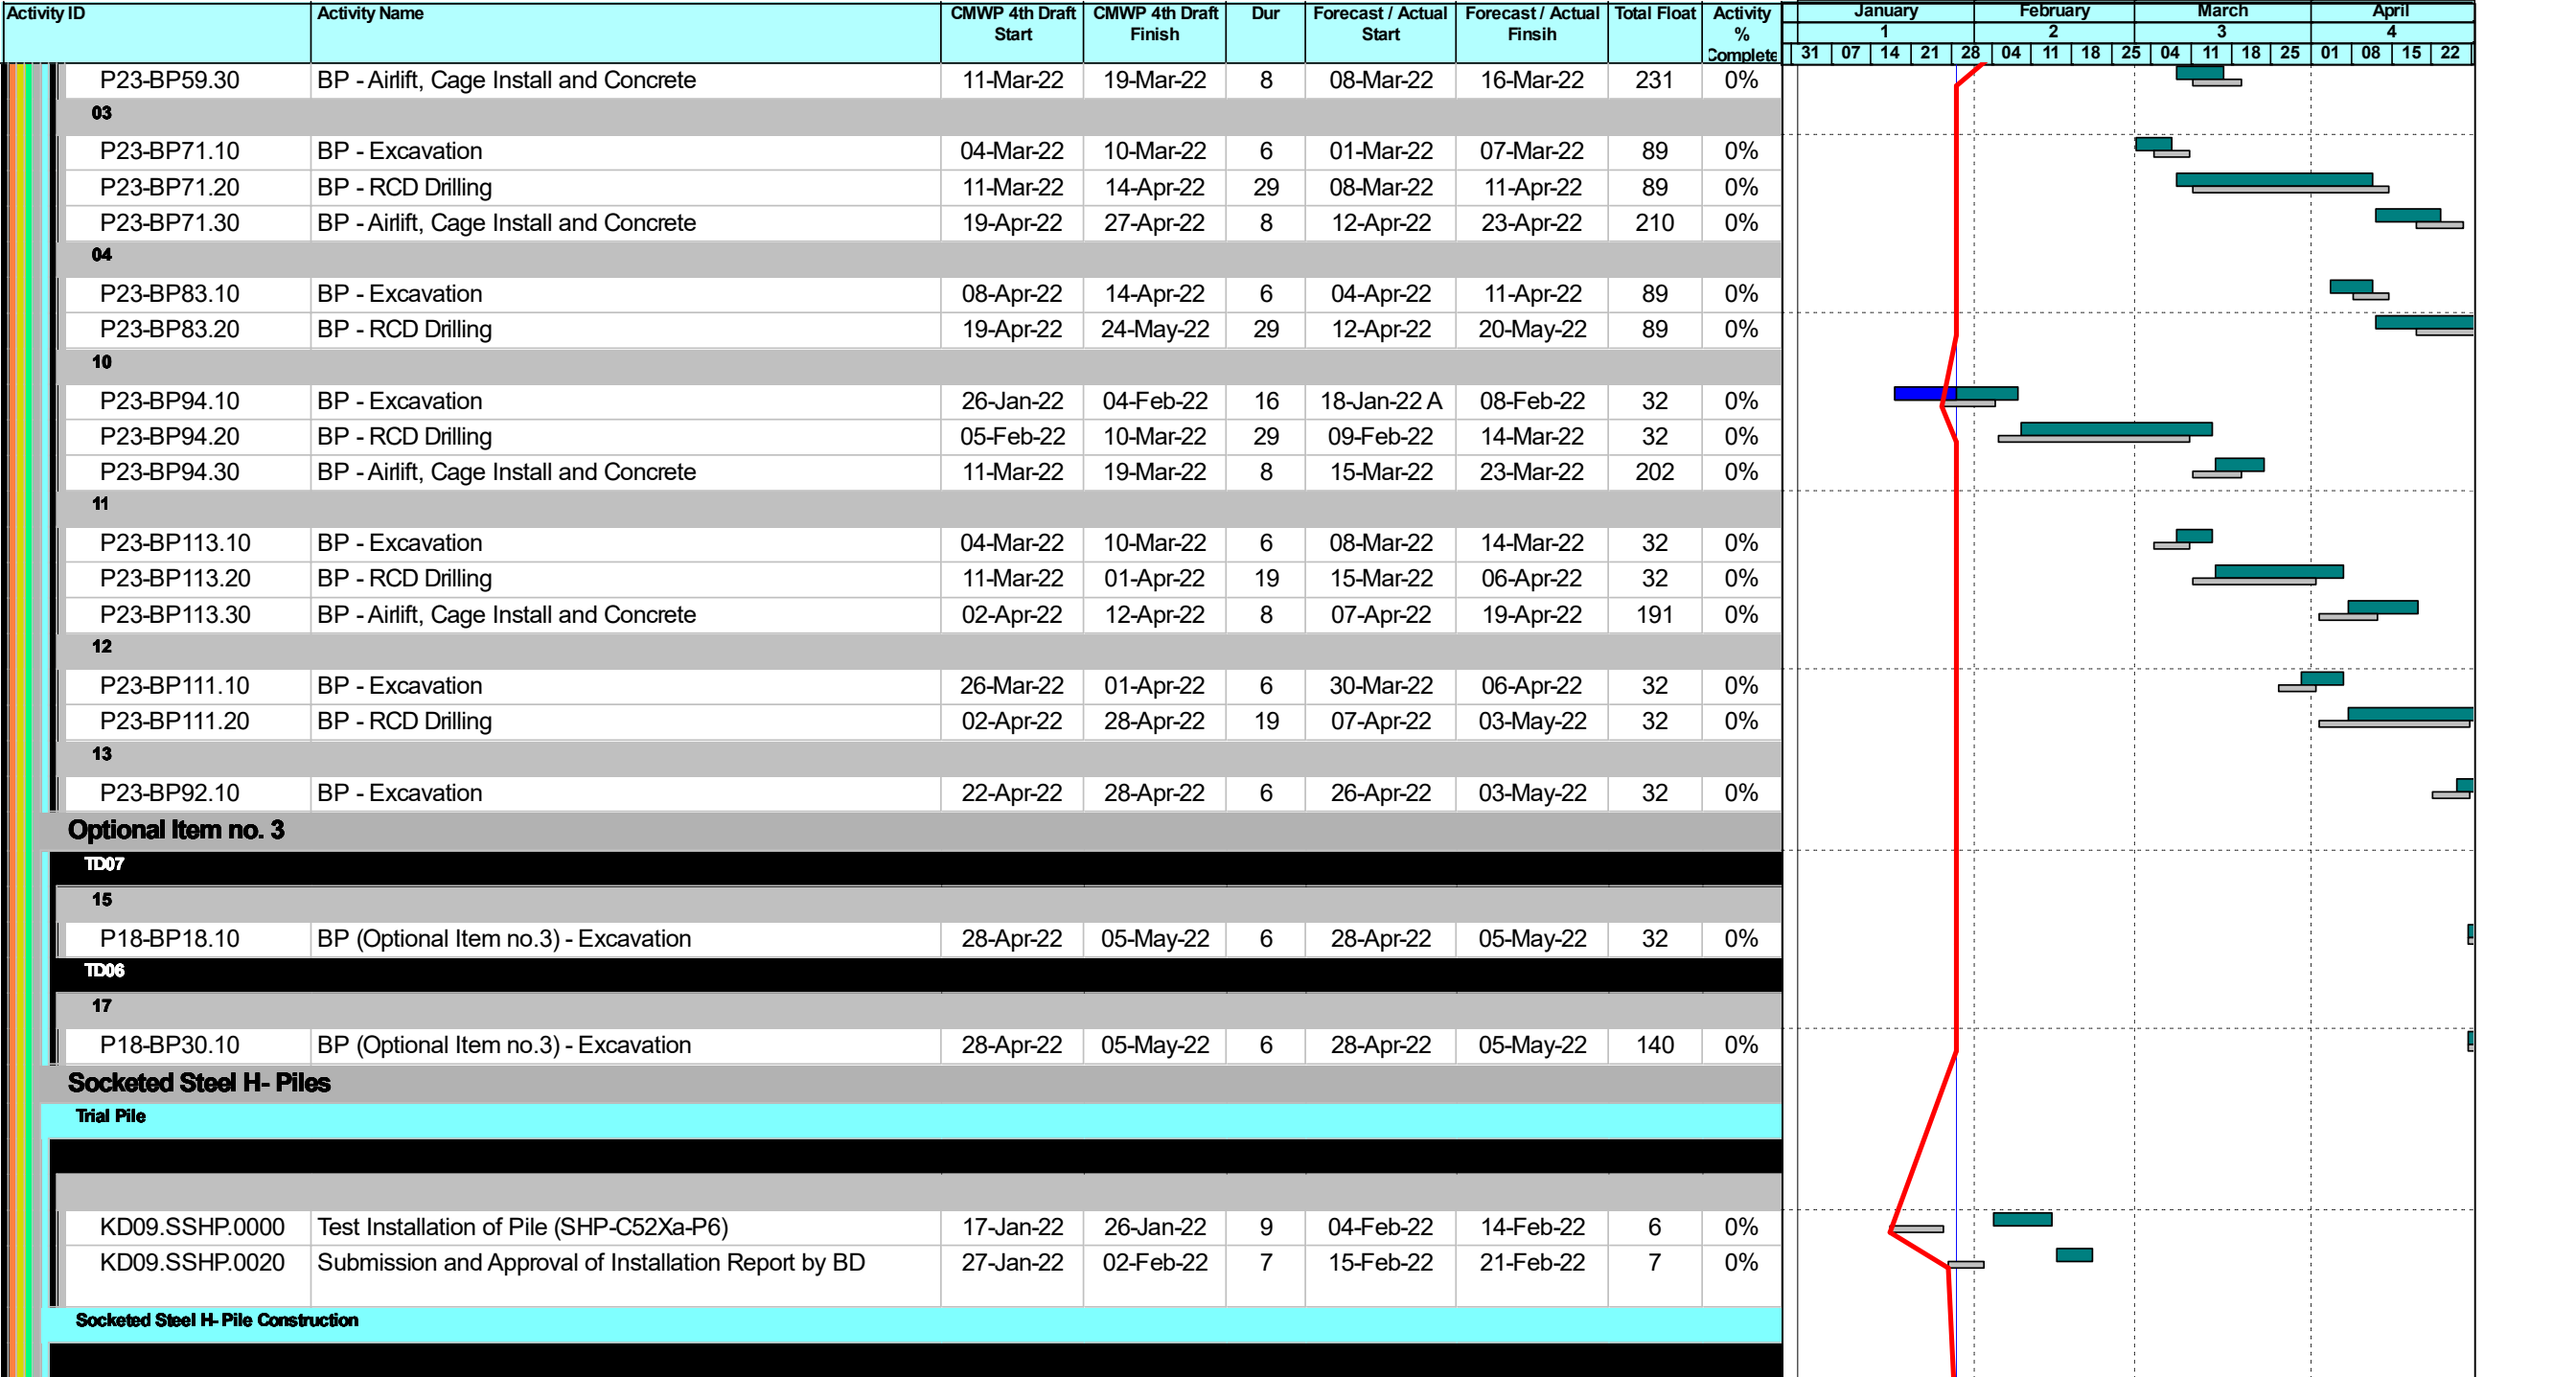


Legend

- Planned Bar (Green rectangle)
- Critical Bar (Red rectangle)
- Baseline (Grey rectangle)
- Milestone (Blue diamond)
- Critical MS (Red diamond)
- Baseline MS (Grey diamond)

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 28 Jan 2022
Based on CMWP 4th Draft

Date	Revision	Checked	Approved
06-Aug-21	1st Draft	KL	N
29-Sep-21	2nd Draft	KL	N
25-Oct-21	3rd Draft	KL	C
26-Nov-21	4th Draft	KL	B

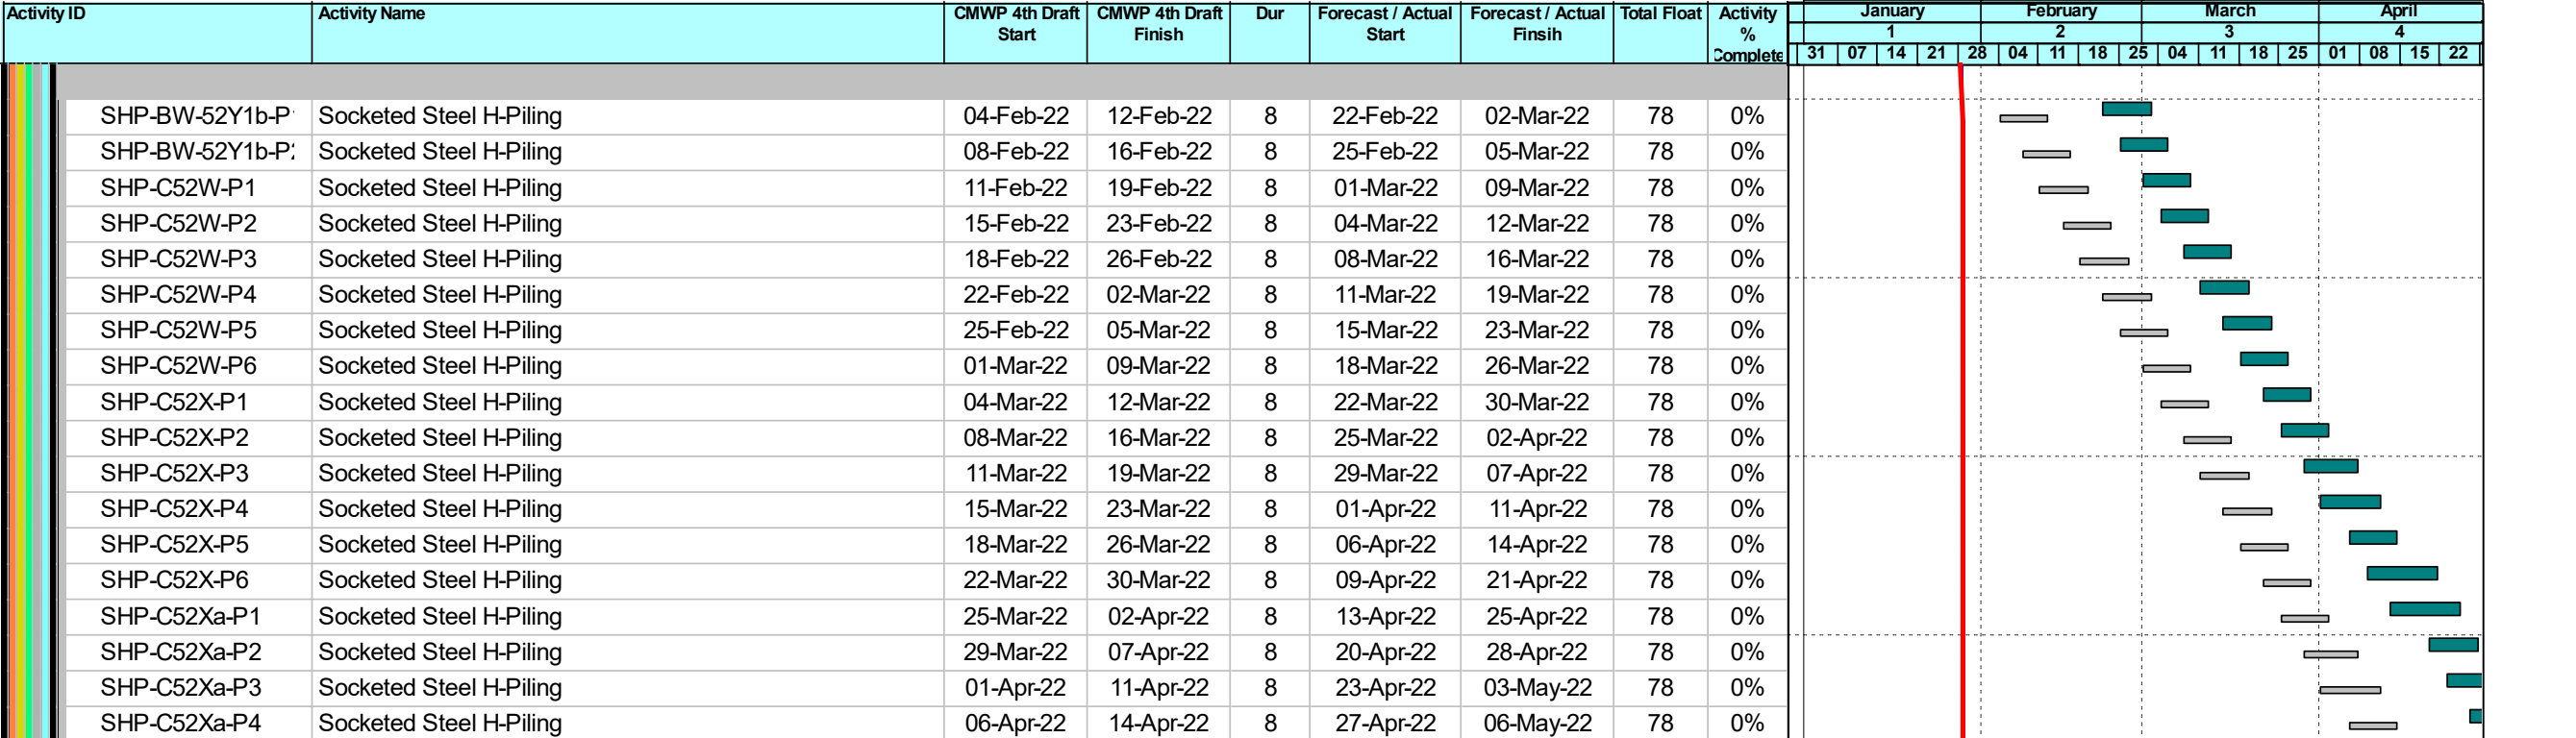

	Planned Bar		Milestone
	Critical Bar		Critical MS
	Baseline		Baseline MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 28 Jan 2022
Based on CMWP 4th Draft

			
Date	Revision	Checked	Approved
06-Aug-21	1st Draft	KL	N
29-Sep-21	2nd Draft	KL	N
25-Oct-21	3rd Draft	KL	C
26-Nov-21	4th Draft	KL	B
