

**Zone 2A**

3-Month Rolling Programme

Activity Description	Duration (Cal. Day)	Start Date	Finish Date	2022																
				May				June				July				August				
				6	13	20	27	3	10	17	24	1	8	15	22	29	5	12	19	26
				W104	W105	W106	W107	W108	W109	W110	W111	W112	W113	W114	W115	W116	W117	W118	W119	W120
Zone 2A-1 Foundation, ELS Works and Blinding to Formation (KD01)																				
ELS (Stage 1) - Grouting / Pipe Pile Works																				
King Post (8/64 Nos Completed) & Erection of Steel Column for Working Platform (11/41 Nos completed)	472	15-May-21	29-Aug-22																	
Stage 2 grouting (270/320 Nos Completed)	366	28-Sep-21	28-Sep-22																	
Pumping Test																				
Installation of Pump Wells (0/24 Nos completed)	57	28-Jun-22	23-Aug-22																	
Zone 2A-2 Foundation, ELS Works and Blinding to Formation (KD02)																				
ELS (Stage 1) - Grouting / Pipe Pile Works																				
King Post (0/86 Nos Completed) & Erection of Steel Column for Working Platform (0/65 Nos Completed)	182	21-May-22	18-Nov-22																	
Pipe Pile Construction (4561/461 Nos Completed)	533	17-Nov-20	3-May-22																	
Stage 2 grouting (434/475 Nos Completed)	285	2-Oct-21	13-Jul-22																	
Pumping Test																				
Installation of Pump Wells (53/102 Nos completed)	62	11-Apr-22	11-Jun-22																	
Baseline Monitoring	1	13-Jun-22	13-Jun-22																	
Pumping Test	14	14-Jul-22	27-Jul-22																	

- Actual
- Remaining Works
- Critical Remaining Works

**Zone 2B & 2C**

Activity ID	Activity Name	CMWP Rev.0 Start	CMWP Rev.0 Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	May				June				July				August						
									1				2				3				4						
									30	07	14	21	28	04	11	18	25	02	09	16	23	30	06	13	20	27	
Piling for Integrated Basement and U/G Road in Zone 2B & 2C																											
Contract Dates																											
Key Dates																											
KD for Zone 2B																											
	KD01	KD01 (Stage 1-1) - (18 May 2022)			18-May-22	0		16-Jul-22*	-59	0%																	
	KD03	KD03 (Stage 3-1) - (26 Aug 2022)			26-Aug-22	0		26-Aug-22*	0	0%																	
KD for Zone 2C																											
	KD04	KD04 (Stage 4-1) - (26 Aug 2022)			25-Aug-22	0		26-Aug-22*	0	0%																	
Optional Works subjected to CA's Instruction																											
	CO2A10	Last CAI date for Optional Works Item No.2A (330 Days to 390 Days after Commencement) if item No. 3 is		16-Aug-22		0	16-Aug-22		71	0%																	
	CO3A	Last CAI date for Optional Works Item No.3 (within 280 Days after Commencement) [not exercised]		28-Apr-22		0	28-Apr-22 A			100%																	
Schedule of Milestones																											
Cost Center A: Preliminaries																											
	MS.A04	Milestone A04 - Month 6 (Jan 2022)			31-Jan-22	0		28-May-22*	-116	0%																	
	MS.A05	Milestone A05 - Month 7 (Feb 2022)			28-Feb-22	0		28-May-22*	-88	0%																	
	MS.A06	Milestone A06 - Month 9 (Apr 2022)			30-Apr-22	0		28-May-22*	-27	0%																	
	MS.A07	Milestone A07 - Month 10 (May 2022)			31-May-22	0		31-May-22*	0	0%																	
	MS.A08	Milestone A08 - Month 12 (Jul 2022)			31-Jul-22	0		31-Jul-22*	0	0%																	
Cost Center B: General and Hoarding Works																											
	MS.B01	Milestone B01 - Month 2 (Sep 2021)			30-Sep-21	0		28-May-22*	-240	0%																	
	MS.B02	Milestone B02 - Month 3 (Oct 2021)			31-Oct-21	0		28-May-22*	-209	0%																	
	MS.B03	Milestone B03 - Month 4 (Nov 2021)			30-Nov-21	0		28-May-22*	-179	0%																	
Cost Center C: Socketed Steel H-Pile Foundation																											
ID: 2B2C-20220527_w		Planned Bar		Milestone		West Kowloon Cultural District Authority Piling for Integrated Basement and U/G Road in Zone 2B 2C 3 Month Rolling Programme as of 27 May 2022 Based on CMWP Rev.0				VIBRO				Date		Revision		Checked		Approved							
Data Date: 28-May-22		Critical Bar		Critical MS										4-Mar-22		Rev.0		KL		B							
Print Date: 30-May-22_17:49		Baseline		Baseline MS																							
Page 1 of 31																											

Activity ID	Activity Name	CMWP Rev.0 Start	CMWP Rev.0 Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	May				June				July				August						
									1				2				3				4						
									30	07	14	21	28	04	11	18	25	02	09	16	23	30	06	13	20	27	
MS.C03	Milestone C03 - Month 8 (Mar 2022)		31-May-22	0		28-May-22*	-23	0%																			
MS.C04	Milestone C04 - Month 9 (Apr 2022)		31-Jul-22	0		31-Jul-22*	0	0%																			
Cost Center D: Bored Pile Foundation at Eastern Part of Zone 2B (KD05/KD01)																											
MS.D02	Milestone D02 - Month 7 (Feb 2022)		31-Mar-22	0		28-May-22*	-89	0%																			
MS.D02^	Milestone D2A^ - Month 6 (Jan 2022)		31-Jan-22	0		28-May-22*	-117	0%																			
MS.D03	Milestone D03 - Month 8 (Mar 2022)		30-Apr-22	0		28-May-22*	-58	0%																			
MS.D03^	Milestone D3A^ - Month 8 (Mar 2022)		31-Mar-22	0		28-May-22*	-58	0%																			
MS.D04	Milestone D04 - Month 11 (Jun 2022)		30-Jun-22	0		30-Jun-22*	0	0%																			
MS.D04^	Milestone D4A^ - Month 10 (May 2022)		31-May-22	0		31-May-22*	0	0%																			
Cost Center E: Bored Pile Foundation at Middle Part of Zone 2B (KD06)																											
MS.E02	Milestone E02 - Month 8 (Mar 2022)		31-Jul-22	0		28-May-22*	-58	0%																			
MS.E03	Milestone E03 - Month 11 (Jun 2022)		30-Sep-22	0		30-Jun-22*	0	0%																			
Cost Center F: Bored Pile Foundation at Western Part of Zone 2B (KD07/KD03)																											
MS.F02	Milestone F02 - Month 11 (Jun 2022)		30-Jun-22	0		30-Jun-22*	0	0%																			
Cost Center G: Bored Pile Foundation at Western Part of Zone 2C (KD08/KD04)																											
MS.G02	Milestone G02 - Month 9 (Apr 2022)		30-Jun-22	0		28-May-22*	-28	0%																			
MS.G03	Milestone G03 - Month 12 (Jul 2022)		31-Aug-22	0		31-Jul-22*	0	0%																			
Cost Center H: Bored Pile Foundation at Eastern Part of Zone 2C (KD09/KD02)																											
MS.H02	Milestone H02 - Month 8 (Mar 2022)		31-May-22	0		28-May-22*	-58	0%																			
MS.H03	Milestone H03 - Month 12 (Jul 2022)		30-Jun-22	0		31-Jul-22*	0	0%																			
MS.H2A^	Milestone H2A^ - Month 8 (Mar 2022)		31-Mar-22	0		28-May-22*	-58	0%																			
MS.H3A^	Milestone H3A^ - Month 11 (Jun 2022)		30-Jun-22	0		30-Jun-22*	0	0%																			
Cost Center M: Optional Works Item No. 1A: Tree Felling Works (KD10)																											

ID: 2B2C-20220527\_w  
Data Date: 28-May-22  
Print Date: 30-May-22\_17:49  
Page 2 of 31

Planned Bar

Critical Bar

Baseline

Milestone

Critical MS

Baseline MS

West Kowloon Cultural District Authority

Piling for Integrated Basement and U/G Road in Zone 2B 2C

3 Month Rolling Programme as of 27 May 2022

Based on CMWP Rev.0

VIBRO

Date

4-Mar-22

Revision

Rev.0

Checked

KL

Approved

B

Activity ID	Activity Name	CMWP Rev.0 Start	CMWP Rev.0 Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	May				June				July				August						
									1				2				3				4						
									30	07	14	21	28	04	11	18	25	02	09	16	23	30	06	13	20	27	
	MS.M01	Milestone M01 - Month 2 (Sep 2021)		30-Sep-21	0		28-May-22*	-239	0%																		
	MS.M02	Milestone M02 - Month 6 (Jan 2022)		31-Jan-22	0		28-May-22*	-117	0%																		
Cost Center N: Optional Works Item No. 1B: Tree Felling Works (KD11)																											
	MS.N01	Milestone N01 - Month 2 (Sep 2021)		30-Sep-21	0		28-May-22*	-239	0%																		
	MS.N02	Milestone N02 - Month 6 (Jan 2022)		31-Jan-22	0		28-May-22*	-117	0%																		
Access Dates of Site Portion																											
	ACD270	Access within 270 days after Commencement (18 Apr 2022)	18-Apr-22		0	28-May-22		12	0%																		
120 days after Commencement																											
	ACB10	Access to Site Portion B10	19-Nov-21		0	28-May-22		-110	0%																		
270 days after Commencement																											
	ACB12	Access to Site Portion B12	18-Apr-22		0	30-Apr-22 A			100%																		
	ACB35	Access to Site Portion B35 (To be agreed with the Zone 2A contractor)	18-Apr-22		0	28-May-22		12	0%																		
Mobilization Stage																											
Site Mobilization Works																											
Pre-Construction Works before Piling Commencement																											
	MOBP.10.1300	Trial Pit for Drillholes & Removal of Existing Substructures / Ground Slab [503 nos]	19-Aug-21	30-Apr-22	297	19-Aug-21 A	11-Jun-22	95	90%																		
Construction Stage																											
Pile Construction																											
Initial Mobilization																											

ID: 2B2C-20220527\_w  
Data Date: 28-May-22  
Print Date: 30-May-22\_17:49  
Page 3 of 31

Planned Bar

Critical Bar

Baseline

Milestone

Critical MS

Baseline MS

West Kowloon Cultural District Authority

Piling for Integrated Basement and U/G Road in Zone 2B 2C

3 Month Rolling Programme as of 27 May 2022

Based on CMWP Rev.0

VIBRO

Date	Revision	Checked	Approved
4-Mar-22	Rev.0	KL	B

Activity ID		Activity Name	CMWP Rev.0 Start	CMWP Rev.0 Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	May 1				June 2				July 3				August 4																			
										1				2				3				4																			
										30	07	14	21	28	04	11	18	25	02	09	16	23	30	06	13	20	27														
MO.1010										Initial Mobilization for Predrilling of BP (CCD / KD05 / KD01)				23-Jul-21				07-Sep-21				258				23-Jul-21 A				07-Jun-22				-16				80%			
MO.1020										Initial Mobilization for Predrilling of BP (CCE / KD06)				23-Jul-21				07-Sep-21				249				23-Jul-21 A				27-May-22 A								50%			
MO.1030										Initial Mobilization for Predrilling of BP (CCF / KD07 / KD03)				23-Jul-21				07-Sep-21				290				23-Jul-21 A				15-Jul-22				36				85%			
MO.1050										Initial Mobilization for Predrilling of BP (CCH / KD09 / KD02)				23-Jul-21				07-Sep-21				260				23-Jul-21 A				09-Jun-22				116				60%			
Predrilling																																									
PD.1080										Predrilling for BP in KD05 [76 nos.]				30-Sep-21				30-Mar-22				200				30-Sep-21 A				07-Jun-22				-22				58%			
PD.1100										Predrilling for BP in KD06 [95 nos.] incl. 5 additional nos.				30-Sep-21				23-May-22				199				30-Sep-21 A				07-Jun-22				107				55%			
PD.1120										Predrilling for BP in KD07 [90 nos.] incl. 2 additional nos.				30-Sep-21				23-May-22				231				30-Sep-21 A				15-Jul-22				166				85%			
PD.1160										Predrilling for BP in KD09 [149 nos.] incl. 4 additional nos.				30-Sep-21				30-Mar-22				203				30-Sep-21 A				09-Jun-22				103				70%			
KD01 (Stage 1-1)																																									
Bored Piles																																									
CD07																																									
07																																									
CBA-BPC41Jb.10										BP - Excavation				13-Apr-22				22-Apr-22				39				13-May-22 A				28-Jun-22				-49				0%			
CBA-BPC41Jb.20										BP - RCD Drilling				23-Apr-22				05-May-22				10				29-Jun-22				11-Jul-22				-49				0%			
CBA-BPC41Jb.30										BP - Airlift, Cage Install and Concrete				06-May-22				12-May-22				5				12-Jul-22				16-Jul-22				-49				0%			
14																																									
CBA-BP04.10										BP - Excavation				12-Apr-22				22-Apr-22				28				20-May-22 A				22-Jun-22				-49				0%			
CBA-BP04.20										BP - RCD Drilling				23-Apr-22				11-May-22				14				23-Jun-22				09-Jul-22				-49				0%			
CBA-BP04.30										BP - Airlift, Cage Install and Concrete				12-May-22				18-May-22				6				11-Jul-22				16-Jul-22				-49				0%			
CD05																																									
04																																									
P22&P19-BP11.30										BP - Airlift, Cage Install and Concrete				25-Feb-22				05-Mar-22				24				08-Apr-22 A				12-May-22 A								100%			
05																																									
P22&P19-BP21.30										BP - Airlift, Cage Install and Concrete				19-Mar-22				28-Mar-22				25				20-Apr-22 A				21-May-22 A								100%			
KD02 (Stage 5-1)																																									
Bored Piles																																									
TD04																																									
03																																									
ID: 2B2C-20220527_w		Planned Bar		Milestone		West Kowloon Cultural District Authority		VIBRO		Date		Revision		Checked		Approved																									
Data Date: 28-May-22		Critical Bar		Critical MS		Piling for Integrated Basement and U/G Road in Zone 2B 2C		H		4-Mar-22		Rev.0		KL		B																									
Print Date: 30-May-22_17:49		Baseline		Baseline MS		3 Month Rolling Programme as of 27 May 2022		M																																	
Page 4 of 31						Based on CMWP Rev.0																																			


Activity ID	Activity Name	CMWP Rev0 Start	CMWP Rev0 Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	May				June				July				August								
									1				2				3				4								
									30	07	14	21	28	04	11	18	25	02	09	16	23	30	06	13	20	27			
	P23-BP117.20	BP - RCD Drilling	10-Dec-21	10-Jan-22	7	22-Apr-22 A	30-Apr-22 A		100%																				
	P23-BP117.30	BP - Airlift, Cage Install and Concrete	20-Jan-22	28-Jan-22	7	03-May-22 A	12-May-22 A		100%																				
KD03 (Stage 3-1)																													
Bored Piles																													
VD02																													
03																													
	P28&P29-BP08.20	BP - RCD Drilling			4	23-Apr-22 A	28-Apr-22 A		100%																				
	P28&P29-BP08.30	BP - Airlift, Cage Install and Concrete			9	29-Apr-22 A	12-May-22 A		100%																				
VD06																													
01																													
	P28&P29-BP29.20	BP - RCD Drilling			3	26-Apr-22 A	29-Apr-22 A		100%																				
	P28&P29-BP29.30	BP - Airlift, Cage Install and Concrete			11	30-Apr-22 A	16-May-22 A		100%																				
11																													
	P28&P29-BP10.10	BP - Excavation			14	19-May-22 A	04-Jun-22	48	0%																				
	P28&P29-BP10.20	BP - RCD Drilling			15	06-Jun-22	22-Jun-22	48	0%																				
	P28&P29-BP10.30	BP - Airlift, Cage Install and Concrete			7	23-Jun-22	30-Jun-22	48	0%																				
VD09																													
01																													
	CBA-BPC54Jb.10	BP - Excavation	26-Feb-22	04-Mar-22	6	28-May-22	04-Jun-22	-41	0%																				
	CBA-BPC54Jb.20	BP - RCD Drilling	05-Mar-22	11-Apr-22	31	06-Jun-22	12-Jul-22	-41	0%																				
	CBA-BPC54Jb.30	BP - Airlift, Cage Install and Concrete	12-Apr-22	21-Apr-22	6	13-Jul-22	19-Jul-22	27	0%																				
02																													
	CBA-BPC54Ka.10	BP - Excavation	04-Apr-22	11-Apr-22	6	06-Jul-22	12-Jul-22	-41	0%																				
	CBA-BPC54Ka.20	BP - RCD Drilling	12-Apr-22	25-May-22	33	13-Jul-22	19-Aug-22	-41	0%																				
	CBA-BPC54Ka.30	BP - Airlift, Cage Install and Concrete	26-May-22	01-Jun-22	6	20-Aug-22	26-Aug-22	0	0%																				
KD04 (Stage 4-1)																													
Bored Piles																													
TD01																													
07																													
	P30-BP06.10	BP - Excavation	31-May-22	07-Jun-22	6	21-Jun-22	27-Jun-22	24	0%																				
	P30-BP06.20	BP - RCD Drilling	08-Jun-22	29-Jun-22	19	28-Jun-22	20-Jul-22	24	0%																				
	P30-BP06.30	BP - Airlift, Cage Install and Concrete	30-Jun-22	09-Jul-22	8	21-Jul-22	29-Jul-22	24	0%																				
TD09																													
01																													
	CBA-BPC54V.10	BP - Excavation	08-Apr-22	14-Apr-22	6	28-May-22	04-Jun-22	-38	0%																				
	CBA-BPC54V.20	BP - RCD Drilling	19-Apr-22	29-Apr-22	10	06-Jun-22	16-Jun-22	-38	0%																				
ID: 2B2C-20220527_w																				Date 4-Mar-22				Revision Rev.0		Checked KL		Approved B	
Data Date: 28-May-22																													
Print Date: 30-May-22_17:49																													
Page 5 of 31																													

Activity ID	Activity Name	CMWP Rev.0 Start	CMWP Rev.0 Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	May				June				July				August								
									1				2				3				4								
									30	07	14	21	28	04	11	18	25	02	09	16	23	30	06	13	20				
CBA-BPC54V.30	BP - Airlift, Cage Install and Concrete	30-Apr-22	06-May-22	5	17-Jun-22	22-Jun-22	55	0%																					
KD05 (Section 1)																													
MO.1060									Initial Mobilization for BP (CCD / KD05 / KD01)																				
		15-Sep-21	15-Nov-21	191	22-Oct-21 A	16-Jun-22	165	80%																					
Bored Piles																													
CD01																													
03																													
P23-BP20.10									BP - Excavation																				
		11-Jan-22	17-Jan-22	6	28-May-22	04-Jun-22	76	0%																					
P23-BP20.20									BP - RCD Drilling																				
		18-Jan-22	07-Feb-22	15	06-Jun-22	22-Jun-22	76	0%																					
P23-BP20.30									BP - Airlift, Cage Install and Concrete																				
		08-Feb-22	15-Feb-22	7	23-Jun-22	30-Jun-22	76	0%																					
16																													
P23-BP31.10									BP - Excavation																				
		13-Jun-22	18-Jun-22	17	27-Apr-22 A	19-May-22 A		100%																					
P23-BP31.20									BP - RCD Drilling																				
		20-Jun-22	07-Jul-22	6	20-May-22 A	27-May-22 A		100%																					
P23-BP31.30									BP - Airlift, Cage Install and Concrete																				
		08-Jul-22	15-Jul-22	40	28-May-22 A	15-Jul-22	64	0%																					
CD07																													
02																													
CBA-BPC43K.10									BP - Excavation																				
		31-Jan-22	09-Feb-22	6	28-May-22	04-Jun-22	-49	0%																					
CBA-BPC43K.20									BP - RCD Drilling																				
		10-Feb-22	21-Feb-22	10	06-Jun-22	16-Jun-22	-49	0%																					
CBA-BPC43K.30									BP - Airlift, Cage Install and Concrete																				
		22-Feb-22	26-Feb-22	5	17-Jun-22	22-Jun-22	78	0%																					
04																													
CBA-BPC40Ja.30									BP - Airlift, Cage Install and Concrete																				
		22-Mar-22	26-Mar-22	11	26-Apr-22 A	11-May-22 A		100%																					
05																													
CBA-BPC42K.10									BP - Excavation																				
		15-Mar-22	21-Mar-22	6	10-Jun-22	16-Jun-22	-49	0%																					
CBA-BPC42K.20									BP - RCD Drilling																				
		22-Mar-22	01-Apr-22	10	17-Jun-22	28-Jun-22	-49	0%																					
CBA-BPC42K.30									BP - Airlift, Cage Install and Concrete																				
		02-Apr-22	08-Apr-22	5	29-Jun-22	05-Jul-22	73	0%																					
08																													
CBA-BPC43J.10									BP - Excavation																				
		28-Apr-22	05-May-22	23	13-Apr-22 A	16-May-22 A		100%																					
CBA-BPC43J.20									BP - RCD Drilling																				
		06-May-22	18-May-22	2	17-May-22 A	19-May-22 A		100%																					
CBA-BPC43J.30									BP - Airlift, Cage Install and Concrete																				
		19-May-22	24-May-22	12	20-May-22 A	02-Jun-22	99	0%																					
09																													
CBA-BP02.10									BP - Excavation																				
		11-May-22	18-May-22	7	04-Jul-22	11-Jul-22	29	0%																					
CBA-BP02.20									BP - RCD Drilling																				
		19-May-22	04-Jun-22	14	12-Jul-22	27-Jul-22	29	0%																					
CBA-BP02.30									BP - Airlift, Cage Install and Concrete																				
		06-Jun-22	11-Jun-22	6	28-Jul-22	03-Aug-22	43	0%																					
10																													
CBA-BP05.10									BP - Excavation																				
		28-May-22	04-Jun-22	6	21-Jul-22	27-Jul-22	29	0%																					
ID: 2B2C-20220527_w		Planned Bar		Milestone		West Kowloon Cultural District Authority Piling for Integrated Basement and U/G Road in Zone 2B 2C 3 Month Rolling Programme as of 27 May 2022 Based on CMWP Rev.0																							
Data Date: 28-May-22		Critical Bar		Critical MS																									
Print Date: 30-May-22_17:49		Baseline		Baseline MS																									
Page 6 of 31																													
						VIBRO								Date 4-Mar-22				Revision Rev.0				Checked KL				Approved B			

[illegible]

Activity ID		Activity Name	CMWP Rev.0 Start	CMWP Rev.0 Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	May 1				June 2				July 3				August 4												
										30	07	14	21	28	04	11	18	25	02	09	16	23	30	06	13	20	27							
10																																		
P22&P19-BP16.10		BP - Excavation	13-Jun-22	18-Jun-22	6	18-Aug-22	24-Aug-22	3	0%																									
P22&P19-BP16.20		BP - RCD Drilling	20-Jun-22	12-Jul-22	19	25-Aug-22	16-Sep-22	3	0%																									
11																																		
P22&P19-BP26.10		BP - Excavation	06-Jan-22	12-Jan-22	6	28-May-22	04-Jun-22	23	0%																									
P22&P19-BP26.20		BP - RCD Drilling	13-Jan-22	18-Feb-22	29	06-Jun-22	09-Jul-22	23	0%																									
P22&P19-BP26.30		BP - Airlift, Cage Install and Concrete	19-Feb-22	28-Feb-22	8	11-Jul-22	19-Jul-22	45	0%																									
13																																		
P22&P19-BP25.10		BP - Excavation	07-Mar-22	12-Mar-22	6	26-Jul-22	01-Aug-22	23	0%																									
P22&P19-BP25.20		BP - RCD Drilling	14-Mar-22	04-Apr-22	19	02-Aug-22	23-Aug-22	23	0%																									
P22&P19-BP25.30		BP - Airlift, Cage Install and Concrete	06-Apr-22	14-Apr-22	8	24-Aug-22	01-Sep-22	23	0%																									
14																																		
P22&P19-BP10.10		BP - Excavation	29-Mar-22	04-Apr-22	11	22-Apr-22 A	06-May-22 A		100%																									
P22&P19-BP10.20		BP - RCD Drilling	06-Apr-22	30-Apr-22	6	07-May-22 A	16-May-22 A		100%																									
P22&P19-BP10.30		BP - Airlift, Cage Install and Concrete	03-May-22	12-May-22	18	17-May-22 A	07-Jun-22	96	0%																									
15																																		
P22&P19-BP17.10		BP - Excavation	25-Apr-22	30-Apr-22	6	28-May-22	04-Jun-22	71	0%																									
P22&P19-BP17.20		BP - RCD Drilling	03-May-22	25-May-22	19	06-Jun-22	27-Jun-22	71	0%																									
P22&P19-BP17.30		BP - Airlift, Cage Install and Concrete	26-May-22	04-Jun-22	8	28-Jun-22	07-Jul-22	71	0%																									
CD04																																		
01																																		
P17-BP03.10		BP - Excavation	24-Nov-21	30-Nov-21	6	28-May-22	04-Jun-22	-63	0%																									
P17-BP03.20		BP - RCD Drilling	01-Dec-21	17-Dec-21	15	06-Jun-22	22-Jun-22	-63	0%																									
P17-BP03.30		BP - Airlift, Cage Install and Concrete	18-Dec-21	28-Dec-21	7	23-Jun-22	30-Jun-22	69	0%																									
02																																		
P17-BP12.10		BP - Excavation	20-Dec-21	28-Dec-21	6	16-Jun-22	22-Jun-22	-63	0%																									
P17-BP12.20		BP - RCD Drilling	29-Dec-21	15-Jan-22	15	23-Jun-22	11-Jul-22	-63	0%																									
P17-BP12.30		BP - Airlift, Cage Install and Concrete	17-Jan-22	24-Jan-22	7	12-Jul-22	19-Jul-22	61	0%																									
03																																		
P17-BP10.30		BP - Airlift, Cage Install and Concrete	07-Feb-22	14-Feb-22	20	20-Apr-22 A	16-May-22 A		100%																									
04																																		
P17-BP14.10		BP - Excavation	27-Jan-22	05-Feb-22	46	17-May-22 A	11-Jul-22	-63	0%																									
P17-BP14.20		BP - RCD Drilling	07-Feb-22	28-Feb-22	19	12-Jul-22	02-Aug-22	-63	0%																									
P17-BP14.30		BP - Airlift, Cage Install and Concrete	01-Mar-22	09-Mar-22	8	03-Aug-22	11-Aug-22	-8	0%																									
05																																		
P17-BP16.10		BP - Excavation	22-Feb-22	28-Feb-22	6	27-Jul-22	02-Aug-22	-63	0%																									
P17-BP16.20		BP - RCD Drilling	01-Mar-22	17-Mar-22	15	03-Aug-22	19-Aug-22	-63	0%																									
ID: 2B2C-20220527_w		Planned Bar	Milestone	West Kowloon Cultural District Authority Piling for Integrated Basement and U/G Road in Zone 2B 2C 3 Month Rolling Programme as of 27 May 2022 Based on CMWP Rev.0																VIBRO H W				Date		Revision		Checked		Approved				
Data Date: 28-May-22		Critical Bar	Critical MS																					4-Mar-22		Rev.0		KL		B				
Print Date: 30-May-22_17:49		Baseline	Baseline MS																															
Page 8 of 31																																		

Activity ID		Activity Name	CMWP Rev.0 Start	CMWP Rev.0 Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	May				June				July				August																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																		
										1				2				3				4																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																		
										30	07	14	21	28	04	11	18	25	02	09	16	23	30	06	13	20	27																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																													
	P17-BP16.30	BP - Airlift, Cage Install and Concrete	18-Mar-22	25-Mar-22	7	20-Aug-22	27-Aug-22	-15	0%																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																															</

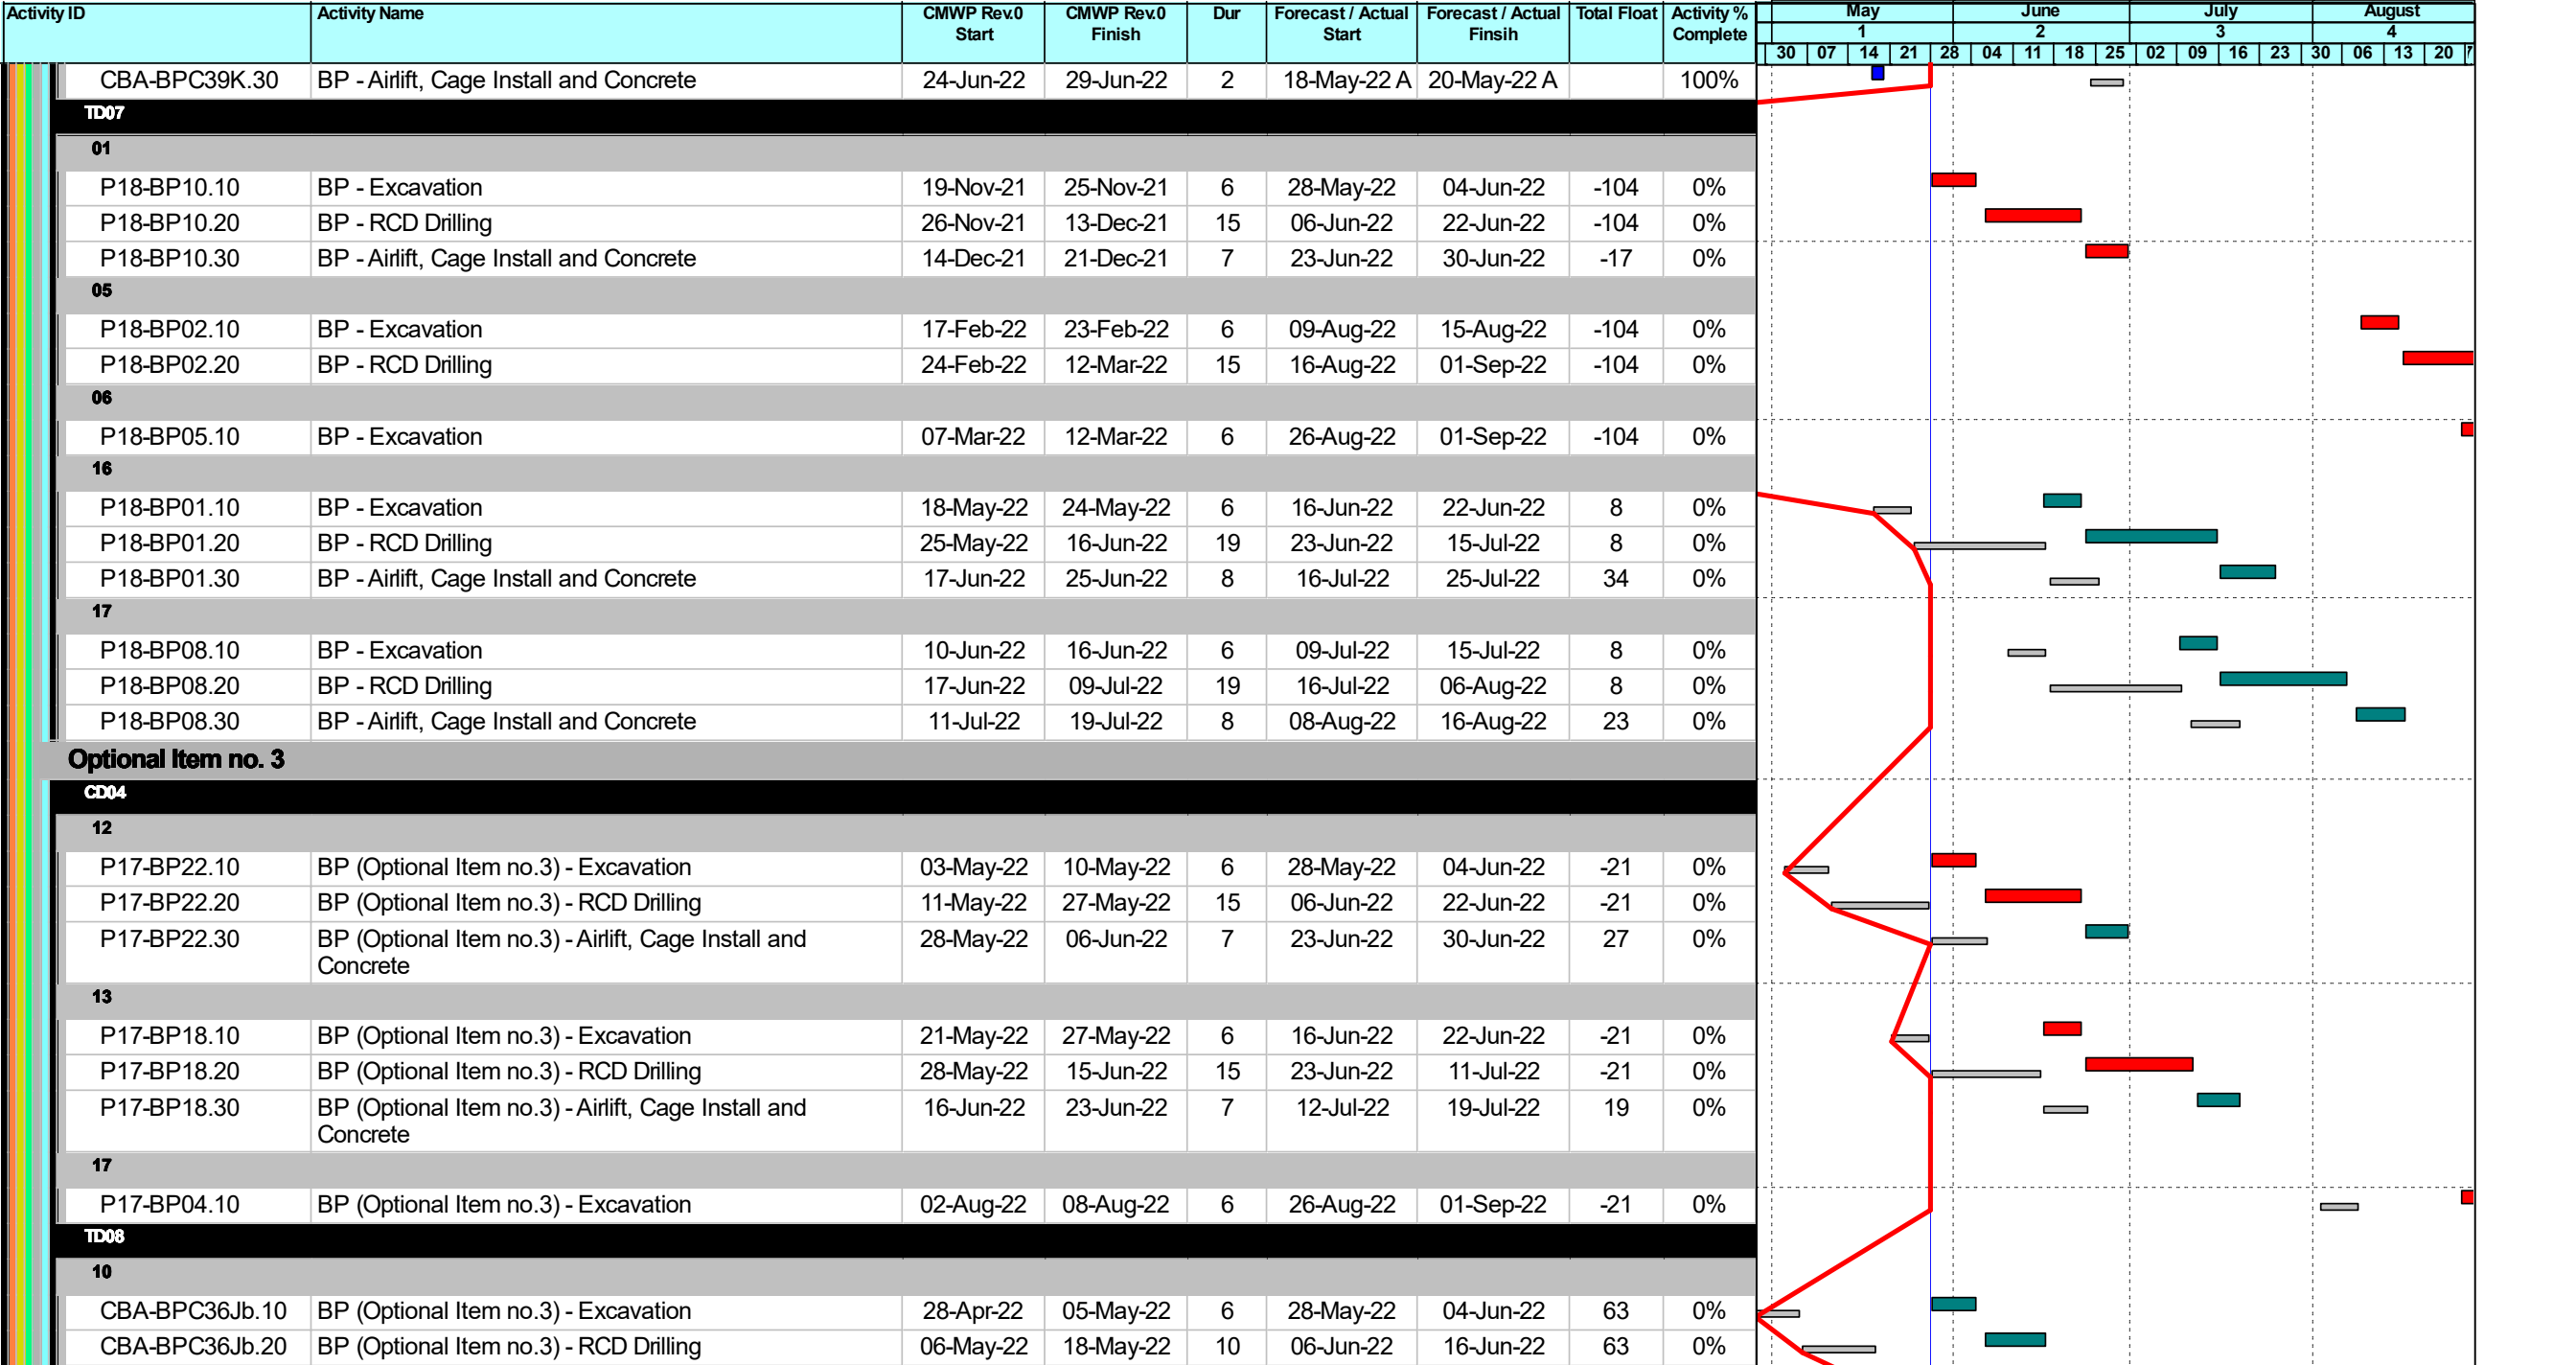

Planned Bar

Critical Bar

Baseline

Milestone

Critical MS

Baseline MS

Activity ID		Activity Name	CMWP Rev.0 Start	CMWP Rev.0 Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	May				June				July				August																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																															
										1				2				3				4																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																															
										30	07	14	21	28	04	11	18	25	02	09	16	23	30	06	13	20	27																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																										
	CBA-BPC36Jb.30	BP (Optional Item no.3) - Airlift, Cage Install and Concrete	19-May-22	24-May-22	5	17-Jun-22	22-Jun-22	73	0%																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																												

Activity ID		Activity Name	CMWP Rev.0 Start	CMWP Rev.0 Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	May 1				June 2				July 3				August 4				
										1				2				3				4				
										30	07	14	21	28	04	11	18	25	02	09	16	23	30	06	13	20
	P24&P27-BP27.20	BP - RCD Drilling			19	11-Jul-22	01-Aug-22	-64	0%																	
	P24&P27-BP27.30	BP - Airlift, Cage Install and Concrete			8	02-Aug-22	10-Aug-22	170	0%																	
	03																									
	P24&P27-BP28.10	BP - Excavation			22	29-Apr-22 A	27-May-22 A		100%																	
	P24&P27-BP28.20	BP - RCD Drilling			19	28-May-22 A	20-Jun-22	205	0%																	
	P24&P27-BP28.30	BP - Airlift, Cage Install and Concrete			8	21-Jun-22	29-Jun-22	205	0%																	
	VD08																									
	01																									
	P23-BP07.10	BP - Excavation	15-Jun-22	21-Jun-22	6	15-Jun-22	21-Jun-22	22	0%																	
	P23-BP07.20	BP - RCD Drilling	22-Jun-22	14-Jul-22	19	22-Jun-22	14-Jul-22	22	0%																	
	P23-BP07.30	BP - Airlift, Cage Install and Concrete	15-Jul-22	23-Jul-22	8	15-Jul-22	23-Jul-22	137	0%																	
	02																									
	P24&P27-BP06.10	BP - Excavation			6	08-Jul-22	14-Jul-22	51	0%																	
	P24&P27-BP06.20	BP - RCD Drilling			29	15-Jul-22	17-Aug-22	51	0%																	
	P24&P27-BP06.30	BP - Airlift, Cage Install and Concrete			8	18-Aug-22	26-Aug-22	116	0%																	
	03																									
	P24&P27-BP04.10	BP - Excavation			6	11-Aug-22	17-Aug-22	51	0%																	
	P24&P27-BP04.20	BP - RCD Drilling			29	18-Aug-22	21-Sep-22	51	0%																	
	08																									
	P24&P27-BP36.10	BP - Excavation			6	08-Jul-22	14-Jul-22	22	0%																	
	P24&P27-BP36.20	BP - RCD Drilling			19	15-Jul-22	05-Aug-22	22	0%																	
	P24&P27-BP36.30	BP - Airlift, Cage Install and Concrete			8	06-Aug-22	15-Aug-22	118	0%																	
	09																									
	P24&P27-BP29.10	BP - Excavation			6	30-Jul-22	05-Aug-22	22	0%																	
	P24&P27-BP29.20	BP - RCD Drilling			19	06-Aug-22	27-Aug-22	22	0%																	
	10																									
	P24&P27-BP05.10	BP - Excavation			6	22-Aug-22	27-Aug-22	22	0%																	
	VD10																									
	01																									
	CBA-BPC47K.10	BP - Excavation	02-Jun-22	10-Jun-22	7	02-Jun-22	10-Jun-22	35	0%																	
	CBA-BPC47K.20	BP - RCD Drilling	11-Jun-22	27-Jun-22	14	11-Jun-22	27-Jun-22	35	0%																	
	CBA-BPC47K.30	BP - Airlift, Cage Install and Concrete	28-Jun-22	05-Jul-22	6	28-Jun-22	05-Jul-22	159	0%																	
	02																									
	CBA-BPC49K.10	BP - Excavation	20-Jun-22	27-Jun-22	7	20-Jun-22	27-Jun-22	35	0%																	
	CBA-BPC49K.20	BP - RCD Drilling	28-Jun-22	14-Jul-22	14	28-Jun-22	14-Jul-22	35	0%																	
	CBA-BPC49K.30	BP - Airlift, Cage Install and Concrete	15-Jul-22	21-Jul-22	6	15-Jul-22	21-Jul-22	151	0%																	
	03																									


ID: 2B2C-20220527_w Data Date: 28-May-22 Print Date: 30-May-22_17:50 Page 12 of 31	<div></div> Planned Bar	<div></div> Milestone	<div><div>West Kowloon Cultural District Authority</div><div>Piling for Integrated Basement and U/G Road in Zone 2B 2C</div><div>3 Month Rolling Programme as of 27 May 2022</div><div>Based on CMWP Rev.0</div></div>	<div><div>VIBRO</div><div></div><div></div></div>	Date	Revision	Checked	Approved
	<div></div> Critical Bar	<div></div> Critical MS			4-Mar-22	Rev.0	KL	B
	<div></div> Baseline	<div></div> Baseline MS						


[illegible]

[illegible]

[illegible]

Activity ID	Activity Name	CMWP Rev.0 Start	CMWP Rev.0 Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	May				June				July				August														
									1				2				3				4														
									30	07	14	21	28	04	11	18	25	02	09	16	23	30	06	13	20										
VD02																																			
02																																			
P24&P27-BP08.10	BP - Excavation			6	28-May-22	04-Jun-22	101	0%																											
P24&P27-BP08.20	BP - RCD Drilling			29	06-Jun-22	09-Jul-22	101	0%																											
P24&P27-BP08.30	BP - Airlift, Cage Install and Concrete			8	11-Jul-22	19-Jul-22	281	0%																											
04																																			
P26-BP03.10	BP - Excavation	06-Apr-22	12-Apr-22	6	04-Jul-22	09-Jul-22	101	0%																											
P26-BP03.20	BP - RCD Drilling	13-Apr-22	21-May-22	29	11-Jul-22	12-Aug-22	101	0%																											
P26-BP03.30	BP - Airlift, Cage Install and Concrete	23-May-22	31-May-22	8	13-Aug-22	22-Aug-22	205	0%																											
05																																			
P26-BP01.10	BP - Excavation	16-May-22	21-May-22	6	06-Aug-22	12-Aug-22	101	0%																											
P26-BP01.20	BP - RCD Drilling	23-May-22	14-Jul-22	44	13-Aug-22	06-Oct-22	101	0%																											
12																																			
P24&P27-BP14.10	BP - Excavation			29	30-Mar-22 A	10-May-22 A		100%																											
P24&P27-BP14.20	BP - RCD Drilling			5	11-May-22 A	17-May-22 A		100%																											
P24&P27-BP14.30	BP - Airlift, Cage Install and Concrete			17	18-May-22 A	07-Jun-22	200	0%																											
13																																			
P28&P29-BP05.10	BP - Excavation			6	28-May-22	04-Jun-22	74	0%																											
P28&P29-BP05.20	BP - RCD Drilling			19	06-Jun-22	27-Jun-22	74	0%																											
P28&P29-BP05.30	BP - Airlift, Cage Install and Concrete			8	28-Jun-22	07-Jul-22	183	0%																											
14																																			
P28&P29-BP09.10	BP - Excavation			6	21-Jun-22	27-Jun-22	74	0%																											
P28&P29-BP09.20	BP - RCD Drilling			19	28-Jun-22	20-Jul-22	74	0%																											
P28&P29-BP09.30	BP - Airlift, Cage Install and Concrete			8	21-Jul-22	29-Jul-22	172	0%																											
16																																			
P24&P27-BP01.10	BP - Excavation			31	19-Apr-22 A	27-May-22 A		100%																											
P24&P27-BP01.20	BP - RCD Drilling			29	28-May-22 A	02-Jul-22	287	0%																											
P24&P27-BP01.30	BP - Airlift, Cage Install and Concrete			8	04-Jul-22	12-Jul-22	287	0%																											
17																																			
P24&P27-BP13.10	BP - Excavation			6	17-Aug-22	23-Aug-22	74	0%																											
P24&P27-BP13.20	BP - RCD Drilling			29	24-Aug-22	27-Sep-22	74	0%																											
VD03																																			
02																																			
P30-BP59.10	BP - Excavation	23-Feb-22	01-Mar-22	111	06-Jan-22 A	26-May-22 A		100%																											
P30-BP59.20	BP - RCD Drilling	02-Mar-22	04-Apr-22	30	27-May-22 A	02-Jul-22	-32	0%																											
P30-BP59.30	BP - Airlift, Cage Install and Concrete	06-Apr-22	14-Apr-22	8	04-Jul-22	12-Jul-22	155	0%																											
09																																			
ID: 2B2C-20220527_w Data Date: 28-May-22 Print Date: 30-May-22_17:50 Page 16 of 31									<div><div><div></div><div></div><div></div></div><div><div>Planned Bar</div><div>Critical Bar</div><div>Baseline</div></div><div><div>◆</div><div>◆</div><div>◆</div></div><div><div>Milestone</div><div>Critical MS</div><div>Baseline MS</div></div></div> <td colspan="9"><div>West Kowloon Cultural District Authority</div><div>Piling for Integrated Basement and U/G Road in Zone 2B 2C</div><div>3 Month Rolling Programme as of 27 May 2022</div><div>Based on CMWP Rev.0</div></td> <td colspan="9"><div><div>VIBRO</div><div><div></div><div></div><div></div></div></div><div><div>Date</div><div>4-Mar-22</div><div>Revision</div><div>Rev.0</div><div>Checked</div><div>KL</div><div>Approved</div><div>B</div></div></td>									<div>West Kowloon Cultural District Authority</div> <div>Piling for Integrated Basement and U/G Road in Zone 2B 2C</div> <div>3 Month Rolling Programme as of 27 May 2022</div> <div>Based on CMWP Rev.0</div>									<div><div>VIBRO</div><div><div></div><div></div><div></div></div></div> <div><div>Date</div><div>4-Mar-22</div><div>Revision</div><div>Rev.0</div><div>Checked</div><div>KL</div><div>Approved</div><div>B</div></div>								

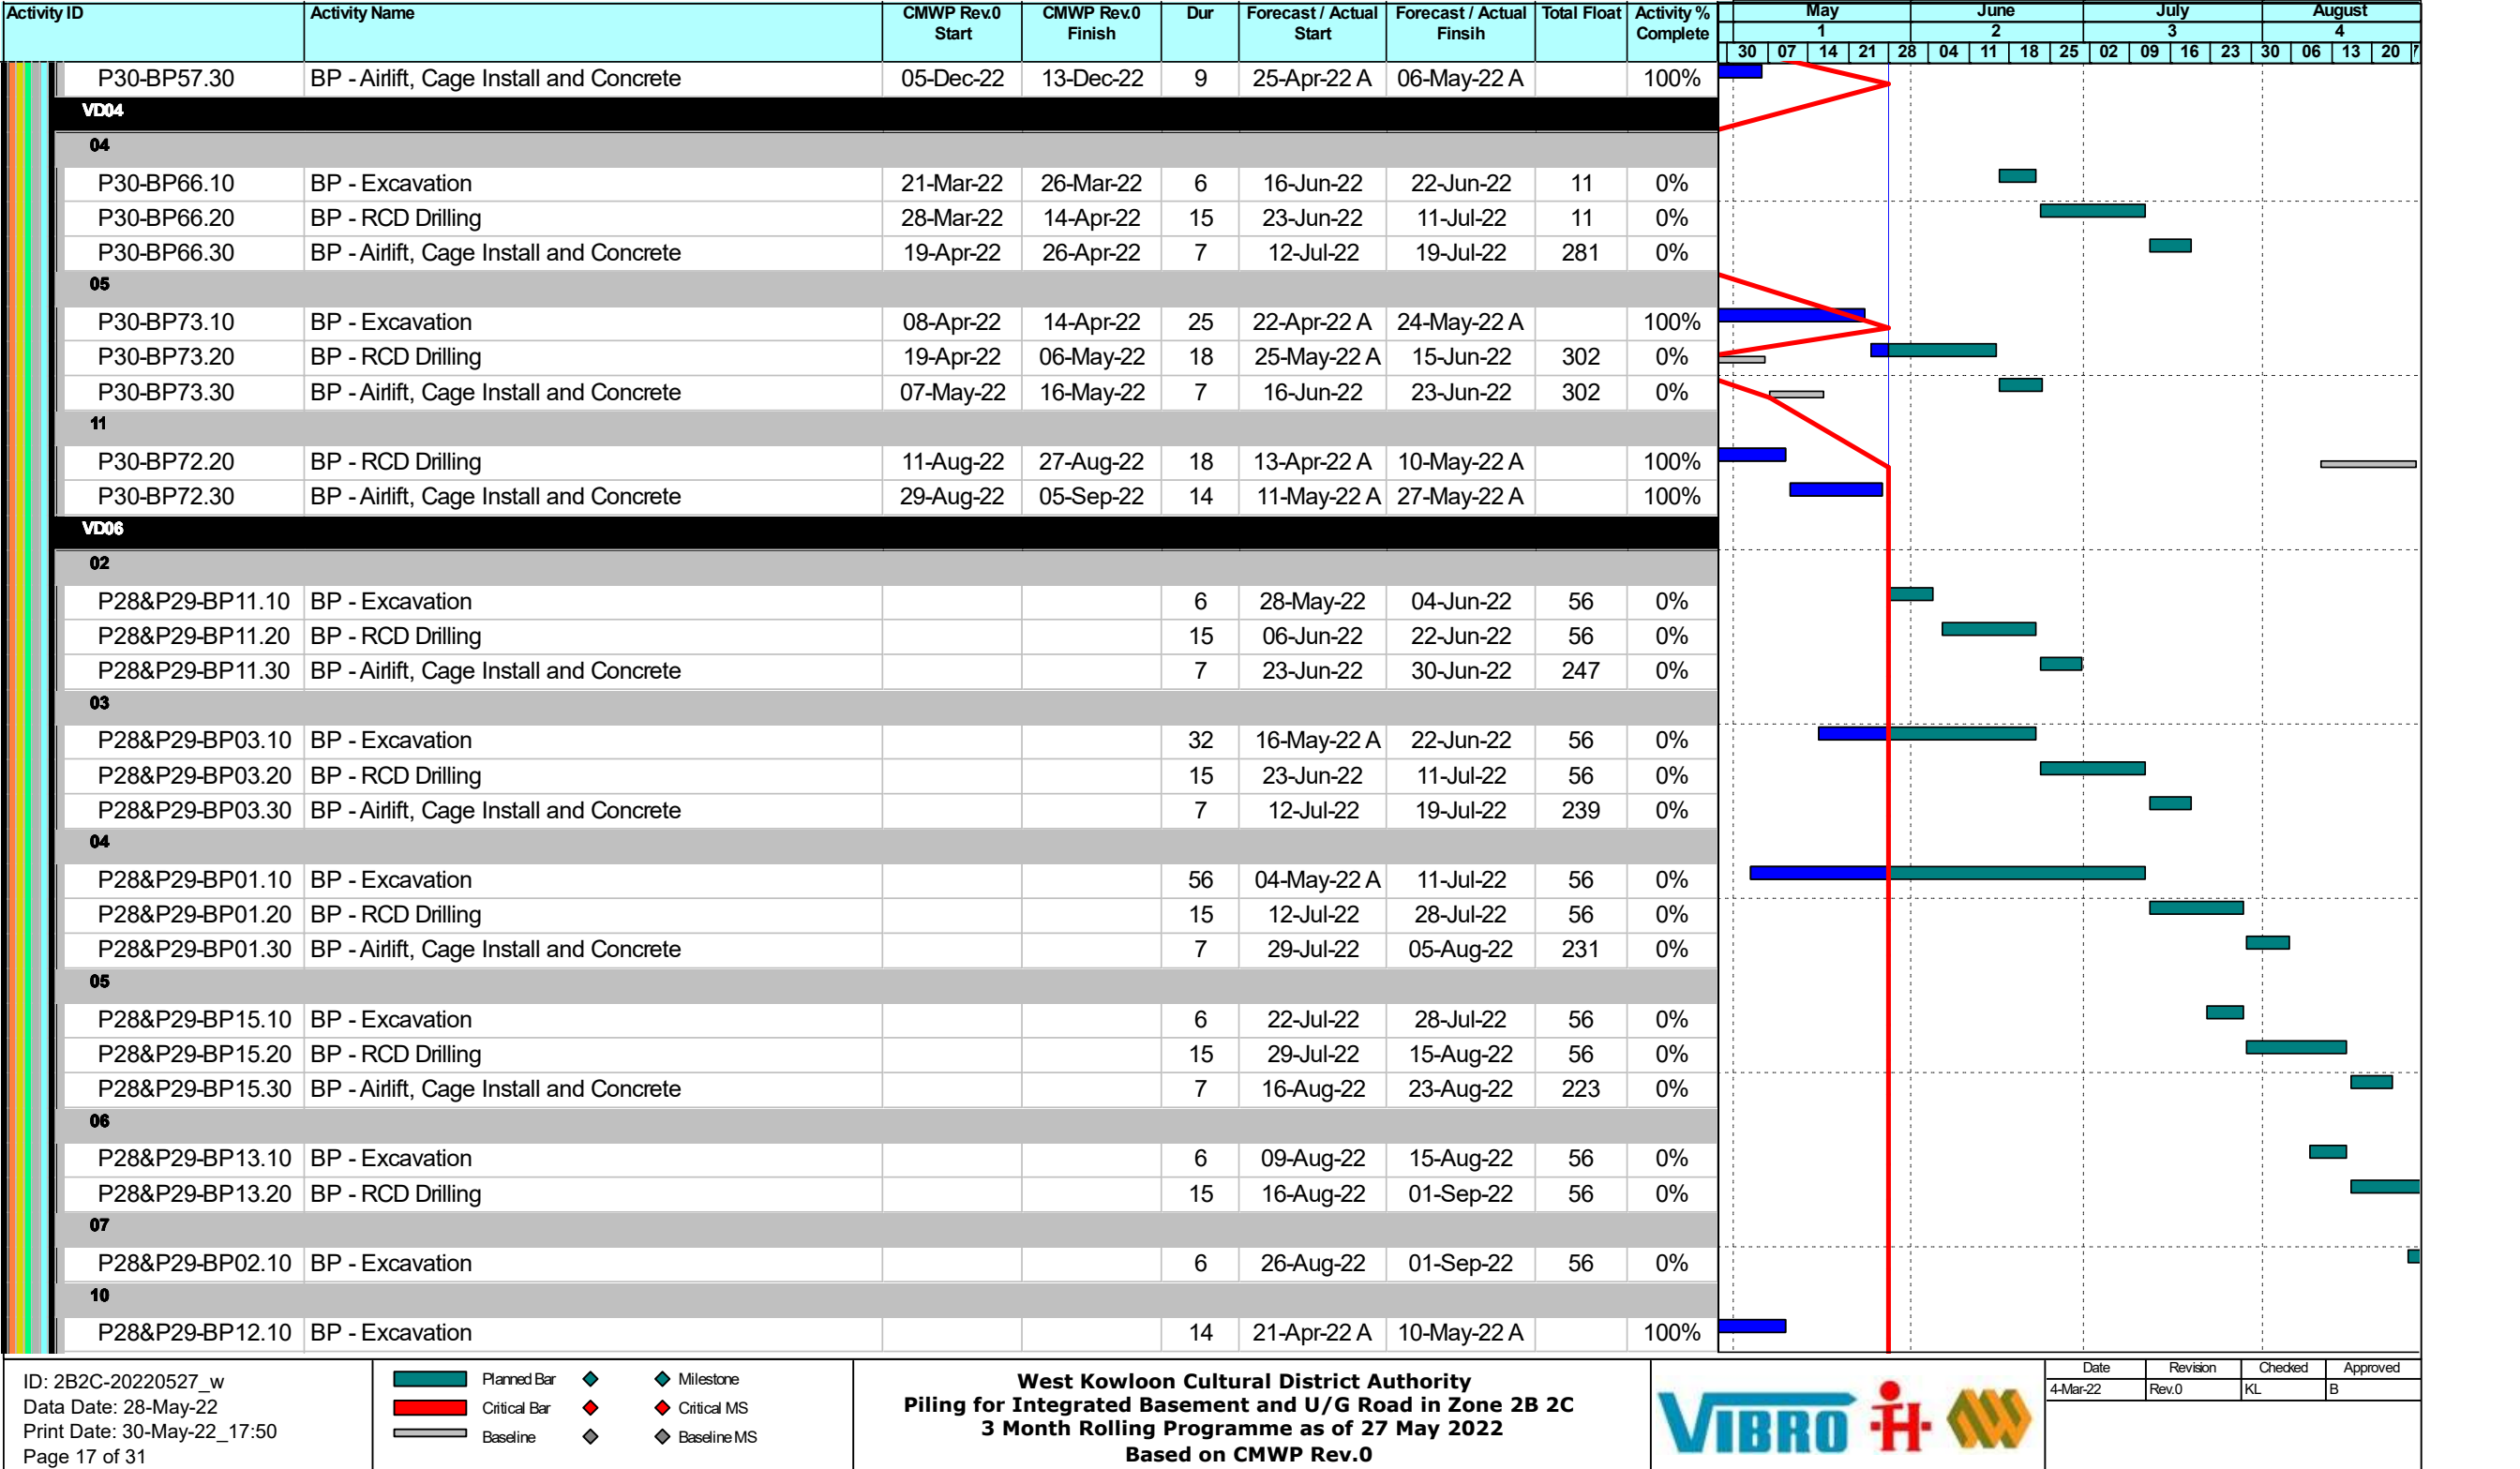

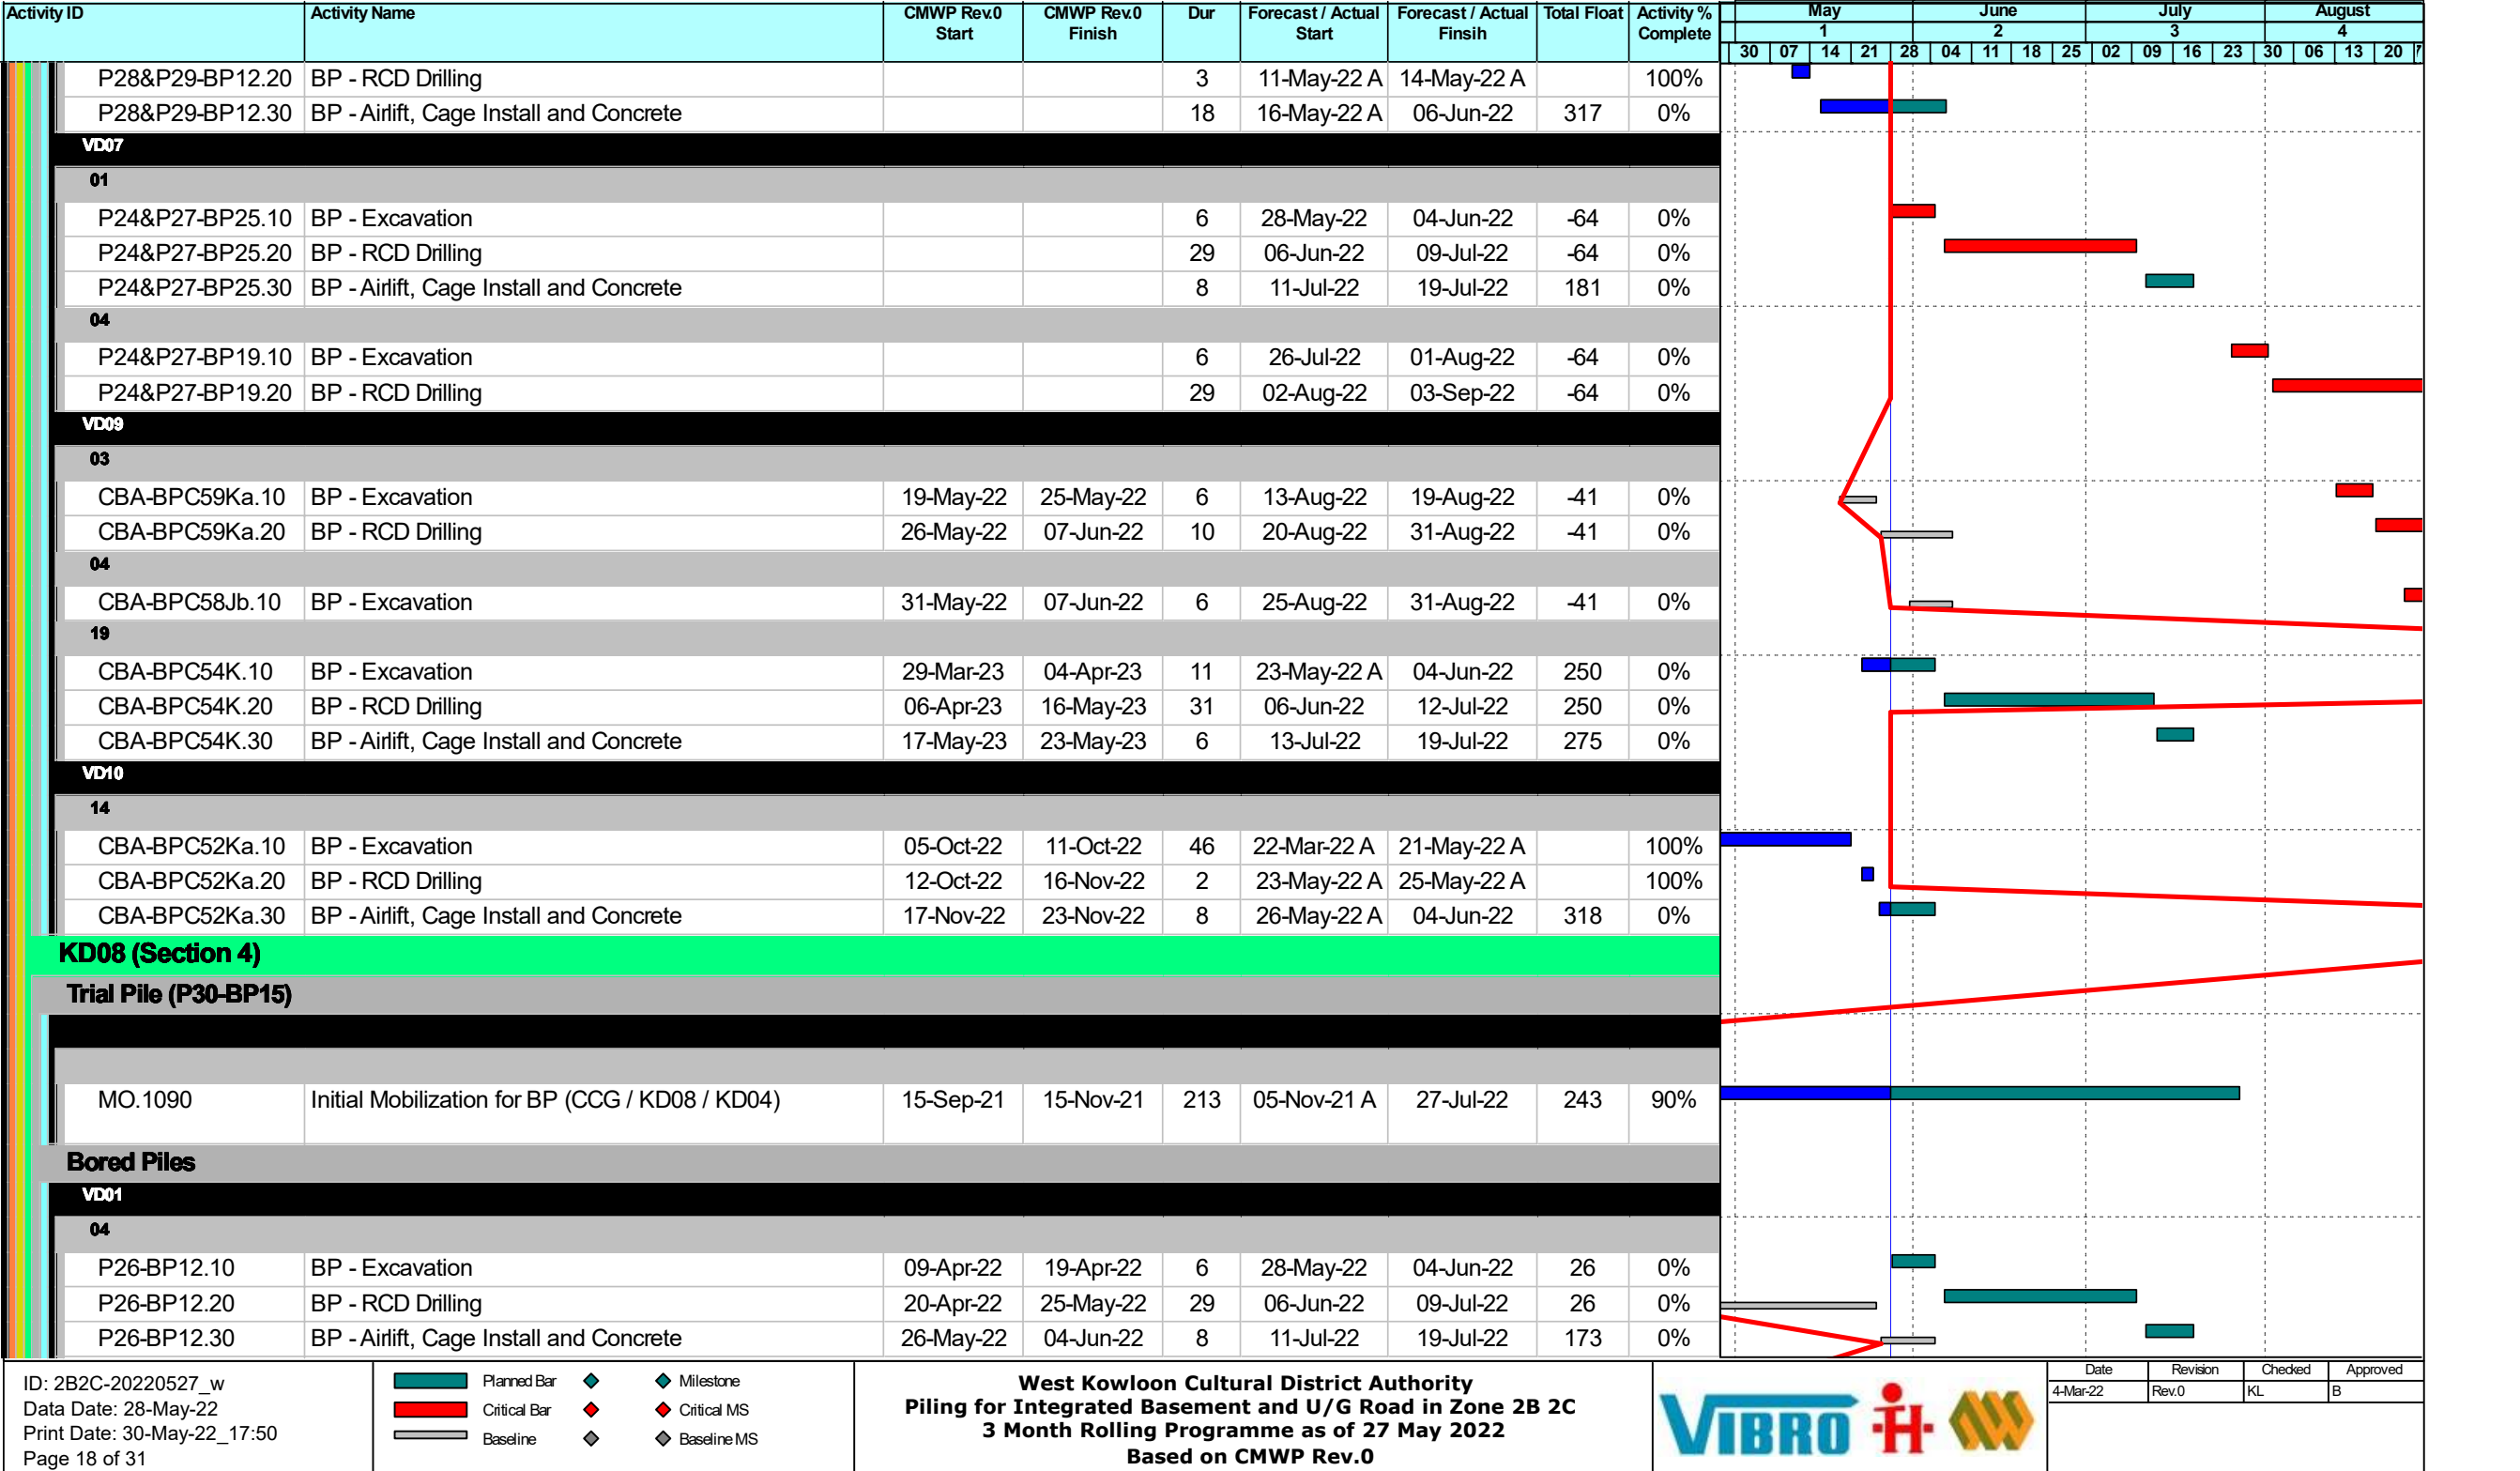

Activity ID	Activity Name	CMWP Rev.0 Start	CMWP Rev.0 Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	May				June				July				August			
									1				2				3				4			
									30	07	14	21	28	04	11	18	25	02	09	16	23	30	06	13
VD03																								
03																								
P30-BP44.10	BP - Excavation	29-Mar-22	04-Apr-22	6	25-Jun-22	02-Jul-22	-32	0%																
P30-BP44.20	BP - RCD Drilling	06-Apr-22	14-May-22	29	04-Jul-22	05-Aug-22	-32	0%																
P30-BP44.30	BP - Airlift, Cage Install and Concrete	16-May-22	24-May-22	8	06-Aug-22	15-Aug-22	134	0%																
04																								
P30-BP50.10	BP - Excavation	07-May-22	14-May-22	6	30-Jul-22	05-Aug-22	-32	0%																
P30-BP50.20	BP - RCD Drilling	16-May-22	07-Jun-22	19	06-Aug-22	27-Aug-22	-32	0%																
05																								
P30-BP55.10	BP - Excavation	31-May-22	07-Jun-22	6	22-Aug-22	27-Aug-22	-32	0%																
10																								
P30-BP45.10	BP - Excavation	28-Nov-22	03-Dec-22	10	14-May-22 A	26-May-22 A		100%																
P30-BP45.20	BP - RCD Drilling	05-Dec-22	10-Jan-23	30	27-May-22 A	02-Jul-22	161	0%																
P30-BP45.30	BP - Airlift, Cage Install and Concrete	11-Jan-23	19-Jan-23	8	04-Jul-22	12-Jul-22	171	0%																
VD04																								
01																								
P30-BP41.10	BP - Excavation	19-Jan-22	25-Jan-22	78	10-Feb-22 A	19-May-22 A		100%																
P30-BP41.20	BP - RCD Drilling	26-Jan-22	15-Feb-22	4	20-May-22 A	25-May-22 A		100%																
P30-BP41.30	BP - Airlift, Cage Install and Concrete	16-Feb-22	23-Feb-22	9	26-May-22 A	06-Jun-22	202	0%																
02																								
P30-BP47.10	BP - Excavation	09-Feb-22	15-Feb-22	6	28-May-22	04-Jun-22	11	0%																
P30-BP47.20	BP - RCD Drilling	16-Feb-22	04-Mar-22	15	06-Jun-22	22-Jun-22	11	0%																
P30-BP47.30	BP - Airlift, Cage Install and Concrete	05-Mar-22	12-Mar-22	7	23-Jun-22	30-Jun-22	188	0%																
03																								
P30-BP58.30	BP - Airlift, Cage Install and Concrete	28-Mar-22	06-Apr-22	8	28-Apr-22 A	10-May-22 A		100%																
06																								
P30-BP62.10	BP - Excavation	29-Apr-22	06-May-22	6	05-Jul-22	11-Jul-22	11	0%																
P30-BP62.20	BP - RCD Drilling	07-May-22	25-May-22	15	12-Jul-22	28-Jul-22	11	0%																
P30-BP62.30	BP - Airlift, Cage Install and Concrete	26-May-22	02-Jun-22	7	29-Jul-22	05-Aug-22	137	0%																
07																								
P30-BP42.10	BP - Excavation	19-May-22	25-May-22	6	22-Jul-22	28-Jul-22	11	0%																
P30-BP42.20	BP - RCD Drilling	26-May-22	13-Jun-22	15	29-Jul-22	15-Aug-22	11	0%																
P30-BP42.30	BP - Airlift, Cage Install and Concrete	14-Jun-22	21-Jun-22	7	16-Aug-22	23-Aug-22	129	0%																
08																								
P30-BP46.10	BP - Excavation	07-Jun-22	13-Jun-22	6	09-Aug-22	15-Aug-22	11	0%																
P30-BP46.20	BP - RCD Drilling	14-Jun-22	30-Jun-22	15	16-Aug-22	01-Sep-22	11	0%																
09																								
ID: 2B2C-20220527_w Data Date: 28-May-22 Print Date: 30-May-22_17:50 Page 19 of 31		<div><div></div><div></div><div></div></div> <div><div>Planned Bar</div><div>Critical Bar</div><div>Baseline</div></div> <div><div></div><div></div><div></div></div> <div><div>Milestone</div><div>Critical MS</div><div>Baseline MS</div></div>		West Kowloon Cultural District Authority Piling for Integrated Basement and U/G Road in Zone 2B 2C 3 Month Rolling Programme as of 27 May 2022 Based on CMWP Rev.0				<div><div>VIBRO</div><div></div><div></div></div>				<div><div>Date</div><div>4-Mar-22</div><div>Revision</div><div>Rev.0</div><div>Checked</div><div>KL</div><div>Approved</div><div>B</div></div>												

Activity ID	Activity Name	CMWP Rev.0 Start	CMWP Rev.0 Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	May							June				July				August			
									1							2				3				4			
									30	07	14	21	28	04	11	18	25	02	09	16	23	30	06	13	20	27	
<div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <																											

Activity ID		Activity Name	CMWP Rev.0 Start	CMWP Rev.0 Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	May 1							June 2				July 3				August 4			
										30	07	14	21	28	04	11	18	25	02	09	16	23	30	06	13	20	27	
<div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div>	P30-BP29.20	BP - RCD Drilling	10-Oct-22	26-Oct-22	15	12-Jul-22	28-Jul-22	138	0%																			
	P30-BP29.30	BP - Airlift, Cage Install and Concrete	27-Oct-22	03-Nov-22	7	29-Jul-22	05-Aug-22	150	0%																			
	21																											
	P30-BP37.10	BP - Excavation	20-Oct-22	26-Oct-22	6	22-Jul-22	28-Jul-22	138	0%																			
	P30-BP37.20	BP - RCD Drilling	27-Oct-22	17-Nov-22	19	29-Jul-22	19-Aug-22	138	0%																			
	P30-BP37.30	BP - Airlift, Cage Install and Concrete	18-Nov-22	26-Nov-22	8	20-Aug-22	29-Aug-22	138	0%																			
	TD01																											
	03																											
	P30-BP03.20	BP - RCD Drilling	17-Mar-22	02-Apr-22	3	28-Apr-22 A	03-May-22 A		100%																			
	P30-BP03.30	BP - Airlift, Cage Install and Concrete	04-Apr-22	12-Apr-22	8	04-May-22 A	14-May-22 A		100%																			
	06																											
	P30-BP11.10	BP - Excavation	07-May-22	14-May-22	6	28-May-22	04-Jun-22	24	0%																			
	P30-BP11.20	BP - RCD Drilling	16-May-22	07-Jun-22	19	06-Jun-22	27-Jun-22	24	0%																			
	P30-BP11.30	BP - Airlift, Cage Install and Concrete	08-Jun-22	16-Jun-22	8	28-Jun-22	07-Jul-22	35	0%																			
	08																											
	P30-BP02.10	BP - Excavation	23-Jun-22	29-Jun-22	55	16-May-22 A	20-Jul-22	33	0%																			
	P30-BP02.20	BP - RCD Drilling	30-Jun-22	18-Jul-22	15	21-Jul-22	06-Aug-22	33	0%																			
	P30-BP02.30	BP - Airlift, Cage Install and Concrete	19-Jul-22	26-Jul-22	7	08-Aug-22	15-Aug-22	142	0%																			
	09																											
	P30-BP18.10	BP - Excavation	12-Jul-22	18-Jul-22	6	01-Aug-22	06-Aug-22	33	0%																			
	P30-BP18.20	BP - RCD Drilling	19-Jul-22	09-Aug-22	19	08-Aug-22	29-Aug-22	33	0%																			
11																												
P30-BP14.10	BP - Excavation	20-Aug-22	26-Aug-22	9	25-Apr-22 A	06-May-22 A		100%																				
P30-BP14.20	BP - RCD Drilling	27-Aug-22	14-Sep-22	8	07-May-22 A	18-May-22 A		100%																				
P30-BP14.30	BP - Airlift, Cage Install and Concrete	15-Sep-22	22-Sep-22	3	19-May-22 A	23-May-22 A		100%																				
12																												
P30-BP09.10	BP - Excavation	07-Sep-22	14-Sep-22	6	23-Aug-22	29-Aug-22	33	0%																				
14																												
P30-BP04.10	BP - Excavation	15-Oct-22	21-Oct-22	111	25-May-22 A	06-Oct-22	33	0%																				
18																												
P30-BP17.10	BP - Excavation	06-Jan-23	12-Jan-23	37	20-Apr-22 A	04-Jun-22	183	0%																				
P30-BP17.20	BP - RCD Drilling	13-Jan-23	07-Feb-23	19	06-Jun-22	27-Jun-22	183	0%																				
P30-BP17.30	BP - Airlift, Cage Install and Concrete	08-Feb-23	16-Feb-23	8	28-Jun-22	07-Jul-22	183	0%																				
TD09																												
02																												
CBA-BPC52Va.10	BP - Excavation	23-Apr-22	29-Apr-22	6	10-Jun-22	16-Jun-22	-38	0%																				
CBA-BPC52Va.20	BP - RCD Drilling	30-Apr-22	13-May-22	10	17-Jun-22	28-Jun-22	-38	0%																				

ID: 2B2C-20220527\_w  
Data Date: 28-May-22  
Print Date: 30-May-22\_17:50  
Page 21 of 31

Planned Bar

Critical Bar

Baseline

Milestone

Critical MS

Baseline MS

West Kowloon Cultural District Authority




Piling for Integrated Basement and U/G Road in Zone 2B 2C


3 Month Rolling Programme as of 27 May 2022

Based on CMWP Rev.0

VIBRO

Date	Revision	Checked	Approved
4-Mar-22	Rev.0	KL	B




Activity ID		Activity Name	CMWP Rev.0 Start	CMWP Rev.0 Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	May 1				June 2				July 3				August 4													
										30	07	14	21	28	04	11	18	25	02	09	16	23	30	06	13	20	27								
	CBA-BPC52Va.30	BP - Airlift, Cage Install and Concrete	14-May-22	19-May-22	5	29-Jun-22	05-Jul-22	110	0%																										
	04																																		
	P26-BP15.10	BP - Excavation	19-May-22	25-May-22	6	05-Jul-22	11-Jul-22	-38	0%																										
	P26-BP15.20	BP - RCD Drilling	26-May-22	02-Jul-22	31	12-Jul-22	16-Aug-22	-38	0%																										
	P26-BP15.30	BP - Airlift, Cage Install and Concrete	04-Jul-22	09-Jul-22	6	17-Aug-22	23-Aug-22	79	0%																										
	05																																		
	P26-BP16.10	BP - Excavation	24-Jun-22	02-Jul-22	7	09-Aug-22	16-Aug-22	-38	0%																										
	P26-BP16.20	BP - RCD Drilling	04-Jul-22	19-Jul-22	14	17-Aug-22	01-Sep-22	-38	0%																										
	06																																		
	CBA-BPC54U.10	BP - Excavation	12-Jul-22	19-Jul-22	7	25-Aug-22	01-Sep-22	-38	0%																										
Socketed Steel H- Piles																																			
Socketed Steel H- Pile Construction																																			
	SHP-BW-52Y1a-P:	Socketed Steel H-Piling	21-Apr-22	30-Apr-22	9	28-May-22	08-Jun-22	42	0%																										
	SHP-BW-53Y1-P2	Socketed Steel H-Piling	30-Apr-22	12-May-22	9	09-Jun-22	18-Jun-22	42	0%																										
	SHP-BW-54Y1b-P:	Socketed Steel H-Piling	12-May-22	21-May-22	9	20-Jun-22	29-Jun-22	42	0%																										
	SHP-C52Wa-P1	Socketed Steel H-Piling	17-May-22	26-May-22	9	24-Jun-22	05-Jul-22	42	0%																										
	SHP-C52Wa-P2	Socketed Steel H-Piling	21-May-22	31-May-22	9	07-May-22 A	19-May-22 A		100%																										
	SHP-C52Wa-P3	Socketed Steel H-Piling	26-May-22	06-Jun-22	9	19-Apr-22 A	29-Apr-22 A		100%																										
	SHP-C52Wa-P5	Socketed Steel H-Piling	06-Jun-22	15-Jun-22	9	06-Jul-22	15-Jul-22	42	0%																										
	SHP-C52Wa-P6	Socketed Steel H-Piling	10-Jun-22	20-Jun-22	9	11-Jul-22	20-Jul-22	42	0%																										
	SHP-C52Xb-P1	Socketed Steel H-Piling	15-Jun-22	24-Jun-22	9	15-Jul-22	25-Jul-22	42	0%																										
	SHP-C52Xb-P2	Socketed Steel H-Piling	20-Jun-22	29-Jun-22	9	20-Jul-22	29-Jul-22	42	0%																										
	SHP-C52Xb-P3	Socketed Steel H-Piling	24-Jun-22	05-Jul-22	10	25-Apr-22 A	07-May-22 A		100%																										
	SHP-C52Xb-P5	Socketed Steel H-Piling	05-Jul-22	14-Jul-22	7	19-May-22 A	27-May-22 A		100%																										
	SHP-C52Xb-P6	Socketed Steel H-Piling	09-Jul-22	19-Jul-22	9	30-Jul-22	09-Aug-22	42	0%																										
	SHP-C52Xc-P1	Socketed Steel H-Piling	14-Jul-22	23-Jul-22	9	04-Aug-22	13-Aug-22	42	0%																										
	SHP-C52Xc-P2	Socketed Steel H-Piling	19-Jul-22	28-Jul-22	9	09-Aug-22	18-Aug-22	42	0%																										
	SHP-C52Xc-P3	Socketed Steel H-Piling	23-Jul-22	02-Aug-22	6	16-May-22 A	23-May-22 A		100%																										
	SHP-C52Xc-P4	Socketed Steel H-Piling	28-Jul-22	06-Aug-22	10	13-Apr-22 A	28-Apr-22 A		100%																										
	SHP-C52Xc-P5	Socketed Steel H-Piling	02-Aug-22	11-Aug-22	9	13-Aug-22	23-Aug-22	89	0%																										
	SHP-C52Xc-P6	Socketed Steel H-Piling	06-Aug-22	16-Aug-22	9	18-Aug-22	27-Aug-22	89	0%																										
	SHP-C53W-P1	Socketed Steel H-Piling	11-Aug-22	20-Aug-22	9	23-Aug-22	01-Sep-22	89	0%																										
	SHP-C53W-P2	Socketed Steel H-Piling	16-Aug-22	25-Aug-22	9	27-Aug-22	06-Sep-22	89	0%																										
	SHP-C53W-P3	Socketed Steel H-Piling	20-Aug-22	30-Aug-22	9	06-May-22 A	18-May-22 A		100%																										
	SHP-C53X-P3	Socketed Steel H-Piling	19-Sep-22	28-Sep-22	9	27-Apr-22 A	10-May-22 A		100%																										
ID: 2B2C-20220527_w		Planned Bar		Milestone		West Kowloon Cultural District Authority Piling for Integrated Basement and U/G Road in Zone 2B 2C 3 Month Rolling Programme as of 27 May 2022 Based on CMWP Rev.0				  				Date	Revision	Checked	Approved																		
Data Date: 28-May-22		Critical Bar		Critical MS										4-Mar-22	Rev.0	KL	B																		
Print Date: 30-May-22_17:50		Baseline		Baseline MS																															
Page 22 of 31																																			

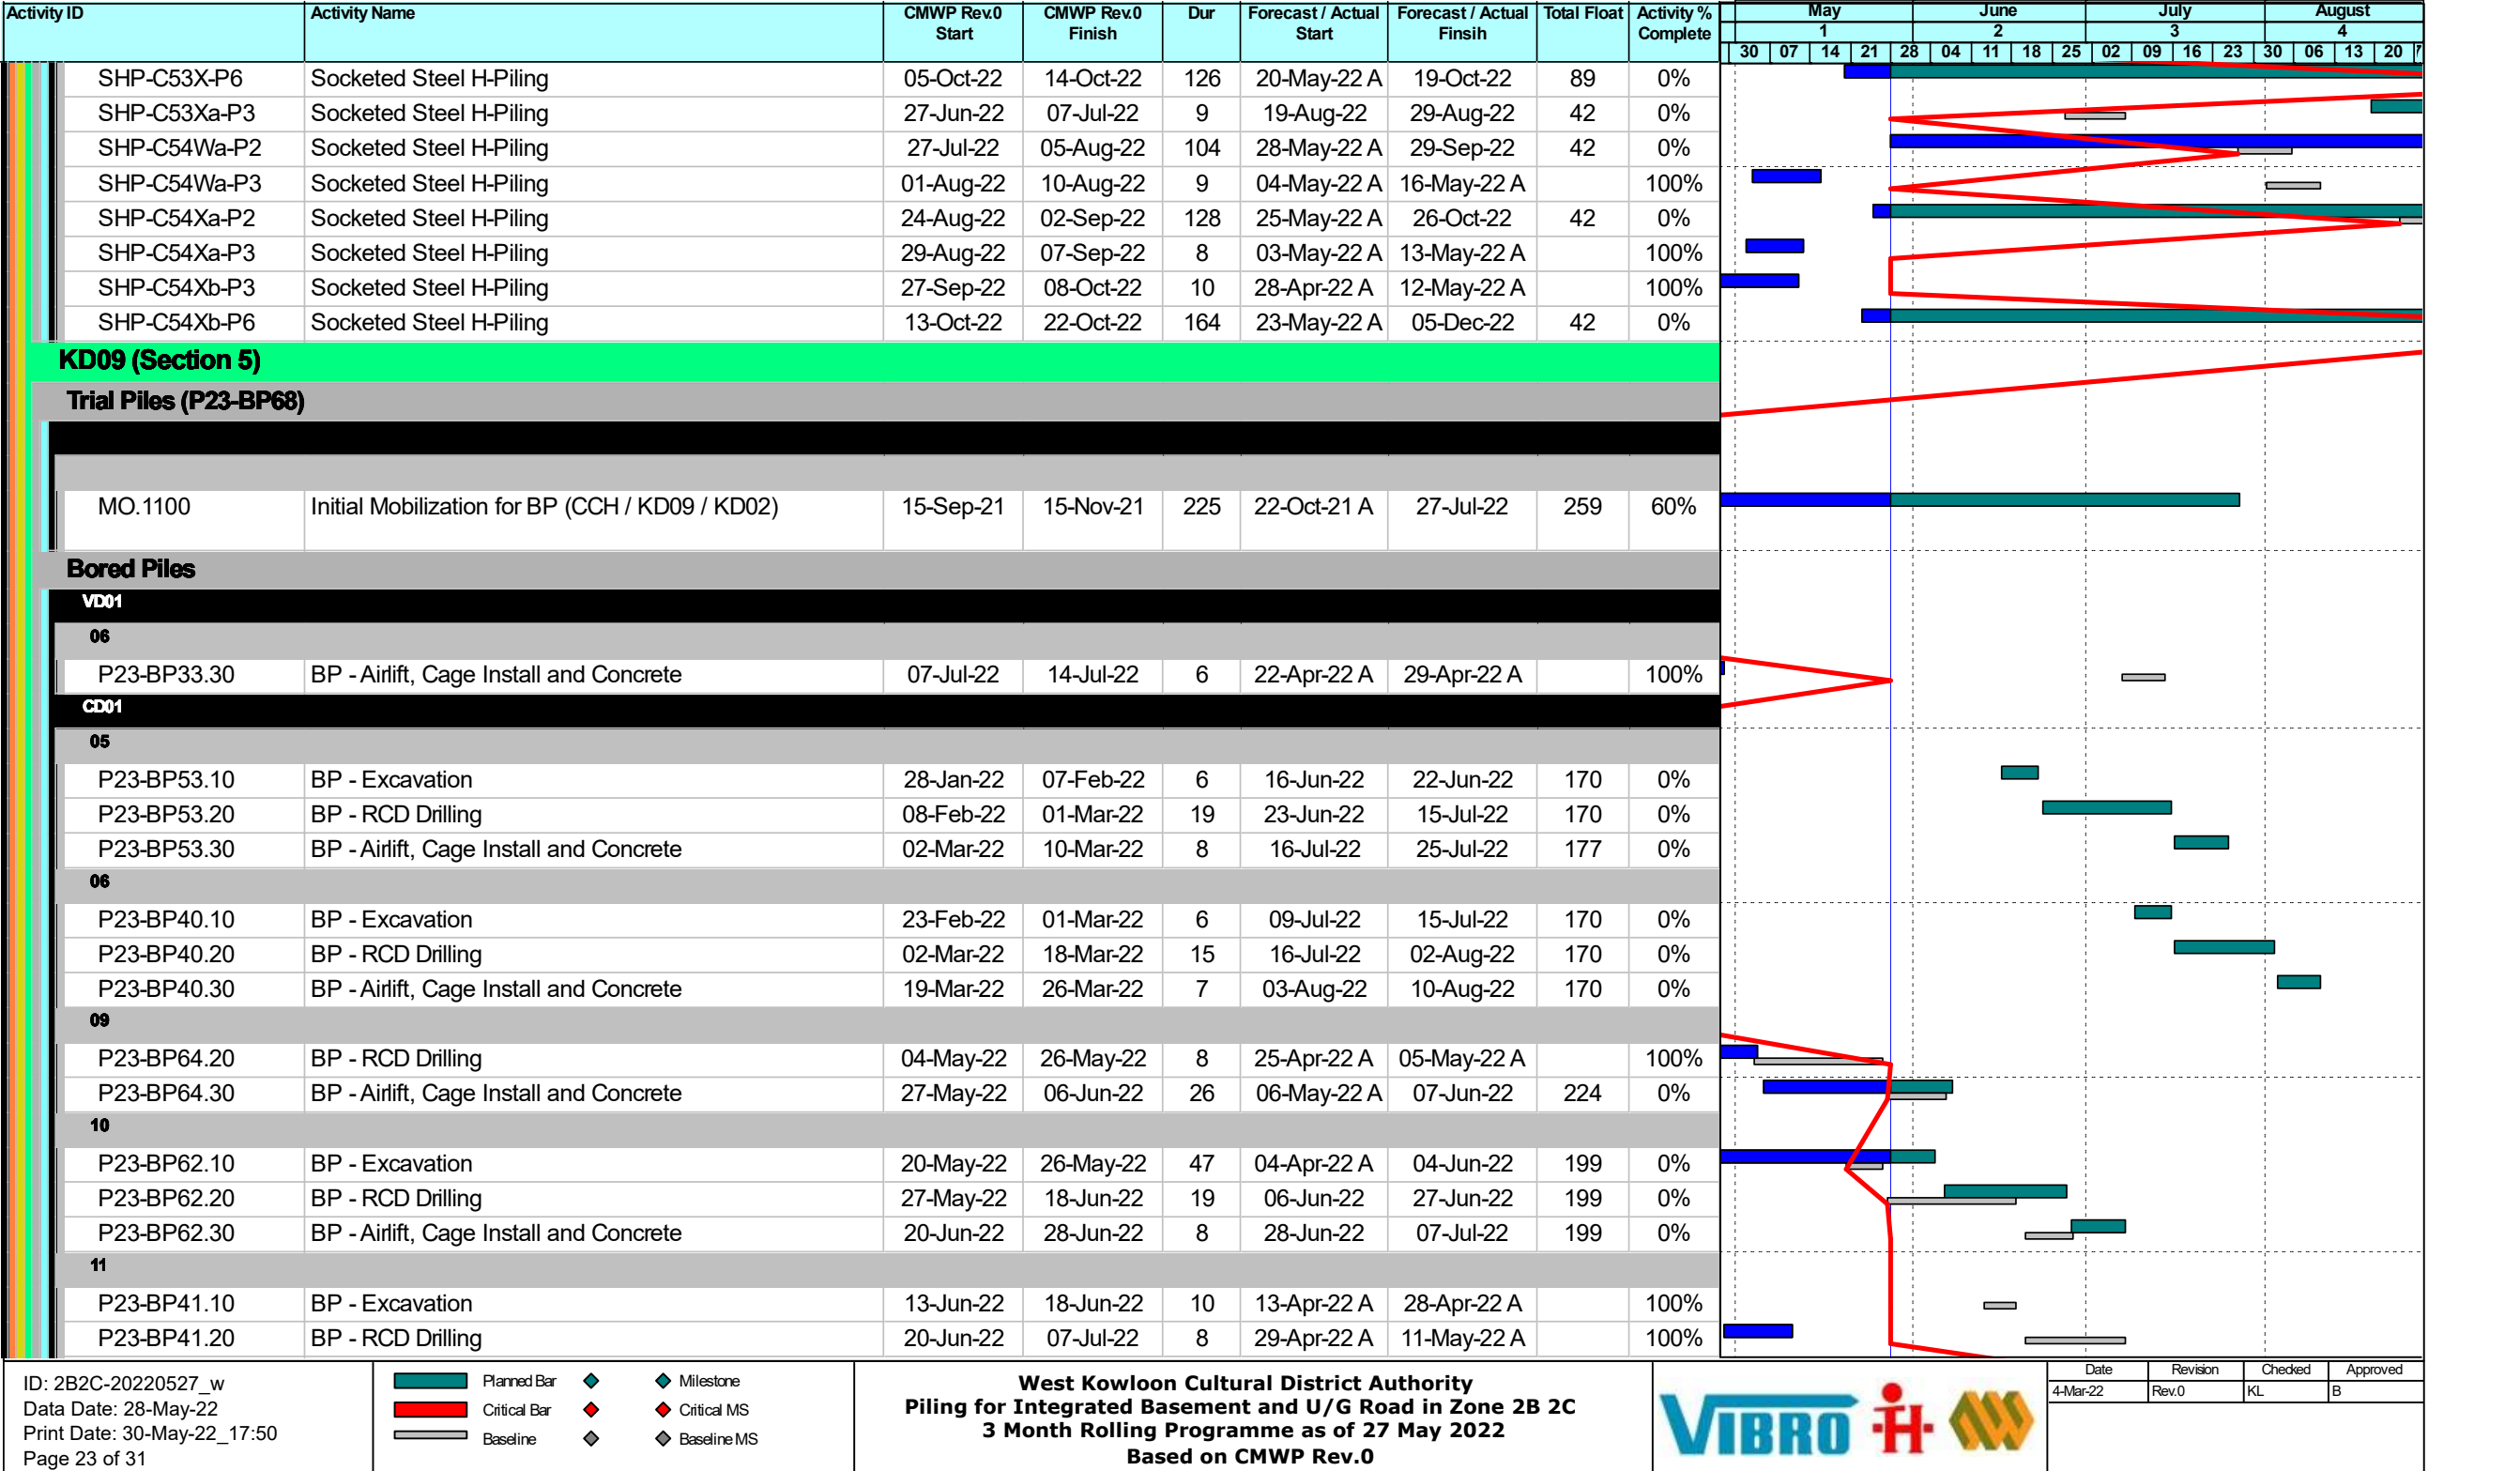

Activity ID		Activity Name	CMWP Rev.0 Start	CMWP Rev.0 Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	May				June				July				August			
										1				2				3				4			
										30	07	14	21	28	04	11	18	25	02	09	16	23	30	06	13
<div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div>																									



Activity ID	Activity Name	CMWP Rev.0 Start	CMWP Rev.0 Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	May				June				July				August																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																					
									1				2				3				4																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																					
									30	07	14	21	28	04	11	18	25	02	09	16	23	30	06	13	20	27																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																
05																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																										</

Activity ID		Activity Name	CMWP Rev.0 Start	CMWP Rev.0 Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	May 1				June 2				July 3				August 4						
										30	07	14	21	28	04	11	18	25	02	09	16	23	30	06	13	20	27	
04																												
	P23-BP107.10	BP - Excavation	04-Jan-22	10-Jan-22	6	28-May-22	04-Jun-22	84	0%																			
	P23-BP107.20	BP - RCD Drilling	11-Jan-22	04-Feb-22	19	06-Jun-22	27-Jun-22	84	0%																			
	P23-BP107.30	BP - Airlift, Cage Install and Concrete	05-Feb-22	14-Feb-22	8	28-Jun-22	07-Jul-22	159	0%																			
05																												
	P23-BP75.10	BP - Excavation	26-Jan-22	04-Feb-22	6	21-Jun-22	27-Jun-22	84	0%																			
	P23-BP75.20	BP - RCD Drilling	05-Feb-22	26-Feb-22	19	28-Jun-22	20-Jul-22	84	0%																			
	P23-BP75.30	BP - Airlift, Cage Install and Concrete	28-Feb-22	08-Mar-22	8	21-Jul-22	29-Jul-22	148	0%																			
06																												
	P23-BP73.10	BP - Excavation	21-Feb-22	26-Feb-22	6	14-Jul-22	20-Jul-22	84	0%																			
	P23-BP73.20	BP - RCD Drilling	28-Feb-22	21-Mar-22	19	21-Jul-22	11-Aug-22	84	0%																			
	P23-BP73.30	BP - Airlift, Cage Install and Concrete	22-Mar-22	30-Mar-22	8	12-Aug-22	20-Aug-22	137	0%																			
07																												
	P23-BP97.10	BP - Excavation	15-Mar-22	21-Mar-22	6	05-Aug-22	11-Aug-22	84	0%																			
	P23-BP97.20	BP - RCD Drilling	22-Mar-22	28-Apr-22	29	12-Aug-22	15-Sep-22	84	0%																			
11																												
	P23-BP108.10	BP - Excavation	26-Jan-22	04-Feb-22	6	28-May-22	04-Jun-22	64	0%																			
	P23-BP108.20	BP - RCD Drilling	05-Feb-22	10-Mar-22	29	06-Jun-22	09-Jul-22	64	0%																			
	P23-BP108.30	BP - Airlift, Cage Install and Concrete	11-Mar-22	19-Mar-22	8	11-Jul-22	19-Jul-22	173	0%																			
12																												
	P23-BP74.10	BP - Excavation	04-Mar-22	10-Mar-22	6	04-Jul-22	09-Jul-22	64	0%																			
	P23-BP74.20	BP - RCD Drilling	11-Mar-22	01-Apr-22	19	11-Jul-22	01-Aug-22	64	0%																			
	P23-BP74.30	BP - Airlift, Cage Install and Concrete	02-Apr-22	12-Apr-22	8	02-Aug-22	10-Aug-22	162	0%																			
13																												
	P23-BP84.10	BP - Excavation	26-Mar-22	01-Apr-22	6	26-Jul-22	01-Aug-22	64	0%																			
	P23-BP84.20	BP - RCD Drilling	02-Apr-22	12-May-22	29	02-Aug-22	03-Sep-22	64	0%																			
14																												
	P23-BP106.10	BP - Excavation	05-May-22	12-May-22	34	23-Apr-22 A	04-Jun-22	199	0%																			
	P23-BP106.20	BP - RCD Drilling	13-May-22	04-Jun-22	19	06-Jun-22	27-Jun-22	199	0%																			
	P23-BP106.30	BP - Airlift, Cage Install and Concrete	06-Jun-22	14-Jun-22	8	28-Jun-22	07-Jul-22	199	0%																			
17																												
	P23-BP116.10	BP - Excavation	06-Aug-22	12-Aug-22	18	14-May-22 A	04-Jun-22	180	0%																			
	P23-BP116.20	BP - RCD Drilling	13-Aug-22	03-Sep-22	19	06-Jun-22	27-Jun-22	180	0%																			
	P23-BP116.30	BP - Airlift, Cage Install and Concrete	05-Sep-22	14-Sep-22	8	28-Jun-22	07-Jul-22	191	0%																			
TD03																												
02																												
	P23-BP101.10	BP - Excavation	20-Jan-22	26-Jan-22	6	28-May-22	04-Jun-22	8	0%																			
ID: 2B2C-20220527_w		Planned Bar		Milestone		West Kowloon Cultural District Authority Piling for Integrated Basement and U/G Road in Zone 2B 2C 3 Month Rolling Programme as of 27 May 2022 Based on CMWP Rev.0				VIBRO   				Date	Revision	Checked	Approved											
Data Date: 28-May-22		Critical Bar		Critical MS													4-Mar-22	Rev.0	KL	B								
Print Date: 30-May-22_17:50		Baseline		Baseline MS																								
Page 27 of 31																												

[illegible]

Activity ID	Activity Name	CMWP Rev.0 Start	CMWP Rev.0 Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	May 1							June 2				July 3				August 4					
									1							2				3				4					
									30	07	14	21	28	04	11	18	25	02	09	16	23	30	06	13	20	27			
P23-BP102.20	BP - RCD Drilling	29-Aug-22	20-Sep-22	19	24-Aug-22	15-Sep-22	94	0%																					
TD02																													
03																													
P23-BP71.10	BP - Excavation	04-Mar-22	10-Mar-22	6	28-May-22	04-Jun-22	19	0%																					
P23-BP71.20	BP - RCD Drilling	11-Mar-22	14-Apr-22	29	06-Jun-22	09-Jul-22	19	0%																					
P23-BP71.30	BP - Airlift, Cage Install and Concrete	19-Apr-22	27-Apr-22	8	11-Jul-22	19-Jul-22	140	0%																					
04																													
P23-BP83.10	BP - Excavation	08-Apr-22	14-Apr-22	6	04-Jul-22	09-Jul-22	19	0%																					
P23-BP83.20	BP - RCD Drilling	19-Apr-22	24-May-22	29	11-Jul-22	12-Aug-22	19	0%																					
P23-BP83.30	BP - Airlift, Cage Install and Concrete	25-May-22	02-Jun-22	8	13-Aug-22	22-Aug-22	119	0%																					
05																													
P23-BP93.10	BP - Excavation	18-May-22	24-May-22	6	06-Aug-22	12-Aug-22	19	0%																					
P23-BP93.20	BP - RCD Drilling	25-May-22	28-Jun-22	29	13-Aug-22	16-Sep-22	19	0%																					
11																													
P23-BP113.10	BP - Excavation	04-Mar-22	10-Mar-22	22	02-Apr-22 A	04-May-22 A		100%																					
P23-BP113.20	BP - RCD Drilling	11-Mar-22	01-Apr-22	10	05-May-22 A	18-May-22 A		100%																					
P23-BP113.30	BP - Airlift, Cage Install and Concrete	02-Apr-22	12-Apr-22	6	19-May-22 A	26-May-22 A		100%																					
12																													
P23-BP111.10	BP - Excavation	26-Mar-22	01-Apr-22	6	28-May-22	04-Jun-22	45	0%																					
P23-BP111.20	BP - RCD Drilling	02-Apr-22	28-Apr-22	19	06-Jun-22	27-Jun-22	45	0%																					
P23-BP111.30	BP - Airlift, Cage Install and Concrete	29-Apr-22	10-May-22	8	28-Jun-22	07-Jul-22	159	0%																					
13																													
P23-BP92.10	BP - Excavation	22-Apr-22	28-Apr-22	6	21-Jun-22	27-Jun-22	45	0%																					
P23-BP92.20	BP - RCD Drilling	29-Apr-22	04-Jun-22	29	28-Jun-22	01-Aug-22	45	0%																					
P23-BP92.30	BP - Airlift, Cage Install and Concrete	06-Jun-22	14-Jun-22	8	02-Aug-22	10-Aug-22	138	0%																					
14																													
P23-BP58.10	BP - Excavation	28-May-22	04-Jun-22	6	26-Jul-22	01-Aug-22	45	0%																					
P23-BP58.20	BP - RCD Drilling	06-Jun-22	09-Jul-22	29	02-Aug-22	03-Sep-22	45	0%																					
18																													
P23-BP72.10	BP - Excavation	05-Oct-22	11-Oct-22	21	11-May-22 A	04-Jun-22	170	0%																					
P23-BP72.20	BP - RCD Drilling	12-Oct-22	14-Nov-22	29	06-Jun-22	09-Jul-22	170	0%																					
P23-BP72.30	BP - Airlift, Cage Install and Concrete	15-Nov-22	23-Nov-22	8	11-Jul-22	19-Jul-22	181	0%																					
20																													
P23-BP70.30	BP - Airlift, Cage Install and Concrete	13-Jan-23	21-Jan-23	7	28-Apr-22 A	07-May-22 A		100%																					
Optional Item no. 3																													
TD07																													
15																													

ID: 2B2C-20220527\_w  
Data Date: 28-May-22  
Print Date: 30-May-22\_17:50  
Page 29 of 31

Planned Bar

Critical Bar

Baseline

Milestone

Critical MS

Baseline MS

West Kowloon Cultural District Authority

Piling for Integrated Basement and U/G Road in Zone 2B 2C

3 Month Rolling Programme as of 27 May 2022

Based on CMWP Rev.0

VIBRO

Date

4-Mar-22

Revision


Rev.0

Checked

KL

Approved

B

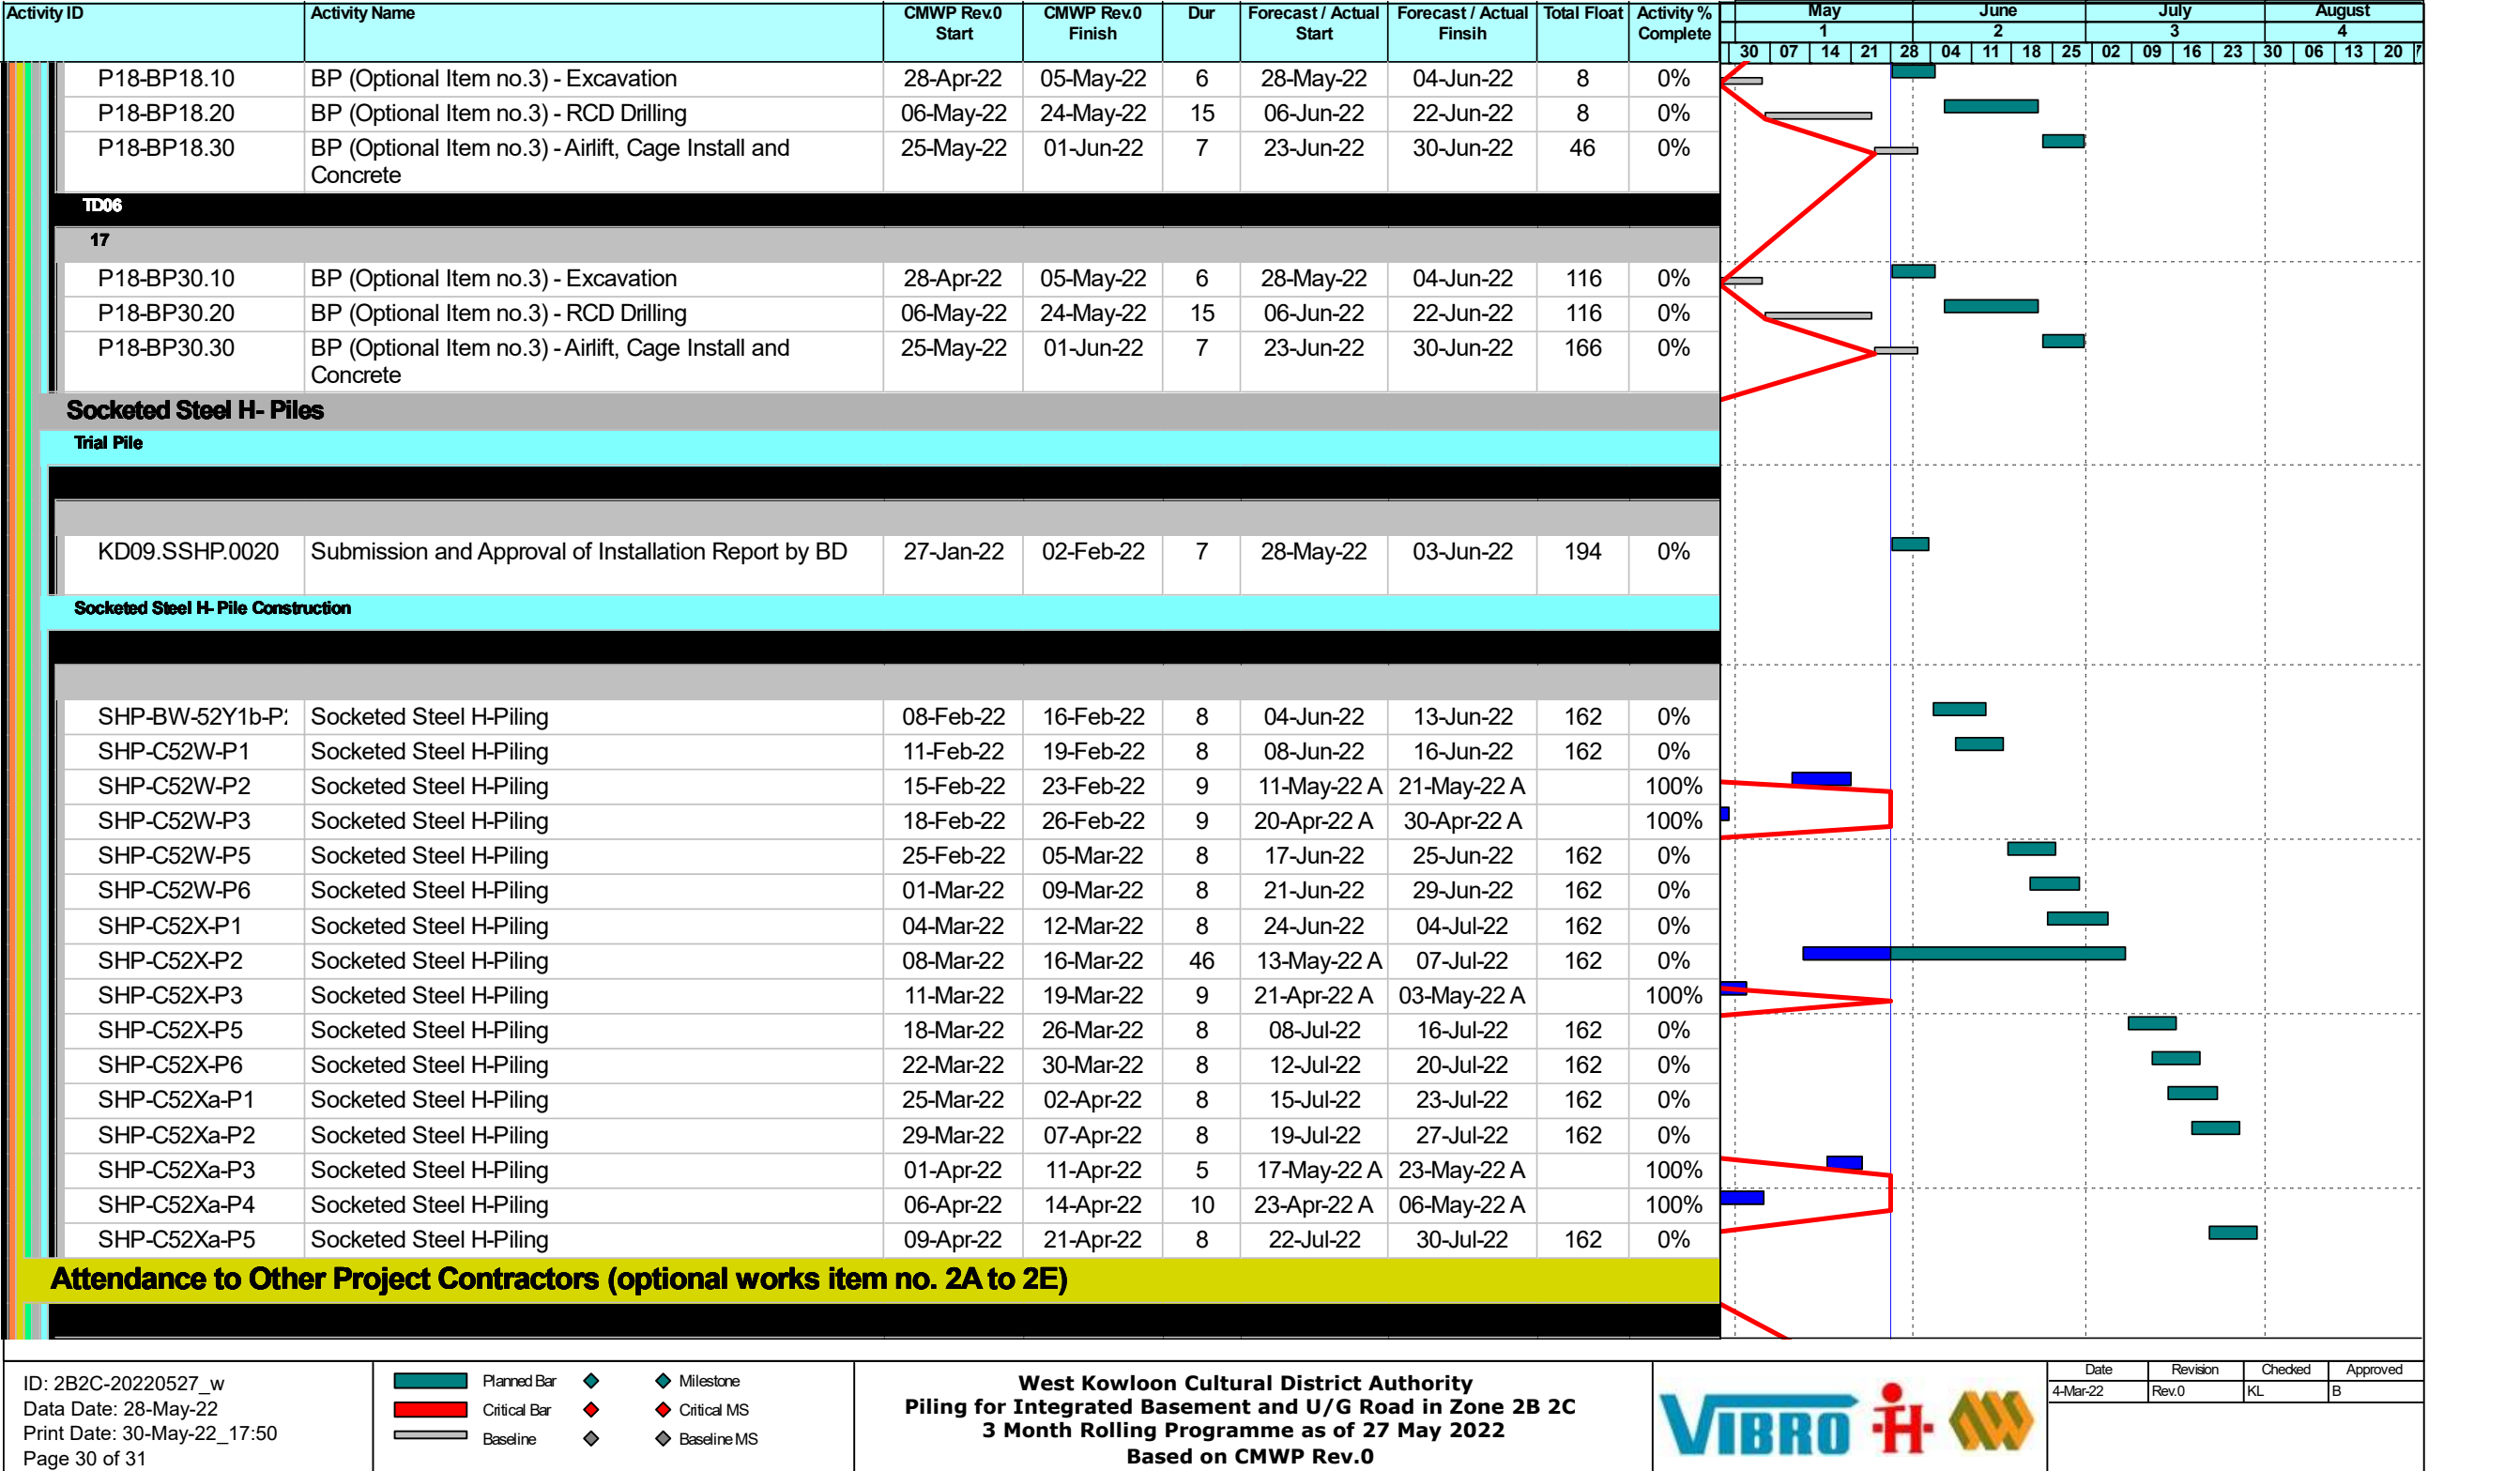

Activity ID	Activity Name	CMWP Rev.0 Start	CMWP Rev.0 Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	May				June				July				August					
									1				2				3				4					
									30	07	14	21	28	04	11	18	25	02	09	16	23	30	06	13	20	27
S1.AT.0020	Attendance at Section 1 Area (optional works item no. 2A) if item No. 3 is instructed (Duration TBC)	16-Aug-22	04-Sep-22	20	16-Aug-22	04-Sep-22	71	0%																		

ID: 2B2C-20220527\_w  
Data Date: 28-May-22  
Print Date: 30-May-22\_17:50  
Page 31 of 31

Planned BarCritical BarBaselineMilestoneCritical MSBaseline MS

West Kowloon Cultural District Authority

Piling for Integrated Basement and U/G Road in Zone 2B 2C

3 Month Rolling Programme as of 27 May 2022

Based on CMWP Rev.0

VIBRO

Date	Revision	Checked	Approved
4-Mar-22	Rev.0	KL	B
