

Zone 2A

Project Name: Foundation and ELS Works for Integrated Basement and Underground Road in Zone 2A of the West Kowloon Cultural District

3-Month Rolling Programme

Activity Description	Duration (Cal. Day)	Start Date	Finish Date	2022					2023										
				December					January				February				March		
				2	9	16	23	30	6	13	20	27	3	10	17	24	3	10	17
W134	W135	W136	W137	W138	W139	W140	W141	W142	W143	W144	W145	W146	W147	W148	W149	W150	W151		
Zone 2A G/F																			
Reinstatement Works at Location A and B																			
Reinstatement Works at Location A and B	46	31-Oct-22	15-Dec-22	█	█														
Zone 2A A&A Works																			
WEK B1/F																			
Sand Removal	91	17-Dec-22	17-Mar-23			█	█	█	█	█	█	█	█	█	█	█	█	█	

█ - Actual
█ - Remaining Works

Zone 2B & 2C

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	November			December				January				February				March
								17	19	26	18				19				20				21
								12	19	26	03	10	17	24	31	07	14	21	28	04	11	18	25

Piling for Integrated Basement and U/G Road in Zone 2B & 2C

Contract Dates								
Key Dates								
KD for Zone 2B								
KD05	KD05 (Section 1) - 03 Jan 2023			03-Jan-23	0	22-Jul-23*	-200	


Optional Works subjected to CA's Instruction								
CO1A	Last CAI date for Optional Works Item No.1A (within 560 Days after Commencement)			02-Feb-23	0	02-Feb-23	1	
CO1B	Last CAI date for Optional Works Item No.1B (within 560 Days after Commencement)			02-Feb-23	0	02-Feb-23	1	
CO2D	Last CAI date for Optional Works Item No.2D (330 Days to 580 Days after Commencement)			22-Feb-23	0	22-Feb-23	71	
CO2E10	Last CAI date for Optional Works Item No.2E (330 Days to 580 Days after Commencement) (NA; item No. 3 not exercised)			22-Feb-23	0	22-Feb-23	301	

Construction Stage

Pile Construction									
KD03 (Stage 3-1)									
VD09									
CBA-BPC54Ja.1i	BP - Excavation			12-Jan-23	18-Jan-23	28	11-Jul-22 A	12-Aug-22 A	
CBA-BPC54Ja.2i	BP - RCD Drilling			19-Jan-23	27-Feb-23	1	13-Aug-22 A	15-Aug-22 A	
CBA-BPC54Ja.3i	BP -Airlift, Cage Install and Concrete			28-Feb-23	06-Mar-23	7	16-Aug-22 A	24-Aug-22 A	

KD05 (Section 1)

Bored Piles									
CD05									
P17-BP05.30	BP -Airlift, Cage Install and Concrete			31-Jan-22	10-Feb-22	7	07-Nov-22 A	15-Nov-22 A	
10									
P22&P19-BP16.:	BP - RCD Drilling			20-Jun-22	12-Jul-22	70	06-Sep-22 A	30-Nov-22 A	
P22&P19-BP16.:	BP -Airlift, Cage Install and Concrete			13-Jul-22	21-Jul-22	6	01-Dec-22 A	08-Dec-22 A	
CD04									
05									
P17-BP16.20	BP - RCD Drilling			01-Mar-22	17-Mar-22	8	09-Nov-22 A	18-Nov-22 A	
P17-BP16.30	BP -Airlift, Cage Install and Concrete			18-Mar-22	25-Mar-22	10	19-Nov-22 A	01-Dec-22 A	
11									
P17-BP06.10	BP - Excavation			23-Jun-22	29-Jun-22	10	17-Nov-22 A	29-Nov-22 A	
P17-BP06.20	BP - RCD Drilling			30-Jun-22	18-Jul-22	7	30-Nov-22 A	08-Dec-22 A	
P17-BP06.30	BP -Airlift, Cage Install and Concrete			19-Jul-22	26-Jul-22	8	09-Dec-22 A	17-Dec-22	-66
19									
P17-BP11.10	BP IAR-N - Excavation			19-Aug-22	25-Aug-22	13	02-Dec-22 A	16-Dec-22	-87
TD07									
01									
P18-BP10.10	BP IAR-S - Excavation			19-Nov-21	25-Nov-21	25	04-Nov-22 A	03-Dec-22 A	
P18-BP10.20	BP IAR-S - RCD Drilling			26-Nov-21	13-Dec-21	20	05-Dec-22 A	29-Dec-22	-144
06									
P18-BP05.10	BP - Excavation			07-Mar-22	12-Mar-22	53	01-Dec-22 A	07-Feb-23	-144
17									

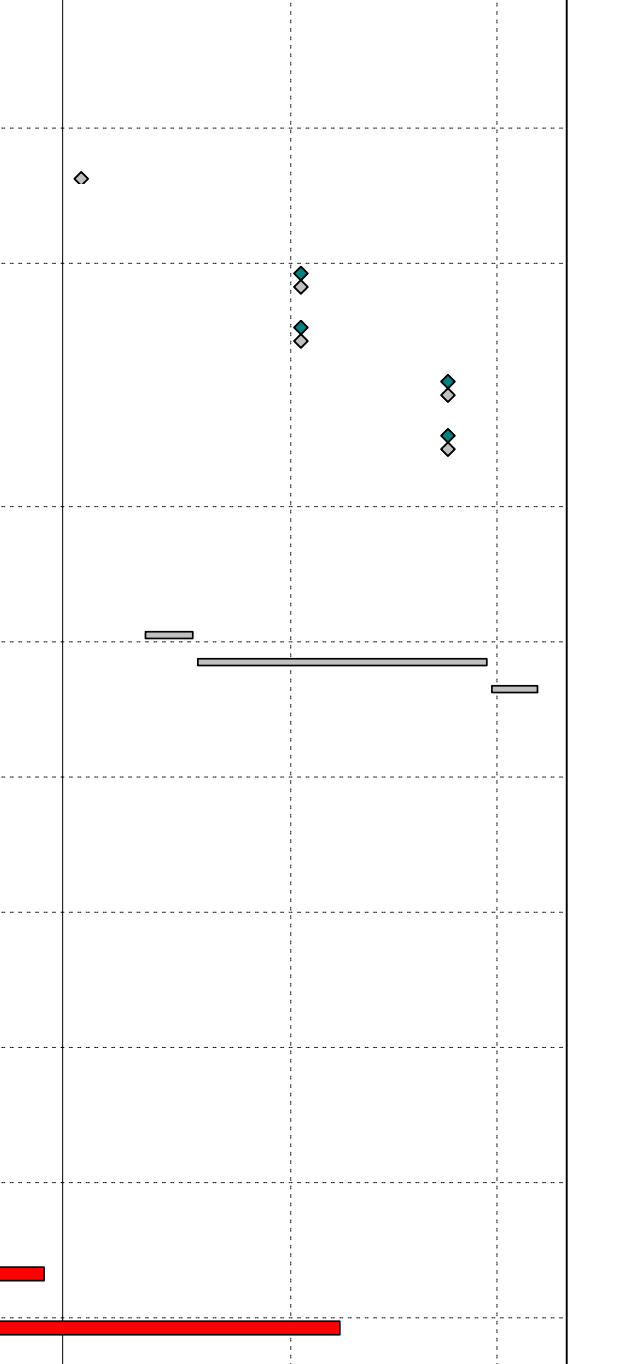

ID: 2B2C-20221210_w
 Data Date: 10-Dec-22
 Print Date: 14-Dec-22_12:32
 Page 1 of 13







■	Planned	◆	Planned MS
■	Critical	◆	Critical MS
■	Actual	◆	Actual MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 9 December 2022
 Based on CMWP Rev.0


	Date	Revision	Checked	Approved
	4-Mar-22	Rev.0	KL	B

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finish	Total Float	November			December				January				February				March	
								17			18				19				20				21	
								12	19	26	03	10	17	24	31	07	14	21	28	04	11	18	25	04
P18-BP08.20	BP - RCD Drilling	17-Jun-22	09-Jul-22	11	07-Nov-22 A	19-Nov-22 A																		
P18-BP08.30	BP - Airlift, Cage Install and Concrete	11-Jul-22	19-Jul-22	6	20-Nov-22 A	28-Nov-22 A																		
19																								
P18-BP11.10	BP IAR-S (Optional Item no.3) - Excavation	21-Jul-22	27-Jul-22	49	20-Sep-22 A	18-Nov-22 A																		
P18-BP11.20	BP IAR-S (Optional Item no.3) - RCD Drilling	28-Jul-22	13-Aug-22	8	19-Nov-22 A	29-Nov-22 A																		
P18-BP11.30	BP IAR-S (Optional Item no.3) - Airlift, Cage Install and Concrete	15-Aug-22	22-Aug-22	16	30-Nov-22 A	17-Dec-22	-66																	
KD06 (Section 2)																								
Bored Piles																								
VD01																								
P23-BP13.10	BP - Excavation	09-Jan-23	14-Jan-23	10	11-Apr-22 A	26-Apr-22 A																		
P23-BP13.20	BP - RCD Drilling	16-Jan-23	04-Feb-23	11	27-Apr-22 A	12-May-22 A																		
P23-BP13.30	BP - Airlift, Cage Install and Concrete	06-Feb-23	13-Feb-23	11	13-May-22 A	26-May-22 A																		
20																								
P23-BP24.10	BP - Excavation	19-Dec-22	24-Dec-22	24	19-Oct-22 A	16-Nov-22 A																		
P23-BP24.20	BP - RCD Drilling	28-Dec-22	19-Jan-23	39	17-Nov-22 A	04-Jan-23	42																	
P23-BP24.30	BP - Airlift, Cage Install and Concrete	20-Jan-23	01-Feb-23	8	05-Jan-23	13-Jan-23	42																	
VD02																								
18																								
P24&P27-BP15.	BP - Excavation	05-Nov-22	11-Nov-22	6	06-Mar-23	11-Mar-23	-60																	
P24&P27-BP15.:	BP - RCD Drilling	12-Nov-22	03-Dec-22	19	13-Mar-23	03-Apr-23	-60																	
P24&P27-BP15.:	BP - Airlift, Cage Install and Concrete	05-Dec-22	13-Dec-22	8	04-Apr-23	17-Apr-23	-31																	
19																								
P24&P27-BP03.	BP - Excavation	28-Nov-22	03-Dec-22	6	28-Mar-23	03-Apr-23	-60																	
P24&P27-BP03.:	BP - RCD Drilling	05-Dec-22	10-Jan-23	29	04-Apr-23	12-May-23	-60																	
P24&P27-BP03.:	BP - Airlift, Cage Install and Concrete	11-Jan-23	19-Jan-23	8	13-May-23	22-May-23	-60																	
VD07																								
09																								
P24&P27-BP38.:	BP - RCD Drilling	20-Sep-22	13-Oct-22	30	01-Nov-22 A	06-Dec-22 A																		
P24&P27-BP38.:	BP - Airlift, Cage Install and Concrete	14-Oct-22	22-Oct-22	11	07-Dec-22 A	19-Dec-22	61																	
10																								
P24&P27-BP22.:	BP - Airlift, Cage Install and Concrete	05-Nov-22	14-Nov-22	8	13-May-23	22-May-23	-60																	
VD08																								
P23-BP01.10	BP - Excavation	23-Nov-22	29-Nov-22	20	12-Jul-22 A	04-Aug-22 A																		
P23-BP01.20	BP - RCD Drilling	30-Nov-22	21-Dec-22	10	05-Aug-22 A	17-Aug-22 A																		
P23-BP01.30	BP - Airlift, Cage Install and Concrete	22-Dec-22	03-Jan-23	13	18-Aug-22 A	02-Sep-22 A																		
P24&P27-BP17.	BP - Excavation	29-Dec-22	05-Jan-23	51	06-Jul-22 A	03-Sep-22 A																		
P24&P27-BP17.:	BP - RCD Drilling	06-Jan-23	31-Jan-23	4	05-Sep-22 A	09-Sep-22 A																		
P24&P27-BP17.:	BP - Airlift, Cage Install and Concrete	01-Feb-23	09-Feb-23	5	10-Sep-22 A	17-Sep-22 A																		
P23-BP02.20	BP - RCD Drilling	08-Nov-22	29-Nov-22	6	24-Sep-22 A	03-Oct-22 A																		
P23-BP02.30	BP - Airlift, Cage Install and Concrete	30-Nov-22	08-Dec-22	11	05-Oct-22 A	18-Oct-22 A																		
P24&P27-BP11.:	BP - Excavation	23-Nov-22	29-Nov-22	24	19-Sep-22 A	19-Oct-22 A																		
P24&P27-BP11.:	BP - RCD Drilling	30-Nov-22	05-Jan-23	5	20-Oct-22 A	26-Oct-22 A																		
P24&P27-BP11.:	BP - Airlift, Cage Install and Concrete	06-Jan-23	14-Jan-23	8	27-Oct-22 A	05-Nov-22 A																		
P24&P27-BP35.:	BP - RCD Drilling	05-Oct-22	26-Oct-22	5	09-Nov-22 A	15-Nov-22 A																		
P24&P27-BP35.:	BP - Airlift, Cage Install and Concrete	27-Oct-22	04-Nov-22	14	16-Nov-22 A	02-Dec-22 A																		


ID: 2B2C-20221210_w
Data Date: 10-Dec-22
Print Date: 14-Dec-22_12:32
Page 2 of 13







	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 9 December 2022
Based on CMWP Rev.0

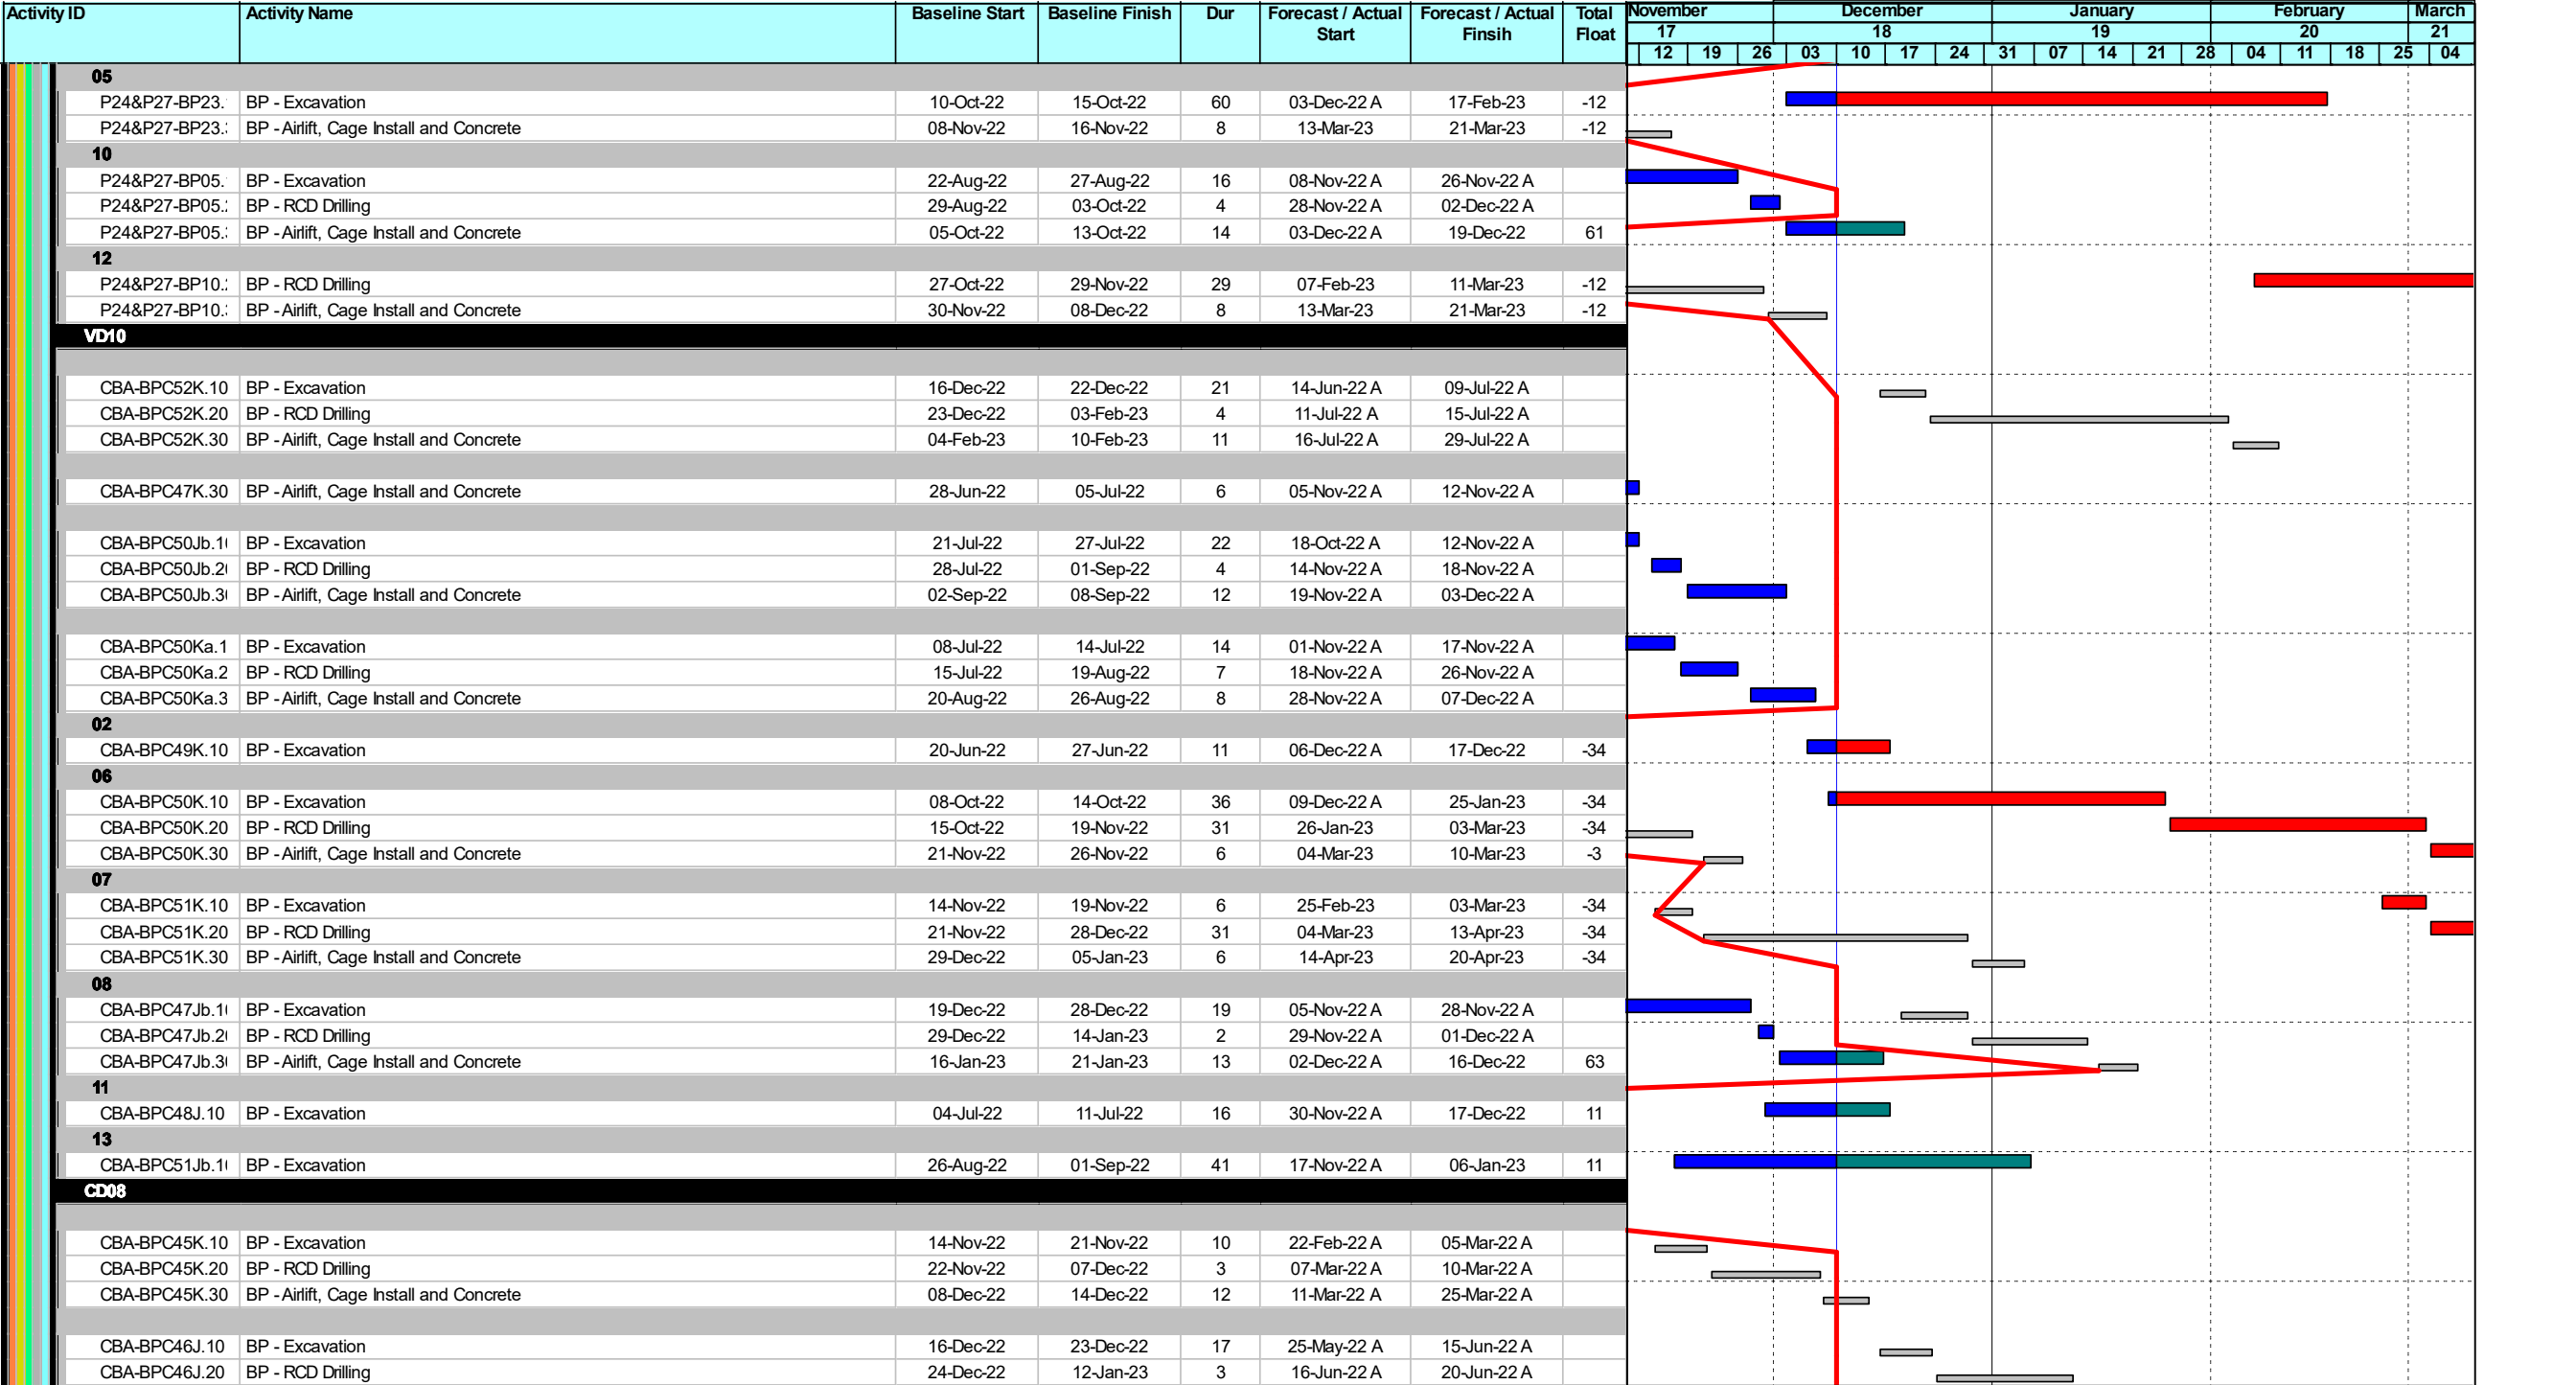

Date	Revision	Checked	Approved
4-Mar-22	Rev.0	KL	B










	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS

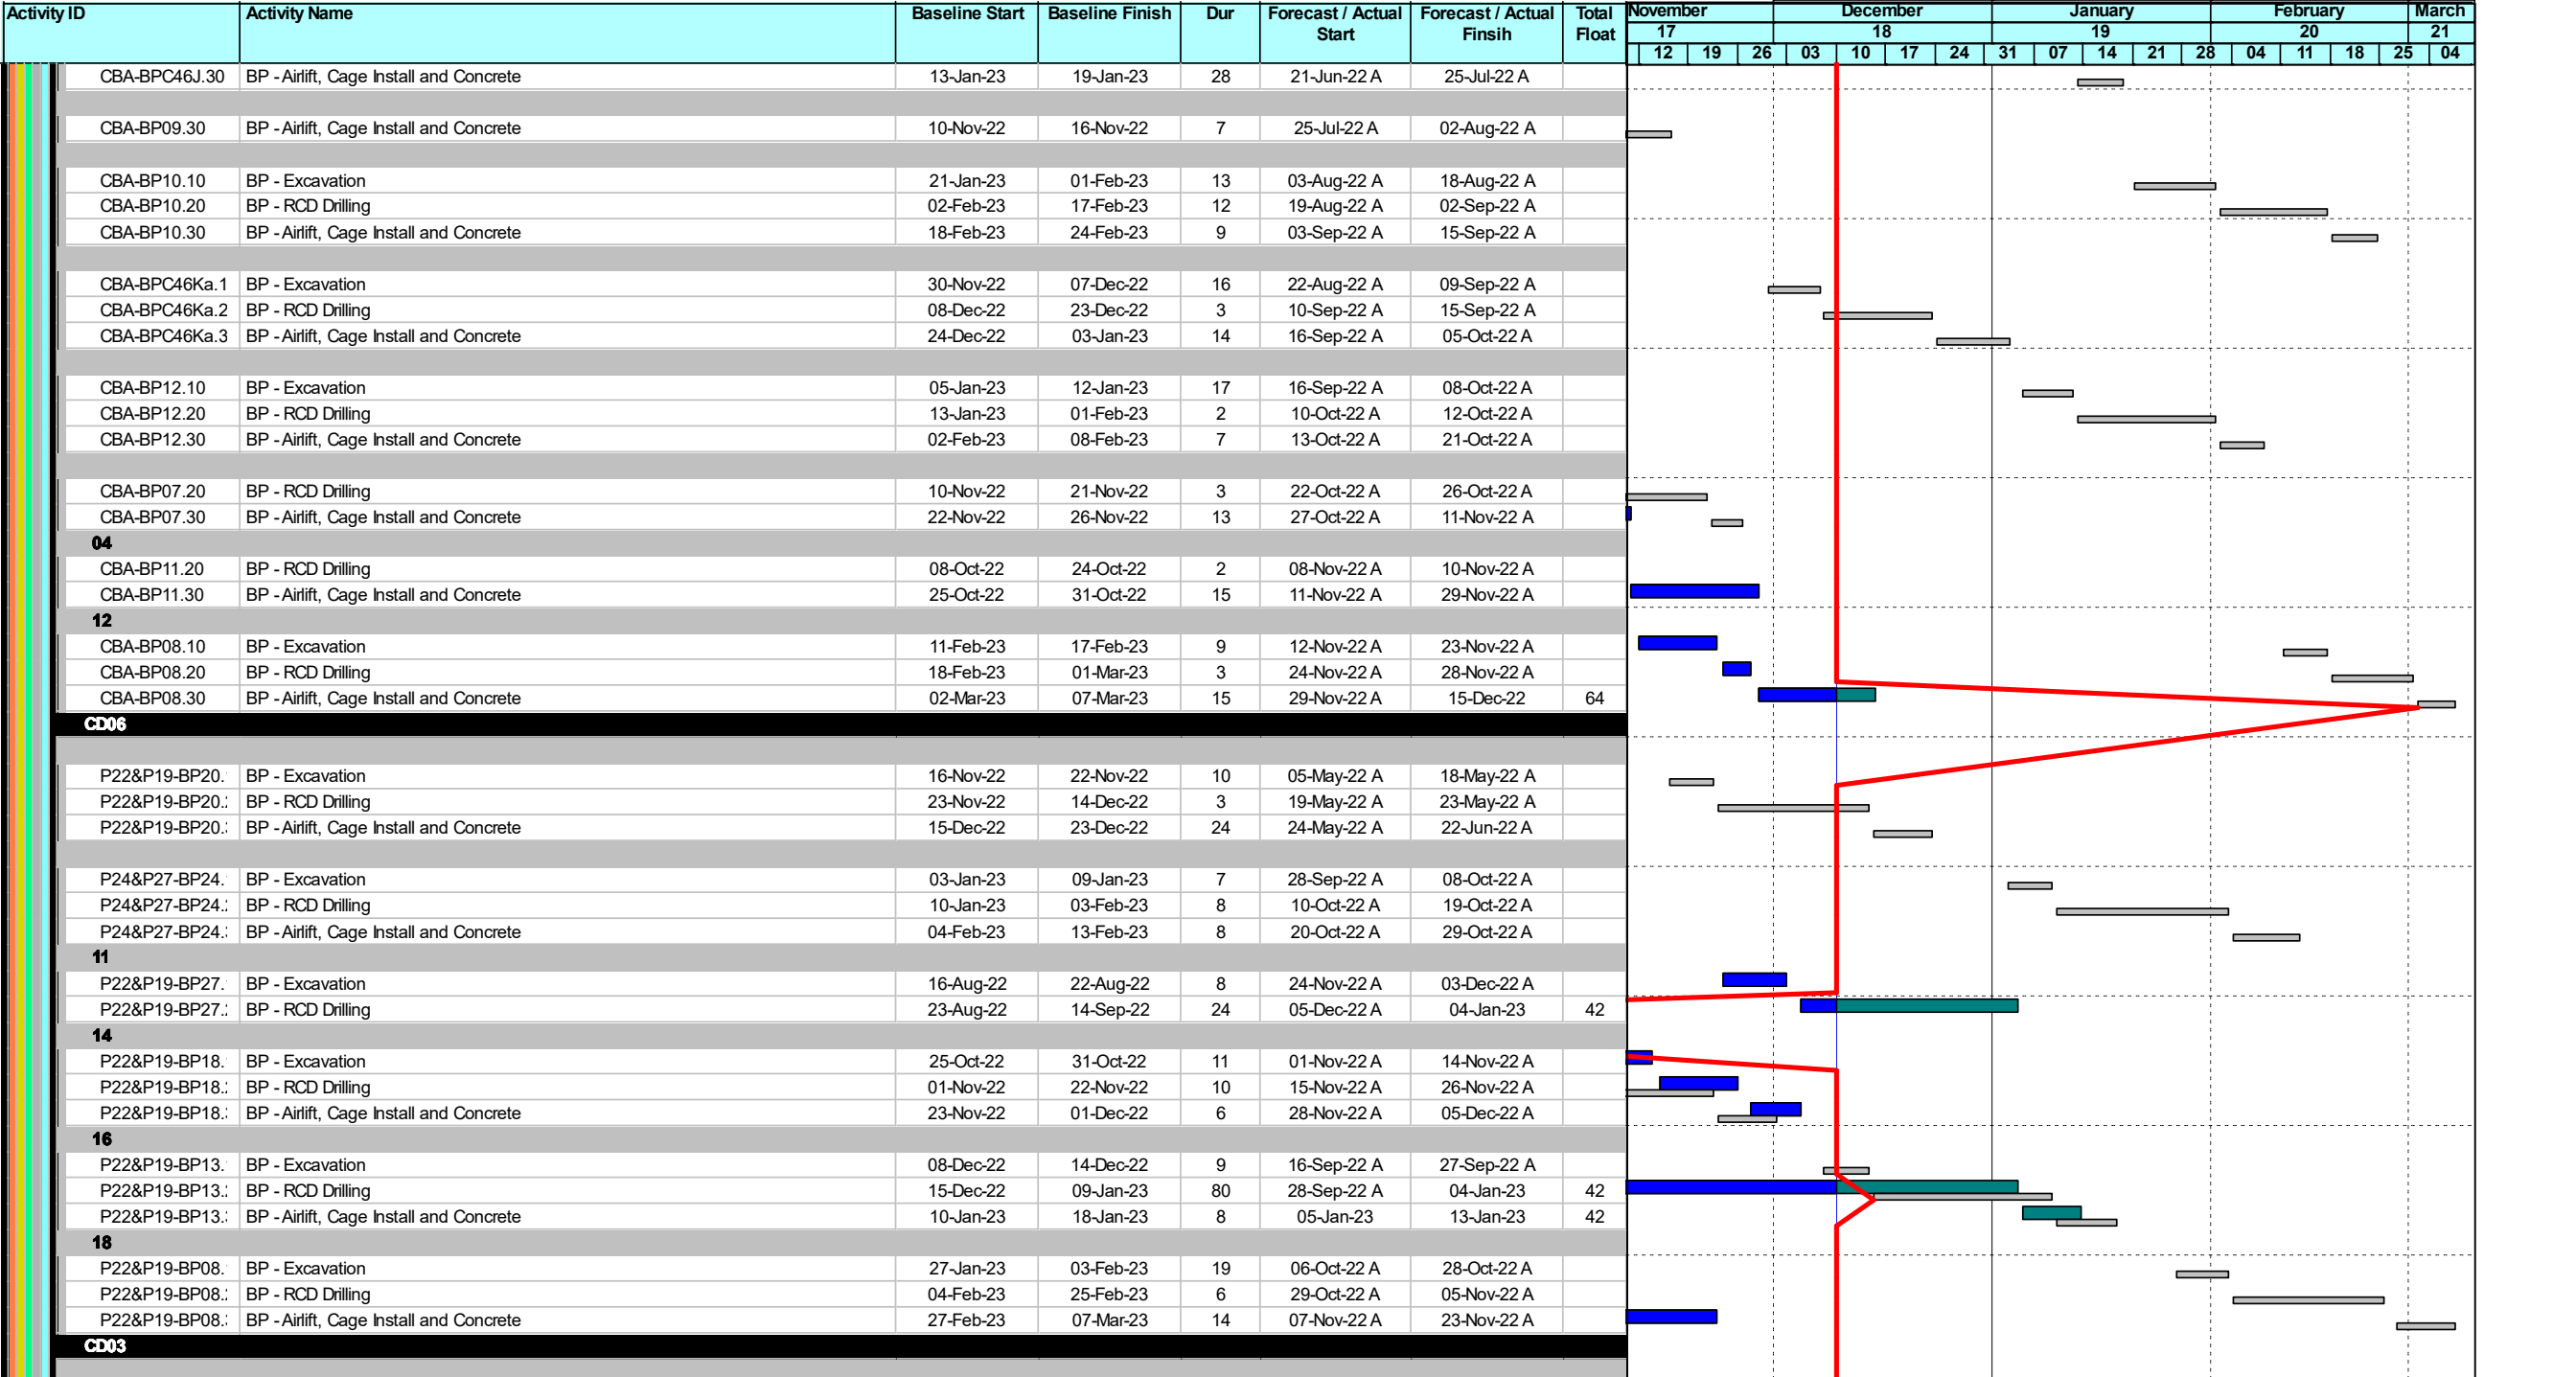West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 9 December 2022
 Based on CMWP Rev.0






Date	Revision	Checked	Approved
4-Mar-22	Rev.0	KL	B






	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS




West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 9 December 2022
 Based on CMWP Rev.0

					
Date	Revision	Checked	Approved		
4-Mar-22	Rev.0	KL	B		

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finish	Total Float	November			December				January				February				March
								17	19	26	18		17	24	31	19		28	20		25	21	
								12	19	26	03	10	17	24	31	07	14	21	28	04	11	18	25
P23-BP03.10	BP - Excavation	12-Nov-22	18-Nov-22	11	14-Oct-22 A	27-Oct-22 A																	
P23-BP03.20	BP - RCD Drilling	19-Nov-22	22-Dec-22	11	28-Oct-22 A	10-Nov-22 A																	
P23-BP03.30	BP - Airlift, Cage Install and Concrete	23-Dec-22	04-Jan-23	6	11-Nov-22 A	18-Nov-22 A																	
11																							
P23-BP08.10	BP - Excavation	12-Aug-22	18-Aug-22	23	21-Nov-22 A	16-Dec-22	36																
14																							
P23-BP16.20	BP - RCD Drilling	28-Oct-22	18-Nov-22	10	31-Oct-22 A	11-Nov-22 A																	
P23-BP16.30	BP - Airlift, Cage Install and Concrete	19-Nov-22	28-Nov-22	12	12-Nov-22 A	26-Nov-22 A																	
KD07 (Section 3)																							
Bored Piles																							
VD01																							
P26-BP09.10	BP - Excavation	30-Jan-23	04-Feb-23	12	07-Nov-22 A	21-Nov-22 A																	
P26-BP09.20	BP - RCD Drilling	06-Feb-23	27-Feb-23	7	22-Nov-22 A	30-Nov-22 A																	
P26-BP09.30	BP - Airlift, Cage Install and Concrete	28-Feb-23	08-Mar-23	16	01-Dec-22 A	19-Dec-22	153																
17																							
P26-BP07.20	BP - RCD Drilling	08-Oct-22	10-Nov-22	29	17-Dec-22	25-Jan-23	-9																
P26-BP07.30	BP - Airlift, Cage Install and Concrete	11-Nov-22	19-Nov-22	8	26-Jan-23	04-Feb-23	118																
VD02																							
P28&P29-BP04.:	BP - Airlift, Cage Install and Concrete	03-Nov-22	10-Nov-22	8	09-Sep-22 A	20-Sep-22 A																	
P28&P29-BP16.:	BP - RCD Drilling	03-Nov-22	19-Nov-22	4	19-Oct-22 A	24-Oct-22 A																	
P28&P29-BP16.:	BP - Airlift, Cage Install and Concrete	21-Nov-22	28-Nov-22	12	25-Oct-22 A	08-Nov-22 A																	
P24&P27-BP07.:	BP - Excavation	04-Jan-23	10-Jan-23	19	20-Oct-22 A	11-Nov-22 A																	
P24&P27-BP07.:	BP - RCD Drilling	11-Jan-23	04-Feb-23	11	12-Nov-22 A	25-Nov-22 A																	
P24&P27-BP07.:	BP - Airlift, Cage Install and Concrete	06-Feb-23	14-Feb-23	11	26-Nov-22 A	09-Dec-22 A																	
05																							
P26-BP01.10	BP - Excavation	16-May-22	21-May-22	76	26-Nov-22 A	01-Mar-23	-13																
11																							
P26-BP02.10	BP - Excavation	14-Nov-22	19-Nov-22	6	25-May-23	01-Jun-23	-13																
P26-BP02.20	BP - RCD Drilling	21-Nov-22	23-Dec-22	29	02-Jun-23	07-Jul-23	-13																
P26-BP02.30	BP - Airlift, Cage Install and Concrete	24-Dec-22	05-Jan-23	8	08-Jul-23	17-Jul-23	-13																
14																							
P28&P29-BP09.:	BP - Excavation	30-Jun-22	07-Jul-22	32	02-Dec-22 A	11-Jan-23	-60																
17																							
P24&P27-BP13.:	BP - RCD Drilling	10-Oct-22	11-Nov-22	29	07-Feb-23	11-Mar-23	-60																
P24&P27-BP13.:	BP - Airlift, Cage Install and Concrete	12-Nov-22	21-Nov-22	8	13-Mar-23	21-Mar-23	80																
VD03																							
P30-BP57.20	BP - RCD Drilling	01-Nov-22	03-Dec-22	10	08-Apr-22 A	23-Apr-22 A																	
P30-BP57.30	BP - Airlift, Cage Install and Concrete	05-Dec-22	13-Dec-22	9	25-Apr-22 A	06-May-22 A																	
P30-BP65.30	BP - Airlift, Cage Install and Concrete	05-Nov-22	14-Nov-22	6	02-Sep-22 A	09-Sep-22 A																	
07																							
P30-BP70.10	BP - Excavation	28-Jul-22	03-Aug-22	22	22-Nov-22 A	16-Dec-22	102																
12																							
P30-BP71.10	BP - Excavation	30-Jan-23	04-Feb-23	6	06-May-23	12-May-23	-13																
P30-BP71.20	BP - RCD Drilling	06-Feb-23	28-Mar-23	44	13-May-23	06-Jul-23	-13																
VD04																							

	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 9 December 2022
 Based on CMWP Rev.0

					
Date	Revision	Checked	Approved		
4-Mar-22	Rev.0	KL	B		

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finish	Total Float	November			December				January				February			March
								17	19	26	18				19				20			21
								12	19	26	03	10	17	24	31	07	14	21	28	04	11	18

P30-BP68.10	BP - Excavation	30-Nov-22	06-Dec-22	12	07-Jul-22 A	21-Jul-22 A	
P30-BP68.20	BP - RCD Drilling	07-Dec-22	30-Dec-22	6	22-Jul-22 A	29-Jul-22 A	
P30-BP68.30	BP - Airlift, Cage Install and Concrete	31-Dec-22	10-Jan-23	11	30-Jul-22 A	12-Aug-22 A	

VD06

P28&P29-BP06.	BP - Excavation	16-Dec-22	22-Dec-22	20	23-Aug-22 A	16-Sep-22 A	
P28&P29-BP06.:	BP - RCD Drilling	23-Dec-22	12-Jan-23	5	17-Sep-22 A	23-Sep-22 A	
P28&P29-BP06.:	BP - Airlift, Cage Install and Concrete	13-Jan-23	20-Jan-23	13	24-Sep-22 A	12-Oct-22 A	

P28&P29-BP20.	BP - Excavation	29-Nov-22	05-Dec-22	16	10-Sep-22 A	30-Sep-22 A	
P28&P29-BP20.:	BP - RCD Drilling	06-Dec-22	22-Dec-22	3	03-Oct-22 A	07-Oct-22 A	
P28&P29-BP20.:	BP - Airlift, Cage Install and Concrete	23-Dec-22	03-Jan-23	10	08-Oct-22 A	20-Oct-22 A	

P28&P29-BP18.:	BP - RCD Drilling	01-Nov-22	17-Nov-22	4	07-Oct-22 A	12-Oct-22 A	
P28&P29-BP18.:	BP - Airlift, Cage Install and Concrete	18-Nov-22	25-Nov-22	12	13-Oct-22 A	27-Oct-22 A	

P28&P29-BP24.:	BP - Airlift, Cage Install and Concrete	06-Sep-22	14-Sep-22	16	29-Oct-22 A	17-Nov-22 A	
----------------	---	-----------	-----------	----	-------------	-------------	--

P28&P29-BP22.:	BP - Airlift, Cage Install and Concrete	24-Sep-22	03-Oct-22	25	09-Nov-22 A	08-Dec-22 A	
----------------	---	-----------	-----------	----	-------------	-------------	--

P28&P29-BP14.	BP - Excavation	20-Jun-22	25-Jun-22	11	29-Oct-22 A	11-Nov-22 A	
P28&P29-BP14.:	BP - RCD Drilling	27-Jun-22	14-Jul-22	5	12-Nov-22 A	18-Nov-22 A	
P28&P29-BP14.:	BP - Airlift, Cage Install and Concrete	15-Jul-22	22-Jul-22	10	19-Nov-22 A	01-Dec-22 A	

P28&P29-BP25.	BP - Excavation	11-Nov-22	17-Nov-22	6	30-Dec-22	06-Jan-23	118
P28&P29-BP25.:	BP - RCD Drilling	18-Nov-22	05-Dec-22	15	07-Jan-23	26-Jan-23	118
P28&P29-BP25.:	BP - Airlift, Cage Install and Concrete	06-Dec-22	13-Dec-22	7	27-Jan-23	04-Feb-23	118

P28&P29-BP19.	BP - Excavation	06-Jan-23	12-Jan-23	6	18-Nov-22 A	25-Nov-22 A	
P28&P29-BP19.:	BP - RCD Drilling	13-Jan-23	02-Feb-23	5	26-Nov-22 A	02-Dec-22 A	
P28&P29-BP19.:	BP - Airlift, Cage Install and Concrete	03-Feb-23	10-Feb-23	49	03-Dec-22 A	04-Feb-23	118

VD07

P24&P27-BP31.	BP - Excavation	20-May-22	26-May-22	20	24-Nov-22 A	16-Dec-22	118
---------------	-----------------	-----------	-----------	----	-------------	-----------	-----


P24&P27-BP26.:	BP - RCD Drilling	05-Nov-22	08-Dec-22	29	13-May-23	16-Jun-23	-64
P24&P27-BP26.:	BP - Airlift, Cage Install and Concrete	09-Dec-22	17-Dec-22	8	17-Jun-23	27-Jun-23	3

P28&P29-BP27.	BP - Excavation	02-Dec-22	08-Dec-22	6	10-Jun-23	16-Jun-23	-64
P28&P29-BP27.:	BP - RCD Drilling	09-Dec-22	03-Jan-23	19	17-Jun-23	11-Jul-23	-64
P28&P29-BP27.:	BP - Airlift, Cage Install and Concrete	04-Jan-23	12-Jan-23	8	12-Jul-23	20-Jul-23	-16

P28&P29-BP21.	BP - Excavation	24-Dec-22	03-Jan-23	6	05-Jul-23	11-Jul-23	-64
P28&P29-BP21.:	BP - RCD Drilling	04-Jan-23	27-Jan-23	19	12-Jul-23	02-Aug-23	-64
P28&P29-BP21.:	BP - Airlift, Cage Install and Concrete	30-Jan-23	07-Feb-23	8	03-Aug-23	11-Aug-23	-35

P28&P29-BP17.	BP - Excavation	19-Jan-23	27-Jan-23	6	27-Jul-23	02-Aug-23	-64
P28&P29-BP17.:	BP - RCD Drilling	30-Jan-23	03-Mar-23	29	03-Aug-23	05-Sep-23	-64
P28&P29-BP17.:	BP - Airlift, Cage Install and Concrete	04-Mar-23	13-Mar-23	8	06-Sep-23	14-Sep-23	-64

P28&P29-BP17.:	BP - Airlift, Cage Install and Concrete	04-Mar-23	13-Mar-23	8	06-Sep-23	14-Sep-23	-64
----------------	---	-----------	-----------	---	-----------	-----------	-----

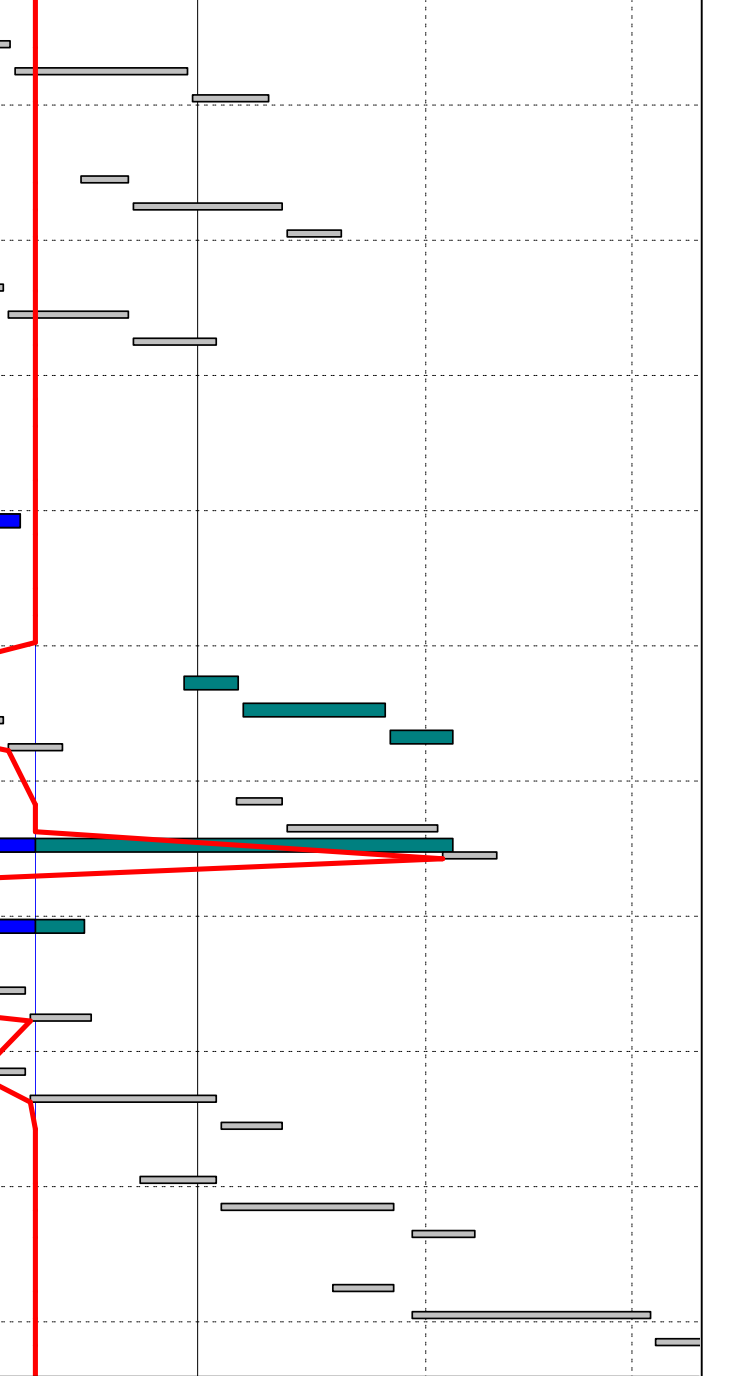


ID: 2B2C-20221210_w
 Data Date: 10-Dec-22
 Print Date: 14-Dec-22_12:32
 Page 6 of 13

■	Planned	◆	Planned MS
■	Critical	◆	Critical MS
■	Actual	◆	Actual MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 9 December 2022
Based on CMWP Rev.0

	Date	Revision	Checked	Approved
	4-Mar-22	Rev.0	KL	B

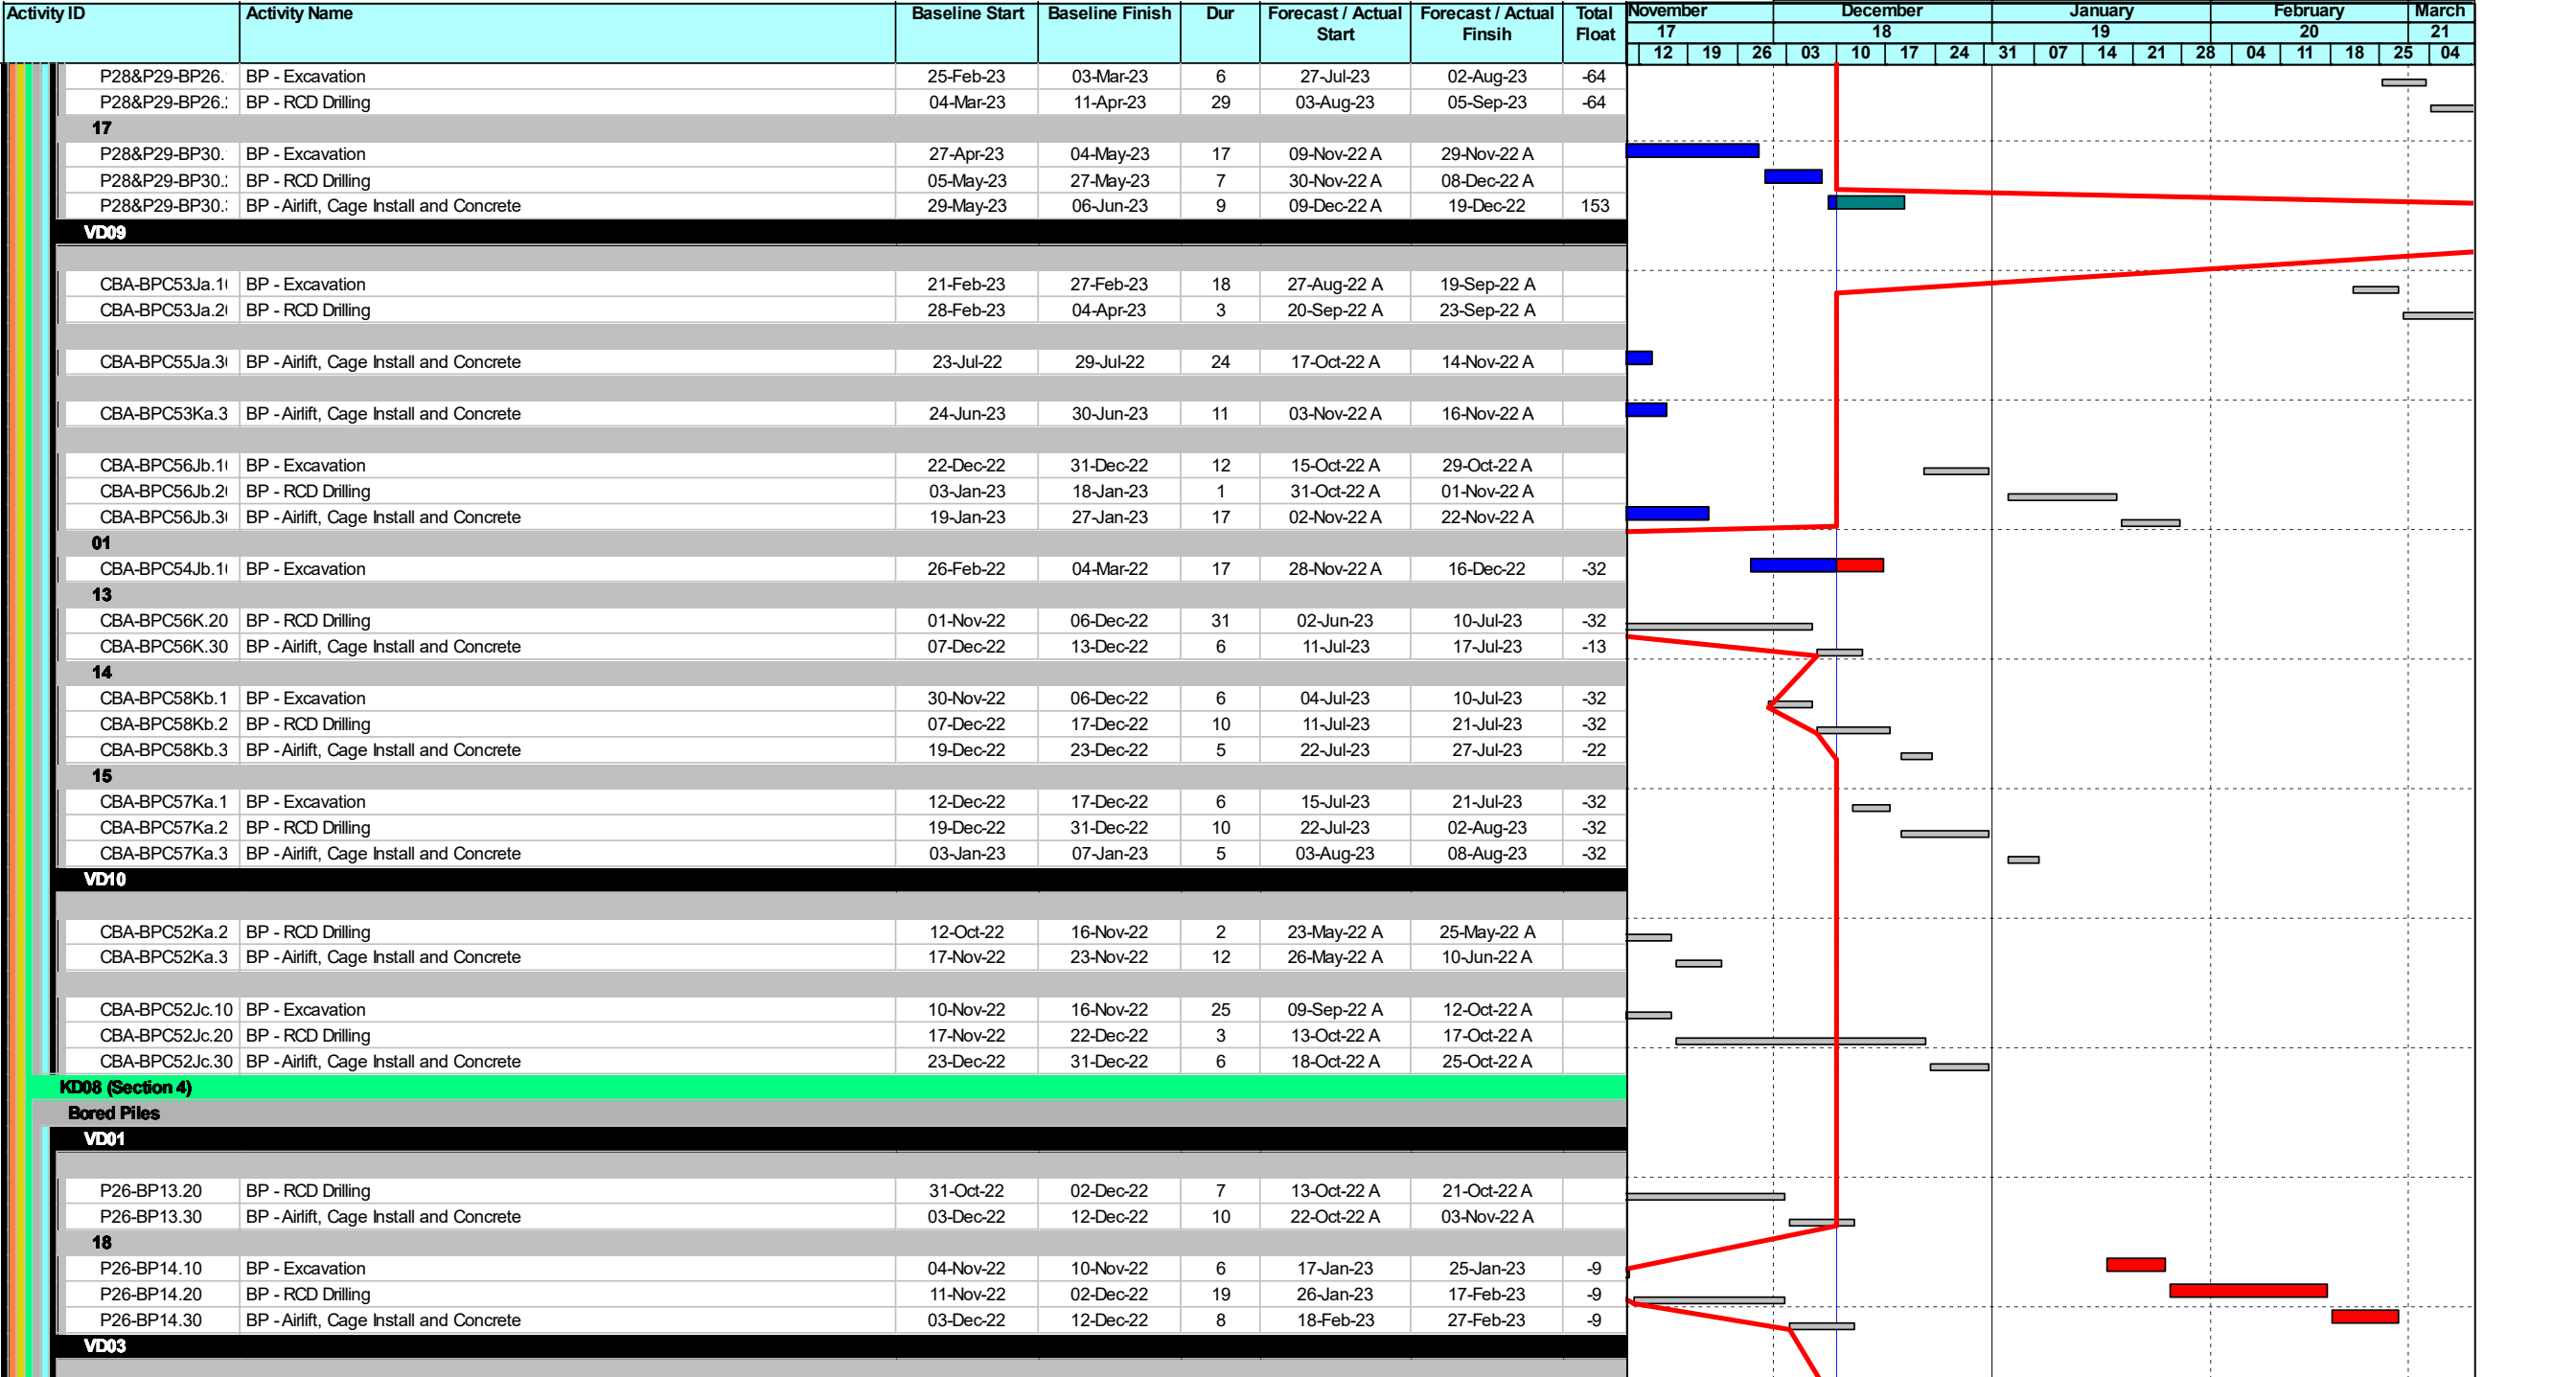

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	November			December			January			February			March				
								17	19	26	03	10	17	24	31	07	14	21	28	04	11	18	25	21
								12	19	26	03	10	17	24	31	07	14	21	28	04	11	18	25	04
13																								
CBA-BPC53U.10	BP - Excavation	14-Nov-22	19-Nov-22	6	10-May-23	16-May-23	-86																	
CBA-BPC53U.20	BP - RCD Drilling	21-Nov-22	01-Dec-22	10	17-May-23	29-May-23	-86																	
CBA-BPC53U.30	BP - Airlift, Cage Install and Concrete	02-Dec-22	07-Dec-22	5	30-May-23	03-Jun-23	-86																	
KD09 (Section 5)																								
Bored Piles																								
VD01																								
P23-BP46.10	BP - Excavation	26-Nov-22	02-Dec-22	16	23-Jul-22 A	11-Aug-22 A																		
P23-BP46.20	BP - RCD Drilling	03-Dec-22	24-Dec-22	33	12-Aug-22 A	21-Sep-22 A																		
P23-BP46.30	BP - Airlift, Cage Install and Concrete	28-Dec-22	06-Jan-23	7	22-Sep-22 A	30-Sep-22 A																		
P23-BP45.10	BP - Excavation	26-Nov-22	02-Dec-22	27	05-Oct-22 A	05-Nov-22 A																		
P23-BP45.20	BP - RCD Drilling	03-Dec-22	20-Dec-22	8	07-Nov-22 A	16-Nov-22 A																		
P23-BP45.30	BP - Airlift, Cage Install and Concrete	21-Dec-22	30-Dec-22	7	17-Nov-22 A	25-Nov-22 A																		
13																								
P23-BP34.10	BP - Excavation	14-Dec-22	20-Dec-22	6	25-Apr-23	02-May-23	-70																	
P23-BP34.20	BP - RCD Drilling	21-Dec-22	14-Jan-23	19	03-May-23	24-May-23	-70																	
P23-BP34.30	BP - Airlift, Cage Install and Concrete	16-Jan-23	26-Jan-23	8	25-May-23	03-Jun-23	-70																	
CD01																								
P23-BP52.30	BP - Airlift, Cage Install and Concrete	20-Jun-22	28-Jun-22	5	04-Nov-22 A	10-Nov-22 A																		
CD02																								
P23-BP61.10	BP - Excavation	17-Dec-22	23-Dec-22	13	15-Aug-22 A	30-Aug-22 A																		
P23-BP61.20	BP - RCD Drilling	24-Dec-22	18-Jan-23	11	31-Aug-22 A	14-Sep-22 A																		
P23-BP61.30	BP - Airlift, Cage Install and Concrete	19-Jan-23	31-Jan-23	7	15-Sep-22 A	23-Sep-22 A																		
13																								
P23-BP49.10	BP - Excavation	22-Oct-22	28-Oct-22	15	14-Nov-22 A	01-Dec-22 A																		
P23-BP49.20	BP - RCD Drilling	29-Oct-22	19-Nov-22	26	02-Dec-22 A	04-Jan-23	42																	
P23-BP49.30	BP - Airlift, Cage Install and Concrete	21-Nov-22	29-Nov-22	8	05-Jan-23	13-Jan-23	42																	
14																								
P23-BP47.10	BP - Excavation	14-Nov-22	19-Nov-22	29	26-Oct-22 A	29-Nov-22 A																		
P23-BP47.20	BP - RCD Drilling	21-Nov-22	23-Dec-22	38	30-Nov-22 A	16-Jan-23	32																	
P23-BP47.30	BP - Airlift, Cage Install and Concrete	24-Dec-22	05-Jan-23	8	17-Jan-23	27-Jan-23	32																	
TD09																								
CBA-BPC40U.10	BP - Excavation	10-Dec-22	17-Dec-22	17	20-Jul-22 A	09-Aug-22 A																		
CBA-BPC40U.20	BP - RCD Drilling	19-Dec-22	06-Jan-23	1	10-Aug-22 A	11-Aug-22 A																		
CBA-BPC40U.30	BP - Airlift, Cage Install and Concrete	07-Jan-23	13-Jan-23	5	12-Aug-22 A	18-Aug-22 A																		
CBA-BPC40V.10	BP - Excavation	04-Feb-23	11-Feb-23	21	30-Aug-22 A	24-Sep-22 A																		
CBA-BPC40V.20	BP - RCD Drilling	13-Feb-23	28-Feb-23	0	26-Sep-22 A	26-Sep-22 A																		
CBA-BPC40V.30	BP - Airlift, Cage Install and Concrete	01-Mar-23	07-Mar-23	3	27-Sep-22 A	30-Sep-22 A																		
CBA-BPC40T.10	BP - Excavation	16-Jan-23	25-Jan-23	20	24-Sep-22 A	20-Oct-22 A																		
CBA-BPC40T.20	BP - RCD Drilling	26-Jan-23	11-Feb-23	0	21-Oct-22 A	21-Oct-22 A																		
CBA-BPC40T.30	BP - Airlift, Cage Install and Concrete	13-Feb-23	18-Feb-23	5	22-Oct-22 A	28-Oct-22 A																		
CBA-BPC40Wa.:	BP - Excavation	29-Dec-22	06-Jan-23	24	06-Oct-22 A	03-Nov-22 A																		
CBA-BPC40Wa.:	BP - RCD Drilling	07-Jan-23	25-Jan-23	0	04-Nov-22 A	04-Nov-22 A																		

	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 9 December 2022
 Based on CMWP Rev.0



Date	Revision	Checked	Approved
4-Mar-22	Rev.0	KL	B

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	November			December				January				February				March			
								17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	01	02	03	04
								12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30

20							
P23-BP66.30	BP - Airlift, Cage Install and Concrete	07-Nov-22	15-Nov-22	8	23-Mar-23	31-Mar-23	-21
TD02							
P23-BP70.10	BP - Excavation	30-Nov-22	06-Dec-22	20	19-Mar-22 A	13-Apr-22 A	
P23-BP70.20	BP - RCD Drilling	07-Dec-22	12-Jan-23	8	14-Apr-22 A	27-Apr-22 A	
P23-BP70.30	BP - Airlift, Cage Install and Concrete	13-Jan-23	21-Jan-23	7	28-Apr-22 A	07-May-22 A	
P23-BP72.20	BP - RCD Drilling	12-Oct-22	14-Nov-22	11	08-Jun-22 A	21-Jun-22 A	
P23-BP72.30	BP - Airlift, Cage Install and Concrete	15-Nov-22	23-Nov-22	12	22-Jun-22 A	07-Jul-22 A	
P23-BP104.10	BP - Excavation	08-Nov-22	14-Nov-22	32	15-Aug-22 A	22-Sep-22 A	
P23-BP104.20	BP - RCD Drilling	15-Nov-22	06-Dec-22	6	23-Sep-22 A	30-Sep-22 A	
P23-BP104.30	BP - Airlift, Cage Install and Concrete	07-Dec-22	15-Dec-22	9	03-Oct-22 A	14-Oct-22 A	
P23-BP111.30	BP - Airlift, Cage Install and Concrete	29-Apr-22	10-May-22	9	02-Nov-22 A	12-Nov-22 A	
P23-BP105.30	BP - Airlift, Cage Install and Concrete	22-Jul-22	30-Jul-22	12	03-Nov-22 A	17-Nov-22 A	
04							
P23-BP83.10	BP - Excavation	08-Apr-22	14-Apr-22	14	01-Dec-22 A	16-Dec-22	-51
09							
P23-BP69.10	BP - Excavation	09-Sep-22	16-Sep-22	23	15-Oct-22 A	11-Nov-22 A	
P23-BP69.20	BP - RCD Drilling	17-Sep-22	09-Nov-22	5	12-Nov-22 A	18-Nov-22 A	
P23-BP69.30	BP - Airlift, Cage Install and Concrete	10-Nov-22	19-Nov-22	9	19-Nov-22 A	30-Nov-22 A	
13							
P23-BP92.20	BP - RCD Drilling	29-Apr-22	04-Jun-22	22	08-Nov-22 A	03-Dec-22 A	
P23-BP92.30	BP - Airlift, Cage Install and Concrete	06-Jun-22	14-Jun-22	13	05-Dec-22 A	19-Dec-22	61

Pile Test

KD05 (Section 1) (incl. BP for KD01 (Stage1-1))


BP							
KD05.TS.1040	Selection of Full Core by BD	27-Oct-22	11-Nov-22	14	16-May-23	01-Jun-23	-161
KD05.TS.1060	Full Core to Proof Drill	12-Nov-22	28-Nov-22	14	02-Jun-23	17-Jun-23	-161
KD05.TS.1080	Obtain BA14 Acknowledgement / Satisfaction of CA, Completion As-built Drawings, Reports & Records	29-Nov-22	03-Jan-23	28	19-Jun-23	22-Jul-23	-161

KD07 (Section 3) (incl. BP for KD03) (Stage 3-1)

BP							
KD07.TS.1000	Sonic Logging Test and Interfacing Coring	20-Feb-23	18-Jul-23	120	31-May-23	21-Oct-23	-80


KD08 (Section 4) (incl. BP for KD04 (Stage 4-1) & SSHP in KD09 (Section 5))

BP							
KD08.TS.1000	Sonic Logging Test and Interfacing Coring	10-Oct-22	04-Mar-23	292	04-Jul-22 A	27-Jun-23	-91
KD08.TS.1020	Submit BA14	06-Mar-23	13-Mar-23	7	28-Jun-23	06-Jul-23	-91
SSHP							
KD08.TS.1100	Post Construction Proof Drilling (2 Nos.)	24-Oct-22	16-Nov-22	13	31-Oct-22 A	15-Nov-22 A	

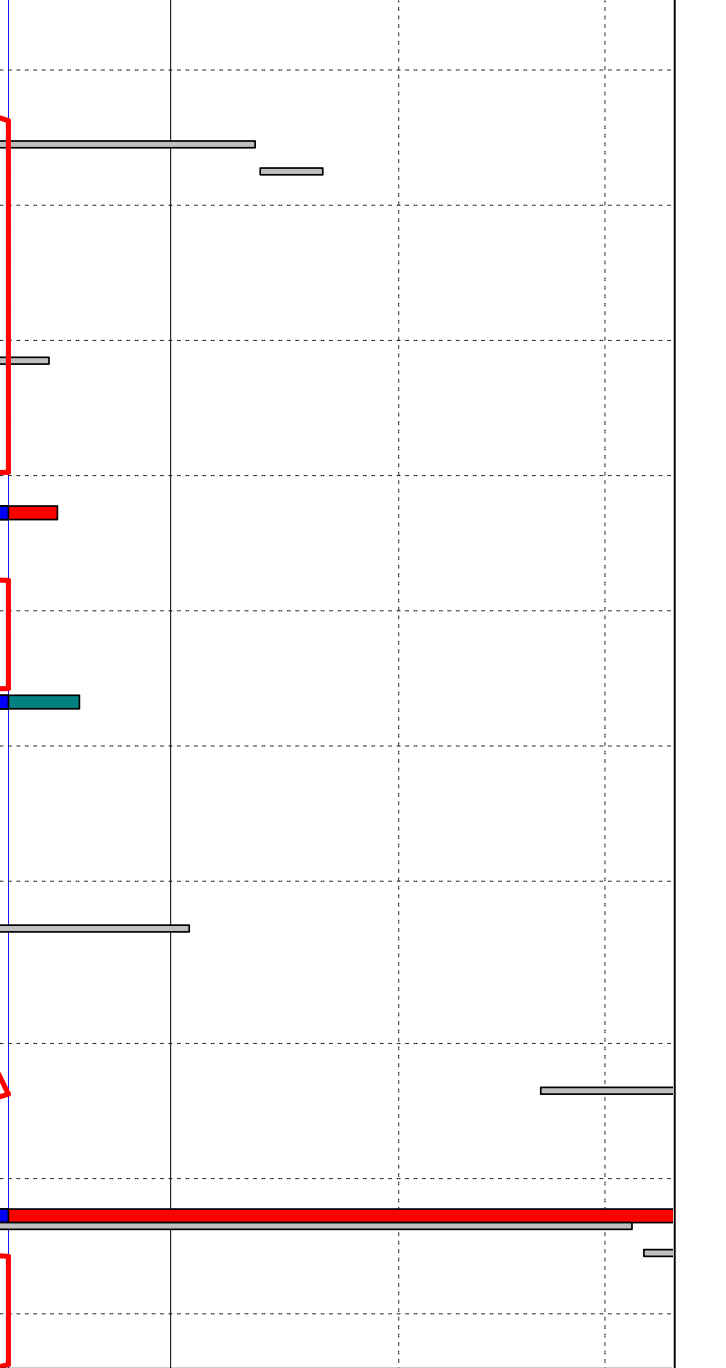

	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS

Date	Revision	Checked	Approved
4-Mar-22	Rev.0	KL	B



Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	November			December			January			February			March						
								17			18			19			20			21						
								12	19	26	03	10	17	24	31	07	14	21	28	04	11	18	25	04		
KD08.TS.1120	Submit BA14	25-Nov-22	02-Dec-22	28	16-Nov-22 A	17-Dec-22	66																			
KD08.TS.1140	Selection of Pile for Static Load Test	03-Dec-22	19-Dec-22	14	19-Dec-22	06-Jan-23	66																			
KD08.TS.1160	Static Load Test of Selected Pile	20-Dec-22	07-Jan-23	14	07-Jan-23	25-Jan-23	66																			
KD08.TS.1180	Obtain BA14 Acknowledgement / Satisfaction of CA, Completion As-built Drawings, Reports & Records	09-Jan-23	13-Feb-23	28	26-Jan-23	28-Feb-23	66																			
Attendance to Other Project Contractors (optional works item no. 2A to 2E)																										
Attendance to Other Project Contractors (optional works item no. 2A to 2E)																										
S4.AT.0000	Attendance at Section 4 Area (optional works item no. 2D) (Duration TBC)	22-Feb-23	13-Mar-23	20	22-Feb-23	13-Mar-23	71																			
S5.AT.0040	Attendance at Section 5 Area (optional works item no. 2E) if item No. 3 is instructed (Duration TBC)	22-Feb-23	13-Mar-23	20	22-Feb-23	13-Mar-23	301																			

	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 9 December 2022
 Based on CMWP Rev.0



Date	Revision	Checked	Approved
4-Mar-22	Rev.0	KL	B
