



Zone 2A

Project Name: Foundation and ELS Works for Integrated Basement and Underground Road in Zone 2A of the West Kowloon Cultural District

3-Month Rolling Programme

Activity Description	Duration (Cal. Day)	Start Date	Finish Date	2023																
				January				February				March				April				
				6	13	20	27	3	10	17	24	3	10	17	24	31	7	14	21	28
Zone 2A A&A Works				W139	W140	W141	W142	W143	W144	W145	W146	W147	W148	W149	W150	W151	W152	W153	W154	W155
WEK B1/F																				
Sand Removal	63	17-Dec-22	17-Feb-23																	

 - Actual
 - Remaining Works

Zone 2B & 2C

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	December				January				February				March				April
								18				19				20				21				22
								10	17	24	31	07	14	21	28	04	11	18	25	04	11	18	25	01

Piling for Integrated Basement and U/G Road in Zone 2B & 2C

Contract Dates

Optional Works subjected to CA's Instruction

CO1A	Last CAI date for Optional Works Item No.1A (within 560 Days after Commencement)	02-Feb-23		0	02-Feb-23		1
CO1B	Last CAI date for Optional Works Item No.1B (within 560 Days after Commencement)	02-Feb-23		0	02-Feb-23		1
CO2D	Last CAI date for Optional Works Item No.2D (330 Days to 580 Days after Commencement)	22-Feb-23		0	22-Feb-23		71
CO2E	Last CAI date for Optional Works Item No.2E (330 Days to 600 Days after Commencement)	14-Mar-23		0	14-Mar-23		71

Construction Stage

File Construction

KD05 (Section 1)

Bored Piles

CD04

02

P17-BP12.10	BP IAR-N - Excavation	03-Dec-22	09-Dec-22	6	07-Jan-23	13-Jan-23	-107
P17-BP12.20	BP IAR-N - RCD Drilling	10-Dec-22	29-Dec-22	15	14-Jan-23	03-Feb-23	-107
P17-BP12.30	BP IAR-N - Airlift, Cage Install and Concrete	30-Dec-22	07-Jan-23	7	04-Feb-23	11-Feb-23	-92

03

P17-BP17.10	BP IAR-N - Excavation	21-Dec-22	29-Dec-22	26	31-Dec-22 A	03-Feb-23	-107
P17-BP17.20	BP IAR-N - RCD Drilling	30-Dec-22	17-Jan-23	15	04-Feb-23	21-Mar-23	-107
P17-BP17.30	BP IAR-N - Airlift, Cage Install and Concrete	18-Jan-23	27-Jan-23	7	22-Feb-23	01-Mar-23	-107

04

P17-BP11.10	BP IAR-N - Excavation	11-Jan-23	17-Jan-23	7	02-Dec-22 A	10-Dec-22 A	
P17-BP11.20	BP IAR-N - RCD Drilling	18-Jan-23	07-Feb-23	6	12-Dec-22 A	19-Dec-22 A	
P17-BP11.30	BP IAR-N - Airlift, Cage Install and Concrete	08-Feb-23	15-Feb-23	56	20-Dec-22 A	01-Mar-23	-107

05

P17-BP13.10	BP IAR-N - Excavation	03-Feb-23	09-Feb-23	6	03-Feb-23	09-Feb-23	-104
P17-BP13.20	BP IAR-N - RCD Drilling	10-Feb-23	27-Feb-23	15	01-Feb-23	17-Feb-23	-104
P17-BP13.30	BP IAR-N - Airlift, Cage Install and Concrete	28-Feb-23	07-Mar-23	7	18-Feb-23	25-Feb-23	-104

CD05


P17-BP06.20	BP - RCD Drilling	24-Mar-23	14-Apr-23	7	30-Nov-22 A	08-Dec-22 A	
P17-BP06.30	BP - Airlift, Cage Install and Concrete	15-Apr-23	22-Apr-23	7	09-Dec-22 A	17-Dec-22 A	

02

P17-BP07.10	BP - Excavation	15-Dec-22	21-Dec-22	9	19-Dec-22 A	31-Dec-22 A	
P17-BP07.20	BP - RCD Drilling	22-Dec-22	11-Jan-23	19	03-Jan-23 A	26-Jan-23	-129
P17-BP07.30	BP - Airlift, Cage Install and Concrete	12-Jan-23	19-Jan-23	7	27-Jan-23	04-Feb-23	-129

03

P17-BP02.10	BP - Excavation	20-Jan-23	30-Jan-23	6	06-Feb-23	11-Feb-23	-129
P17-BP02.20	BP - RCD Drilling	31-Jan-23	16-Feb-23	15	13-Feb-23	01-Mar-23	-129
P17-BP02.30	BP - Airlift, Cage Install and Concrete	17-Feb-23	24-Feb-23	7	02-Mar-23	09-Mar-23	-114

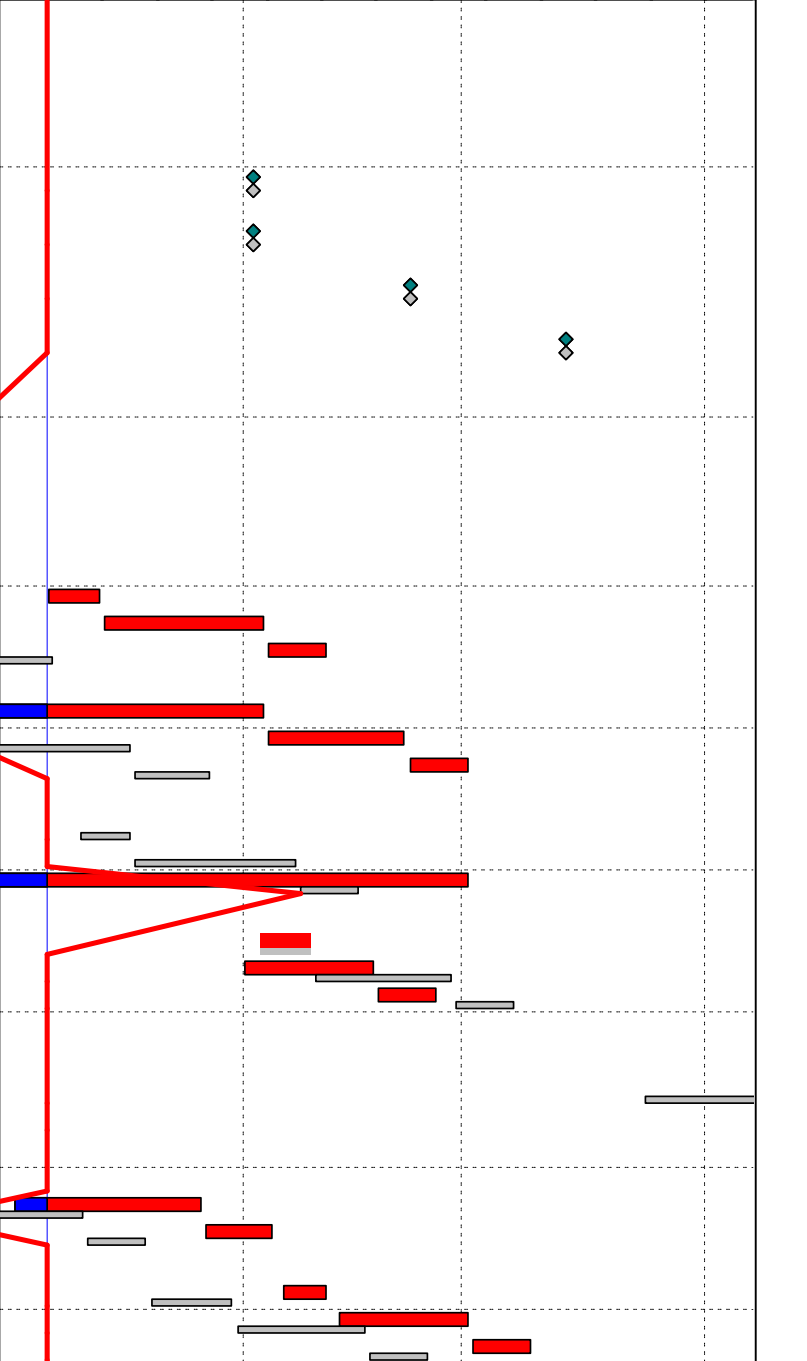


ID: 2BC-202230106_w TBC
 Data Date: 07-Jan-23
 Print Date: 11-Jan-23_10:49
 Page 1 of 16

■	Planned	◆	Planned MS
■	Critical	◆	Critical MS
■	Actual	◆	Actual MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 6 January 2023
Based on CMWP Rev.0 (3rd Draft)



Date	Revision	Checked	Approved
4-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C

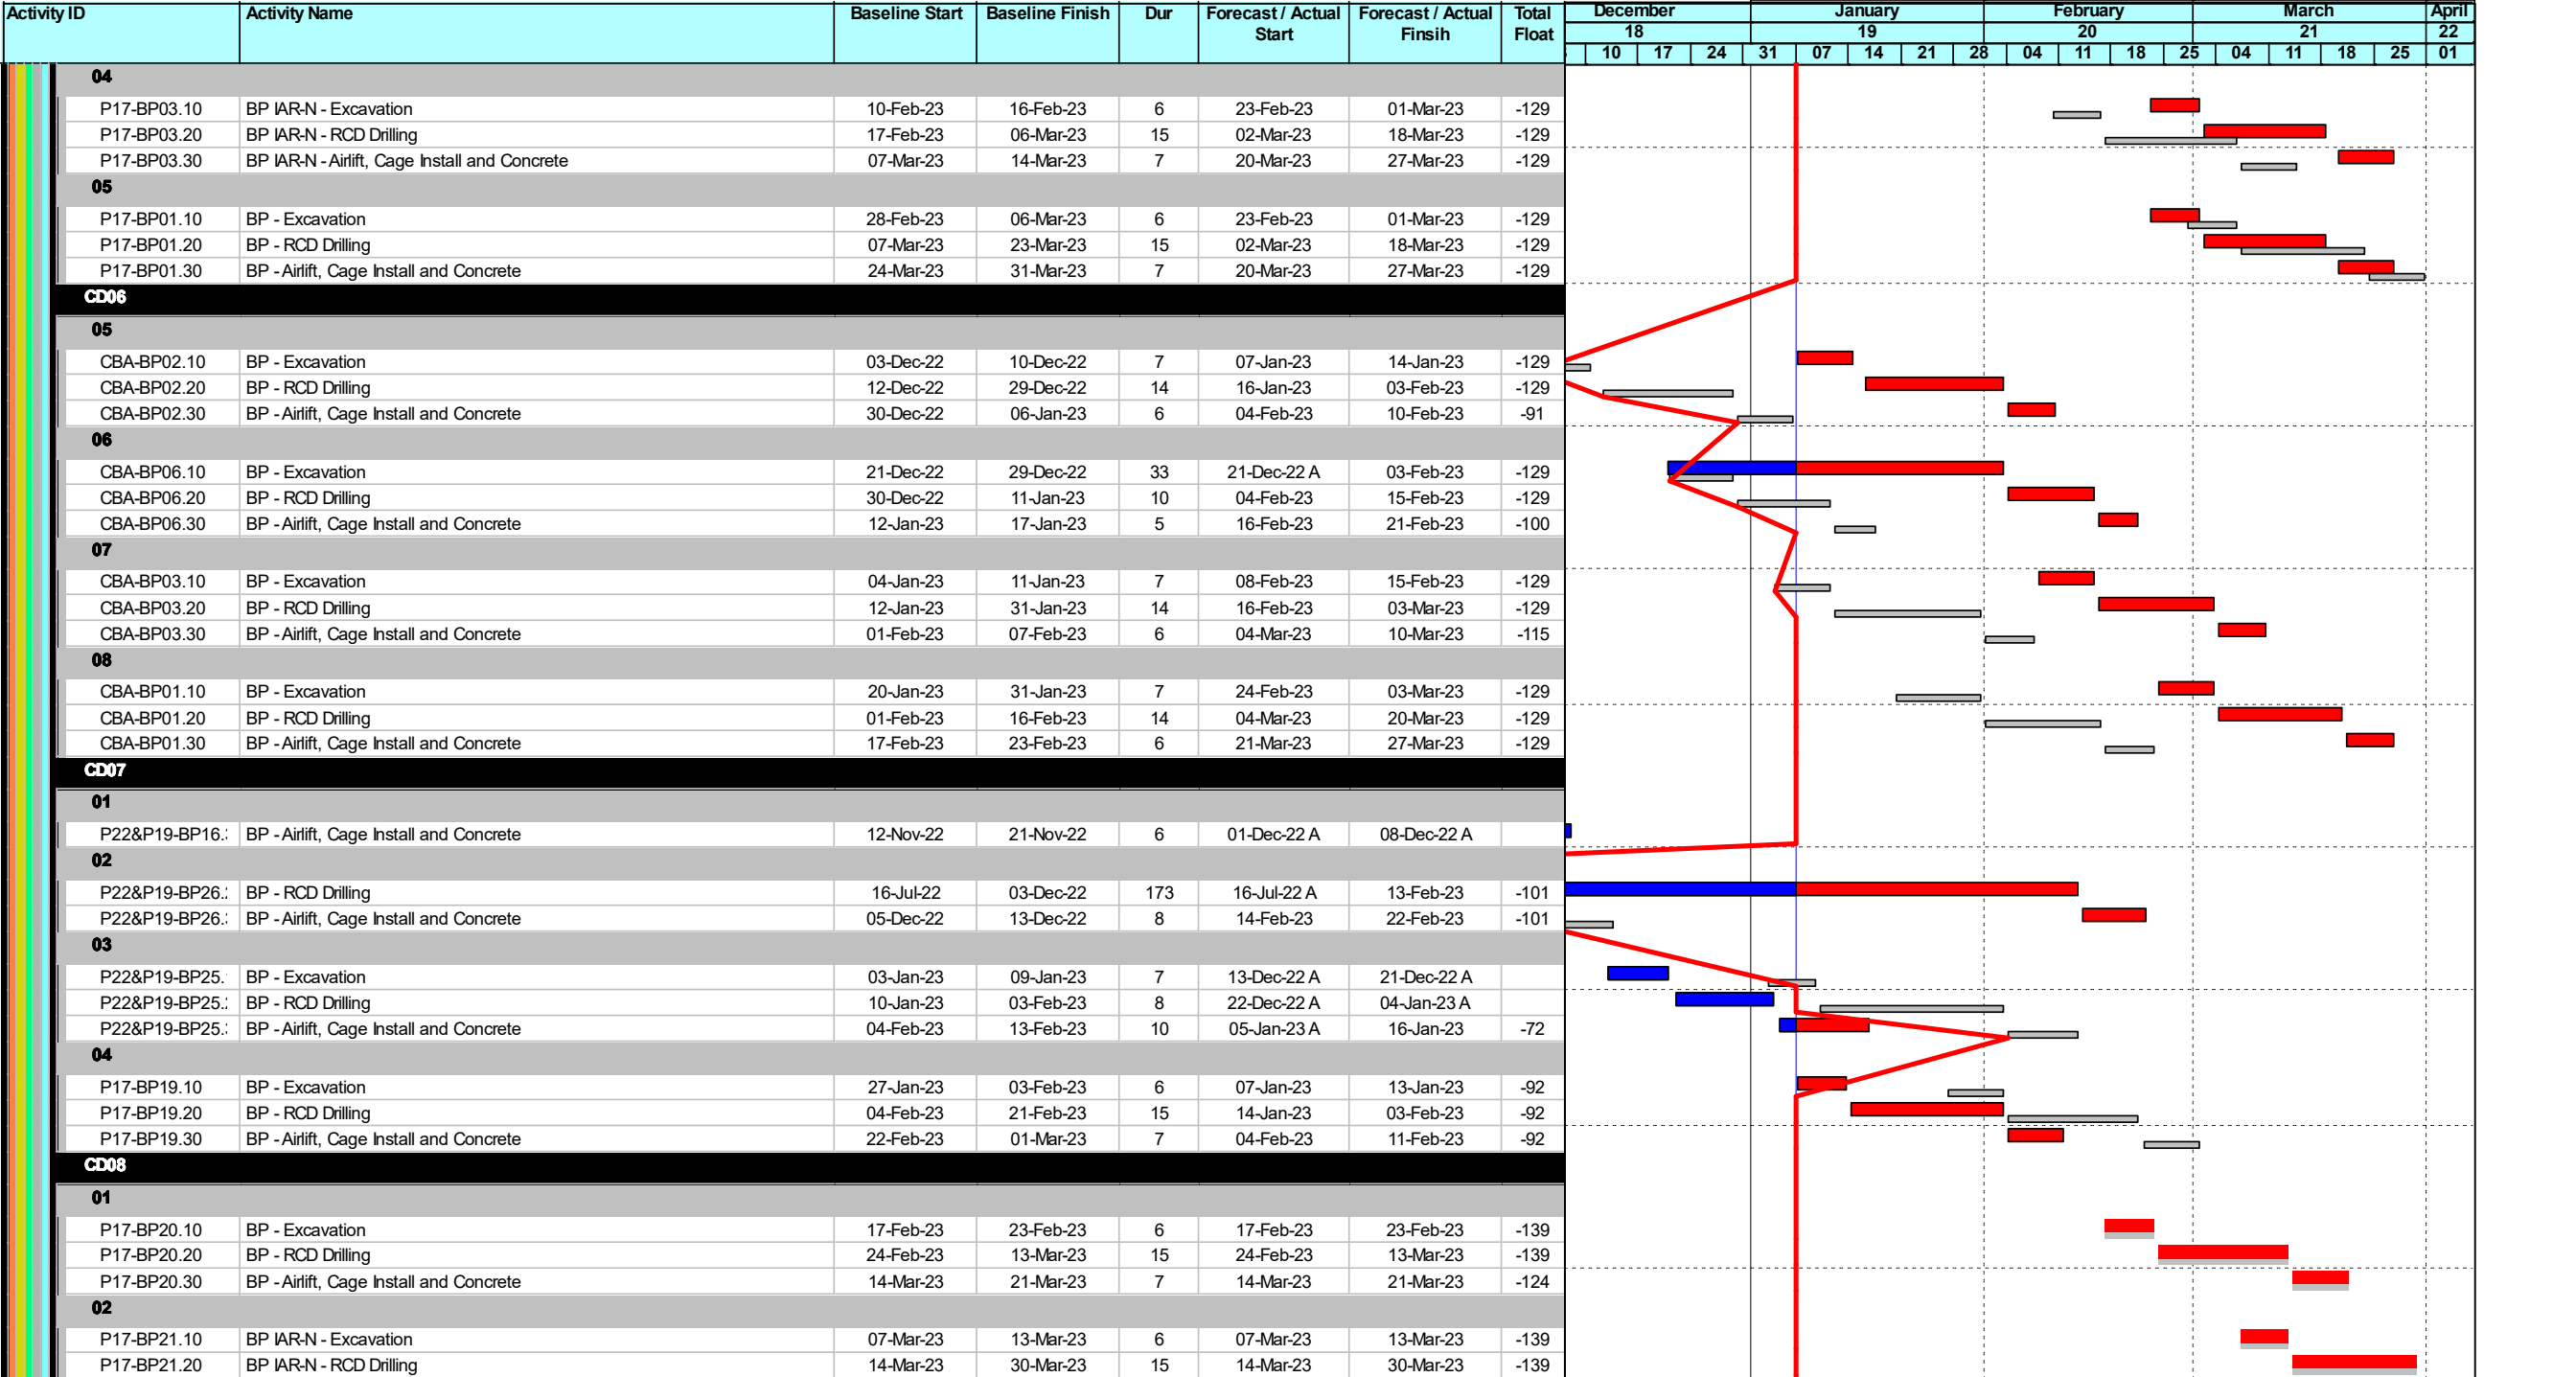


	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 6 January 2023
 Based on CMWP Rev.0 (3rd Draft)




Date	Revision	Checked	Approved
4-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C

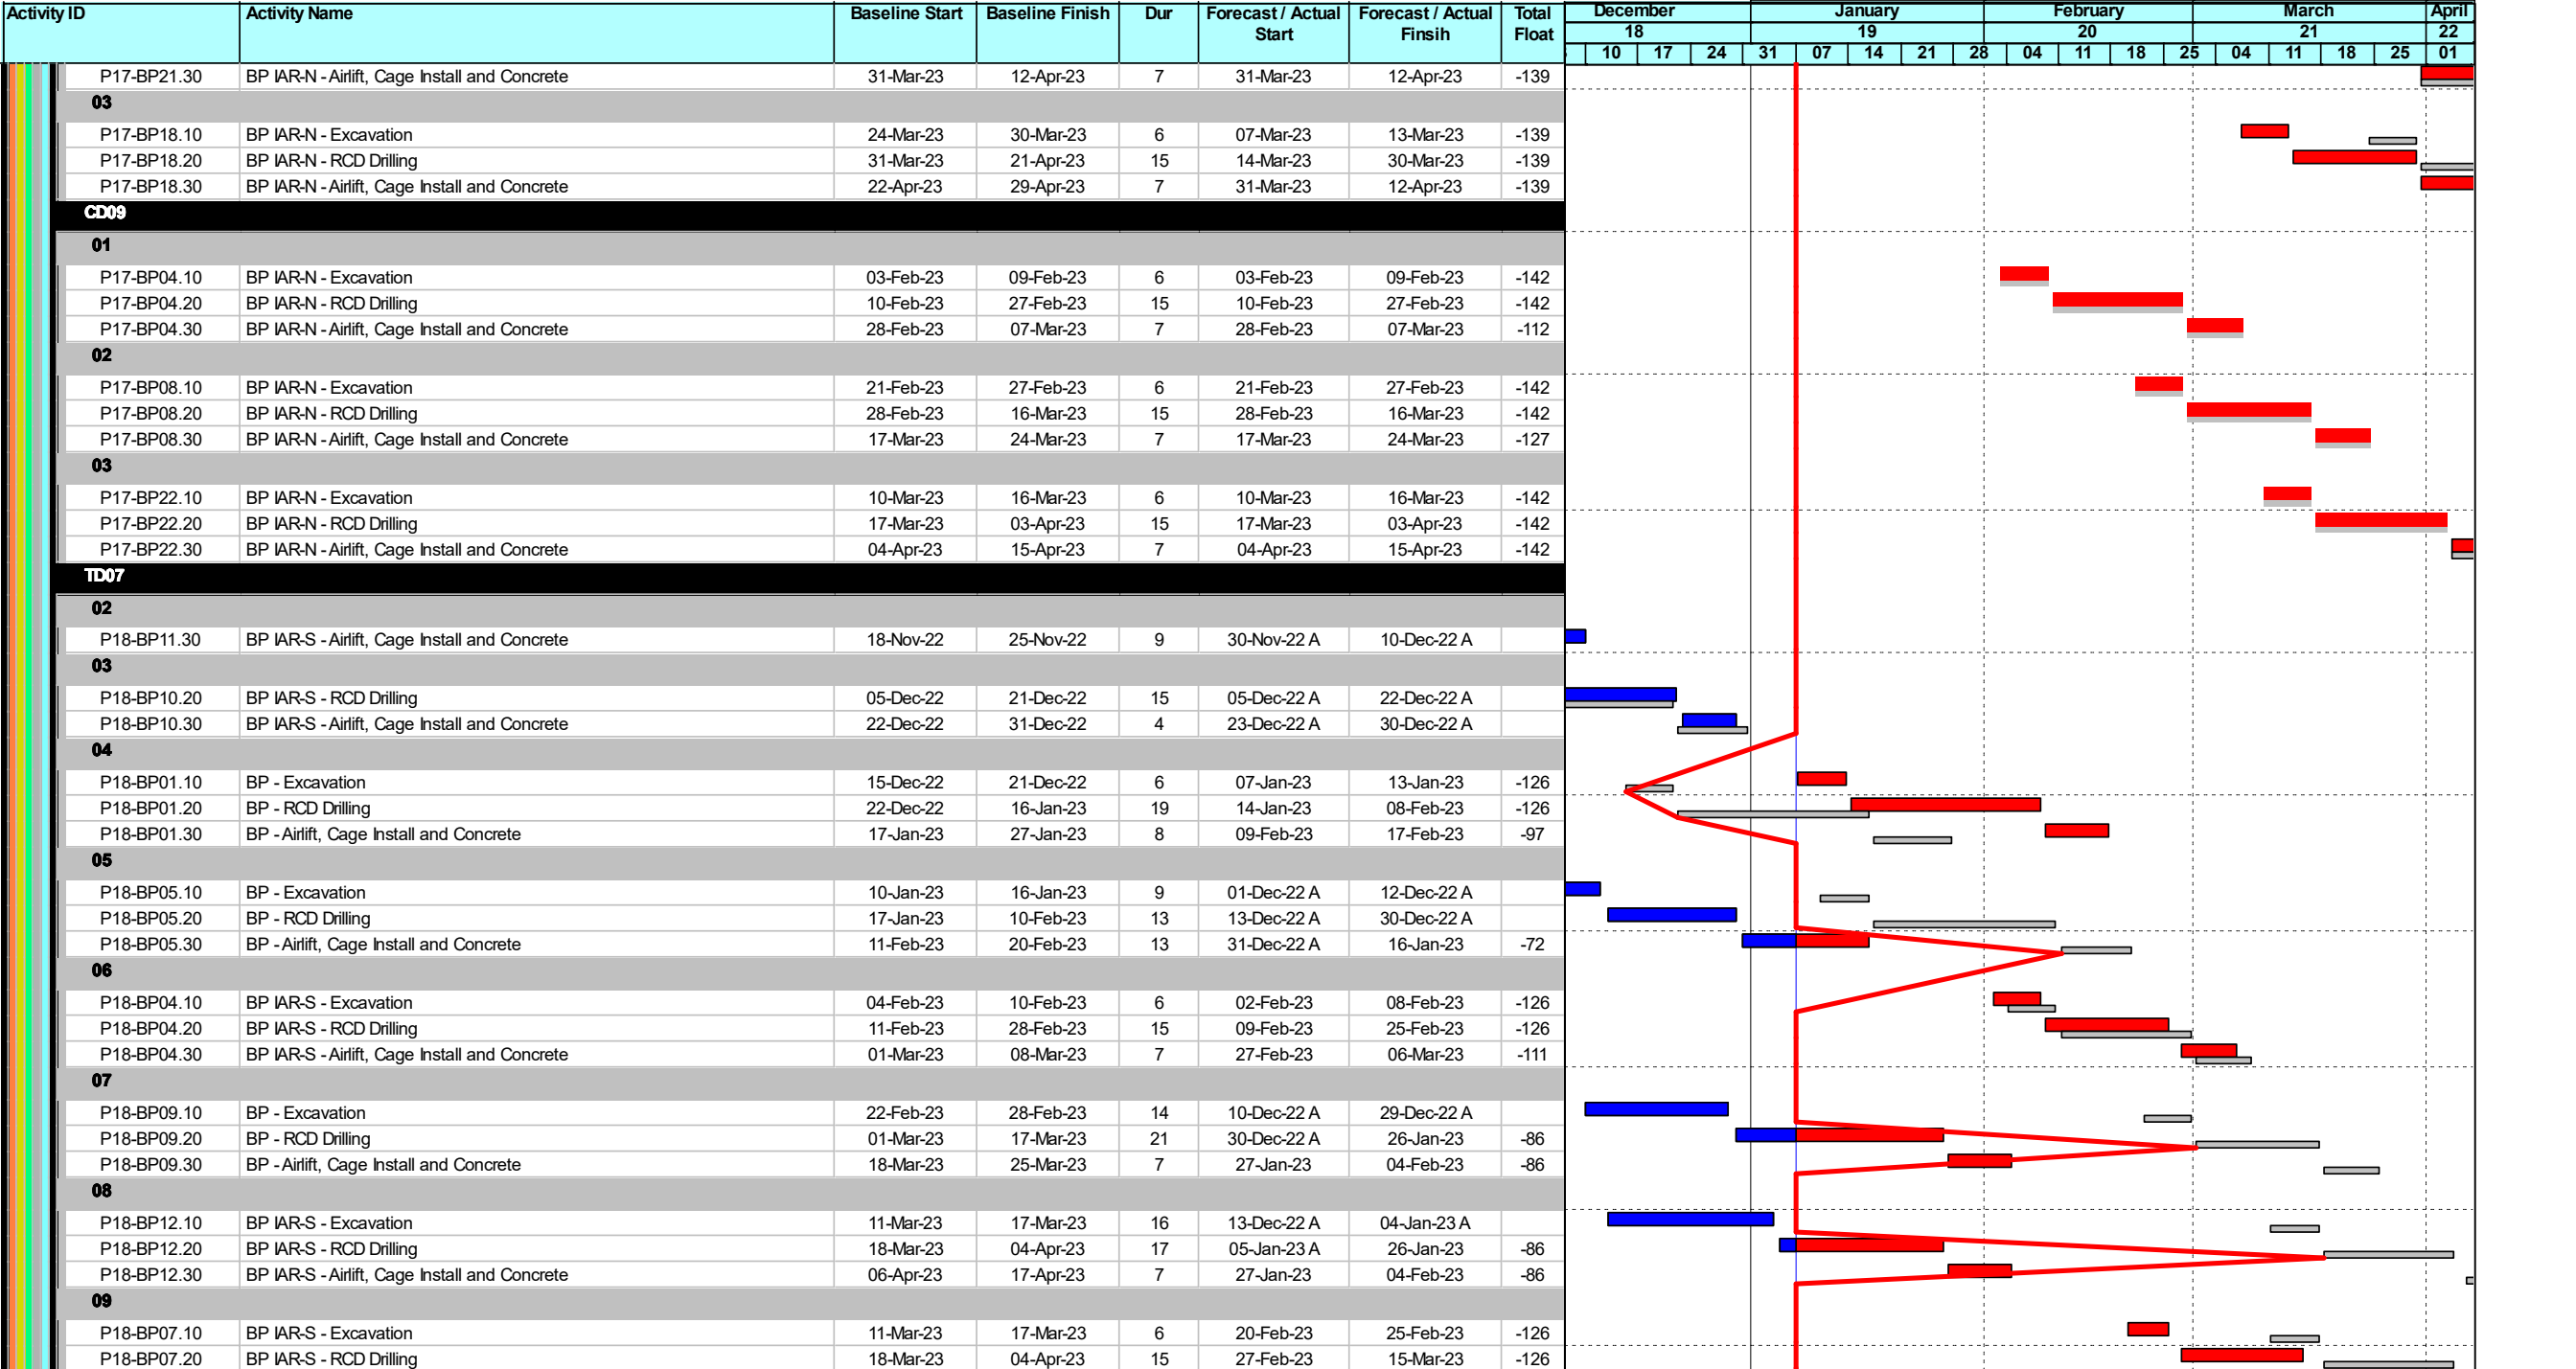

Planned	Planned MS
Critical	Critical MS
Actual	Actual MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 6 January 2023
Based on CMWP Rev.0 (3rd Draft)

	Date	Revision	Checked	Approved
	4-Mar-22	R0	KL	B
	02-Dec-22	R03D	KL	C

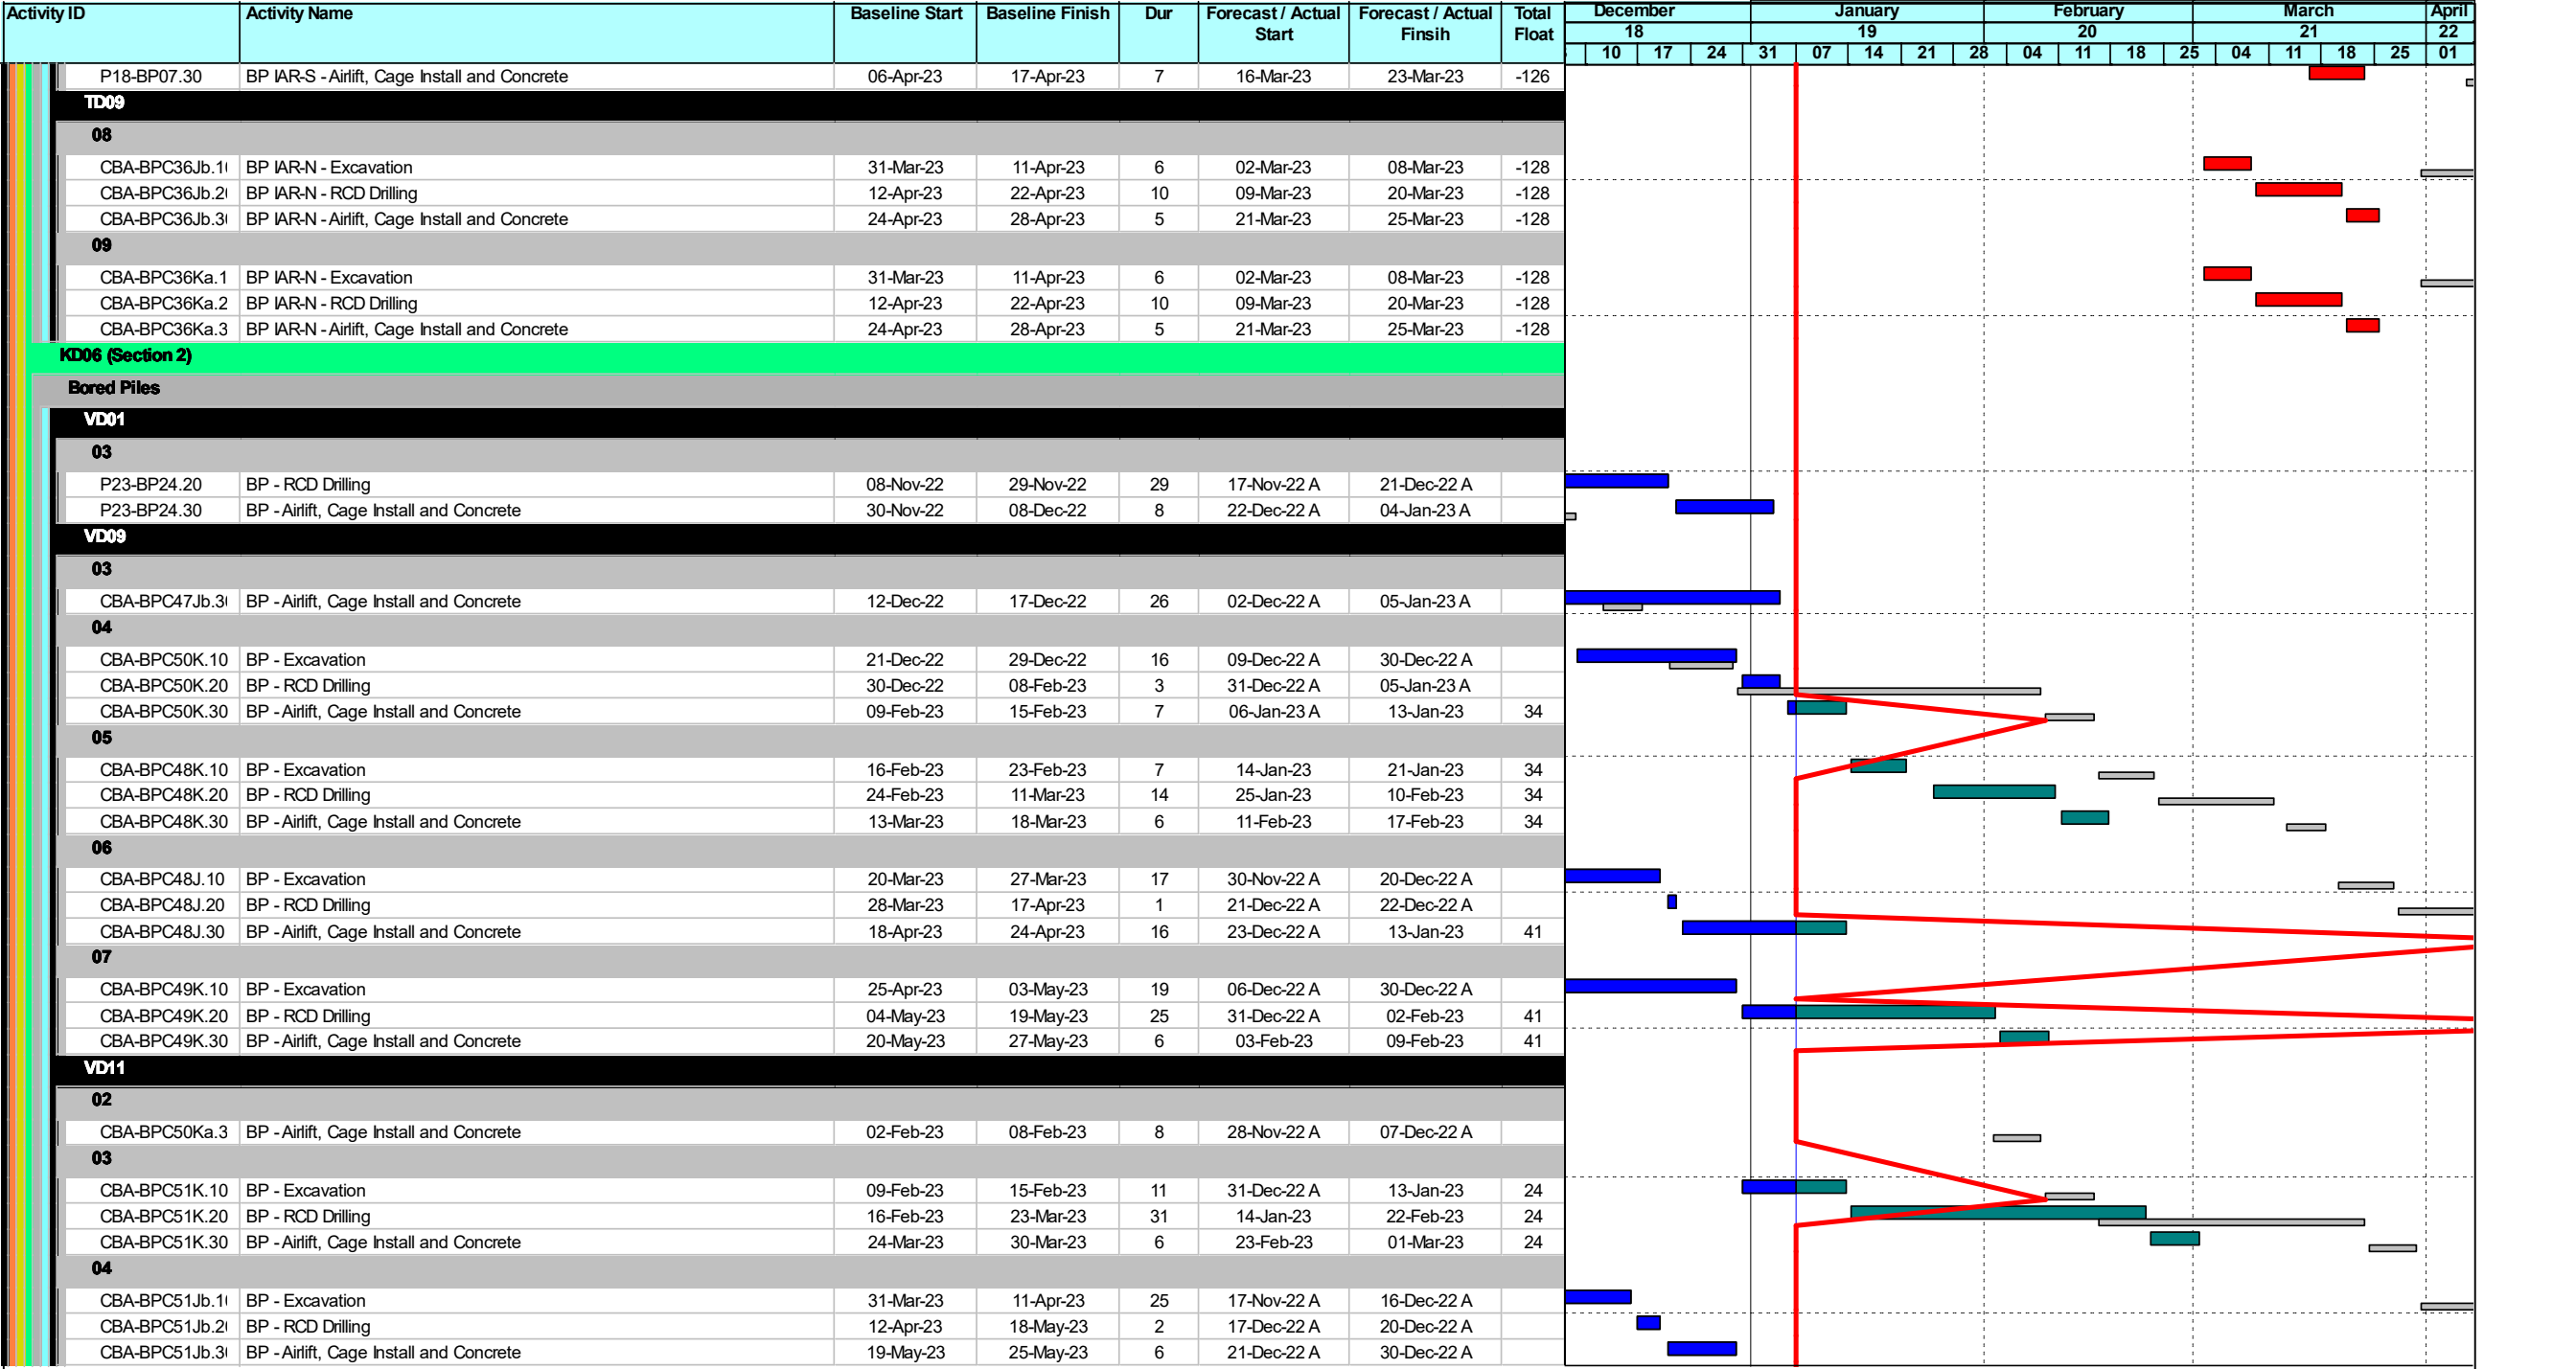

	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 6 January 2023
 Based on CMWP Rev.0 (3rd Draft)


	Date	Revision	Checked	Approved
	4-Mar-22	R0	KL	B
	02-Dec-22	R03D	KL	C

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	December				January				February				March				April
								18				19				20				21				22
								10	17	24	31	07	14	21	28	04	11	18	25	04	11	18	25	01

VD14							
02							
P24&P27-BP38.:	BP - Airlift, Cage Install and Concrete	18-Nov-22	26-Nov-22	11	07-Dec-22 A	20-Dec-22 A	
03							
P24&P27-BP23.:	BP - Excavation	09-Dec-22	15-Dec-22	13	03-Dec-22 A	19-Dec-22 A	
P24&P27-BP23.:	BP - RCD Drilling	16-Dec-22	10-Jan-23	9	20-Dec-22 A	03-Jan-23 A	
P24&P27-BP23.:	BP - Airlift, Cage Install and Concrete	11-Jan-23	19-Jan-23	11	04-Jan-23 A	16-Jan-23	59
04							
P24&P27-BP33.:	BP - Excavation	04-Jan-23	10-Jan-23	6	07-Jan-23	13-Jan-23	-61
P24&P27-BP33.:	BP - RCD Drilling	11-Jan-23	04-Feb-23	19	14-Jan-23	08-Feb-23	-61
P24&P27-BP33.:	BP - Airlift, Cage Install and Concrete	06-Feb-23	14-Feb-23	8	09-Feb-23	17-Feb-23	34
05							
P24&P27-BP15.:	BP - Excavation	30-Jan-23	04-Feb-23	6	02-Feb-23	08-Feb-23	-61
P24&P27-BP15.:	BP - RCD Drilling	06-Feb-23	27-Feb-23	19	09-Feb-23	02-Mar-23	-61
P24&P27-BP15.:	BP - Airlift, Cage Install and Concrete	28-Feb-23	08-Mar-23	8	03-Mar-23	11-Mar-23	15
06							
P24&P27-BP22.:	BP - Excavation	21-Feb-23	27-Feb-23	6	24-Feb-23	02-Mar-23	-61
P24&P27-BP22.:	BP - RCD Drilling	28-Feb-23	21-Mar-23	19	03-Mar-23	24-Mar-23	-61
P24&P27-BP22.:	BP - Airlift, Cage Install and Concrete	22-Mar-23	30-Mar-23	8	25-Mar-23	03-Apr-23	-4
07							
P24&P27-BP16.:	BP - Excavation	15-Mar-23	21-Mar-23	6	18-Mar-23	24-Mar-23	-61
P24&P27-BP16.:	BP - RCD Drilling	22-Mar-23	17-Apr-23	19	25-Mar-23	20-Apr-23	-61

VD15							
03							
P24&P27-BP05.:	BP - Airlift, Cage Install and Concrete	23-Dec-22	04-Jan-23	10	03-Dec-22 A	15-Dec-22 A	
05							
P24&P27-BP29.:	BP - Excavation	20-Jan-23	30-Jan-23	6	14-Feb-23	20-Feb-23	-53
P24&P27-BP29.:	BP - RCD Drilling	31-Jan-23	21-Feb-23	19	21-Feb-23	14-Mar-23	-53
P24&P27-BP29.:	BP - Airlift, Cage Install and Concrete	22-Feb-23	02-Mar-23	8	15-Mar-23	23-Mar-23	5
06							
P24&P27-BP03.:	BP - Excavation	15-Feb-23	21-Feb-23	6	08-Mar-23	14-Mar-23	-53
P24&P27-BP03.:	BP - RCD Drilling	22-Feb-23	27-Mar-23	29	15-Mar-23	21-Apr-23	-53
08							
P24&P27-BP04.:	BP - Excavation	28-Apr-23	05-May-23	22	16-Dec-22 A	13-Jan-23	24
P24&P27-BP04.:	BP - RCD Drilling	06-May-23	09-Jun-23	29	14-Jan-23	20-Feb-23	24
P24&P27-BP04.:	BP - Airlift, Cage Install and Concrete	10-Jun-23	19-Jun-23	8	21-Feb-23	01-Mar-23	24

CD01							
02							
P23-BP14.10	BP - Excavation	03-Dec-22	09-Dec-22	6	07-Jan-23	13-Jan-23	-73
P23-BP14.20	BP - RCD Drilling	10-Dec-22	04-Jan-23	19	14-Jan-23	08-Feb-23	-73
P23-BP14.30	BP - Airlift, Cage Install and Concrete	05-Jan-23	13-Jan-23	8	09-Feb-23	17-Feb-23	34
04							
P23-BP09.10	BP - Excavation	20-Jan-23	30-Jan-23	6	24-Feb-23	02-Mar-23	-73
P23-BP09.20	BP - RCD Drilling	31-Jan-23	21-Feb-23	19	03-Mar-23	24-Mar-23	-73
P23-BP09.30	BP - Airlift, Cage Install and Concrete	22-Feb-23	02-Mar-23	8	25-Mar-23	03-Apr-23	-4
05							
P23-BP26.10	BP - Excavation	15-Feb-23	21-Feb-23	6	18-Mar-23	24-Mar-23	-73

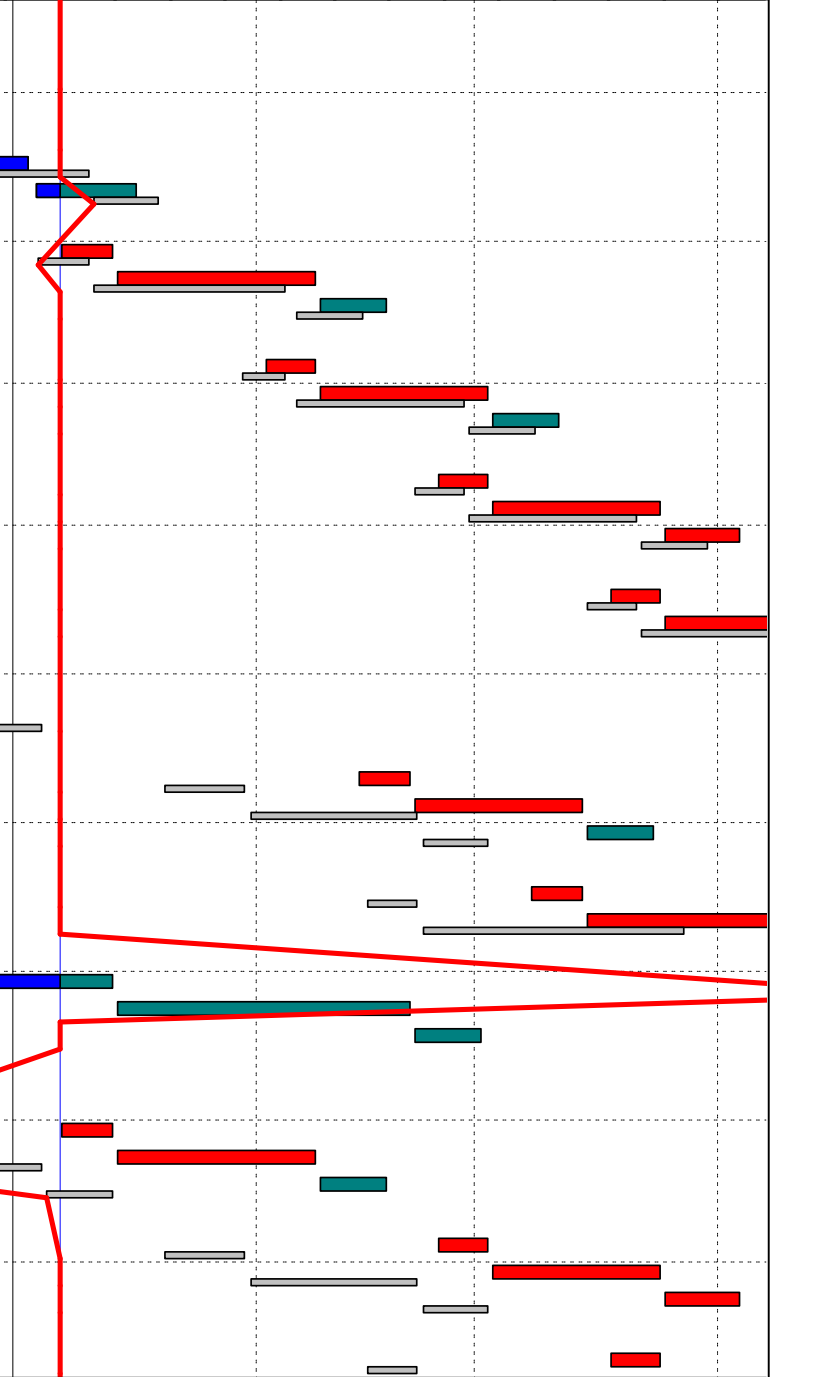


	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 6 January 2023
Based on CMWP Rev.0 (3rd Draft)




Date	Revision	Checked	Approved
4-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C

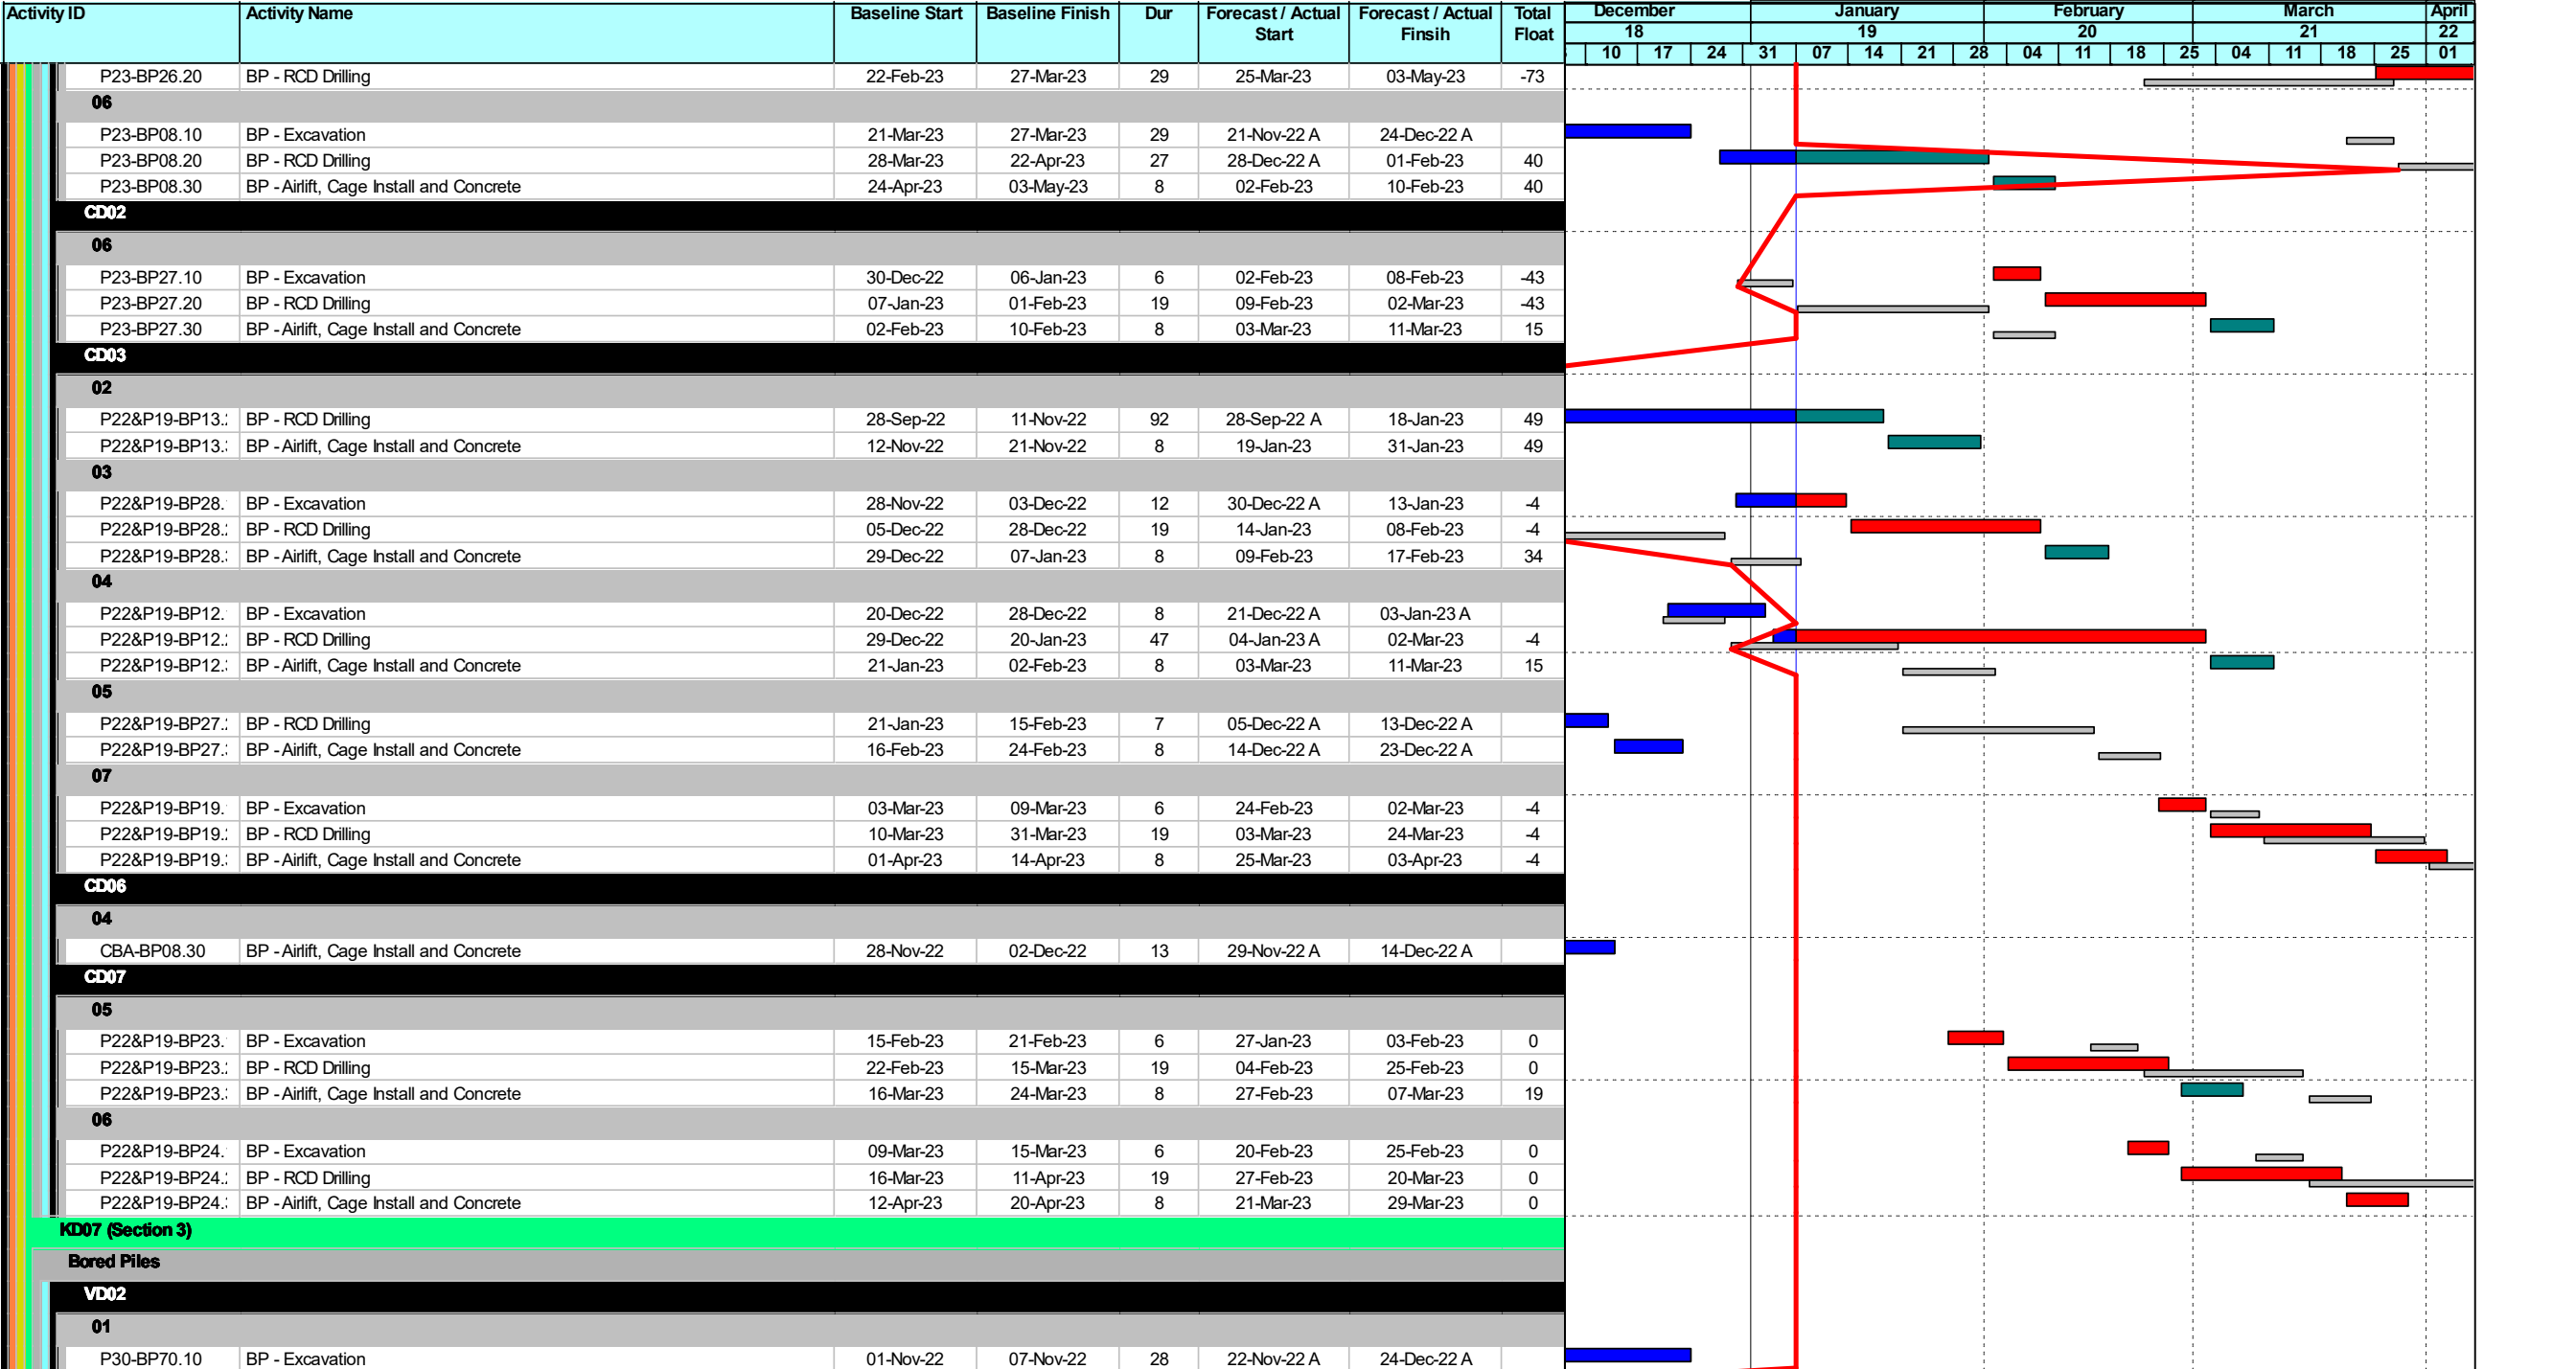





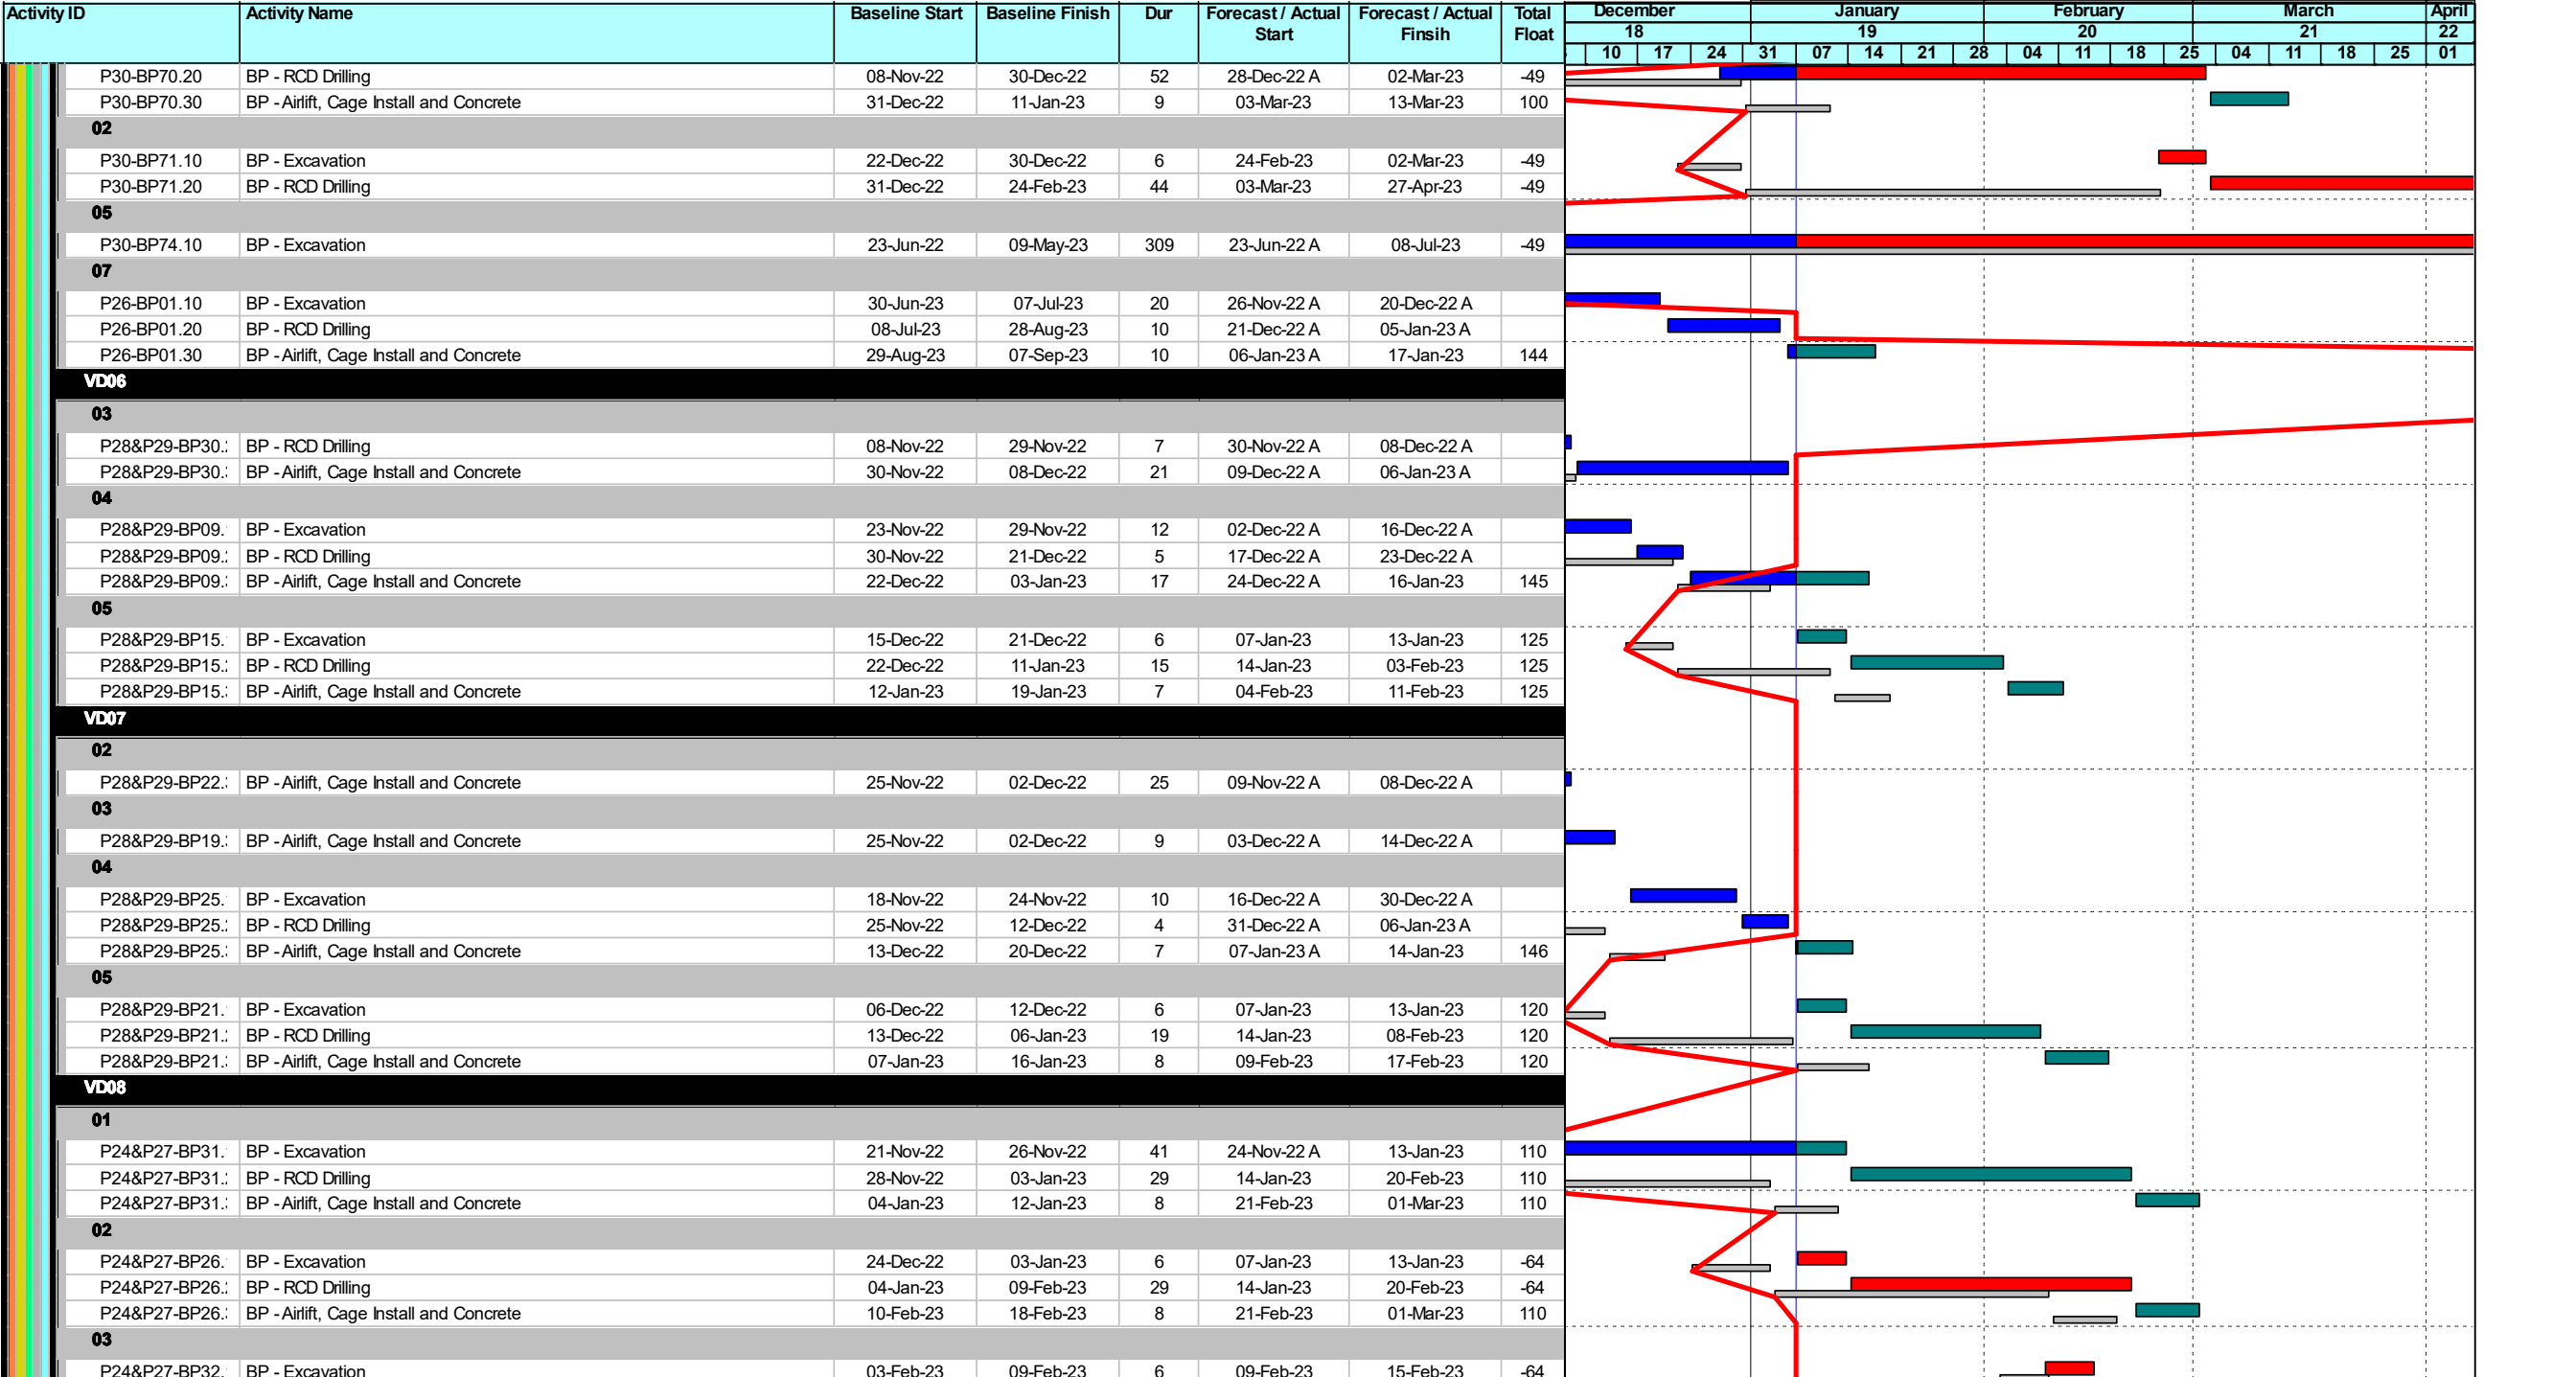

■	Planned	◆	Planned MS
■	Critical	◆	Critical MS
■	Actual	◆	Actual MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 6 January 2023
 Based on CMWP Rev.0 (3rd Draft)

		Date	Revision	Checked	Approved
		4-Mar-22	R0	KL	B
		02-Dec-22	R03D	KL	C










	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS

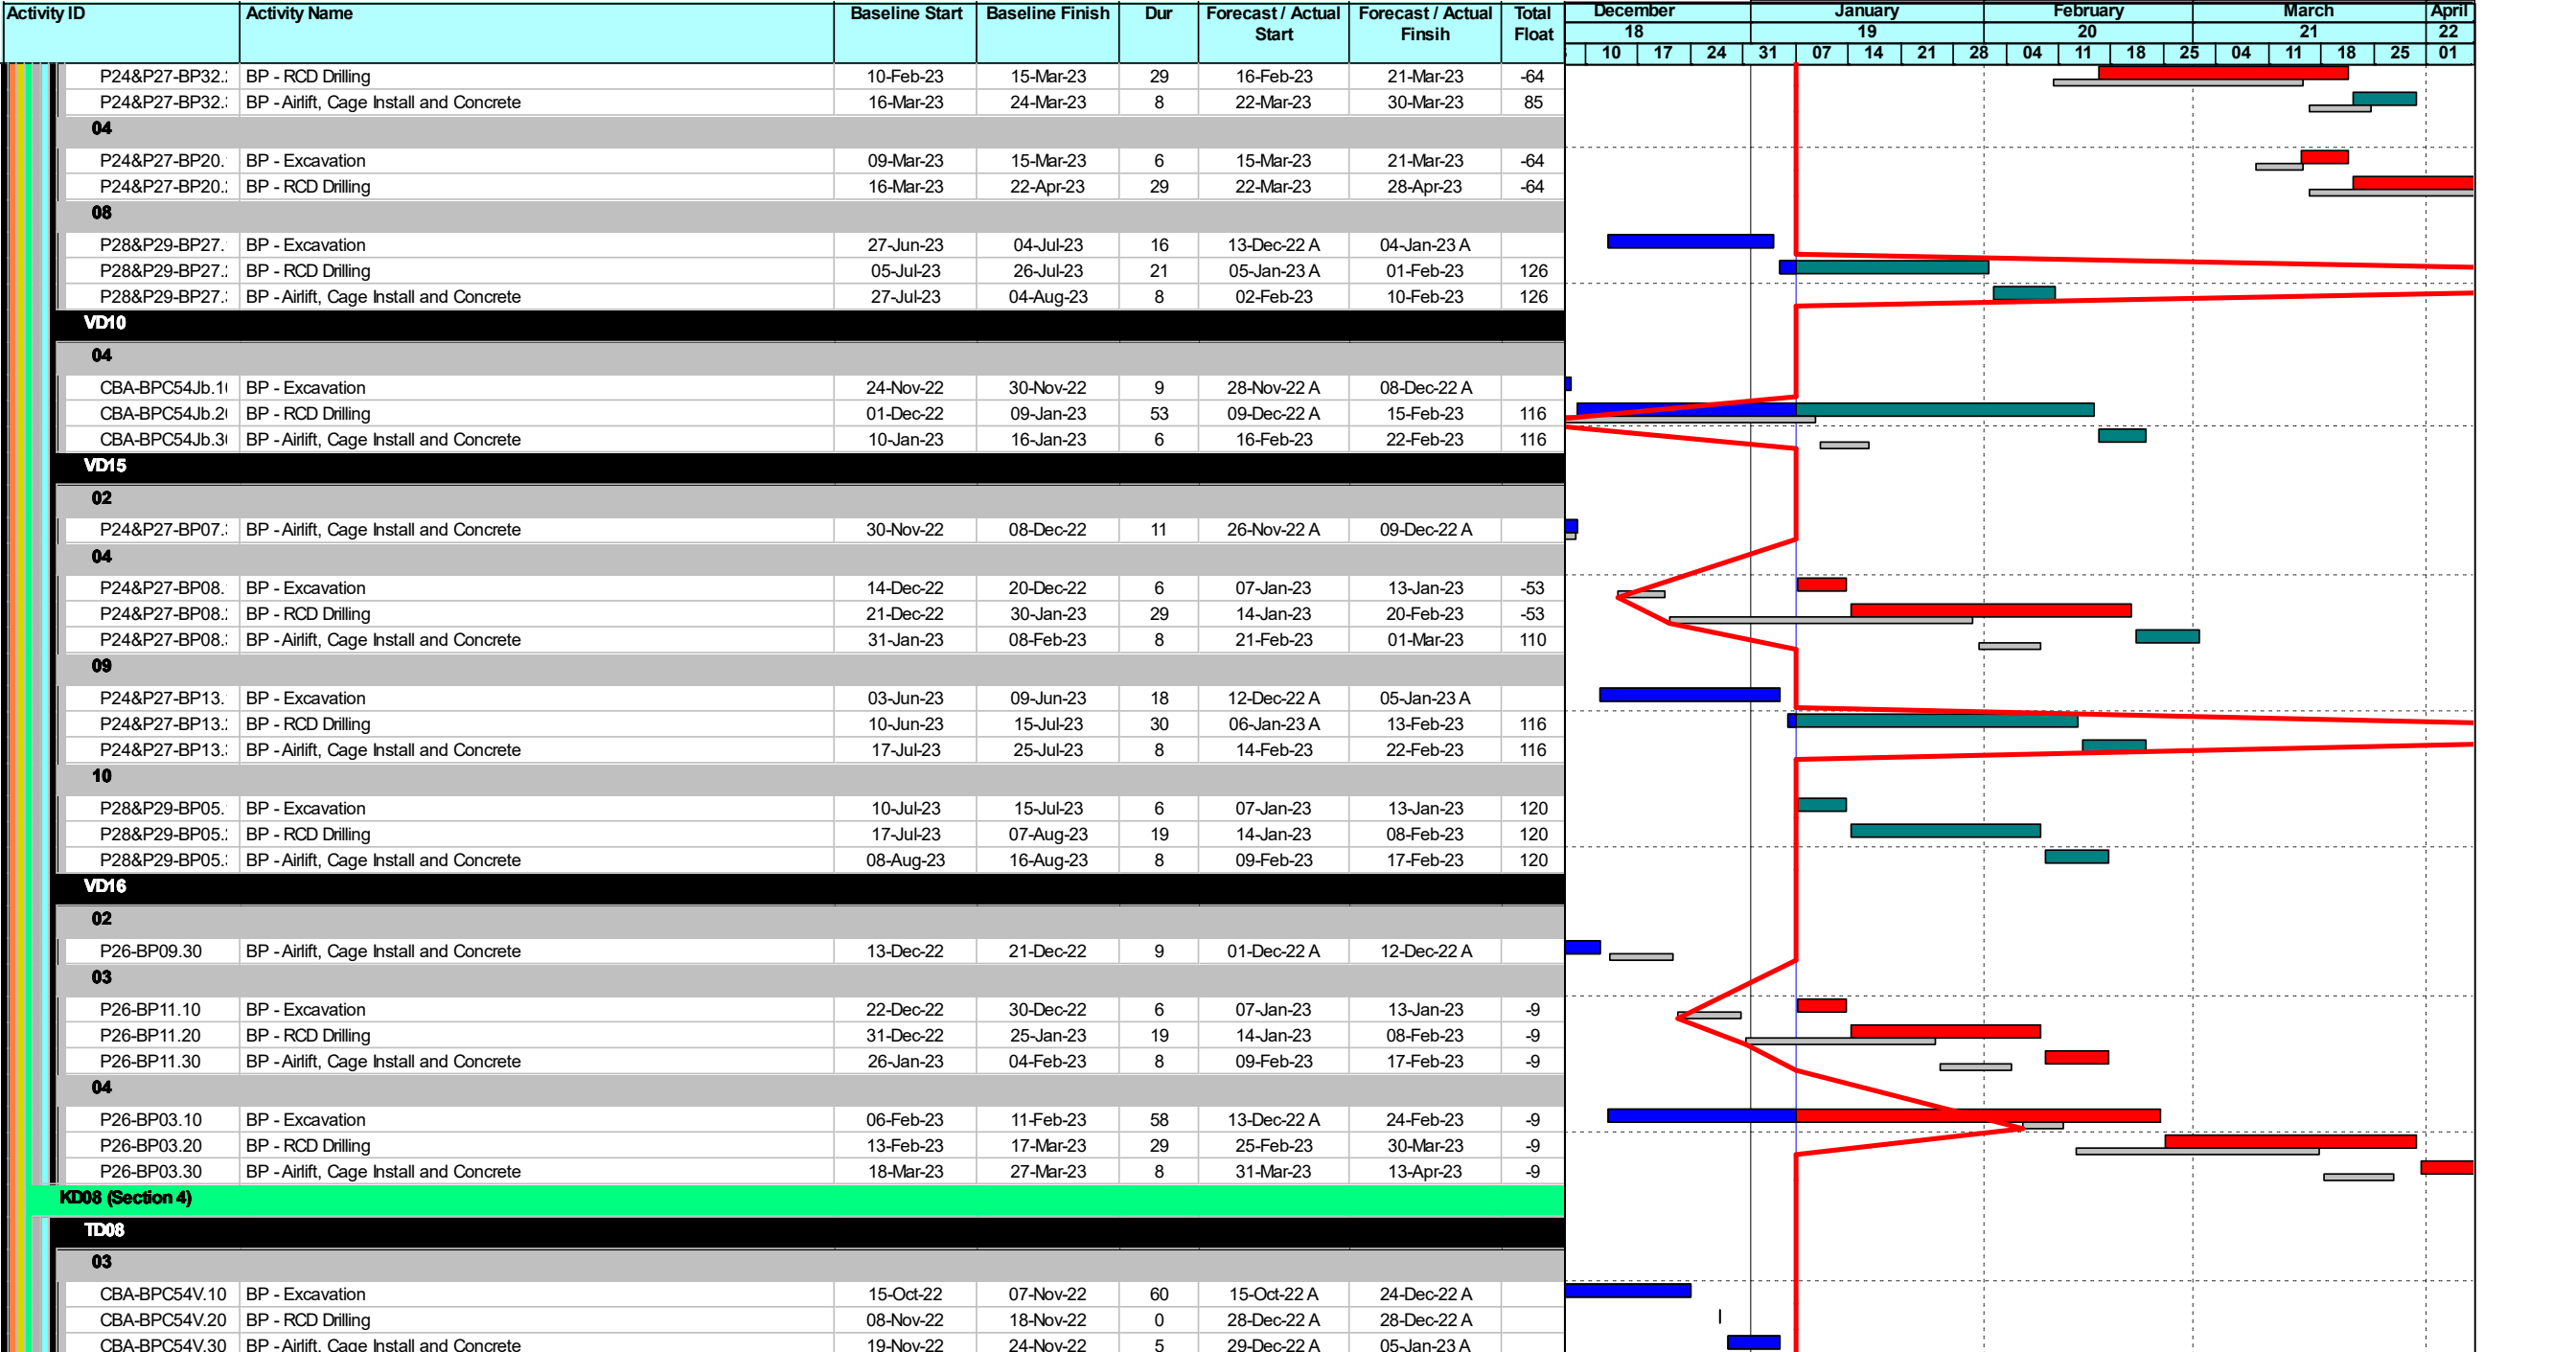West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 6 January 2023
Based on CMWP Rev.0 (3rd Draft)



Date	Revision	Checked	Approved
4-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C



	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS


West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 6 January 2023
Based on CMWP Rev.0 (3rd Draft)



Date	Revision	Checked	Approved
4-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	December 18				January 19				February 20				March 21				April 22
								10	17	24	31	07	14	21	28	04	11	18	25	04	11	18	25	01

Bored Piles							
VD01							
04							
P26-BP12.10	BP - Excavation	01-Nov-22	07-Nov-22	37	04-Nov-22 A	17-Dec-22 A	
P26-BP12.20	BP - RCD Drilling	08-Nov-22	10-Dec-22	43	19-Dec-22 A	13-Feb-23	-25
P26-BP12.30	BP - Airlift, Cage Install and Concrete	12-Dec-22	20-Dec-22	8	14-Feb-23	22-Feb-23	13
06							
P26-BP14.10	BP - Excavation	01-Apr-23	12-Apr-23	6	01-Apr-23	12-Apr-23	-52
VD03							
01							
P30-BP62.30	BP - Airlift, Cage Install and Concrete	25-Nov-22	02-Dec-22	11	30-Nov-22 A	13-Dec-22 A	
02							
P30-BP34.10	BP - Excavation	01-Dec-22	07-Dec-22	6	07-Jan-23	13-Jan-23	-62
P30-BP34.20	BP - RCD Drilling	08-Dec-22	24-Dec-22	15	14-Jan-23	03-Feb-23	-62
P30-BP34.30	BP - Airlift, Cage Install and Concrete	28-Dec-22	05-Jan-23	7	04-Feb-23	11-Feb-23	22
03							
P30-BP52.10	BP - Excavation	19-Dec-22	24-Dec-22	6	27-Jan-23	03-Feb-23	-62
P30-BP52.20	BP - RCD Drilling	28-Dec-22	19-Jan-23	19	04-Feb-23	25-Feb-23	-62
P30-BP52.30	BP - Airlift, Cage Install and Concrete	20-Jan-23	01-Feb-23	8	27-Feb-23	07-Mar-23	2
04							
P30-BP46.10	BP - Excavation	13-Jan-23	19-Jan-23	6	20-Feb-23	25-Feb-23	-62
P30-BP46.20	BP - RCD Drilling	20-Jan-23	09-Feb-23	15	27-Feb-23	15-Mar-23	-62
P30-BP46.30	BP - Airlift, Cage Install and Concrete	10-Feb-23	17-Feb-23	7	16-Mar-23	23-Mar-23	-12
05							
P30-BP47.10	BP - Excavation	03-Feb-23	09-Feb-23	6	09-Mar-23	15-Mar-23	-62
P30-BP47.20	BP - RCD Drilling	10-Feb-23	27-Feb-23	15	16-Mar-23	01-Apr-23	-62
P30-BP47.30	BP - Airlift, Cage Install and Concrete	28-Feb-23	07-Mar-23	7	03-Apr-23	14-Apr-23	-27
06							
P30-BP40.10	BP - Excavation	21-Feb-23	27-Feb-23	6	27-Mar-23	01-Apr-23	-62
P30-BP40.20	BP - RCD Drilling	28-Feb-23	16-Mar-23	15	03-Apr-23	24-Apr-23	-62
VD04							
02							
P30-BP19.30	BP - Airlift, Cage Install and Concrete	12-Dec-22	20-Dec-22	14	07-Dec-22 A	23-Dec-22 A	
03							
P30-BP29.20	BP - RCD Drilling	16-Dec-22	05-Jan-23	16	05-Dec-22 A	23-Dec-22 A	
P30-BP29.30	BP - Airlift, Cage Install and Concrete	06-Jan-23	13-Jan-23	8	24-Dec-22 A	06-Jan-23 A	
04							
P30-BP25.10	BP - Excavation	29-Dec-22	05-Jan-23	15	24-Dec-22 A	13-Jan-23	-61
P30-BP25.20	BP - RCD Drilling	06-Jan-23	31-Jan-23	19	14-Jan-23	08-Feb-23	-61
P30-BP25.30	BP - Airlift, Cage Install and Concrete	01-Feb-23	09-Feb-23	8	09-Feb-23	17-Feb-23	17
05							
P30-BP36.10	BP - Excavation	21-Jan-23	31-Jan-23	6	02-Feb-23	08-Feb-23	-61
P30-BP36.20	BP - RCD Drilling	01-Feb-23	17-Feb-23	15	09-Feb-23	25-Feb-23	-61
P30-BP36.30	BP - Airlift, Cage Install and Concrete	18-Feb-23	25-Feb-23	7	27-Feb-23	06-Mar-23	3
06							
P30-BP31.10	BP - Excavation	11-Feb-23	17-Feb-23	6	20-Feb-23	25-Feb-23	-61

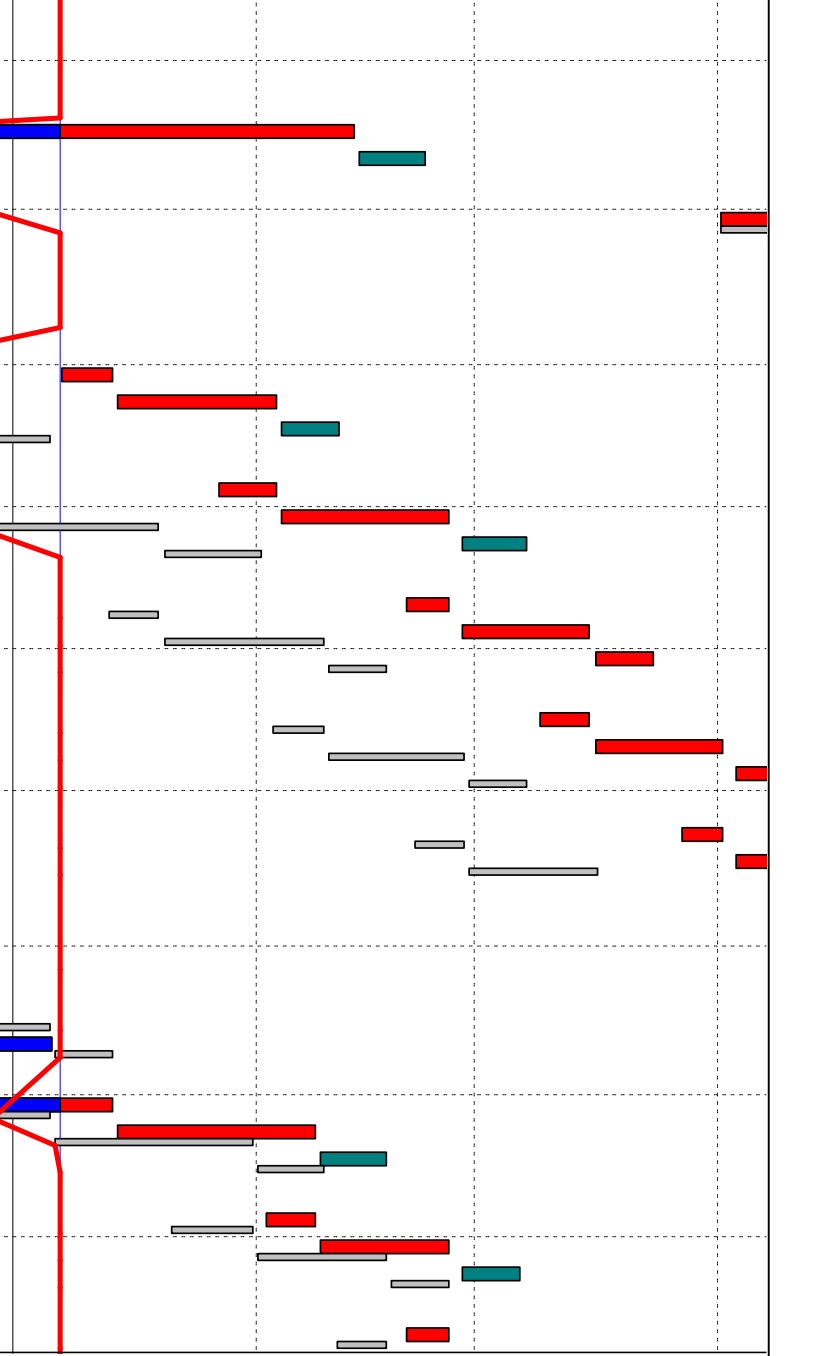


ID: 2BC-202230106_w TBC
 Data Date: 07-Jan-23
 Print Date: 11-Jan-23_10:49
 Page 9 of 16




	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 6 January 2023
Based on CMWP Rev.0 (3rd Draft)

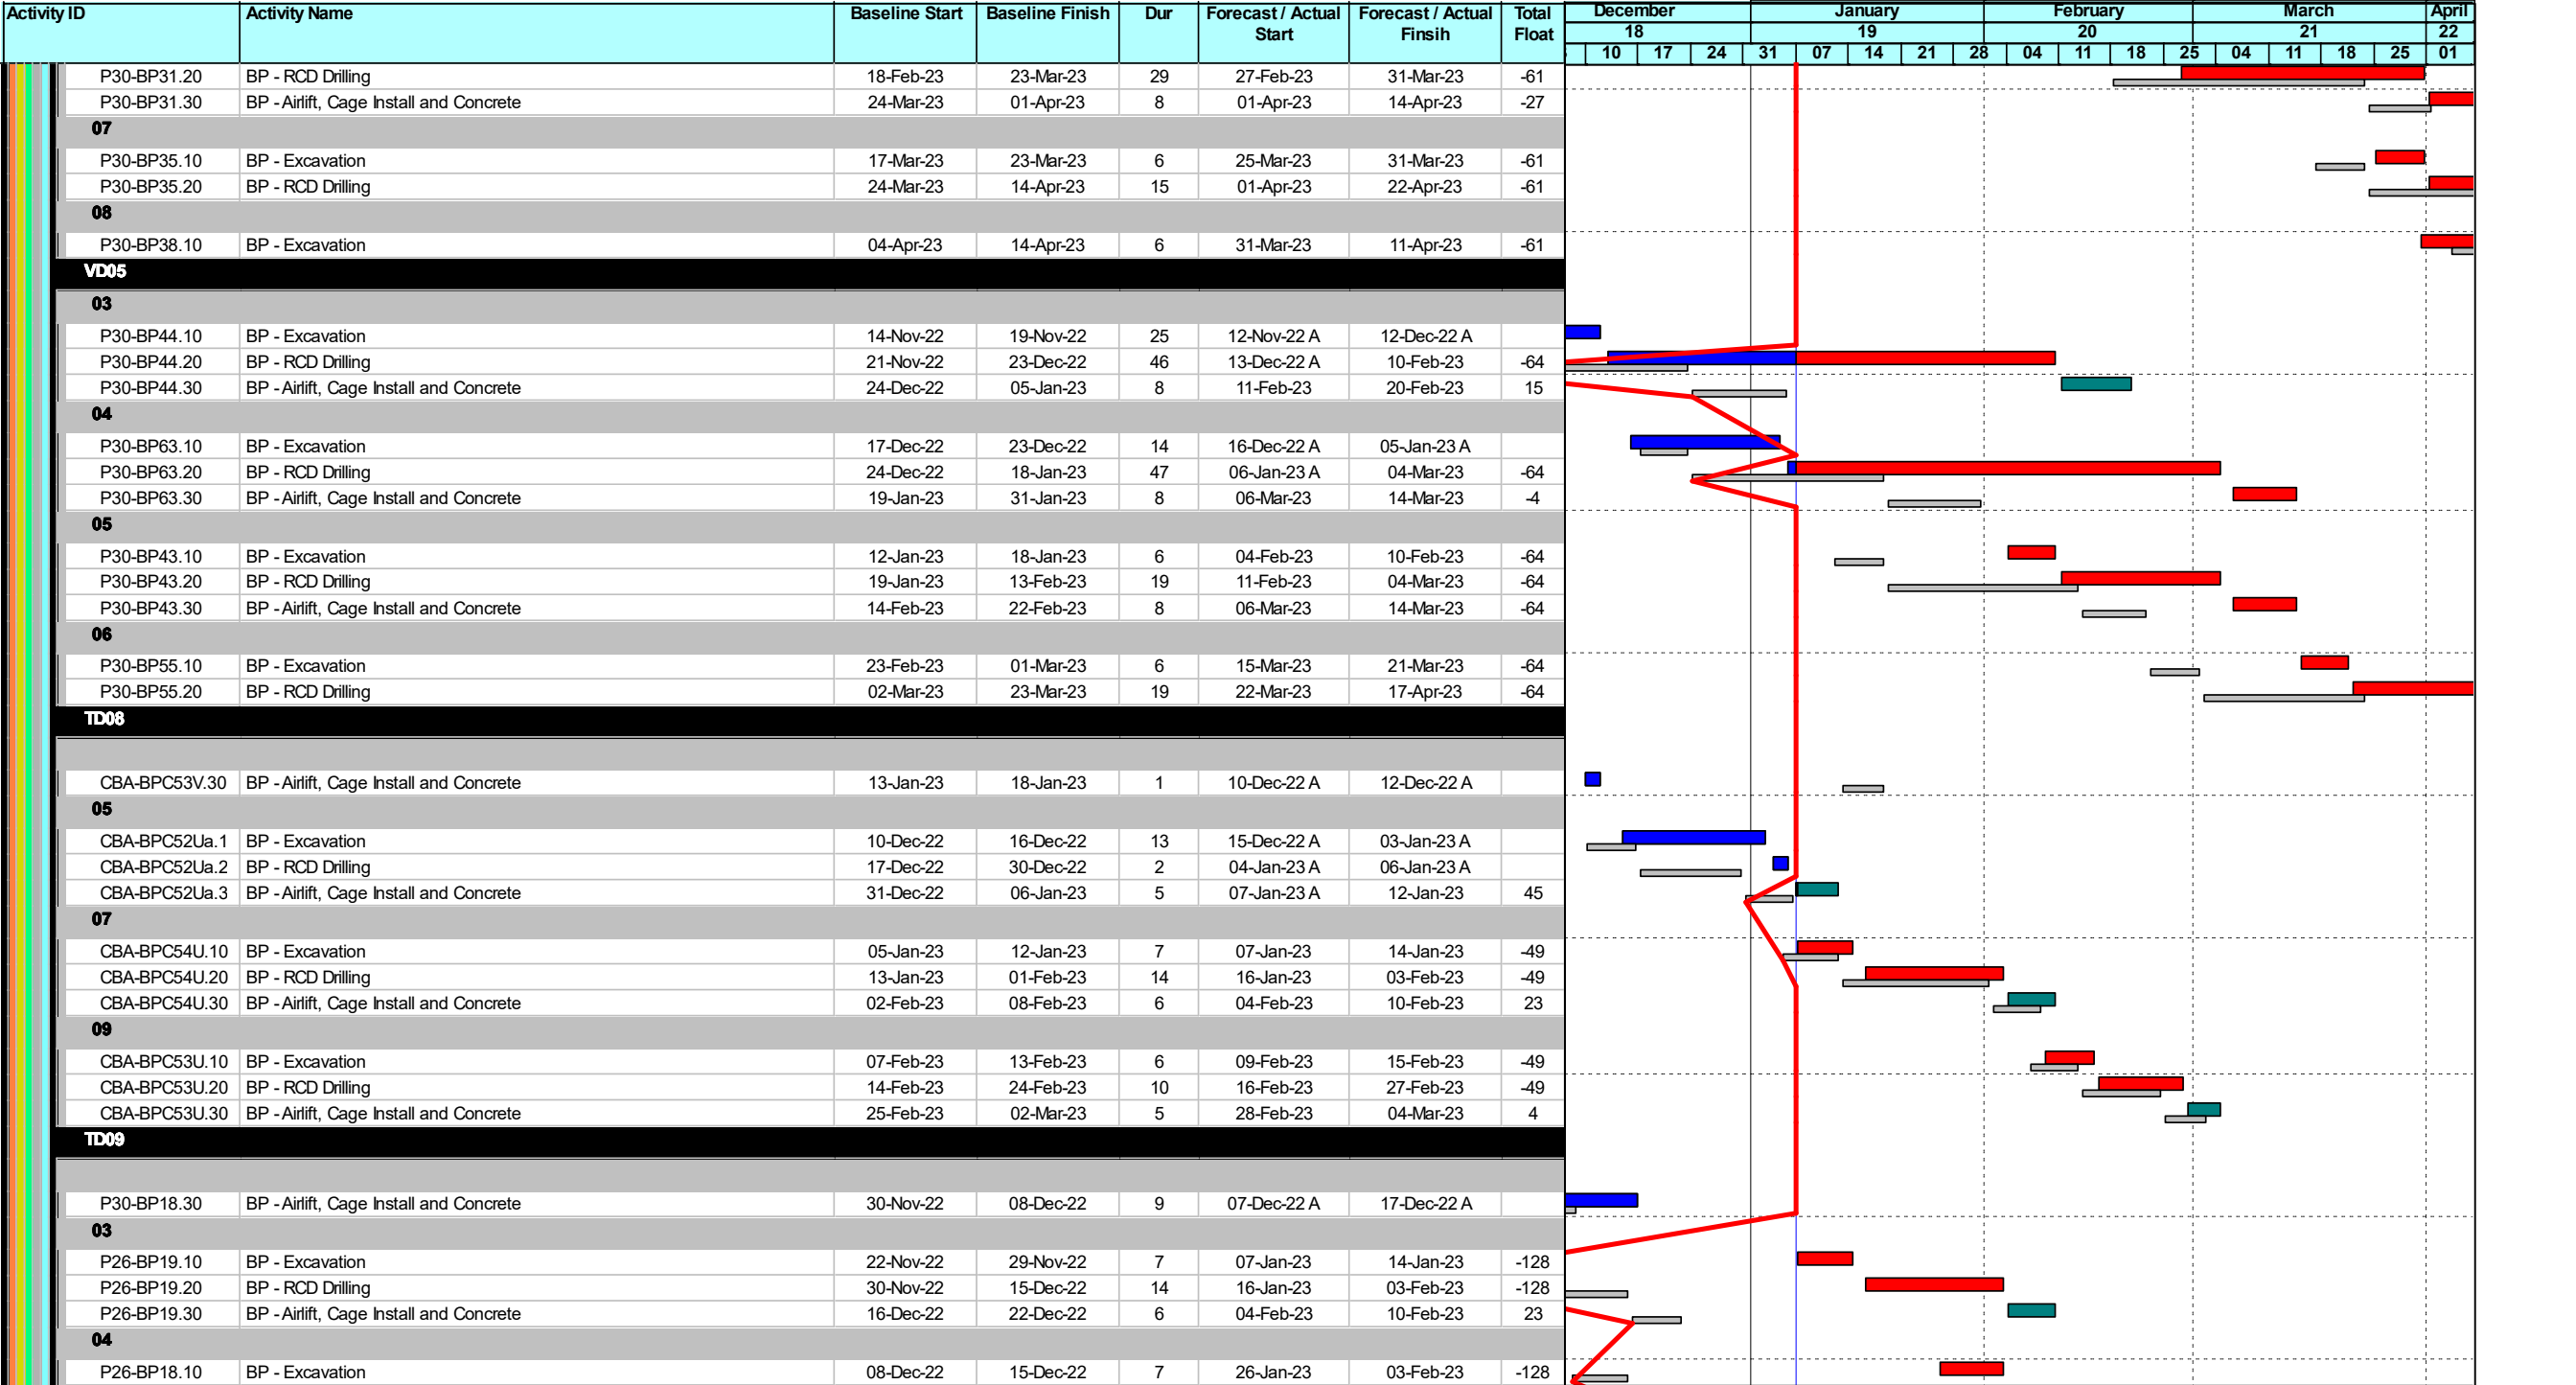


Date	Revision	Checked	Approved
4-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C



	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 6 January 2023
Based on CMWP Rev.0 (3rd Draft)

	Date	Revision	Checked	Approved
	4-Mar-22	R0	KL	B
	02-Dec-22	R03D	KL	C

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finish	Total Float	December 18				January 19				February 20				March 21				April 22			
								10	17	24	31	07	14	21	28	04	11	18	25	04	11	18	25	01			
P26-BP18.20	BP - RCD Drilling	16-Dec-22	04-Jan-23	14	04-Feb-23	20-Feb-23	-128																				
P26-BP18.30	BP - Airlift, Cage Install and Concrete	05-Jan-23	11-Jan-23	6	21-Feb-23	27-Feb-23	9																				
05																											
P26-BP16.10	BP - Excavation	24-Dec-22	04-Jan-23	7	13-Feb-23	20-Feb-23	-128																				
P26-BP16.20	BP - RCD Drilling	05-Jan-23	20-Jan-23	14	21-Feb-23	08-Mar-23	-128																				
P26-BP16.30	BP - Airlift, Cage Install and Concrete	21-Jan-23	31-Jan-23	6	09-Mar-23	15-Mar-23	-5																				
06																											
P26-BP15.10	BP - Excavation	14-Jan-23	20-Jan-23	6	02-Mar-23	08-Mar-23	-128																				
P26-BP15.20	BP - RCD Drilling	21-Jan-23	01-Mar-23	31	09-Mar-23	18-Apr-23	-128																				
07																											
P26-BP17.10	BP - Excavation	23-Feb-23	01-Mar-23	6	02-Mar-23	08-Mar-23	-128																				
P26-BP17.20	BP - RCD Drilling	02-Mar-23	11-Apr-23	31	09-Mar-23	18-Apr-23	-128																				

KD09 (Section 5)

Bored Piles

VD01

05

P23-BP34.10

P23-BP34.20

P23-BP34.30

CD01

03

P23-BP35.10

P23-BP35.20

P23-BP35.30

CD02

03

P23-BP47.20

P23-BP47.30

04

P23-BP38.10

P23-BP38.20

P23-BP38.30

05

P23-BP49.20

P23-BP49.30

07

P23-BP48.10

P23-BP48.20

08

P23-BP37.10

09

P23-BP36.10

TD01

02

P18-BP57.10

P18-BP57.20


ID: 2BC-202230106_w TBC
 Data Date: 07-Jan-23
 Print Date: 11-Jan-23_10:49
 Page 11 of 16

	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 6 January 2023
Based on CMWP Rev.0 (3rd Draft)



Date	Revision	Checked	Approved
4-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C

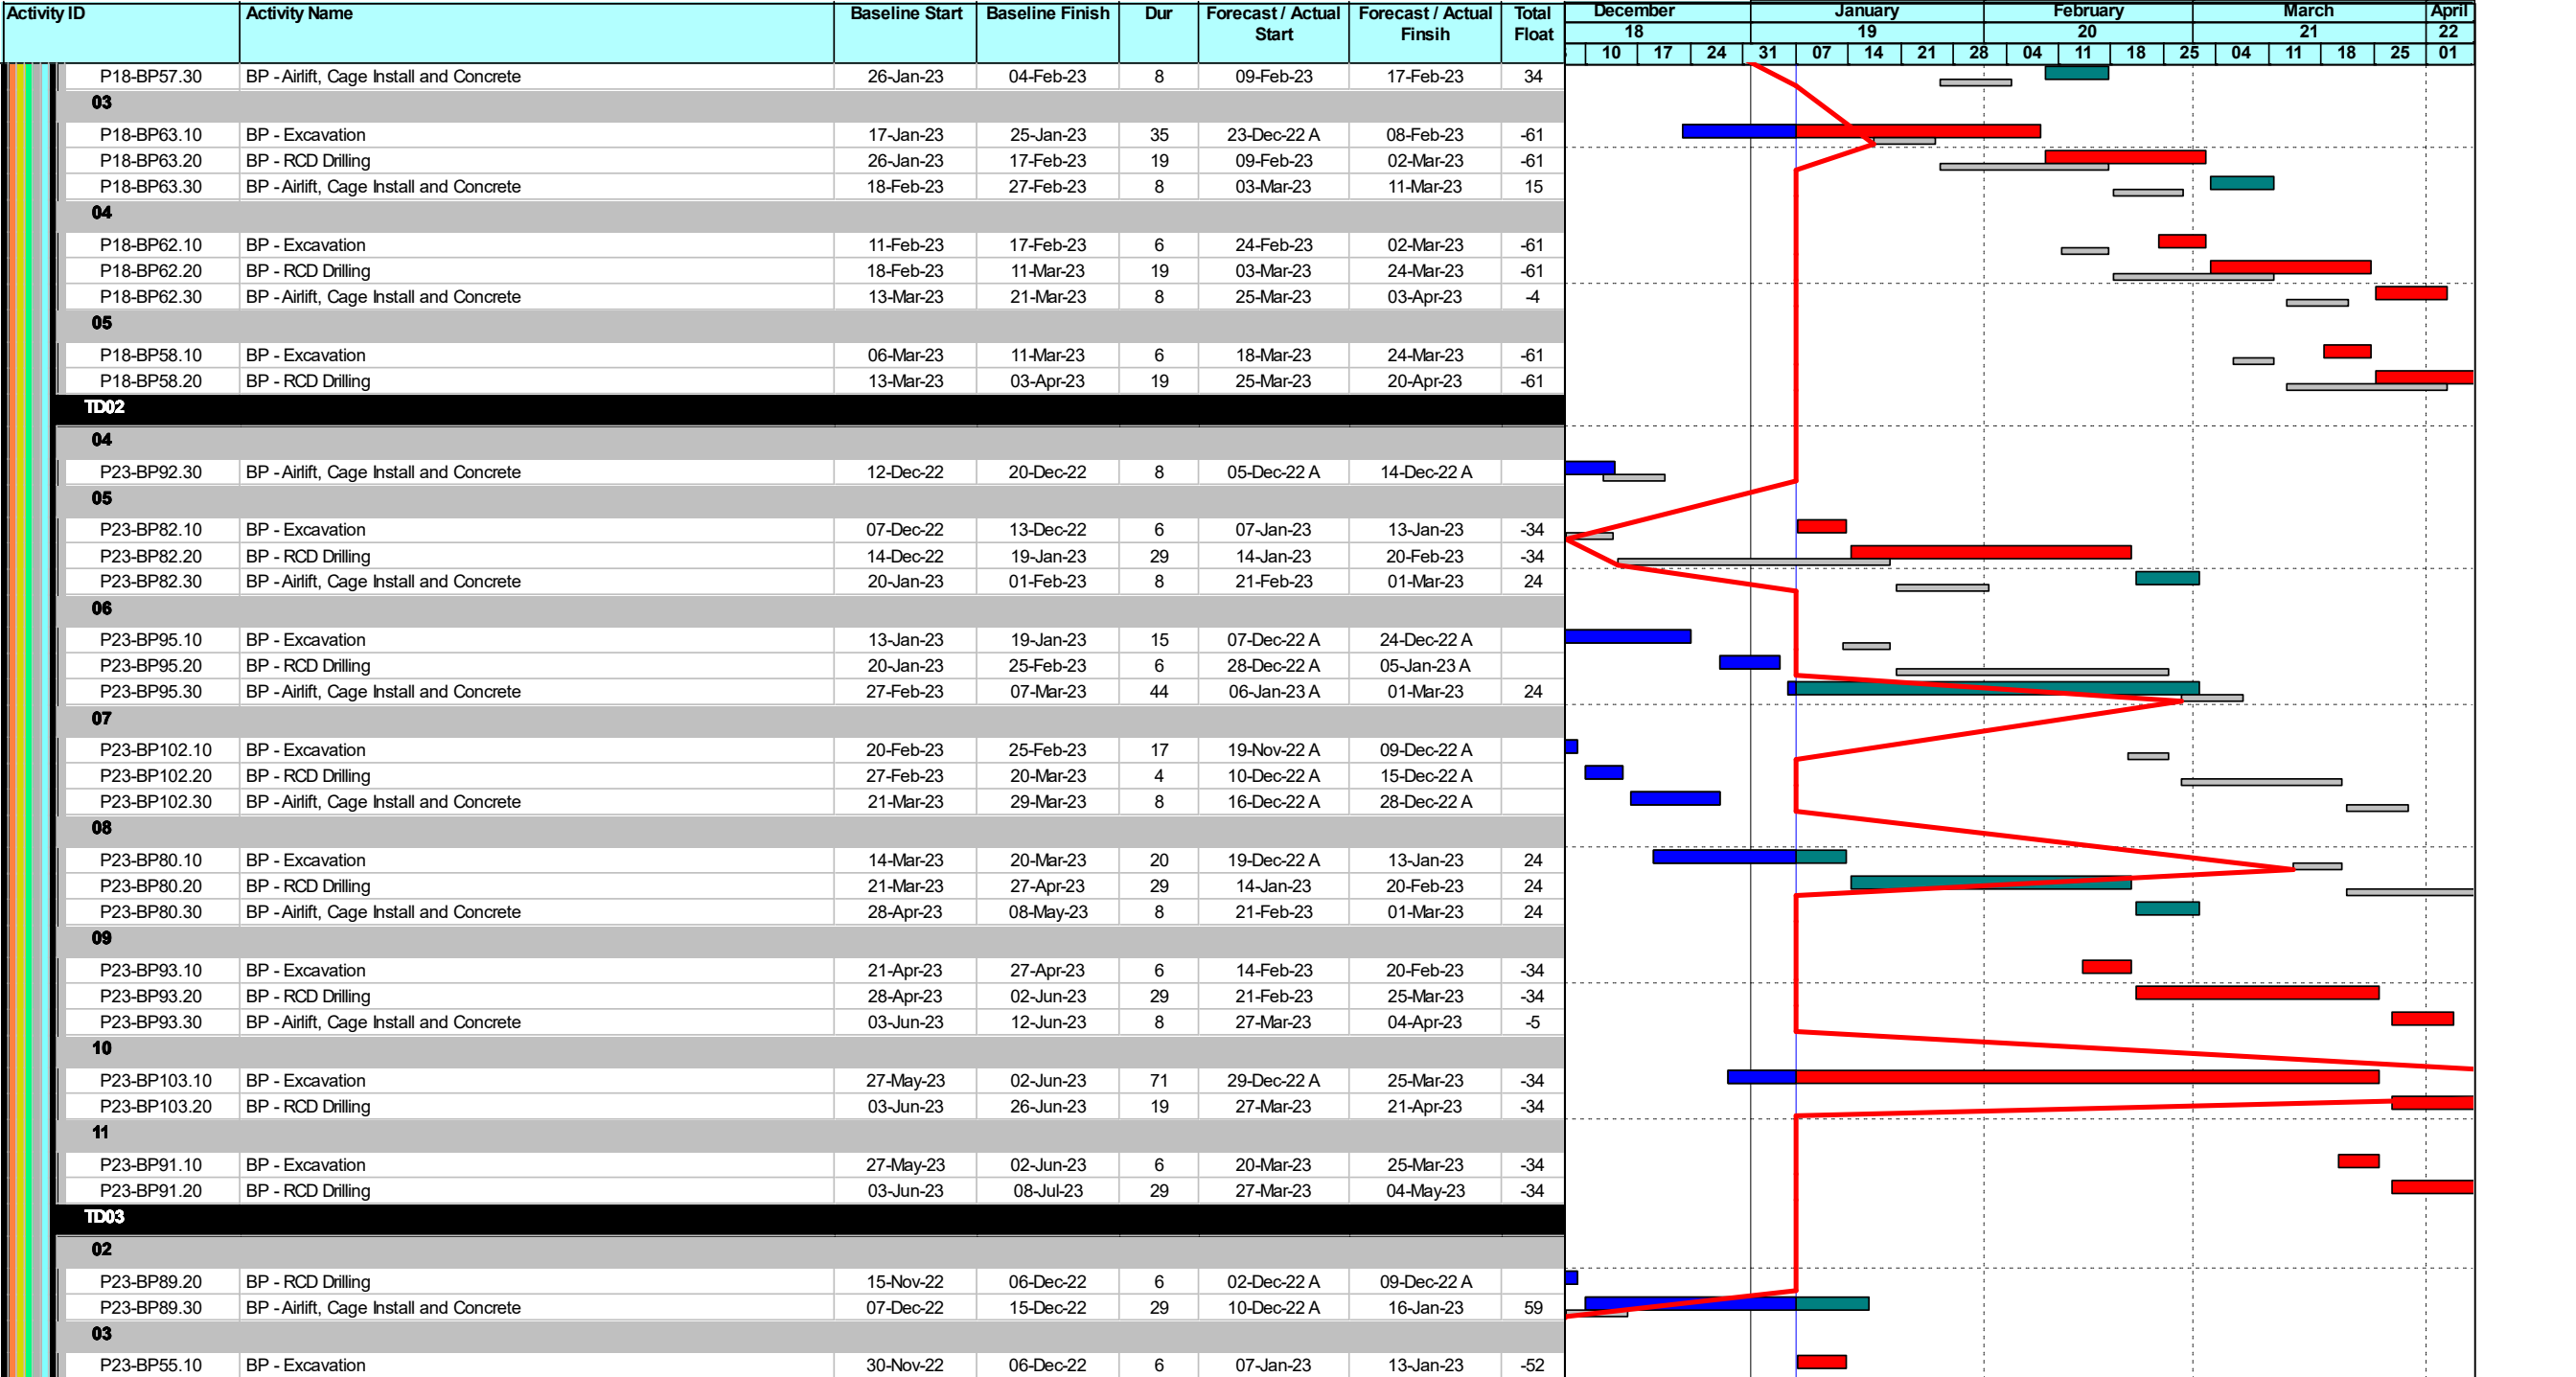


	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS







West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 6 January 2023
 Based on CMWP Rev.0 (3rd Draft)

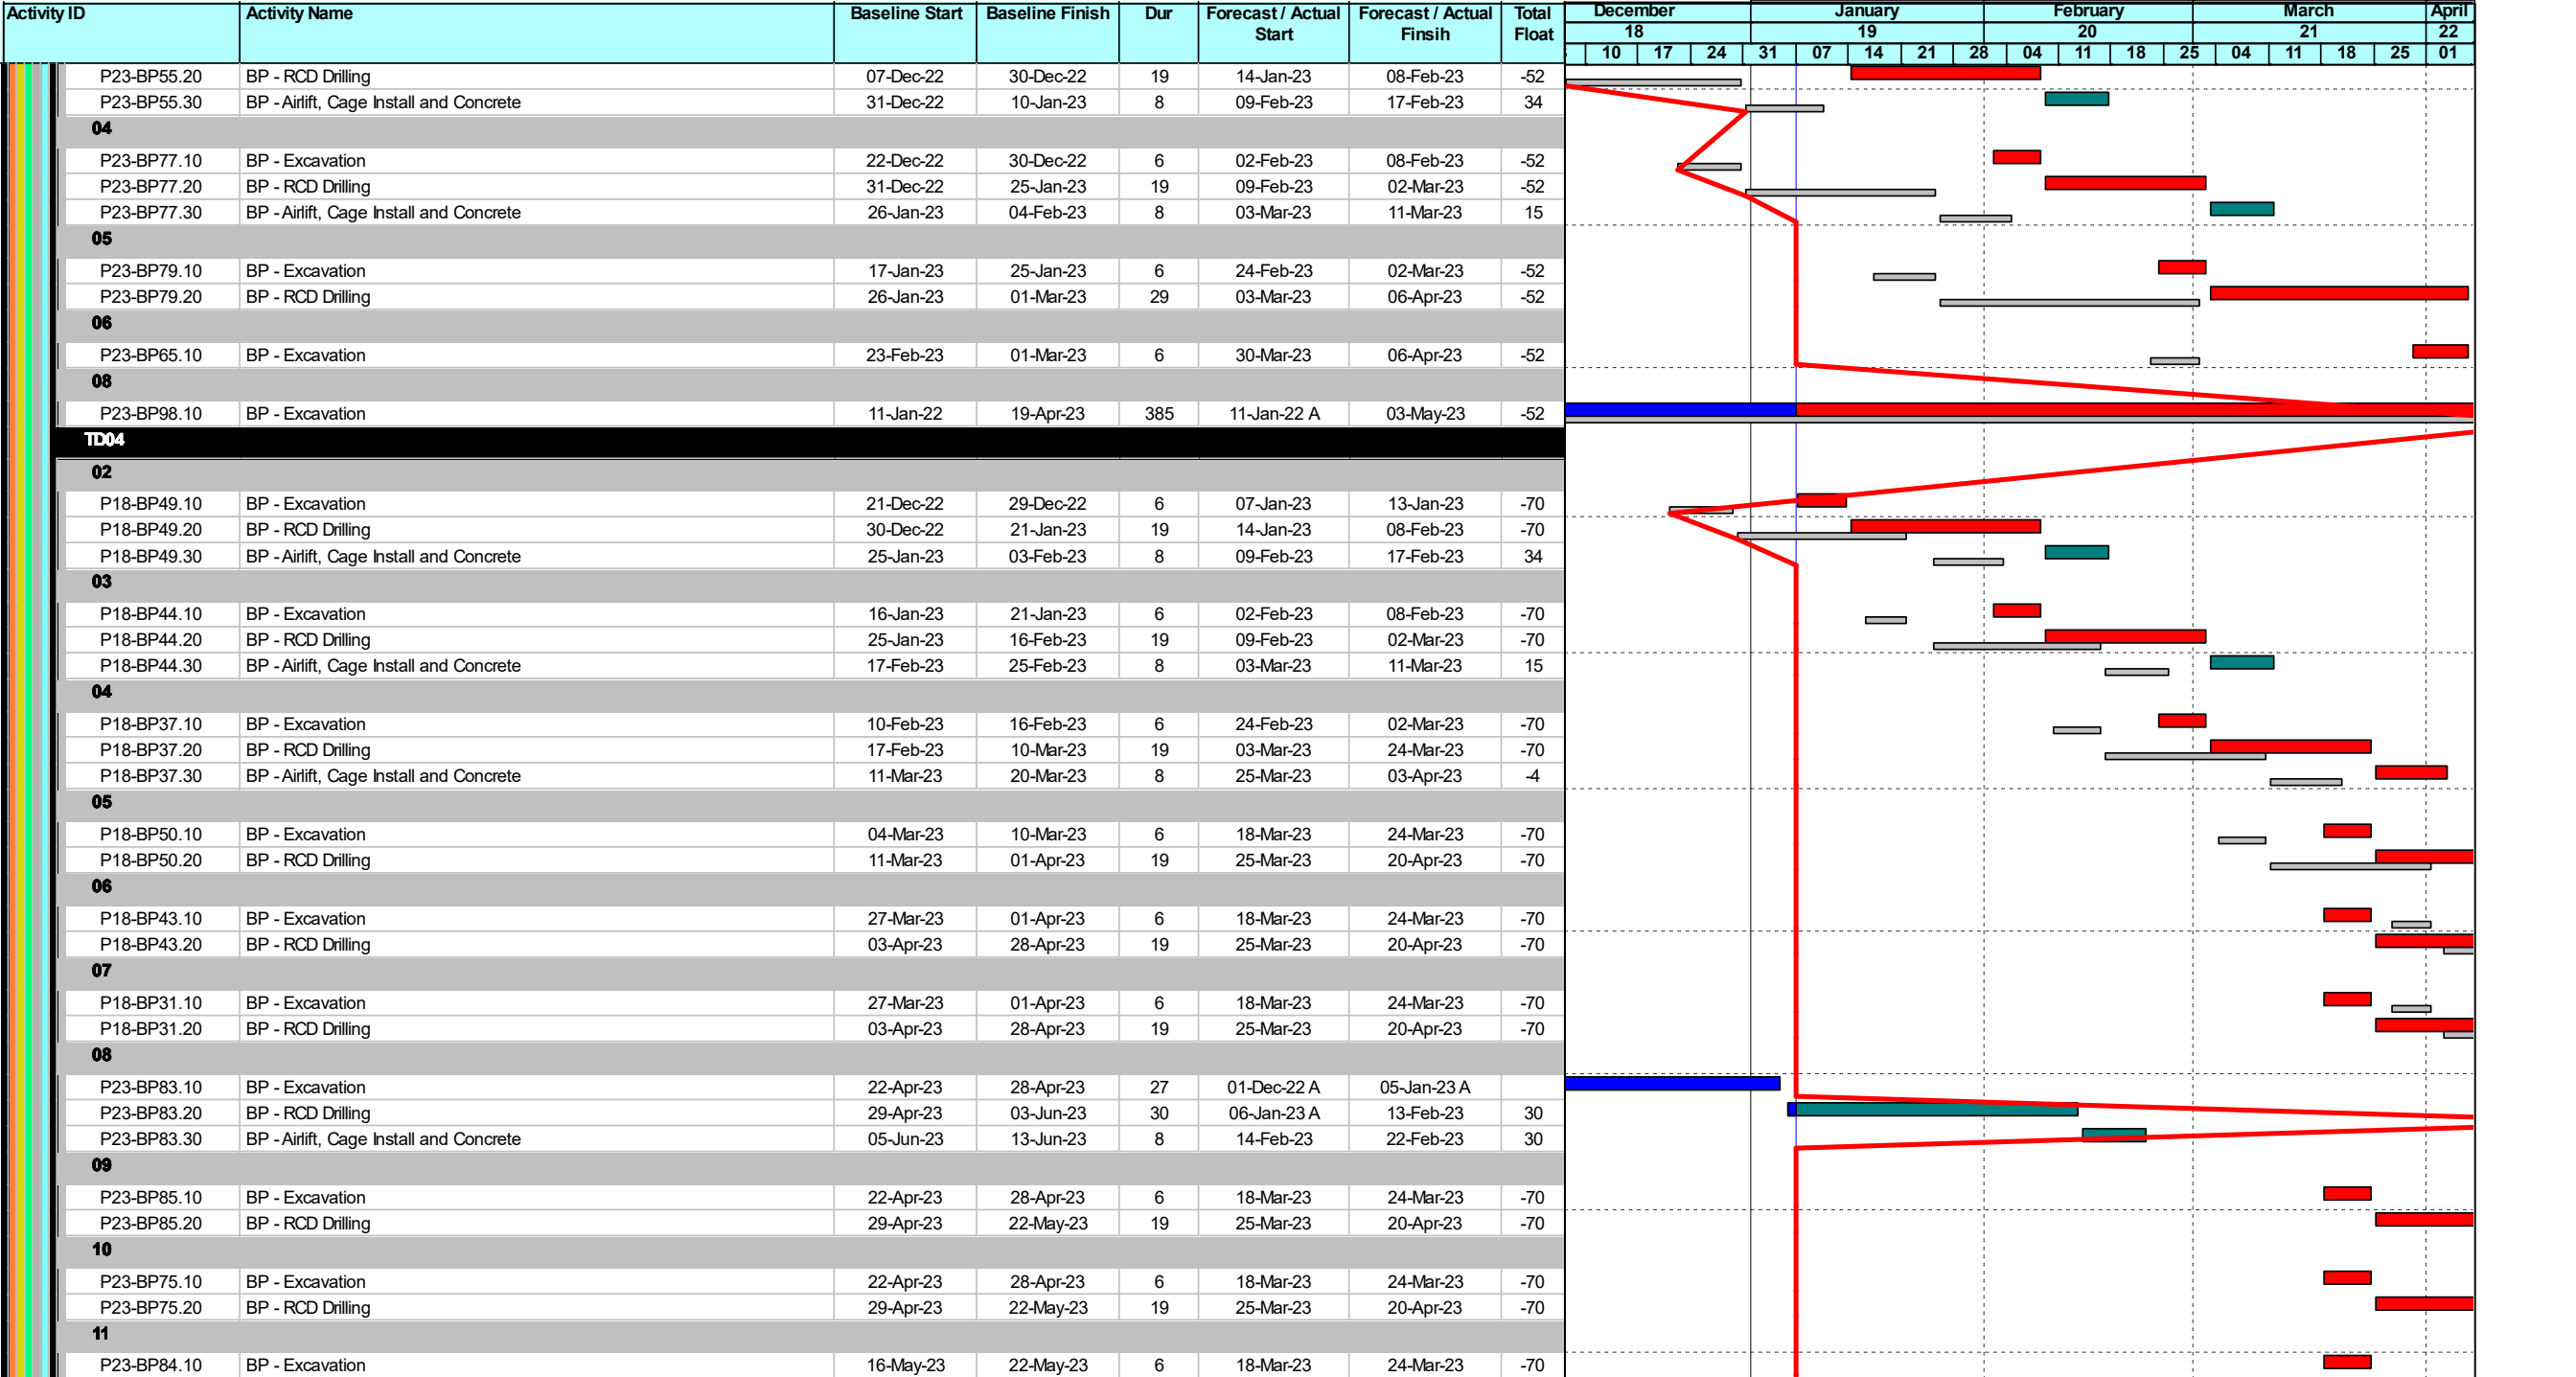

Date	Revision	Checked	Approved
4-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C





ID: 2BC-202230106_w TBC
 Data Date: 07-Jan-23
 Print Date: 11-Jan-23_10:49
 Page 13 of 16

	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 6 January 2023
Based on CMWP Rev.0 (3rd Draft)






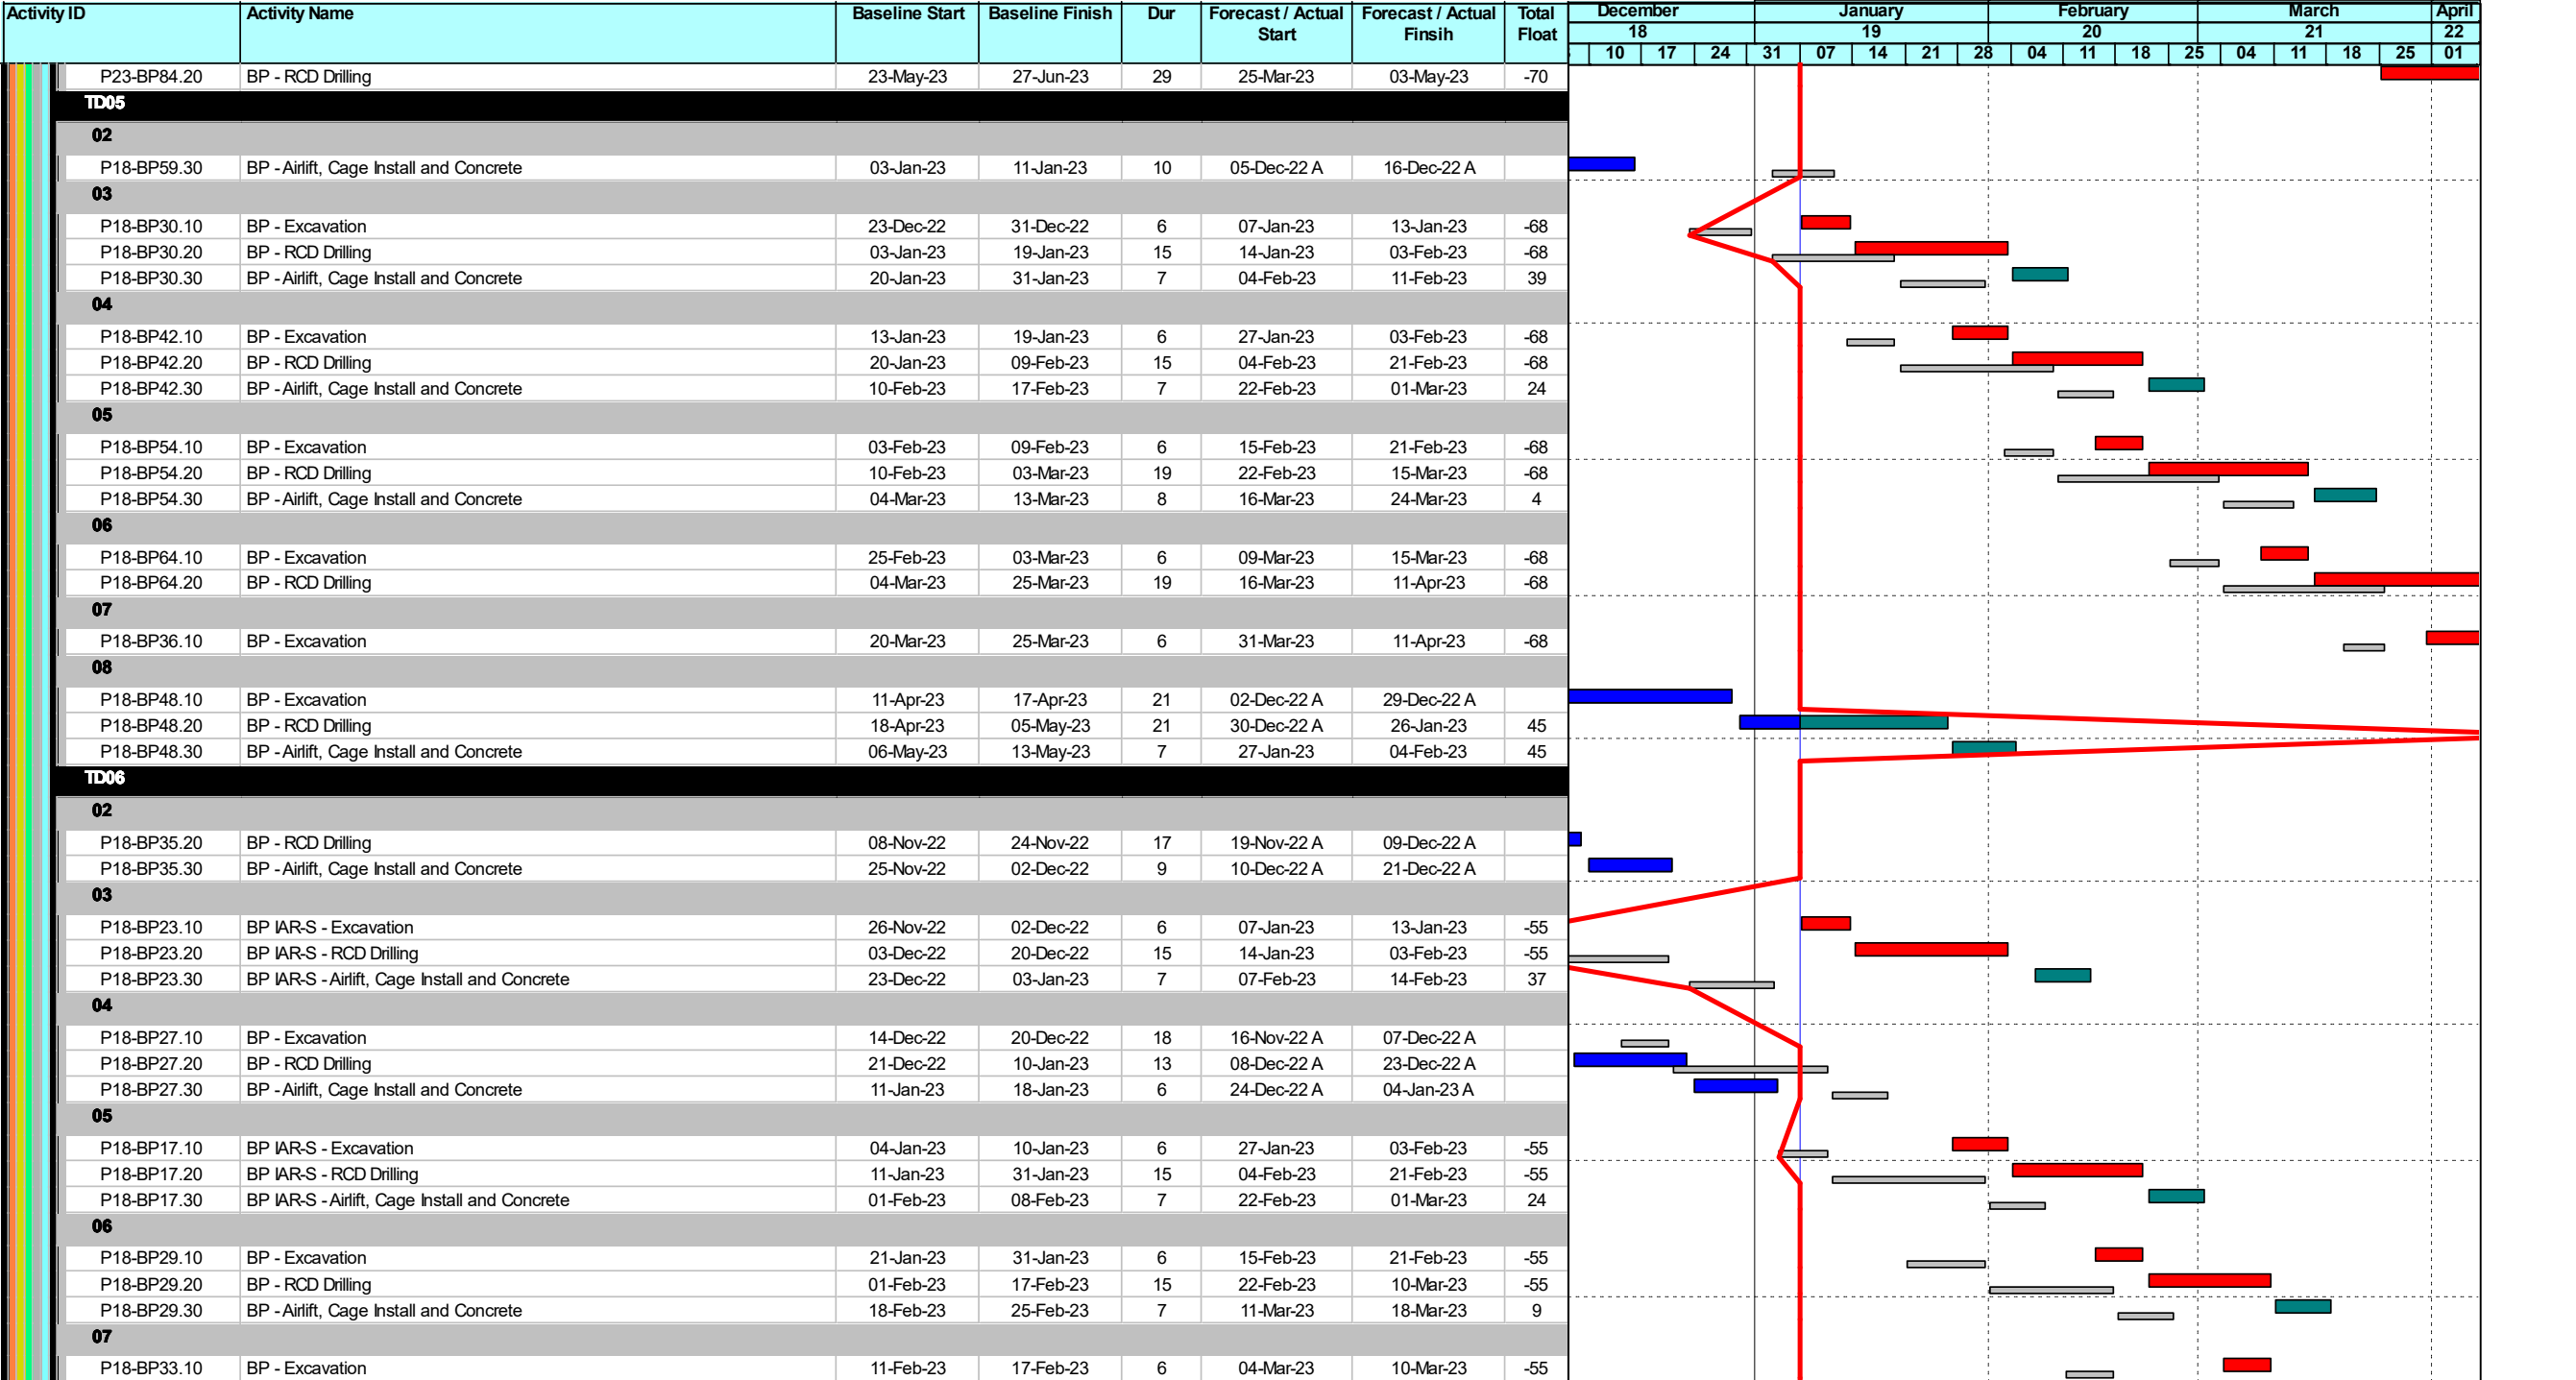



Date	Revision	Checked	Approved
4-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C

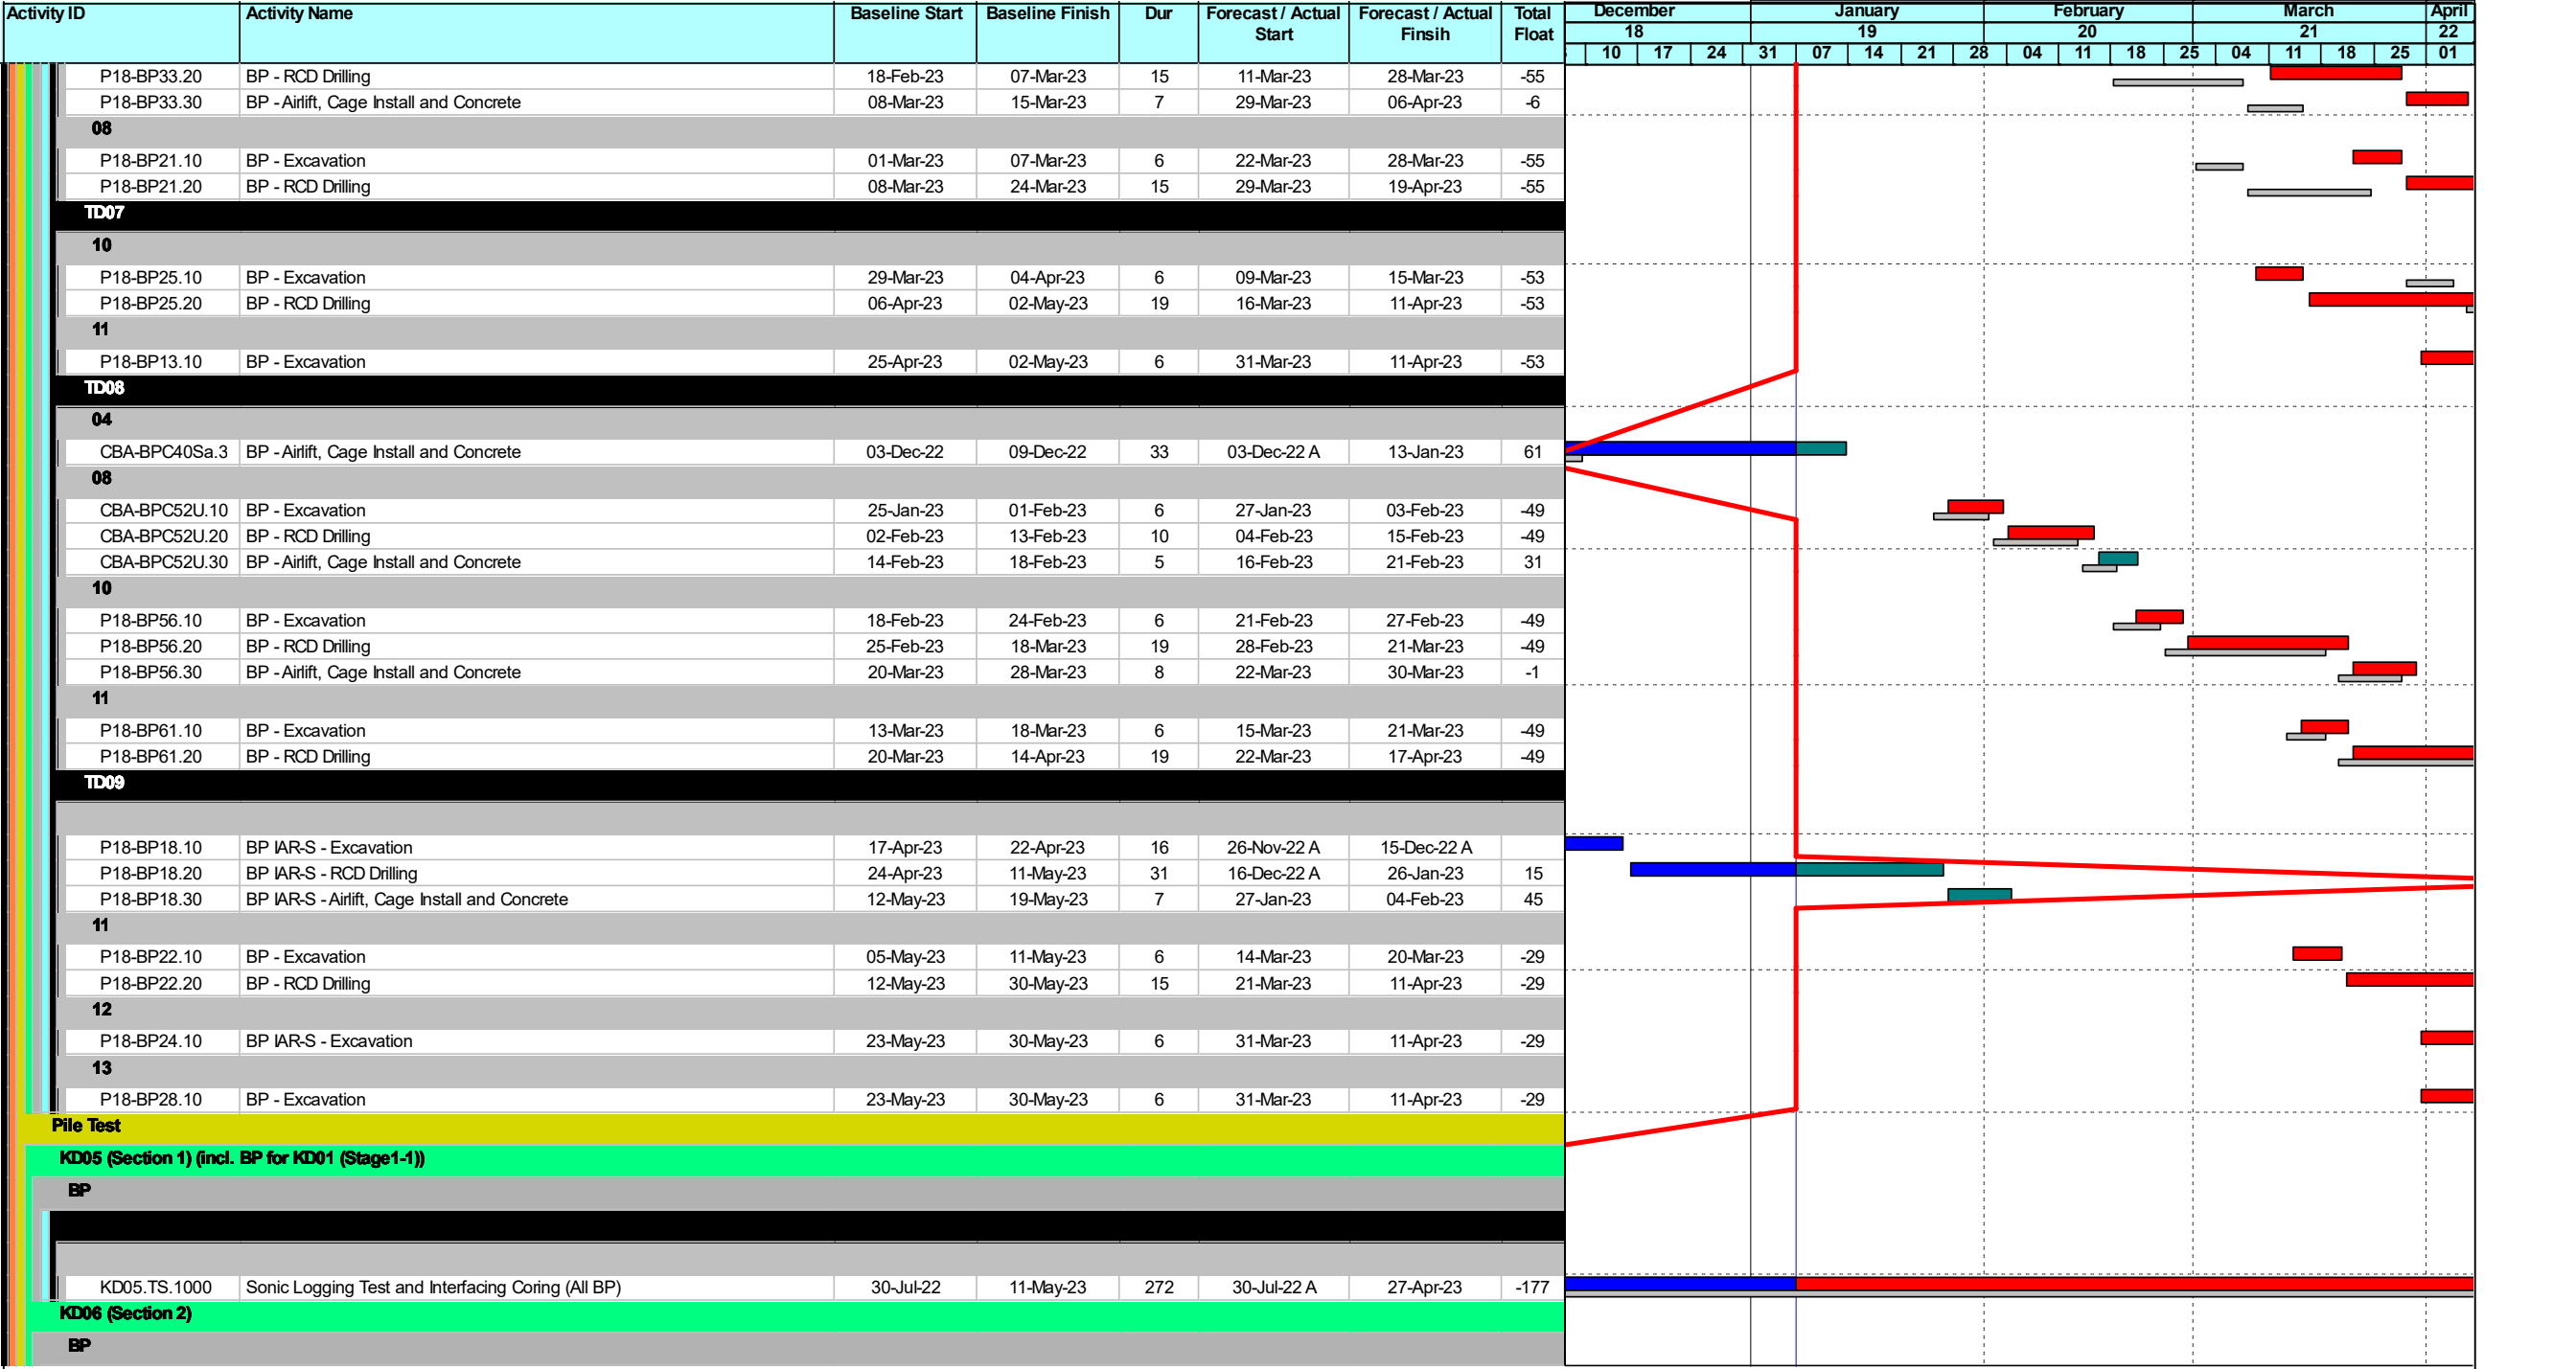

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 6 January 2023
Based on CMWP Rev.0 (3rd Draft)

		Date	Revision	Checked	Approved
		4-Mar-22	R0	KL	B
		02-Dec-22	R03D	KL	C









	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 6 January 2023
 Based on CMWP Rev.0 (3rd Draft)



Date	Revision	Checked	Approved
4-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	December				January				February				March				April			
								18				19				20				21				22			
								10	17	24	31	07	14	21	28	04	11	18	25	04	11	18	25	01			
KD06.TS.1000	Sonic Logging Test and Interfacing Coring (All BP)	27-Jul-22	12-Jul-23	351	27-Jul-22 A	12-Jul-23	-93																				
KD07 (Section 3) (incl. BP for KD03) (Stage 3-1)																											
BP																											
KD07.TS.1000	Sonic Logging Test and Interfacing Coring (All BP)	14-Jun-23	11-Oct-23	306	10-Dec-22 A	11-Oct-23	-74																				
KD08 (Section 4) (incl. BP for KD04 (Stage 4-1) & SSHP in KD09 (Section 5))																											
BP																											
KD08.TS.1000	Sonic Logging Test and Interfacing Coring (All BP)	04-Jul-22	11-Jun-23	343	04-Jul-22 A	11-Jun-23	-82																				
SSHP																											
KD08.TS.1120	Submit BA14	15-Nov-22	21-Nov-22	7	07-Jan-23	13-Jan-23	73																				
KD08.TS.1140	Selection of Pile for Static Load Test	22-Nov-22	05-Dec-22	14	14-Jan-23	27-Jan-23	73																				
KD08.TS.1160	Static Load Test of Selected Pile	06-Dec-22	19-Dec-22	14	28-Jan-23	10-Feb-23	73																				
KD08.TS.1180	Obtain BA14 Acknowledgement / Satisfaction of CA, Completion As-built Drawings, Reports & Records	20-Dec-22	16-Jan-23	28	11-Feb-23	10-Mar-23	73																				
KD09 (Section 5) (incl. BP for KD02 (Stage 5-1))																											
BP																											
KD09.TS.1000	Sonic Logging Test and Interfacing Coring (All BP)	23-May-22	12-Aug-23	413	23-May-22 A	09-Jul-23	-90																				
Attendance to Other Project Contractors (optional works item no. 2A to 2E)																											
S4.AT.0000	Attendance at Section 4 Area (optional works item no. 2D) (Duration TBC)	22-Feb-23	13-Mar-23	20	22-Feb-23	13-Mar-23	71																				
S5.AT.0000	Attendance at Section 5 Area (optional works item no. 2E) (Duration TBC)	14-Mar-23	02-Apr-23	20	14-Mar-23	02-Apr-23	71																				

	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 6 January 2023
 Based on CMWP Rev.0 (3rd Draft)

Date	Revision	Checked	Approved
4-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C

