

Zone 2A

Project Name: Foundation and ELS Works for Integrated Basement and Underground Road in Zone 2A of the West Kowloon Cultural District

3-Month Rolling Programme

Activity Description	Duration (Cal. Day)	Start Date	Finish Date	2023															
				March					April				May				June		
				3	10	17	24	31	7	14	21	28	5	12	19	26	2	9	16
W147	W148	W149	W150	W151	W152	W153	W154	W155	W156	W157	W158	W159	W160	W161	W162	W163	W164		
Zone 2A A&A Works																			
WEK G/F																			
Dismantling the Metal Roof Trusses at the Subcontractor's Works Area	8	28-Feb-23	7-Mar-23	■															

■ - Actual
 ■ - Remaining Works

Zone 2B & 2C

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	March					April				May				June		
								21					22				23				24		
								25	04	11	18	25	01	08	15	22	29	06	13	20	27	03	10

Piling for Integrated Basement and U/G Road in Zone 2B & 2C

Contract Dates

Optional Works subjected to CA's Instruction

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float
CO2B	Last CAI date for Optional Works Item No.2B (330 Days to 660 Days after Commencement)	13-May-23		0	13-May-23		11
CO2E	Last CAI date for Optional Works Item No.2E (330 Days to 600 Days after Commencement)	14-Mar-23		0	14-Mar-23 A		

Construction Stage

Pile Construction

KD05 (Section 1)

Bored Piles - Drainage Diversion

CD04

05

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float
P17-BP13.10	BP IAR-N - Excavation	03-Feb-23	09-Feb-23	10	27-Feb-23 A	10-Mar-23 A	
P17-BP13.20	BP IAR-N - RCD Drilling	10-Feb-23	27-Feb-23	8	11-Mar-23 A	21-Mar-23 A	
P17-BP13.30	BP IAR-N - Airlift, Cage Install and Concrete	28-Feb-23	07-Mar-23	10	22-Mar-23 A	01-Apr-23	-134

CD07

04

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float
P17-BP19.10	BP - Excavation	27-Jan-23	03-Feb-23	6	25-Mar-23	31-Mar-23	-203
P17-BP19.20	BP - RCD Drilling	04-Feb-23	21-Feb-23	15	01-Apr-23	22-Apr-23	-203
P17-BP19.30	BP - Airlift, Cage Install and Concrete	22-Feb-23	01-Mar-23	6	24-Apr-23	29-Apr-23	-154

CD08

01

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float
P17-BP20.10	BP - Excavation	17-Feb-23	23-Feb-23	4	19-Apr-23	22-Apr-23	-203
P17-BP20.20	BP - RCD Drilling	24-Feb-23	13-Mar-23	15	24-Apr-23	11-May-23	-203
P17-BP20.30	BP - Airlift, Cage Install and Concrete	14-Mar-23	21-Mar-23	7	12-May-23	19-May-23	-170

02

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float
P17-BP21.10	BP IAR-N - Excavation	07-Mar-23	13-Mar-23	4	12-May-23	16-May-23	-203
P17-BP21.20	BP IAR-N - RCD Drilling	14-Mar-23	30-Mar-23	15	17-May-23	03-Jun-23	-203
P17-BP21.30	BP IAR-N - Airlift, Cage Install and Concrete	31-Mar-23	12-Apr-23	7	05-Jun-23	12-Jun-23	-189

03

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float
P17-BP18.10	BP IAR-N - Excavation	24-Mar-23	30-Mar-23	4	31-May-23	03-Jun-23	-203
P17-BP18.20	BP IAR-N - RCD Drilling	31-Mar-23	21-Apr-23	15	05-Jun-23	21-Jun-23	-203
P17-BP18.30	BP IAR-N - Airlift, Cage Install and Concrete	22-Apr-23	29-Apr-23	7	23-Jun-23	30-Jun-23	-203

Bored Piles - Gantry Gate A

CD06


08

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float
CBA-BP01.10	BP - Excavation	20-Jan-23	31-Jan-23	7	15-Apr-23	22-Apr-23	-168
CBA-BP01.20	BP - RCD Drilling	01-Feb-23	16-Feb-23	14	24-Apr-23	10-May-23	-168
CBA-BP01.30	BP - Airlift, Cage Install and Concrete	17-Feb-23	23-Feb-23	6	11-May-23	17-May-23	-168

CD07

02

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float
P22&P19-BP26.:	BP - RCD Drilling	16-Jul-22	03-Dec-22	213	16-Jul-22 A	31-Mar-23	-141

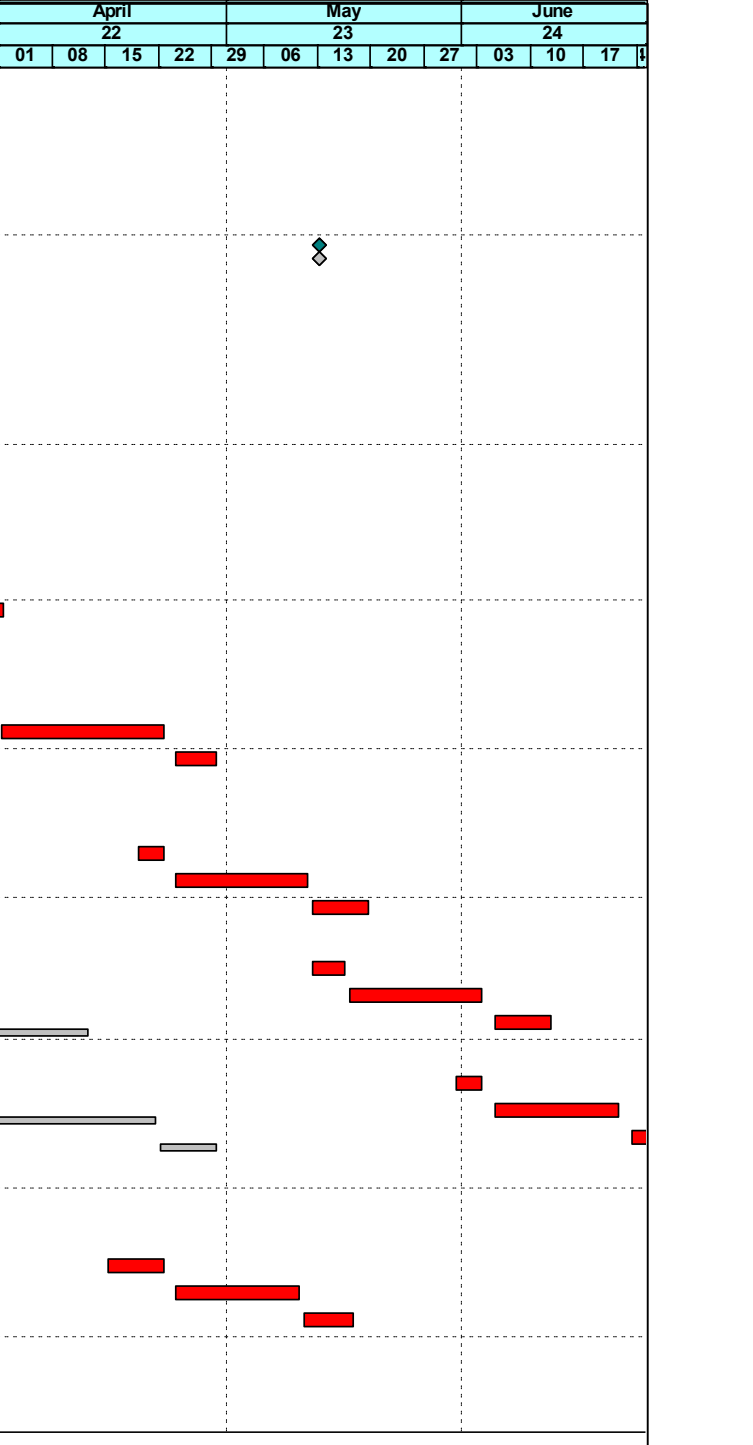







ID: 2BC-20230324_bw
 Data Date: 25-Mar-23
 Print Date: 24-Mar-23_17:18
 Page 1 of 14

■ Planned	◆ Planned MS
■ Critical	◆ Critical MS
■ Actual	◆ Actual MS

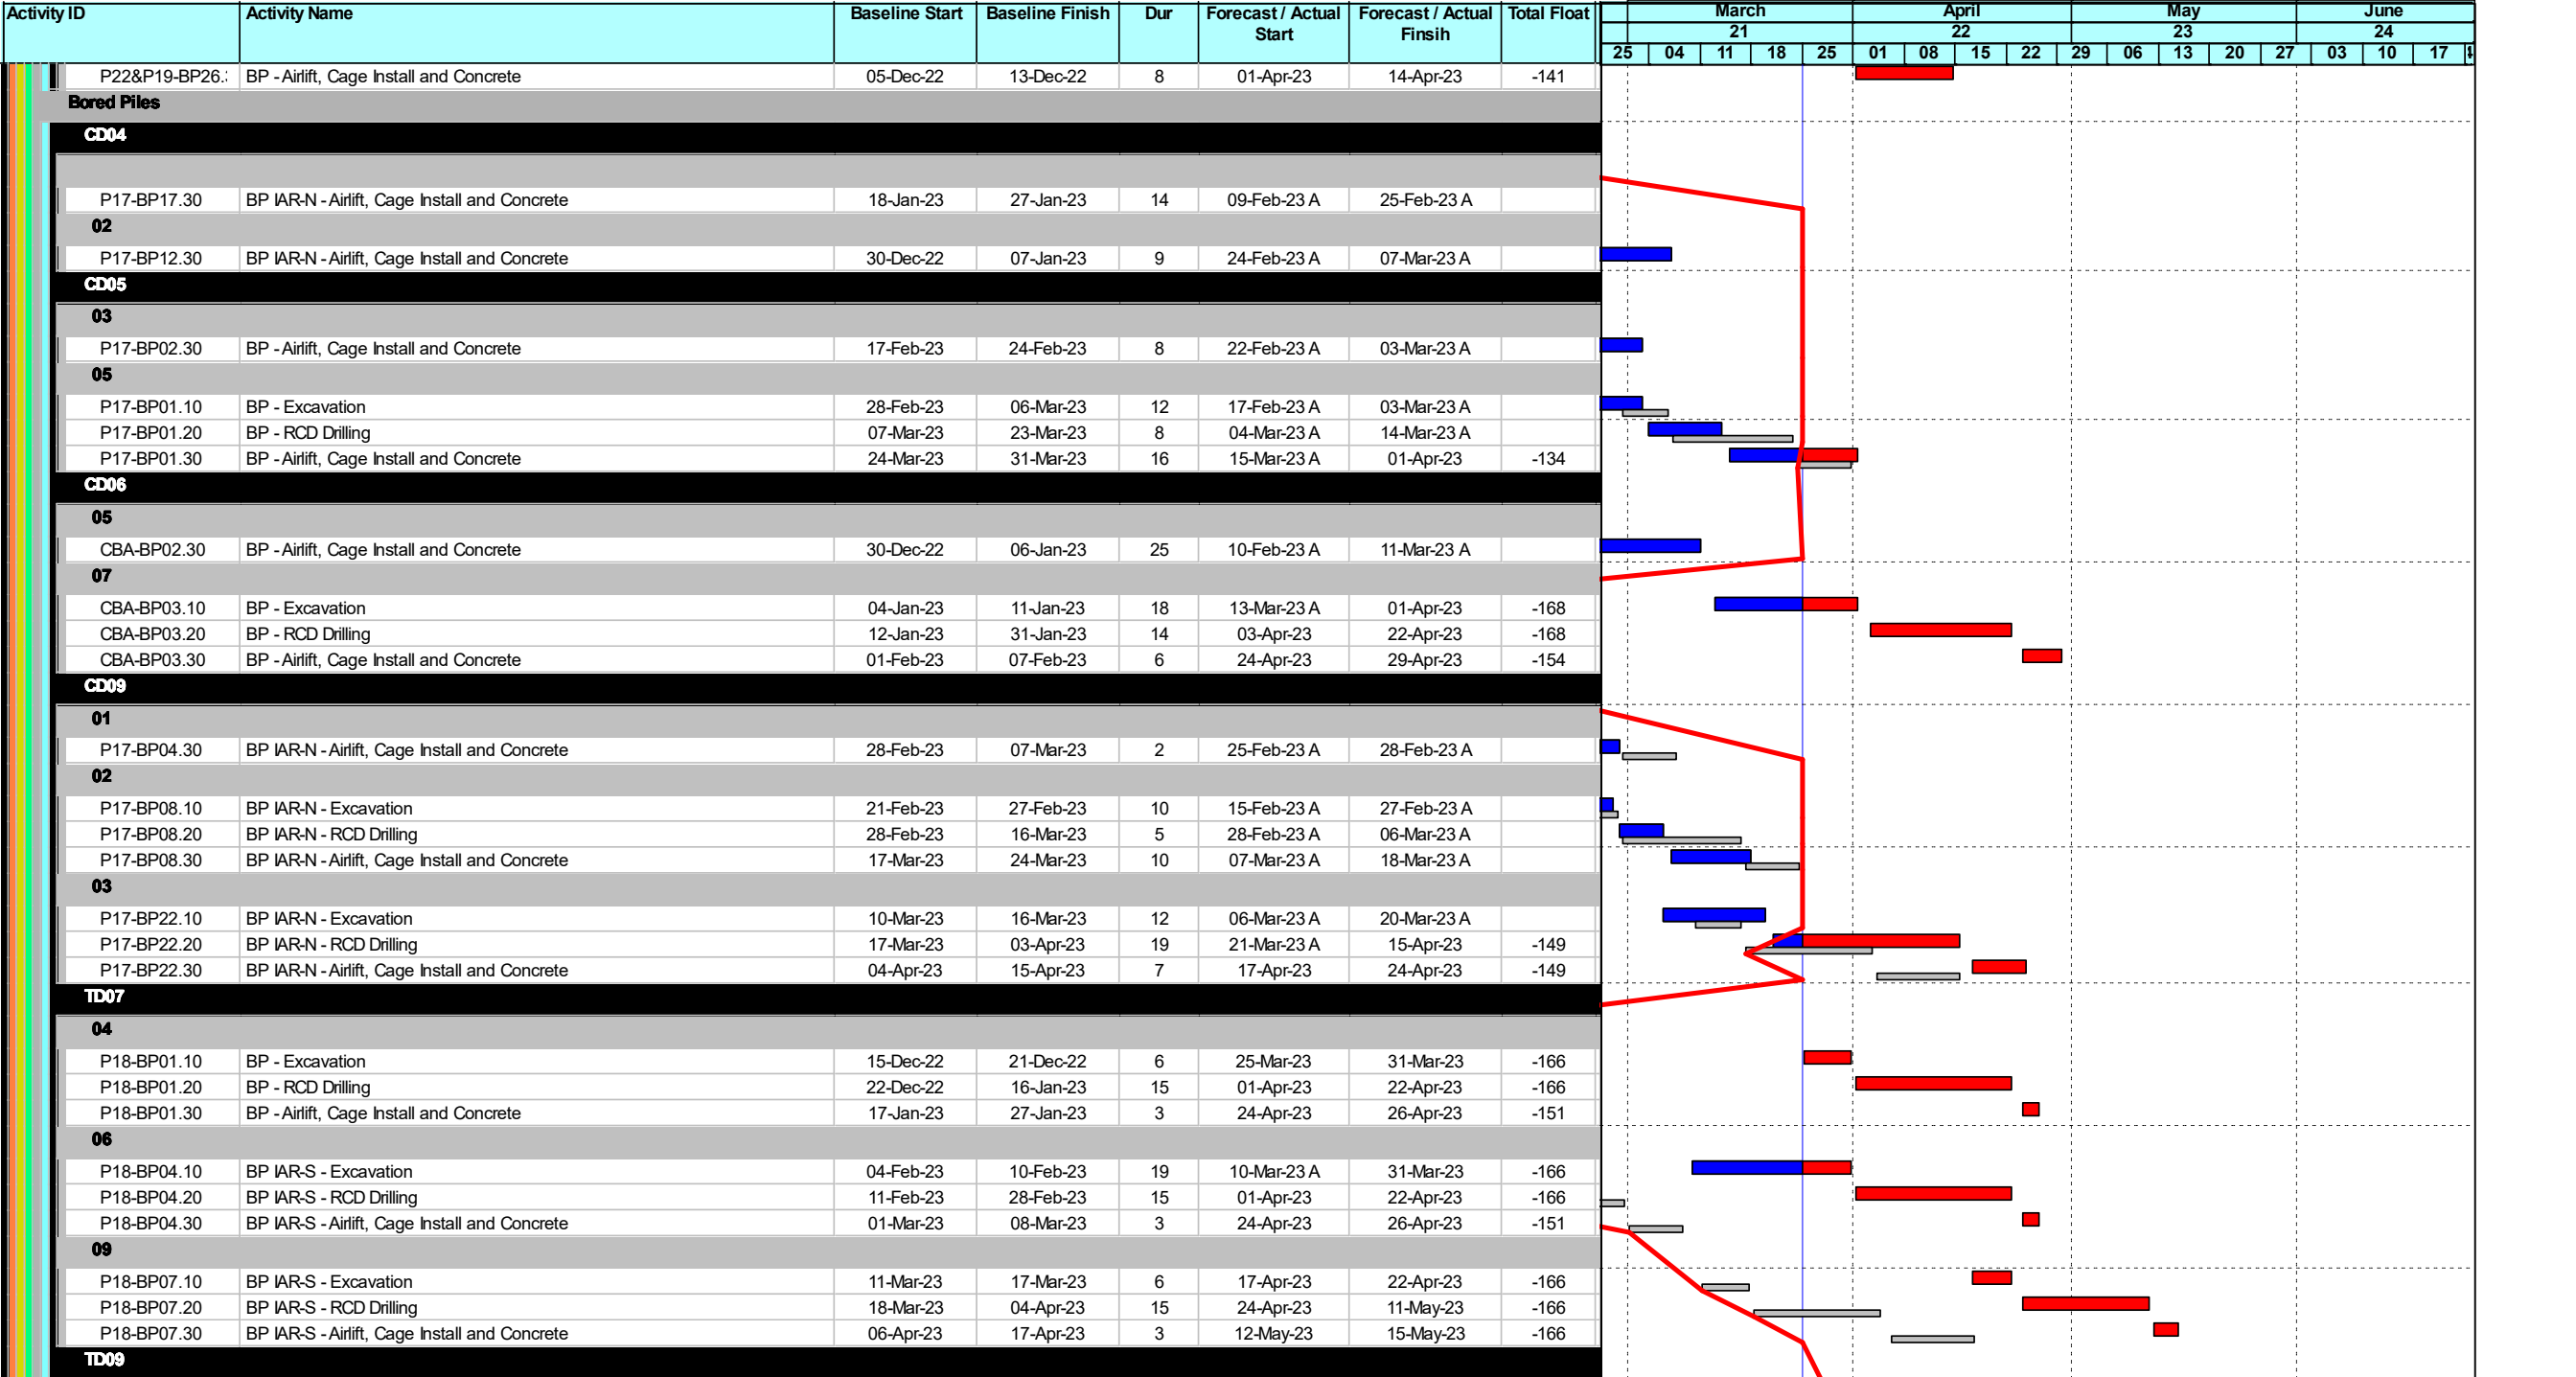West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 24 March 2023
Based on CMWP Rev.0 (3rd Draft)

Date	Revision	Checked	Approved
4-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C










	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS

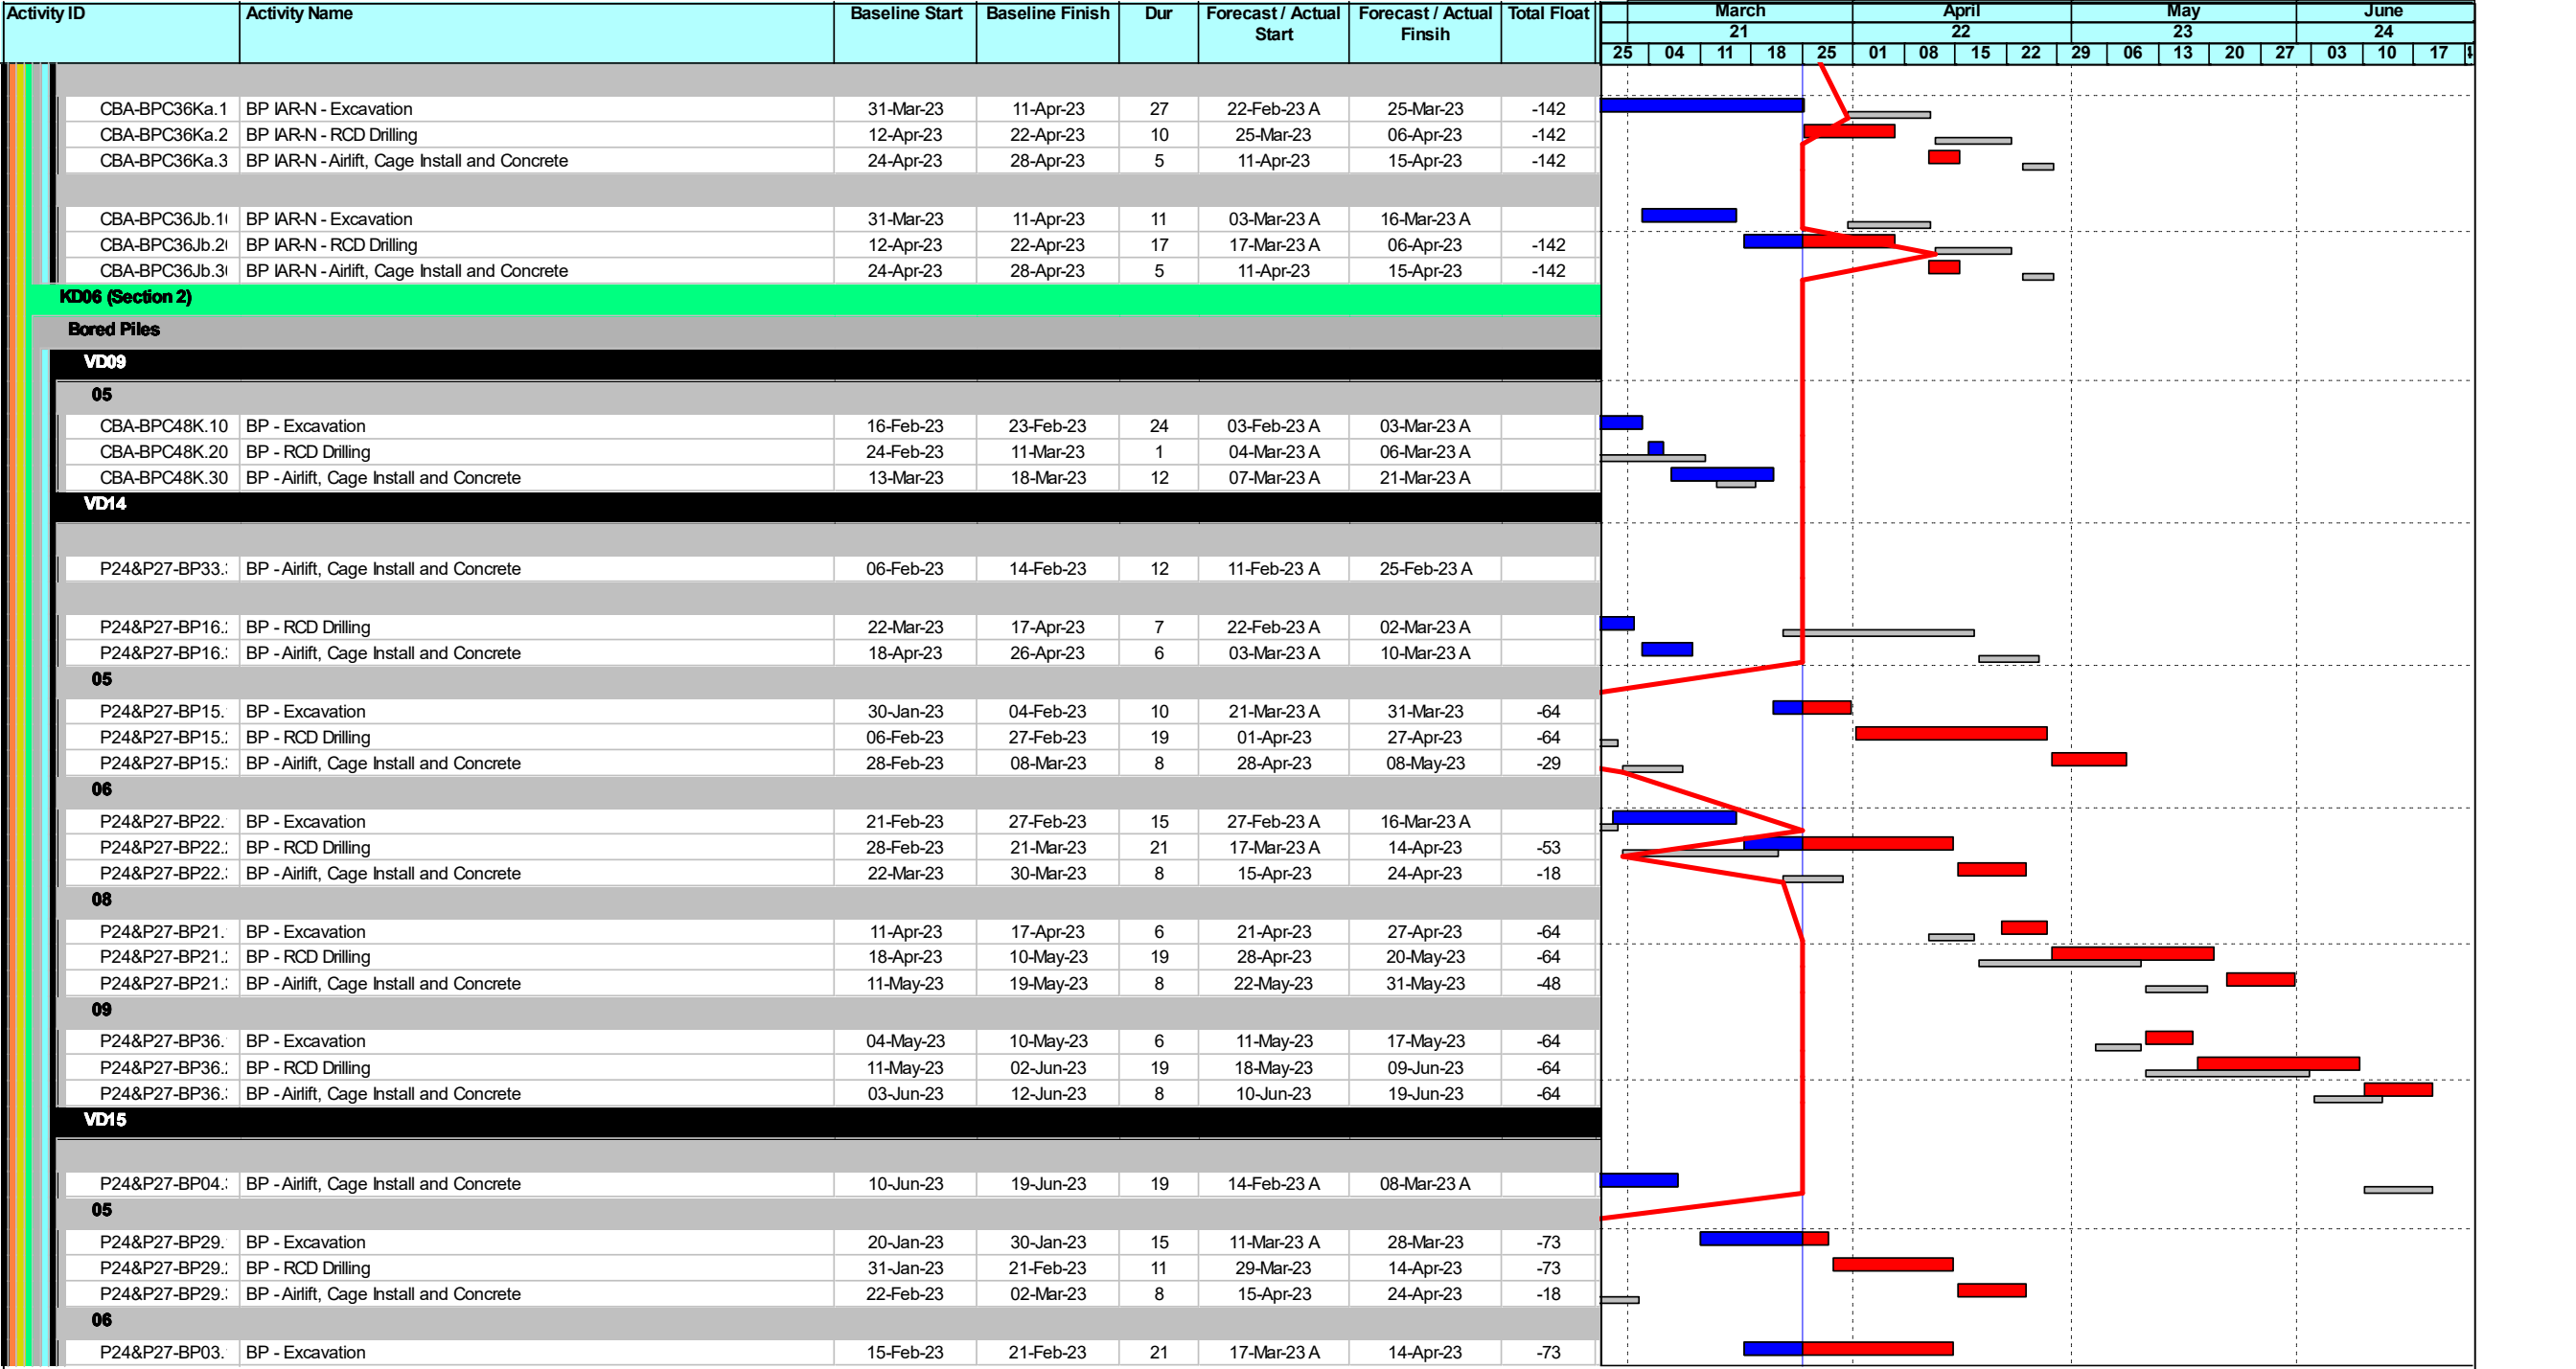West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 24 March 2023
 Based on CMWP Rev.0 (3rd Draft)



Date	Revision	Checked	Approved
4-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C




	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 24 March 2023
Based on CMWP Rev.0 (3rd Draft)



Date	Revision	Checked	Approved
4-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C

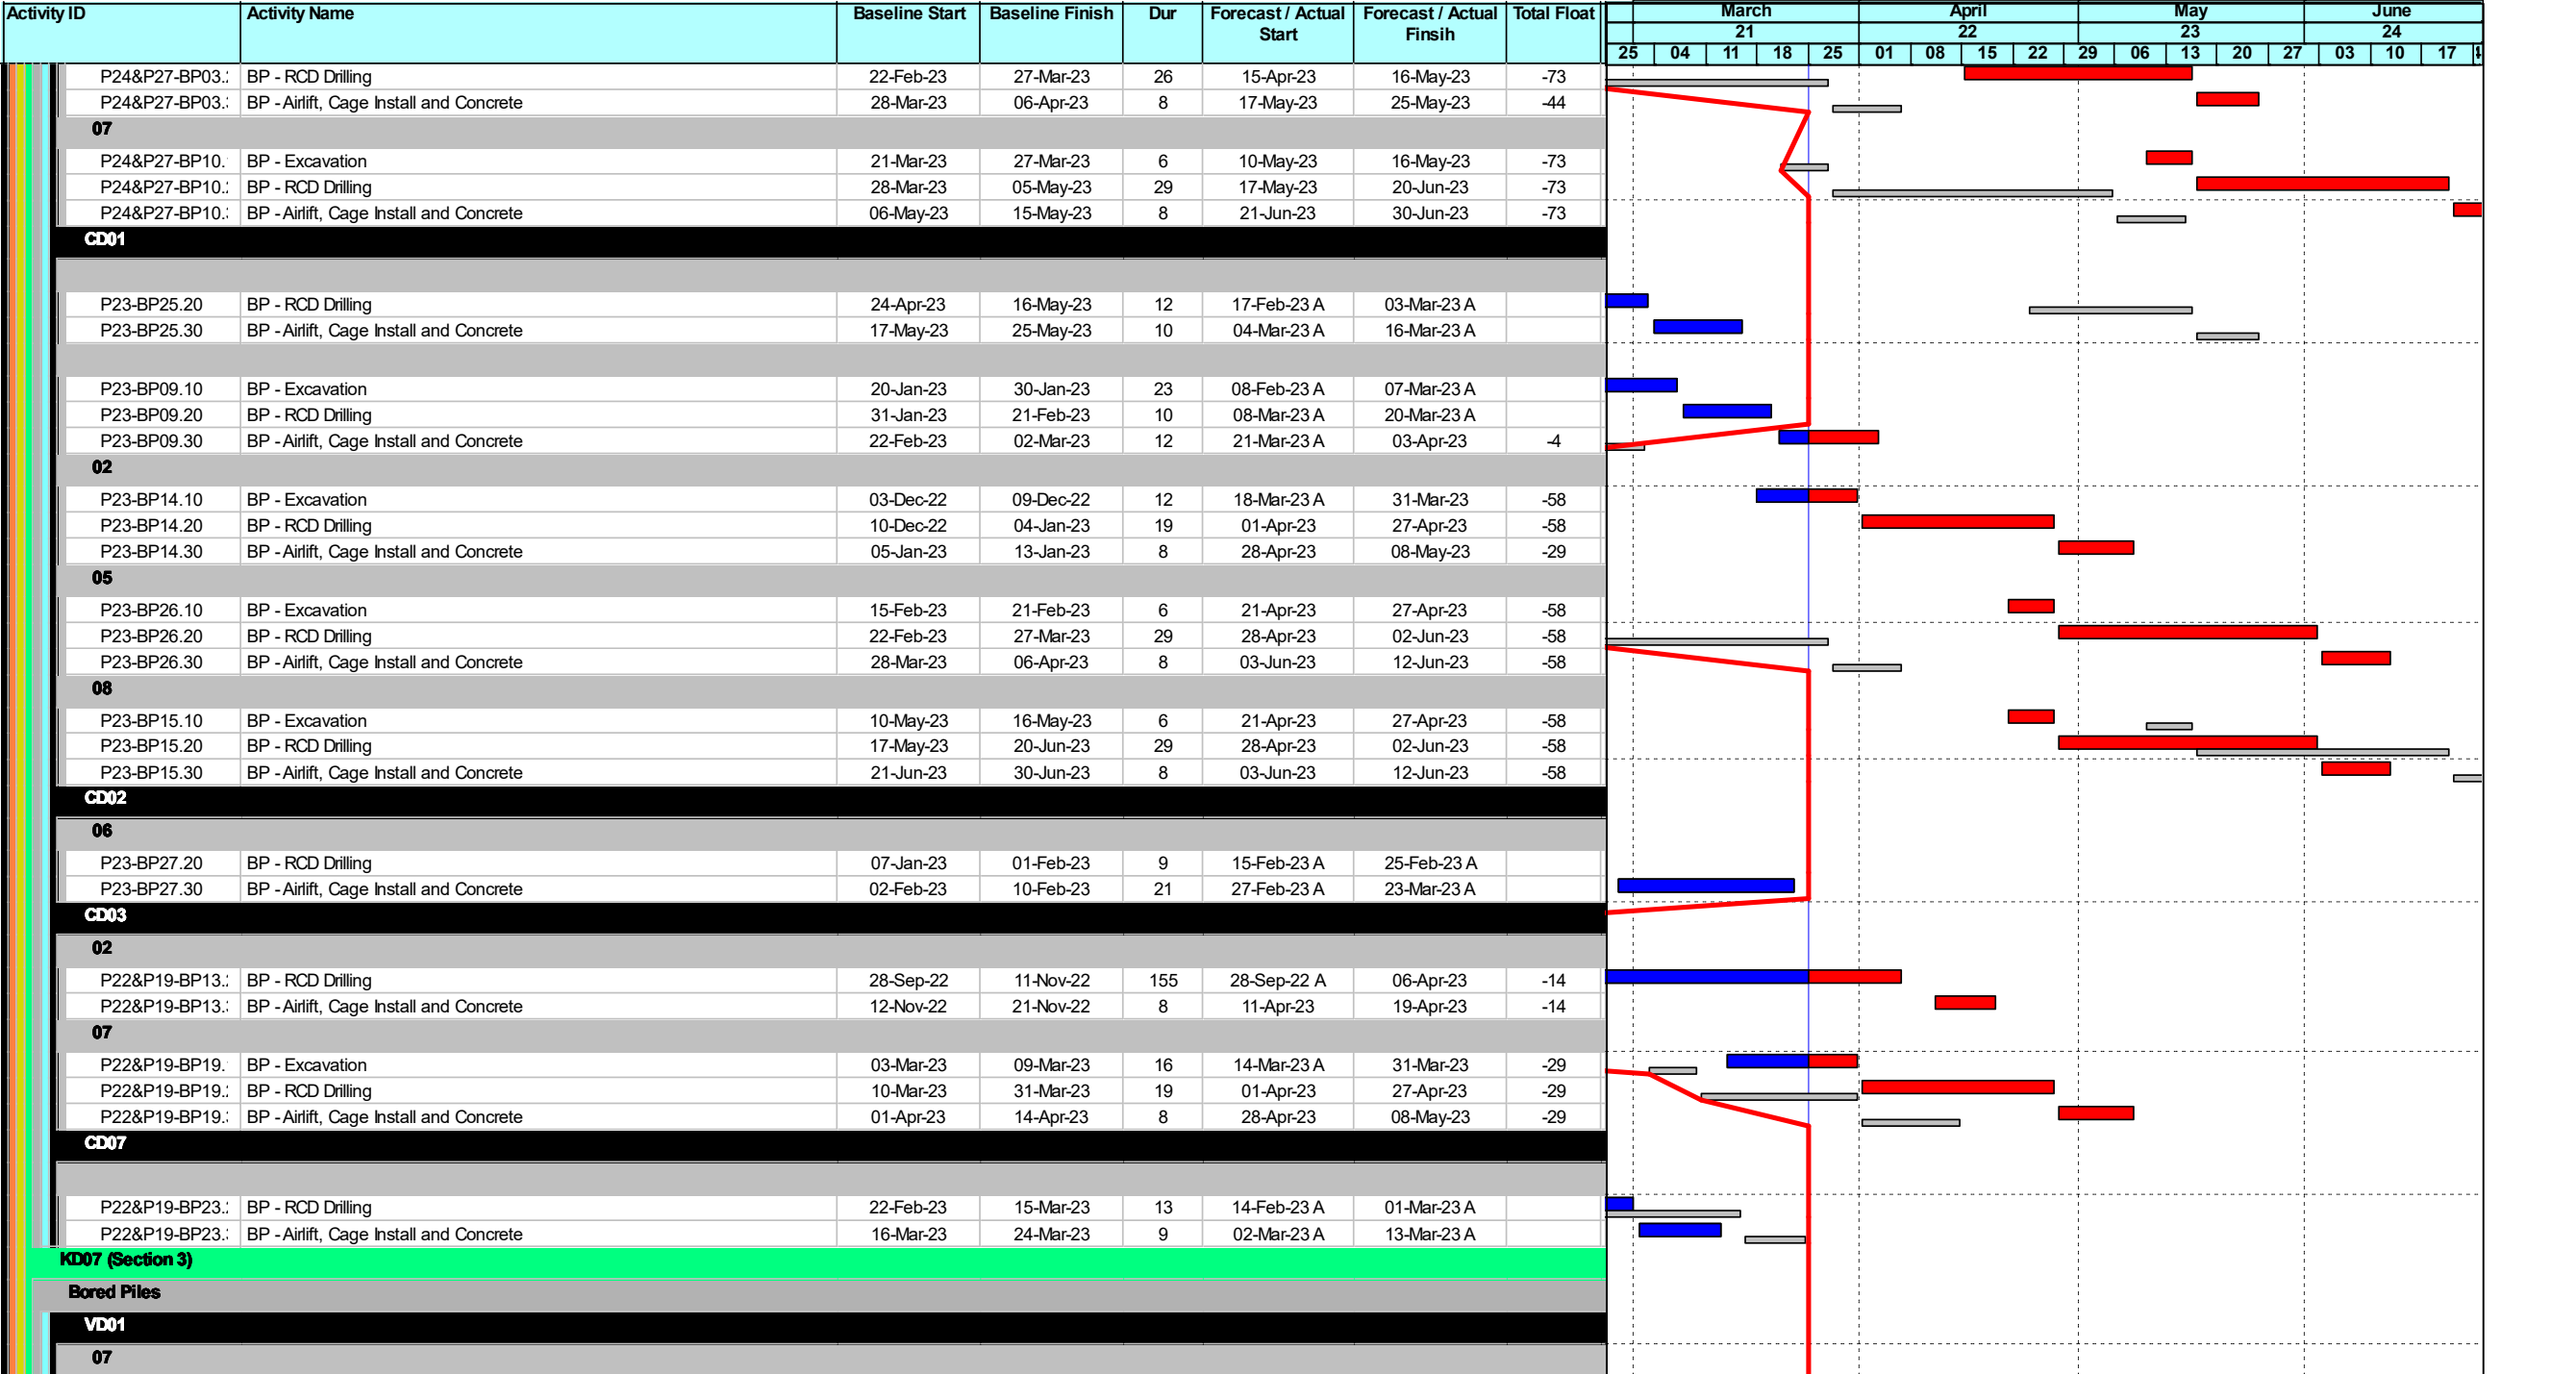

KD07 (Section 3)

Bored Piles

VD01

07

ID: 2BC-20230324_bw
 Data Date: 25-Mar-23
 Print Date: 24-Mar-23_17:18
 Page 4 of 14

	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 24 March 2023
 Based on CMWP Rev.0 (3rd Draft)



Date	Revision	Checked	Approved
4-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	March 21				April 22				May 23				June 24							
								25	04	11	18	25	01	08	15	22	29	06	13	20	27	03	10	17			
								Gantt Chart Area																			
P26-BP07.10	BP - Excavation	28-Apr-23	05-May-23	6	25-Mar-23	31-Mar-23	18																				
P26-BP07.20	BP - RCD Drilling	06-May-23	09-Jun-23	29	01-Apr-23	10-May-23	18																				
P26-BP07.30	BP - Airift, Cage Install and Concrete	10-Jun-23	19-Jun-23	8	11-May-23	19-May-23	47																				
08																											
P26-BP05.10	BP - Excavation	03-Jun-23	09-Jun-23	6	04-May-23	10-May-23	18																				
P26-BP05.20	BP - RCD Drilling	10-Jun-23	15-Jul-23	29	11-May-23	14-Jun-23	18																				
P26-BP05.30	BP - Airift, Cage Install and Concrete	17-Jul-23	25-Jul-23	8	15-Jun-23	24-Jun-23	18																				
VD02																											
02																											
P30-BP71.10	BP - Excavation	22-Dec-22	30-Dec-22	6	25-Mar-23	31-Mar-23	-45																				
P30-BP71.20	BP - RCD Drilling	31-Dec-22	24-Feb-23	44	01-Apr-23	29-May-23	-45																				
P30-BP71.30	BP - Airift, Cage Install and Concrete	25-Feb-23	07-Mar-23	9	30-May-23	08-Jun-23	31																				
03																											
P30-BP64.10	BP - Excavation	18-Feb-23	24-Feb-23	12	20-Feb-23 A	06-Mar-23 A																					
P30-BP64.20	BP - RCD Drilling	25-Feb-23	30-Mar-23	5	07-Mar-23 A	13-Mar-23 A																					
P30-BP64.30	BP - Airift, Cage Install and Concrete	31-Mar-23	13-Apr-23	7	14-Mar-23 A	22-Mar-23 A																					
04																											
P30-BP75.10	BP - Excavation	24-Mar-23	30-Mar-23	6	22-May-23	29-May-23	-45																				
P30-BP75.20	BP - RCD Drilling	31-Mar-23	09-May-23	29	30-May-23	04-Jul-23	-45																				
05																											
P30-BP74.10	BP - Excavation	23-Jun-22	09-May-23	305	23-Jun-22 A	04-Jul-23	-45																				
VD06																											
05																											
P28&P29-BP15.:	BP - Airift, Cage Install and Concrete	12-Jan-23	19-Jan-23	14	17-Feb-23 A	06-Mar-23 A																					
VD08																											
05																											
P24&P27-BP26.:	BP - RCD Drilling	04-Jan-23	09-Feb-23	7	22-Feb-23 A	02-Mar-23 A																					
P24&P27-BP26.:	BP - Airift, Cage Install and Concrete	10-Feb-23	18-Feb-23	14	03-Mar-23 A	20-Mar-23 A																					
03																											
P28&P29-BP17.:	BP - Excavation	27-Jun-23	04-Jul-23	11	27-Feb-23 A	11-Mar-23 A																					
P28&P29-BP17.:	BP - RCD Drilling	05-Jul-23	07-Aug-23	6	13-Mar-23 A	20-Mar-23 A																					
P28&P29-BP17.:	BP - Airift, Cage Install and Concrete	08-Aug-23	16-Aug-23	12	21-Mar-23 A	03-Apr-23	82																				
03																											
P24&P27-BP32.:	BP - Excavation	03-Feb-23	09-Feb-23	6	25-Mar-23	31-Mar-23	-64																				
P24&P27-BP32.:	BP - RCD Drilling	10-Feb-23	15-Mar-23	29	01-Apr-23	10-May-23	-64																				
P24&P27-BP32.:	BP - Airift, Cage Install and Concrete	16-Mar-23	24-Mar-23	8	11-May-23	19-May-23	47																				
04																											
P24&P27-BP20.:	BP - Excavation	09-Mar-23	15-Mar-23	6	04-May-23	10-May-23	-64																				
P24&P27-BP20.:	BP - RCD Drilling	16-Mar-23	22-Apr-23	29	11-May-23	14-Jun-23	-64																				
P24&P27-BP20.:	BP - Airift, Cage Install and Concrete	24-Apr-23	03-May-23	8	15-Jun-23	24-Jun-23	18																				
05																											
P24&P27-BP19.:	BP - Excavation	17-Apr-23	22-Apr-23	6	08-Jun-23	14-Jun-23	-64																				
P24&P27-BP19.:	BP - RCD Drilling	24-Apr-23	29-May-23	29	15-Jun-23	20-Jul-23	-64																				
VD12																											
05																											
CBA-BPC58Ka.1	BP - Excavation	14-Jul-23	20-Jul-23	7	04-Mar-23 A	13-Mar-23 A																					
CBA-BPC58Ka.2	BP - RCD Drilling	21-Jul-23	01-Aug-23	1	14-Mar-23 A	15-Mar-23 A																					


ID: 2BC-20230324_bw
 Data Date: 25-Mar-23
 Print Date: 24-Mar-23_17:18
 Page 5 of 14

- Planned
- Critical
- Actual
- Planned MS
- Critical MS
- Actual MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 24 March 2023
Based on CMWP Rev.0 (3rd Draft)



Date	Revision	Checked	Approved
4-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C

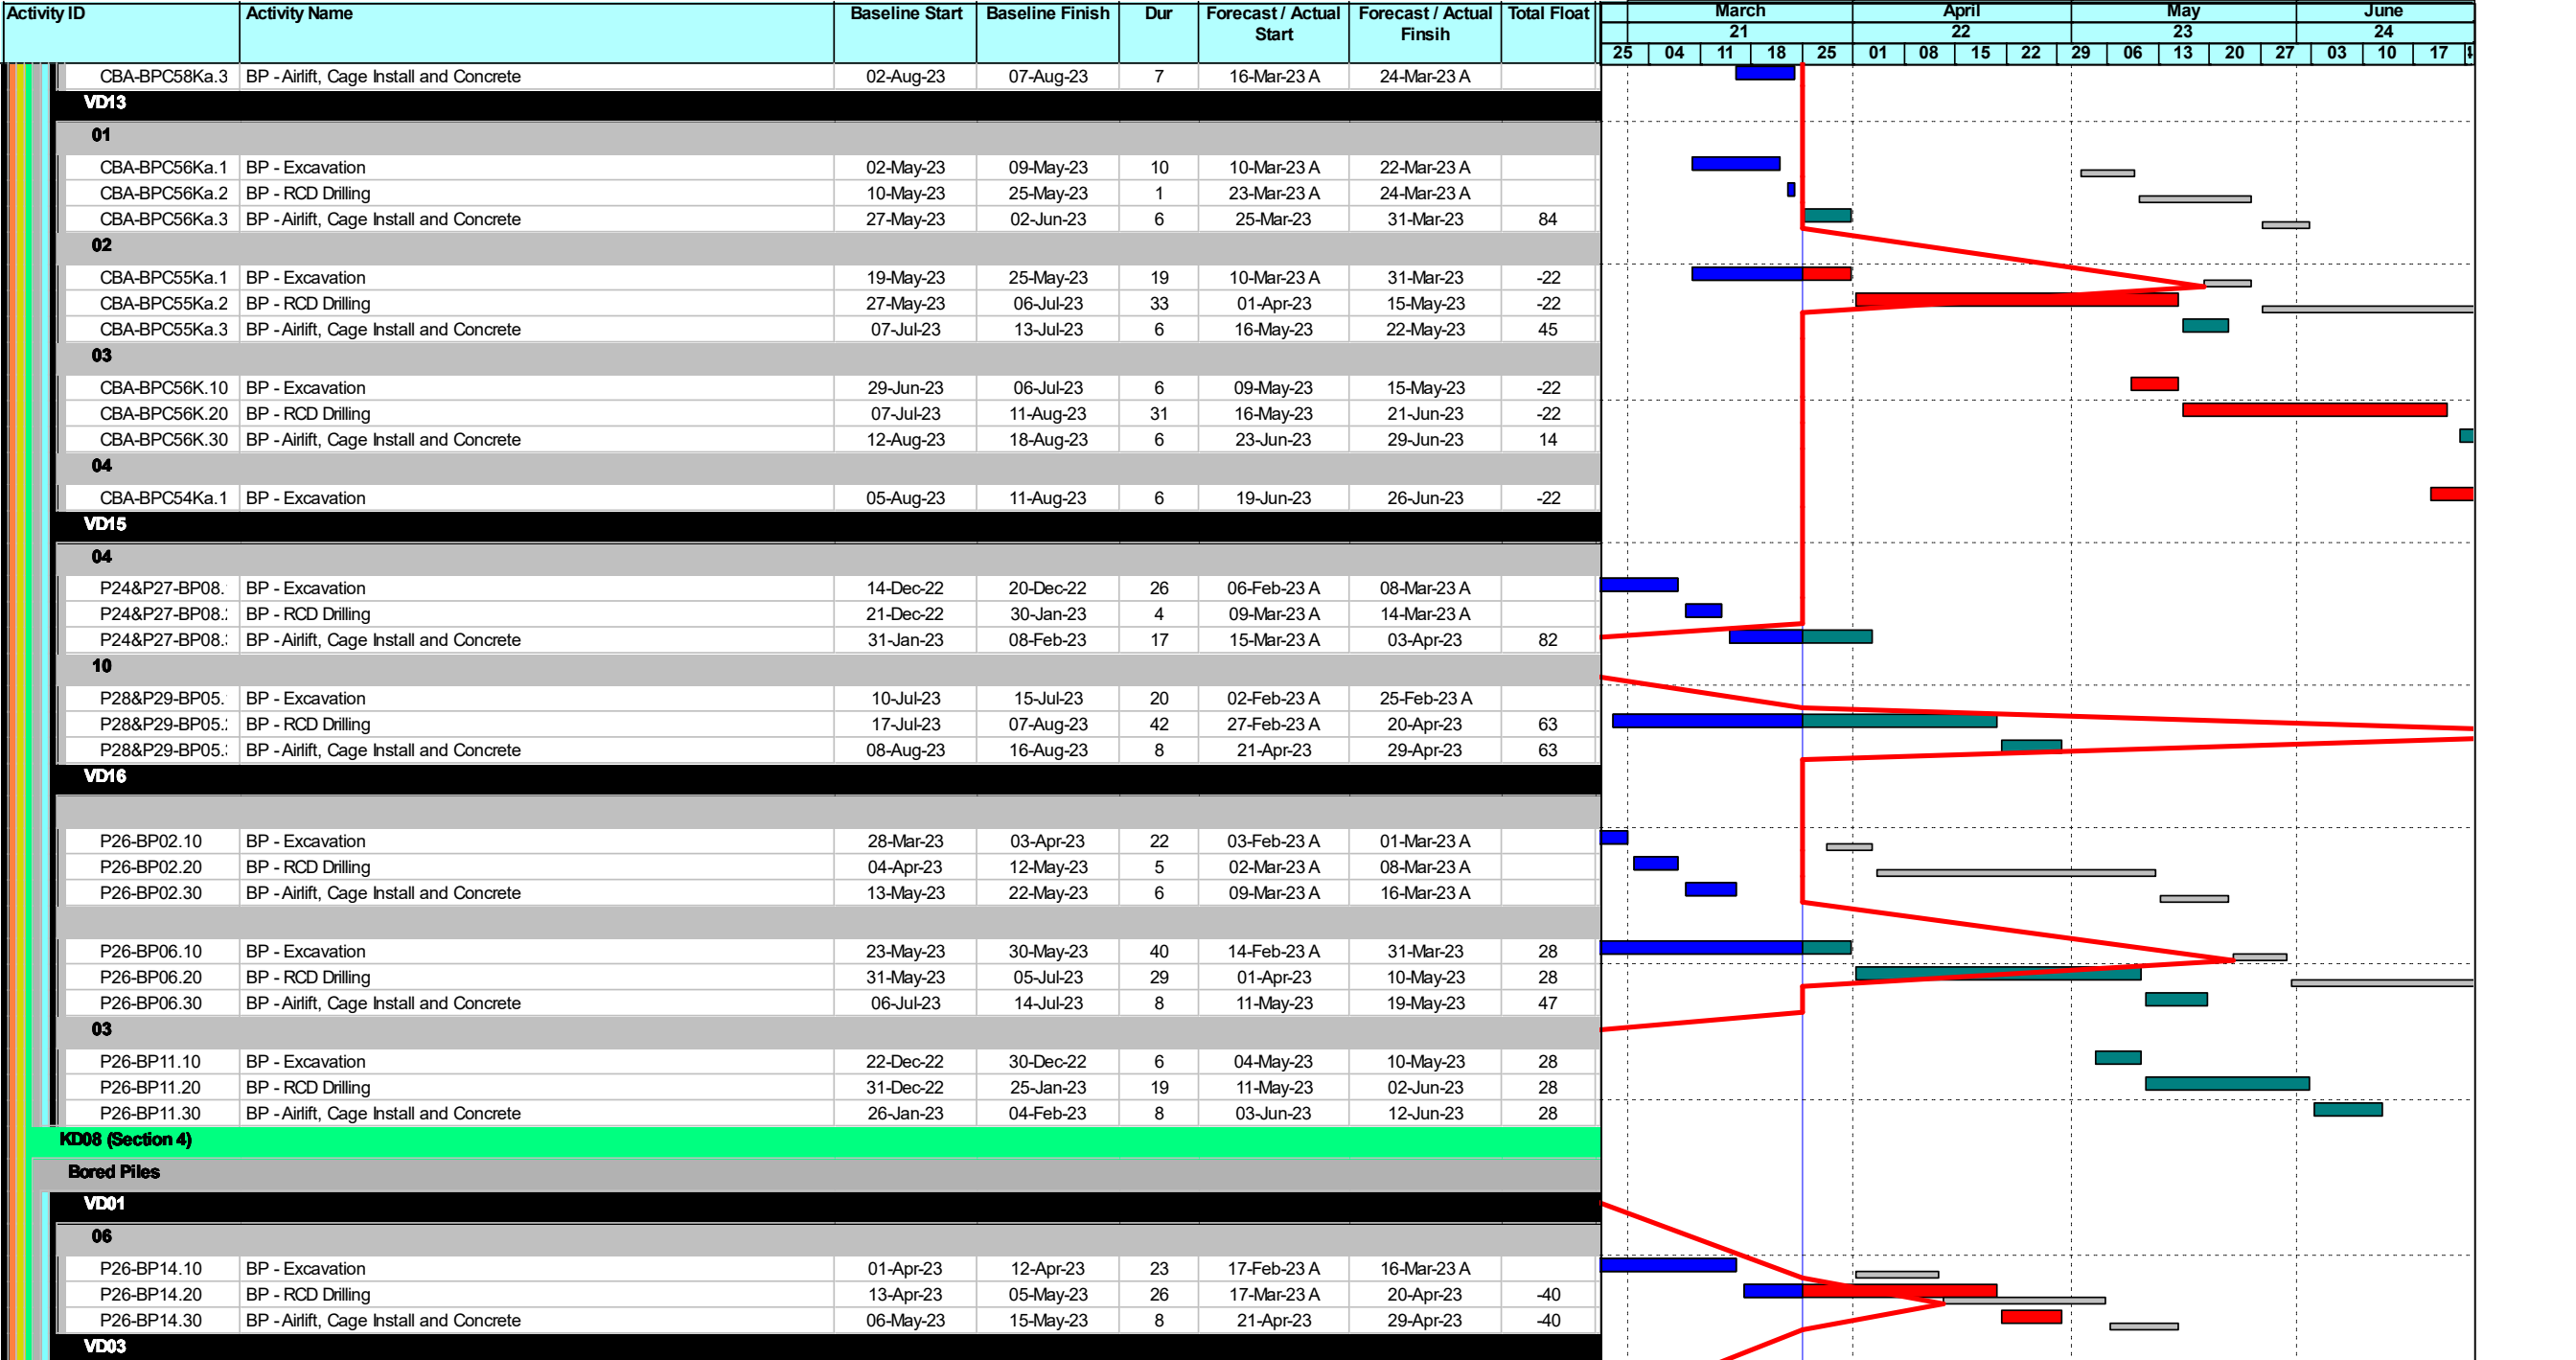








	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS

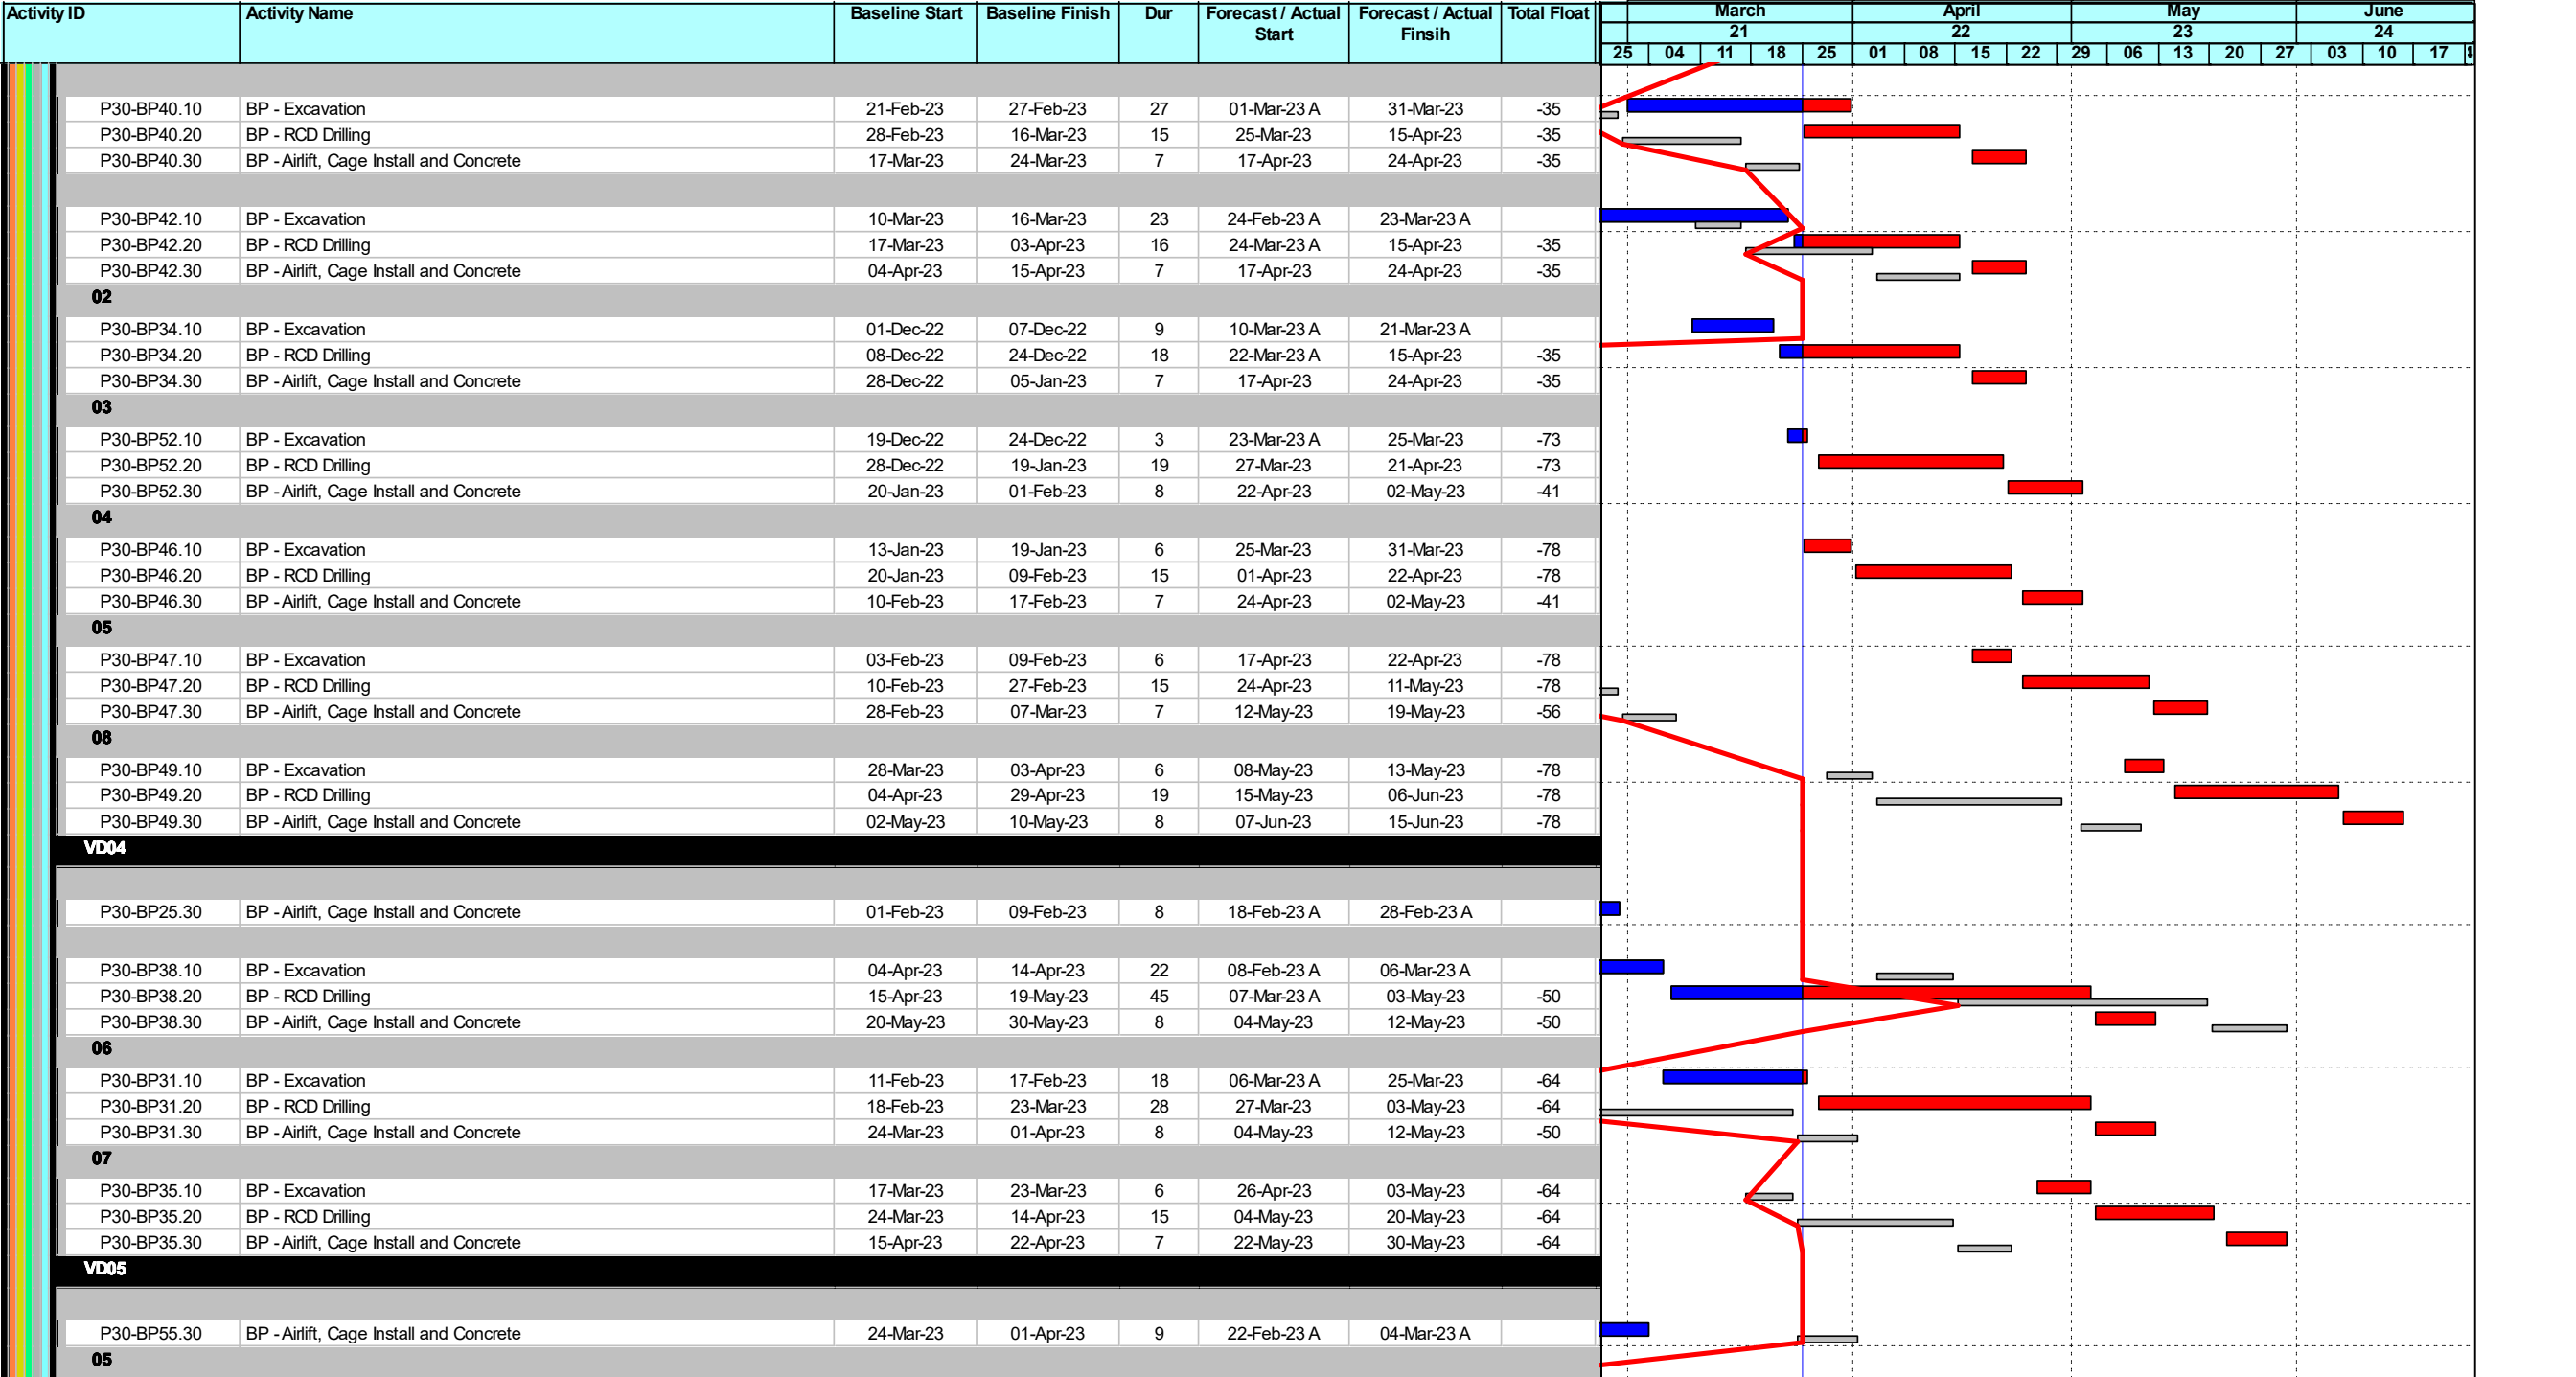West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 24 March 2023
 Based on CMWP Rev.0 (3rd Draft)



Date	Revision	Checked	Approved
4-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C










	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 24 March 2023
 Based on CMWP Rev.0 (3rd Draft)

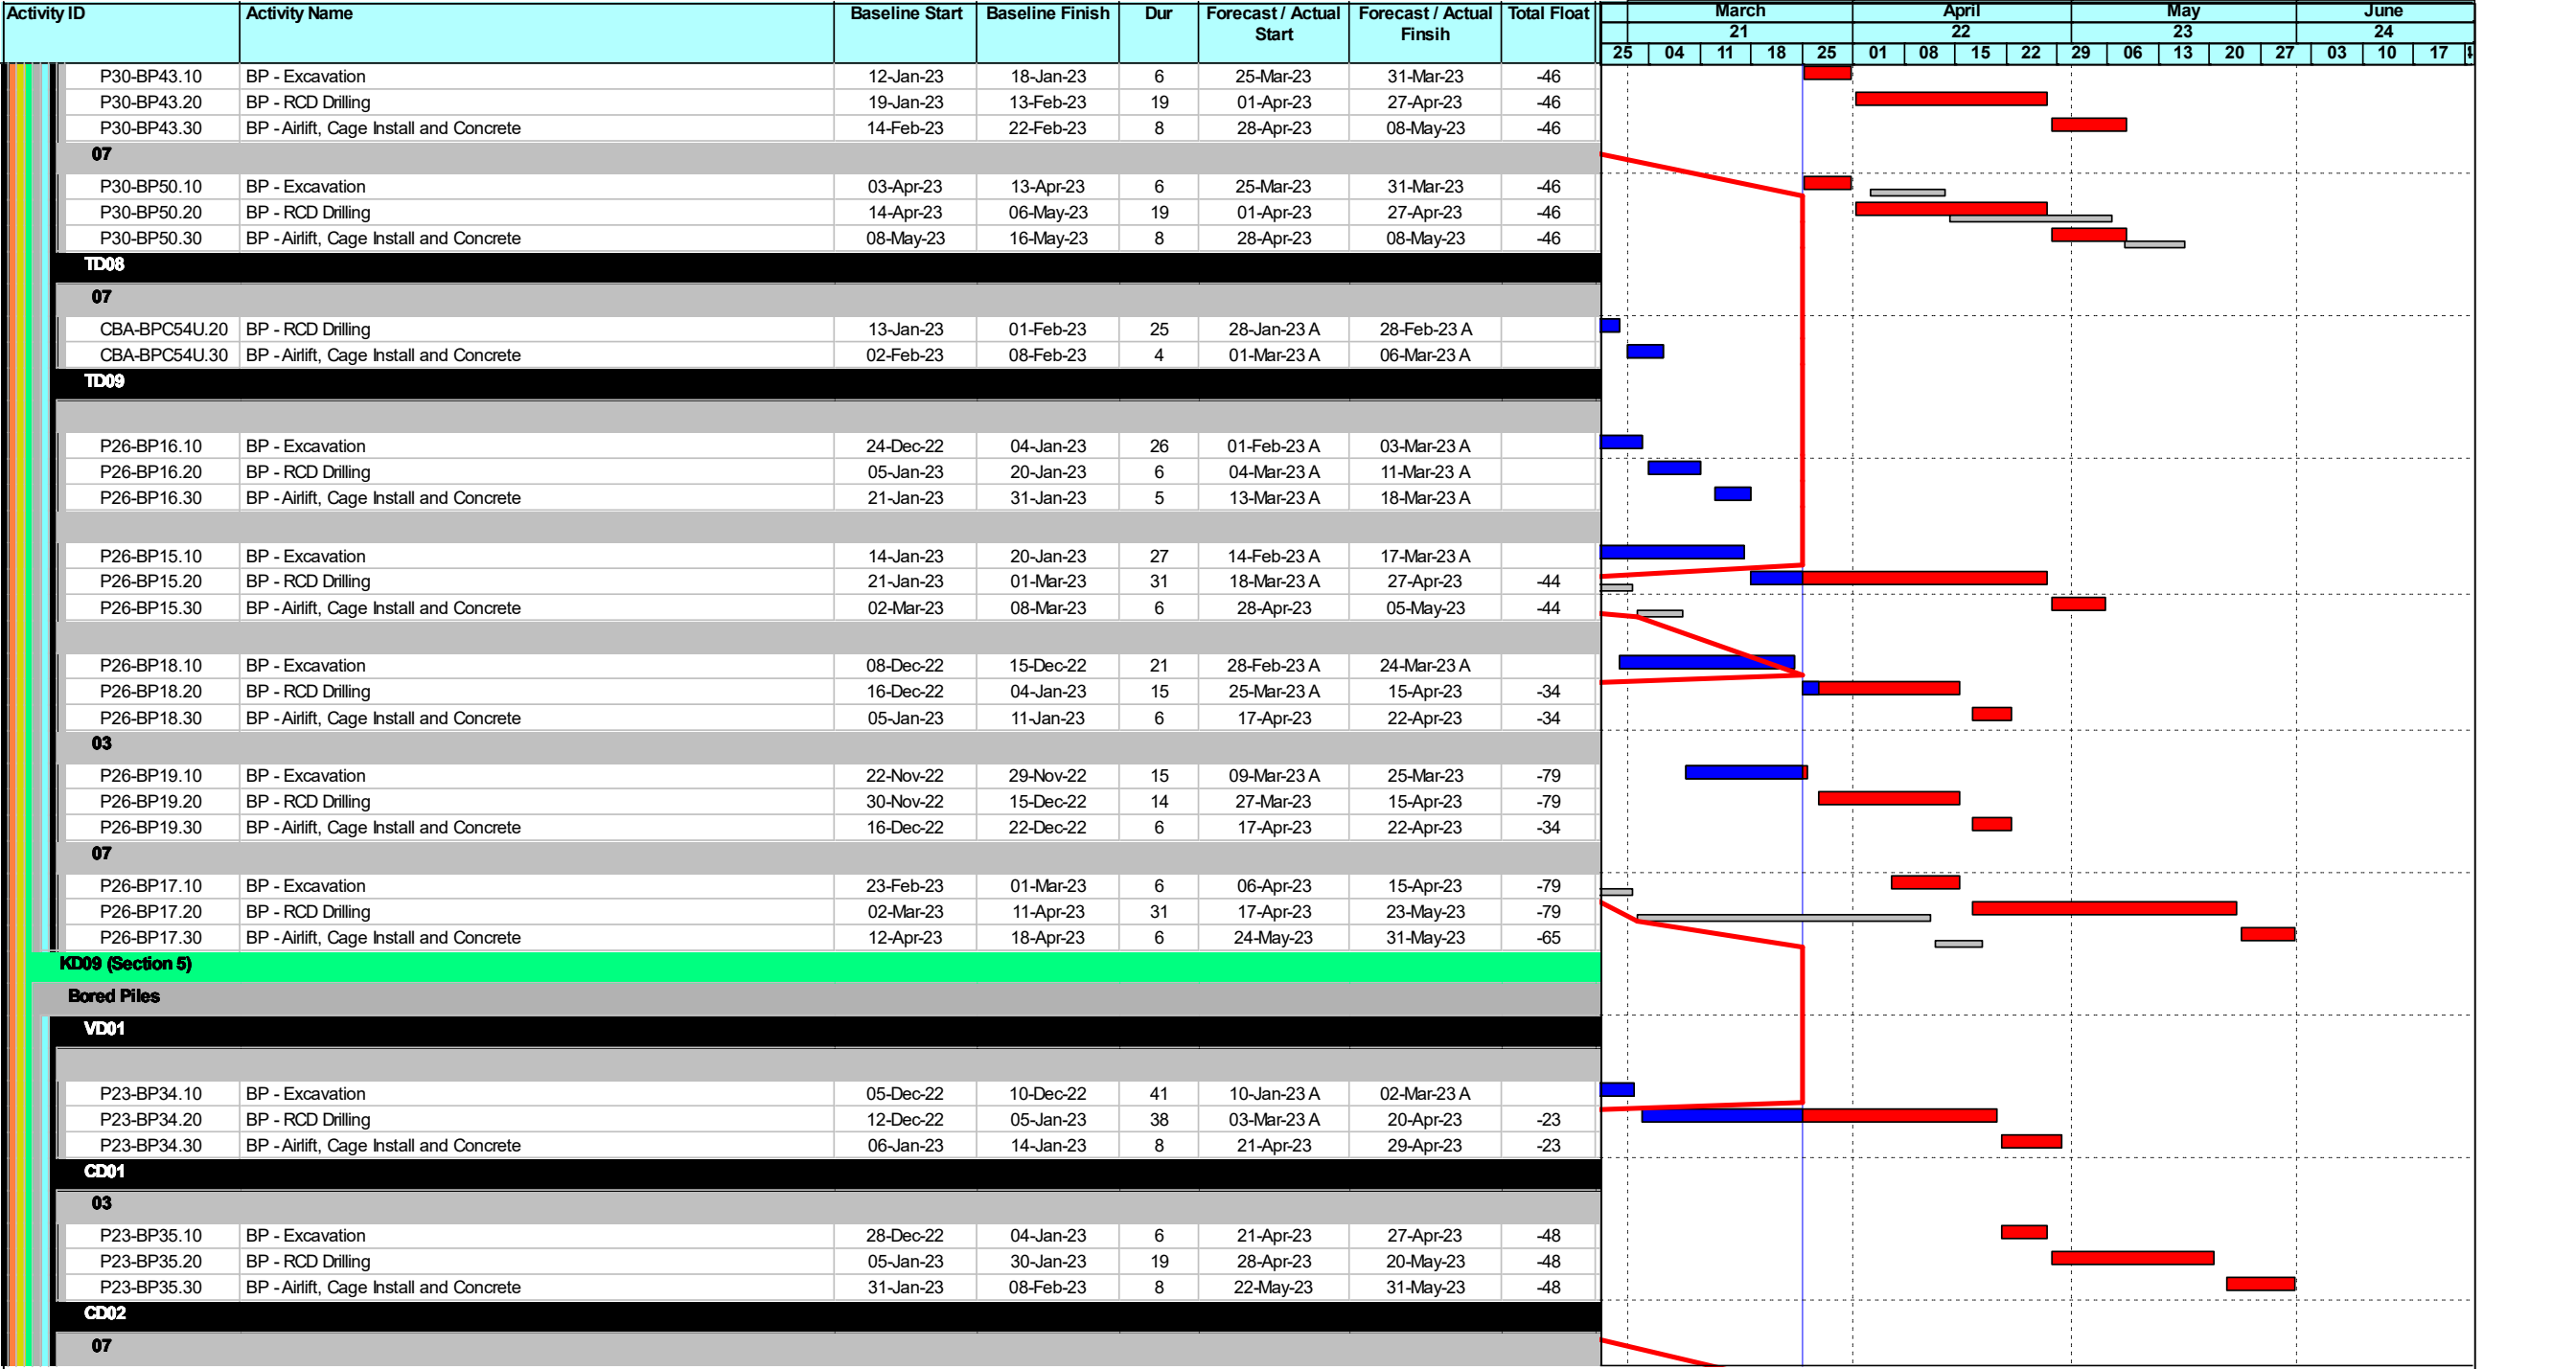

Date	Revision	Checked	Approved
4-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C










	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS

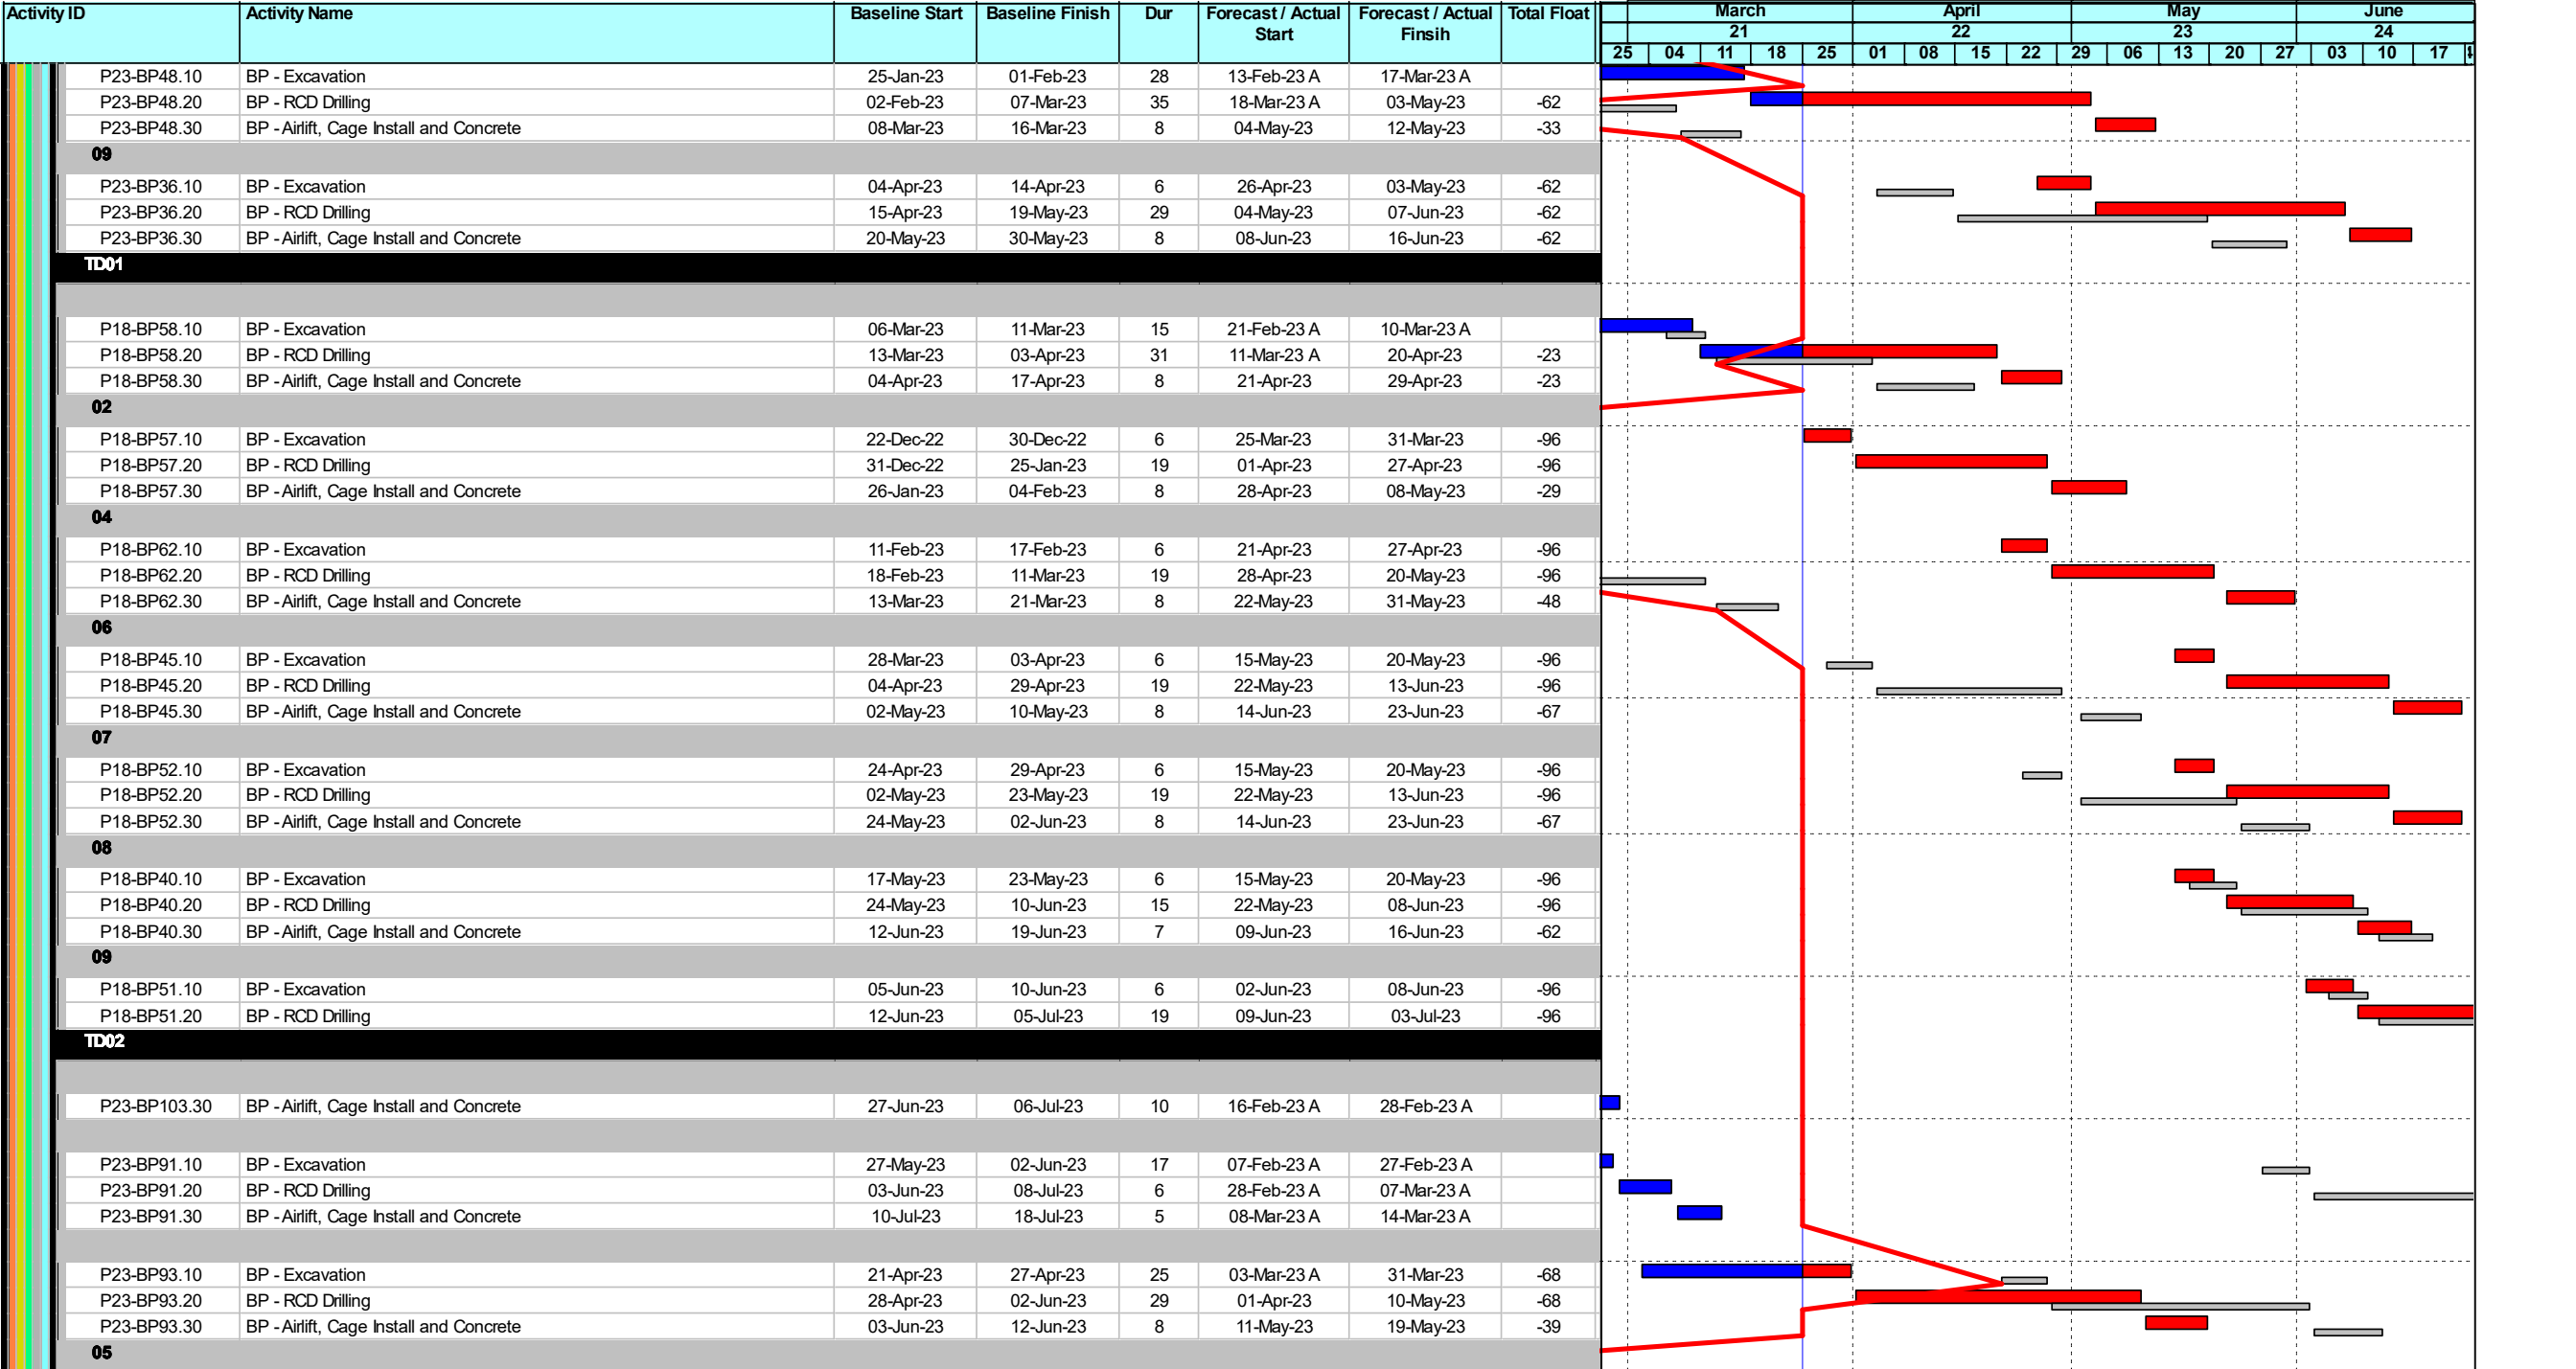West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 24 March 2023
 Based on CMWP Rev.0 (3rd Draft)



Date	Revision	Checked	Approved
4-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C





	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 24 March 2023
Based on CMWP Rev.0 (3rd Draft)



Date	Revision	Checked	Approved
4-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C

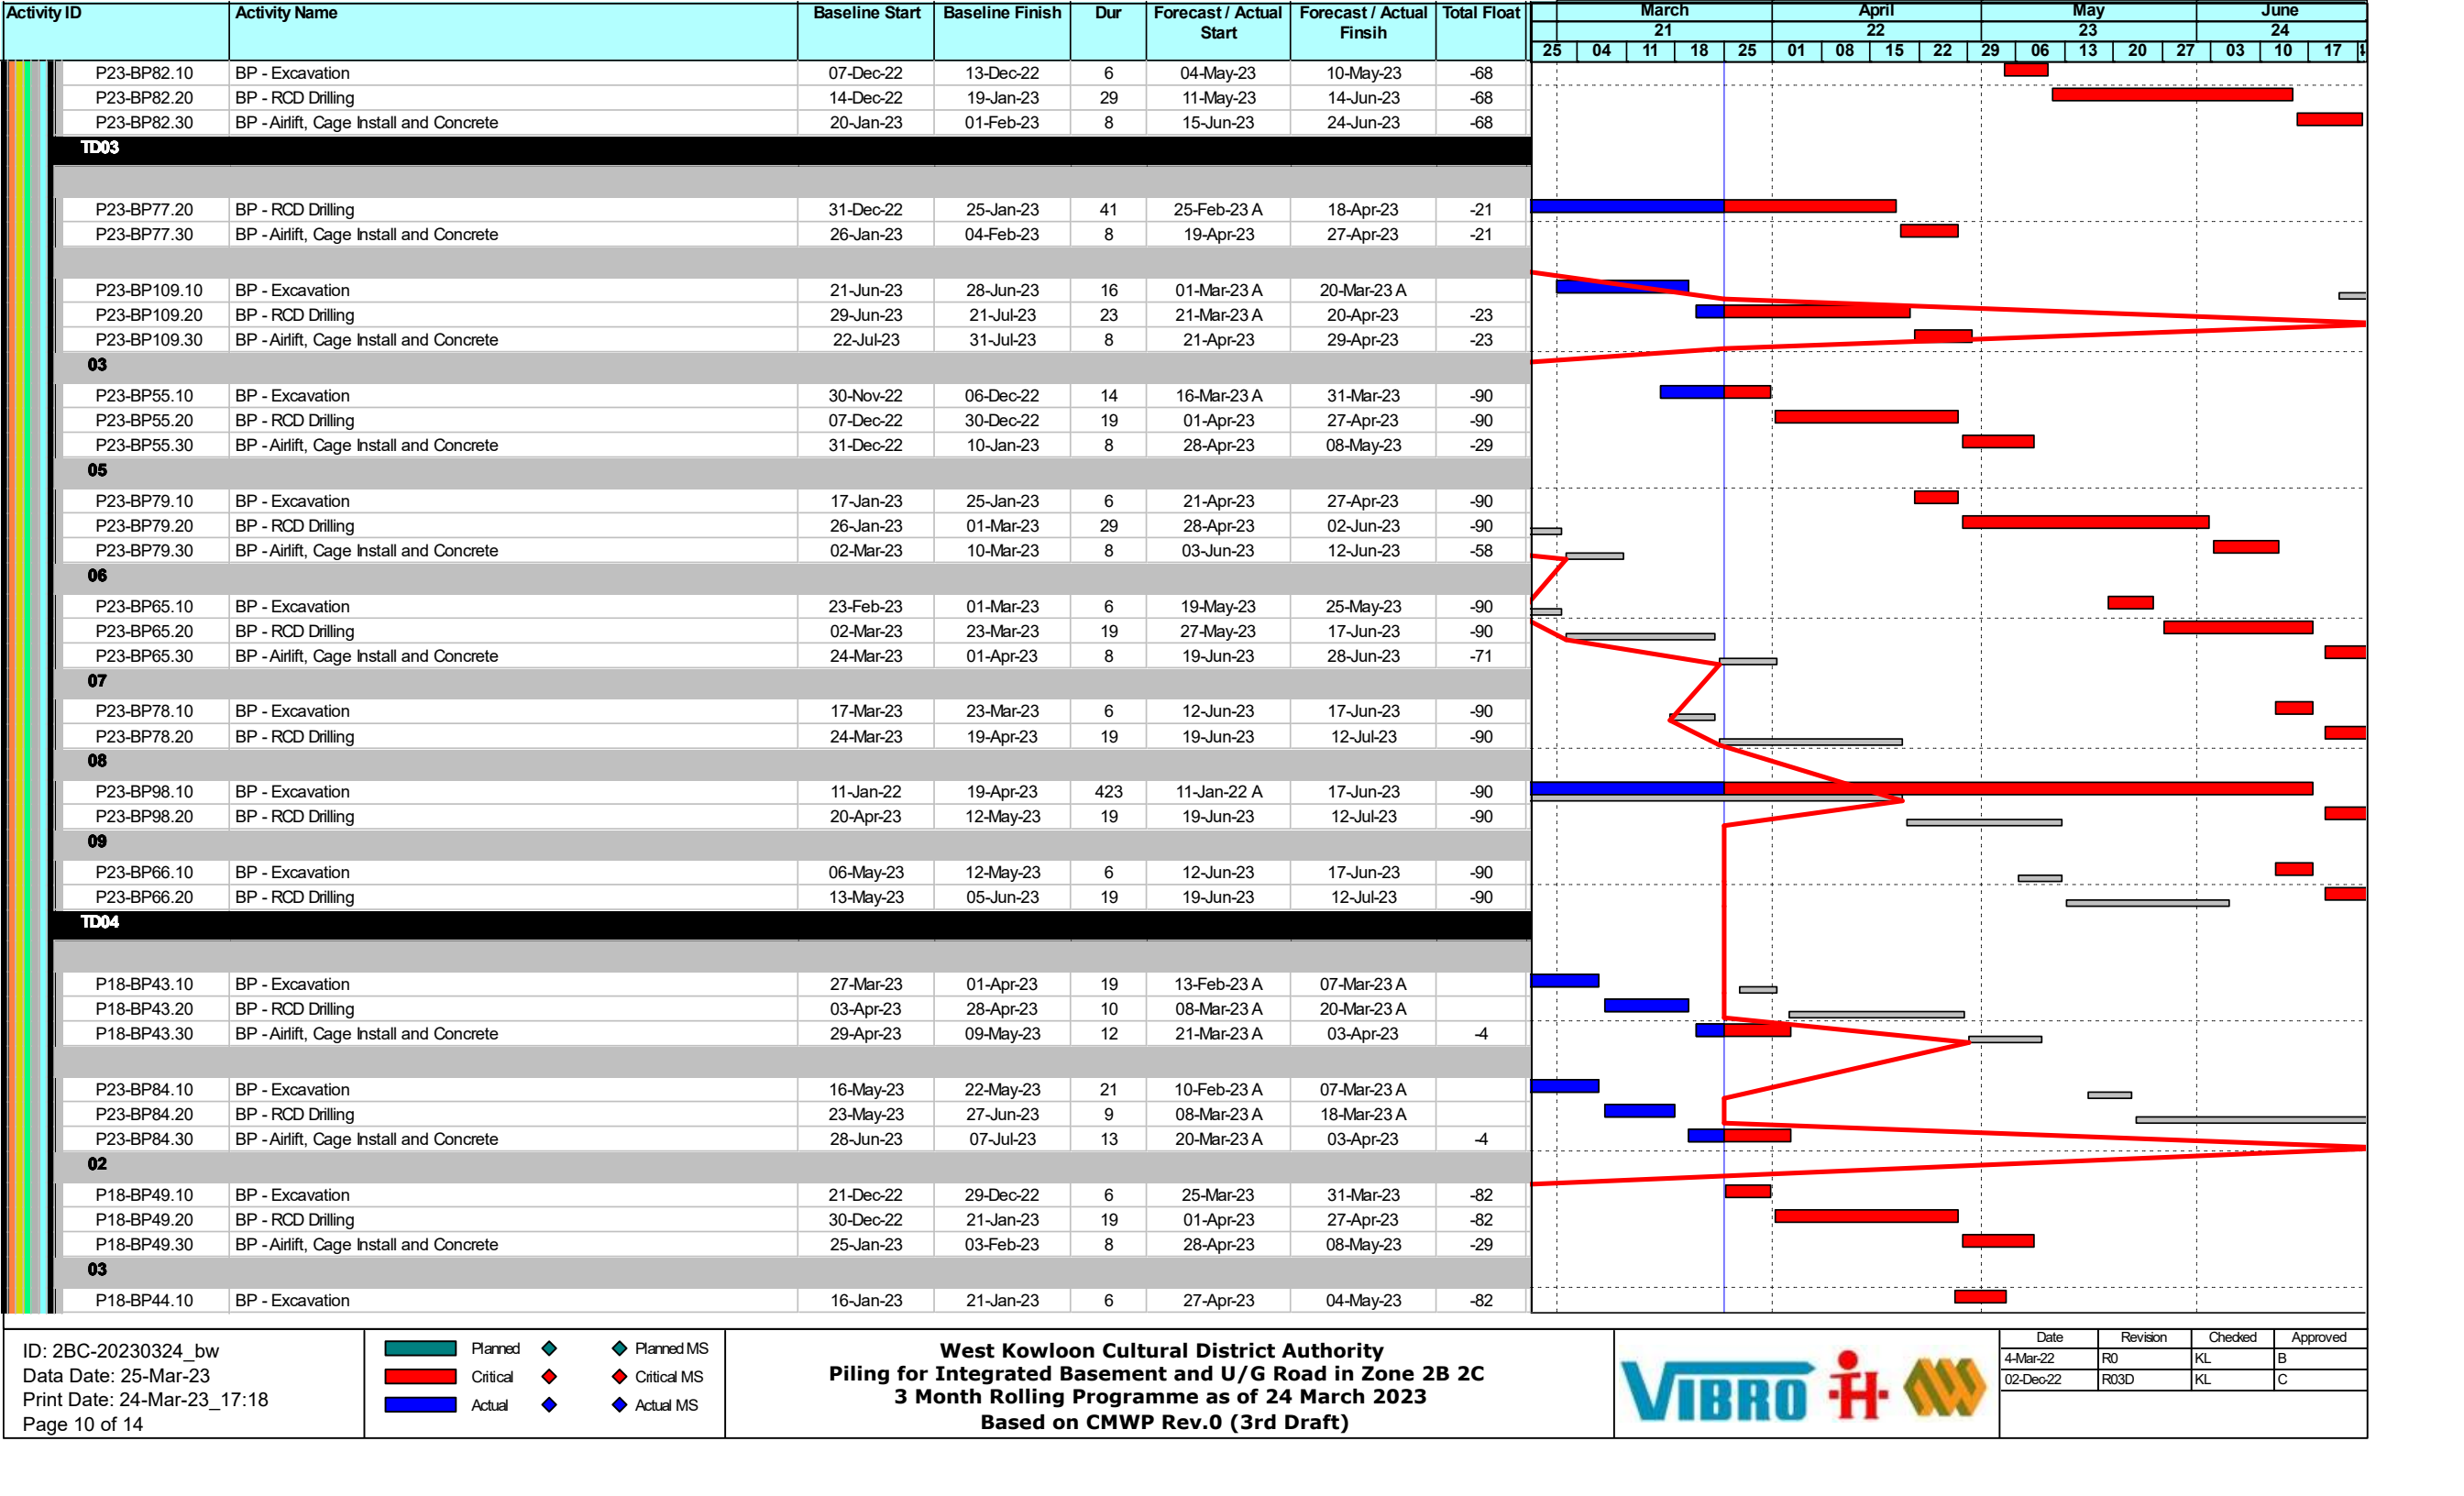

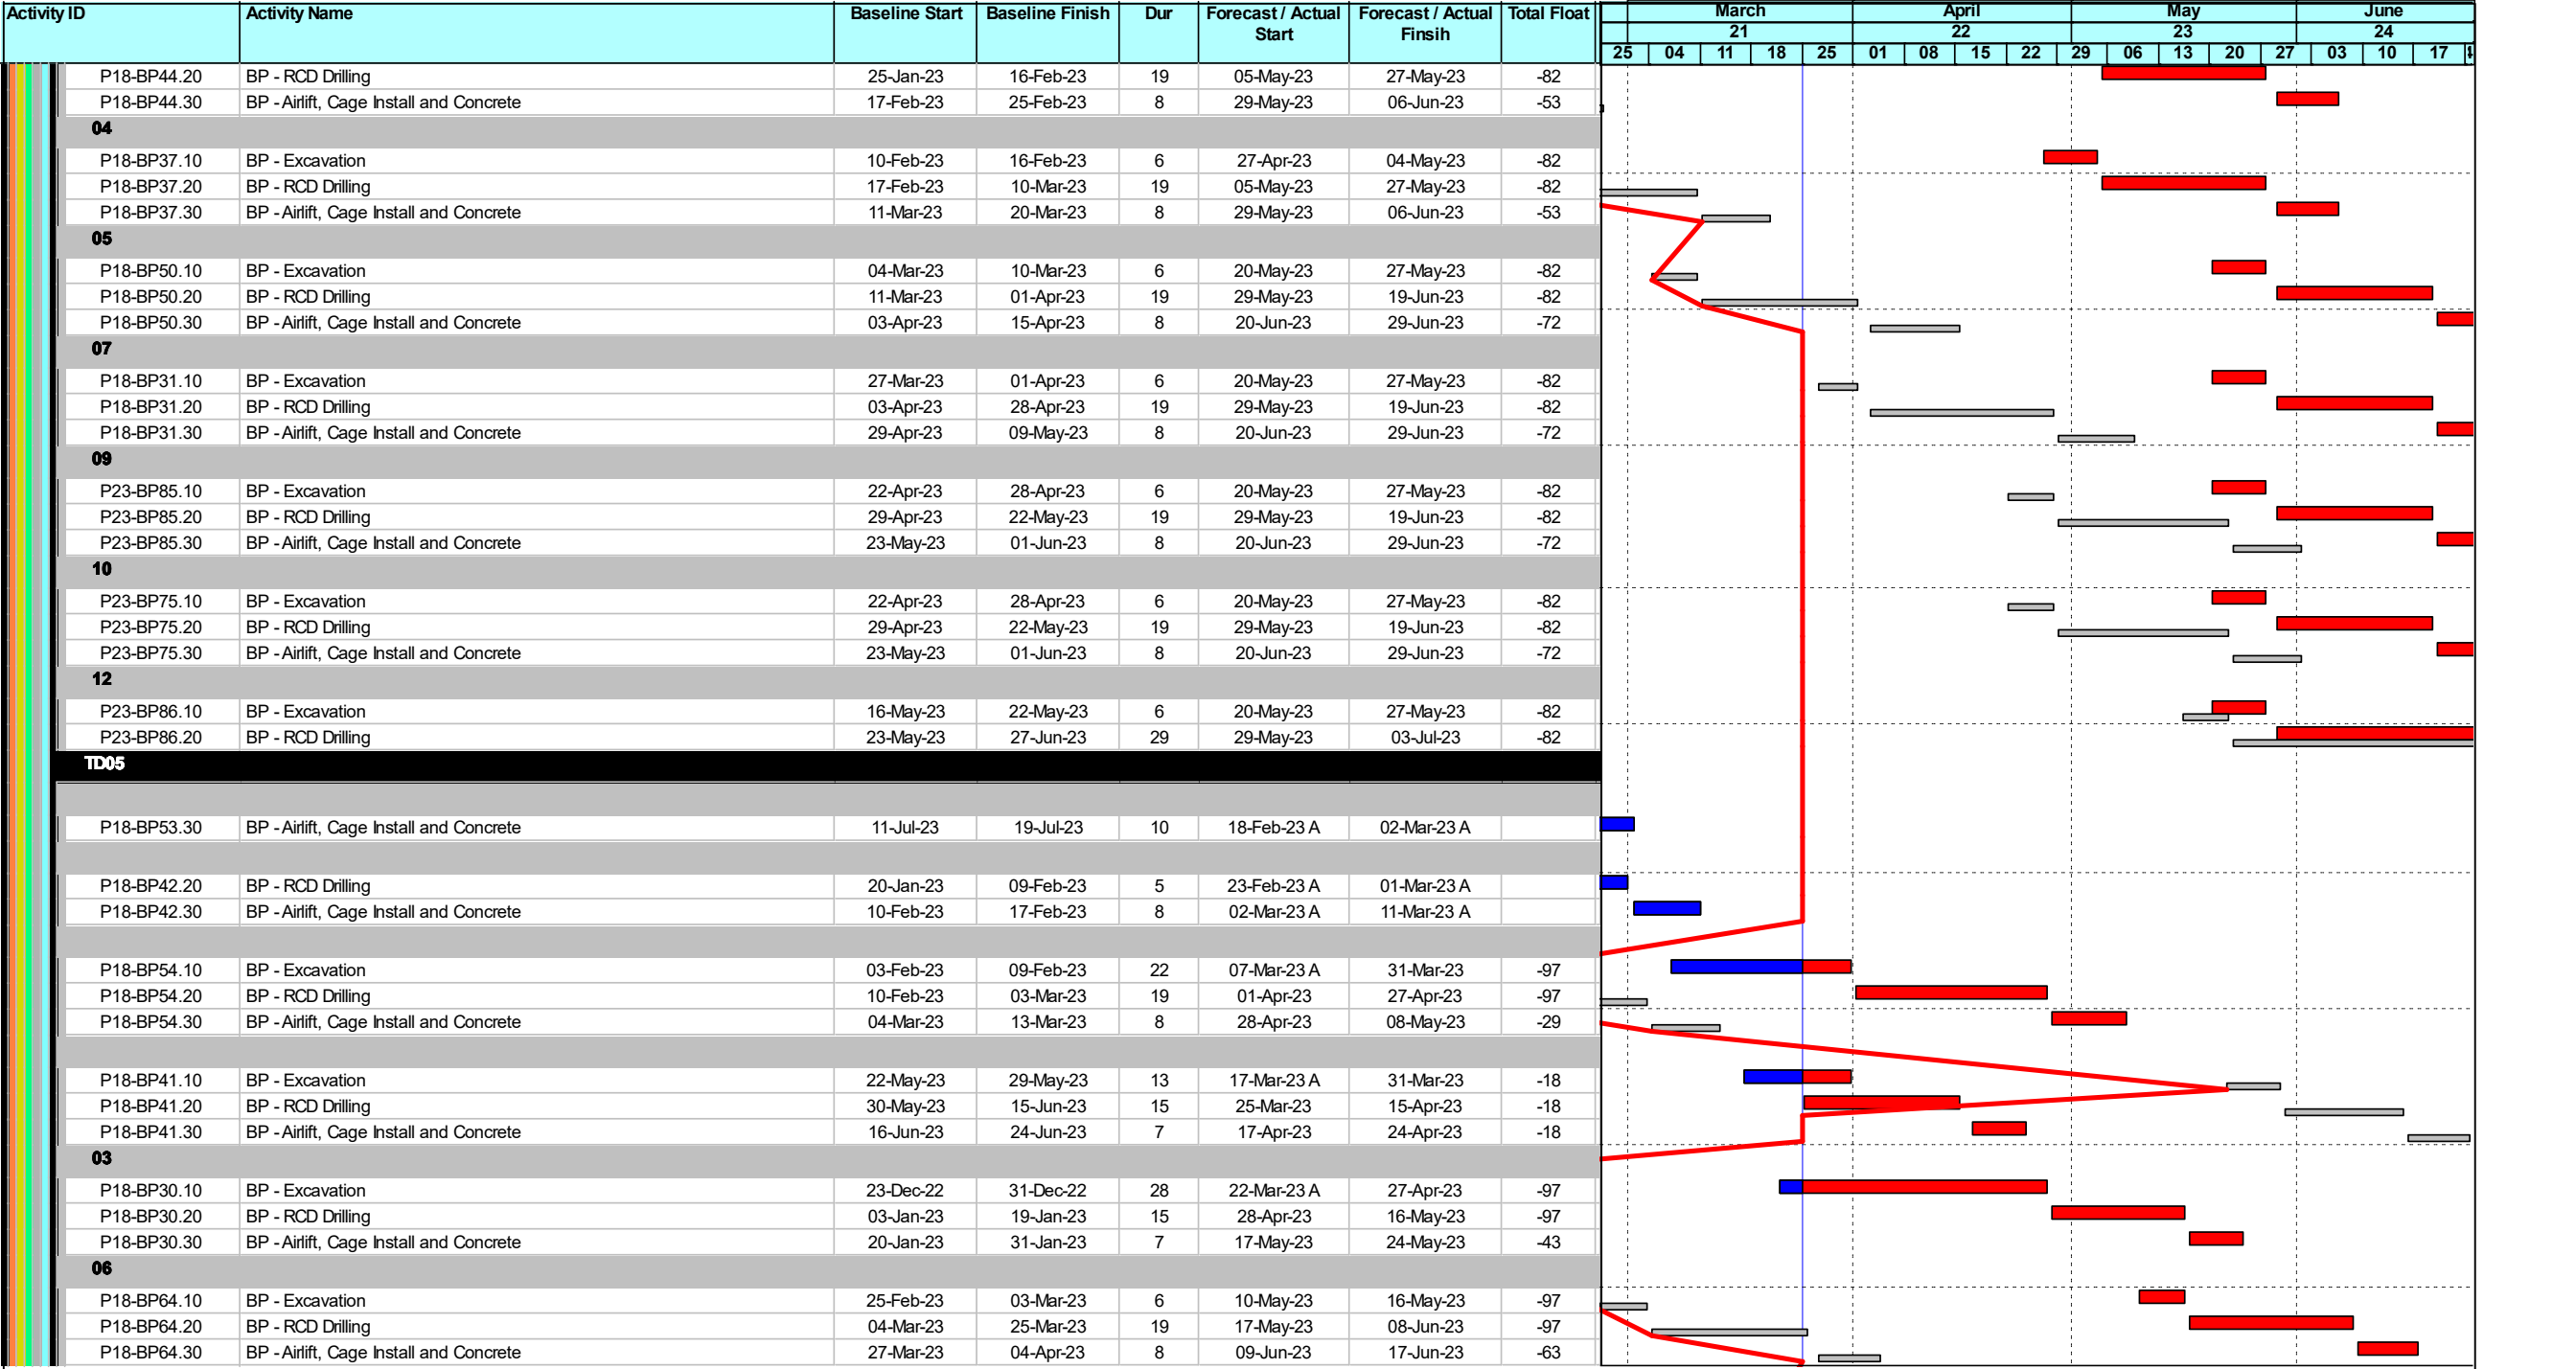








	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 24 March 2023
 Based on CMWP Rev.0 (3rd Draft)

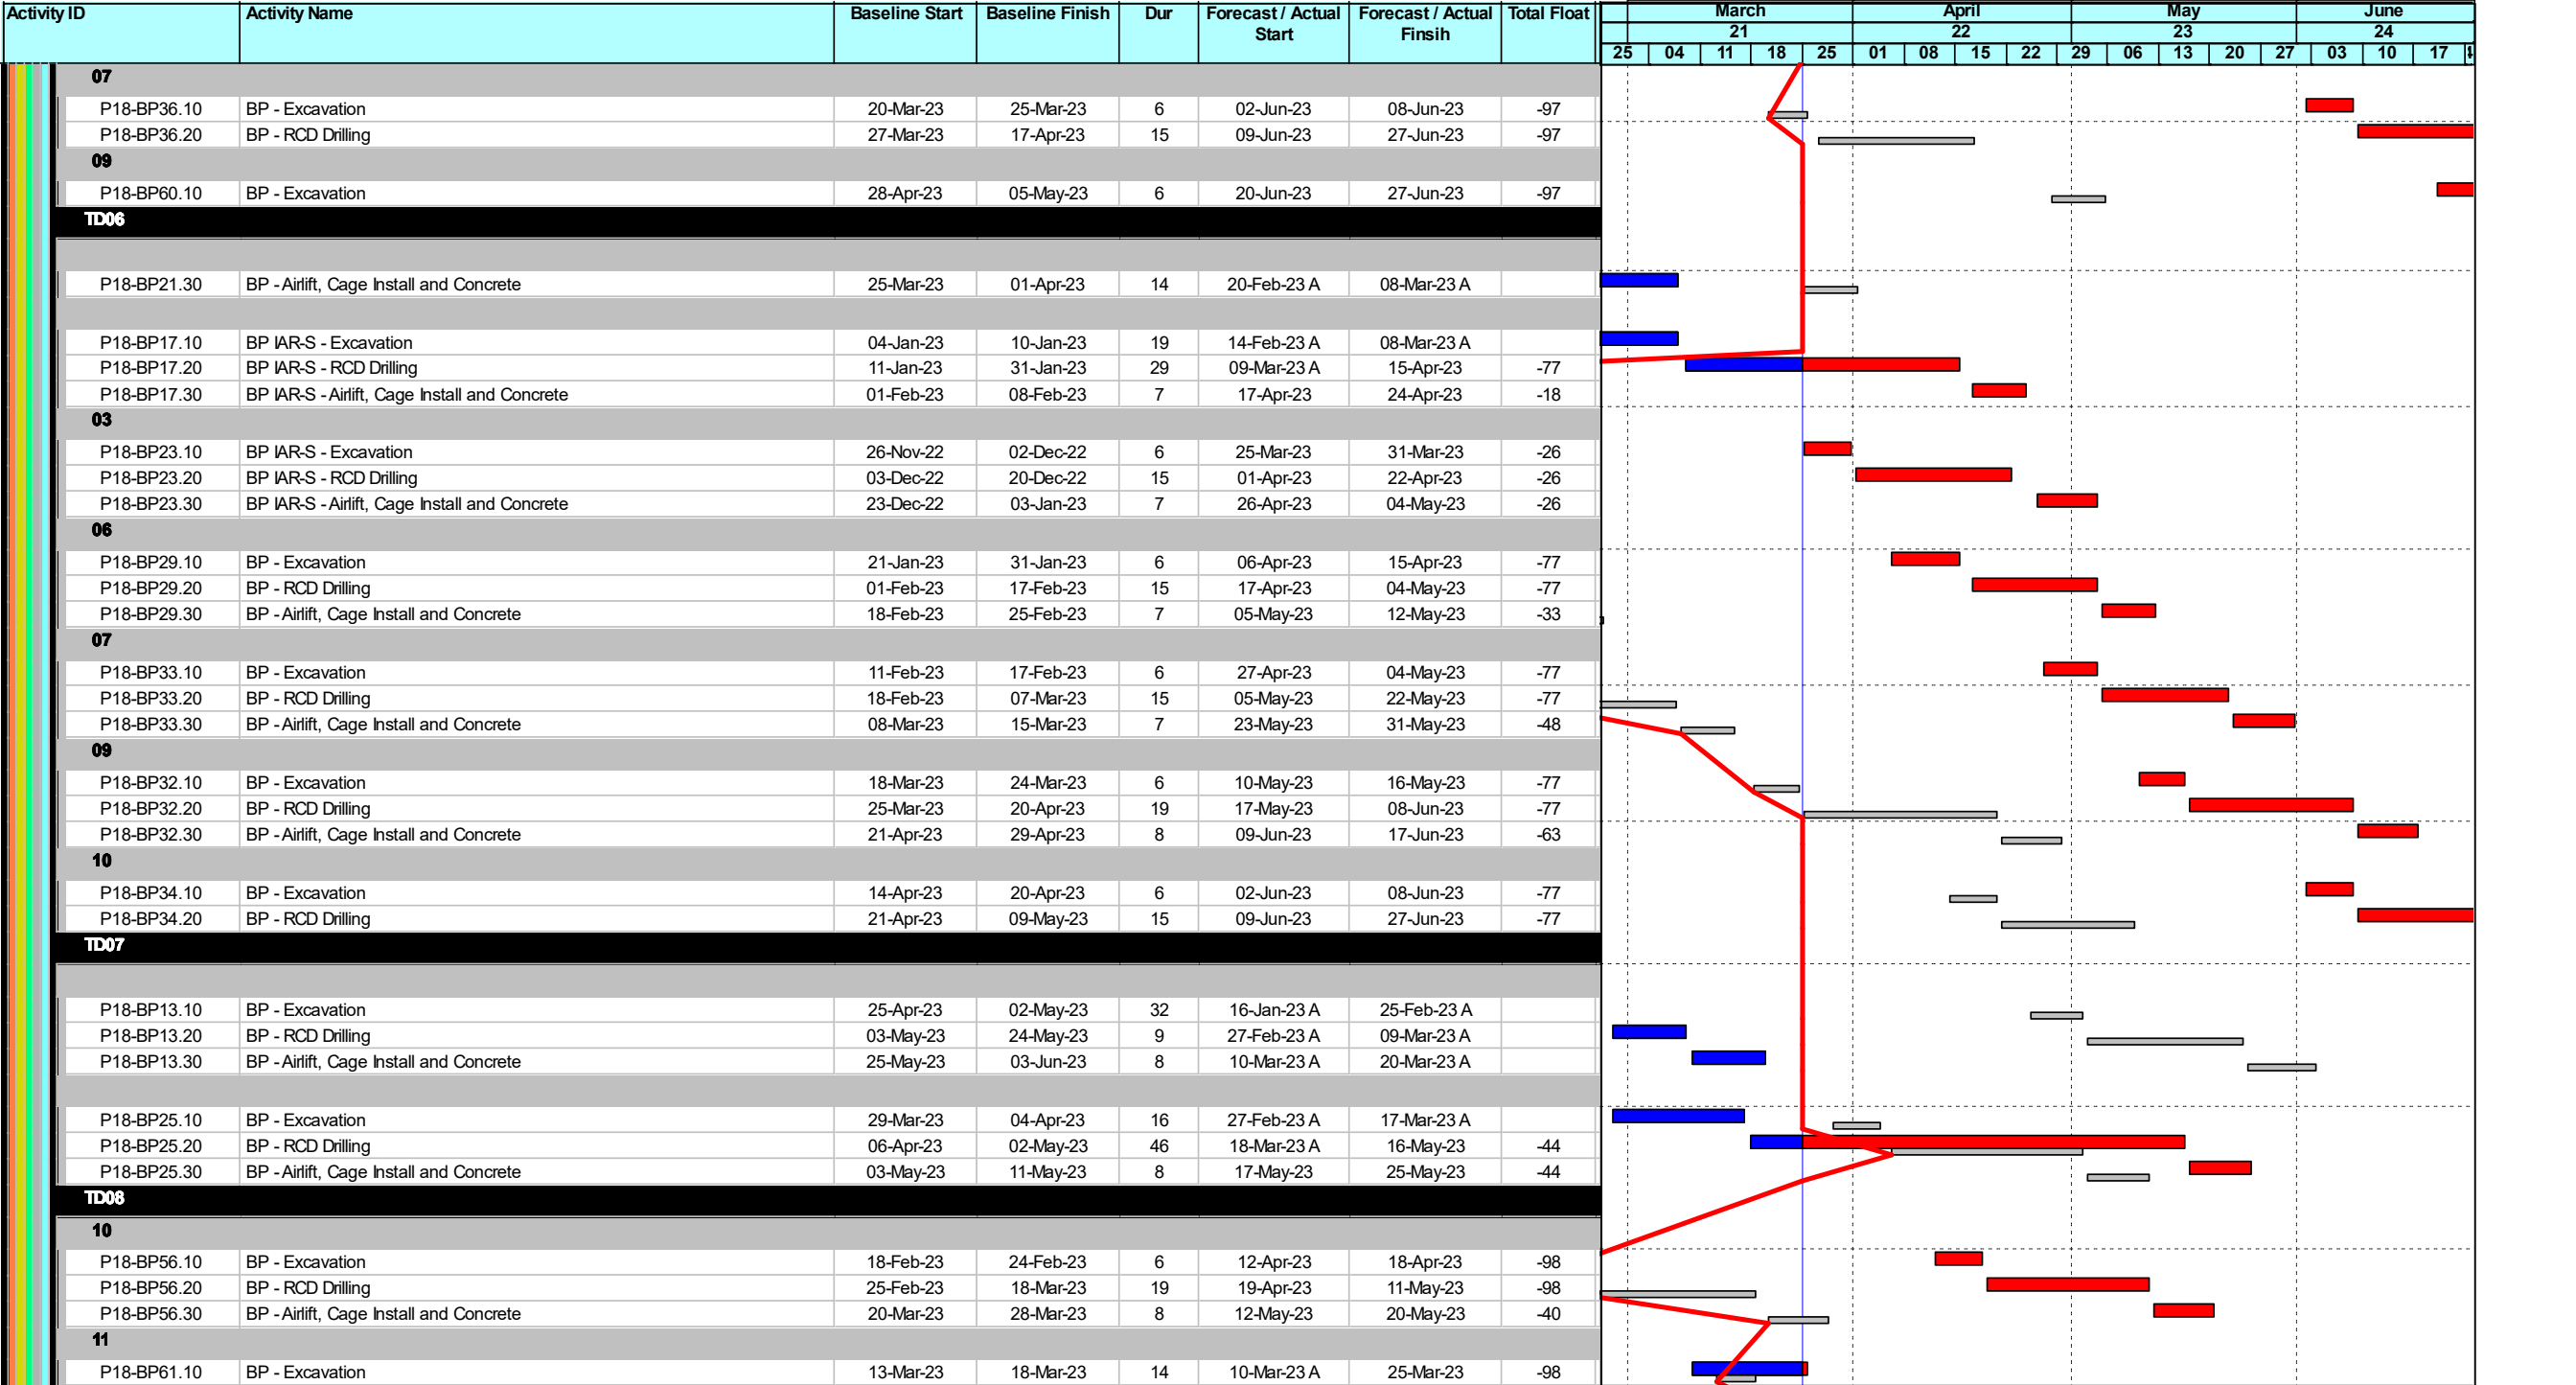

Date	Revision	Checked	Approved
4-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C




	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 24 March 2023
Based on CMWP Rev.0 (3rd Draft)



Date	Revision	Checked	Approved
4-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C

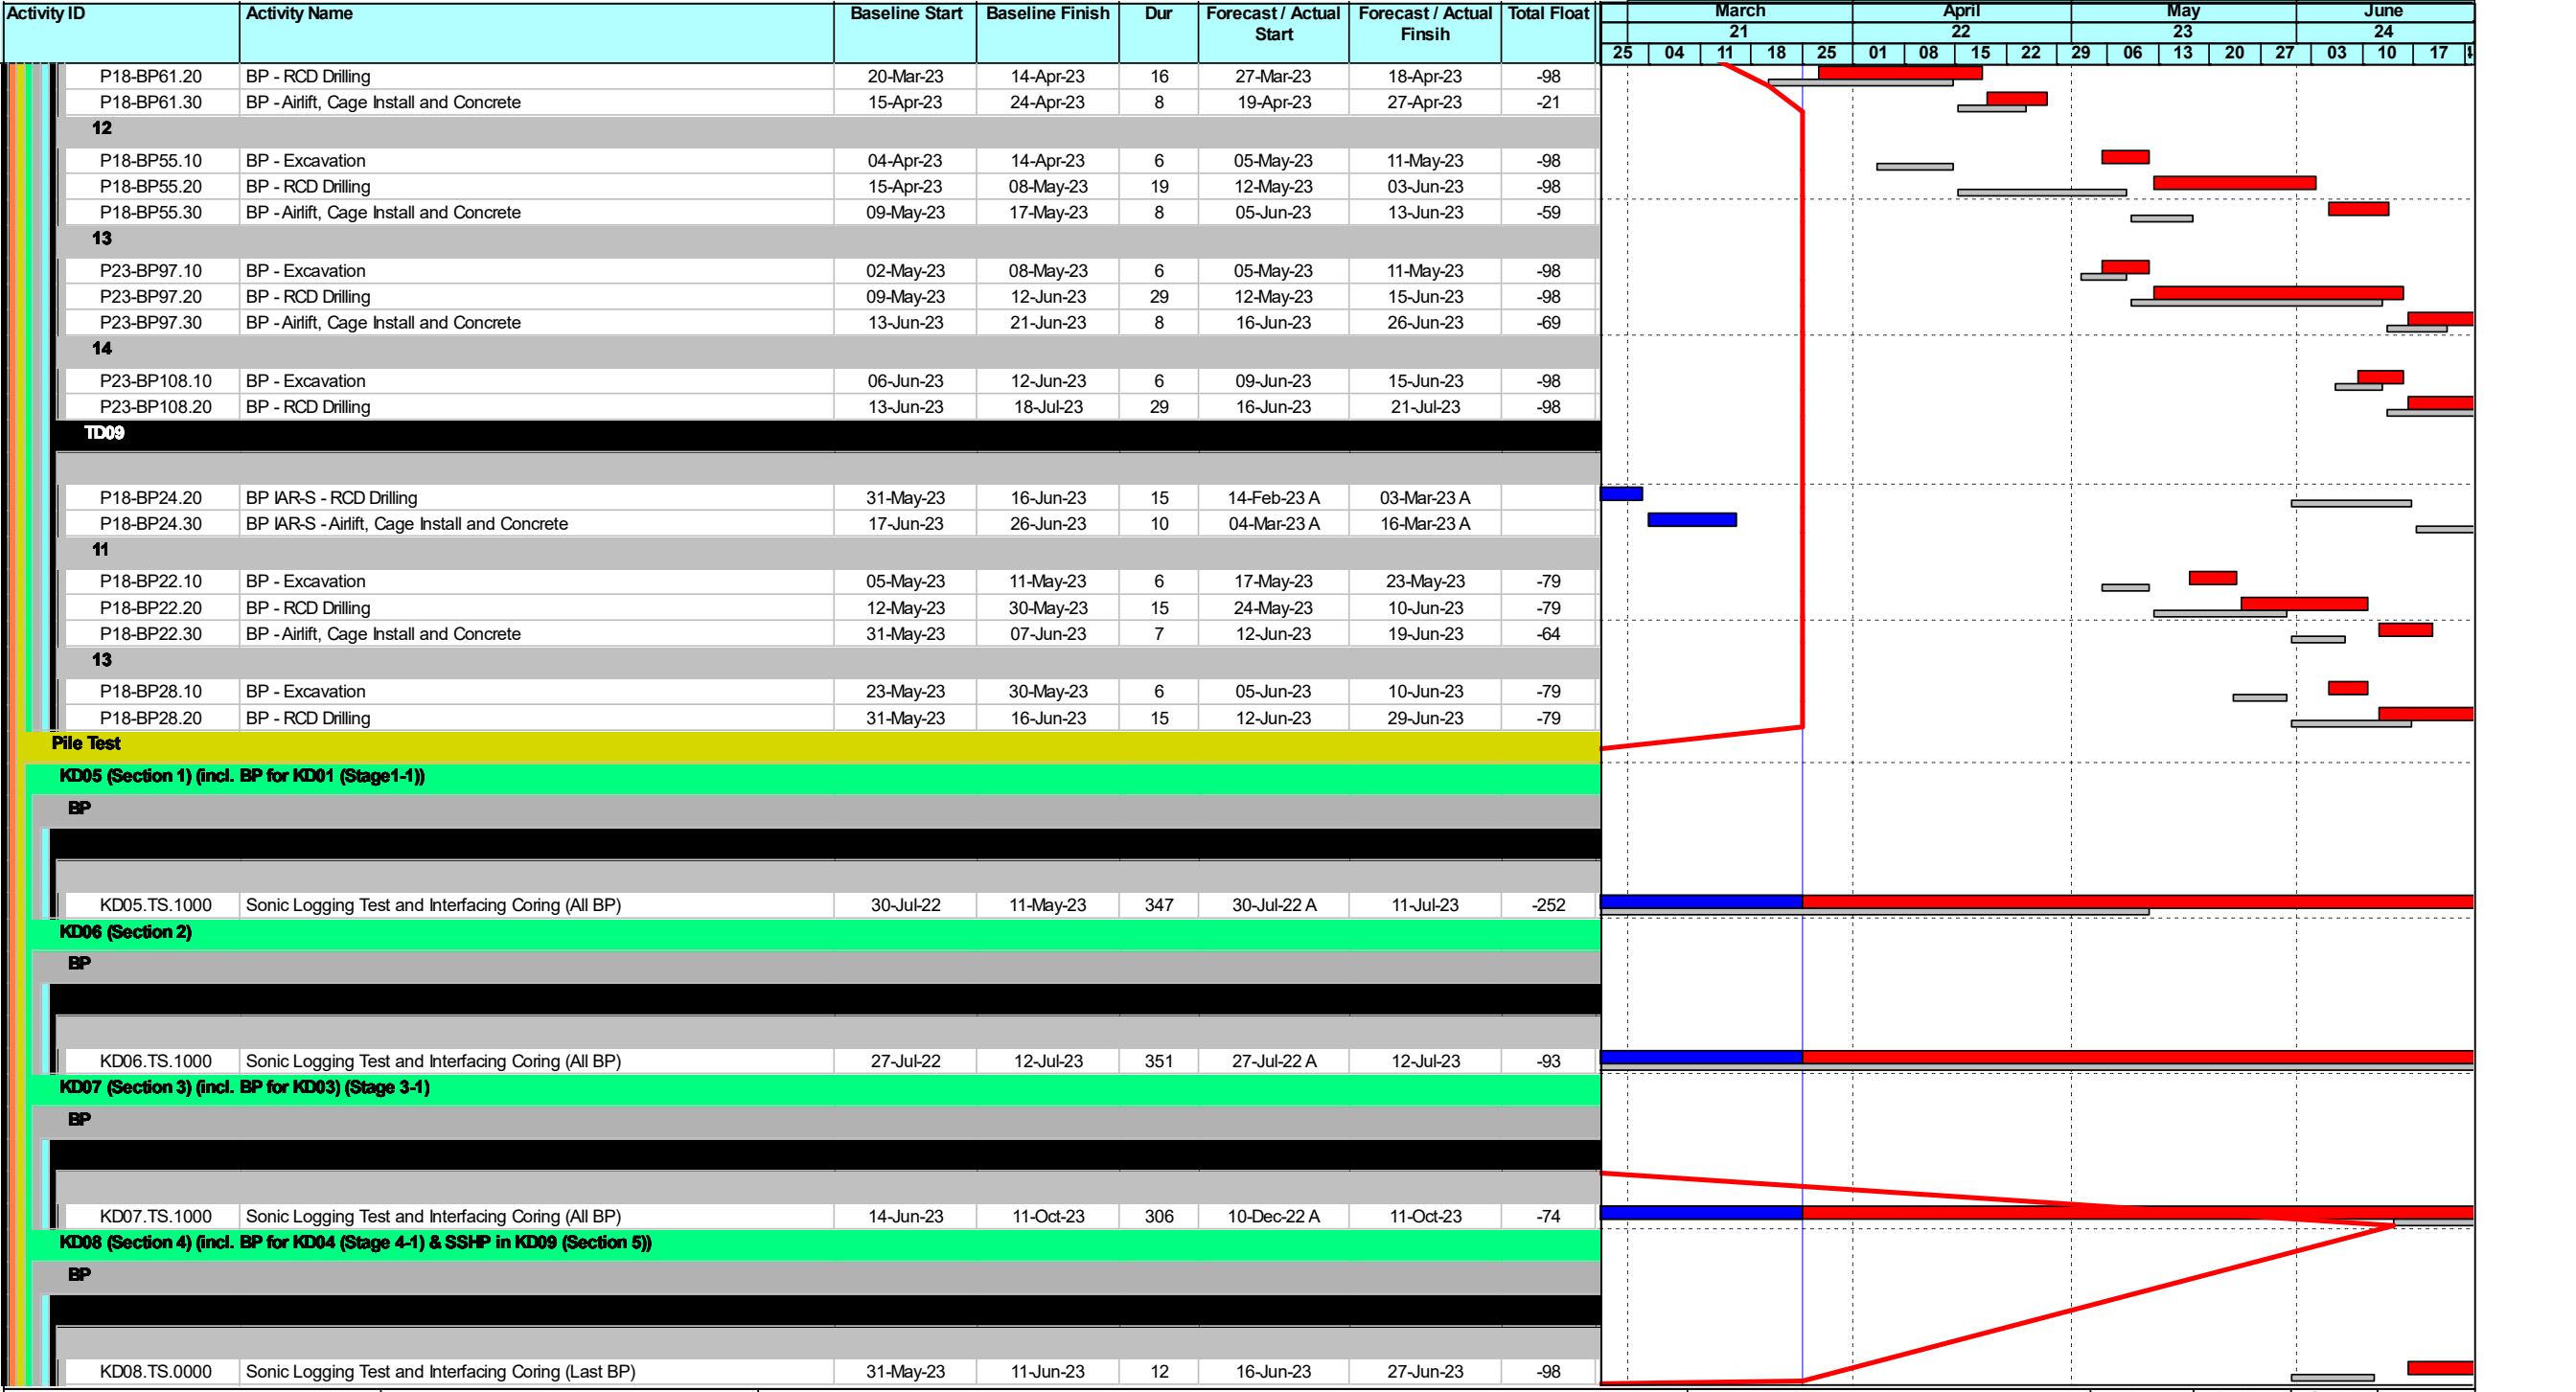

	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 24 March 2023
 Based on CMWP Rev.0 (3rd Draft)



Date	Revision	Checked	Approved
4-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	March				April				May				June							
								21				22				23				24							
								25	04	11	18	25	01	08	15	22	29	06	13	20	27	03	10	17	24		
KD08.TS.1000	Sonic Logging Test and Interfacing Coring (All BP)	04-Jul-22	11-Jun-23	359	04-Jul-22 A	27-Jun-23	-98																				
SSHP																											
KD08.TS.1120	Submit BA14	15-Nov-22	21-Nov-22	7	25-Mar-23	31-Mar-23	-4																				
KD08.TS.1140	Selection of Pile for Static Load Test	22-Nov-22	05-Dec-22	14	01-Apr-23	14-Apr-23	-4																				
KD08.TS.1160	Static Load Test of Selected Pile	06-Dec-22	19-Dec-22	14	15-Apr-23	28-Apr-23	-4																				
KD08.TS.1180	Obtain BA14 Acknowledgement / Satisfaction of CA, Completion As-built Drawings, Reports & Records	20-Dec-22	16-Jan-23	28	29-Apr-23	26-May-23	-4																				
KD09 (Section 5) (incl. BP for KD02 (Stage 5-1))																											
BP																											
KD09.TS.1000	Sonic Logging Test and Interfacing Coring (All BP)	23-May-22	12-Aug-23	447	23-May-22 A	12-Aug-23	-124																				
Attendance to Other Project Contractors (optional works item no. 2A to 2E)																											
S2.AT.0000	Attendance at Section 2 Area (optional works item no. 2B) (Duration TBC)	13-May-23	01-Jun-23	20	13-May-23	01-Jun-23	11																				
S4.AT.0000	Attendance at Section 4 Area (optional works item no. 2D) (not exercised)	22-Feb-23	13-Mar-23	19	22-Feb-23 A	13-Mar-23 A																					
S5.AT.0000	Attendance at Section 5 Area (optional works item no. 2E) (not exercised)	14-Mar-23	02-Apr-23	19	14-Mar-23 A	02-Apr-23 A																					

	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 24 March 2023
 Based on CMWP Rev.0 (3rd Draft)



Date	Revision	Checked	Approved
4-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C
