



**Zone 2B & 2C**

[illegible]

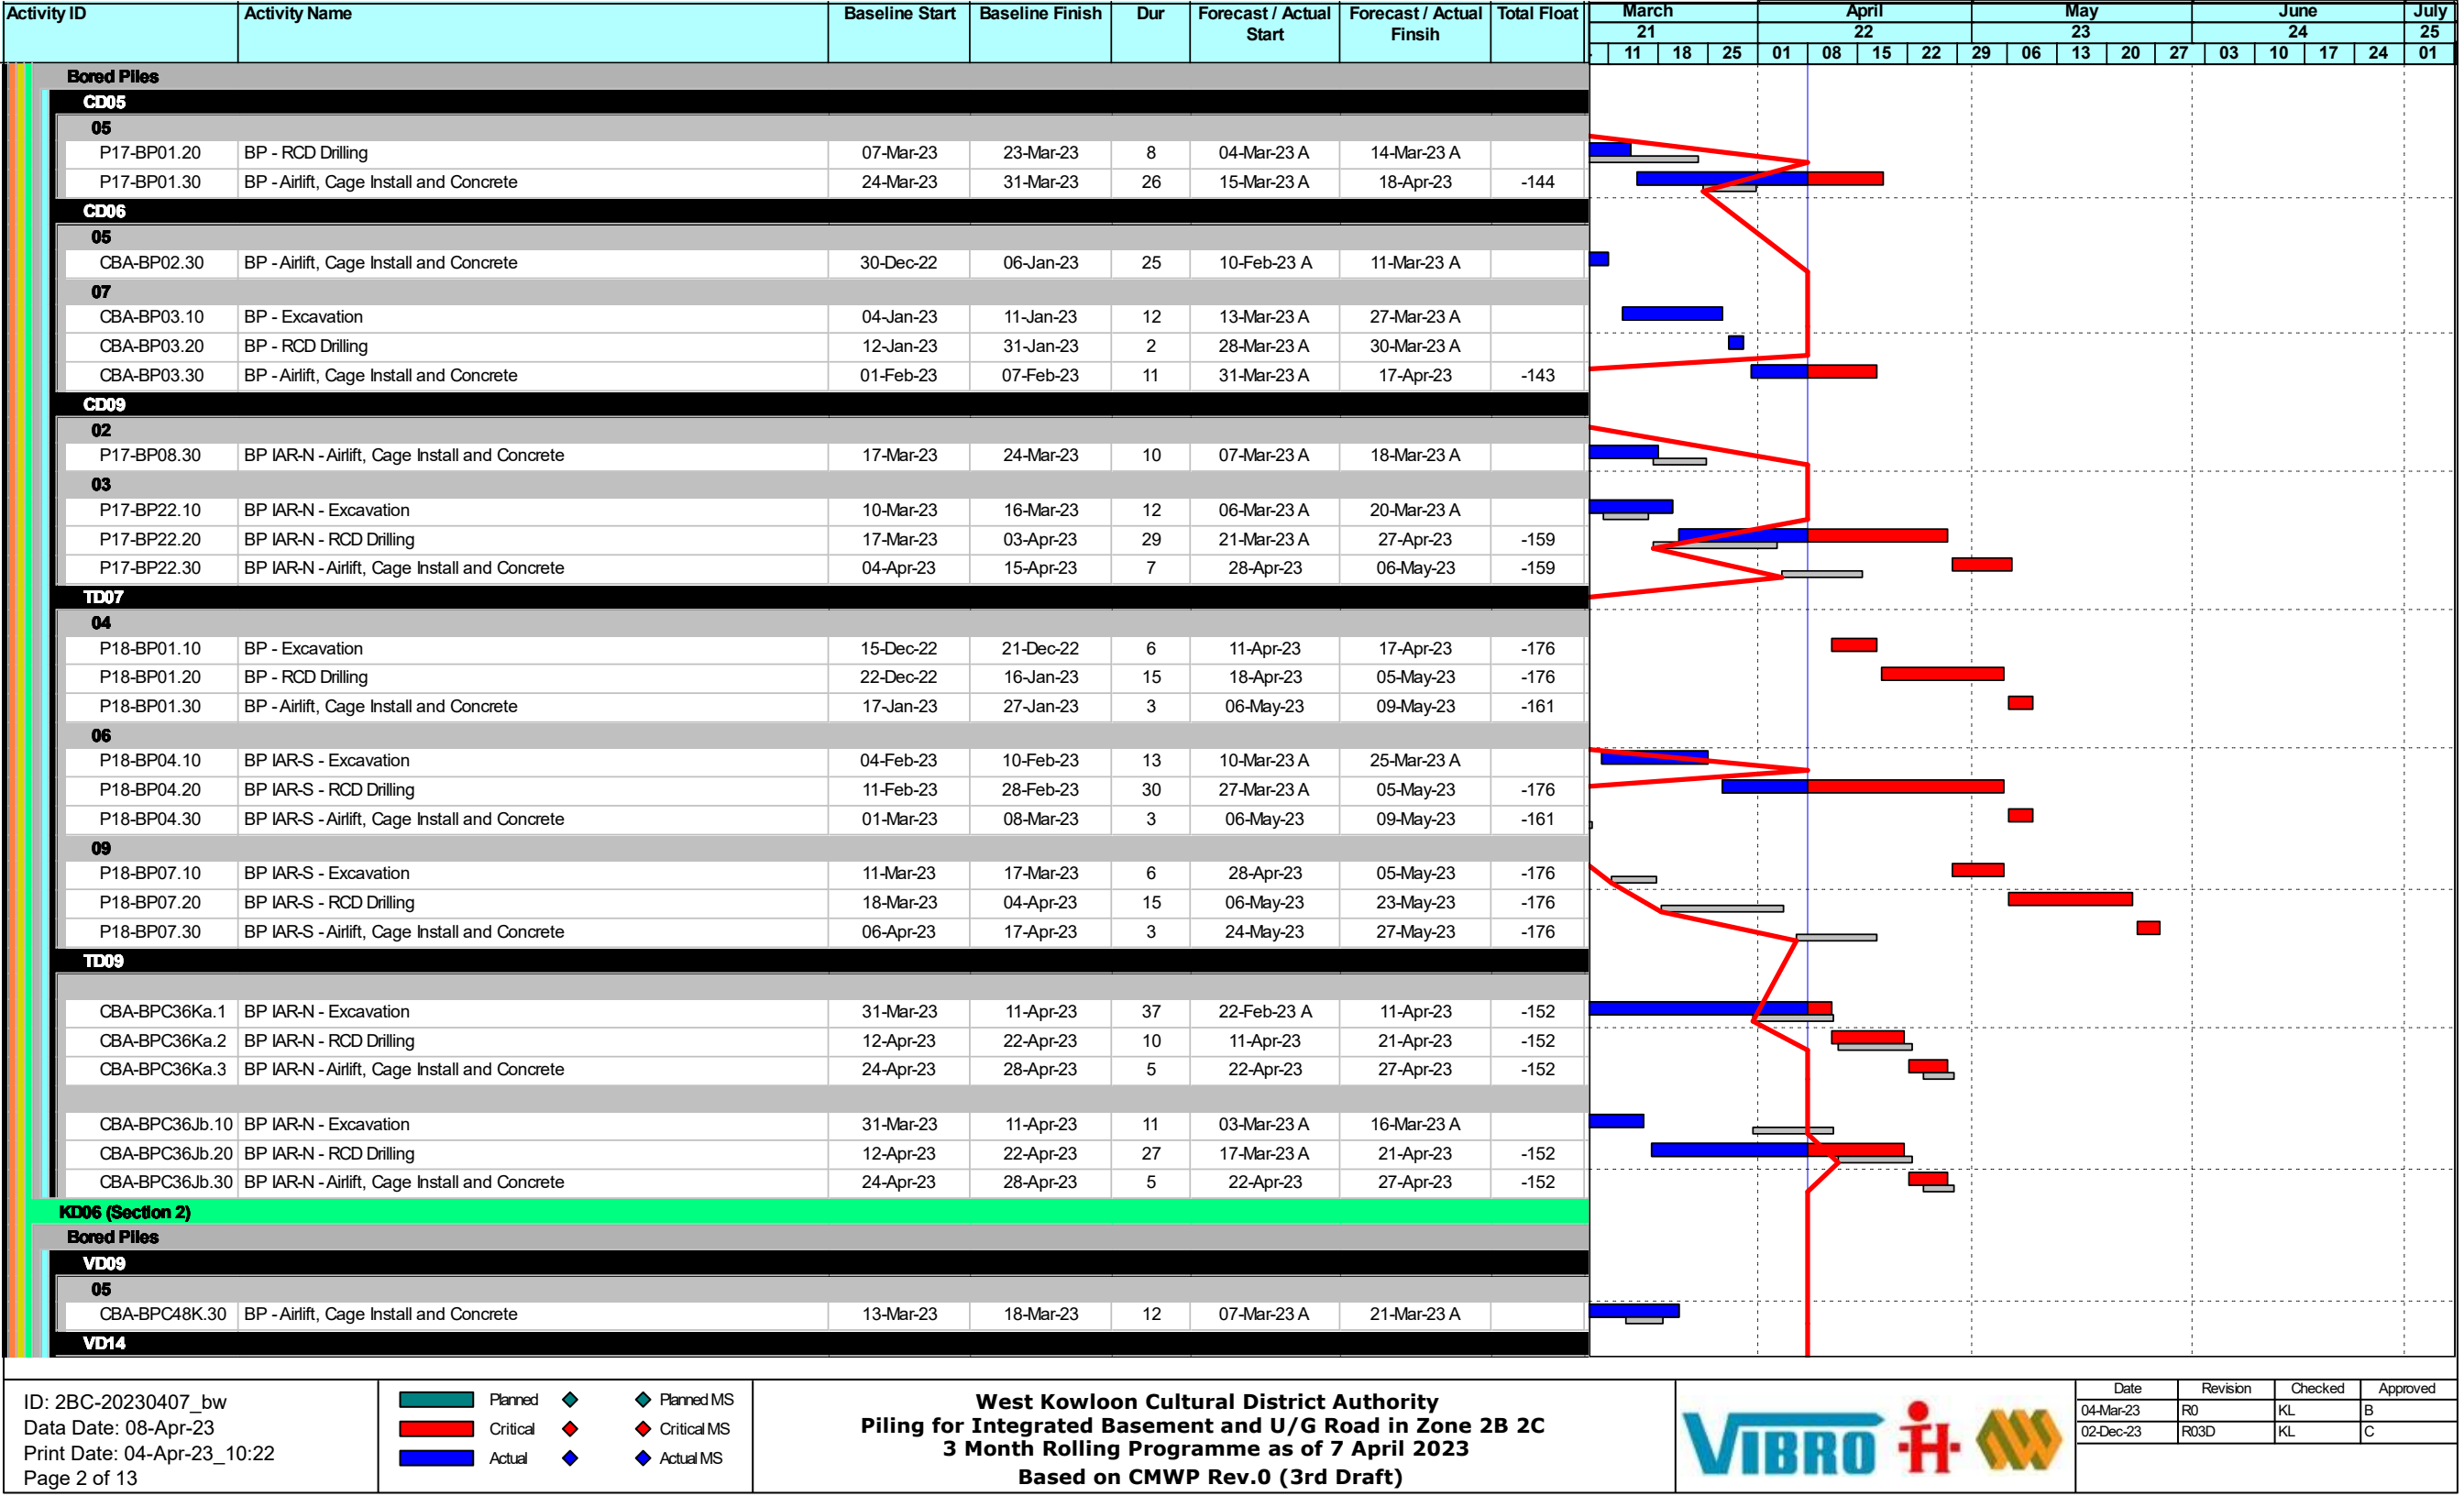

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	March 21				April 22				May 23				June 24				July 25			
								11	18	25	01	08	15	22	29	06	13	20	27	03	10	17	24	01			
	P24&P27-BP16.: BP - Airlift, Cage Install and Concrete	18-Apr-23	26-Apr-23	6	03-Mar-23 A	10-Mar-23 A																					
05																											
	P24&P27-BP15.: BP - Excavation	30-Jan-23	04-Feb-23	23	21-Mar-23 A	20-Apr-23	-73																				
	P24&P27-BP15.: BP - RCD Drilling	06-Feb-23	27-Feb-23	19	21-Apr-23	13-May-23	-73																				
	P24&P27-BP15.: BP - Airlift, Cage Install and Concrete	28-Feb-23	08-Mar-23	8	15-May-23	23-May-23	-42																				
06																											
	P24&P27-BP22.: BP - Excavation	21-Feb-23	27-Feb-23	15	27-Feb-23 A	16-Mar-23 A																					
	P24&P27-BP22.: BP - RCD Drilling	28-Feb-23	21-Mar-23	9	17-Mar-23 A	28-Mar-23 A																					
	P24&P27-BP22.: BP - Airlift, Cage Install and Concrete	22-Mar-23	30-Mar-23	15	29-Mar-23 A	19-Apr-23	-14																				
08																											
	P24&P27-BP21.: BP - Excavation	11-Apr-23	17-Apr-23	6	08-May-23	13-May-23	-73																				
	P24&P27-BP21.: BP - RCD Drilling	18-Apr-23	10-May-23	19	15-May-23	06-Jun-23	-73																				
	P24&P27-BP21.: BP - Airlift, Cage Install and Concrete	11-May-23	19-May-23	8	07-Jun-23	15-Jun-23	-61																				
09																											
	P24&P27-BP36.: BP - Excavation	04-May-23	10-May-23	6	22-May-23	29-May-23	-73																				
	P24&P27-BP36.: BP - RCD Drilling	11-May-23	02-Jun-23	19	30-May-23	20-Jun-23	-73																				
	P24&P27-BP36.: BP - Airlift, Cage Install and Concrete	03-Jun-23	12-Jun-23	8	21-Jun-23	30-Jun-23	-73																				
VD15																											
	P24&P27-BP04.: BP - Airlift, Cage Install and Concrete	10-Jun-23	19-Jun-23	19	14-Feb-23 A	08-Mar-23 A																					
05																											
	P24&P27-BP29.: BP - Excavation	20-Jan-23	30-Jan-23	17	11-Mar-23 A	31-Mar-23 A																					
	P24&P27-BP29.: BP - RCD Drilling	31-Jan-23	21-Feb-23	9	01-Apr-23 A	15-Apr-23	-68																				
	P24&P27-BP29.: BP - Airlift, Cage Install and Concrete	22-Feb-23	02-Mar-23	8	17-Apr-23	25-Apr-23	-19																				
06																											
	P24&P27-BP03.: BP - Excavation	15-Feb-23	21-Feb-23	22	17-Mar-23 A	15-Apr-23	-68																				
	P24&P27-BP03.: BP - RCD Drilling	22-Feb-23	27-Mar-23	20	17-Apr-23	10-May-23	-68																				
	P24&P27-BP03.: BP - Airlift, Cage Install and Concrete	28-Mar-23	06-Apr-23	8	11-May-23	19-May-23	-39																				
07																											
	P24&P27-BP10.: BP - Excavation	21-Mar-23	27-Mar-23	6	04-May-23	10-May-23	-68																				
	P24&P27-BP10.: BP - RCD Drilling	28-Mar-23	05-May-23	29	11-May-23	14-Jun-23	-68																				
	P24&P27-BP10.: BP - Airlift, Cage Install and Concrete	06-May-23	15-May-23	8	15-Jun-23	24-Jun-23	-68																				
CD01																											
	P23-BP25.30 BP - Airlift, Cage Install and Concrete	17-May-23	25-May-23	10	04-Mar-23 A	16-Mar-23 A																					
	P23-BP09.20 BP - RCD Drilling	31-Jan-23	21-Feb-23	10	08-Mar-23 A	20-Mar-23 A																					
	P23-BP09.30 BP - Airlift, Cage Install and Concrete	22-Feb-23	02-Mar-23	7	21-Mar-23 A	29-Mar-23 A																					
02																											
	P23-BP14.10 BP - Excavation	03-Dec-22	09-Dec-22	22	18-Mar-23 A	17-Apr-23	-68																				
	P23-BP14.20 BP - RCD Drilling	10-Dec-22	04-Jan-23	19	18-Apr-23	10-May-23	-68																				
	P23-BP14.30 BP - Airlift, Cage Install and Concrete	05-Jan-23	13-Jan-23	8	11-May-23	19-May-23	-39																				
05																											
	P23-BP26.10 BP - Excavation	15-Feb-23	21-Feb-23	36	24-Mar-23 A	10-May-23	-68																				
	P23-BP26.20 BP - RCD Drilling	22-Feb-23	27-Mar-23	29	11-May-23	14-Jun-23	-68																				
	P23-BP26.30 BP - Airlift, Cage Install and Concrete	28-Mar-23	06-Apr-23	8	15-Jun-23	24-Jun-23	-68																				
ID: 2BC-20230407_bw		<div><div></div>Planned</div> <div><div></div>Critical</div> <div><div></div>Actual</div>				<div><div></div>Planned MS</div> <div><div></div>Critical MS</div> <div><div></div>Actual MS</div>				West Kowloon Cultural District Authority Piling for Integrated Basement and U/G Road in Zone 2B 2C 3 Month Rolling Programme as of 7 April 2023 Based on CMWP Rev.0 (3rd Draft)										<div>Date</div> <div>Revision</div> <div>Checked</div> <div>Approved</div>				<div>04-Mar-23</div> <div>02-Dec-23</div> <div></div>	<div>R0</div> <div>R03D</div> <div></div>	<div>KL</div> <div>KL</div> <div></div>	<div>B</div> <div>C</div> <div></div>
Data Date: 08-Apr-23										<div>VIBRO</div> <div></div> <div></div>																	
Print Date: 04-Apr-23_10:22																											
Page 3 of 13																											

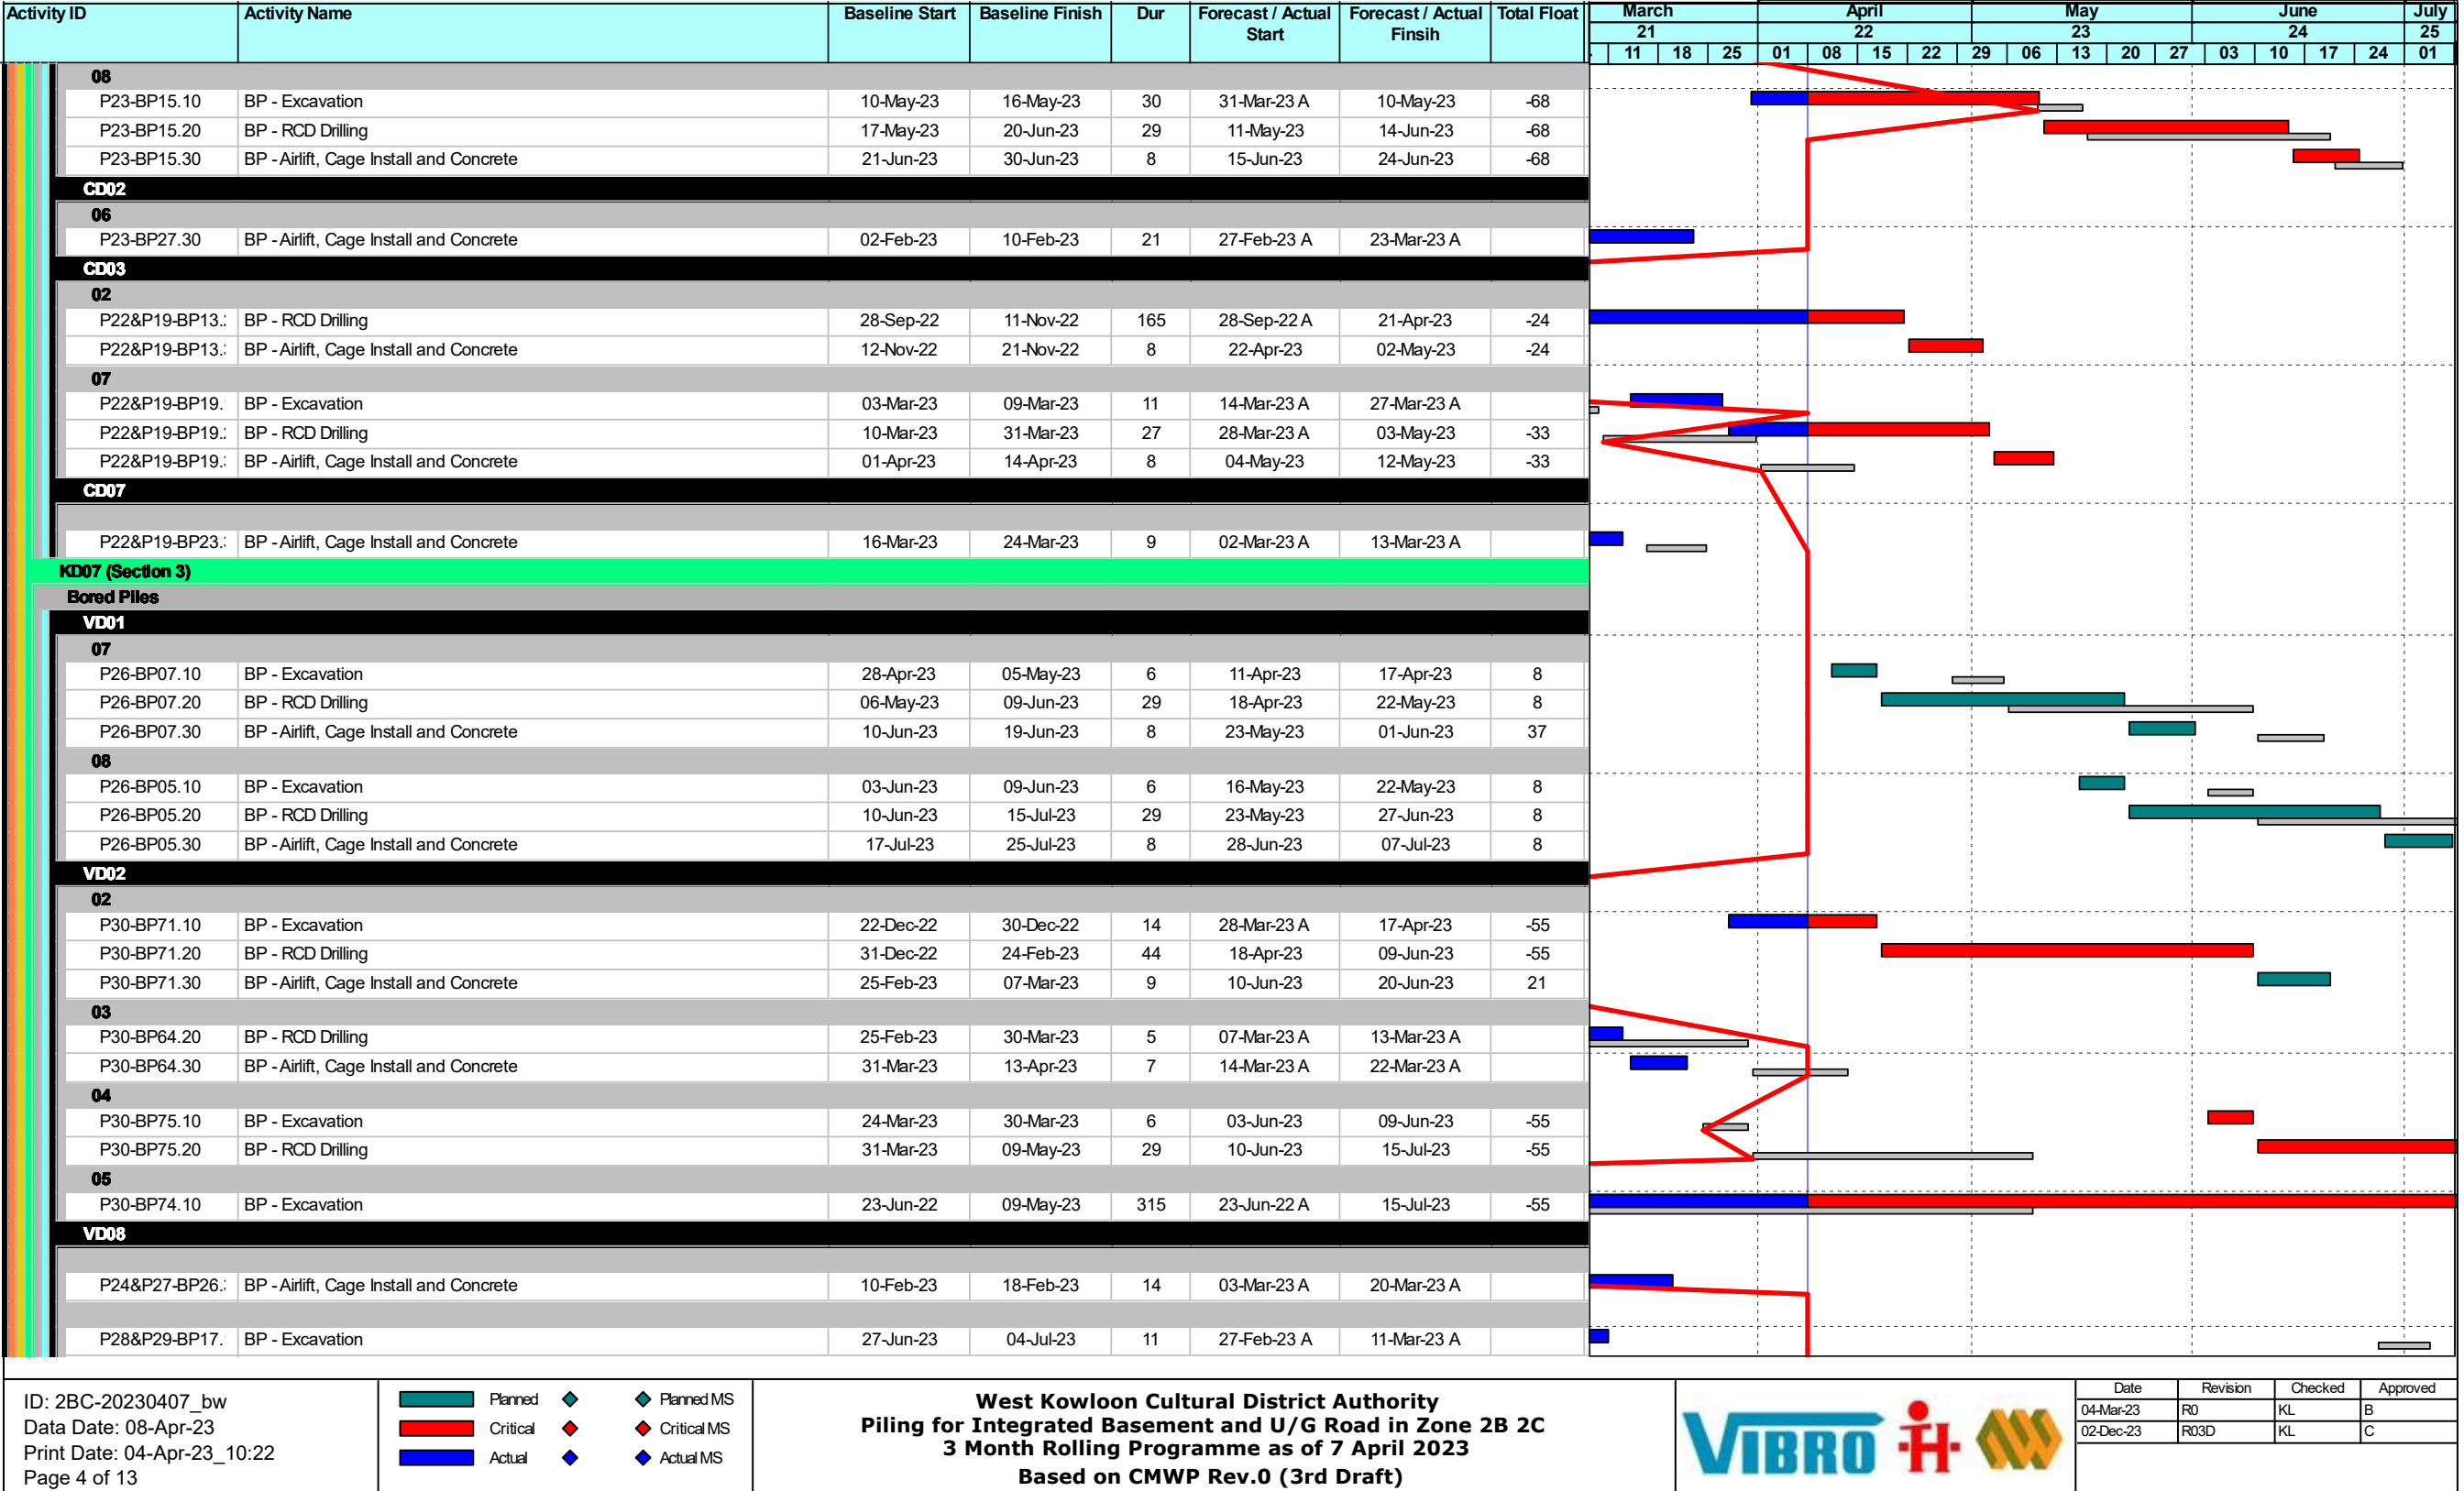

[illegible]

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	March				April				May				June				July				
								21				22				23				24				25				
								11	18	25	01	08	15	22	29	06	13	20	27	03	10	17	24	01				
	P28&P29-BP05.1	BP - RCD Drilling	17-Jul-23	07-Aug-23	21	27-Feb-23 A	23-Mar-23 A																					
	P28&P29-BP05.2	BP - Airlift, Cage Install and Concrete	08-Aug-23	16-Aug-23	19	24-Mar-23 A	19-Apr-23	72																				
VD16																												
	P26-BP02.20	BP - RCD Drilling	04-Apr-23	12-May-23	5	02-Mar-23 A	08-Mar-23 A																					
	P26-BP02.30	BP - Airlift, Cage Install and Concrete	13-May-23	22-May-23	6	09-Mar-23 A	16-Mar-23 A																					
	P26-BP06.10	BP - Excavation	23-May-23	30-May-23	50	14-Feb-23 A	17-Apr-23	18																				
	P26-BP06.20	BP - RCD Drilling	31-May-23	05-Jul-23	29	18-Apr-23	22-May-23	18																				
	P26-BP06.30	BP - Airlift, Cage Install and Concrete	06-Jul-23	14-Jul-23	8	23-May-23	01-Jun-23	37																				
03																												
	P26-BP11.10	BP - Excavation	22-Dec-22	30-Dec-22	6	16-May-23	22-May-23	18																				
	P26-BP11.20	BP - RCD Drilling	31-Dec-22	25-Jan-23	19	23-May-23	14-Jun-23	18																				
	P26-BP11.30	BP - Airlift, Cage Install and Concrete	26-Jan-23	04-Feb-23	8	15-Jun-23	24-Jun-23	18																				
KD08 (Section 4)																												
Bored Piles																												
VD01																												
06																												
	P26-BP14.10	BP - Excavation	01-Apr-23	12-Apr-23	23	17-Feb-23 A	16-Mar-23 A																					
	P26-BP14.20	BP - RCD Drilling	13-Apr-23	05-May-23	36	17-Mar-23 A	03-May-23	-50																				
	P26-BP14.30	BP - Airlift, Cage Install and Concrete	06-May-23	15-May-23	8	04-May-23	12-May-23	-50																				
VD03																												
	P30-BP40.10	BP - Excavation	21-Feb-23	27-Feb-23	37	01-Mar-23 A	17-Apr-23	-45																				
	P30-BP40.20	BP - RCD Drilling	28-Feb-23	16-Mar-23	15	11-Apr-23	27-Apr-23	-45																				
	P30-BP40.30	BP - Airlift, Cage Install and Concrete	17-Mar-23	24-Mar-23	7	28-Apr-23	06-May-23	-45																				
	P30-BP42.10	BP - Excavation	10-Mar-23	16-Mar-23	23	24-Feb-23 A	23-Mar-23 A																					
	P30-BP42.20	BP - RCD Drilling	17-Mar-23	03-Apr-23	6	24-Mar-23 A	31-Mar-23 A																					
	P30-BP42.30	BP - Airlift, Cage Install and Concrete	04-Apr-23	15-Apr-23	11	01-Apr-23 A	18-Apr-23	-30																				
02																												
	P30-BP34.10	BP - Excavation	01-Dec-22	07-Dec-22	9	10-Mar-23 A	21-Mar-23 A																					
	P30-BP34.20	BP - RCD Drilling	08-Dec-22	24-Dec-22	3	22-Mar-23 A	25-Mar-23 A																					
	P30-BP34.30	BP - Airlift, Cage Install and Concrete	28-Dec-22	05-Jan-23	16	27-Mar-23 A	18-Apr-23	-30																				
03																												
	P30-BP52.10	BP - Excavation	19-Dec-22	24-Dec-22	13	23-Mar-23 A	11-Apr-23	-73																				
	P30-BP52.20	BP - RCD Drilling	28-Dec-22	19-Jan-23	19	12-Apr-23	04-May-23	-73																				
	P30-BP52.30	BP - Airlift, Cage Install and Concrete	20-Jan-23	01-Feb-23	8	05-May-23	13-May-23	-51																				
04																												
	P30-BP46.10	BP - Excavation	13-Jan-23	19-Jan-23	6	11-Apr-23	17-Apr-23	-78																				
	P30-BP46.20	BP - RCD Drilling	20-Jan-23	09-Feb-23	15	18-Apr-23	05-May-23	-78																				
	P30-BP46.30	BP - Airlift, Cage Install and Concrete	10-Feb-23	17-Feb-23	7	06-May-23	13-May-23	-51																				
05																												
	P30-BP47.10	BP - Excavation	03-Feb-23	09-Feb-23	6	28-Apr-23	05-May-23	-78																				
	P30-BP47.20	BP - RCD Drilling	10-Feb-23	27-Feb-23	15	06-May-23	23-May-23	-78																				
	P30-BP47.30	BP - Airlift, Cage Install and Concrete	28-Feb-23	07-Mar-23	7	24-May-23	01-Jun-23	-66																				
08																												

ID: 2BC-20230407\_bw

Data Date: 08-Apr-23

Print Date: 04-Apr-23\_10:22

Page 6 of 13

Planned

Critical

Actual

Planned MS

Critical MS

Actual MS

West Kowloon Cultural District Authority

Piling for Integrated Basement and U/G Road in Zone 2B 2C


3 Month Rolling Programme as of 7 April 2023

Based on CMWP Rev.0 (3rd Draft)

VIBRO


Date	Revision	Checked	Approved
04-Mar-23	R0	KL	B
02-Dec-23	R03D	KL	C




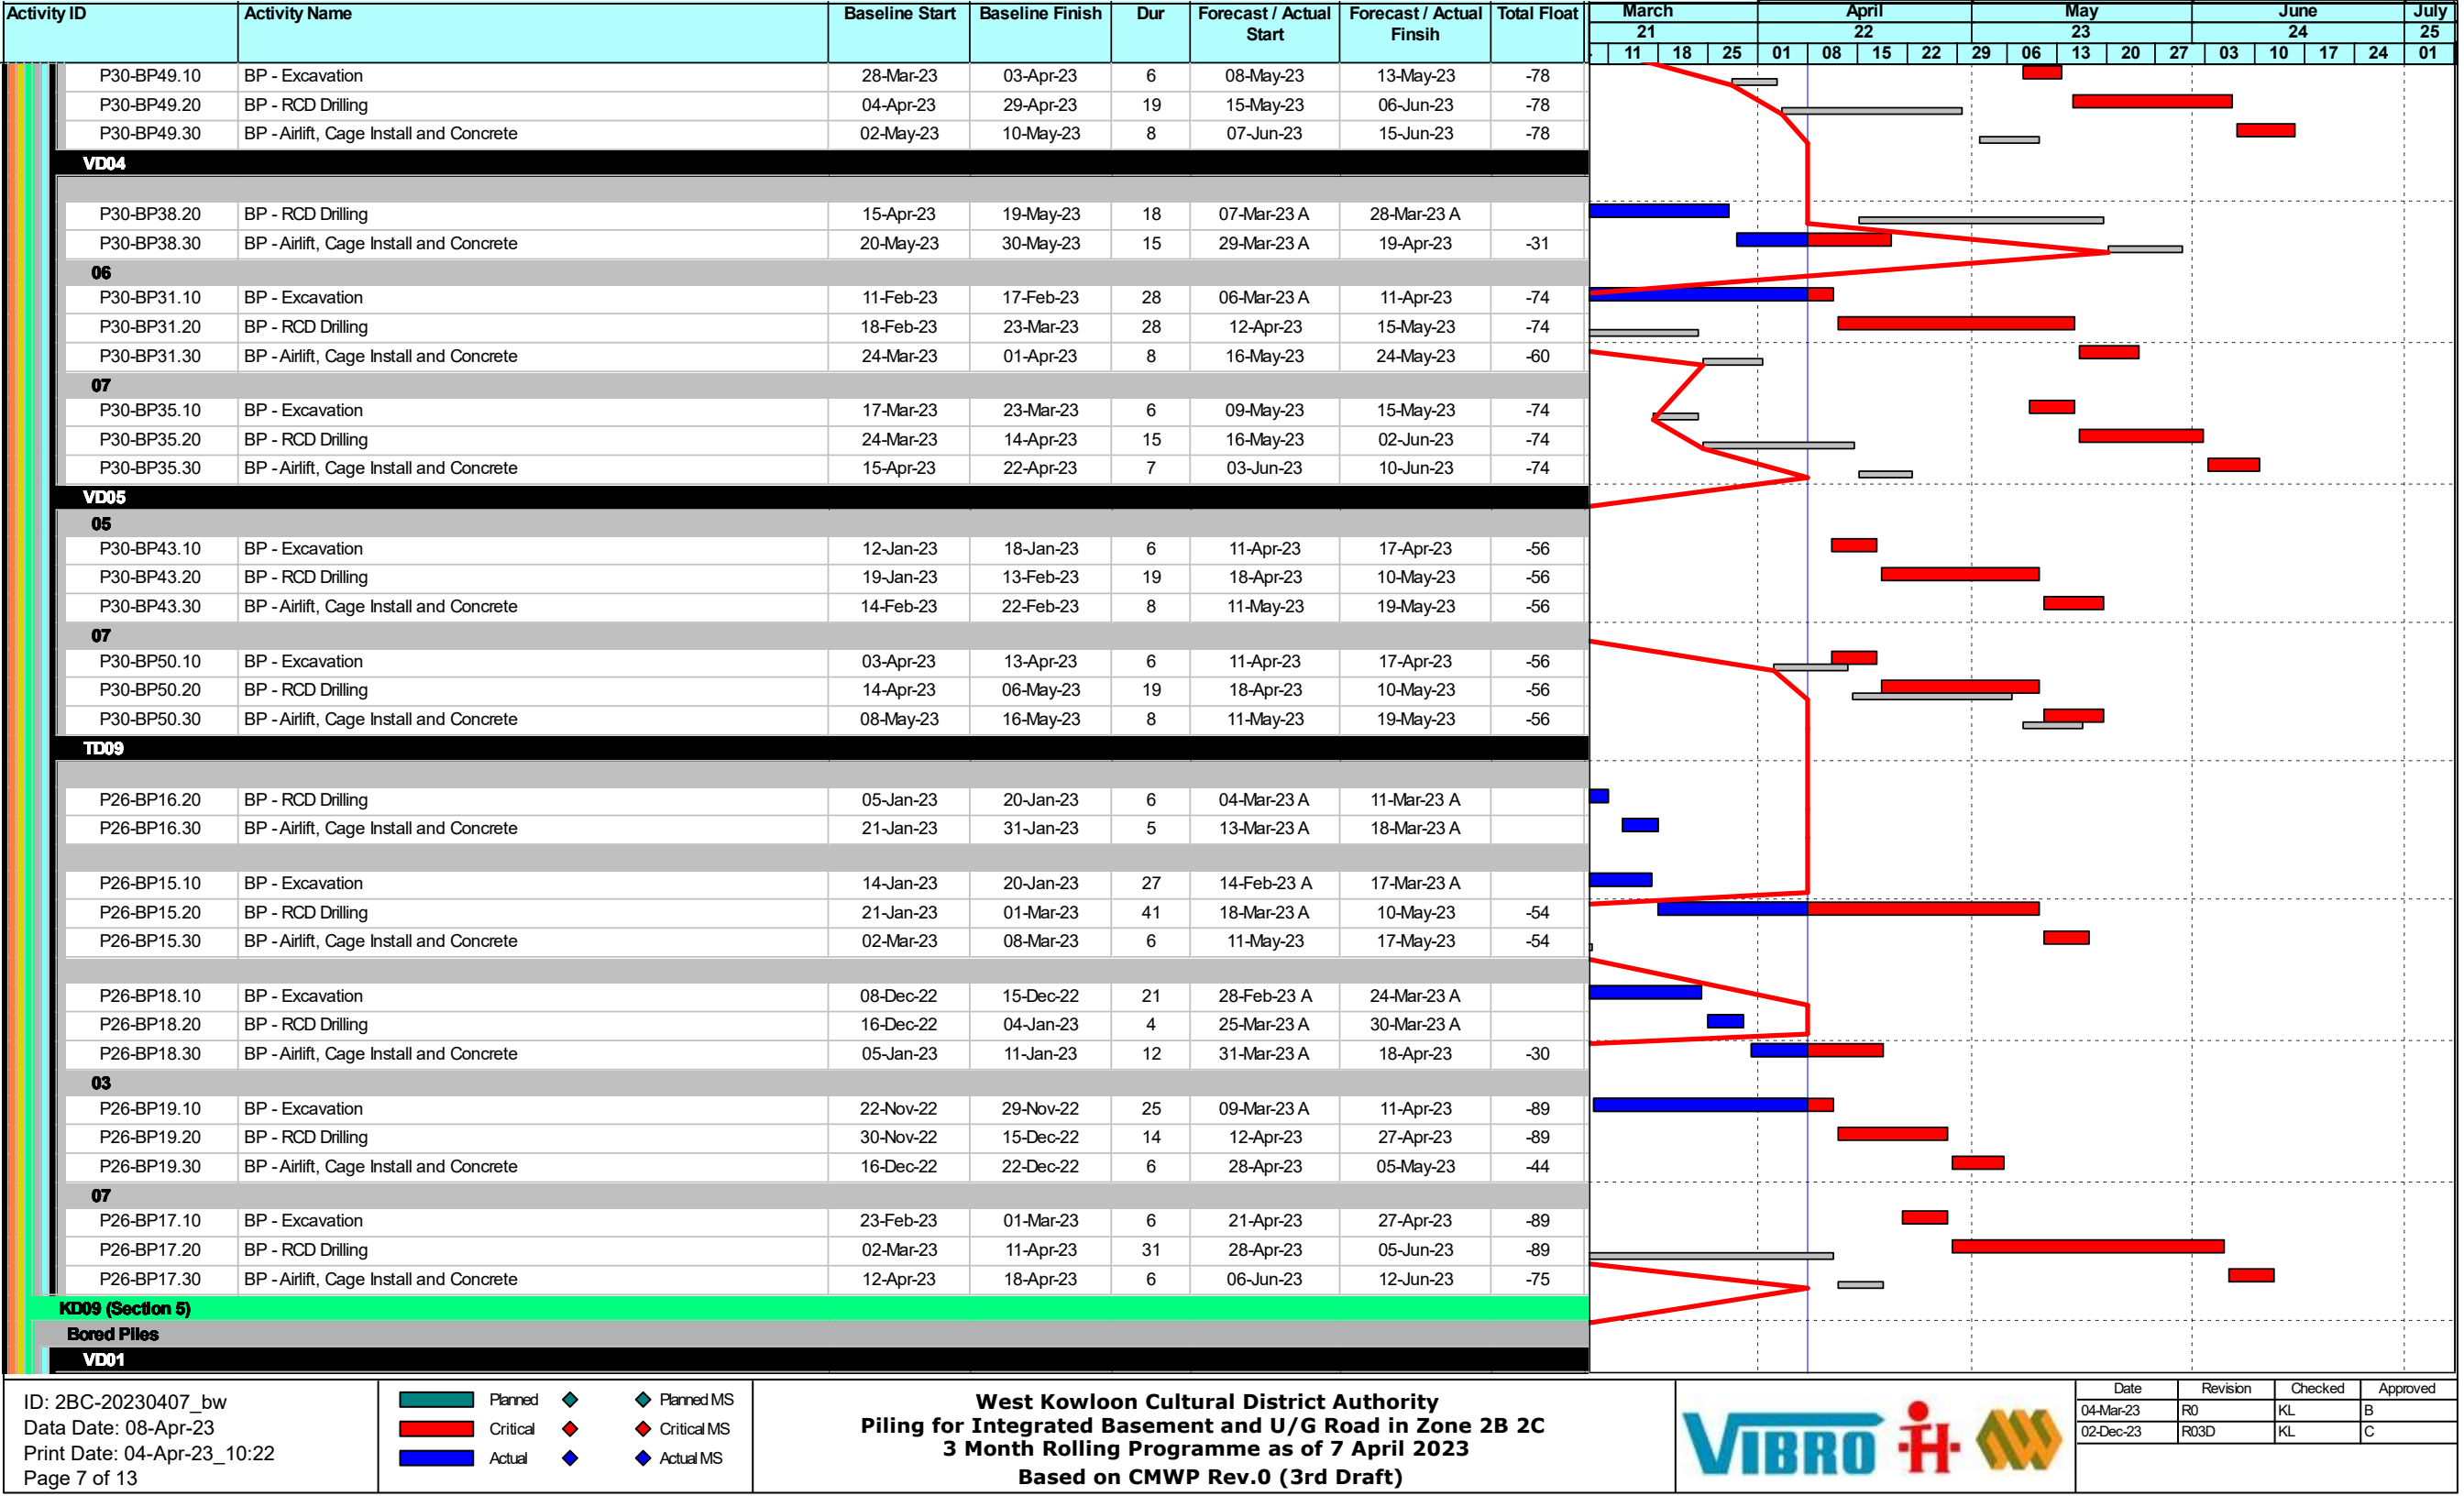



Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	March			April				May				June				July																
								21			22				23				24				25																
								11	18	25	01	08	15	22	29	06	13	20	27	03	10	17	24	01															
	P23-BP34.20	BP - RCD Drilling	12-Dec-22	05-Jan-23	48	03-Mar-23 A	03-May-23	-33																															
	P23-BP34.30	BP - Airlift, Cage Install and Concrete	06-Jan-23	14-Jan-23	8	04-May-23	12-May-23	-33																															
CD01																																							
03																																							
	P23-BP35.10	BP - Excavation	28-Dec-22	04-Jan-23	6	04-May-23	10-May-23	-58																															
	P23-BP35.20	BP - RCD Drilling	05-Jan-23	30-Jan-23	19	11-May-23	02-Jun-23	-58																															
	P23-BP35.30	BP - Airlift, Cage Install and Concrete	31-Jan-23	08-Feb-23	8	03-Jun-23	12-Jun-23	-58																															
CD02																																							
07																																							
	P23-BP48.10	BP - Excavation	25-Jan-23	01-Feb-23	28	13-Feb-23 A	17-Mar-23 A																																
	P23-BP48.20	BP - RCD Drilling	02-Feb-23	07-Mar-23	9	18-Mar-23 A	29-Mar-23 A																																
	P23-BP48.30	BP - Airlift, Cage Install and Concrete	08-Mar-23	16-Mar-23	14	30-Mar-23 A	19-Apr-23	-14																															
09																																							
	P23-BP36.10	BP - Excavation	04-Apr-23	14-Apr-23	6	11-Apr-23	17-Apr-23	-49																															
	P23-BP36.20	BP - RCD Drilling	15-Apr-23	19-May-23	29	18-Apr-23	22-May-23	-49																															
	P23-BP36.30	BP - Airlift, Cage Install and Concrete	20-May-23	30-May-23	8	23-May-23	01-Jun-23	-49																															
TD01																																							
	P18-BP58.10	BP - Excavation	06-Mar-23	11-Mar-23	15	21-Feb-23 A	10-Mar-23 A																																
	P18-BP58.20	BP - RCD Drilling	13-Mar-23	03-Apr-23	16	11-Mar-23 A	30-Mar-23 A																																
	P18-BP58.30	BP - Airlift, Cage Install and Concrete	04-Apr-23	17-Apr-23	13	31-Mar-23 A	19-Apr-23	-14																															
02																																							
	P18-BP57.10	BP - Excavation	22-Dec-22	30-Dec-22	6	11-Apr-23	17-Apr-23	-98																															
	P18-BP57.20	BP - RCD Drilling	31-Dec-22	25-Jan-23	19	18-Apr-23	10-May-23	-98																															
	P18-BP57.30	BP - Airlift, Cage Install and Concrete	26-Jan-23	04-Feb-23	8	11-May-23	19-May-23	-39																															
04																																							
	P18-BP62.10	BP - Excavation	11-Feb-23	17-Feb-23	6	04-May-23	10-May-23	-98																															
	P18-BP62.20	BP - RCD Drilling	18-Feb-23	11-Mar-23	19	11-May-23	02-Jun-23	-98																															
	P18-BP62.30	BP - Airlift, Cage Install and Concrete	13-Mar-23	21-Mar-23	8	03-Jun-23	12-Jun-23	-58																															
06																																							
	P18-BP45.10	BP - Excavation	28-Mar-23	03-Apr-23	6	27-May-23	02-Jun-23	-98																															
	P18-BP45.20	BP - RCD Drilling	04-Apr-23	29-Apr-23	19	03-Jun-23	26-Jun-23	-98																															
	P18-BP45.30	BP - Airlift, Cage Install and Concrete	02-May-23	10-May-23	8	27-Jun-23	06-Jul-23	-77																															
07																																							
	P18-BP52.10	BP - Excavation	24-Apr-23	29-Apr-23	6	27-May-23	02-Jun-23	-98																															
	P18-BP52.20	BP - RCD Drilling	02-May-23	23-May-23	19	03-Jun-23	26-Jun-23	-98																															
	P18-BP52.30	BP - Airlift, Cage Install and Concrete	24-May-23	02-Jun-23	8	27-Jun-23	06-Jul-23	-77																															
08																																							
	P18-BP40.10	BP - Excavation	17-May-23	23-May-23	6	27-May-23	02-Jun-23	-98																															
	P18-BP40.20	BP - RCD Drilling	24-May-23	10-Jun-23	15	03-Jun-23	20-Jun-23	-98																															
	P18-BP40.30	BP - Airlift, Cage Install and Concrete	12-Jun-23	19-Jun-23	7	21-Jun-23	29-Jun-23	-72																															
09																																							
	P18-BP51.10	BP - Excavation	05-Jun-23	10-Jun-23	6	14-Jun-23	20-Jun-23	-98																															
	P18-BP51.20	BP - RCD Drilling	12-Jun-23	05-Jul-23	19	21-Jun-23	14-Jul-23	-98																															
10																																							
	P18-BP46.10	BP - Excavation	28-Jun-23	05-Jul-23	6	28-Jun-23	05-Jul-23	-98																															
ID: 2BC-20230407_bw Data Date: 08-Apr-23 Print Date: 04-Apr-23_10:22 Page 8 of 13									<div><div></div>Planned<div></div>Critical<div></div>Actual<div></div>Planned MS<div></div>Critical MS<div></div>Actual MS</div>									West Kowloon Cultural District Authority Piling for Integrated Basement and U/G Road in Zone 2B 2C 3 Month Rolling Programme as of 7 April 2023 Based on CMWP Rev.0 (3rd Draft)									<div><div>VIBRO</div><div></div><div></div></div>									Date	Revision	Checked	Approved
																																				04-Mar-23	R0	KL	B
																																				02-Dec-23	R03D	KL	C

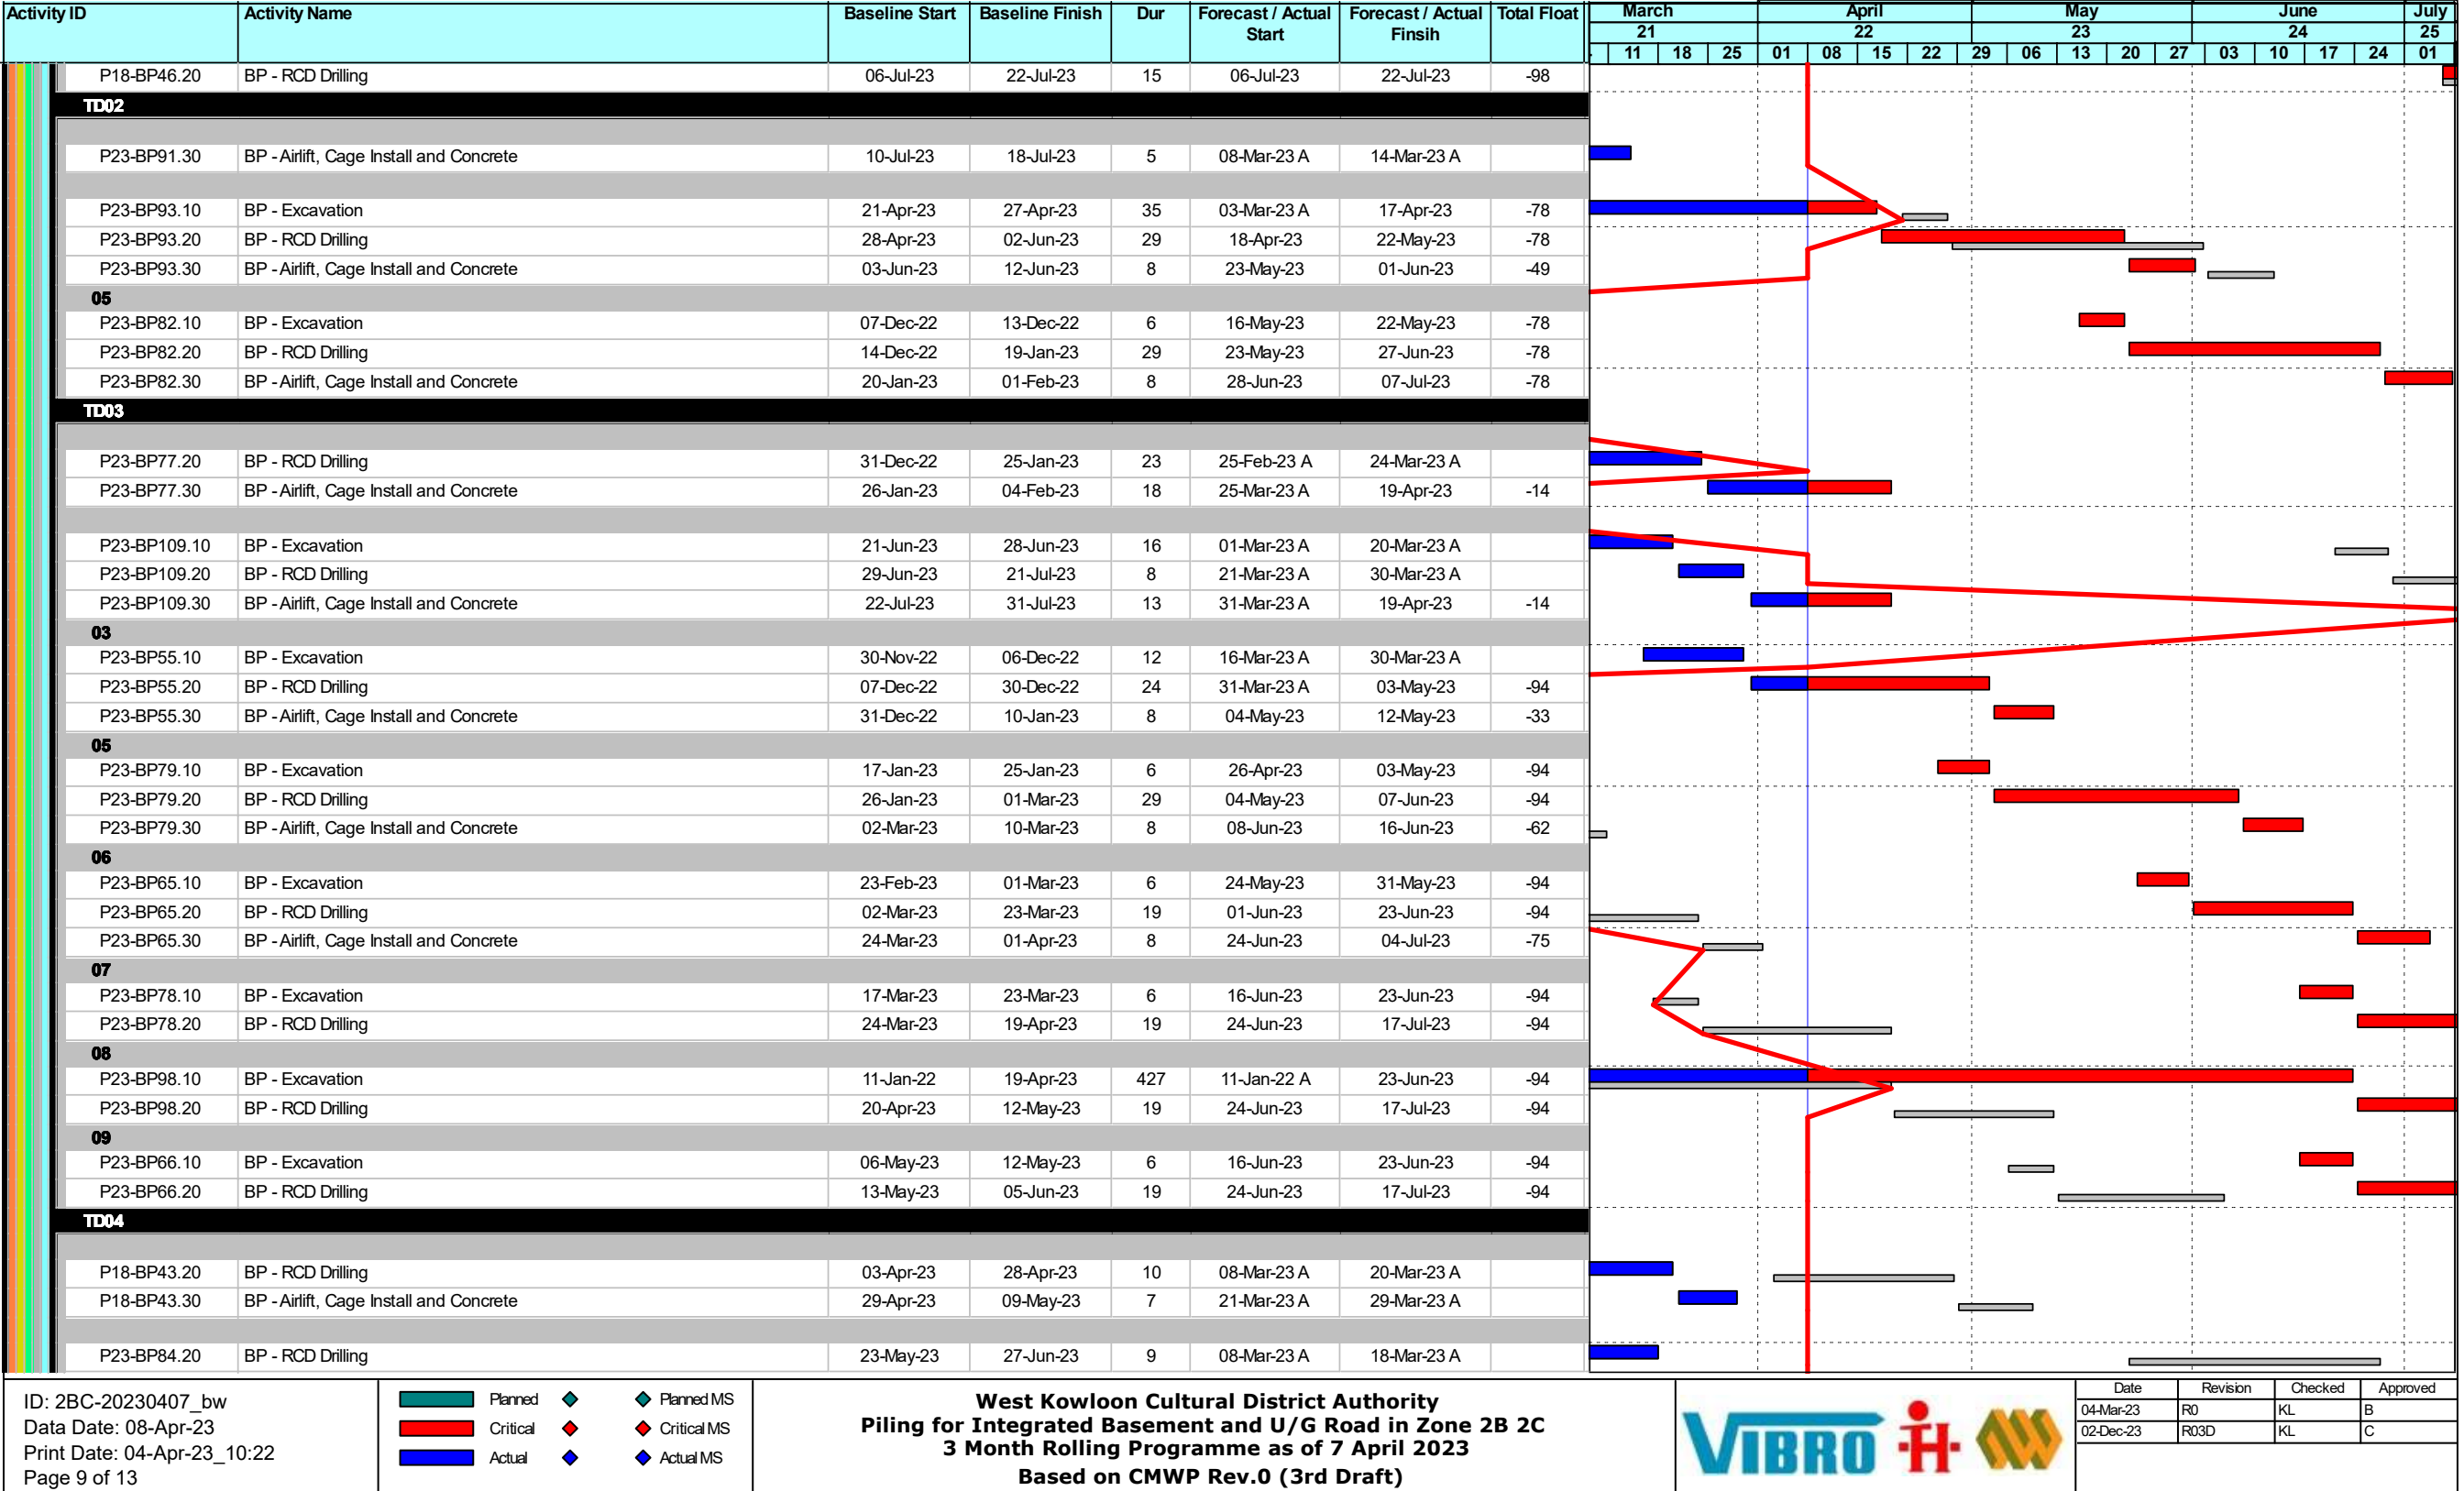

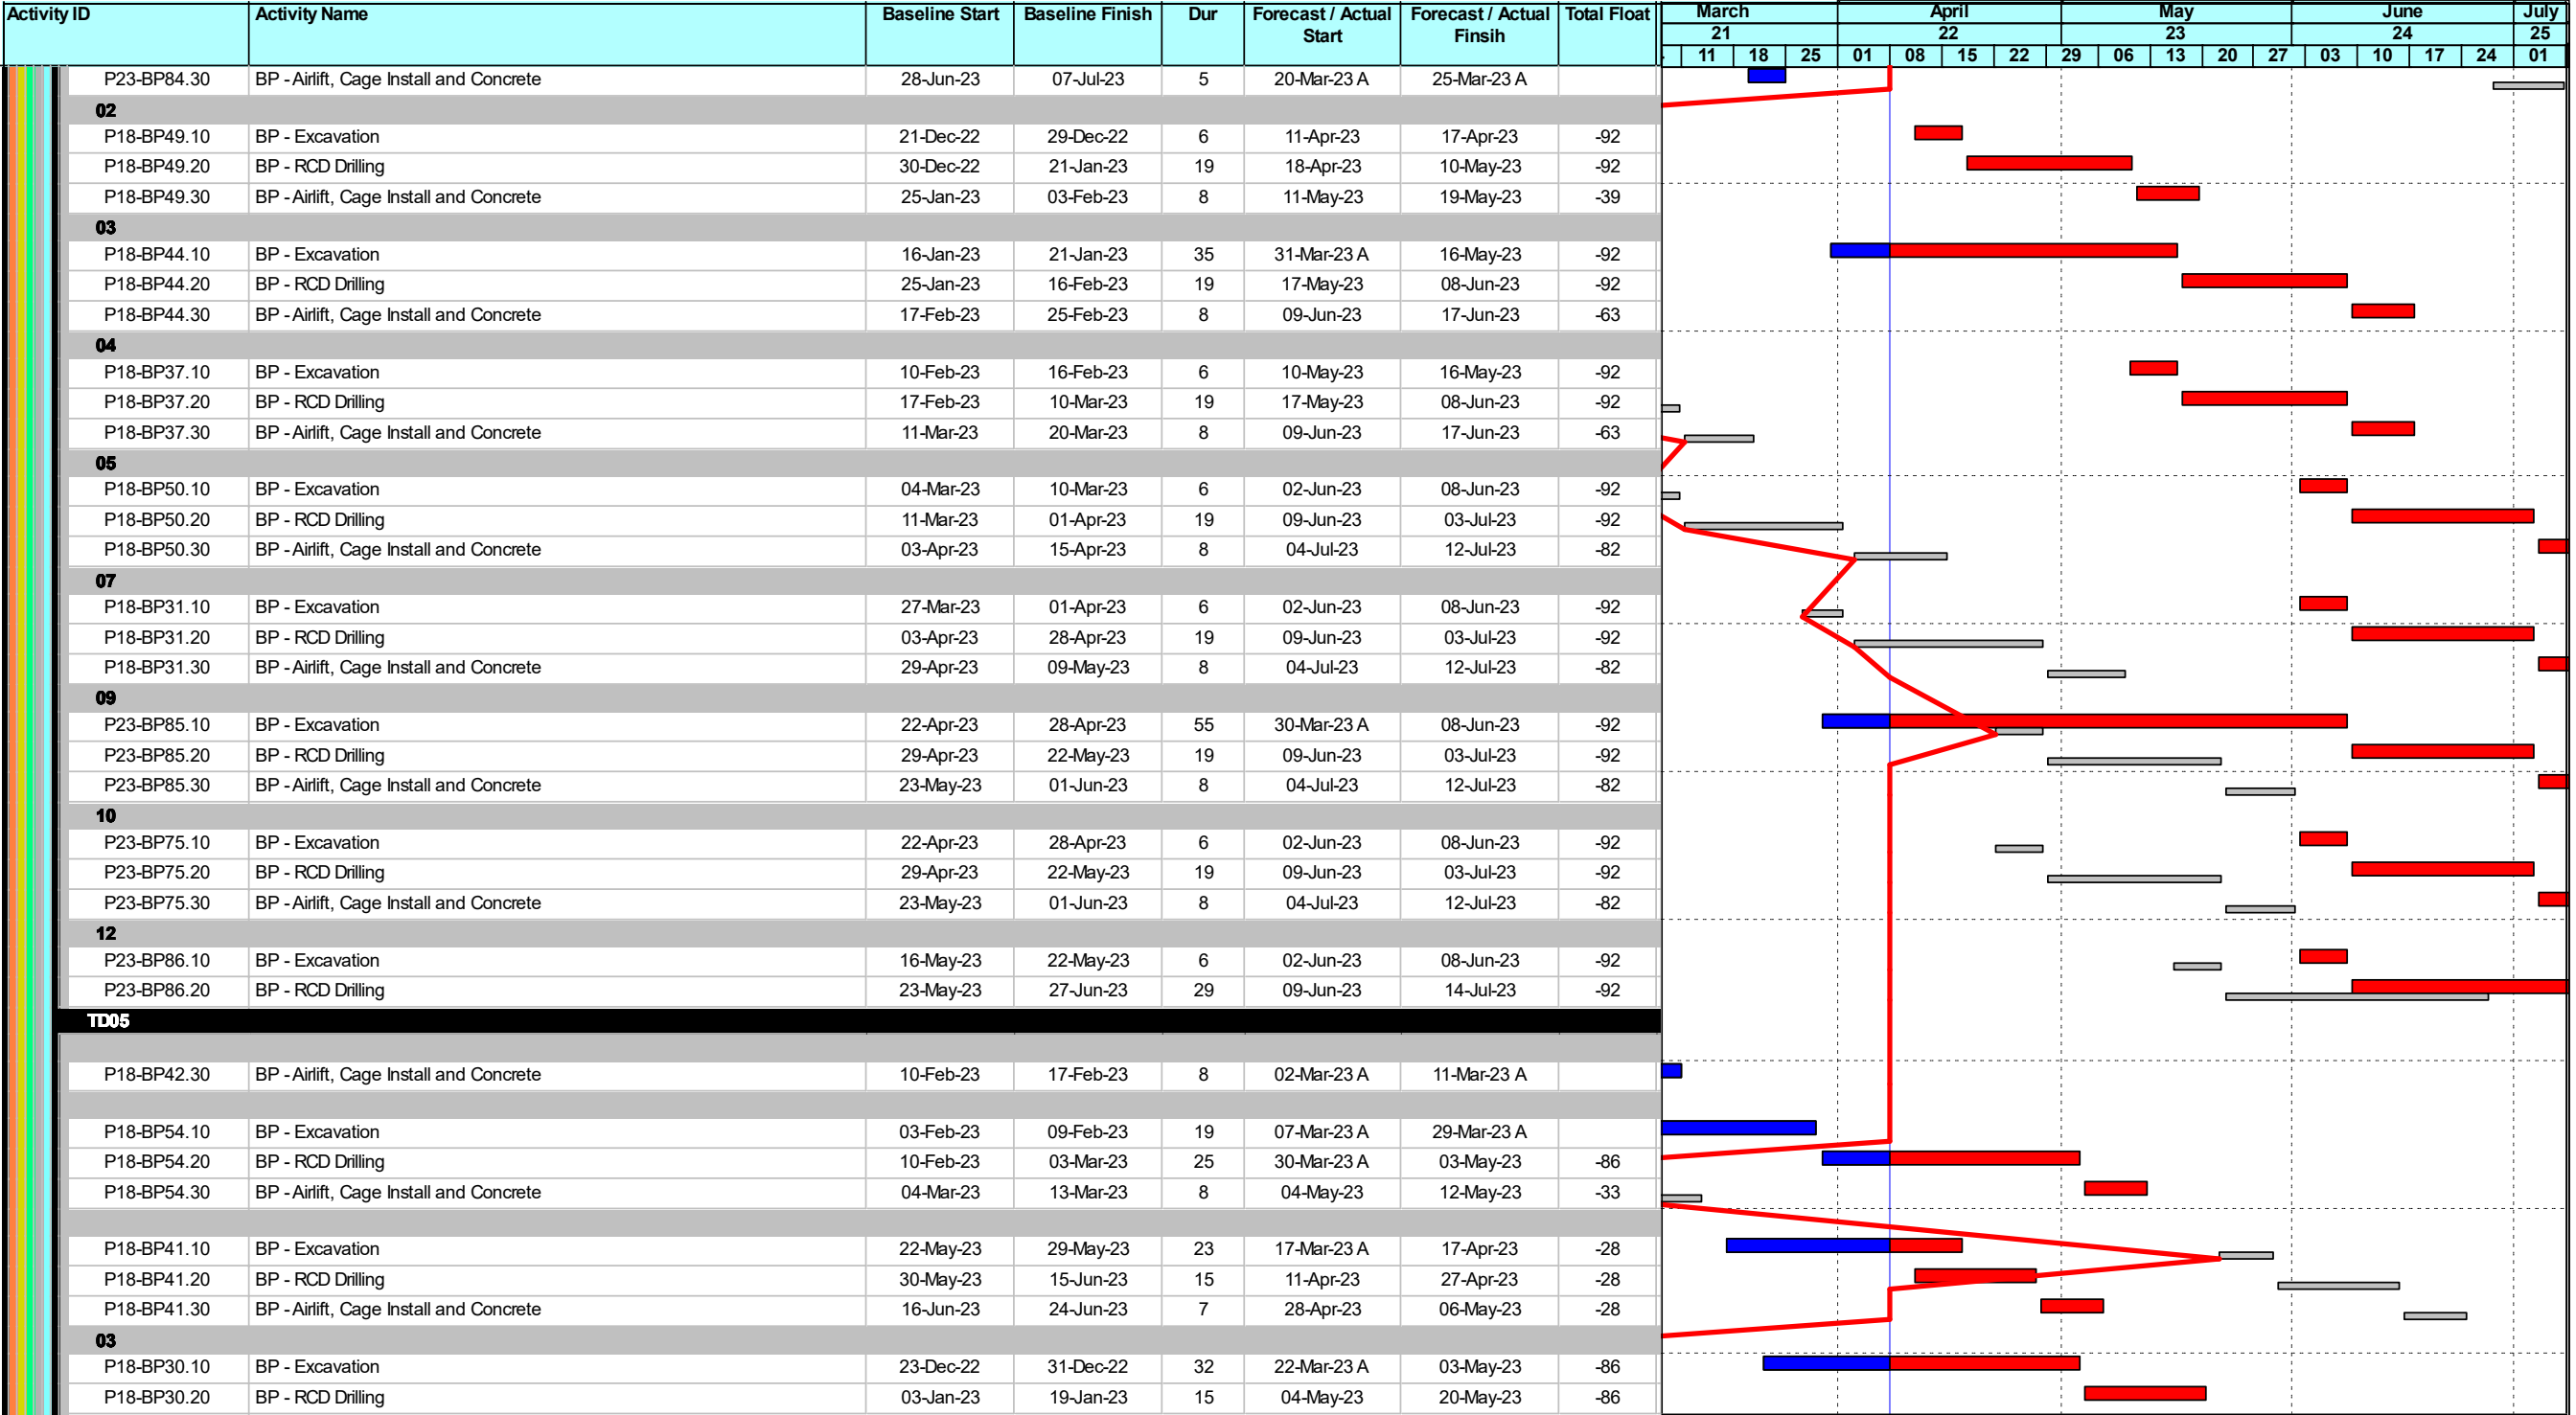

Activity ID		Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	March 21				April 22				May 23				June 24				July 25																									
									11	18	25	01	08	15	22	29	06	13	20	27	03	10	17	24	01																									
		P18-BP30.30	BP - Airlift, Cage Install and Concrete	20-Jan-23	31-Jan-23	7	22-May-23	30-May-23	-47																																									
		06																																																
		P18-BP64.10	BP - Excavation	25-Feb-23	03-Mar-23	6	15-May-23	20-May-23	-86																																									
		P18-BP64.20	BP - RCD Drilling	04-Mar-23	25-Mar-23	19	22-May-23	13-Jun-23	-86																																									
		P18-BP64.30	BP - Airlift, Cage Install and Concrete	27-Mar-23	04-Apr-23	8	14-Jun-23	23-Jun-23	-67																																									
		07																																																
		P18-BP36.10	BP - Excavation	20-Mar-23	25-Mar-23	6	07-Jun-23	13-Jun-23	-86																																									
		P18-BP36.20	BP - RCD Drilling	27-Mar-23	17-Apr-23	15	14-Jun-23	03-Jul-23	-86																																									
		P18-BP36.30	BP - Airlift, Cage Install and Concrete	18-Apr-23	25-Apr-23	7	04-Jul-23	11-Jul-23	-81																																									
		09																																																
		P18-BP60.10	BP - Excavation	28-Apr-23	05-May-23	6	07-Jun-23	13-Jun-23	-86																																									
		P18-BP60.20	BP - RCD Drilling	06-May-23	29-May-23	19	14-Jun-23	07-Jul-23	-86																																									
		TD06																																																
		P18-BP21.30	BP - Airlift, Cage Install and Concrete	25-Mar-23	01-Apr-23	14	20-Feb-23 A	08-Mar-23 A																																										
		P18-BP17.10	BP IAR-S - Excavation	04-Jan-23	10-Jan-23	19	14-Feb-23 A	08-Mar-23 A																																										
		P18-BP17.20	BP IAR-S - RCD Drilling	11-Jan-23	31-Jan-23	39	09-Mar-23 A	27-Apr-23	-87																																									
		P18-BP17.30	BP IAR-S - Airlift, Cage Install and Concrete	01-Feb-23	08-Feb-23	7	28-Apr-23	06-May-23	-28																																									
		03																																																
		P18-BP23.10	BP IAR-S - Excavation	26-Nov-22	02-Dec-22	6	11-Apr-23	17-Apr-23	-36																																									
		P18-BP23.20	BP IAR-S - RCD Drilling	03-Dec-22	20-Dec-22	15	18-Apr-23	05-May-23	-36																																									
		P18-BP23.30	BP IAR-S - Airlift, Cage Install and Concrete	23-Dec-22	03-Jan-23	7	09-May-23	16-May-23	-36																																									
		06																																																
		P18-BP29.10	BP - Excavation	21-Jan-23	31-Jan-23	6	21-Apr-23	27-Apr-23	-87																																									
		P18-BP29.20	BP - RCD Drilling	01-Feb-23	17-Feb-23	15	28-Apr-23	16-May-23	-87																																									
		P18-BP29.30	BP - Airlift, Cage Install and Concrete	18-Feb-23	25-Feb-23	7	17-May-23	24-May-23	-43																																									
		07																																																
		P18-BP33.10	BP - Excavation	11-Feb-23	17-Feb-23	6	10-May-23	16-May-23	-87																																									
		P18-BP33.20	BP - RCD Drilling	18-Feb-23	07-Mar-23	15	17-May-23	03-Jun-23	-87																																									
		P18-BP33.30	BP - Airlift, Cage Install and Concrete	08-Mar-23	15-Mar-23	7	05-Jun-23	12-Jun-23	-58																																									
		09																																																
		P18-BP32.10	BP - Excavation	18-Mar-23	24-Mar-23	6	22-May-23	29-May-23	-87																																									
		P18-BP32.20	BP - RCD Drilling	25-Mar-23	20-Apr-23	19	30-May-23	20-Jun-23	-87																																									
		P18-BP32.30	BP - Airlift, Cage Install and Concrete	21-Apr-23	29-Apr-23	8	21-Jun-23	30-Jun-23	-73																																									
		10																																																
		P18-BP34.10	BP - Excavation	14-Apr-23	20-Apr-23	6	14-Jun-23	20-Jun-23	-87																																									
		P18-BP34.20	BP - RCD Drilling	21-Apr-23	09-May-23	15	21-Jun-23	10-Jul-23	-87																																									
		TD07																																																
		P18-BP13.20	BP - RCD Drilling	03-May-23	24-May-23	9	27-Feb-23 A	09-Mar-23 A																																										
		P18-BP13.30	BP - Airlift, Cage Install and Concrete	25-May-23	03-Jun-23	8	10-Mar-23 A	20-Mar-23 A																																										
		P18-BP25.10	BP - Excavation	29-Mar-23	04-Apr-23	16	27-Feb-23 A	17-Mar-23 A																																										
		P18-BP25.20	BP - RCD Drilling	06-Apr-23	02-May-23	56	18-Mar-23 A	29-May-23	-54																																									
		P18-BP25.30	BP - Airlift, Cage Install and Concrete	03-May-23	11-May-23	8	30-May-23	07-Jun-23	-54																																									
		TD08																																																
ID: 2BC-20230407_bw Data Date: 08-Apr-23 Print Date: 04-Apr-23_10:22 Page 11 of 13			<div><div><div></div><div></div><div></div></div><div><div>Planned</div><div>Critical</div><div>Actual</div></div><div><div></div><div></div><div></div></div><div><div>Planned MS</div><div>Critical MS</div><div>Actual MS</div></div></div>						<div><div><div>West Kowloon Cultural District Authority</div><div>Piling for Integrated Basement and U/G Road in Zone 2B 2C</div><div>3 Month Rolling Programme as of 7 April 2023</div><div>Based on CMWP Rev.0 (3rd Draft)</div></div></div>						<div><div>VIBRO</div><div></div><div></div></div> <div><div>Date</div><div>Revision</div><div>Checked</div><div>Approved</div></div> <div><div>04-Mar-23</div><div>R0</div><div>KL</div><div>B</div></div> <div><div>02-Dec-23</div><div>R03D</div><div>KL</div><div>C</div></div>																																			

