

**Zone 2B & 2C**

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	May 23				June 24				July 25				August 26				
								29	06	13	20	27	03	10	17	24	01	08	15	22	29	05	12	19

**Piling for Integrated Basement and U/G Road In Zone 2B & 2C**

**Contract Dates**

**Optional Works subjected to CA's Instruction**

CO2B	Last CAI date for Optional Works Item No.2B (330 Days to 660 Days after Commencement)	13-May-23		0	13-May-23 A		
CO2C	Last CAI date for Optional Works Item No.2C (330 Days to 710 Days after Commencement)	02-Jul-23		0	02-Jul-23		71

**Construction Stage**

**Pile Construction**

**KD05 (Section 1)**

**Bored Piles - Drainage Diversion**

**CD07**

**04**

P17-BP19.10	BP - Excavation	27-Jan-23	03-Feb-23	9	27-Apr-23 A	09-May-23 A	
P17-BP19.20	BP - RCD Drilling	04-Feb-23	21-Feb-23	5	10-May-23 A	16-May-23 A	
P17-BP19.30	BP - Airlift, Cage Install and Concrete	22-Feb-23	01-Mar-23	7	17-May-23 A	25-May-23 A	

**CD08**

P17-BP21.10	BP IAR-N - Excavation	07-Mar-23	13-Mar-23	15	11-Apr-23 A	28-Apr-23 A	
P17-BP21.20	BP IAR-N - RCD Drilling	14-Mar-23	30-Mar-23	5	29-Apr-23 A	06-May-23 A	
P17-BP21.30	BP IAR-N - Airlift, Cage Install and Concrete	31-Mar-23	12-Apr-23	7	08-May-23 A	16-May-23 A	

**01**

P17-BP20.10	BP - Excavation	17-Feb-23	23-Feb-23	4	27-May-23	31-May-23	-201
P17-BP20.20	BP - RCD Drilling	24-Feb-23	13-Mar-23	15	01-Jun-23	17-Jun-23	-201
P17-BP20.30	BP - Airlift, Cage Install and Concrete	14-Mar-23	21-Mar-23	7	19-Jun-23	27-Jun-23	-201

**03**

P17-BP18.10	BP IAR-N - Excavation	24-Mar-23	30-Mar-23	11	20-May-23 A	02-Jun-23	-203
P17-BP18.20	BP IAR-N - RCD Drilling	31-Mar-23	21-Apr-23	15	03-Jun-23 A	20-Jun-23	-203
P17-BP18.30	BP IAR-N - Airlift, Cage Install and Concrete	22-Apr-23	29-Apr-23	7	21-Jun-23 A	29-Jun-23	-203

**Bored Piles - Gantry Gate A**

**CD06**

**08**

CBA-BP01.30	BP - Airlift, Cage Install and Concrete	17-Feb-23	23-Feb-23	9	24-Apr-23 A	05-May-23 A	
-------------	---	-----------	-----------	---	-------------	-------------	--

**CD07**

**02**

P22&P19-BP26.:	BP - RCD Drilling	16-Jul-22	03-Dec-22	261	16-Jul-22 A	02-Jun-23	-189
P22&P19-BP26.:	BP - Airlift, Cage Install and Concrete	05-Dec-22	13-Dec-22	8	03-Jun-23	12-Jun-23	-189

**Bored Piles**


**CD09**

**03**

P17-BP22.30	BP IAR-N - Airlift, Cage Install and Concrete	04-Apr-23	15-Apr-23	7	20-Apr-23 A	28-Apr-23 A	
-------------	---	-----------	-----------	---	-------------	-------------	--

**TD07**

P18-BP04.30	BP IAR-S - Airlift, Cage Install and Concrete	01-Mar-23	08-Mar-23	11	19-Apr-23 A	03-May-23 A	
P18-BP01.20	BP - RCD Drilling	22-Dec-22	16-Jan-23	21	26-Apr-23 A	22-May-23 A	

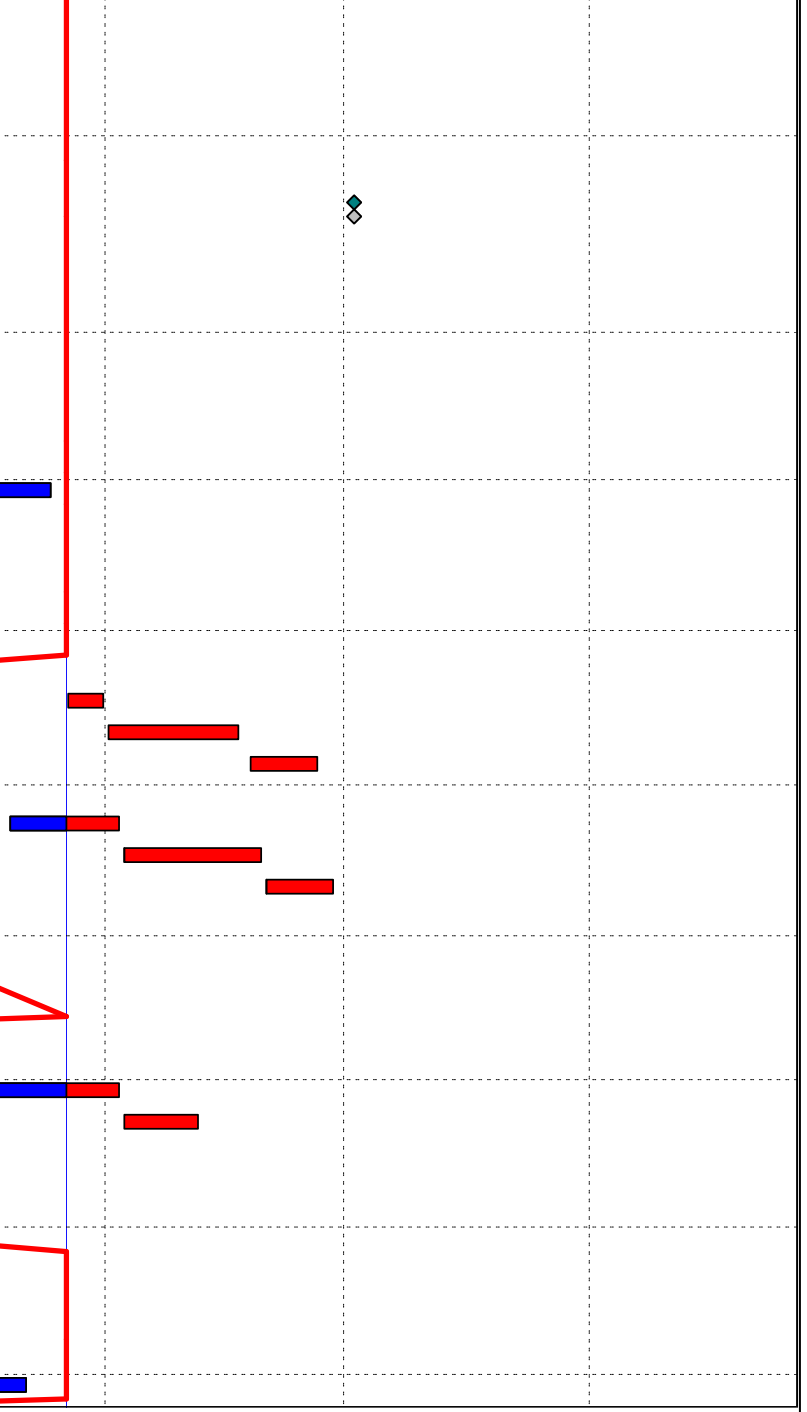


	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS





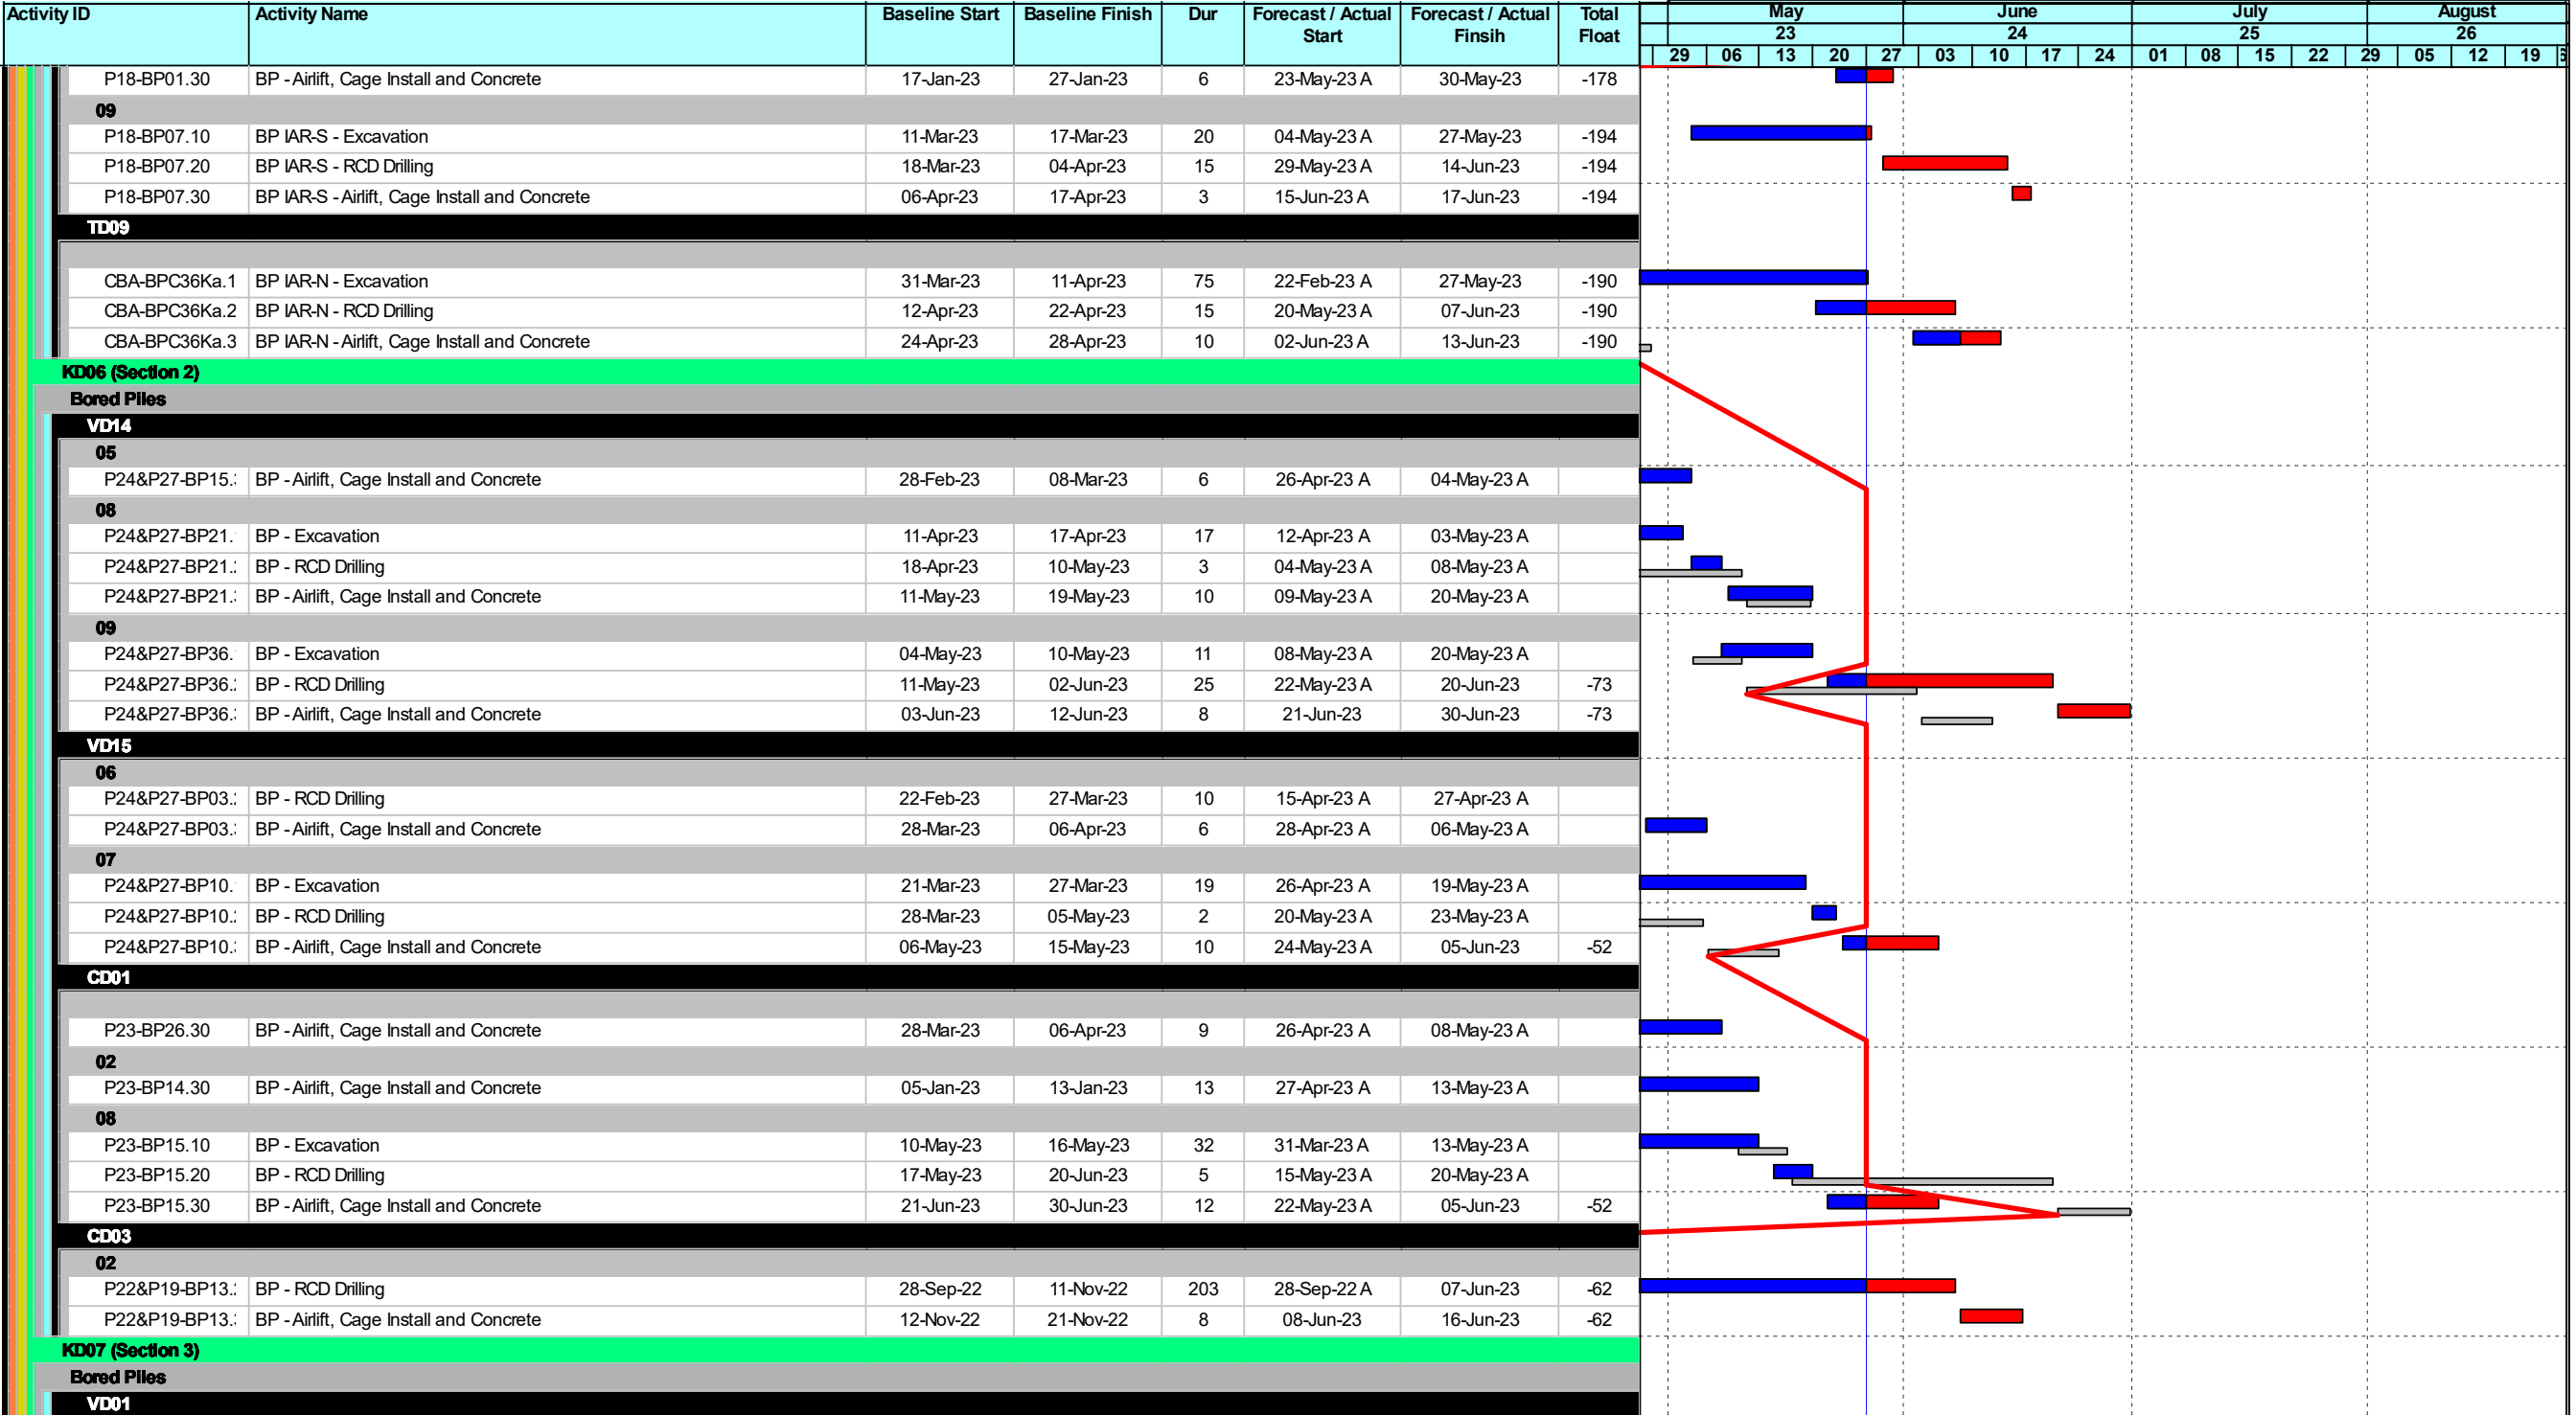

**West Kowloon Cultural District Authority**  
**Piling for Integrated Basement and U/G Road in Zone 2B 2C**  
**3 Month Rolling Programme as of 26 May 2023**  
**Based on CMWP Rev.0 (3rd Draft)**



Date	Revision	Checked	Approved
04-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C




Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	May 23				June 24				July 25				August 26				
								29	06	13	20	27	03	10	17	24	01	08	15	22	29	05	12	19
<b>07</b>																								
P26-BP07.10	BP - Excavation	28-Apr-23	05-May-23	6	27-May-23	02-Jun-23	-30																	
P26-BP07.20	BP - RCD Drilling	06-May-23	09-Jun-23	29	03-Jun-23	08-Jul-23	-30																	
P26-BP07.30	BP - Airlift, Cage Install and Concrete	10-Jun-23	19-Jun-23	8	10-Jul-23	18-Jul-23	-1																	
<b>08</b>																								
P26-BP05.10	BP - Excavation	03-Jun-23	09-Jun-23	6	03-Jul-23	08-Jul-23	-30																	
P26-BP05.20	BP - RCD Drilling	10-Jun-23	15-Jul-23	29	10-Jul-23	11-Aug-23	-30																	
P26-BP05.30	BP - Airlift, Cage Install and Concrete	17-Jul-23	25-Jul-23	8	12-Aug-23	21-Aug-23	-30																	
<b>VD02</b>																								
<b>02</b>																								
P30-BP71.20	BP - RCD Drilling	31-Dec-22	24-Feb-23	13	22-Apr-23 A	09-May-23 A																		
P30-BP71.30	BP - Airlift, Cage Install and Concrete	25-Feb-23	07-Mar-23	23	10-May-23 A	06-Jun-23	33																	
<b>04</b>																								
P30-BP75.10	BP - Excavation	24-Mar-23	30-Mar-23	6	27-May-23	02-Jun-23	-20																	
P30-BP75.20	BP - RCD Drilling	31-Mar-23	09-May-23	29	03-Jun-23	08-Jul-23	-20																	
P30-BP75.30	BP - Airlift, Cage Install and Concrete	10-May-23	18-May-23	8	10-Jul-23	18-Jul-23	-1																	
<b>05</b>																								
P30-BP74.10	BP - Excavation	23-Jun-22	09-May-23	280	23-Jun-22 A	02-Jun-23	-20																	
P30-BP74.20	BP - RCD Drilling	10-May-23	01-Jun-23	24	29-May-23 A	26-Jun-23	-20																	
P30-BP74.30	BP - Airlift, Cage Install and Concrete	02-Jun-23	10-Jun-23	8	27-Jun-23	06-Jul-23	9																	
<b>06</b>																								
P26-BP04.10	BP - Excavation	25-May-23	01-Jun-23	6	19-Jun-23	26-Jun-23	-20																	
P26-BP04.20	BP - RCD Drilling	02-Jun-23	07-Jul-23	29	27-Jun-23	31-Jul-23	-20																	
P26-BP04.30	BP - Airlift, Cage Install and Concrete	08-Jul-23	17-Jul-23	8	01-Aug-23	09-Aug-23	-20																	
<b>VD08</b>																								
P28&P29-BP23.	BP - Excavation	20-Jul-23	26-Jul-23	25	28-Mar-23 A	02-May-23 A																		
P28&P29-BP23.:	BP - RCD Drilling	27-Jul-23	17-Aug-23	4	03-May-23 A	08-May-23 A																		
P28&P29-BP23.:	BP - Airlift, Cage Install and Concrete	18-Aug-23	26-Aug-23	15	08-May-23 A	25-May-23 A																		
P24&P27-BP25.	BP - Excavation	22-May-23	29-May-23	35	20-Apr-23 A	01-Jun-23	-64																	
P24&P27-BP25.:	BP - RCD Drilling	30-May-23	04-Jul-23	34	27-May-23 A	07-Jul-23	-64																	
P24&P27-BP25.:	BP - Airlift, Cage Install and Concrete	05-Jul-23	13-Jul-23	8	08-Jul-23	17-Jul-23	0																	
<b>03</b>																								
P24&P27-BP32.	BP - Excavation	03-Feb-23	09-Feb-23	6	09-Jun-23	15-Jun-23	-64																	
P24&P27-BP32.:	BP - RCD Drilling	10-Feb-23	15-Mar-23	29	16-Jun-23	21-Jul-23	-64																	
P24&P27-BP32.:	BP - Airlift, Cage Install and Concrete	16-Mar-23	24-Mar-23	8	22-Jul-23	31-Jul-23	-12																	
<b>04</b>																								
P24&P27-BP20.	BP - Excavation	09-Mar-23	15-Mar-23	6	15-Jul-23	21-Jul-23	-64																	
P24&P27-BP20.:	BP - RCD Drilling	16-Mar-23	22-Apr-23	29	22-Jul-23	24-Aug-23	-64																	
P24&P27-BP20.:	BP - Airlift, Cage Install and Concrete	24-Apr-23	03-May-23	8	25-Aug-23	02-Sep-23	-41																	
<b>05</b>																								
P24&P27-BP19.	BP - Excavation	17-Apr-23	22-Apr-23	6	11-Aug-23	17-Aug-23	-64																	
P24&P27-BP19.:	BP - RCD Drilling	24-Apr-23	29-May-23	29	18-Aug-23	20-Sep-23	-64																	
<b>07</b>																								
P28&P29-BP26.	BP - Excavation	11-Aug-23	17-Aug-23	6	11-Aug-23	17-Aug-23	-64																	







 Planned	 Planned MS
 Critical	 Critical MS
 Actual	 Actual MS

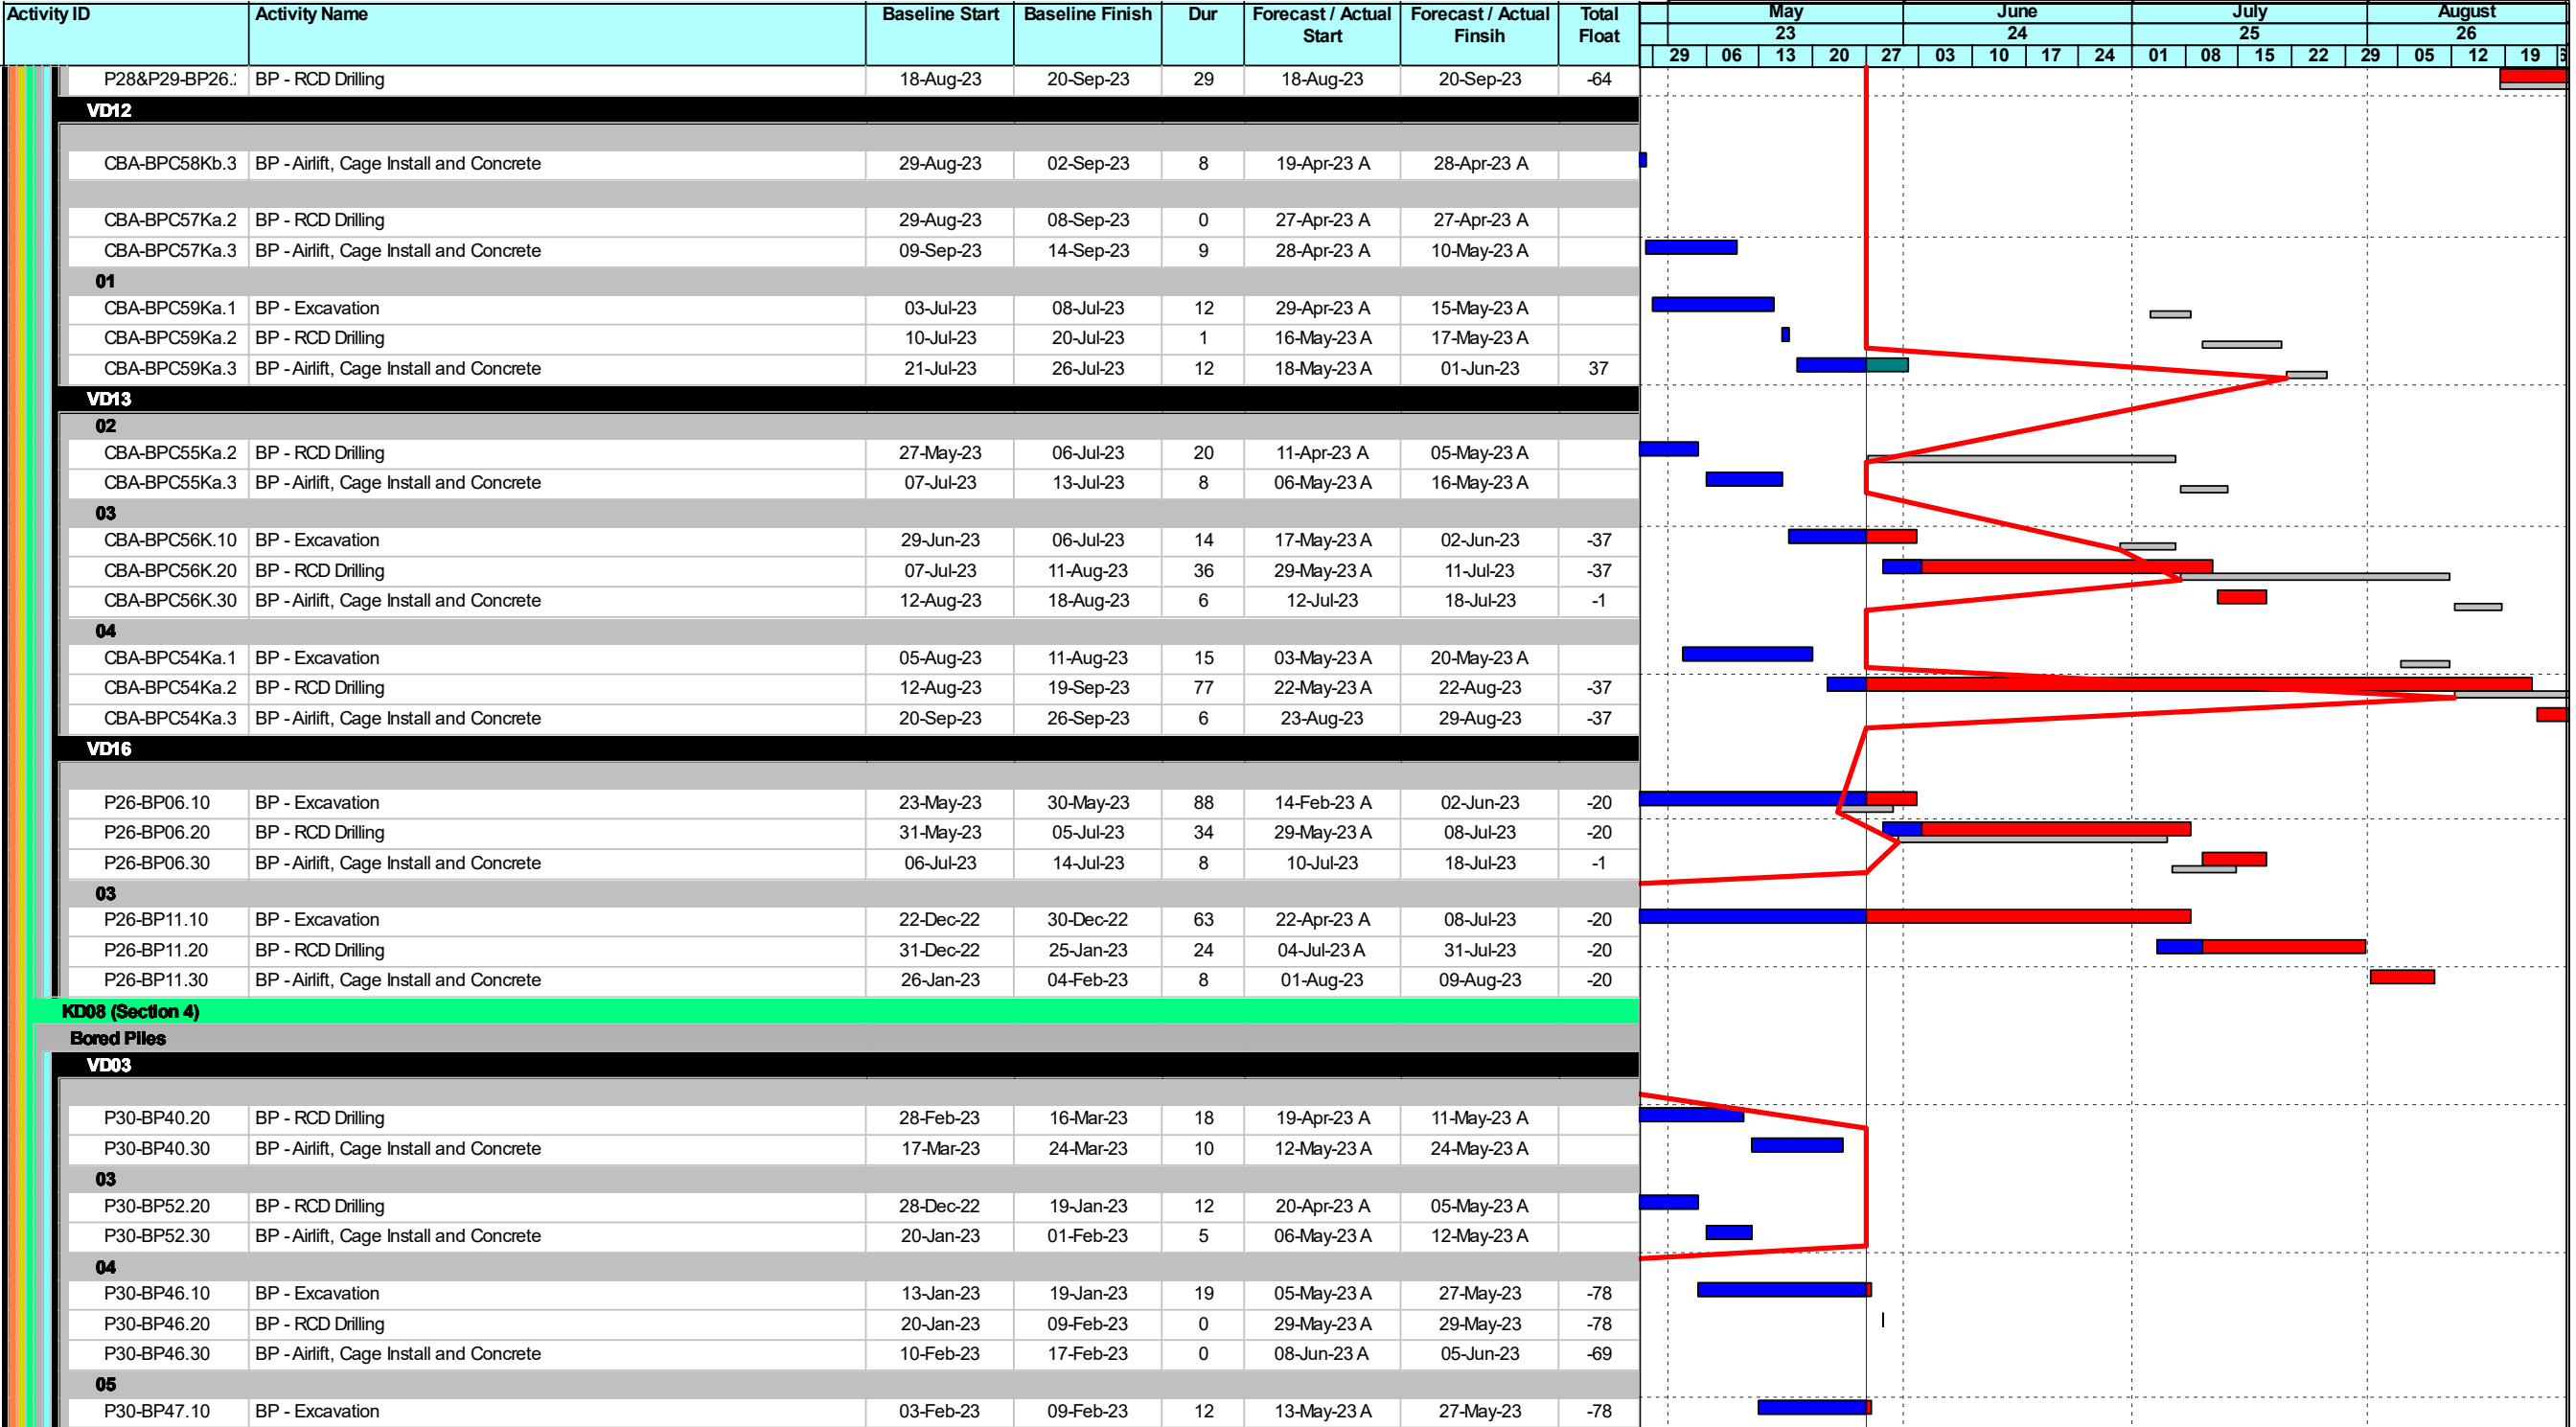**West Kowloon Cultural District Authority**  
**Piling for Integrated Basement and U/G Road in Zone 2B 2C**  
**3 Month Rolling Programme as of 26 May 2023**  
 Based on CMWP Rev.0 (3rd Draft)




Date	Revision	Checked	Approved
04-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C



	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS

	Date	Revision	Checked	Approved
	04-Mar-22	R0	KL	B
	02-Dec-22	R03D	KL	C

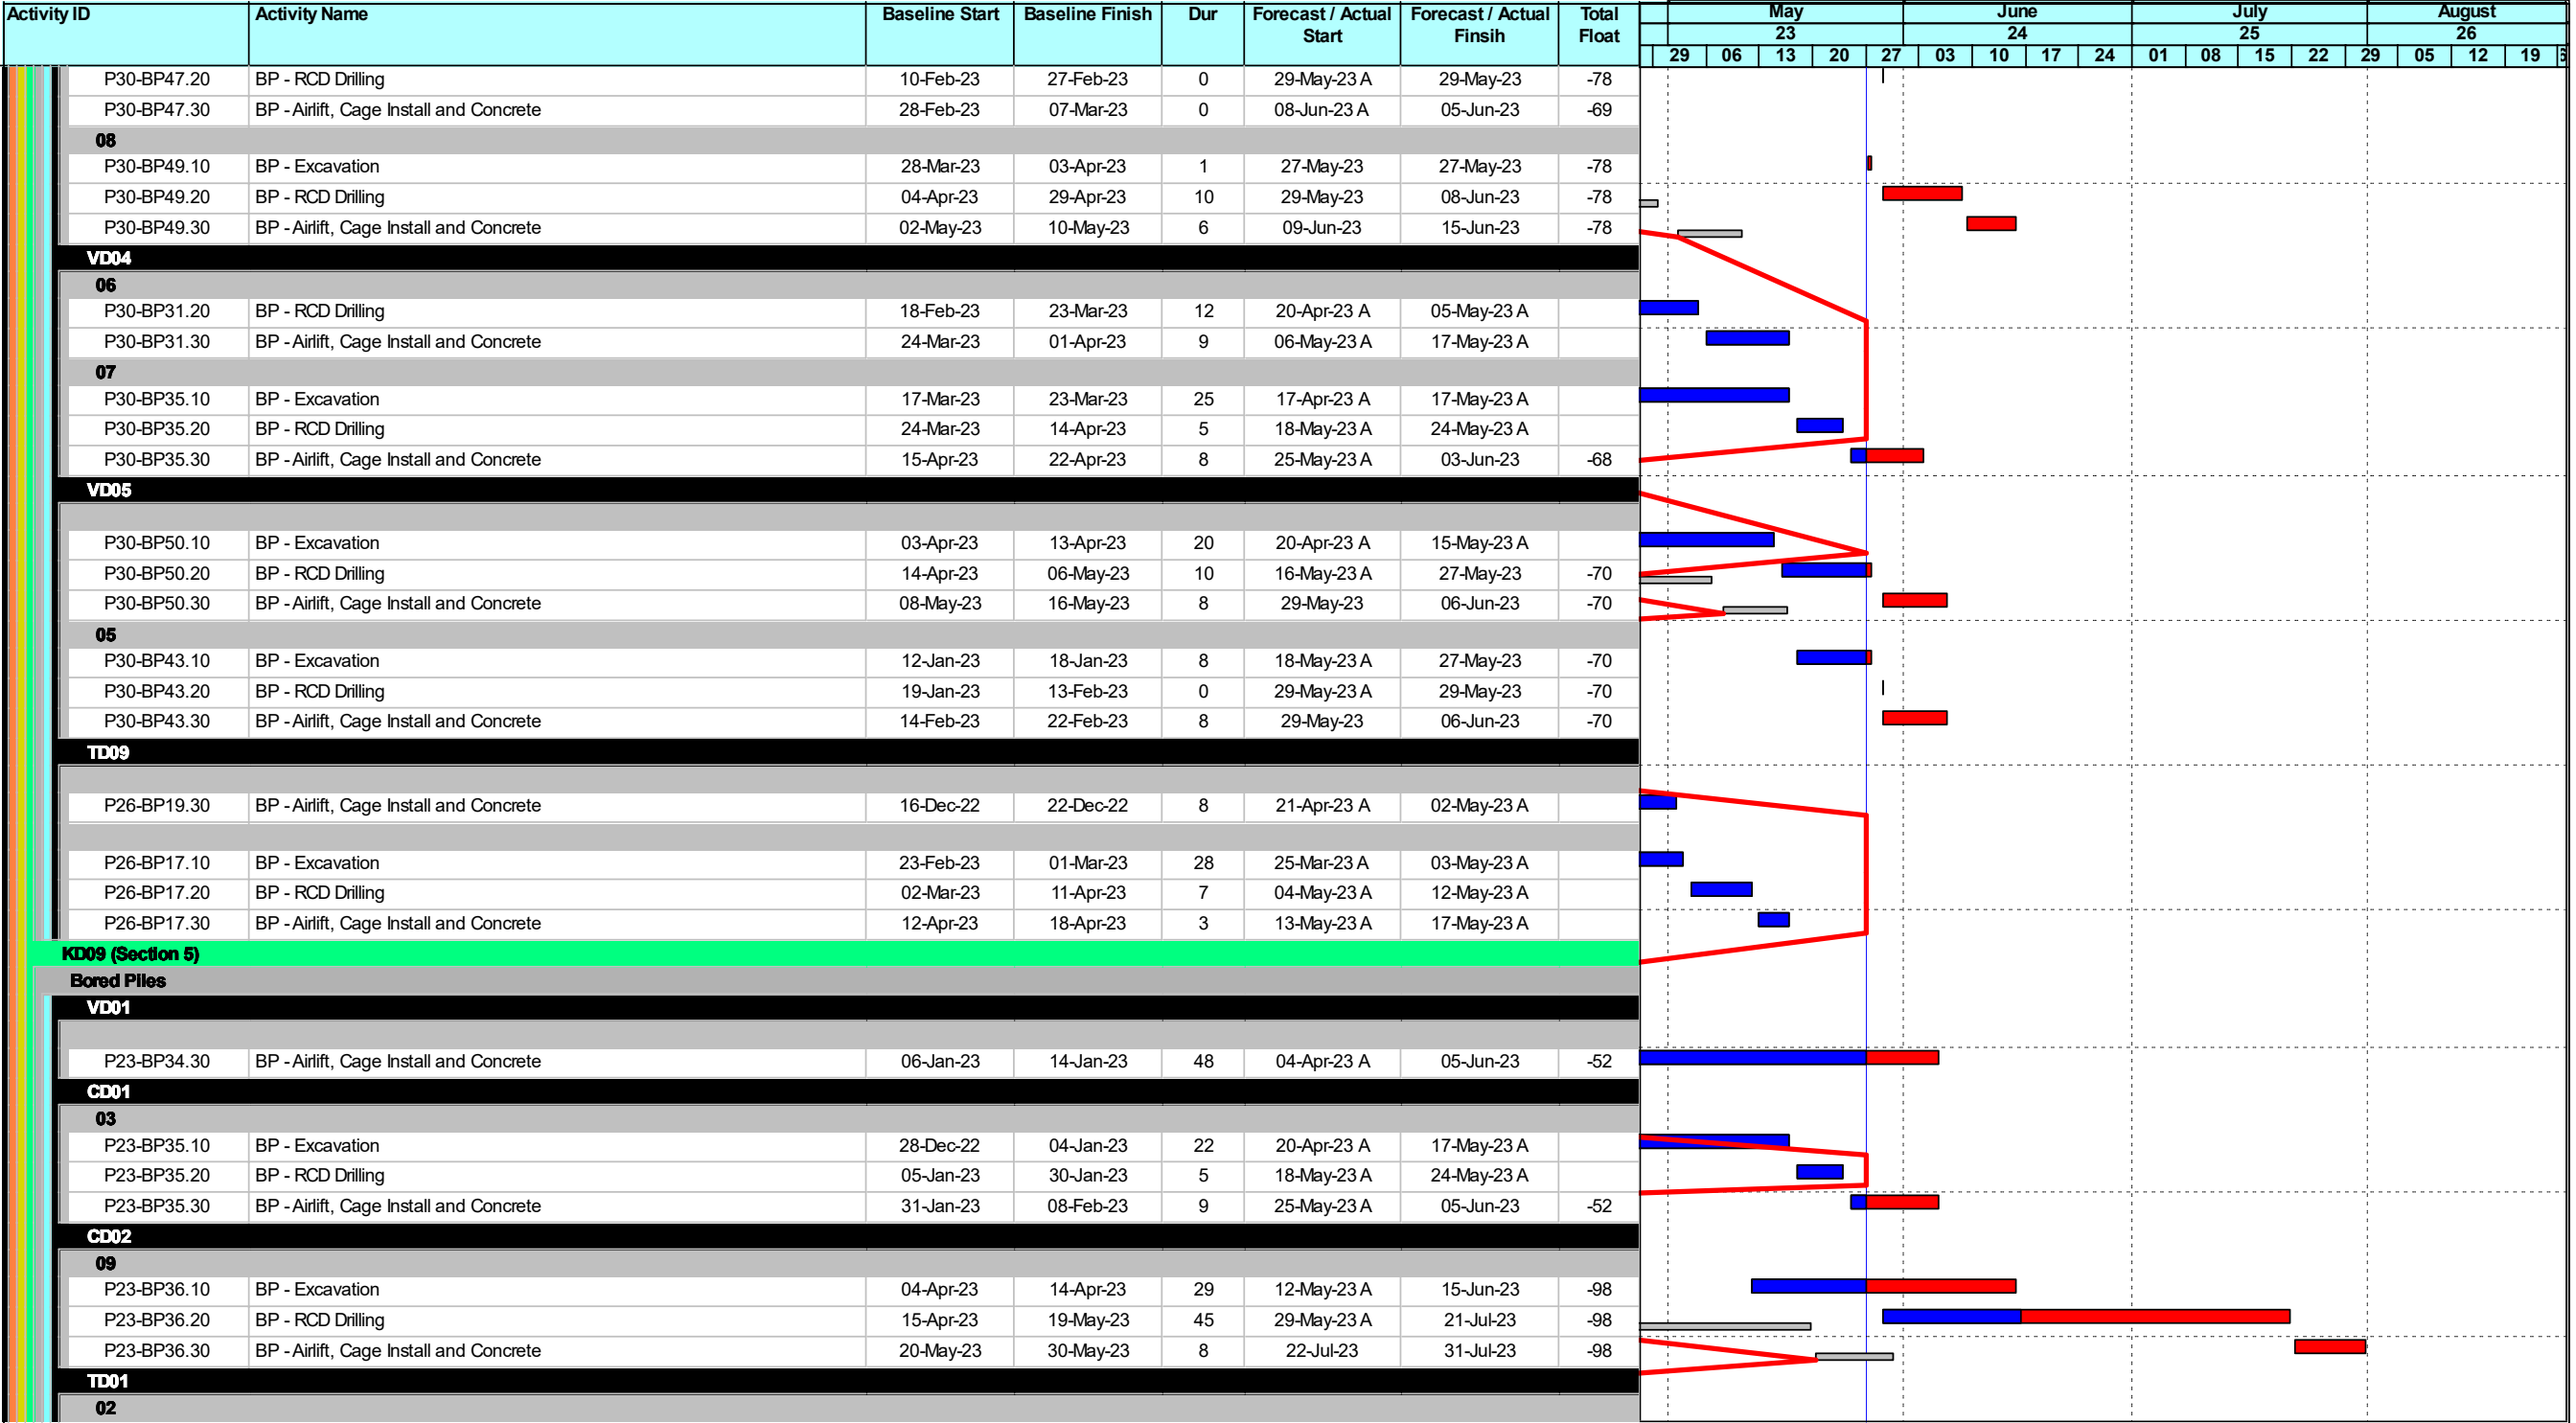

█ Planned   ◆ Critical   █ Actual  
◆ Planned MS   ◆ Critical MS   ◆ Actual MS

**West Kowloon Cultural District Authority**  
**Piling for Integrated Basement and U/G Road in Zone 2B 2C**  
**3 Month Rolling Programme as of 26 May 2023**  
**Based on CMWP Rev.0 (3rd Draft)**



Date	Revision	Checked	Approved
04-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	May				June				July				August									
								23		20		24		25		26		26		19									
								29	06	13	20	03	10	17	24	01	08	15	22	29	05	12	19						
P18-BP57.10	BP - Excavation	22-Dec-22	30-Dec-22	6	27-May-23	02-Jun-23	-77																						
P18-BP57.20	BP - RCD Drilling	31-Dec-22	25-Jan-23	19	03-Jun-23	26-Jun-23	-77																						
P18-BP57.30	BP - Airlift, Cage Install and Concrete	26-Jan-23	04-Feb-23	8	27-Jun-23	06-Jul-23	-77																						
<b>04</b>																													
P18-BP62.10	BP - Excavation	11-Feb-23	17-Feb-23	6	27-May-23	02-Jun-23	-95																						
P18-BP62.20	BP - RCD Drilling	18-Feb-23	11-Mar-23	19	03-Jun-23	26-Jun-23	-95																						
P18-BP62.30	BP - Airlift, Cage Install and Concrete	13-Mar-23	21-Mar-23	8	27-Jun-23	06-Jul-23	-77																						
<b>06</b>																													
P18-BP45.10	BP - Excavation	28-Mar-23	03-Apr-23	6	27-May-23	02-Jun-23	-95																						
P18-BP45.20	BP - RCD Drilling	04-Apr-23	29-Apr-23	19	03-Jun-23	26-Jun-23	-95																						
P18-BP45.30	BP - Airlift, Cage Install and Concrete	02-May-23	10-May-23	8	27-Jun-23	06-Jul-23	-77																						
<b>07</b>																													
P18-BP52.10	BP - Excavation	24-Apr-23	29-Apr-23	6	27-May-23	02-Jun-23	-95																						
P18-BP52.20	BP - RCD Drilling	02-May-23	23-May-23	19	03-Jun-23	26-Jun-23	-95																						
P18-BP52.30	BP - Airlift, Cage Install and Concrete	24-May-23	02-Jun-23	8	27-Jun-23	06-Jul-23	-77																						
<b>08</b>																													
P18-BP40.10	BP - Excavation	17-May-23	23-May-23	6	27-May-23	02-Jun-23	-95																						
P18-BP40.20	BP - RCD Drilling	24-May-23	10-Jun-23	15	03-Jun-23	20-Jun-23	-95																						
P18-BP40.30	BP - Airlift, Cage Install and Concrete	12-Jun-23	19-Jun-23	7	21-Jun-23	29-Jun-23	-72																						
<b>09</b>																													
P18-BP51.10	BP - Excavation	05-Jun-23	10-Jun-23	6	08-Jun-23	14-Jun-23	-95																						
P18-BP51.20	BP - RCD Drilling	12-Jun-23	05-Jul-23	19	15-Jun-23	08-Jul-23	-95																						
P18-BP51.30	BP - Airlift, Cage Install and Concrete	06-Jul-23	14-Jul-23	8	10-Jul-23	18-Jul-23	-87																						
<b>10</b>																													
P18-BP46.10	BP - Excavation	28-Jun-23	05-Jul-23	6	24-Jun-23	30-Jun-23	-95																						
P18-BP46.20	BP - RCD Drilling	06-Jul-23	22-Jul-23	15	03-Jul-23	19-Jul-23	-95																						
P18-BP46.30	BP - Airlift, Cage Install and Concrete	24-Jul-23	31-Jul-23	7	20-Jul-23	27-Jul-23	-95																						
<b>TD02</b>																													
P23-BP93.30	BP - Airlift, Cage Install and Concrete	03-Jun-23	12-Jun-23	8	25-Apr-23 A	05-May-23 A																							
<b>05</b>																													
P23-BP82.10	BP - Excavation	07-Dec-22	13-Dec-22	23	06-May-23 A	02-Jun-23	-87																						
P23-BP82.20	BP - RCD Drilling	14-Dec-22	19-Jan-23	34	29-May-23 A	08-Jul-23	-87																						
P23-BP82.30	BP - Airlift, Cage Install and Concrete	20-Jan-23	01-Feb-23	8	10-Jul-23	18-Jul-23	-87																						
<b>TD03</b>																													
<b>03</b>																													
P23-BP55.30	BP - Airlift, Cage Install and Concrete	31-Dec-22	10-Jan-23	6	22-Apr-23 A	29-Apr-23 A																							
<b>05</b>																													
P23-BP79.10	BP - Excavation	17-Jan-23	25-Jan-23	17	03-Apr-23 A	27-Apr-23 A																							
P23-BP79.20	BP - RCD Drilling	26-Jan-23	01-Mar-23	45	28-Apr-23 A	21-Jun-23	-93																						
P23-BP79.30	BP - Airlift, Cage Install and Concrete	02-Mar-23	10-Mar-23	8	23-Jun-23	03-Jul-23	-74																						
<b>06</b>																													
P23-BP65.10	BP - Excavation	23-Feb-23	01-Mar-23	19	02-May-23 A	24-May-23 A																							
P23-BP65.20	BP - RCD Drilling	02-Mar-23	23-Mar-23	42	25-May-23 A	15-Jul-23	-93																						
P23-BP65.30	BP - Airlift, Cage Install and Concrete	24-Mar-23	01-Apr-23	8	17-Jul-23	25-Jul-23	-93																						
<b>07</b>																													

	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS

**West Kowloon Cultural District Authority**  
**Piling for Integrated Basement and U/G Road in Zone 2B 2C**  
**3 Month Rolling Programme as of 26 May 2023**  
 Based on CMWP Rev.0 (3rd Draft)

Date	Revision	Checked	Approved
04-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C




Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	May 23				June 24				July 25				August 26				
								29	06	13	20	27	03	10	17	24	01	08	15	22	29	05	12	19
								Gantt Chart Area																
P23-BP78.10	BP - Excavation	17-Mar-23	23-Mar-23	6	15-Jun-23	21-Jun-23	-93	[Gantt bars for P23-BP78.10]																
P23-BP78.20	BP - RCD Drilling	24-Mar-23	19-Apr-23	19	23-Jun-23	15-Jul-23	-93	[Gantt bars for P23-BP78.20]																
P23-BP78.30	BP - Airlift, Cage Install and Concrete	20-Apr-23	28-Apr-23	8	17-Jul-23	25-Jul-23	-93	[Gantt bars for P23-BP78.30]																
<b>08</b>								[Gantt bars for section 08]																
P23-BP98.10	BP - Excavation	11-Jan-22	19-Apr-23	426	11-Jan-22 A	21-Jun-23	-93	[Gantt bars for P23-BP98.10]																
P23-BP98.20	BP - RCD Drilling	20-Apr-23	12-May-23	17	26-Jun-23 A	15-Jul-23	-93	[Gantt bars for P23-BP98.20]																
P23-BP98.30	BP - Airlift, Cage Install and Concrete	13-May-23	22-May-23	8	17-Jul-23	25-Jul-23	-93	[Gantt bars for P23-BP98.30]																
<b>09</b>								[Gantt bars for section 09]																
P23-BP66.10	BP - Excavation	06-May-23	12-May-23	6	15-Jun-23	21-Jun-23	-93	[Gantt bars for P23-BP66.10]																
P23-BP66.20	BP - RCD Drilling	13-May-23	05-Jun-23	19	23-Jun-23	15-Jul-23	-93	[Gantt bars for P23-BP66.20]																
P23-BP66.30	BP - Airlift, Cage Install and Concrete	06-Jun-23	14-Jun-23	8	17-Jul-23	25-Jul-23	-93	[Gantt bars for P23-BP66.30]																
<b>TD04</b>								[Gantt bars for section TD04]																
P23-BP85.20	BP - RCD Drilling	29-Apr-23	22-May-23	12	20-Apr-23 A	05-May-23 A		[Gantt bars for P23-BP85.20]																
P23-BP85.30	BP - Airlift, Cage Install and Concrete	23-May-23	01-Jun-23	4	06-May-23 A	11-May-23 A		[Gantt bars for P23-BP85.30]																
<b>02</b>								[Gantt bars for section 02]																
P18-BP44.10	BP - Excavation	16-Jan-23	21-Jan-23	20	31-Mar-23 A	28-Apr-23 A		[Gantt bars for P18-BP44.10]																
P18-BP44.20	BP - RCD Drilling	25-Jan-23	16-Feb-23	41	29-Apr-23 A	17-Jun-23	-71	[Gantt bars for P18-BP44.20]																
P18-BP44.30	BP - Airlift, Cage Install and Concrete	17-Feb-23	25-Feb-23	8	19-Jun-23	28-Jun-23	-71	[Gantt bars for P18-BP44.30]																
<b>04</b>								[Gantt bars for section 04]																
P18-BP49.10	BP - Excavation	21-Dec-22	29-Dec-22	6	27-May-23	02-Jun-23	-77	[Gantt bars for P18-BP49.10]																
P18-BP49.20	BP - RCD Drilling	30-Dec-22	21-Jan-23	19	03-Jun-23	26-Jun-23	-77	[Gantt bars for P18-BP49.20]																
P18-BP49.30	BP - Airlift, Cage Install and Concrete	25-Jan-23	03-Feb-23	8	27-Jun-23	06-Jul-23	-77	[Gantt bars for P18-BP49.30]																
<b>05</b>								[Gantt bars for section 05]																
P18-BP37.10	BP - Excavation	10-Feb-23	16-Feb-23	6	27-May-23	02-Jun-23	-77	[Gantt bars for P18-BP37.10]																
P18-BP37.20	BP - RCD Drilling	17-Feb-23	10-Mar-23	19	03-Jun-23	26-Jun-23	-77	[Gantt bars for P18-BP37.20]																
P18-BP37.30	BP - Airlift, Cage Install and Concrete	11-Mar-23	20-Mar-23	8	27-Jun-23	06-Jul-23	-77	[Gantt bars for P18-BP37.30]																
<b>07</b>								[Gantt bars for section 07]																
P18-BP50.10	BP - Excavation	04-Mar-23	10-Mar-23	6	27-May-23	02-Jun-23	-77	[Gantt bars for P18-BP50.10]																
P18-BP50.20	BP - RCD Drilling	11-Mar-23	01-Apr-23	19	03-Jun-23	26-Jun-23	-77	[Gantt bars for P18-BP50.20]																
P18-BP50.30	BP - Airlift, Cage Install and Concrete	03-Apr-23	15-Apr-23	8	27-Jun-23	06-Jul-23	-77	[Gantt bars for P18-BP50.30]																
<b>10</b>								[Gantt bars for section 10]																
P18-BP31.10	BP - Excavation	27-Mar-23	01-Apr-23	21	18-Apr-23 A	13-May-23 A		[Gantt bars for P18-BP31.10]																
P18-BP31.20	BP - RCD Drilling	03-Apr-23	28-Apr-23	5	15-May-23 A	20-May-23 A		[Gantt bars for P18-BP31.20]																
P18-BP31.30	BP - Airlift, Cage Install and Concrete	29-Apr-23	09-May-23	12	22-May-23 A	05-Jun-23	-52	[Gantt bars for P18-BP31.30]																
<b>12</b>								[Gantt bars for section 12]																
P23-BP75.10	BP - Excavation	22-Apr-23	28-Apr-23	6	27-May-23	02-Jun-23	-77	[Gantt bars for P23-BP75.10]																
P23-BP75.20	BP - RCD Drilling	29-Apr-23	22-May-23	19	03-Jun-23	26-Jun-23	-77	[Gantt bars for P23-BP75.20]																
P23-BP75.30	BP - Airlift, Cage Install and Concrete	23-May-23	01-Jun-23	8	27-Jun-23	06-Jul-23	-77	[Gantt bars for P23-BP75.30]																
<b>12</b>								[Gantt bars for section 12]																
P23-BP86.10	BP - Excavation	16-May-23	22-May-23	17	13-May-23 A	02-Jun-23	-87	[Gantt bars for P23-BP86.10]																
P23-BP86.20	BP - RCD Drilling	23-May-23	27-Jun-23	19	15-Jun-23 A	08-Jul-23	-87	[Gantt bars for P23-BP86.20]																
P23-BP86.30	BP - Airlift, Cage Install and Concrete	28-Jun-23	07-Jul-23	8	10-Jul-23	18-Jul-23	-87	[Gantt bars for P23-BP86.30]																
<b>TD05</b>								[Gantt bars for section TD05]																
P18-BP54.30	BP - Airlift, Cage Install and Concrete	04-Mar-23	13-Mar-23	8	24-Apr-23 A	04-May-23 A		[Gantt bars for P18-BP54.30]																







	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS

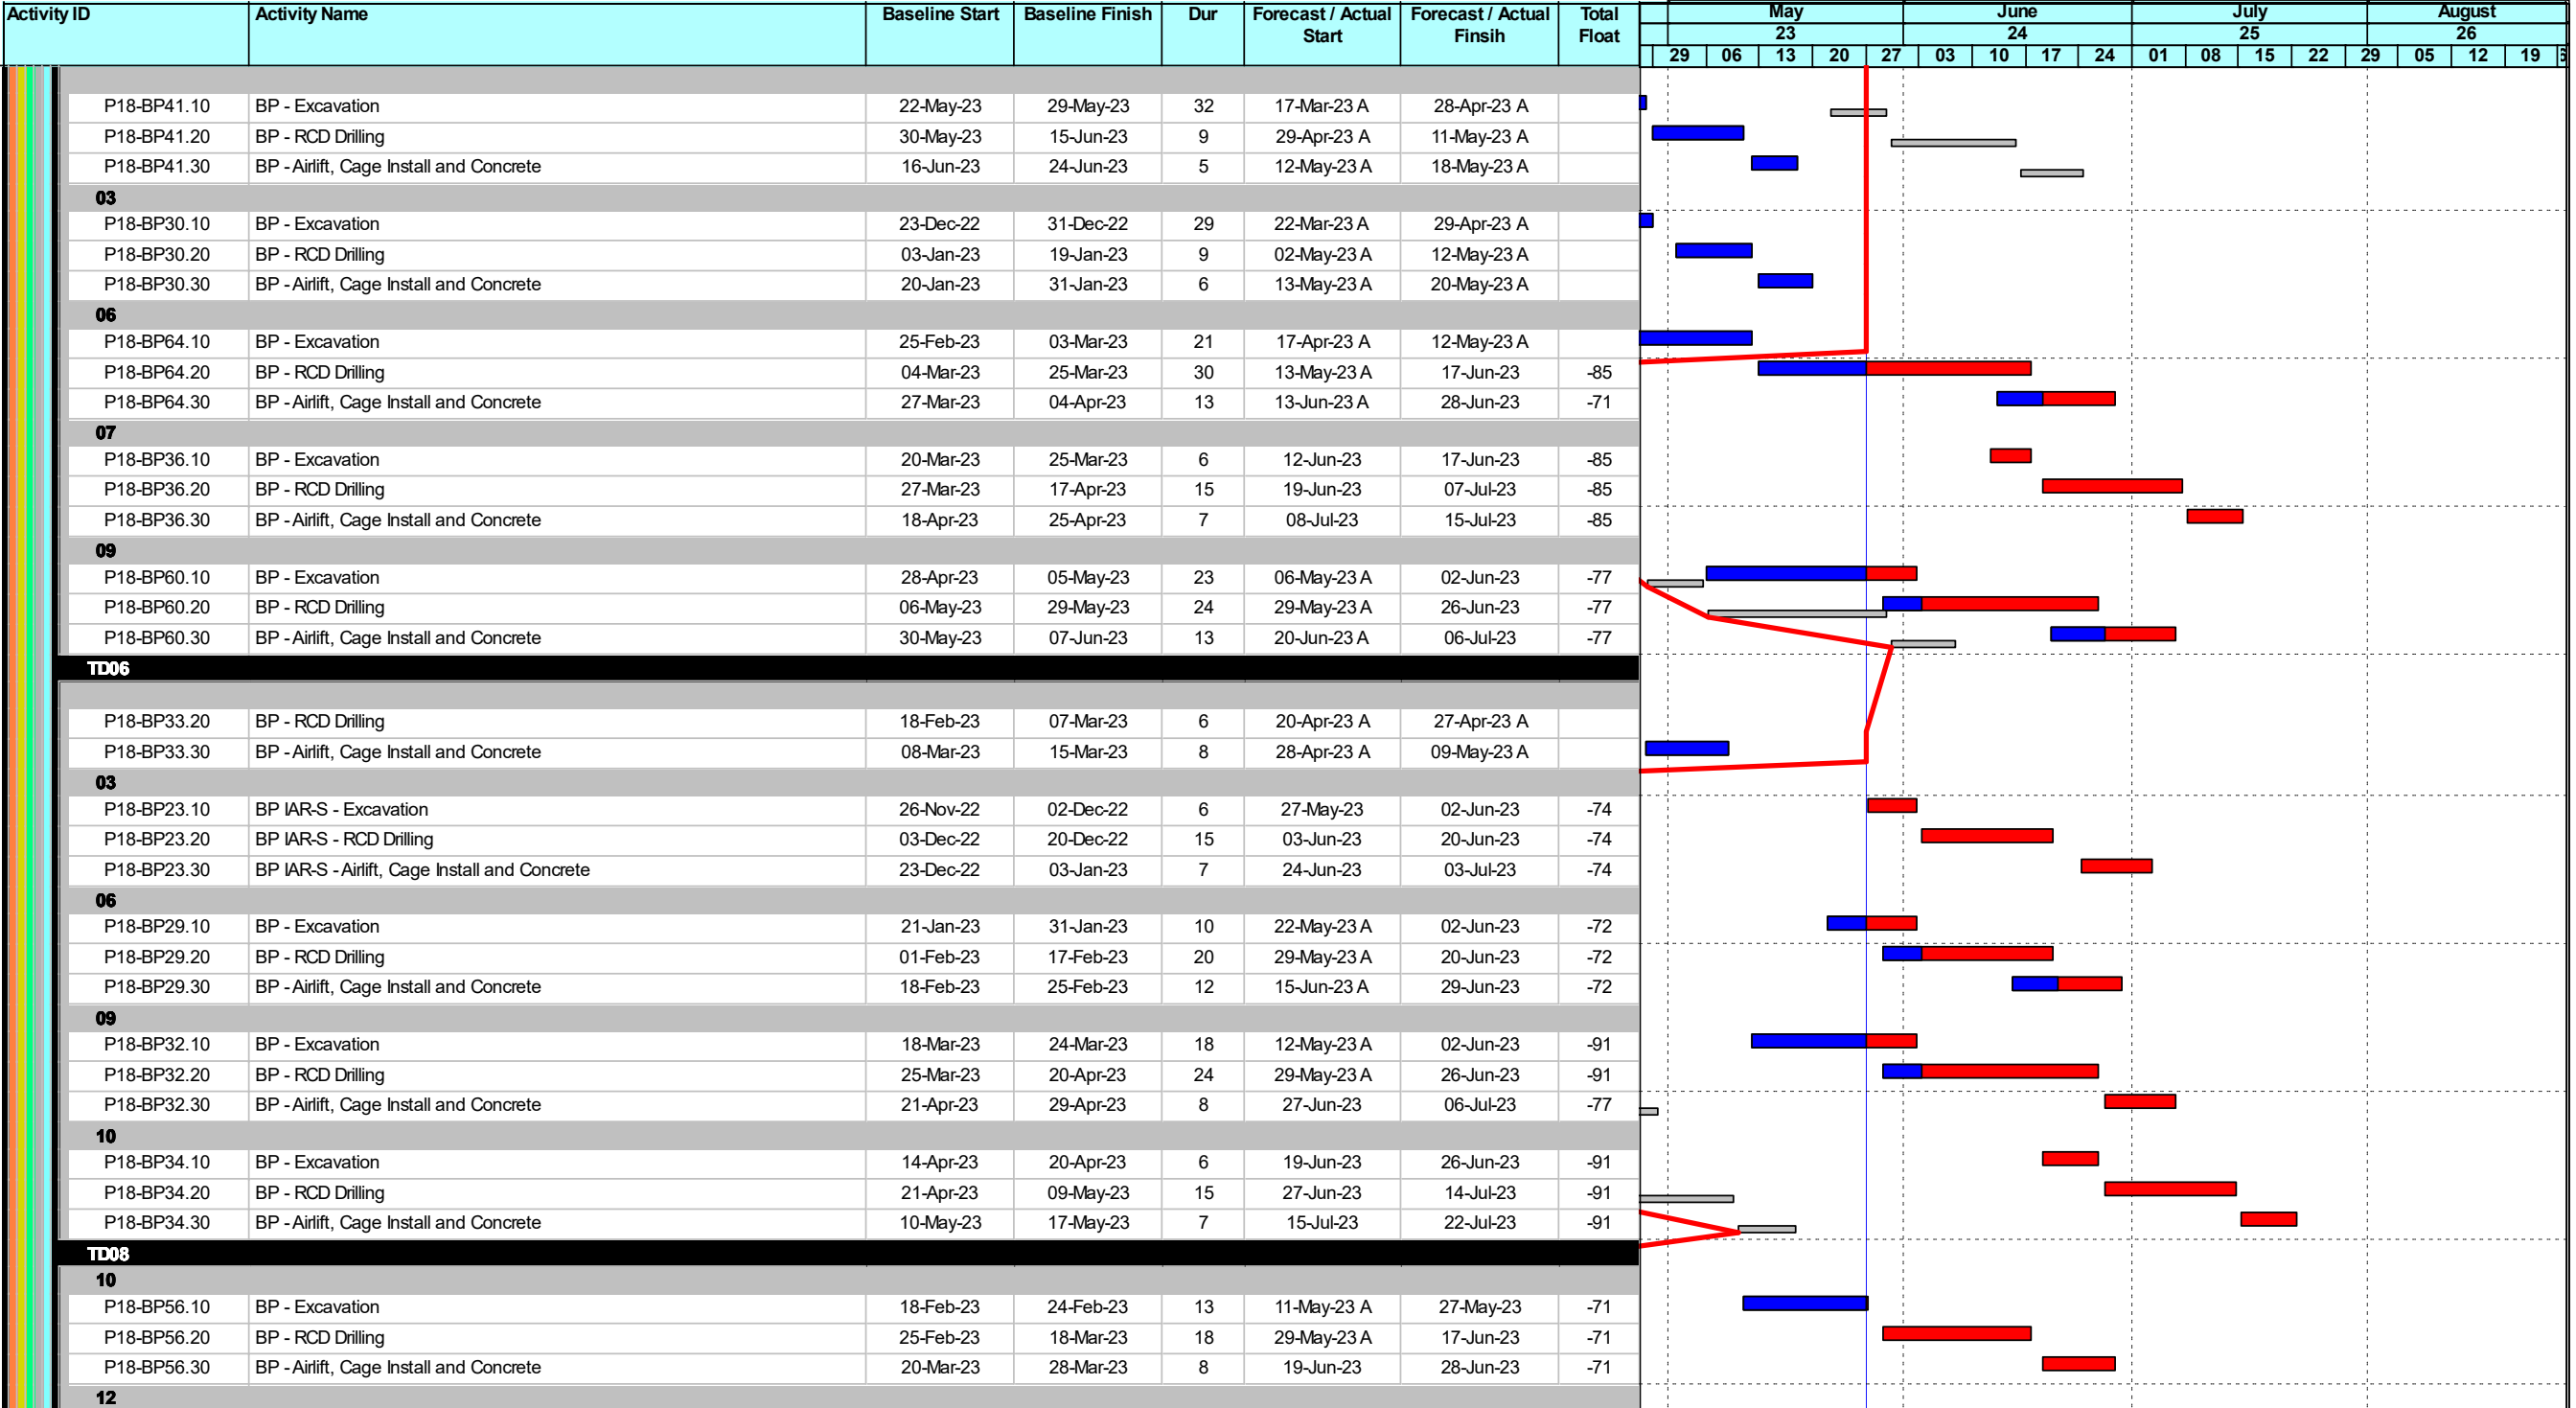**West Kowloon Cultural District Authority**  
**Piling for Integrated Basement and U/G Road in Zone 2B 2C**  
**3 Month Rolling Programme as of 26 May 2023**  
**Based on CMWP Rev.0 (3rd Draft)**

Date	Revision	Checked	Approved
04-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C






	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS

**West Kowloon Cultural District Authority**  
**Piling for Integrated Basement and U/G Road in Zone 2B 2C**  
**3 Month Rolling Programme as of 26 May 2023**  
 Based on CMWP Rev.0 (3rd Draft)



Date	Revision	Checked	Approved
04-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C

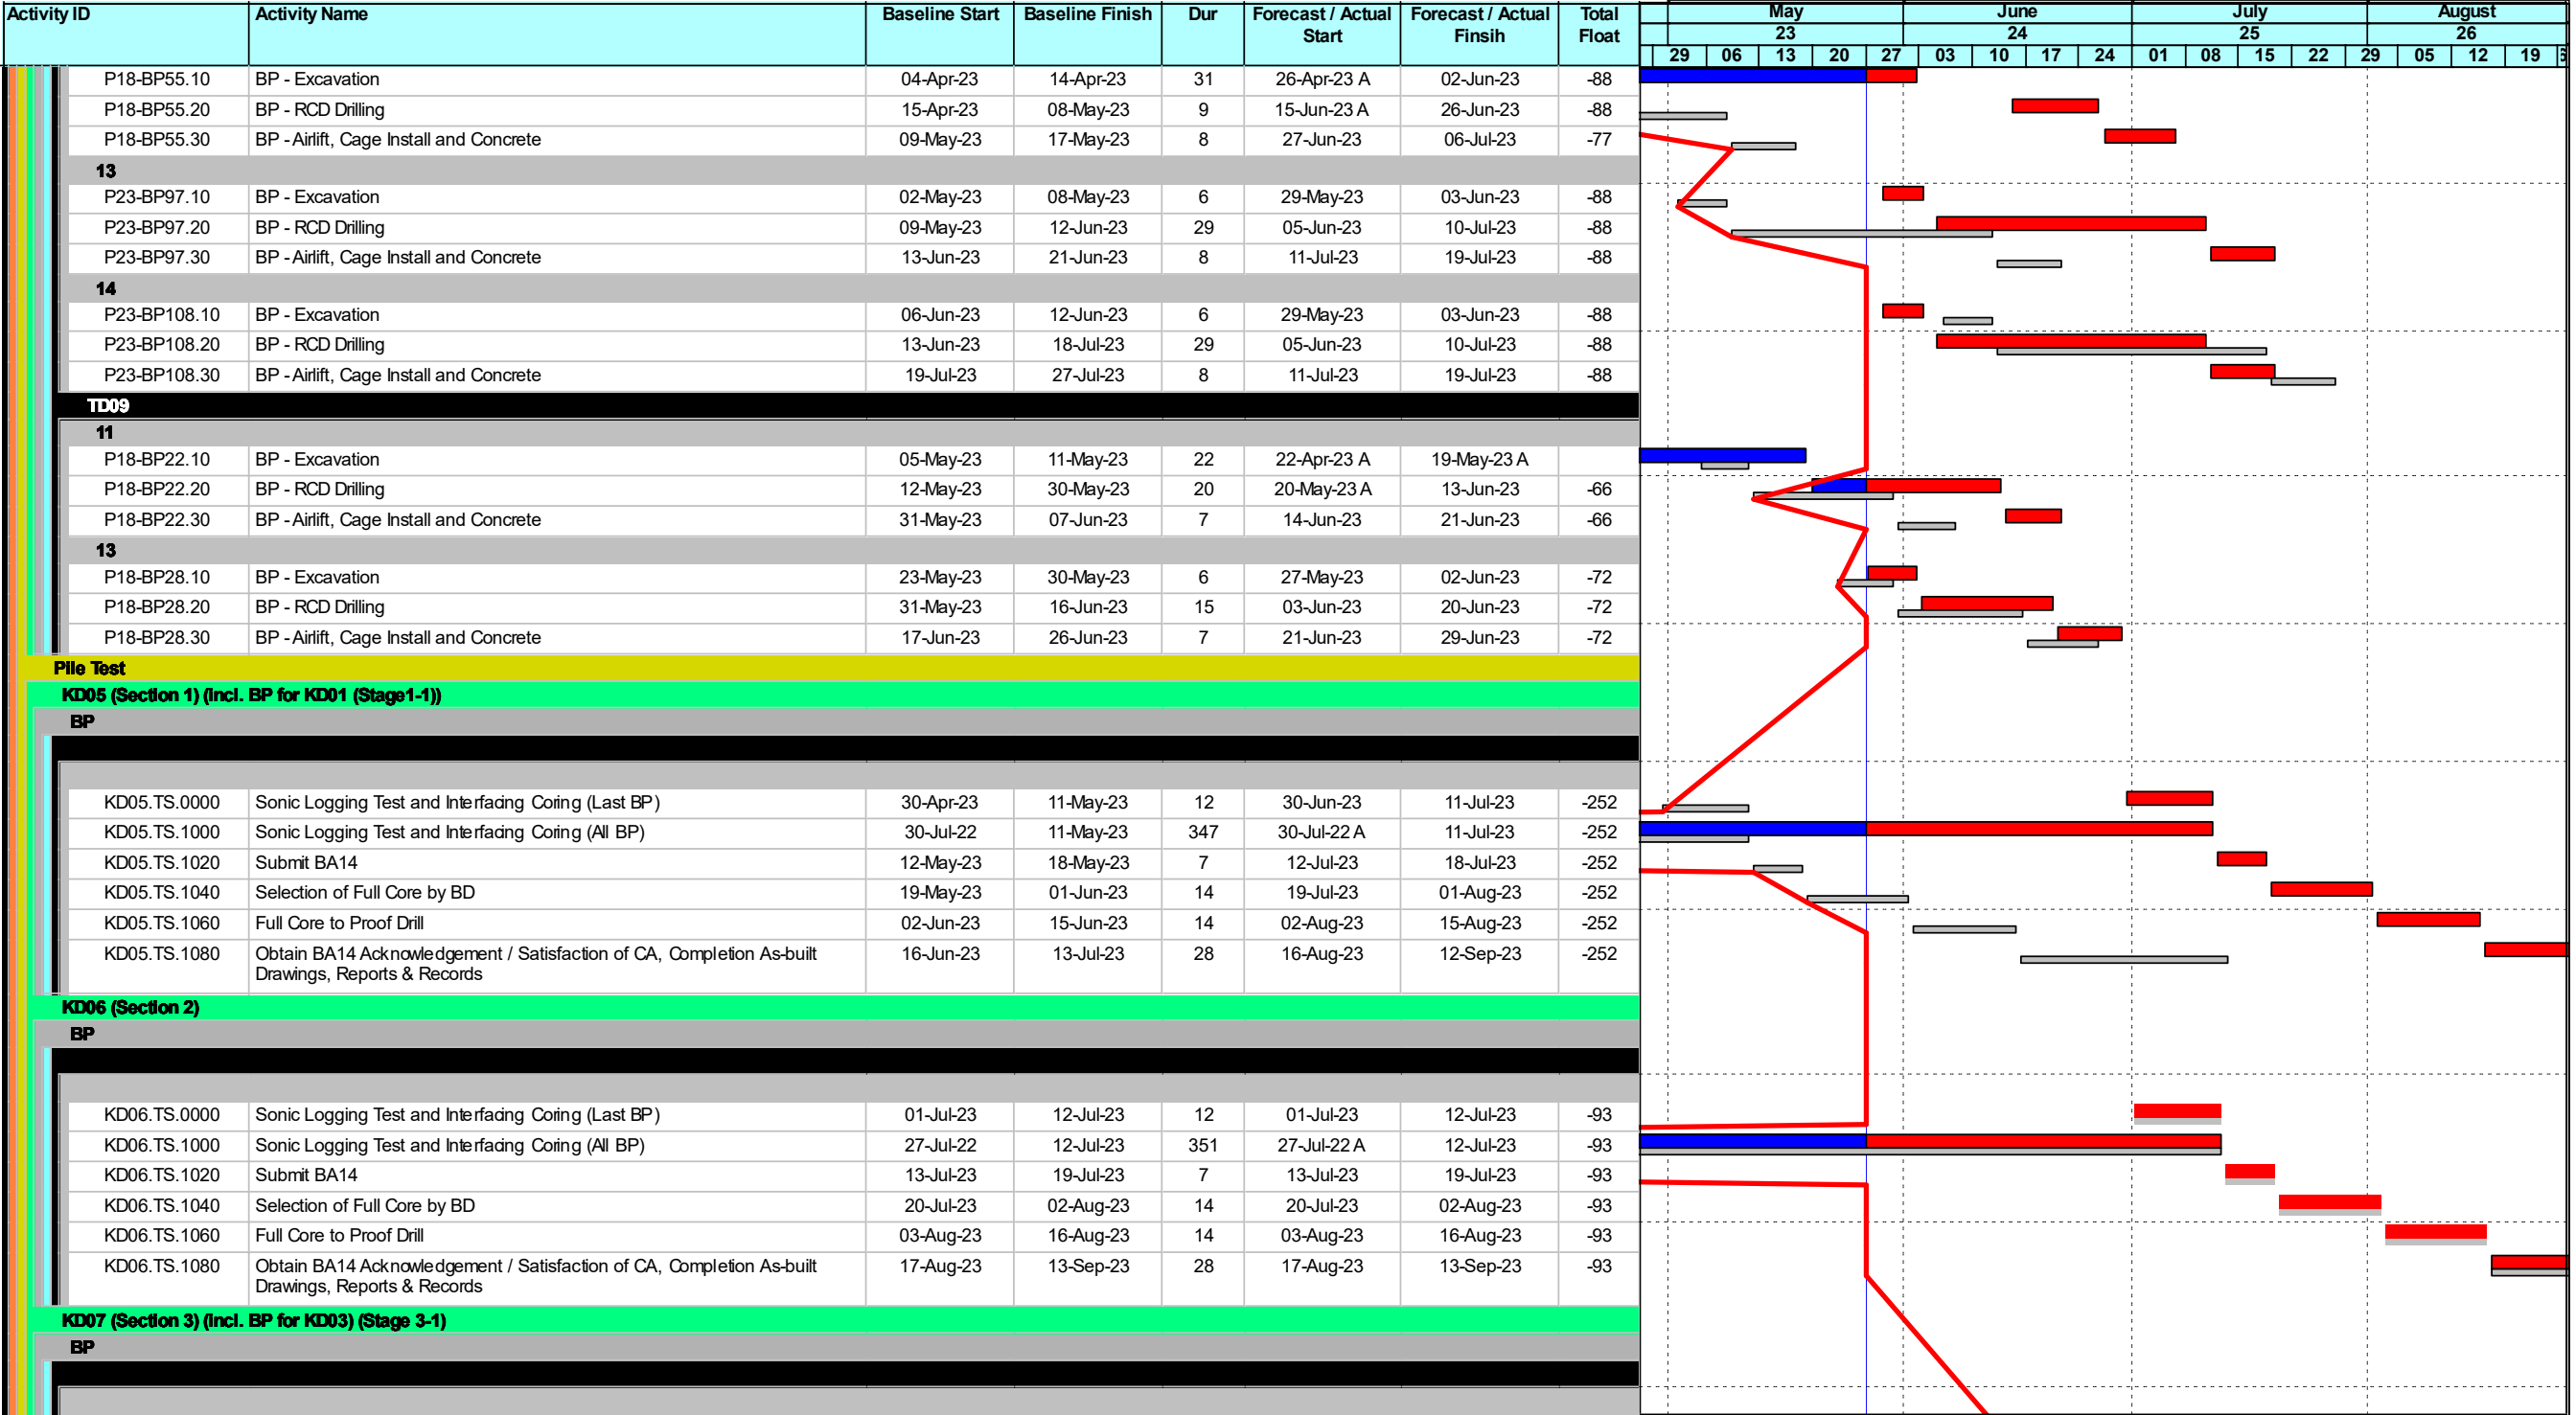

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	May 23				June 24				July 25				August 26				
								29	06	13	20	27	03	10	17	24	01	08	15	22	29	05	12	19
KD07.TS.1000	Sonic Logging Test and Interfacing Coring (All BP)	14-Jun-23	11-Oct-23	306	10-Dec-22 A	11-Oct-23	-74																	
<b>KD08 (Section 4) (Incl. BP for KD04 (Stage 4-1) &amp; SSHP in KD09 (Section 5))</b>																								
<b>BP</b>																								
KD08.TS.0000	Sonic Logging Test and Interfacing Coring (Last BP)	31-May-23	11-Jun-23	12	16-Jun-23	27-Jun-23	-98																	
KD08.TS.1000	Sonic Logging Test and Interfacing Coring (All BP)	04-Jul-22	11-Jun-23	359	04-Jul-22 A	27-Jun-23	-98																	
KD08.TS.1020	Submit BA14	12-Jun-23	18-Jun-23	7	28-Jun-23	04-Jul-23	-98																	
KD08.TS.1040	Selection of Full Core by BD	19-Jun-23	02-Jul-23	14	05-Jul-23	18-Jul-23	-98																	
KD08.TS.1060	Full Core to Proof Drill	03-Jul-23	16-Jul-23	14	19-Jul-23	01-Aug-23	-98																	
KD08.TS.1080	Obtain BA14 Acknowledgement / Satisfaction of CA, Completion As-built Drawings, Reports & Records	17-Jul-23	13-Aug-23	28	02-Aug-23	29-Aug-23	-98																	
<b>SSHP</b>																								
KD08.TS.1120	Submit BA14	15-Nov-22	21-Nov-22	7	27-May-23	02-Jun-23	-67																	
KD08.TS.1140	Selection of Pile for Static Load Test	22-Nov-22	05-Dec-22	14	03-Jun-23	16-Jun-23	-67																	
KD08.TS.1160	Static Load Test of Selected Pile	06-Dec-22	19-Dec-22	14	17-Jun-23	30-Jun-23	-67																	
KD08.TS.1180	Obtain BA14 Acknowledgement / Satisfaction of CA, Completion As-built Drawings, Reports & Records	20-Dec-22	16-Jan-23	28	01-Jul-23	28-Jul-23	-67																	
<b>KD09 (Section 5) (Incl. BP for KD02 (Stage 5-1))</b>																								
<b>BP</b>																								
KD09.TS.0000	Sonic Logging Test and Interfacing Coring (Last BP)	01-Aug-23	12-Aug-23	12	01-Aug-23	12-Aug-23	-124																	
KD09.TS.1000	Sonic Logging Test and Interfacing Coring (All BP)	23-May-22	12-Aug-23	447	23-May-22 A	12-Aug-23	-124																	
KD09.TS.1020	Submit BA14	13-Aug-23	19-Aug-23	7	13-Aug-23	19-Aug-23	-124																	
KD09.TS.1040	Selection of Full Core by BD	20-Aug-23	02-Sep-23	14	20-Aug-23	02-Sep-23	-124																	
<b>Attendance to Other Project Contractors (optional works item no. 2A to 2E)</b>																								
S2.AT.0000	Attendance at Section 2 Area (optional works item no. 2B) (Duration TBC)	13-May-23	01-Jun-23	20	27-May-23	15-Jun-23	-3																	
S3.AT.0000	Attendance at Section 3 Area (optional works item no. 2C) (Duration TBC)	02-Jul-23	21-Jul-23	20	02-Jul-23	21-Jul-23	71																	

	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS

**West Kowloon Cultural District Authority**  
**Piling for Integrated Basement and U/G Road in Zone 2B 2C**  
**3 Month Rolling Programme as of 26 May 2023**  
**Based on CMWP Rev.0 (3rd Draft)**



Date	Revision	Checked	Approved
04-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C
