

Zone 2B & 2C

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	June				July				August				September			
								24				25				26				27			
								03	10	17	24	01	08	15	22	29	05	12	19	26	02	09	16

Piling for Integrated Basement and U/G Road in Zone 2B & 2C

Contract Dates

Key Dates

KD for Zone 2B

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float
KD05	KD05 (Section 1) - 03 Jan 2023		13-Jul-23	0		25-Sep-23*	-265
KD06	KD06 (Section 2) - 12 Jun 2023		13-Sep-23	0		09-Sep-23*	-89

KD for Zone 2C

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float
KD08	KD08 (Section 4) - 23 May 2023		13-Aug-23	0		10-Sep-23*	-110

Optional Works subjected to CA's Instruction

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float
CO2C	Last CAI date for Optional Works Item No.2C (330 Days to 710 Days after Commencement)	02-Jul-23		0	02-Jul-23		71

Construction Stage

Pile Construction

KD05 (Section 1)

Bored Piles - Drainage Diversion

CD08

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float
01							
P17-BP20.10	BP - Excavation	17-Feb-23	23-Feb-23	16	27-May-23 A	15-Jun-23 A	
P17-BP20.20	BP - RCD Drilling	24-Feb-23	13-Mar-23	9	16-Jun-23 A	28-Jun-23 A	
P17-BP20.30	BP - Airlift, Cage Install and Concrete	14-Mar-23	21-Mar-23	9	29-Jun-23 A	10-Jul-23	-211
03							
P17-BP18.10	BP IAR-N - Excavation	24-Mar-23	30-Mar-23	13	20-May-23 A	06-Jun-23 A	
P17-BP18.20	BP IAR-N - RCD Drilling	31-Mar-23	21-Apr-23	6	07-Jun-23 A	14-Jun-23 A	
P17-BP18.30	BP IAR-N - Airlift, Cage Install and Concrete	22-Apr-23	29-Apr-23	22	15-Jun-23 A	12-Jul-23	-213

Bored Piles - Gantry Gate A


CD07

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float
02							
P22&P19-BP26.:	BP - RCD Drilling	16-Jul-22	03-Dec-22	284	16-Jul-22 A	03-Jul-23	-212
P22&P19-BP26.:	BP - Airlift, Cage Install and Concrete	05-Dec-22	13-Dec-22	8	03-Jul-23	11-Jul-23	-212

Bored Piles

TD07

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float
04							
P18-BP01.30	BP - Airlift, Cage Install and Concrete	17-Jan-23	27-Jan-23	7	23-May-23 A	01-Jun-23 A	
09							
P18-BP07.20	BP IAR-S - RCD Drilling	18-Mar-23	04-Apr-23	10	31-May-23 A	12-Jun-23 A	
P18-BP07.30	BP IAR-S - Airlift, Cage Install and Concrete	06-Apr-23	17-Apr-23	5	24-Jun-23 A	30-Jun-23 A	

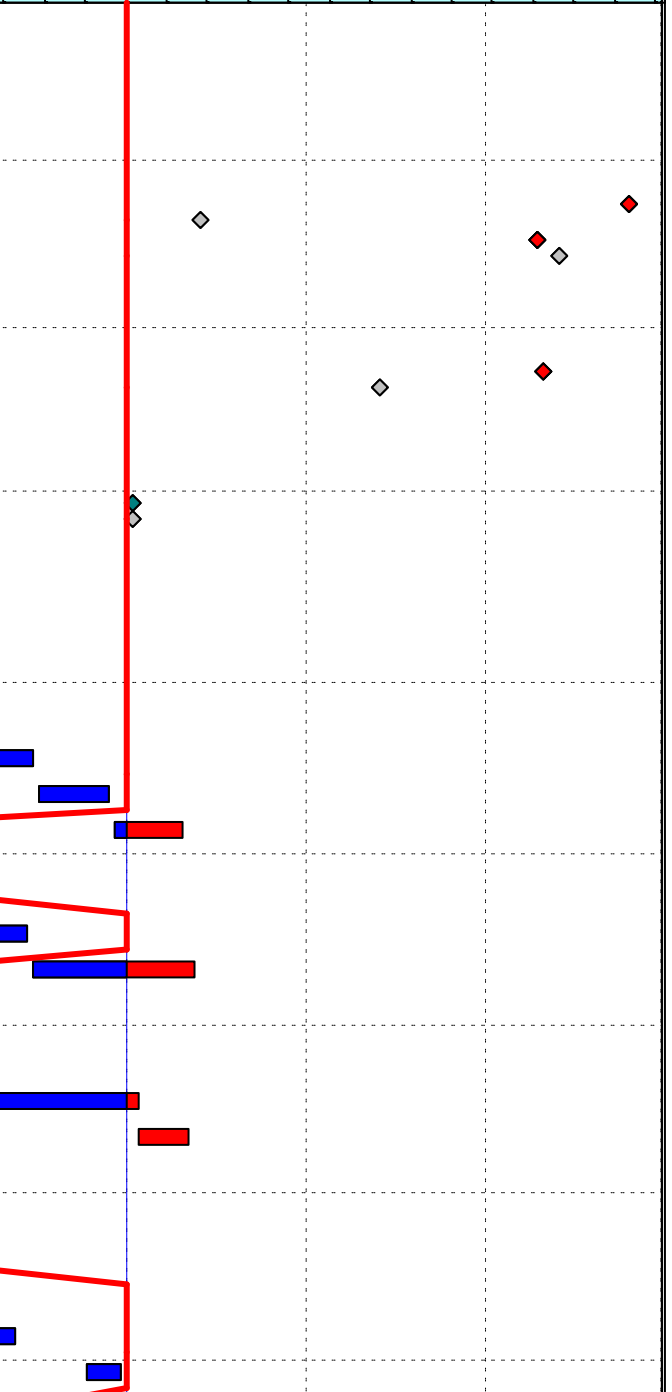

	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS

Date	Revision	Checked	Approved
04-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	June				July				August				September			
								24				25				26				27			
								03	10	17	24	01	08	15	22	29	05	12	19	26	02	09	16


TD09							
CBA-BPC36Ka.1	BP IAR-N - Excavation	31-Mar-23	11-Apr-23	104	22-Feb-23 A	03-Jul-23	-209
CBA-BPC36Ka.2	BP IAR-N - RCD Drilling	12-Apr-23	22-Apr-23	37	20-May-23 A	05-Jul-23	-209
CBA-BPC36Ka.3	BP IAR-N - Airlift, Cage Install and Concrete	24-Apr-23	28-Apr-23	29	02-Jun-23 A	07-Jul-23	-209

KD06 (Section 2)

Bored Piles							
VD14							
09							
P24&P27-BP36.:	BP - Airlift, Cage Install and Concrete	03-Jun-23	12-Jun-23	10	30-May-23 A	10-Jun-23 A	
VD15							
07							
P24&P27-BP10.:	BP - Airlift, Cage Install and Concrete	06-May-23	15-May-23	12	24-May-23 A	08-Jun-23 A	
CD01							
08							
P23-BP15.30	BP - Airlift, Cage Install and Concrete	21-Jun-23	30-Jun-23	19	22-May-23 A	14-Jun-23 A	
CD03							
02							
P22&P19-BP13.:	BP - RCD Drilling	28-Sep-22	11-Nov-22	200	28-Sep-22 A	05-Jun-23 A	
P22&P19-BP13.:	BP - Airlift, Cage Install and Concrete	12-Nov-22	21-Nov-22	16	06-Jun-23 A	26-Jun-23 A	


KD07 (Section 3)

Bored Piles							
VD01							
07							
P26-BP07.10	BP - Excavation	28-Apr-23	05-May-23	6	03-Jul-23	08-Jul-23	-30
P26-BP07.20	BP - RCD Drilling	06-May-23	09-Jun-23	29	10-Jul-23	11-Aug-23	-30
P26-BP07.30	BP - Airlift, Cage Install and Concrete	10-Jun-23	19-Jun-23	8	12-Aug-23	21-Aug-23	-30
08							
P26-BP05.10	BP - Excavation	03-Jun-23	09-Jun-23	6	03-Jul-23	08-Jul-23	-30
P26-BP05.20	BP - RCD Drilling	10-Jun-23	15-Jul-23	29	10-Jul-23	11-Aug-23	-30
P26-BP05.30	BP - Airlift, Cage Install and Concrete	17-Jul-23	25-Jul-23	8	12-Aug-23	21-Aug-23	-30
VD02							
02							
P30-BP71.30	BP - Airlift, Cage Install and Concrete	25-Feb-23	07-Mar-23	19	10-May-23 A	02-Jun-23 A	
04							
P30-BP75.10	BP - Excavation	24-Mar-23	30-Mar-23	17	17-Jun-23 A	08-Jul-23	-30
P30-BP75.20	BP - RCD Drilling	31-Mar-23	09-May-23	29	10-Jul-23	11-Aug-23	-30
P30-BP75.30	BP - Airlift, Cage Install and Concrete	10-May-23	18-May-23	8	12-Aug-23	21-Aug-23	-30
05							
P30-BP74.10	BP - Excavation	23-Jun-22	09-May-23	294	23-Jun-22 A	20-Jun-23 A	
P30-BP74.20	BP - RCD Drilling	10-May-23	01-Jun-23	33	21-Jun-23 A	31-Jul-23	-30
P30-BP74.30	BP - Airlift, Cage Install and Concrete	02-Jun-23	10-Jun-23	8	01-Aug-23	09-Aug-23	-20

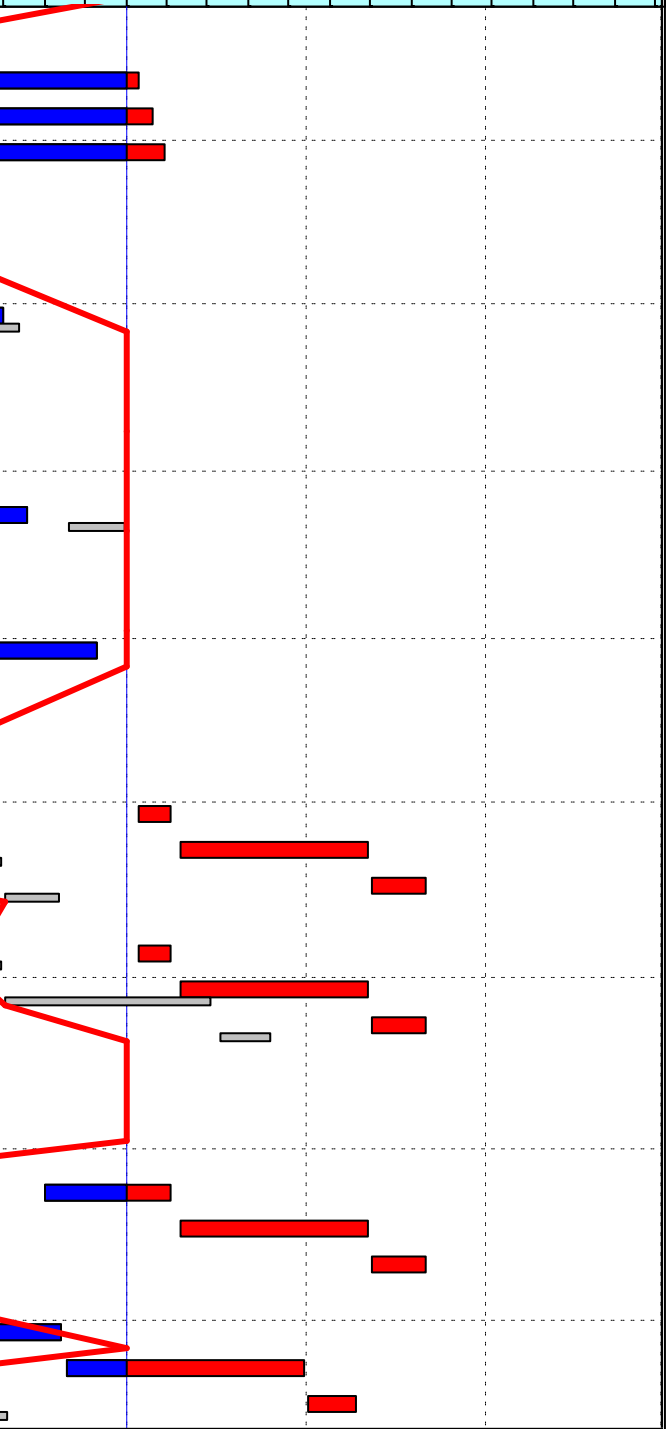

	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS

Date	Revision	Checked	Approved
04-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C

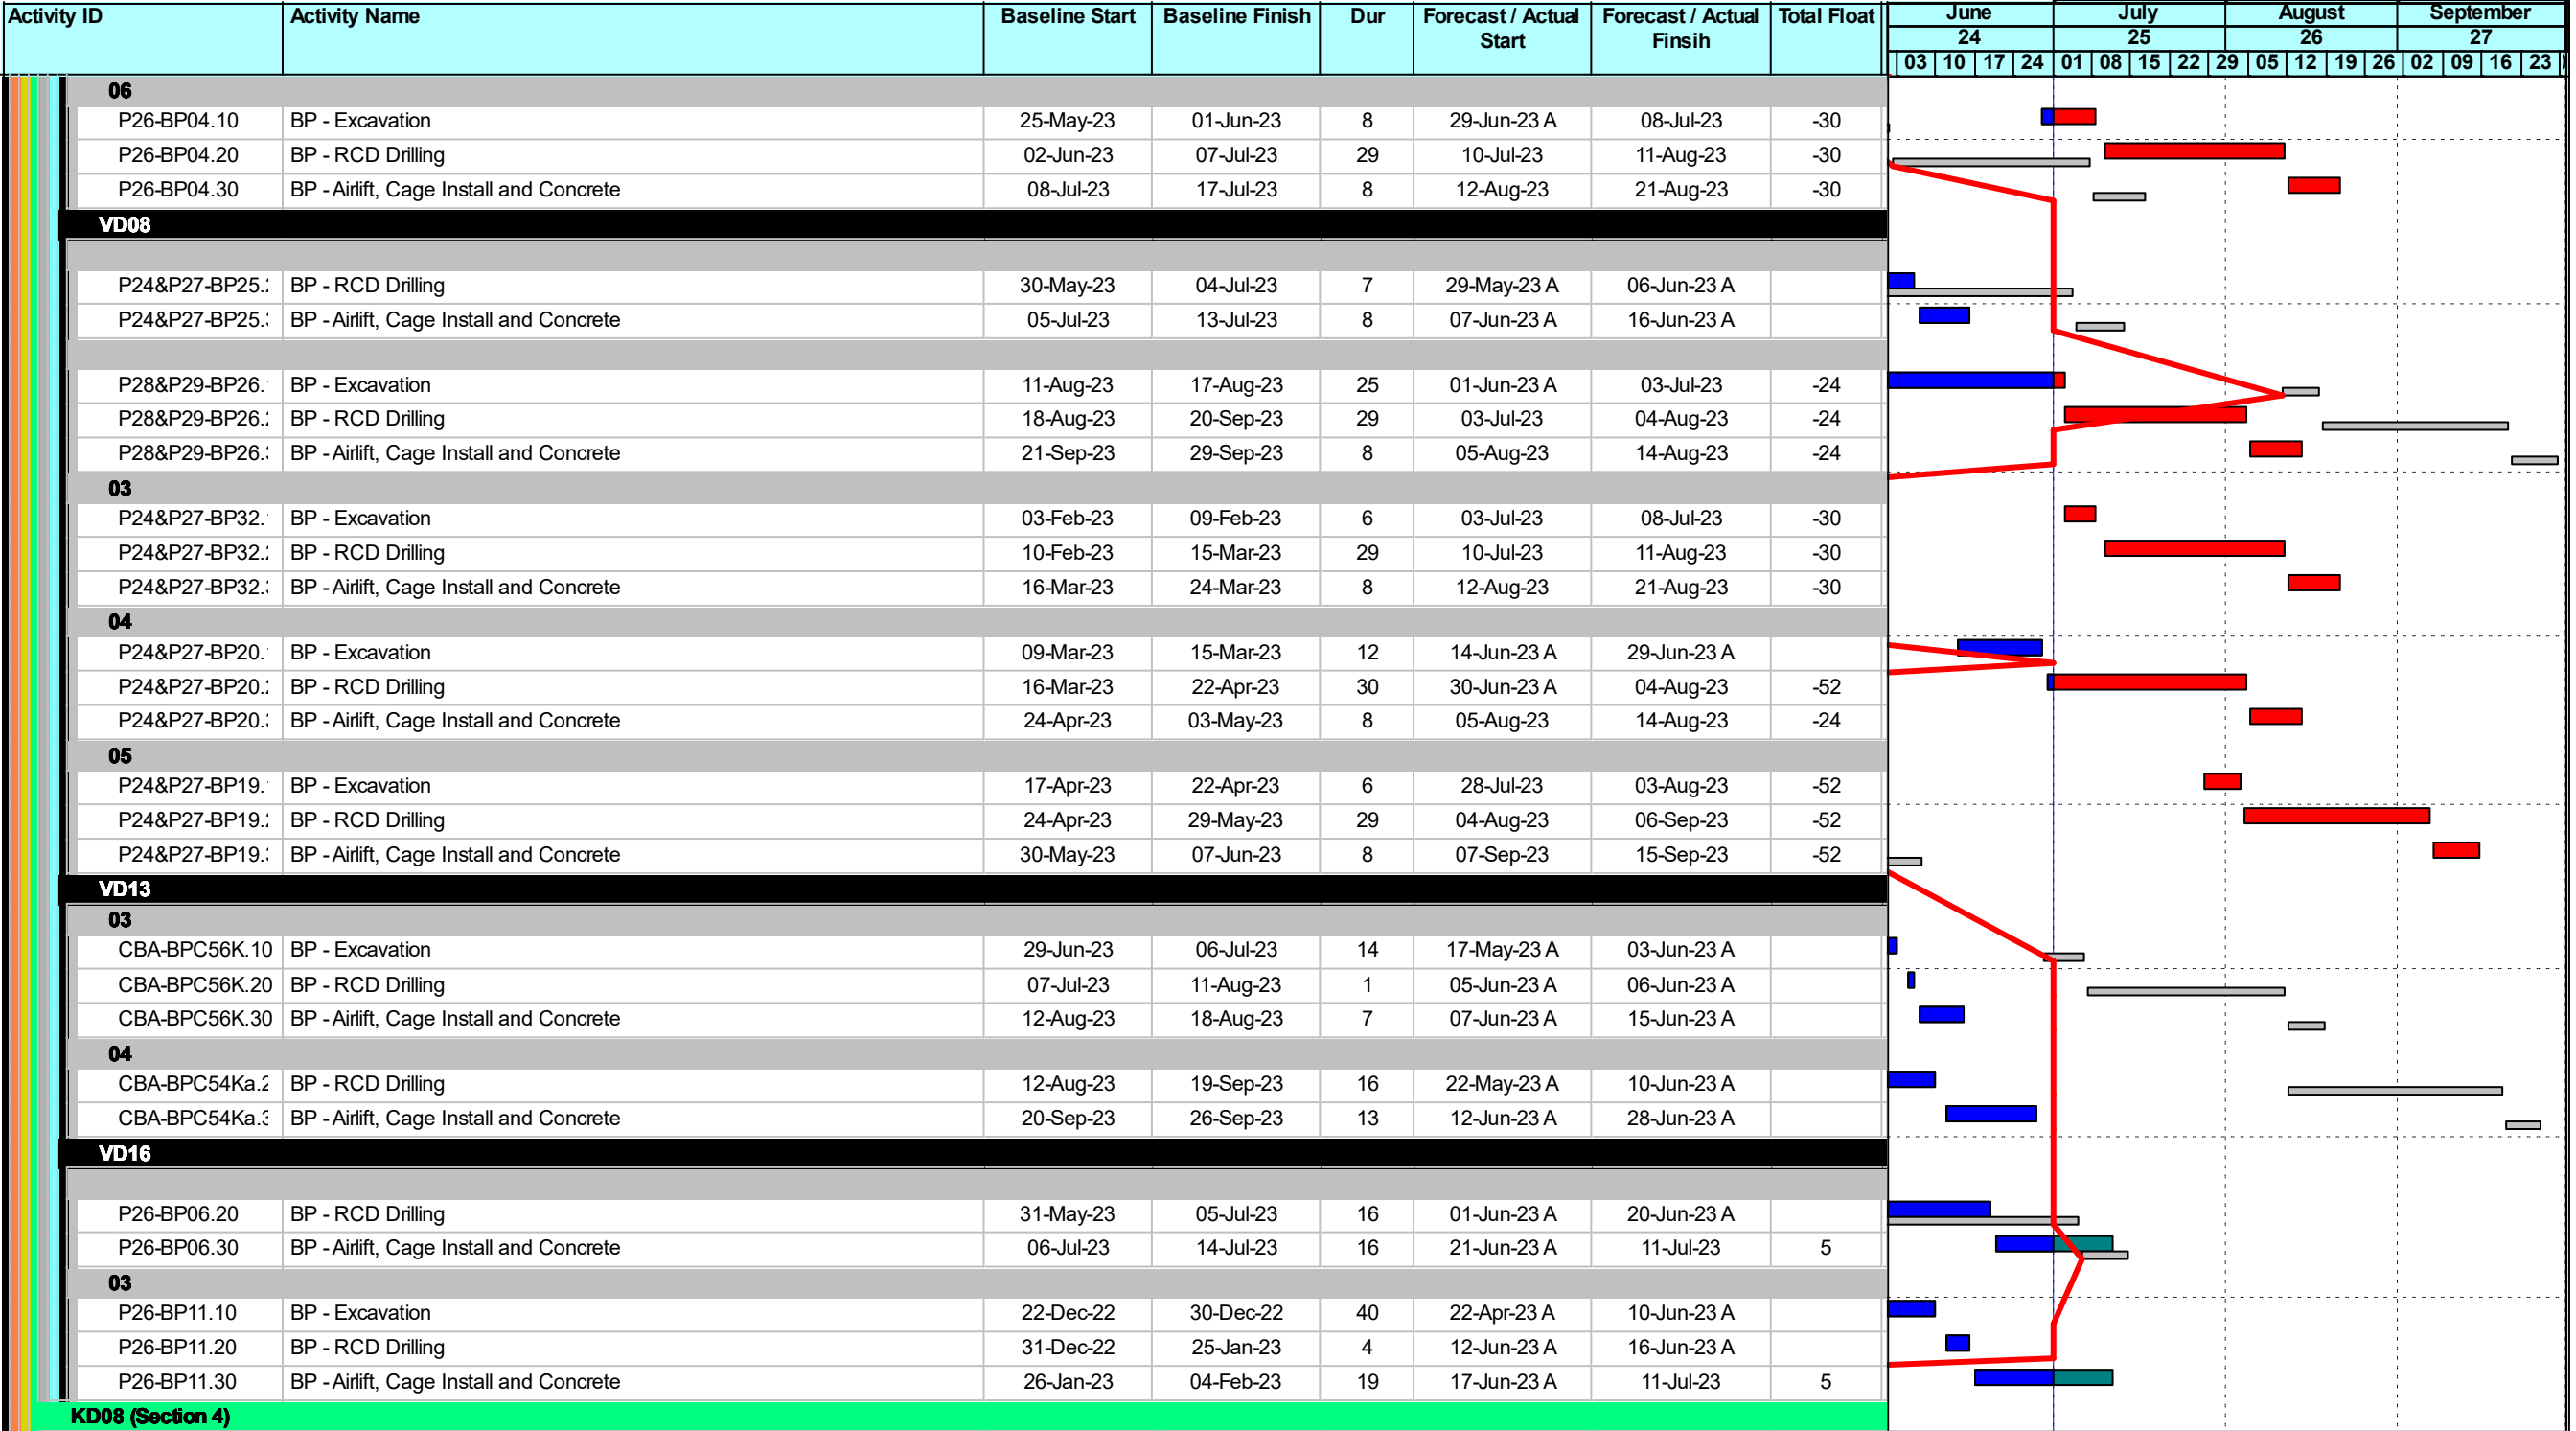

KD08 (Section 4)

	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS

Date	Revision	Checked	Approved
04-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	June				July				August				September			
								24				25				26				27			
								03	10	17	24	01	08	15	22	29	05	12	19	26	02	09	16

Bored Piles

VD03

04

P30-BP46.10	BP - Excavation	13-Jan-23	19-Jan-23	22	05-May-23 A	01-Jun-23 A	
P30-BP46.20	BP - RCD Drilling	20-Jan-23	09-Feb-23	7	02-Jun-23 A	10-Jun-23 A	
P30-BP46.30	BP - Airlift, Cage Install and Concrete	10-Feb-23	17-Feb-23	6	12-Jun-23 A	19-Jun-23 A	

05

P30-BP47.10	BP - Excavation	03-Feb-23	09-Feb-23	19	13-May-23 A	06-Jun-23 A	
P30-BP47.20	BP - RCD Drilling	10-Feb-23	27-Feb-23	4	07-Jun-23 A	12-Jun-23 A	
P30-BP47.30	BP - Airlift, Cage Install and Concrete	28-Feb-23	07-Mar-23	7	13-Jun-23 A	21-Jun-23 A	

08

P30-BP49.10	BP - Excavation	28-Mar-23	03-Apr-23	11	27-May-23 A	09-Jun-23 A	
P30-BP49.20	BP - RCD Drilling	04-Apr-23	29-Apr-23	5	10-Jun-23 A	16-Jun-23 A	
P30-BP49.30	BP - Airlift, Cage Install and Concrete	02-May-23	10-May-23	7	17-Jun-23 A	27-Jun-23 A	

VD04

07

P30-BP35.30	BP - Airlift, Cage Install and Concrete	15-Apr-23	22-Apr-23	9	25-May-23 A	06-Jun-23 A	
-------------	---	-----------	-----------	---	-------------	-------------	--

VD05

P30-BP50.30	BP - Airlift, Cage Install and Concrete	08-May-23	16-May-23	12	30-May-23 A	13-Jun-23 A	
-------------	---	-----------	-----------	----	-------------	-------------	--

05

P30-BP43.10	BP - Excavation	12-Jan-23	18-Jan-23	18	18-May-23 A	09-Jun-23 A	
P30-BP43.20	BP - RCD Drilling	19-Jan-23	13-Feb-23	4	10-Jun-23 A	15-Jun-23 A	
P30-BP43.30	BP - Airlift, Cage Install and Concrete	14-Feb-23	22-Feb-23	6	16-Jun-23 A	24-Jun-23 A	

KD09 (Section 5)

Bored Piles

CD01

03

P23-BP35.30	BP - Airlift, Cage Install and Concrete	31-Jan-23	08-Feb-23	12	25-May-23 A	09-Jun-23 A	
-------------	---	-----------	-----------	----	-------------	-------------	--

CD02

09

P23-BP36.10	BP - Excavation	04-Apr-23	14-Apr-23	21	12-May-23 A	07-Jun-23 A	
P23-BP36.20	BP - RCD Drilling	15-Apr-23	19-May-23	7	08-Jun-23 A	16-Jun-23 A	
P23-BP36.30	BP - Airlift, Cage Install and Concrete	20-May-23	30-May-23	19	17-Jun-23 A	11-Jul-23	-81


TD01

02

P18-BP57.10	BP - Excavation	22-Dec-22	30-Dec-22	6	03-Jul-23	08-Jul-23	-106
P18-BP57.20	BP - RCD Drilling	31-Dec-22	25-Jan-23	19	10-Jul-23	31-Jul-23	-106
P18-BP57.30	BP - Airlift, Cage Install and Concrete	26-Jan-23	04-Feb-23	8	01-Aug-23	09-Aug-23	-106

04


P18-BP62.10	BP - Excavation	11-Feb-23	17-Feb-23	6	03-Jul-23	08-Jul-23	-116
-------------	-----------------	-----------	-----------	---	-----------	-----------	------

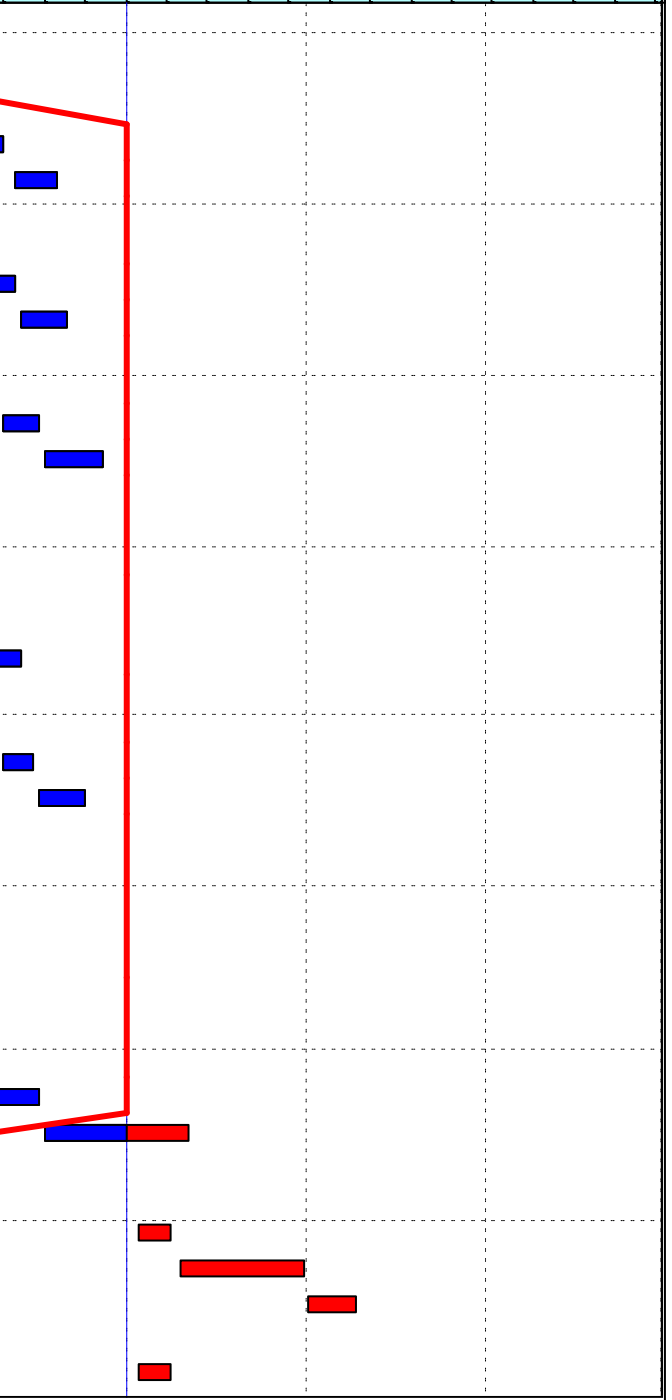

Planned	Planned MS
Critical	Critical MS
Actual	Actual MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 30 June 2023
 Based on CMWP Rev.0 (3rd Draft)

		Date	Revision	Checked	Approved
		04-Mar-22	R0	KL	B
		02-Dec-22	R03D	KL	C

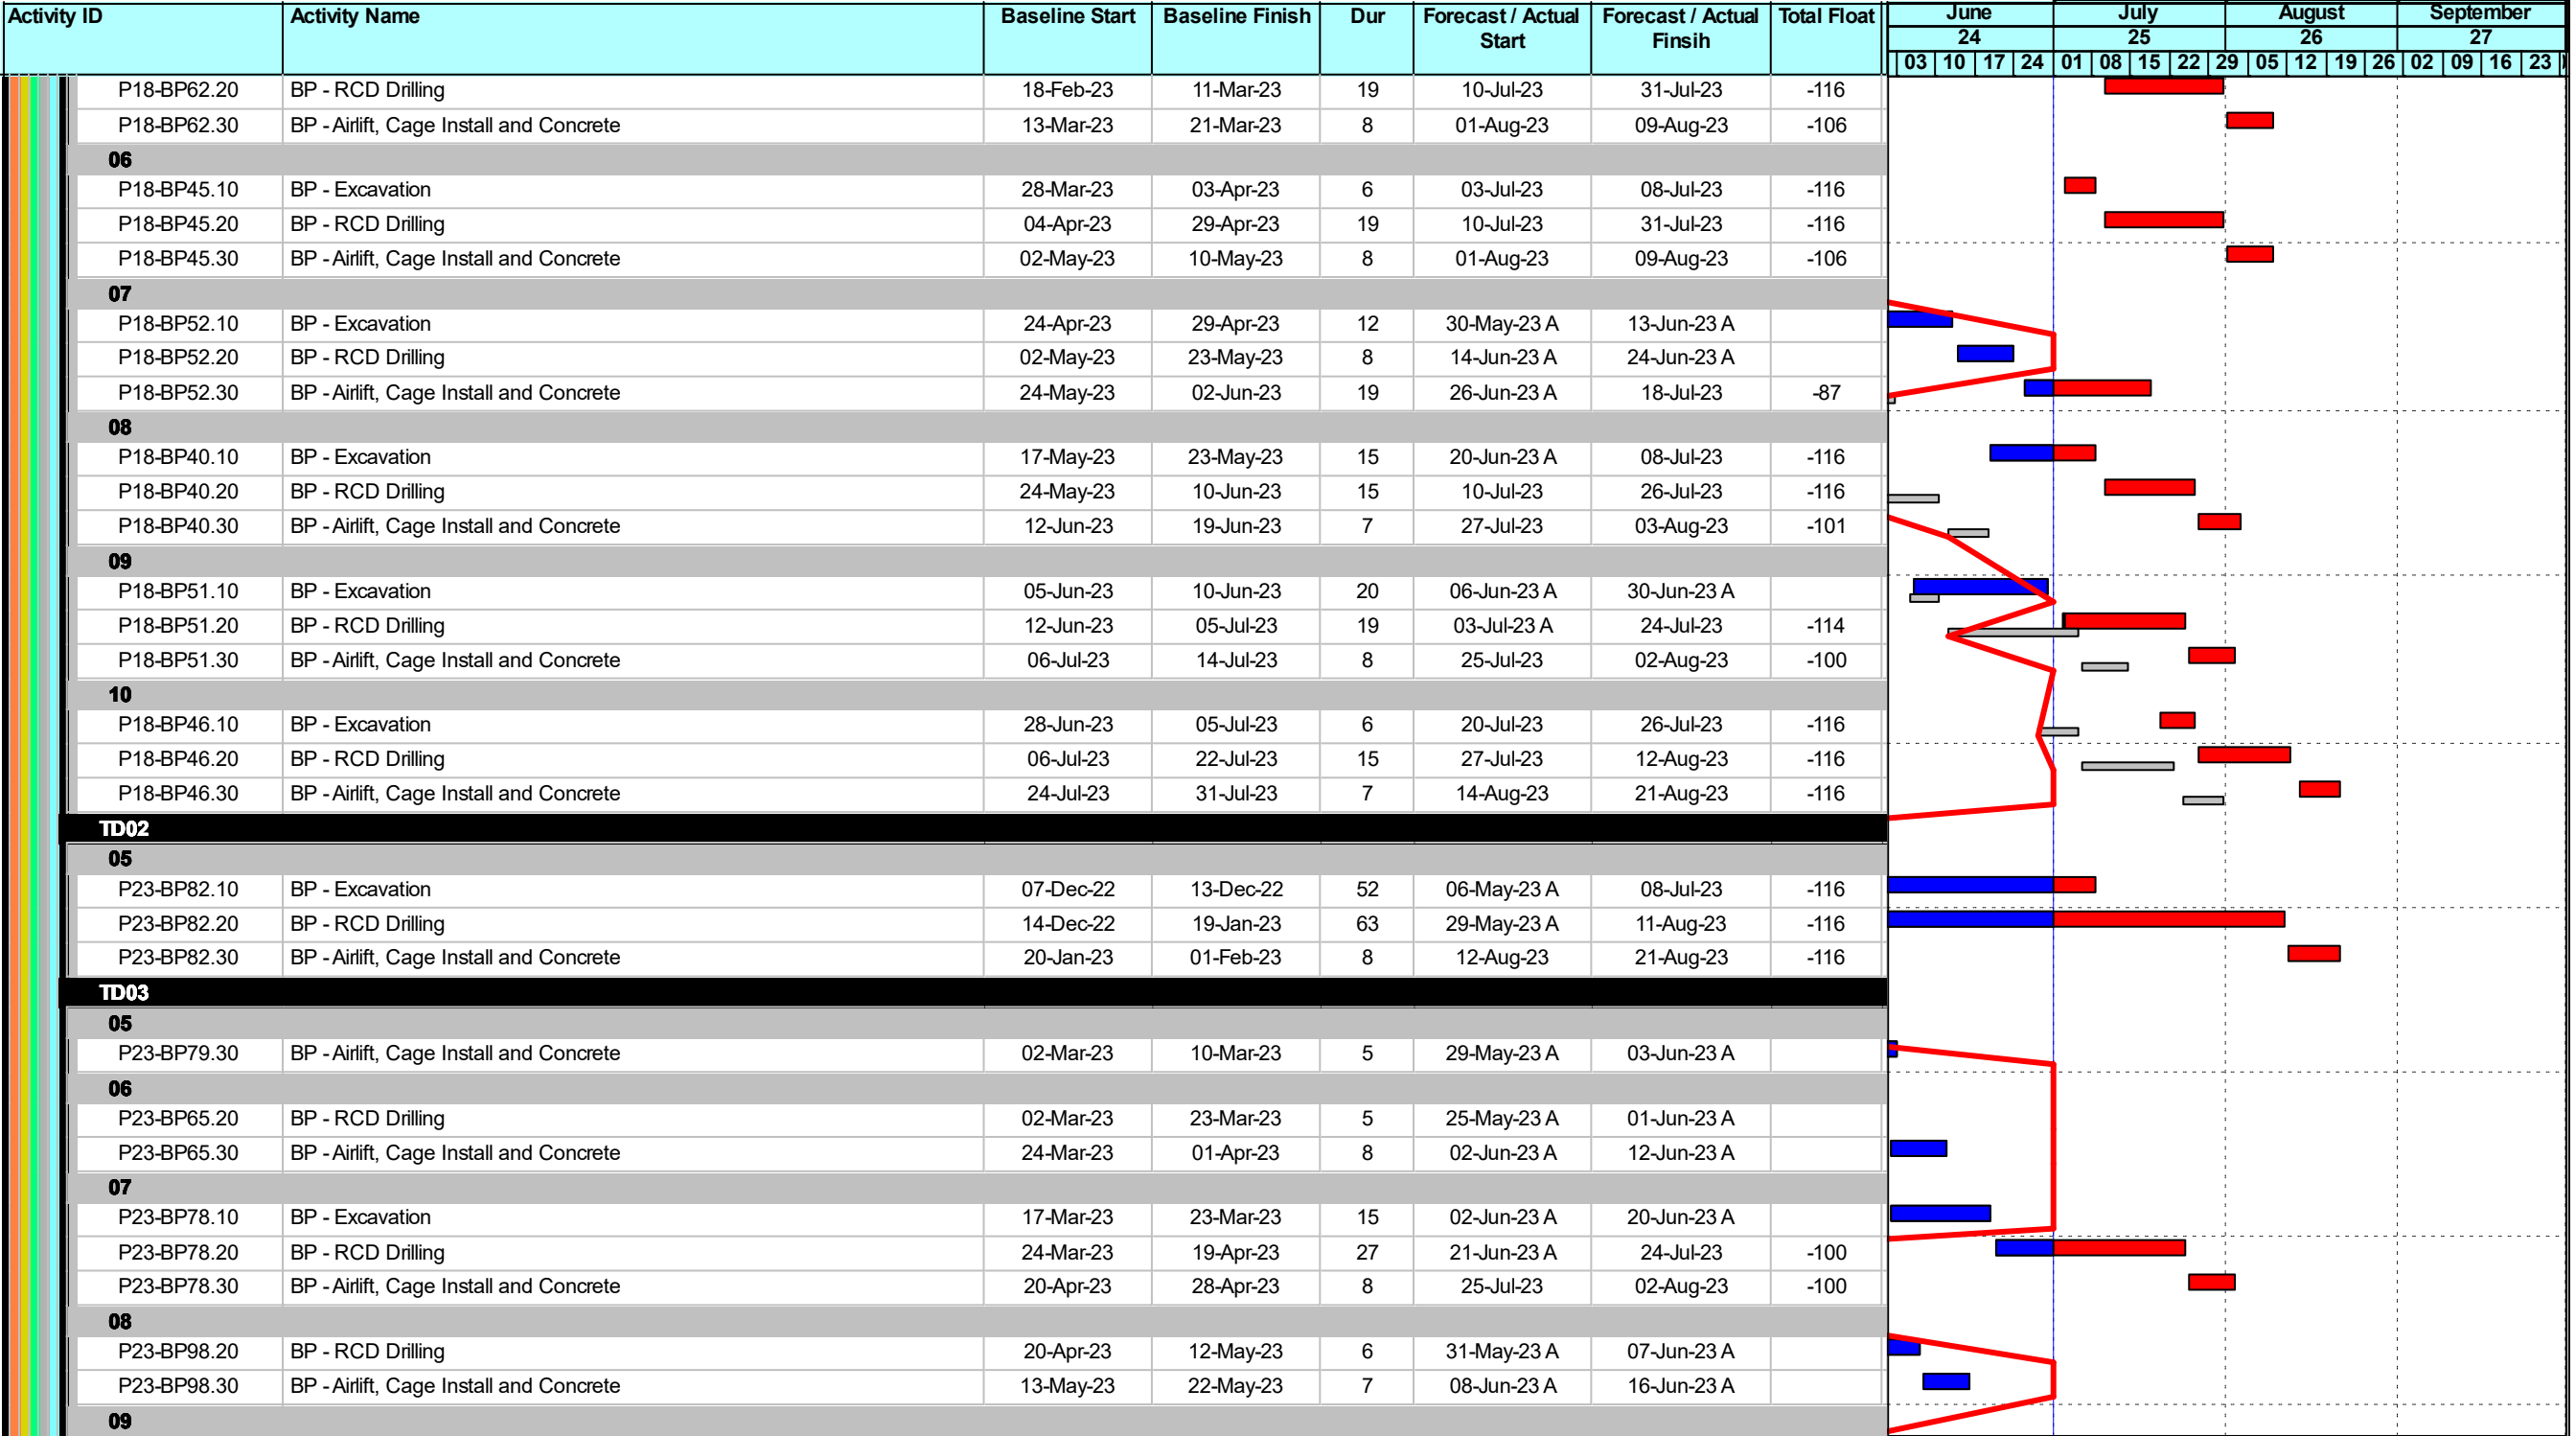

■ Planned	◆ Planned MS
■ Critical	◆ Critical MS
■ Actual	◆ Actual MS


		Date	Revision	Checked	Approved
		04-Mar-22	R0	KL	B
		02-Dec-22	R03D	KL	C







Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	June				July			August				September				
								24				25			26				27				
								03	10	17	24	01	08	15	22	29	05	12	19	26	02	09	16
P23-BP66.10	BP - Excavation	06-May-23	12-May-23	21	13-Jun-23 A	08-Jul-23	-106																
P23-BP66.20	BP - RCD Drilling	13-May-23	05-Jun-23	19	10-Jul-23	31-Jul-23	-106																
P23-BP66.30	BP - Airlift, Cage Install and Concrete	06-Jun-23	14-Jun-23	8	01-Aug-23	09-Aug-23	-106																
TD04																							
02																							
P18-BP49.10	BP - Excavation	21-Dec-22	29-Dec-22	6	03-Jul-23	08-Jul-23	-106																
P18-BP49.20	BP - RCD Drilling	30-Dec-22	21-Jan-23	19	10-Jul-23	31-Jul-23	-106																
P18-BP49.30	BP - Airlift, Cage Install and Concrete	25-Jan-23	03-Feb-23	8	01-Aug-23	09-Aug-23	-106																
04																							
P18-BP37.10	BP - Excavation	10-Feb-23	16-Feb-23	23	01-Jun-23 A	29-Jun-23 A	-100																
P18-BP37.20	BP - RCD Drilling	17-Feb-23	10-Mar-23	20	30-Jun-23 A	24-Jul-23	-100																
P18-BP37.30	BP - Airlift, Cage Install and Concrete	11-Mar-23	20-Mar-23	8	25-Jul-23	02-Aug-23	-100																
05																							
P18-BP50.10	BP - Excavation	04-Mar-23	10-Mar-23	6	03-Jul-23	08-Jul-23	-106																
P18-BP50.20	BP - RCD Drilling	11-Mar-23	01-Apr-23	19	10-Jul-23	31-Jul-23	-106																
P18-BP50.30	BP - Airlift, Cage Install and Concrete	03-Apr-23	15-Apr-23	8	01-Aug-23	09-Aug-23	-106																
10																							
P23-BP75.10	BP - Excavation	22-Apr-23	28-Apr-23	6	03-Jul-23	08-Jul-23	-106																
P23-BP75.20	BP - RCD Drilling	29-Apr-23	22-May-23	19	10-Jul-23	31-Jul-23	-106																
P23-BP75.30	BP - Airlift, Cage Install and Concrete	23-May-23	01-Jun-23	8	01-Aug-23	09-Aug-23	-106																
12																							
P23-BP86.10	BP - Excavation	16-May-23	22-May-23	15	13-May-23 A	01-Jun-23 A																	
P23-BP86.20	BP - RCD Drilling	23-May-23	27-Jun-23	5	02-Jun-23 A	08-Jun-23 A																	
P23-BP86.30	BP - Airlift, Cage Install and Concrete	28-Jun-23	07-Jul-23	14	09-Jun-23 A	27-Jun-23 A																	
TD05																							
06																							
P18-BP64.20	BP - RCD Drilling	04-Mar-23	25-Mar-23	26	13-May-23 A	14-Jun-23 A																	
P18-BP64.30	BP - Airlift, Cage Install and Concrete	27-Mar-23	04-Apr-23	21	15-Jun-23 A	11-Jul-23	-81																
07																							
P18-BP36.10	BP - Excavation	20-Mar-23	25-Mar-23	6	03-Jul-23	08-Jul-23	-101																
P18-BP36.20	BP - RCD Drilling	27-Mar-23	17-Apr-23	15	10-Jul-23	26-Jul-23	-101																
P18-BP36.30	BP - Airlift, Cage Install and Concrete	18-Apr-23	25-Apr-23	7	27-Jul-23	03-Aug-23	-101																
09																							
P18-BP60.20	BP - RCD Drilling	06-May-23	29-May-23	5	31-May-23 A	06-Jun-23 A																	
P18-BP60.30	BP - Airlift, Cage Install and Concrete	30-May-23	07-Jun-23	9	07-Jun-23 A	17-Jun-23 A																	
TD06																							
03																							
P18-BP23.10	BP IAR-S - Excavation	26-Nov-22	02-Dec-22	6	03-Jul-23	08-Jul-23	-103																
P18-BP23.20	BP IAR-S - RCD Drilling	03-Dec-22	20-Dec-22	15	10-Jul-23	26-Jul-23	-103																
P18-BP23.30	BP IAR-S - Airlift, Cage Install and Concrete	23-Dec-22	03-Jan-23	7	29-Jul-23	05-Aug-23	-103																
06																							

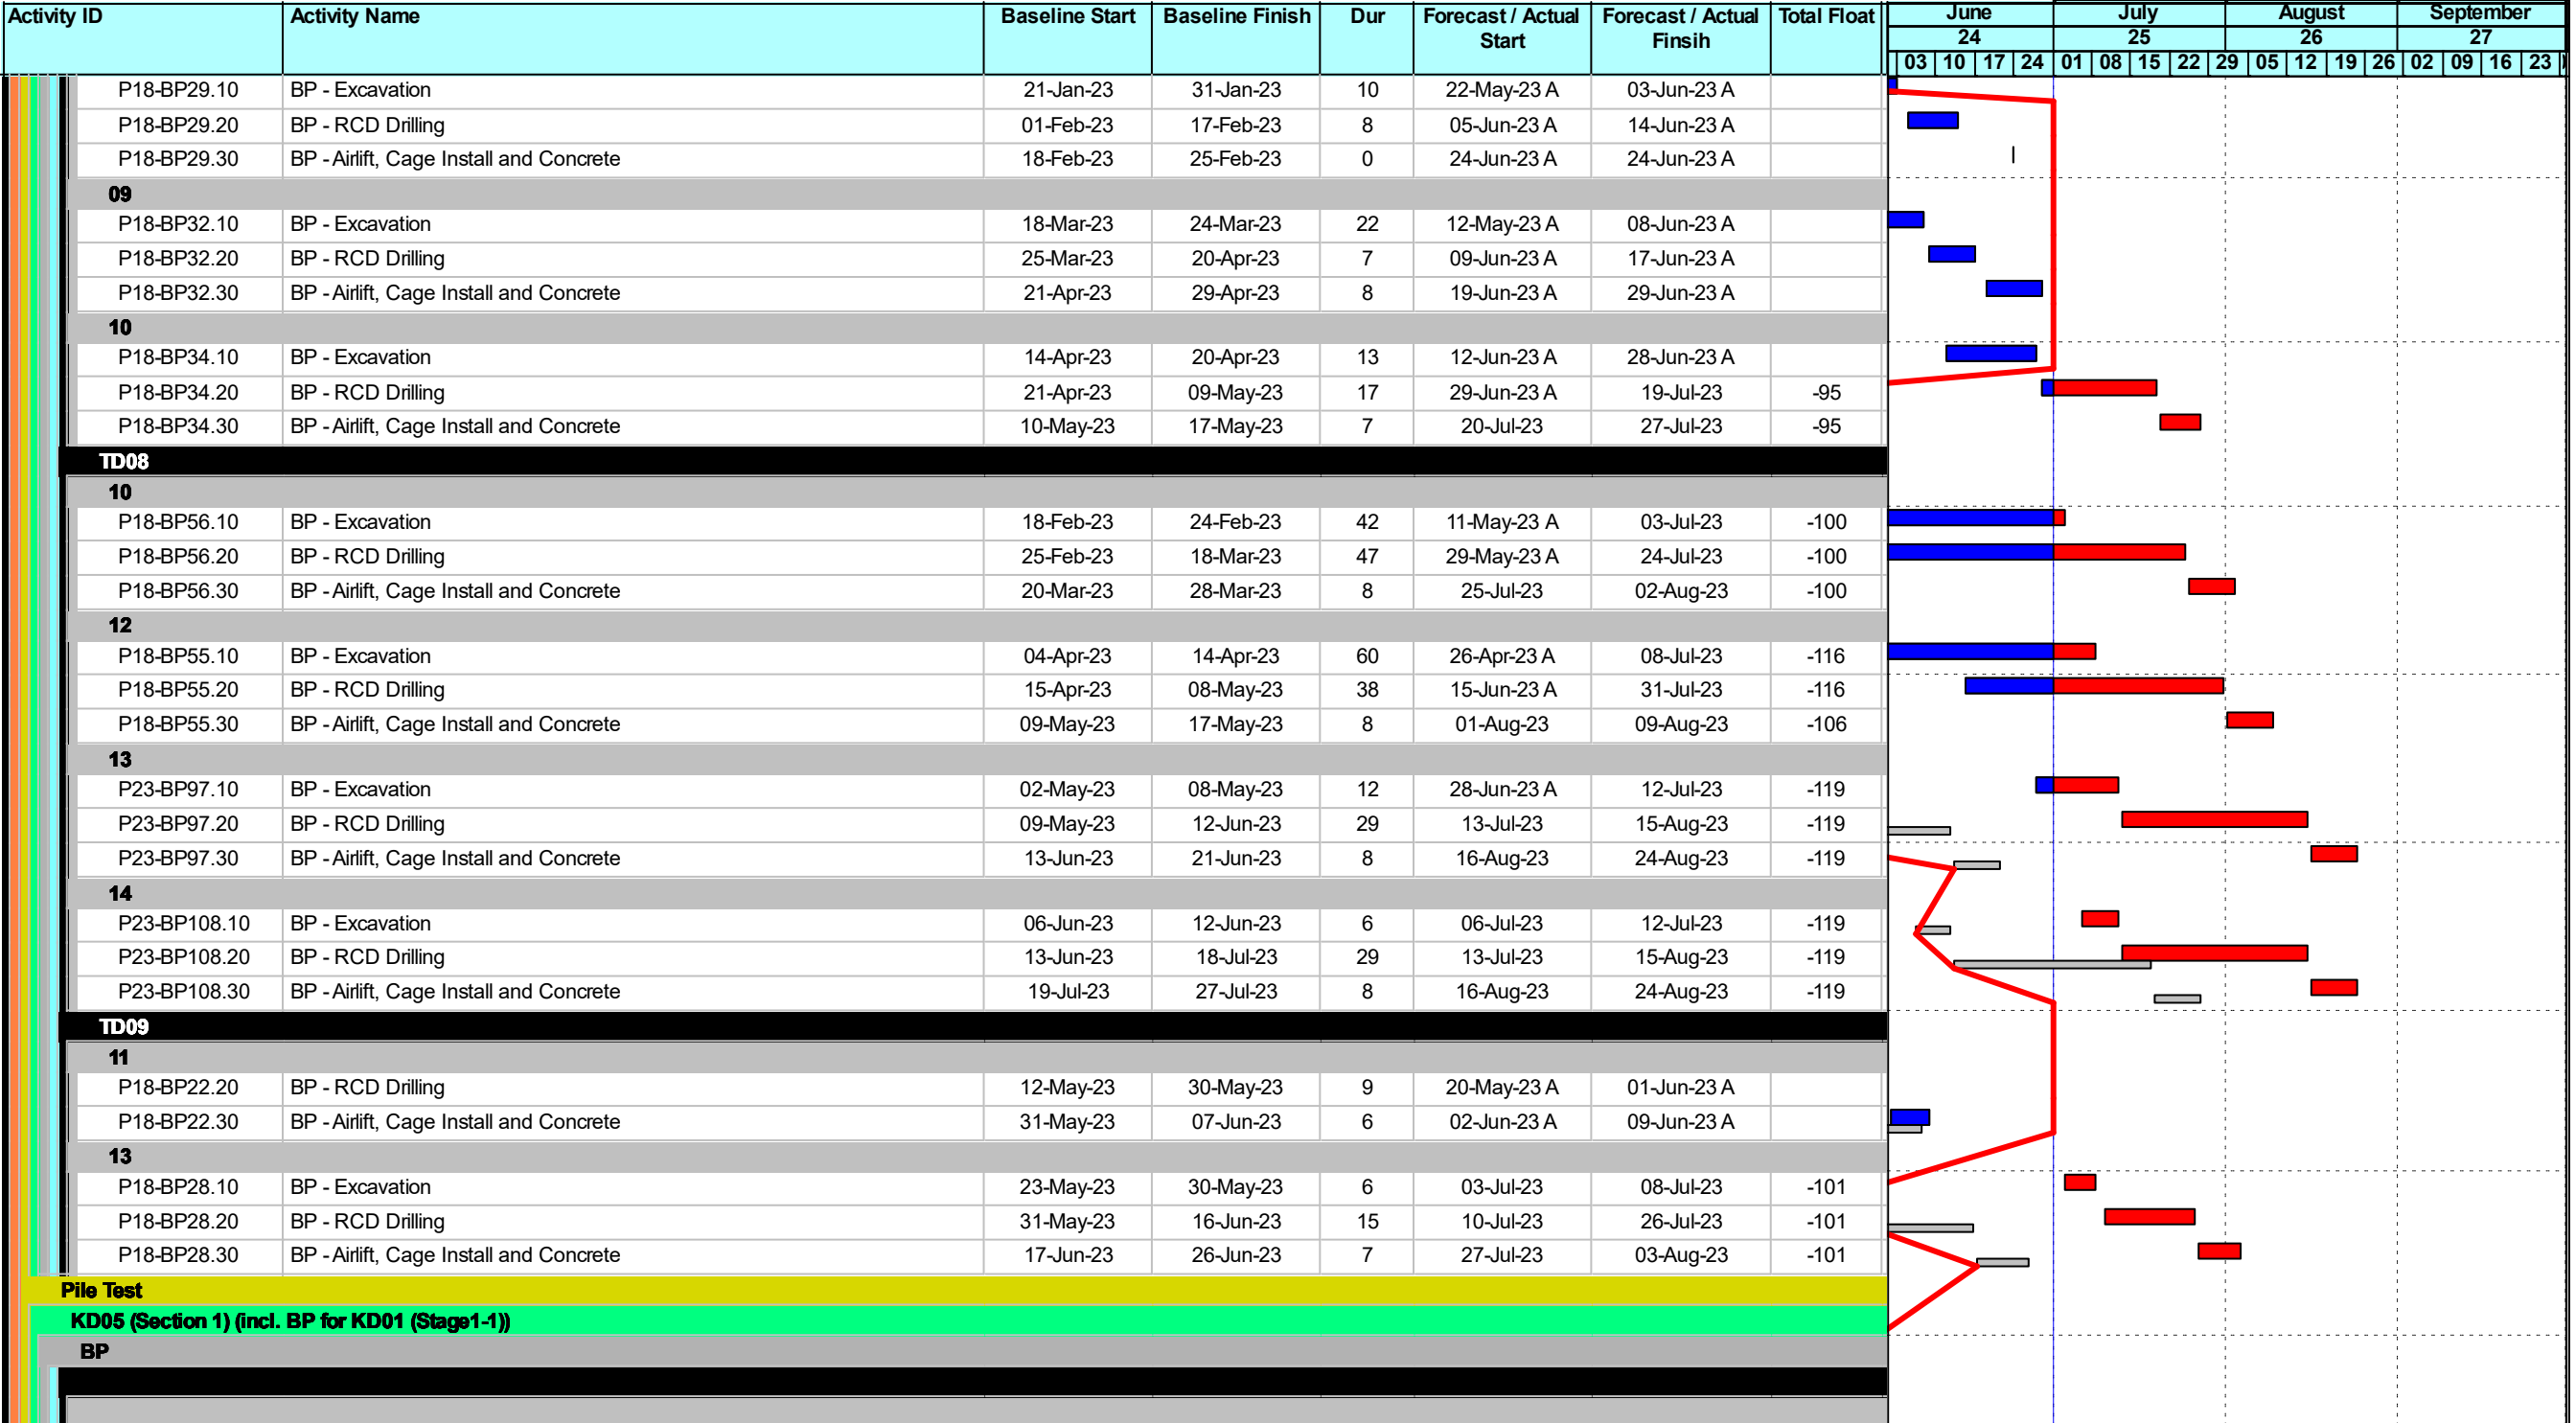Planned	Planned MS
Critical	Critical MS
Actual	Actual MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 30 June 2023
 Based on CMWP Rev.0 (3rd Draft)


Date	Revision	Checked	Approved
04-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C



	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 30 June 2023
 Based on CMWP Rev.0 (3rd Draft)

		Date	Revision	Checked	Approved
		04-Mar-22	R0	KL	B
		02-Dec-22	R03D	KL	C

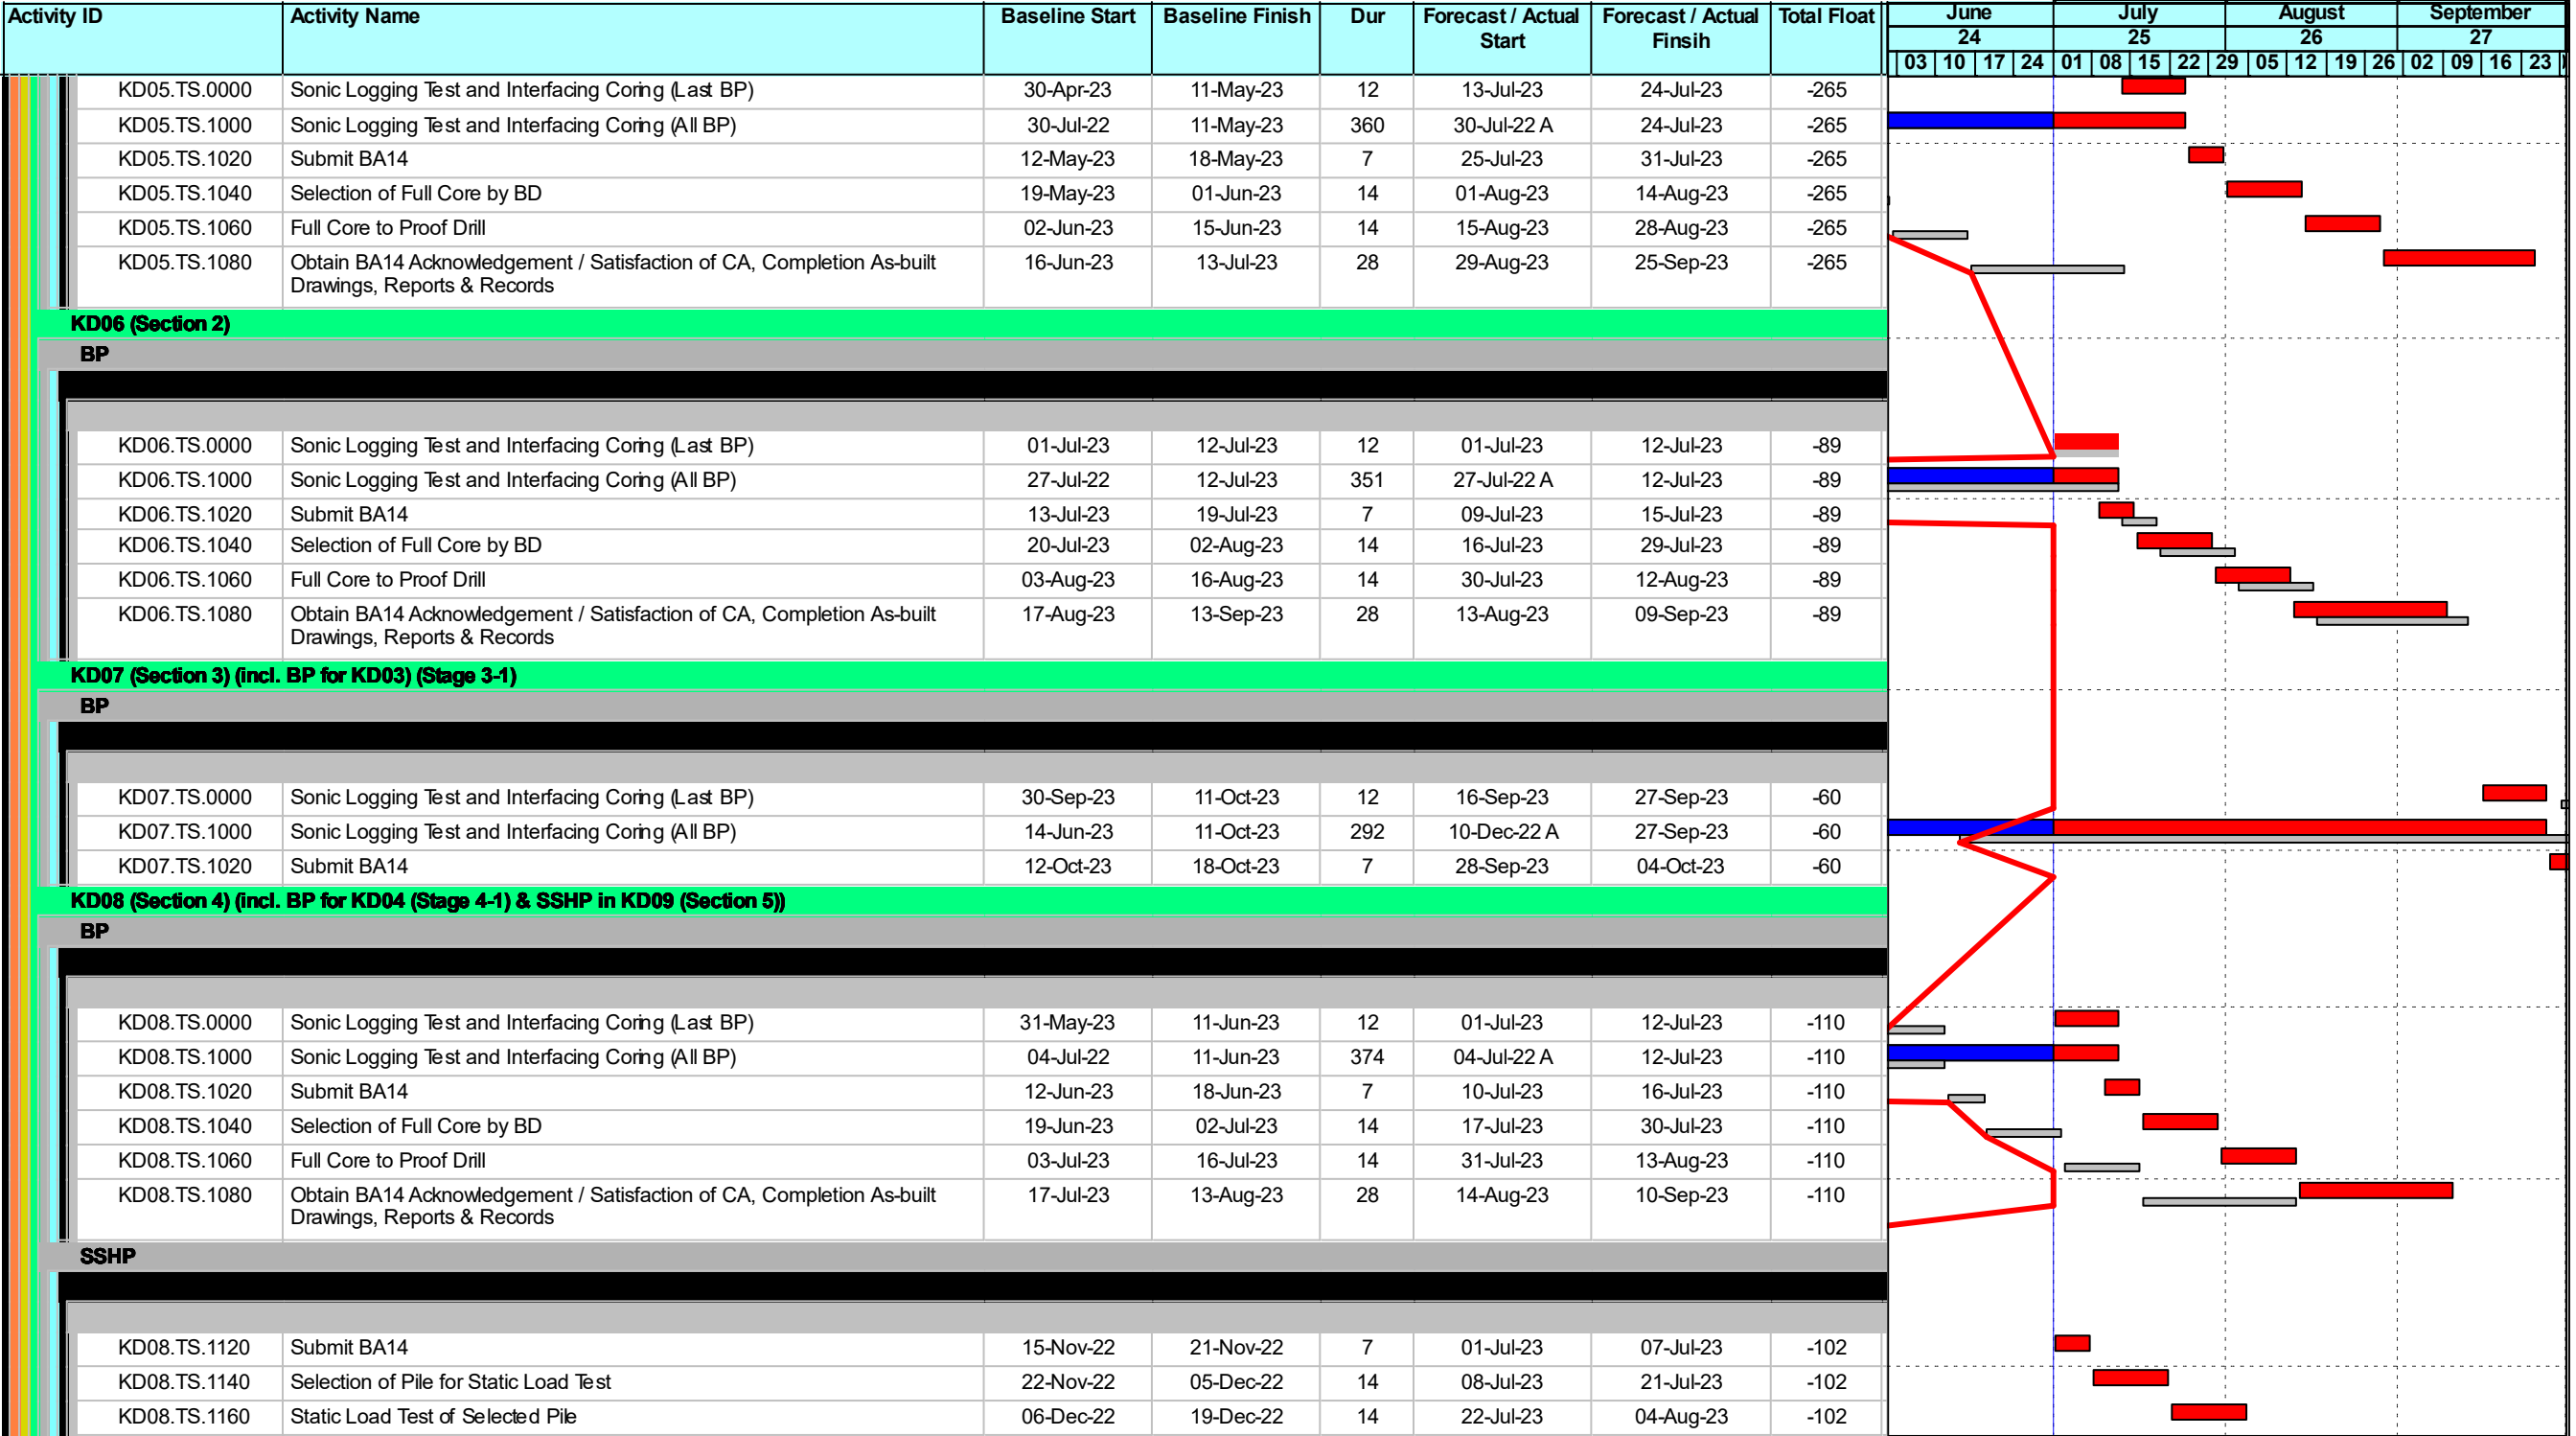

	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 30 June 2023
Based on CMWP Rev.0 (3rd Draft)

	Date	Revision	Checked	Approved
	04-Mar-22	R0	KL	B
	02-Dec-22	R03D	KL	C

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	June				July				August				September			
								24				25				26				27			
								03	10	17	24	01	08	15	22	29	05	12	19	26	02	09	16
KD08.TS.1180	Obtain BA14 Acknowledgement / Satisfaction of CA, Completion As-built Drawings, Reports & Records	20-Dec-22	16-Jan-23	28	05-Aug-23	01-Sep-23	-102																
KD09 (Section 5) (incl. BP for KD02 (Stage 5-1))																							
BP																							
KD09.TS.0000	Sonic Logging Test and Interfacing Coring (Last BP)	01-Aug-23	12-Aug-23	12	25-Aug-23	05-Sep-23	-148																
KD09.TS.1000	Sonic Logging Test and Interfacing Coring (All BP)	23-May-22	12-Aug-23	471	23-May-22 A	05-Sep-23	-148																
KD09.TS.1020	Submit BA14	13-Aug-23	19-Aug-23	7	06-Sep-23	12-Sep-23	-148																
KD09.TS.1040	Selection of Full Core by BD	20-Aug-23	02-Sep-23	14	13-Sep-23	26-Sep-23	-148																
KD09.TS.1060	Full Core to Proof Drill	03-Sep-23	16-Sep-23	14	27-Sep-23	10-Oct-23	-148																
Attendance to Other Project Contractors (optional works item no. 2A to 2E)																							
S2.AT.0000	Attendance at Section 2 Area (optional works item no. 2B) (Duration TBC)	13-May-23	01-Jun-23	20	01-Jul-23	20-Jul-23	-38																
S3.AT.0000	Attendance at Section 3 Area (optional works item no. 2C) (Duration TBC)	02-Jul-23	21-Jul-23	20	02-Jul-23	21-Jul-23	71																

	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 30 June 2023
 Based on CMWP Rev.0 (3rd Draft)

Date	Revision	Checked	Approved
04-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C
