


Zone 2B & 2C

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	July				August				September				October			
								25				26				27				28			
								01	08	15	22	29	05	12	19	26	02	09	16	23	30	07	14

Piling for Integrated Basement and U/G Road in Zone 2B & 2C


Contract Dates							
Key Dates							
KD for Zone 2B							
KD05	KD05 (Section 1) - 03 Jan 2023		13-Jul-23	0		25-Sep-23*	-265
KD06	KD06 (Section 2) - 12 Jun 2023		13-Sep-23	0		06-Sep-23*	-86
KD for Zone 2C							
KD08	KD08 (Section 4) - 23 May 2023		13-Aug-23	0		13-Sep-23*	-113
Optional Works subjected to CA's Instruction							
CO2C	Last CAI date for Optional Works Item No.2C (330 Days to 710 Days after Commencement)		02-Jul-23	0	02-Jul-23 A		
Construction Stage							
Pile Construction							
KD05 (Section 1)							
Bored Piles - Drainage Diversion							
CD08							
P17-BP18.30	BP IAR-N - Airlift, Cage Install and Concrete		22-Apr-23	29-Apr-23	0	10-Jul-23 A	10-Jul-23 A
P17-BP20.30	BP - Airlift, Cage Install and Concrete (Rev. to P17-BP20A)		14-Mar-23	21-Mar-23	10	29-Jun-23 A	12-Jul-23 A
Bored Piles							
TD07							
09							
P18-BP07.30	BP IAR-S - Airlift, Cage Install and Concrete		06-Apr-23	17-Apr-23	14	13-Jun-23 A	30-Jun-23 A
KD07 (Section 3)							
Bored Piles							
VD01							
P26-BP07.10	BP - Excavation		28-Apr-23	05-May-23	20	06-Jul-23 A	29-Jul-23
P26-BP07.20	BP - RCD Drilling		06-May-23	09-Jun-23	29	29-Jul-23	31-Aug-23
P26-BP07.30	BP - Airlift, Cage Install and Concrete		10-Jun-23	19-Jun-23	8	01-Sep-23	09-Sep-23
08							
P26-BP05.10	BP - Excavation		03-Jun-23	09-Jun-23	21	11-Jul-23 A	03-Aug-23
P26-BP05.20	BP - RCD Drilling		10-Jun-23	15-Jul-23	29	04-Aug-23	06-Sep-23
P26-BP05.30	BP - Airlift, Cage Install and Concrete		17-Jul-23	25-Jul-23	8	07-Sep-23	15-Sep-23
VD02							

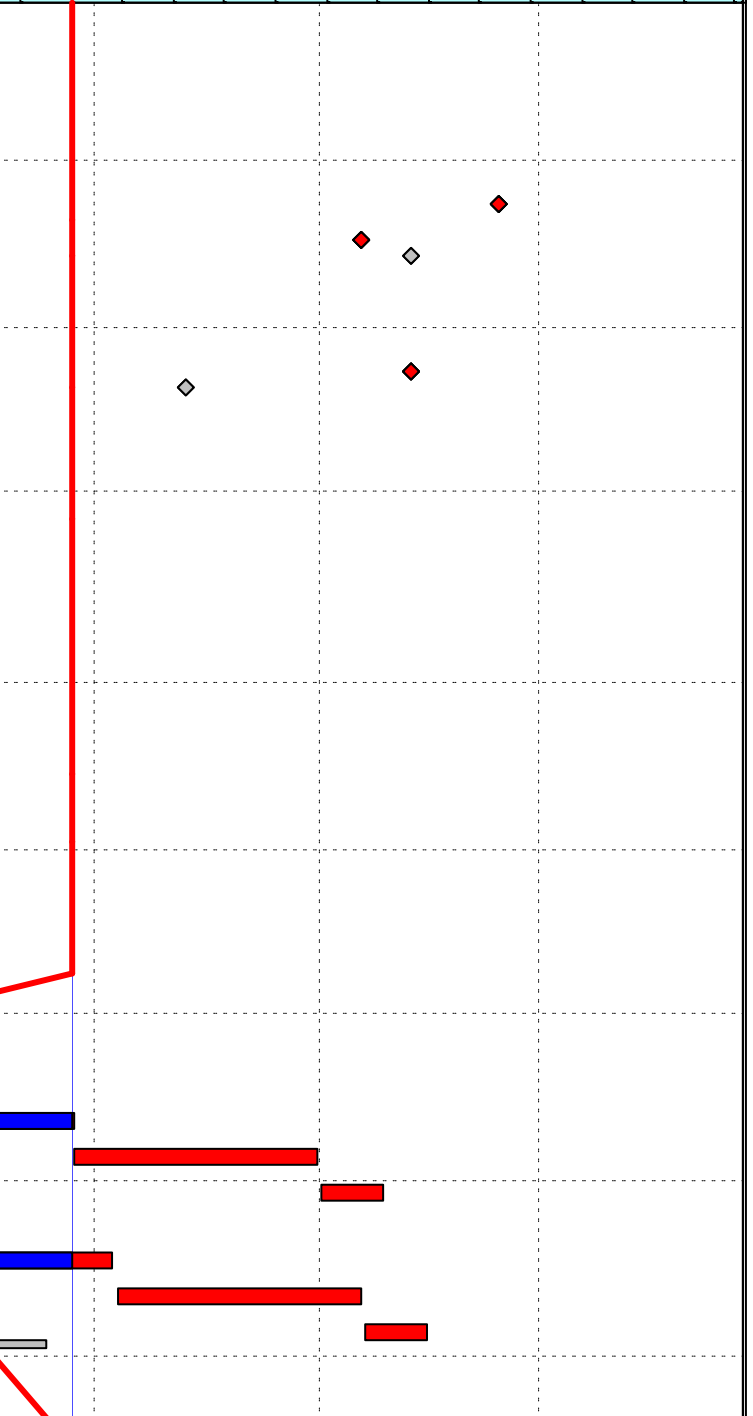

	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS



Date	Revision	Checked	Approved
04-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C

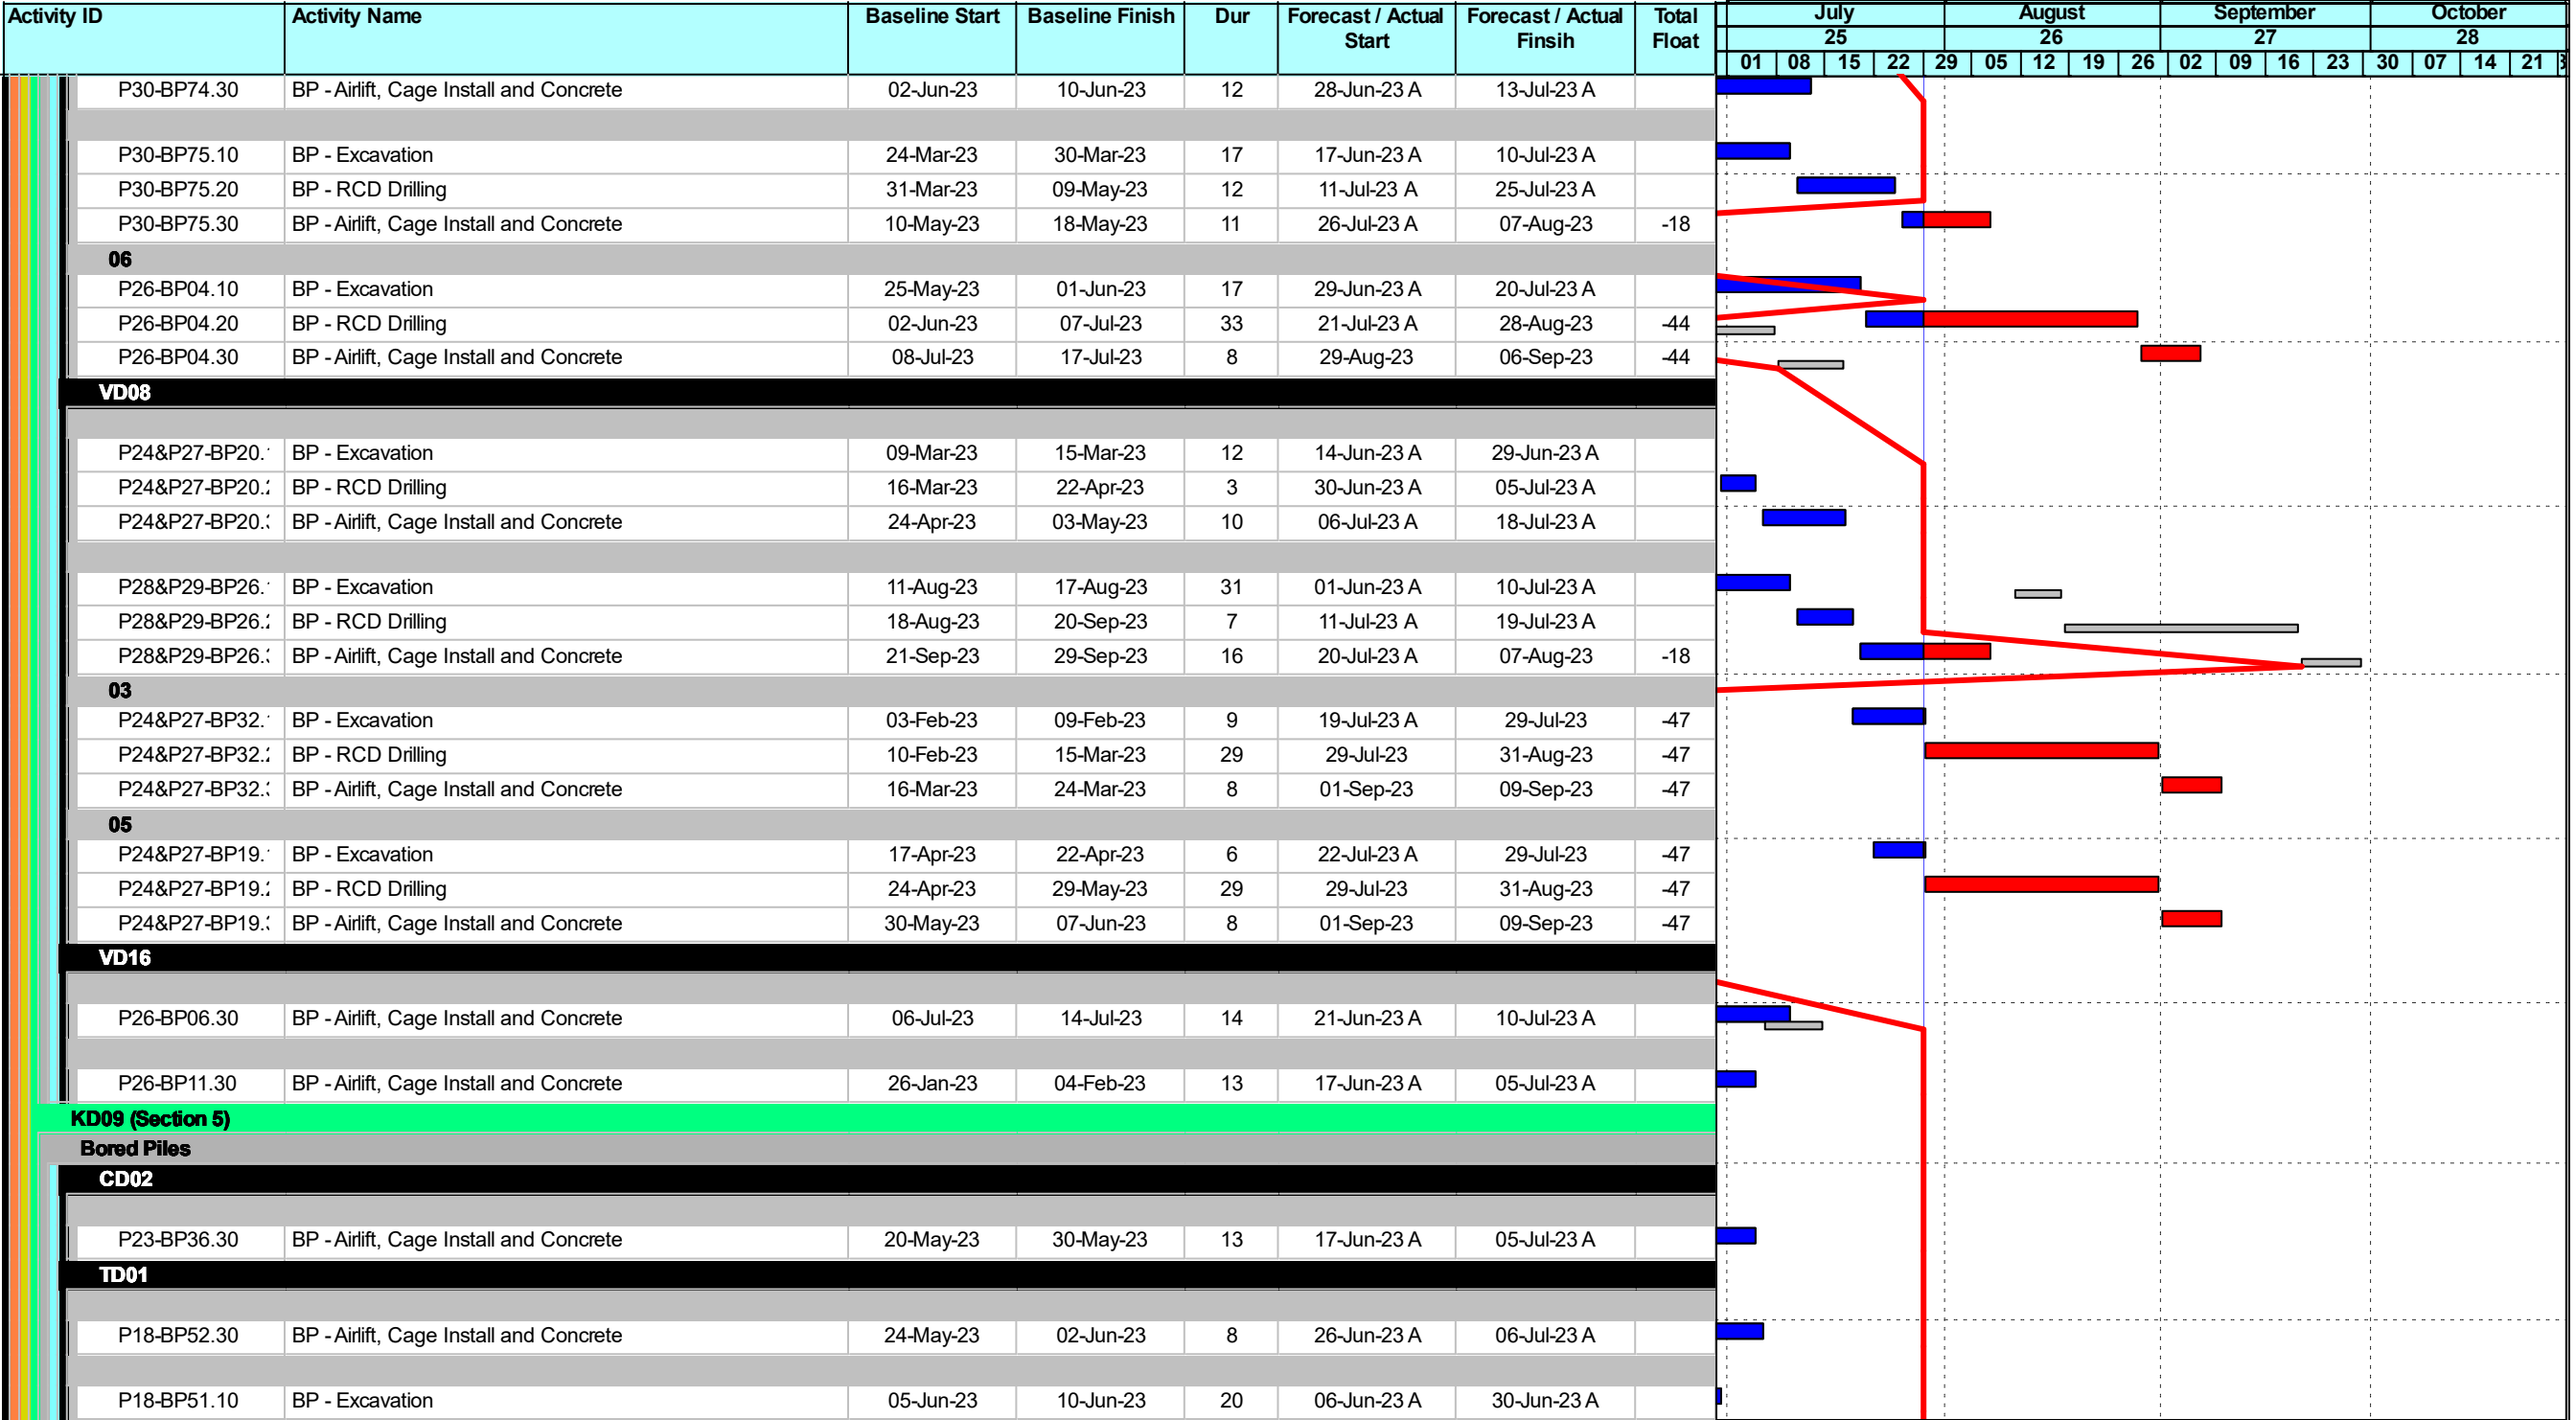


	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 28 July 2023
Based on CMWP Rev.0 (3rd Draft)



Date	Revision	Checked	Approved
04-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C

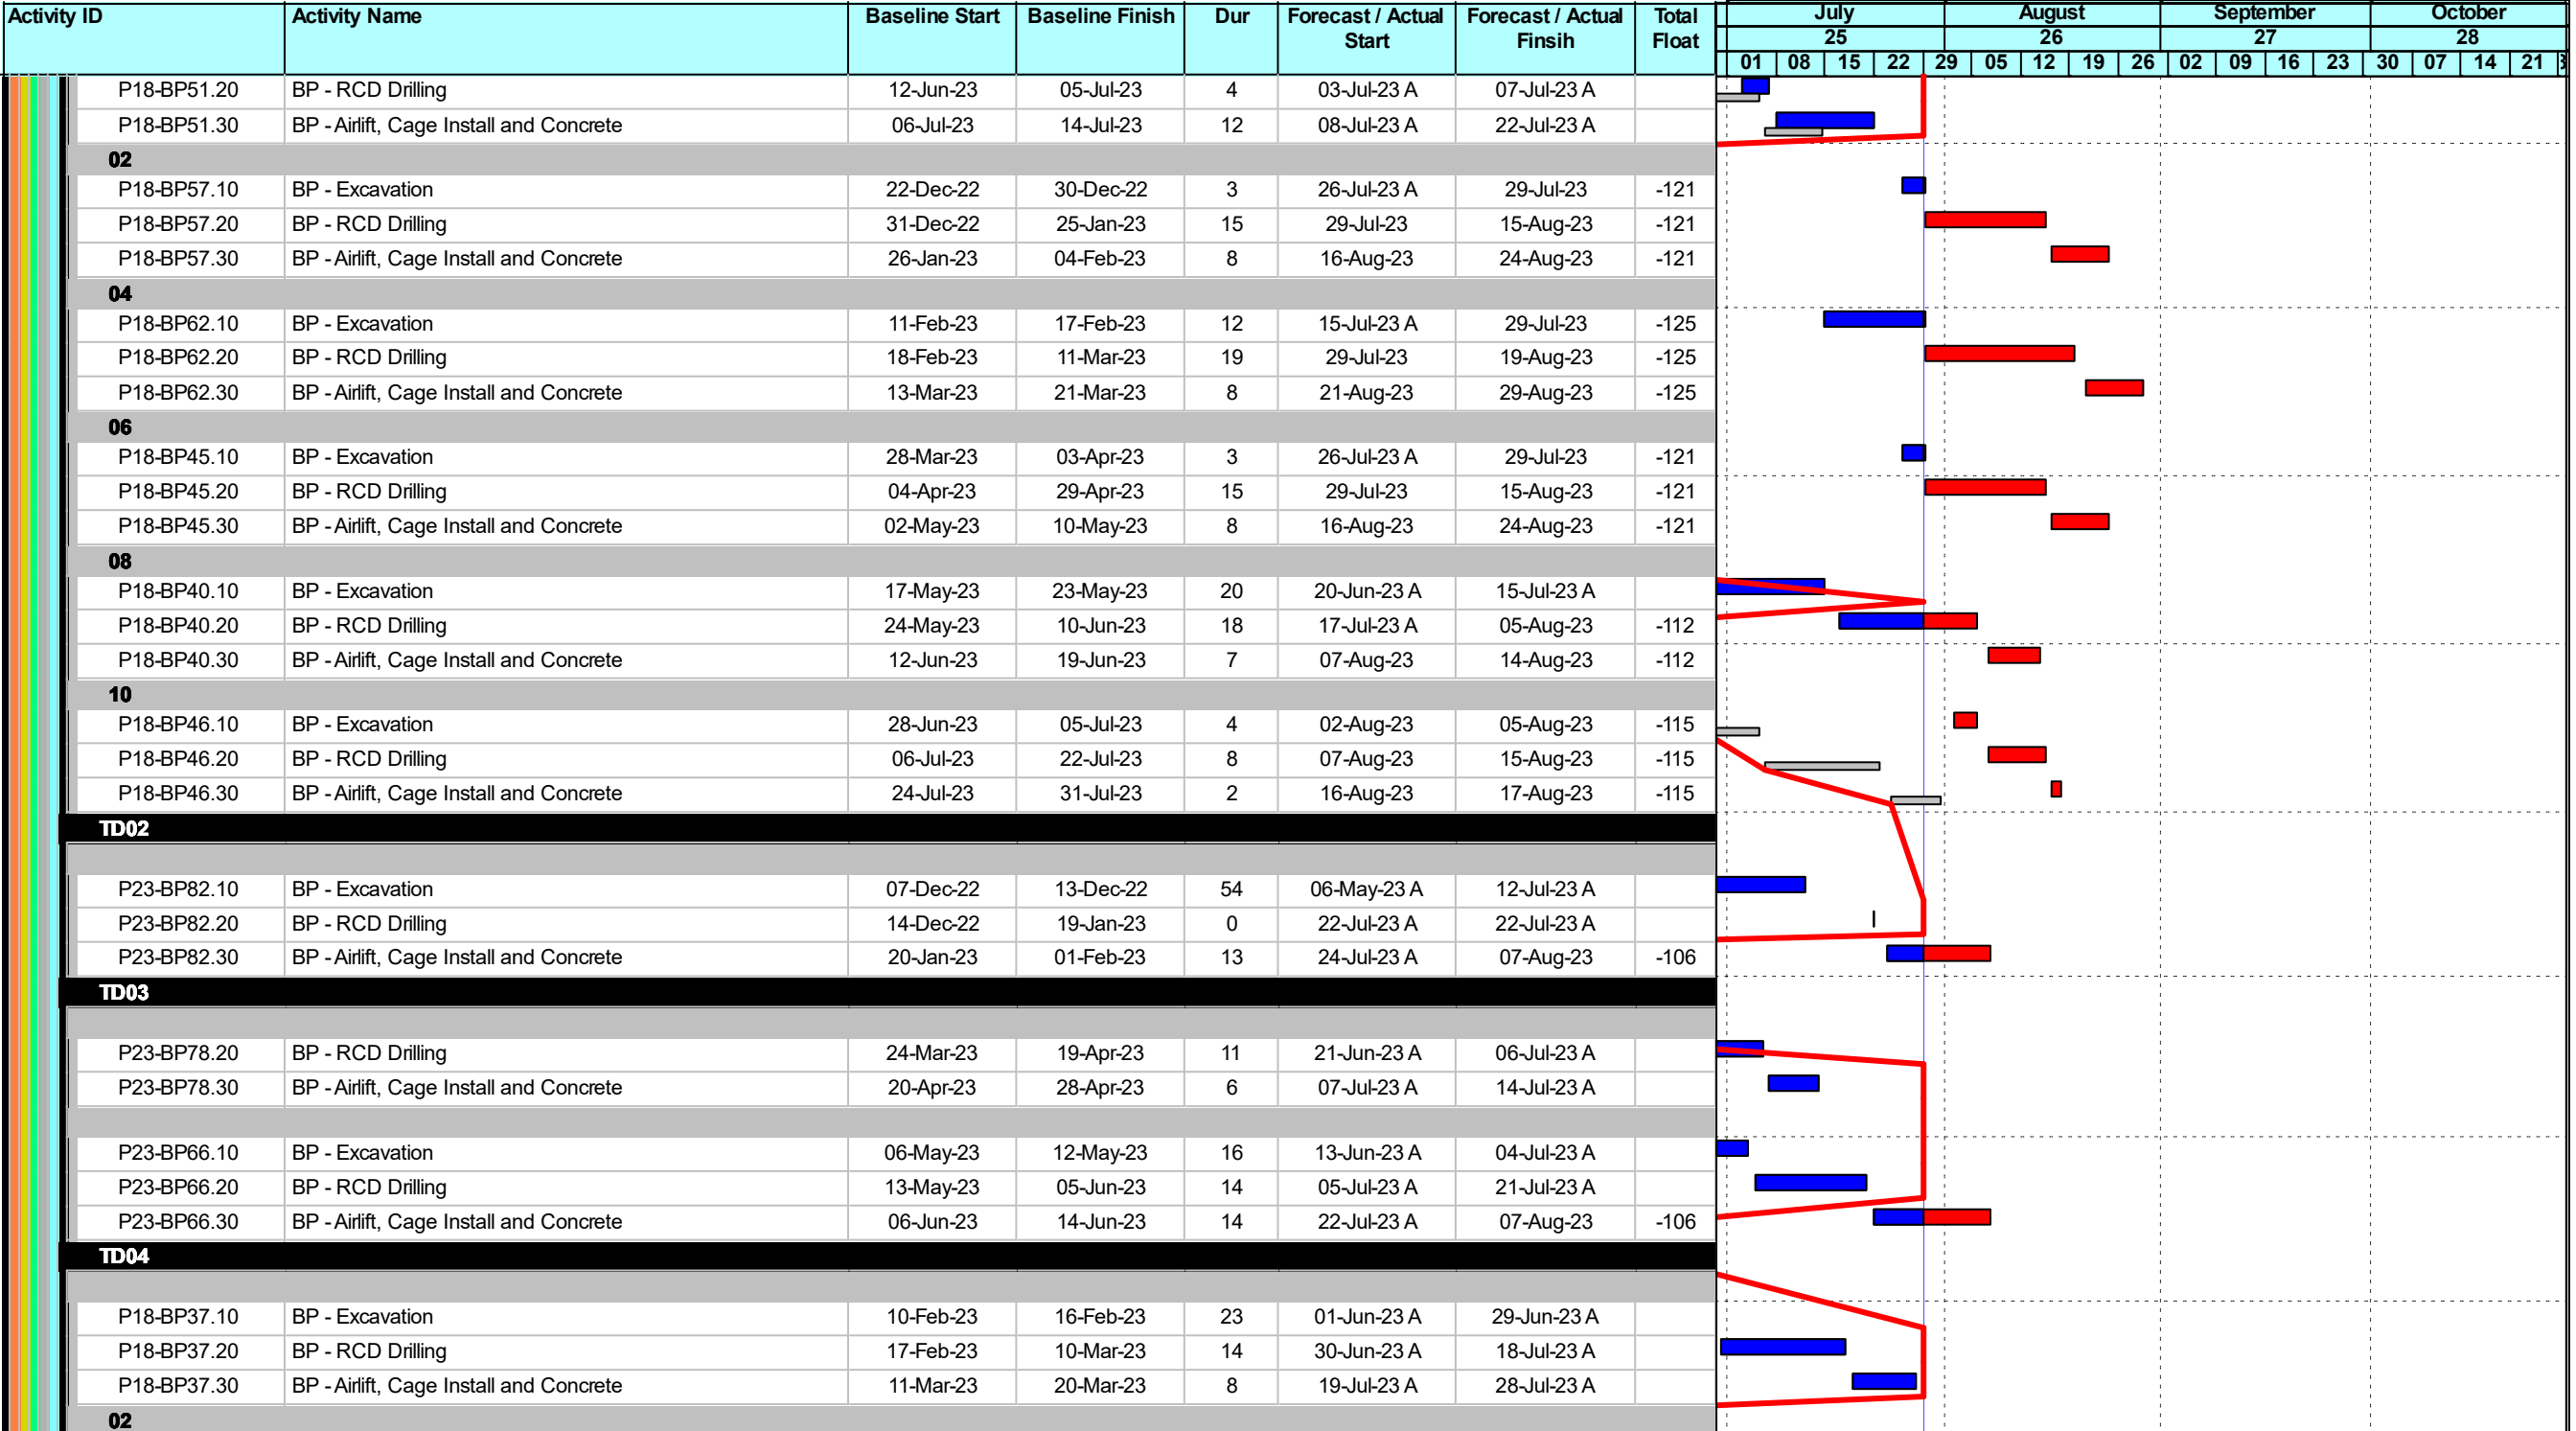







 Planned	◆ Planned MS
 Critical	◆ Critical MS
 Actual	◆ Actual MS




Date	Revision	Checked	Approved
04-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	July				August					September				October			
								25				26					27				28			
								01	08	15	22	29	05	12	19	26	02	09	16	23	30	07	14	21
P18-BP49.10	BP - Excavation	21-Dec-22	29-Dec-22	18	08-Jul-23 A	29-Jul-23	-123																	
P18-BP49.20	BP - RCD Drilling	30-Dec-22	21-Jan-23	17	29-Jul-23	17-Aug-23	-123																	
P18-BP49.30	BP - Airlift, Cage Install and Concrete	25-Jan-23	03-Feb-23	8	18-Aug-23	26-Aug-23	-123																	
05																								
P18-BP50.10	BP - Excavation	04-Mar-23	10-Mar-23	3	29-Jul-23	01-Aug-23	-123																	
P18-BP50.20	BP - RCD Drilling	11-Mar-23	01-Apr-23	14	02-Aug-23	17-Aug-23	-123																	
P18-BP50.30	BP - Airlift, Cage Install and Concrete	03-Apr-23	15-Apr-23	8	18-Aug-23	26-Aug-23	-123																	
10																								
P23-BP75.10	BP - Excavation	22-Apr-23	28-Apr-23	18	07-Jul-23 A	28-Jul-23 A																		
P23-BP75.20	BP - RCD Drilling	29-Apr-23	22-May-23	14	29-Jul-23 A	14-Aug-23	-120																	
P23-BP75.30	BP - Airlift, Cage Install and Concrete	23-May-23	01-Jun-23	8	15-Aug-23	23-Aug-23	-120																	
TD05																								
P18-BP64.30	BP - Airlift, Cage Install and Concrete	27-Mar-23	04-Apr-23	20	15-Jun-23 A	11-Jul-23 A																		
07																								
P18-BP36.10	BP - Excavation	20-Mar-23	25-Mar-23	19	07-Jul-23 A	29-Jul-23	-118																	
P18-BP36.20	BP - RCD Drilling	27-Mar-23	17-Apr-23	13	29-Jul-23	12-Aug-23	-118																	
P18-BP36.30	BP - Airlift, Cage Install and Concrete	18-Apr-23	25-Apr-23	7	14-Aug-23	21-Aug-23	-118																	
TD06																								
P18-BP32.30	BP - Airlift, Cage Install and Concrete	21-Apr-23	29-Apr-23	8	19-Jun-23 A	29-Jun-23 A																		
P18-BP34.20	BP - RCD Drilling	21-Apr-23	09-May-23	7	29-Jun-23 A	08-Jul-23 A																		
P18-BP34.30	BP - Airlift, Cage Install and Concrete	10-May-23	17-May-23	9	10-Jul-23 A	20-Jul-23 A																		
03																								
P18-BP23.10	BP IAR-S - Excavation	26-Nov-22	02-Dec-22	3	29-Jul-23	01-Aug-23	-124																	
P18-BP23.20	BP IAR-S - RCD Drilling	03-Dec-22	20-Dec-22	14	02-Aug-23	17-Aug-23	-124																	
P18-BP23.30	BP IAR-S - Airlift, Cage Install and Concrete	23-Dec-22	03-Jan-23	7	21-Aug-23	28-Aug-23	-124																	
TD08																								
10																								
P18-BP56.10	BP - Excavation	18-Feb-23	24-Feb-23	42	11-May-23 A	03-Jul-23 A																		
P18-BP56.20	BP - RCD Drilling	25-Feb-23	18-Mar-23	9	04-Jul-23 A	14-Jul-23 A																		
P18-BP56.30	BP - Airlift, Cage Install and Concrete	20-Mar-23	28-Mar-23	8	15-Jul-23 A	25-Jul-23 A																		
12																								
P18-BP55.10	BP - Excavation	04-Apr-23	14-Apr-23	77	26-Apr-23 A	29-Jul-23	-106																	
P18-BP55.20	BP - RCD Drilling	15-Apr-23	08-May-23	36	15-Jun-23 A	29-Jul-23	-106																	
P18-BP55.30	BP - Airlift, Cage Install and Concrete	09-May-23	17-May-23	8	29-Jul-23	07-Aug-23	-106																	
13																								
P23-BP97.10	BP - Excavation	02-May-23	08-May-23	14	28-Jun-23 A	15-Jul-23 A																		
P23-BP97.20	BP - RCD Drilling	09-May-23	12-Jun-23	7	17-Jul-23 A	25-Jul-23 A																		
P23-BP97.30	BP - Airlift, Cage Install and Concrete	13-Jun-23	21-Jun-23	11	26-Jul-23 A	07-Aug-23	-106																	

	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 28 July 2023
Based on CMWP Rev.0 (3rd Draft)


			
Date	Revision	Checked	Approved
04-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C

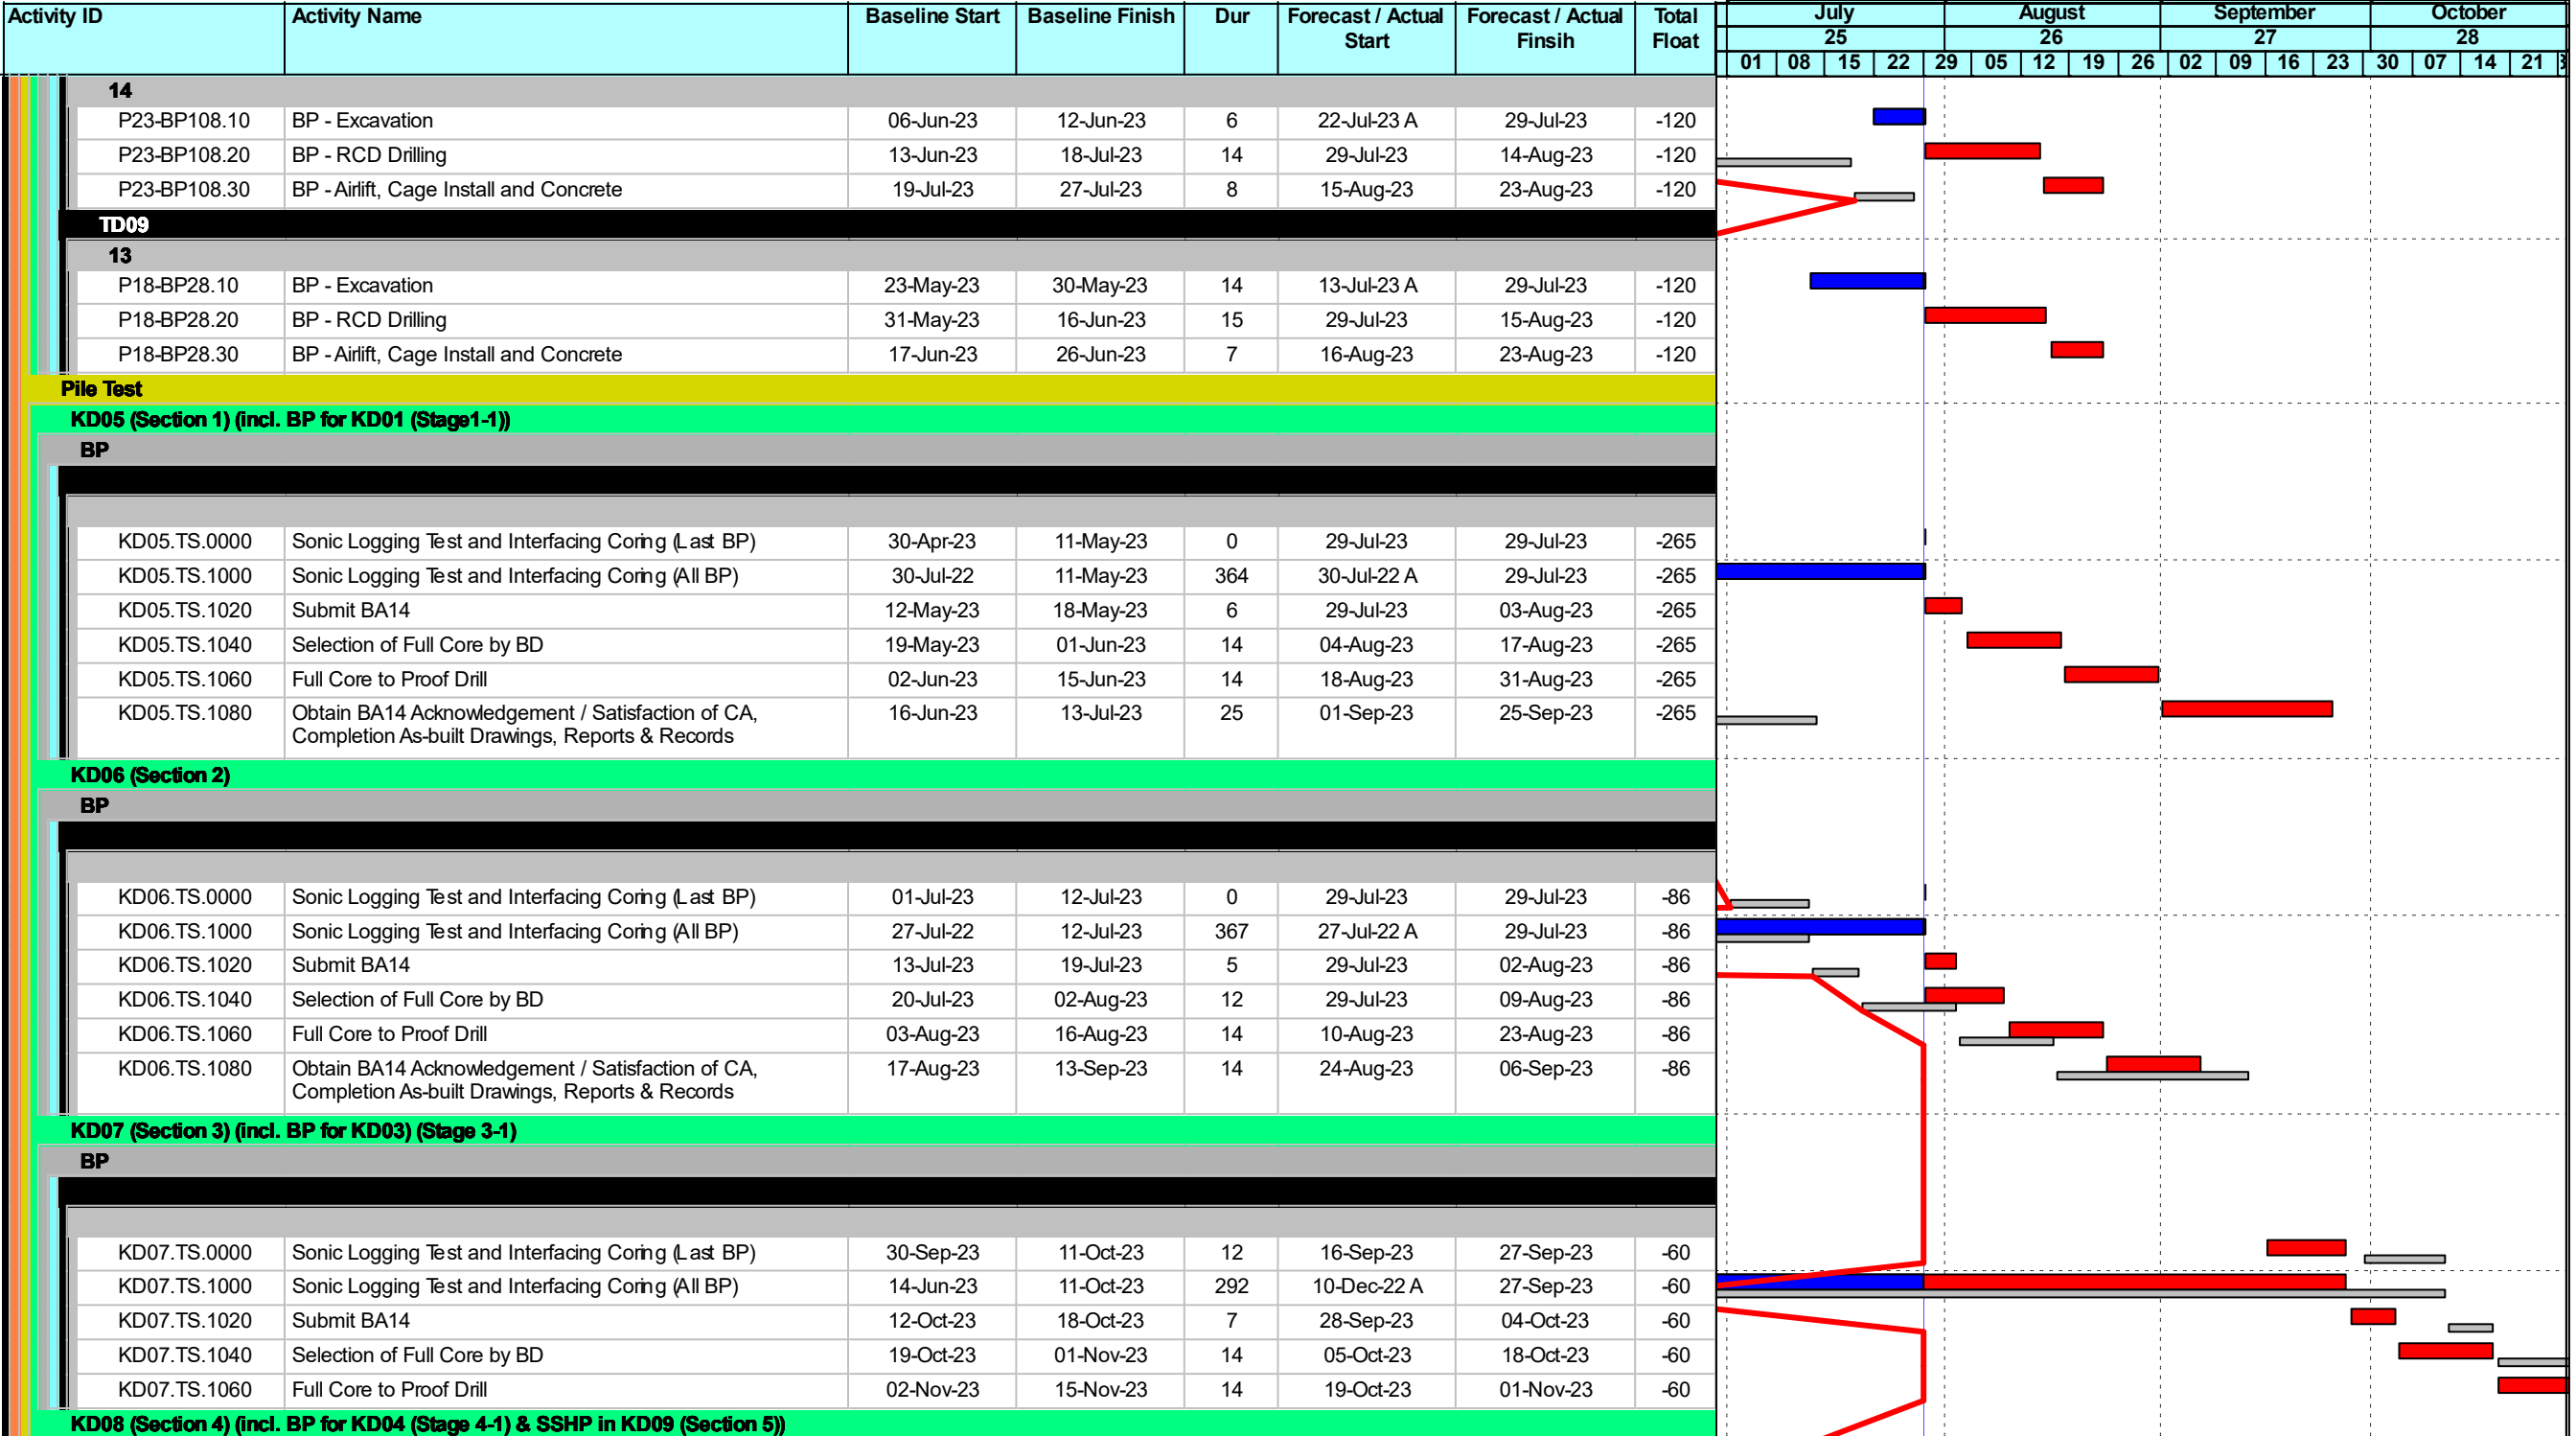

	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS



Date	Revision	Checked	Approved
04-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C

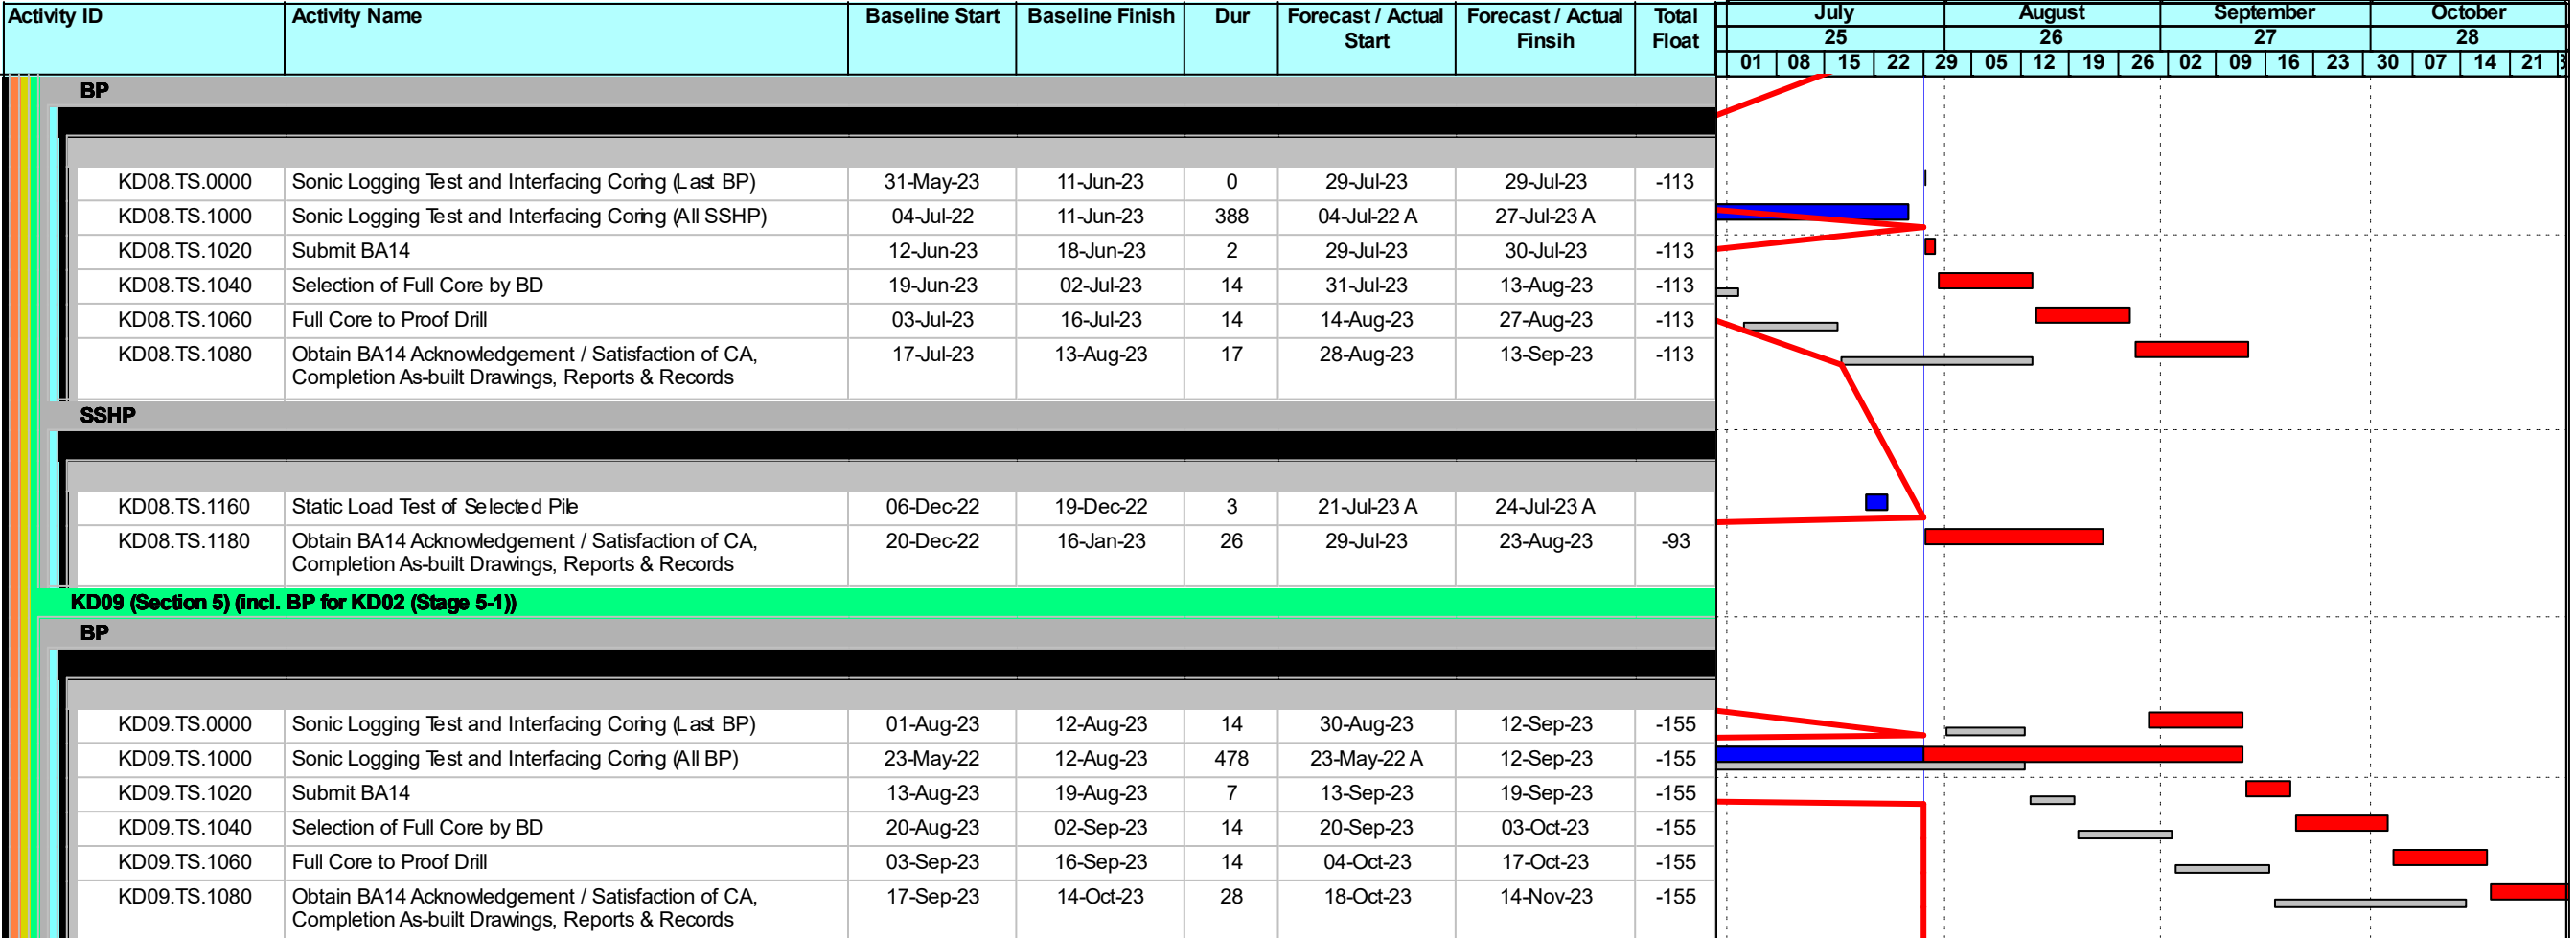

	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 28 July 2023
 Based on CMWP Rev.0 (3rd Draft)



Date	Revision	Checked	Approved
04-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C
