

**Zone 2B & 2C**

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	August				September				October				November			
								26				27				28				29			
								29	05	12	19	26	02	09	16	23	30	07	14	21	28	04	11

**Piling for Integrated Basement and U/G Road in Zone 2B & 2C**

<b>Contract Dates</b>								
<b>Key Dates</b>								
<b>KD for Zone 2B</b>								
KD05	KD05 (Section 1) - 03 Jan 2023			13-Jul-23	0		25-Sep-23*	-265
KD06	KD06 (Section 2) - 12 Jun 2023			13-Sep-23	0		06-Sep-23*	-86

<b>KD for Zone 2C</b>								
KD08	KD08 (Section 4) - 23 May 2023			13-Aug-23	0		13-Sep-23*	-113

**Construction Stage**

**Pile Construction**

**KD07 (Section 3)**

**Bored Piles**

**VD01**

P26-BP07.10	BP - Excavation	28-Apr-23	05-May-23	25	06-Jul-23 A	04-Aug-23 A	
P26-BP07.20	BP - RCD Drilling	06-May-23	09-Jun-23	6	05-Aug-23 A	12-Aug-23 A	
P26-BP07.30	BP - Airlift, Cage Install and Concrete	10-Jun-23	19-Jun-23	8	14-Aug-23 A	23-Aug-23 A	

**08**

P26-BP05.10	BP - Excavation	03-Jun-23	09-Jun-23	17	11-Jul-23 A	31-Jul-23 A	
P26-BP05.20	BP - RCD Drilling	10-Jun-23	15-Jul-23	5	01-Aug-23 A	07-Aug-23 A	
P26-BP05.30	BP - Airlift, Cage Install and Concrete	17-Jul-23	25-Jul-23	6	08-Aug-23 A	15-Aug-23 A	

**VD02**

P30-BP75.30	BP - Airlift, Cage Install and Concrete	10-May-23	18-May-23	8	26-Jul-23 A	04-Aug-23 A	
-------------	---	-----------	-----------	---	-------------	-------------	--

**06**

P26-BP04.20	BP - RCD Drilling	02-Jun-23	07-Jul-23	13	21-Jul-23 A	05-Aug-23 A	
P26-BP04.30	BP - Airlift, Cage Install and Concrete	08-Jul-23	17-Jul-23	10	07-Aug-23 A	18-Aug-23 A	

**VD08**


P28&P29-BP26.:	BP - Airlift, Cage Install and Concrete	21-Sep-23	29-Sep-23	9	20-Jul-23 A	31-Jul-23 A	
----------------	---	-----------	-----------	---	-------------	-------------	--

**03**

P24&P27-BP32.:	BP - Excavation	03-Feb-23	09-Feb-23	14	19-Jul-23 A	04-Aug-23 A	
P24&P27-BP32.:	BP - RCD Drilling	10-Feb-23	15-Mar-23	9	05-Aug-23 A	16-Aug-23 A	
P24&P27-BP32.:	BP - Airlift, Cage Install and Concrete	16-Mar-23	24-Mar-23	13	17-Aug-23 A	31-Aug-23	-52

**05**

P24&P27-BP19.:	BP - Excavation	17-Apr-23	22-Apr-23	21	22-Jul-23 A	16-Aug-23 A	
P24&P27-BP19.:	BP - RCD Drilling	24-Apr-23	29-May-23	5	17-Aug-23 A	23-Aug-23 A	
P24&P27-BP19.:	BP - Airlift, Cage Install and Concrete	30-May-23	07-Jun-23	7	24-Aug-23 A	31-Aug-23	-51

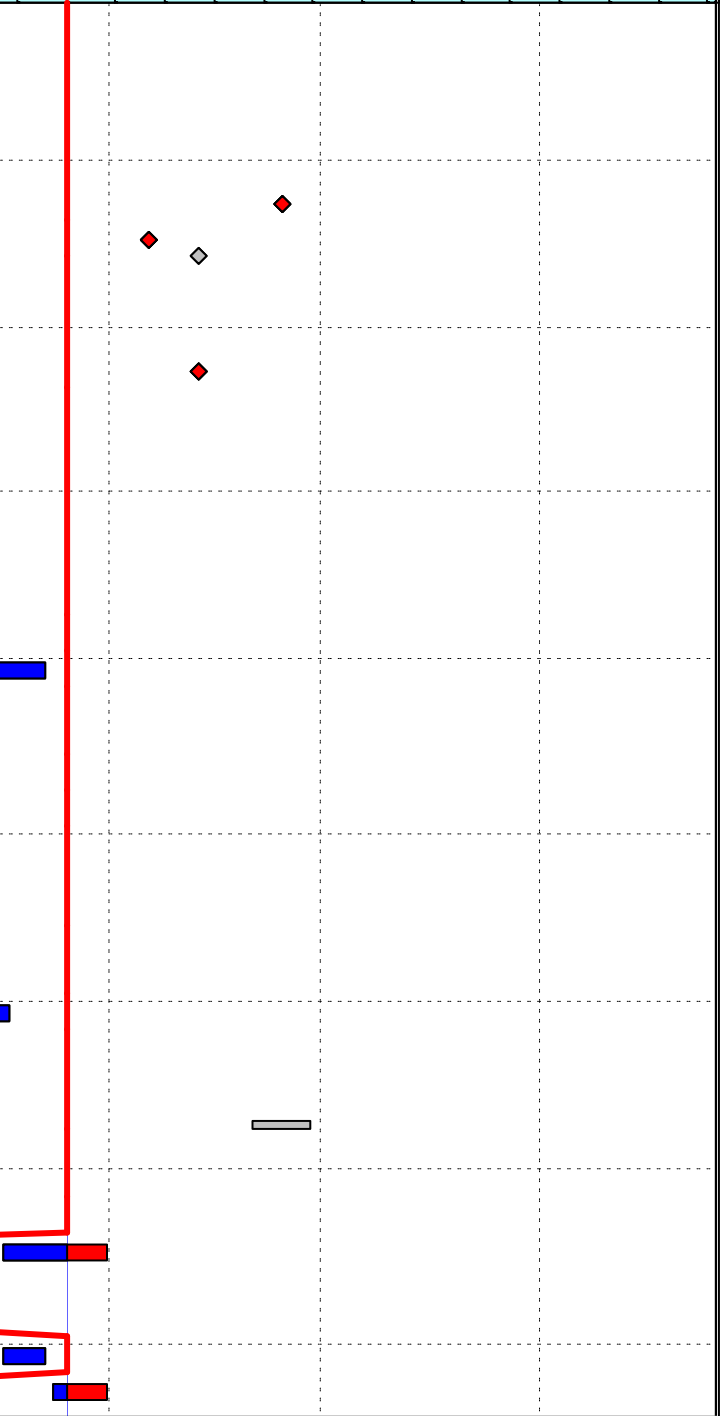

ID: 2BC-20230825\_bw  
 Data Date: 26-Aug-23  
 Print Date: 28-Aug-23\_10:55  
 Page 1 of 5

	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS

**West Kowloon Cultural District Authority**  
**Piling for Integrated Basement and U/G Road in Zone 2B 2C**  
**3 Month Rolling Programme as of 25 August 2023**  
**Based on CMWP Rev.0 (3rd Draft)**

Date	Revision	Checked	Approved
04-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	August				September				October				November		
								26				27				28				29		
								29	05	12	19	26	02	09	16	23	30	07	14	21	28	04

**KD09 (Section 5)**

**Bored Piles**

**TD01**

P18-BP40.20	BP - RCD Drilling	24-May-23	10-Jun-23	17	17-Jul-23 A	05-Aug-23 A	
P18-BP40.30	BP - Airlift, Cage Install and Concrete	12-Jun-23	19-Jun-23	6	07-Aug-23 A	14-Aug-23 A	
P18-BP62.10	BP - Excavation	11-Feb-23	17-Feb-23	18	15-Jul-23 A	05-Aug-23 A	
P18-BP62.20	BP - RCD Drilling	18-Feb-23	11-Mar-23	5	07-Aug-23 A	12-Aug-23 A	
P18-BP62.30	BP - Airlift, Cage Install and Concrete	13-Mar-23	21-Mar-23	6	14-Aug-23 A	21-Aug-23 A	
<b>02</b>							
P18-BP57.10	BP - Excavation	22-Dec-22	30-Dec-22	24	26-Jul-23 A	23-Aug-23 A	
P18-BP57.20	BP - RCD Drilling	31-Dec-22	25-Jan-23	7	24-Aug-23 A	31-Aug-23	-130
P18-BP57.30	BP - Airlift, Cage Install and Concrete	26-Jan-23	04-Feb-23	5	01-Sep-23	06-Sep-23	-130
<b>06</b>							
P18-BP45.10	BP - Excavation	28-Mar-23	03-Apr-23	22	26-Jul-23 A	21-Aug-23 A	
P18-BP45.20	BP - RCD Drilling	04-Apr-23	29-Apr-23	14	22-Aug-23 A	06-Sep-23	-138
P18-BP45.30	BP - Airlift, Cage Install and Concrete	02-May-23	10-May-23	8	07-Sep-23	15-Sep-23	-138
<b>10</b>							
P18-BP46.10	BP - Excavation	28-Jun-23	05-Jul-23	23	29-Jul-23 A	25-Aug-23 A	
P18-BP46.20	BP - RCD Drilling	06-Jul-23	22-Jul-23	9	26-Aug-23 A	05-Sep-23	-131
P18-BP46.30	BP - Airlift, Cage Install and Concrete	24-Jul-23	31-Jul-23	2	06-Sep-23	07-Sep-23	-131

**TD02**


P23-BP82.30	BP - Airlift, Cage Install and Concrete	20-Jan-23	01-Feb-23	7	24-Jul-23 A	01-Aug-23 A	
-------------	---	-----------	-----------	---	-------------	-------------	--

**TD03**

P23-BP66.30	BP - Airlift, Cage Install and Concrete	06-Jun-23	14-Jun-23	11	22-Jul-23 A	04-Aug-23 A	
-------------	---	-----------	-----------	----	-------------	-------------	--


**TD04**

P18-BP37.30	BP - Airlift, Cage Install and Concrete	11-Mar-23	20-Mar-23	8	19-Jul-23 A	28-Jul-23 A	
P23-BP75.10	BP - Excavation	22-Apr-23	28-Apr-23	18	07-Jul-23 A	28-Jul-23 A	
P23-BP75.20	BP - RCD Drilling	29-Apr-23	22-May-23	4	29-Jul-23 A	03-Aug-23 A	
P23-BP75.30	BP - Airlift, Cage Install and Concrete	23-May-23	01-Jun-23	6	04-Aug-23 A	11-Aug-23 A	
<b>02</b>							
P18-BP49.10	BP - Excavation	21-Dec-22	29-Dec-22	29	08-Jul-23 A	11-Aug-23 A	
P18-BP49.20	BP - RCD Drilling	30-Dec-22	21-Jan-23	7	12-Aug-23 A	21-Aug-23 A	
P18-BP49.30	BP - Airlift, Cage Install and Concrete	25-Jan-23	03-Feb-23	12	22-Aug-23 A	04-Sep-23	-128
<b>05</b>							
P18-BP50.10	BP - Excavation	04-Mar-23	10-Mar-23	21	31-Jul-23 A	24-Aug-23 A	

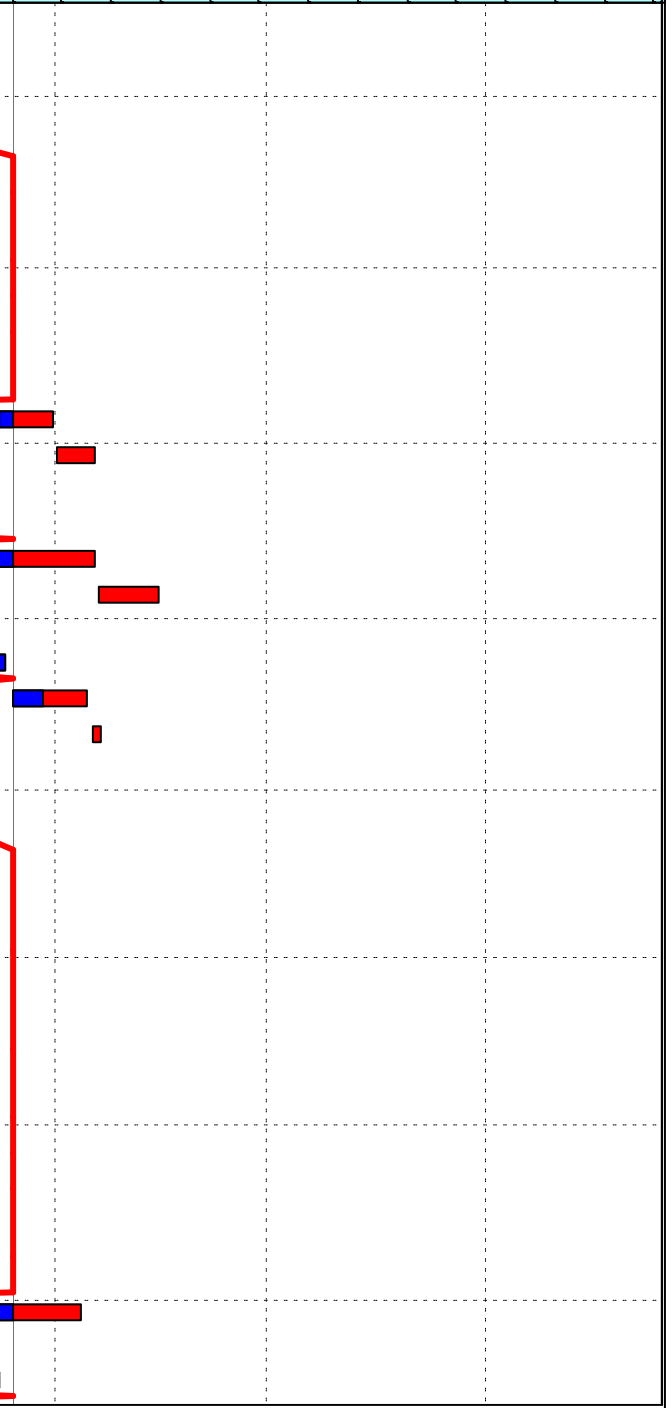

	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS

Date	Revision	Checked	Approved
04-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C

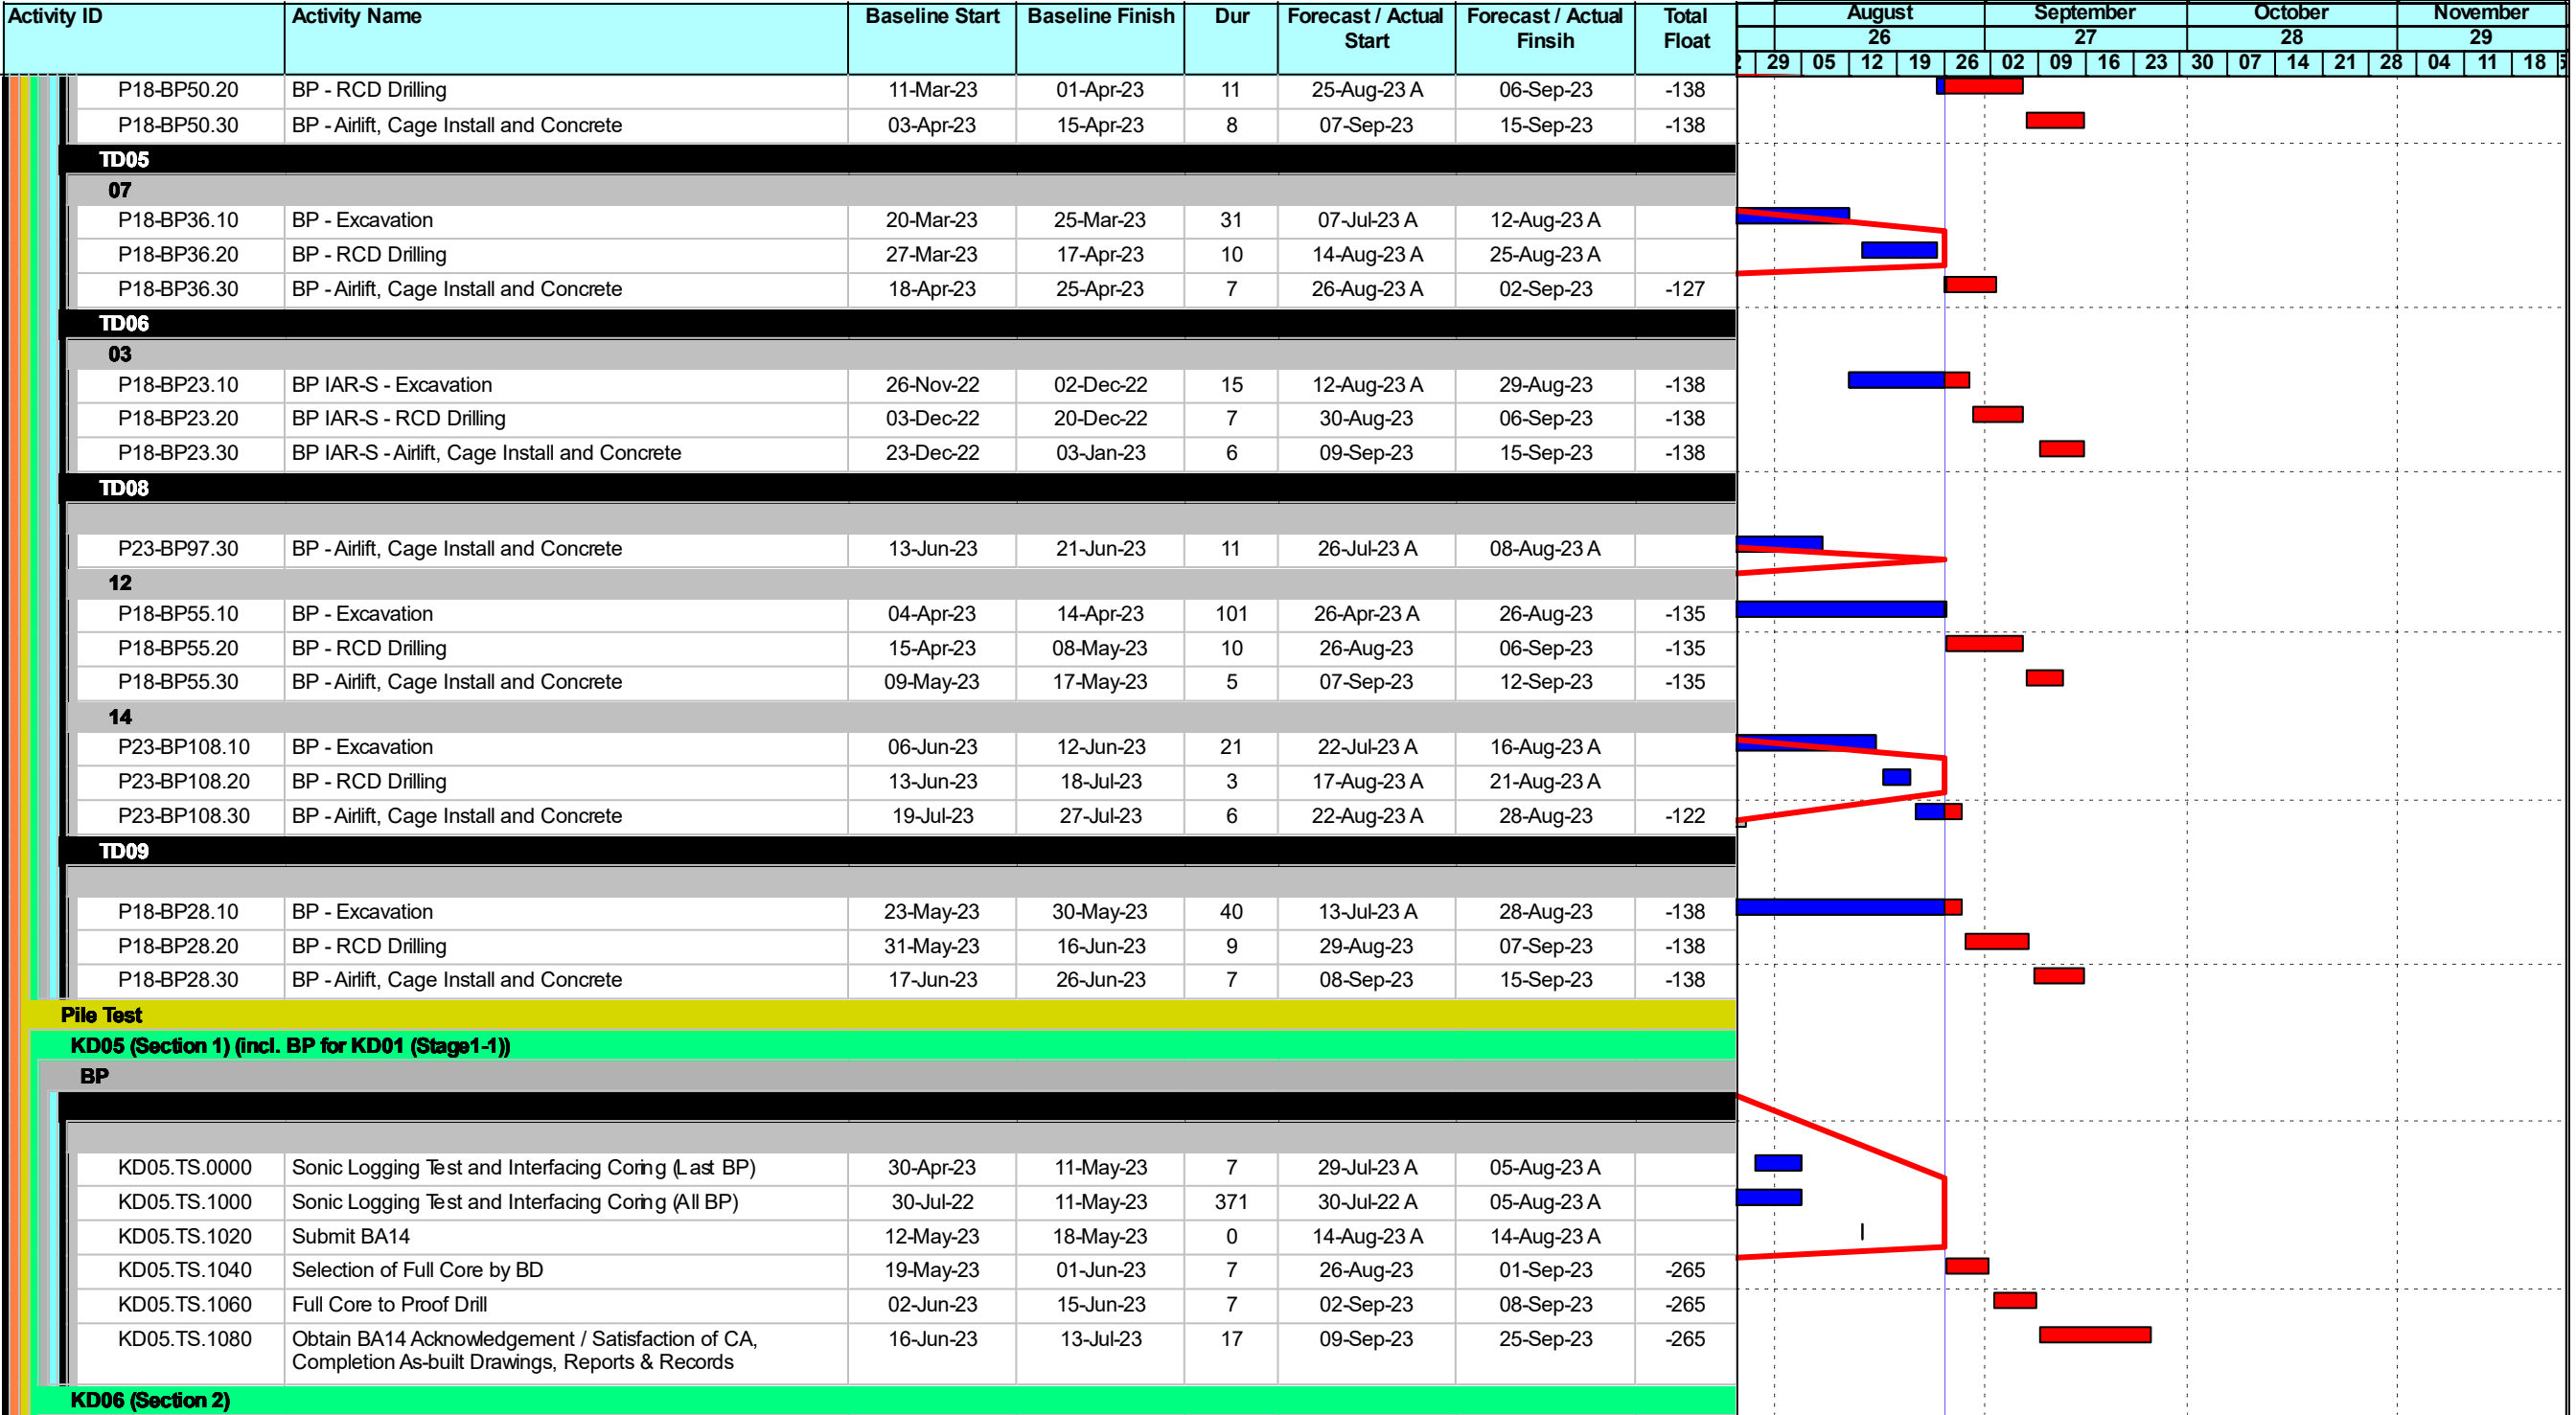

	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS

**West Kowloon Cultural District Authority**  
**Piling for Integrated Basement and U/G Road in Zone 2B 2C**  
**3 Month Rolling Programme as of 25 August 2023**  
**Based on CMWP Rev.0 (3rd Draft)**

	Date	Revision	Checked	Approved
	04-Mar-22	R0	KL	B
	02-Dec-22	R03D	KL	C

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	August				September				October				November		
								26	29	05	12	19	26	02	09	16	23	30	07	14	21	28

**BP**

KD06.TS.1020	Submit BA14	13-Jul-23	19-Jul-23	29	28-Jul-23 A	26-Aug-23	-86
KD06.TS.1040	Selection of Full Core by BD	20-Jul-23	02-Aug-23	0	26-Aug-23	26-Aug-23	-86
KD06.TS.1060	Full Core to Proof Drill	03-Aug-23	16-Aug-23	5	26-Aug-23	30-Aug-23	-86
KD06.TS.1080	Obtain BA14 Acknowledgement / Satisfaction of CA, Completion As-built Drawings, Reports & Records	17-Aug-23	13-Sep-23	7	31-Aug-23	06-Sep-23	-86

**KD07 (Section 3) (incl. BP for KD03) (Stage 3-1)**

**BP**

KD07.TS.0000	Sonic Logging Test and Interfacing Coring (Last BP)	30-Sep-23	11-Oct-23	12	02-Sep-23	13-Sep-23	-60
KD07.TS.1000	Sonic Logging Test and Interfacing Coring (All BP)	14-Jun-23	11-Oct-23	278	10-Dec-22 A	13-Sep-23	-60
KD07.TS.1020	Submit BA14	12-Oct-23	18-Oct-23	7	14-Sep-23	20-Sep-23	-60
KD07.TS.1040	Selection of Full Core by BD	19-Oct-23	01-Nov-23	14	21-Sep-23	04-Oct-23	-60
KD07.TS.1060	Full Core to Proof Drill	02-Nov-23	15-Nov-23	28	05-Oct-23	01-Nov-23	-60
KD07.TS.1080	Obtain BA14 Acknowledgement / Satisfaction of CA, Completion As-built Drawings, Reports & Records	16-Nov-23	13-Dec-23	28	02-Nov-23	29-Nov-23	-60

**KD08 (Section 4) (incl. BP for KD04 (Stage 4-1) & SSHP in KD09 (Section 5))**

**BP**

KD08.TS.0000	Sonic Logging Test and Interfacing Coring (Last BP)	31-May-23	11-Jun-23	12	15-Jul-23 A	27-Jul-23 A	
KD08.TS.1000	Sonic Logging Test and Interfacing Coring (All BP)	04-Jul-22	11-Jun-23	388	04-Jul-22 A	27-Jul-23 A	
KD08.TS.1020	Submit BA14	12-Jun-23	18-Jun-23	0	17-Aug-23 A	17-Aug-23 A	
KD08.TS.1040	Selection of Full Core by BD	19-Jun-23	02-Jul-23	5	26-Aug-23	30-Aug-23	-113
KD08.TS.1060	Full Core to Proof Drill	03-Jul-23	16-Jul-23	7	31-Aug-23	06-Sep-23	-113
KD08.TS.1080	Obtain BA14 Acknowledgement / Satisfaction of CA, Completion As-built Drawings, Reports & Records	17-Jul-23	13-Aug-23	7	07-Sep-23	13-Sep-23	-113


**SSHP**

KD08.TS.1180	Obtain BA14 Acknowledgement / Satisfaction of CA, Completion As-built Drawings, Reports & Records	20-Dec-22	16-Jan-23	7	26-Aug-23	01-Sep-23	-102
--------------	---	-----------	-----------	---	-----------	-----------	------

**KD09 (Section 5) (incl. BP for KD02 (Stage 5-1))**

**BP**



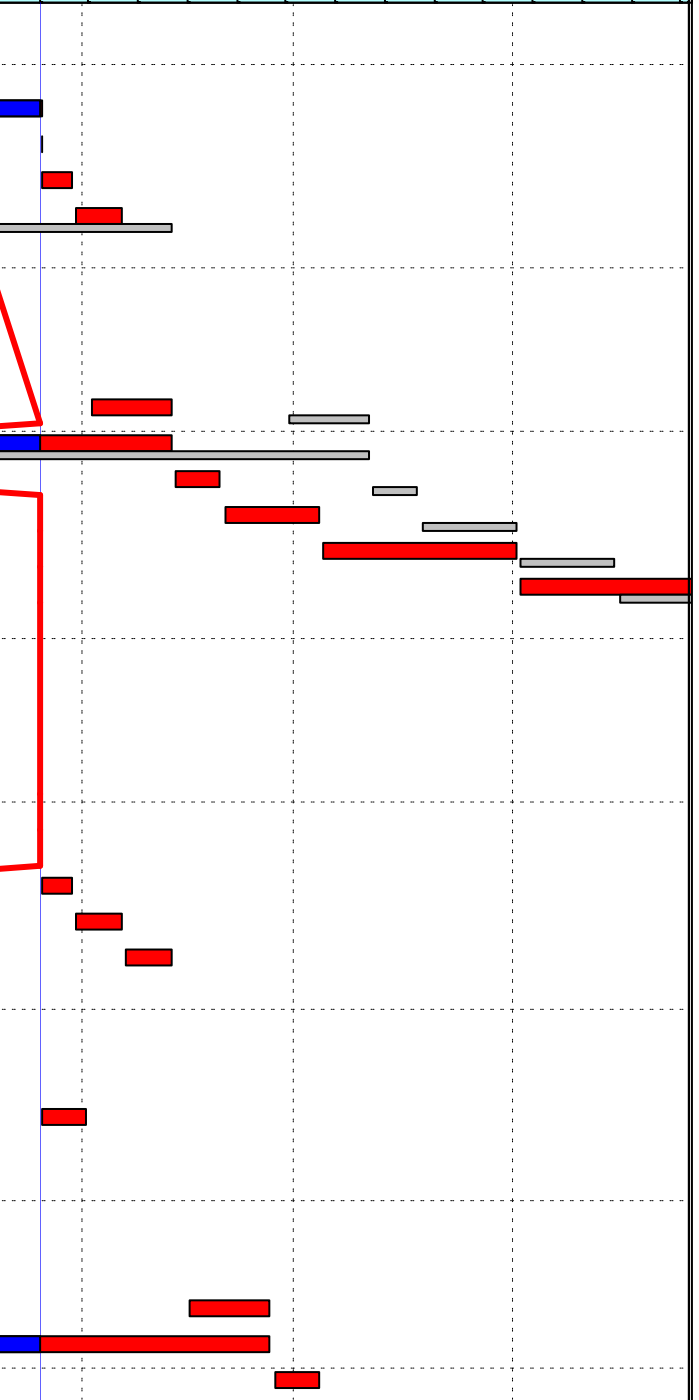



KD09.TS.0000	Sonic Logging Test and Interfacing Coring (Last BP)	01-Aug-23	12-Aug-23	12	16-Sep-23	27-Sep-23	-170
KD09.TS.1000	Sonic Logging Test and Interfacing Coring (All BP)	23-May-22	12-Aug-23	493	23-May-22 A	27-Sep-23	-170
KD09.TS.1020	Submit BA14	13-Aug-23	19-Aug-23	7	28-Sep-23	04-Oct-23	-170



Planned	Planned MS
Critical	Critical MS
Actual	Actual MS

Date	Revision	Checked	Approved
04-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	August				September				October				November			
								26				27				28				29			
								29	05	12	19	26	02	09	16	23	30	07	14	21	28	04	11
KD09.TS.1040	Selection of Full Core by BD	20-Aug-23	02-Sep-23	14	05-Oct-23	18-Oct-23	-170																
KD09.TS.1060	Full Core to Proof Drill	03-Sep-23	16-Sep-23	14	19-Oct-23	01-Nov-23	-170																
KD09.TS.1080	Obtain BA14 Acknowledgement / Satisfaction of CA, Completion As-built Drawings, Reports & Records	17-Sep-23	14-Oct-23	28	02-Nov-23	29-Nov-23	-170																

	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS

**West Kowloon Cultural District Authority**  
**Piling for Integrated Basement and U/G Road in Zone 2B 2C**  
**3 Month Rolling Programme as of 25 August 2023**  
**Based on CMWP Rev.0 (3rd Draft)**



Date	Revision	Checked	Approved
04-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C
