


Zone 2B & 2C

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	September				October				November				December			
								27				28				29				30			
								02	09	16	23	30	07	14	21	28	04	11	18	25	02	09	16

Piling for Integrated Basement and U/G Road in Zone 2B & 2C

Contract Dates								
Key Dates								
KD for Zone 2B								
KD05	KD05 (Section 1) - 03 Jan 2023			13-Jul-23	0	30-Sep-23*	-269	
KD06	KD06 (Section 2) - 12 Jun 2023			13-Sep-23	0	30-Sep-23*	-109	
KD07	KD07 (Section 3) - 30 Sep 2023			13-Dec-23	0	29-Nov-23*	-60	
KD for Zone 2C								
KD08	KD08 (Section 4) - 23 May 2023			13-Aug-23	0	30-Sep-23*	-129	
KD09	KD09 (Section 5) - 12 Jun 2023			14-Oct-23	0	29-Nov-23*	-170	
Construction Stage								
Pile Construction								
KD07 (Section 3)								
Bored Piles								
VD01								
P26-BP07.30	BP - Airlift, Cage Install and Concrete			10-Jun-23	19-Jun-23	8	14-Aug-23 A	23-Aug-23 A
VD08								
03								
P24&P27-BP32.:	BP - Airlift, Cage Install and Concrete			16-Mar-23	24-Mar-23	9	17-Aug-23 A	28-Aug-23 A
05								
P24&P27-BP19.:	BP - RCD Drilling			24-Apr-23	29-May-23	5	17-Aug-23 A	23-Aug-23 A
P24&P27-BP19.:	BP - Airlift, Cage Install and Concrete			30-May-23	07-Jun-23	6	24-Aug-23 A	31-Aug-23 A
KD09 (Section 5)								
Bored Piles								
TD01								
02								
P18-BP57.10	BP - Excavation			22-Dec-22	30-Dec-22	24	26-Jul-23 A	23-Aug-23 A
P18-BP57.20	BP - RCD Drilling			31-Dec-22	25-Jan-23	6	24-Aug-23 A	31-Aug-23 A
P18-BP57.30	BP - Airlift, Cage Install and Concrete			26-Jan-23	04-Feb-23	7	01-Sep-23 A	09-Sep-23 A
06								
P18-BP45.20	BP - RCD Drilling			04-Apr-23	29-Apr-23	12	22-Aug-23 A	05-Sep-23 A
P18-BP45.30	BP - Airlift, Cage Install and Concrete			02-May-23	10-May-23	7	06-Sep-23 A	14-Sep-23 A
10								
P18-BP46.10	BP - Excavation			28-Jun-23	05-Jul-23	23	29-Jul-23 A	25-Aug-23 A
P18-BP46.20	BP - RCD Drilling			06-Jul-23	22-Jul-23	4	26-Aug-23 A	31-Aug-23 A
P18-BP46.30	BP - Airlift, Cage Install and Concrete			24-Jul-23	31-Jul-23	9	01-Sep-23 A	12-Sep-23 A
TD04								

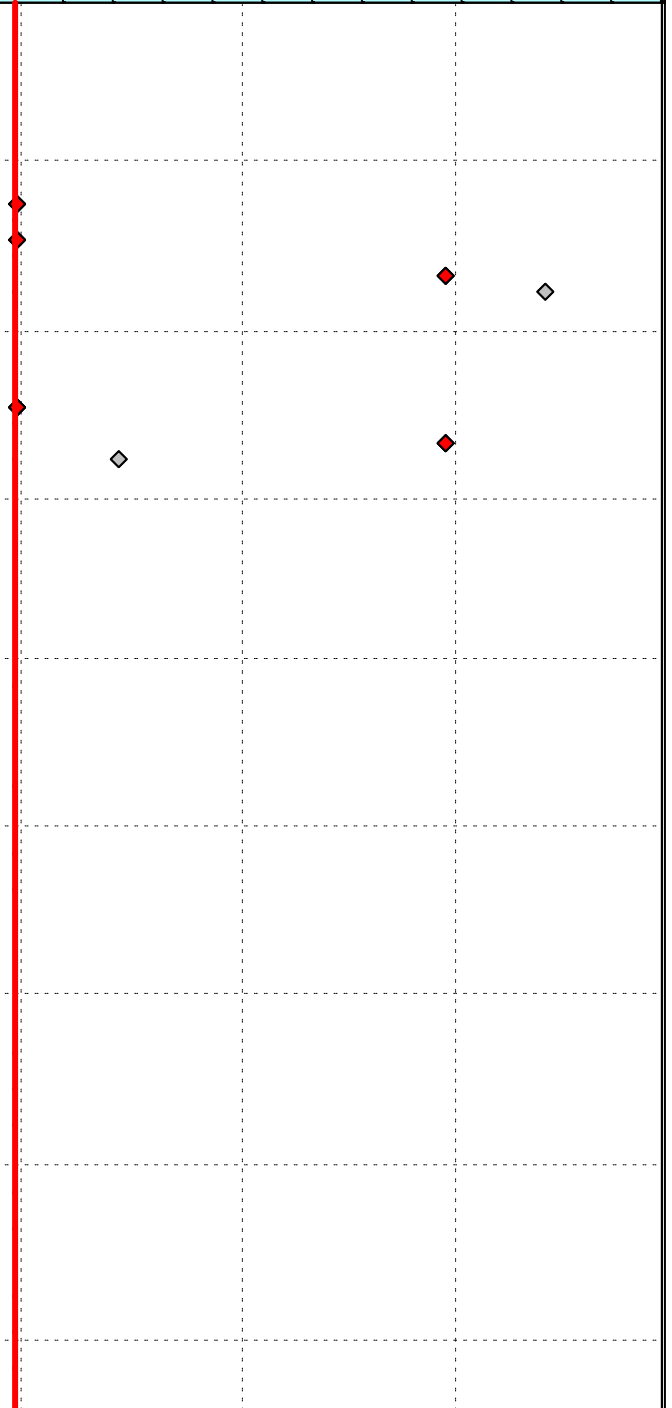

	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS



Date	Revision	Checked	Approved
04-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	September				October				November				December				
								27				28				29				30				
								02	09	16	23	30	07	14	21	28	04	11	18	25	02	09	16	23
02																								
P18-BP49.30	BP - Airlift, Cage Install and Concrete	25-Jan-23	03-Feb-23	13	22-Aug-23 A	06-Sep-23 A																		
05																								
P18-BP50.10	BP - Excavation	04-Mar-23	10-Mar-23	21	31-Jul-23 A	24-Aug-23 A																		
P18-BP50.20	BP - RCD Drilling	11-Mar-23	01-Apr-23	15	25-Aug-23 A	12-Sep-23 A																		
P18-BP50.30	BP - Airlift, Cage Install and Concrete	03-Apr-23	15-Apr-23	6	13-Sep-23 A	19-Sep-23 A																		
TD05																								
07																								
P18-BP36.20	BP - RCD Drilling	27-Mar-23	17-Apr-23	10	14-Aug-23 A	25-Aug-23 A																		
P18-BP36.30	BP - Airlift, Cage Install and Concrete	18-Apr-23	25-Apr-23	4	26-Aug-23 A	31-Aug-23 A																		
TD06																								
03																								
P18-BP23.30	BP IAR-S - Airlift, Cage Install and Concrete	23-Dec-22	03-Jan-23	5	19-Aug-23 A	25-Aug-23 A																		
TD08																								
P23-BP108.30	BP - Airlift, Cage Install and Concrete	19-Jul-23	27-Jul-23	5	22-Aug-23 A	28-Aug-23 A																		
12																								
P18-BP55.10	BP - Excavation	04-Apr-23	14-Apr-23	113	26-Apr-23 A	09-Sep-23 A																		
P18-BP55.20	BP - RCD Drilling	15-Apr-23	08-May-23	9	11-Sep-23 A	21-Sep-23 A																		
P18-BP55.30	BP - Airlift, Cage Install and Concrete	09-May-23	17-May-23	6	15-Sep-23 A	21-Sep-23 A																		
TD09																								
P18-BP28.10	BP - Excavation	23-May-23	30-May-23	40	13-Jul-23 A	29-Aug-23 A																		
P18-BP28.20	BP - RCD Drilling	31-May-23	16-Jun-23	10	30-Aug-23 A	11-Sep-23 A																		
P18-BP28.30	BP - Airlift, Cage Install and Concrete	17-Jun-23	26-Jun-23	5	12-Sep-23 A	16-Sep-23 A																		
Pile Test																								
KD05 (Section 1) (incl. BP for KD01 (Stage1-1))																								
BP																								
KD05.TS.1040	Selection of Full Core by BD	19-May-23	01-Jun-23	0	30-Sep-23	30-Sep-23	-269																	
KD05.TS.1060	Full Core to Proof Drill	02-Jun-23	15-Jun-23	0	30-Sep-23	30-Sep-23	-269																	
KD05.TS.1080	Obtain BA14 Acknowledgement / Satisfaction of CA, Completion As-built Drawings, Reports & Records	16-Jun-23	13-Jul-23	0	30-Sep-23	30-Sep-23	-269																	
KD06 (Section 2)																								
BP																								
KD06.TS.1040	Selection of Full Core by BD	20-Jul-23	02-Aug-23	0	30-Sep-23	30-Sep-23	-109																	
KD06.TS.1060	Full Core to Proof Drill	03-Aug-23	16-Aug-23	0	30-Sep-23	30-Sep-23	-109																	
KD06.TS.1080	Obtain BA14 Acknowledgement / Satisfaction of CA, Compl	17-Aug-23	13-Sep-23	0	30-Sep-23	30-Sep-23	-109																	
KD07 (Section 3) (incl. BP for KD03) (Stage 3-1)																								

- Planned
- Critical
- Actual
- Planned MS
- Critical MS
- Actual MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 29 September 2023
 Based on CMWP Rev.0 (3rd Draft)



Date	Revision	Checked	Approved
04-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	September				October				November				December			
								27				28				29				30			
								02	09	16	23	30	07	14	21	28	04	11	18	25	02	09	16
BP																							
KD07.TS.0000	Sonic Logging Test and Interfacing Coring (Last BP)	30-Sep-23	11-Oct-23	0	30-Sep-23	30-Sep-23	-58																
KD07.TS.1000	Sonic Logging Test and Interfacing Coring (All BP)	14-Jun-23	11-Oct-23	296	10-Dec-22 A	01-Oct-23	-60																
KD07.TS.1020	Submit BA14	12-Oct-23	18-Oct-23	0	02-Oct-23	02-Oct-23	-60																
KD07.TS.1040	Selection of Full Core by BD	19-Oct-23	01-Nov-23	3	02-Oct-23	04-Oct-23	-60																
KD07.TS.1060	Full Core to Proof Drill	02-Nov-23	15-Nov-23	28	05-Oct-23	01-Nov-23	-60																
KD07.TS.1080	Obtain BA14 Acknowledgement / Satisfaction of CA, Compli	16-Nov-23	13-Dec-23	28	02-Nov-23	29-Nov-23	-60																
KD08 (Section 4) (incl. BP for KD04 (Stage 4-1) & SSHP in KD09 (Section 5))																							
BP																							
KD08.TS.1040	Selection of Full Core by BD	19-Jun-23	02-Jul-23	0	30-Sep-23	30-Sep-23	-129																
KD08.TS.1060	Full Core to Proof Drill	03-Jul-23	16-Jul-23	0	30-Sep-23	30-Sep-23	-129																
KD08.TS.1080	Obtain BA14 Acknowledgement / Satisfaction of CA, Compli	17-Jul-23	13-Aug-23	0	30-Sep-23	30-Sep-23	-129																
SSHP																							
KD08.TS.1180	Obtain BA14 Acknowledgement / Satisfaction of CA, Compli	20-Dec-22	16-Jan-23	0	30-Sep-23	30-Sep-23	-130																
KD09 (Section 5) (incl. BP for KD02 (Stage 5-1))																							
BP																							
KD09.TS.0000	Sonic Logging Test and Interfacing Coring (Last BP)	01-Aug-23	12-Aug-23	1	30-Sep-23	30-Sep-23	-170																
KD09.TS.1000	Sonic Logging Test and Interfacing Coring (All BP)	23-May-22	12-Aug-23	496	23-May-22 A	01-Oct-23	-170																
KD09.TS.1020	Submit BA14	13-Aug-23	19-Aug-23	4	01-Oct-23	04-Oct-23	-170																
KD09.TS.1040	Selection of Full Core by BD	20-Aug-23	02-Sep-23	14	05-Oct-23	18-Oct-23	-170																
KD09.TS.1060	Full Core to Proof Drill	03-Sep-23	16-Sep-23	14	19-Oct-23	01-Nov-23	-170																
KD09.TS.1080	Obtain BA14 Acknowledgement / Satisfaction of CA, Compli	17-Sep-23	14-Oct-23	28	02-Nov-23	29-Nov-23	-170																

	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS



Date	Revision	Checked	Approved
04-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C
