


Zone 2B & 2C

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	October					November					December				January											
								28	29	30	01	02	03	04	05	06	07	08	09	10	11	12	13	14	15	16	17	18	19	20	21	22	23

Piling for Integrated Basement and U/G Road in Zone 2B & 2C

Contract Dates								
Key Dates								
KD for Zone 2B								
KD05	KD05 (Section 1) - 03 Jan 2023			13-Jul-23	0	21-Oct-23*	-290	
KD06	KD06 (Section 2) - 12 Jun 2023			13-Sep-23	0	21-Oct-23*	-130	
KD07	KD07 (Section 3) - 30 Sep 2023			13-Dec-23	0	29-Nov-23*	-60	
KD for Zone 2C								
KD08	KD08 (Section 4) - 23 May 2023			13-Aug-23	0	21-Oct-23*	-150	
KD09	KD09 (Section 5) - 12 Jun 2023			14-Oct-23	0	29-Nov-23*	-170	
KD for Zone 2B (Optional Items)								
KD10	KD10 (Section 6) (Tree felling at Austin Road West) (180 days after CA's Instruction) (Optional Works Item No.1A)			30-Jul-23	0	21-Oct-23*	-81	
KD for Zone 2C (Optional Items)								
KD11	KD11 (Section 7) (Tree felling at Zone 2C) (180 days after CA's Instruction) (Optional Works Item No.1B)			30-Jul-23	0	21-Oct-23*	-81	
Construction Stage								
Pile Construction								
KD09 (Section 5)								
Bored Piles								
TD01								
P18-BP45.30	BP - Airlift, Cage Install and Concrete			02-May-23	10-May-23	7	06-Sep-23 A	14-Sep-23 A
TD04								
05								
P18-BP50.30	BP - Airlift, Cage Install and Concrete			03-Apr-23	15-Apr-23	6	13-Sep-23 A	19-Sep-23 A
TD08								
P18-BP55.20	BP - RCD Drilling			15-Apr-23	08-May-23	9	11-Sep-23 A	21-Sep-23 A
P18-BP55.30	BP - Airlift, Cage Install and Concrete			09-May-23	17-May-23	6	15-Sep-23 A	21-Sep-23 A
TD09								
P18-BP28.30	BP - Airlift, Cage Install and Concrete			17-Jun-23	26-Jun-23	5	12-Sep-23 A	16-Sep-23 A
Pile Test								
KD05 (Section 1) (incl. BP for KD01 (Stage1-1))								

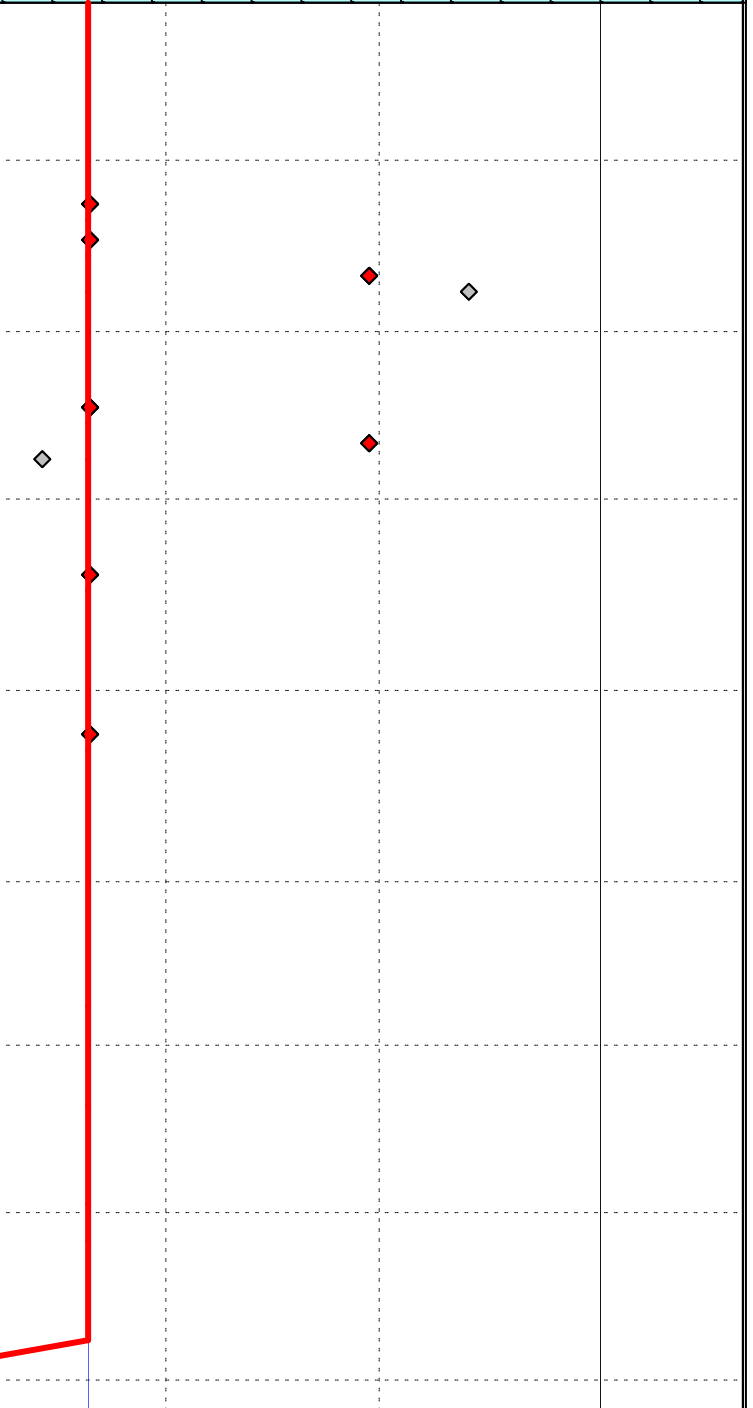

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	October					November					December				January		
								28					29					30				31		
								8	25	02	09	16	23	30	06	13	20	27	04	11	18	25	01	08

BP

KD05.TS.1040	Selection of Full Core by BD	19-May-23	01-Jun-23	0	21-Oct-23	21-Oct-23	-290
KD05.TS.1060	Full Core to Proof Drill	02-Jun-23	15-Jun-23	0	21-Oct-23	21-Oct-23	-290
KD05.TS.1080	Obtain BA14 Acknowledgement / Satisfaction of CA, Completion As-built Drawings, Reports & Records	16-Jun-23	13-Jul-23	0	21-Oct-23	21-Oct-23	-290

KD06 (Section 2)

BP

KD06.TS.1040	Selection of Full Core by BD	20-Jul-23	02-Aug-23	0	21-Oct-23	21-Oct-23	-130
KD06.TS.1060	Full Core to Proof Drill	03-Aug-23	16-Aug-23	0	21-Oct-23	21-Oct-23	-130
KD06.TS.1080	Obtain BA14 Acknowledgement / Satisfaction of CA, Completion As-built Drawings, Reports & Records	17-Aug-23	13-Sep-23	0	21-Oct-23	21-Oct-23	-130

KD07 (Section 3) (incl. BP for KD03) (Stage 3-1)

BP

KD07.TS.0000	Sonic Logging Test and Interfacing Coring (Last BP)	30-Sep-23	11-Oct-23	15	11-Sep-23 A	26-Sep-23 A	
KD07.TS.1000	Sonic Logging Test and Interfacing Coring (All BP)	14-Jun-23	11-Oct-23	291	10-Dec-22 A	26-Sep-23 A	
KD07.TS.1020	Submit BA14	12-Oct-23	18-Oct-23	1	21-Oct-23	21-Oct-23	-60
KD07.TS.1040	Selection of Full Core by BD	19-Oct-23	01-Nov-23	11	22-Oct-23	01-Nov-23	-60
KD07.TS.1060	Full Core to Proof Drill	02-Nov-23	15-Nov-23	14	02-Nov-23	15-Nov-23	-60
KD07.TS.1080	Obtain BA14 Acknowledgement / Satisfaction of CA, Completion As-built Drawings, Reports & Records	16-Nov-23	13-Dec-23	14	16-Nov-23	29-Nov-23	-60

KD08 (Section 4) (incl. BP for KD04 (Stage 4-1) & SSHP in KD09 (Section 5))

BP

KD08.TS.1040	Selection of Full Core by BD	19-Jun-23	02-Jul-23	0	21-Oct-23	21-Oct-23	-150
KD08.TS.1060	Full Core to Proof Drill	03-Jul-23	16-Jul-23	0	21-Oct-23	21-Oct-23	-150
KD08.TS.1080	Obtain BA14 Acknowledgement / Satisfaction of CA, Completion As-built Drawings, Reports & Records	17-Jul-23	13-Aug-23	0	21-Oct-23	21-Oct-23	-150


SSHP

KD08.TS.1180	Obtain BA14 Acknowledgement / Satisfaction of CA, Completion As-built Drawings, Reports & Records	20-Dec-22	16-Jan-23	0	21-Oct-23	21-Oct-23	-151
--------------	---	-----------	-----------	---	-----------	-----------	------





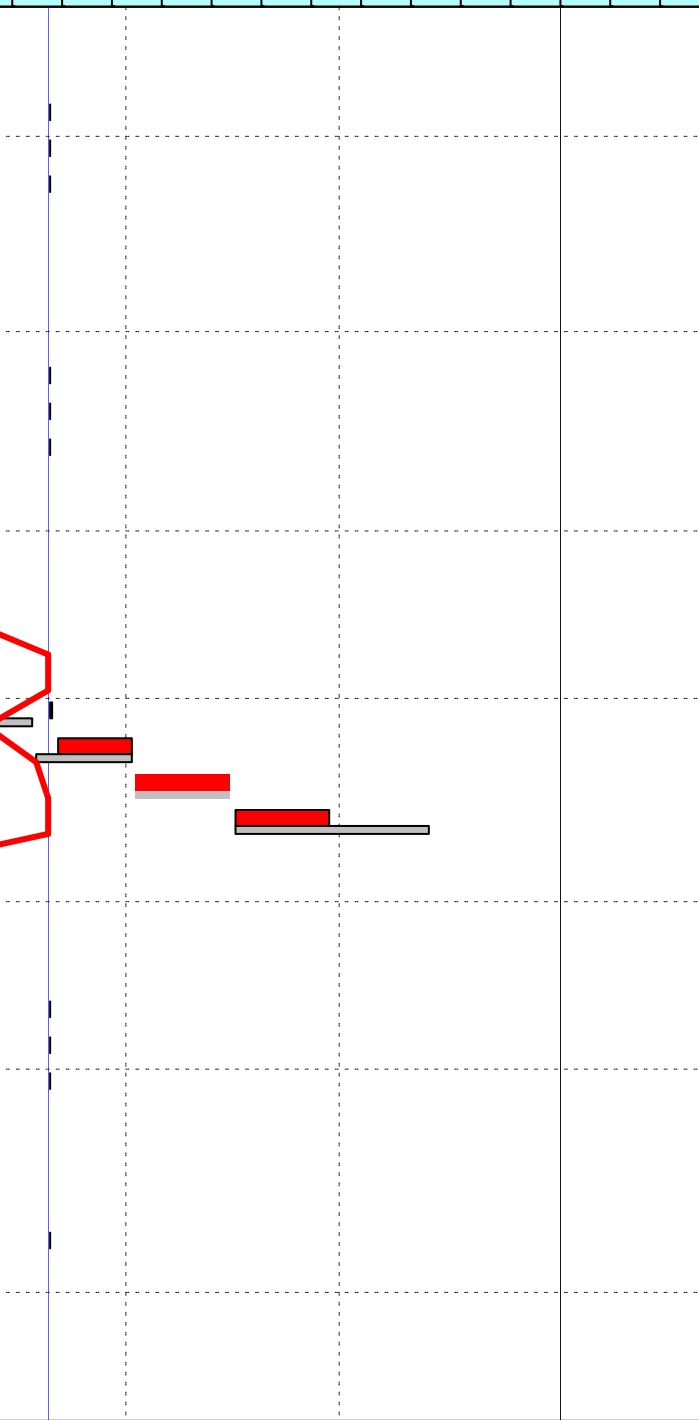

KD09 (Section 5) (incl. BP for KD02 (Stage 5-1))

BP

--	--	--	--	--	--	--	--



Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	October							November					December				January		
								28							29					30				31		
								8	25	02	09	16	23	30	06	13	20	27	04	11	18	25	01	08	15	
KD09.TS.0000	Sonic Logging Test and Interfacing Coring (Last BP)	01-Aug-23	12-Aug-23	149	18-May-23 A	13-Oct-23 A		[Gantt bar: 18-May-23 to 13-Oct-23]																		
KD09.TS.1000	Sonic Logging Test and Interfacing Coring (All BP)	23-May-22	12-Aug-23	508	23-May-22 A	13-Oct-23 A		[Gantt bar: 23-May-22 to 13-Oct-23]																		
KD09.TS.1020	Submit BA14	13-Aug-23	19-Aug-23	1	21-Oct-23	21-Oct-23	-170																			
KD09.TS.1040	Selection of Full Core by BD	20-Aug-23	02-Sep-23	11	22-Oct-23	01-Nov-23	-170								[Gantt bar: 22-Oct-23 to 01-Nov-23]											
KD09.TS.1060	Full Core to Proof Drill	03-Sep-23	16-Sep-23	14	02-Nov-23	15-Nov-23	-170								[Gantt bar: 02-Nov-23 to 15-Nov-23]											
KD09.TS.1080	Obtain BA14 Acknowledgement / Satisfaction of CA, Completion As-built Drawings, Reports & Records	17-Sep-23	14-Oct-23	14	16-Nov-23	29-Nov-23	-170	[Gantt bar: 17-Sep-23 to 14-Oct-23]																		

	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 20 October 2023
Based on CMWP Rev.0 (3rd Draft)

			
Date	Revision	Checked	Approved
04-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C
