

Zone 2B & 2C

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	November					December				January				February			
								29					30				31				32			
								0	06	13	20	27	04	11	18	25	01	08	15	22	29	05	12	19

Piling for Integrated Basement and U/G Road in Zone 2B & 2C

Contract Dates

Key Dates

KD for Zone 2B

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float
KD05	KD05 (Section 1) - 03 Jan 2023		13-Jul-23	0		27-Dec-23*	-358
KD06	KD06 (Section 2) - 12 Jun 2023		13-Sep-23	0		27-Dec-23*	-198
KD07	KD07 (Section 3) - 30 Sep 2023		13-Dec-23	0		27-Dec-23*	-88

KD for Zone 2C

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float
KD08	KD08 (Section 4) - 23 May 2023		13-Aug-23	0		27-Dec-23*	-218
KD09	KD09 (Section 5) - 12 Jun 2023		14-Oct-23	0		28-Dec-23*	-199

Construction Stage

Pile Test

KD05 (Section 1) (incl. BP for KD01 (Stage1-1))

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float
BP							
KD05.TS.1040	Selection of Full Core by BD	19-May-23	01-Jun-23	2	02-Dec-23	03-Dec-23	-358
KD05.TS.1060	Full Core to Proof Drill	02-Jun-23	15-Jun-23	10	04-Dec-23	13-Dec-23	-358
KD05.TS.1080	Obtain BA14 Acknowledgement / Satisfaction of CA, Completion As-built Drawings, Reports & Records	16-Jun-23	13-Jul-23	14	14-Dec-23	27-Dec-23	-358

KD06 (Section 2)


Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float
BP							
KD06.TS.1040	Selection of Full Core by BD	20-Jul-23	02-Aug-23	1	07-Nov-23 A	07-Nov-23 A	
KD06.TS.1060	Full Core to Proof Drill	03-Aug-23	16-Aug-23	19	25-Nov-23 A	13-Dec-23	-198
KD06.TS.1080	Obtain BA14 Acknowledgement / Satisfaction of CA, Completion As-built Drawings, Reports & Records	17-Aug-23	13-Sep-23	14	14-Dec-23	27-Dec-23	-198

KD07 (Section 3) (incl. BP for KD03) (Stage 3-1)

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float
BP							
KD07.TS.1040	Selection of Full Core by BD	19-Oct-23	01-Nov-23	4	02-Dec-23	05-Dec-23	-88
KD07.TS.1060	Full Core to Proof Drill	02-Nov-23	15-Nov-23	8	06-Dec-23	13-Dec-23	-88
KD07.TS.1080	Obtain BA14 Acknowledgement / Satisfaction of CA, Completion As-built Drawings, Reports & Records	16-Nov-23	13-Dec-23	14	14-Dec-23	27-Dec-23	-88

KD08 (Section 4) (incl. BP for KD04 (Stage 4-1) & SSHP in KD09 (Section 5))



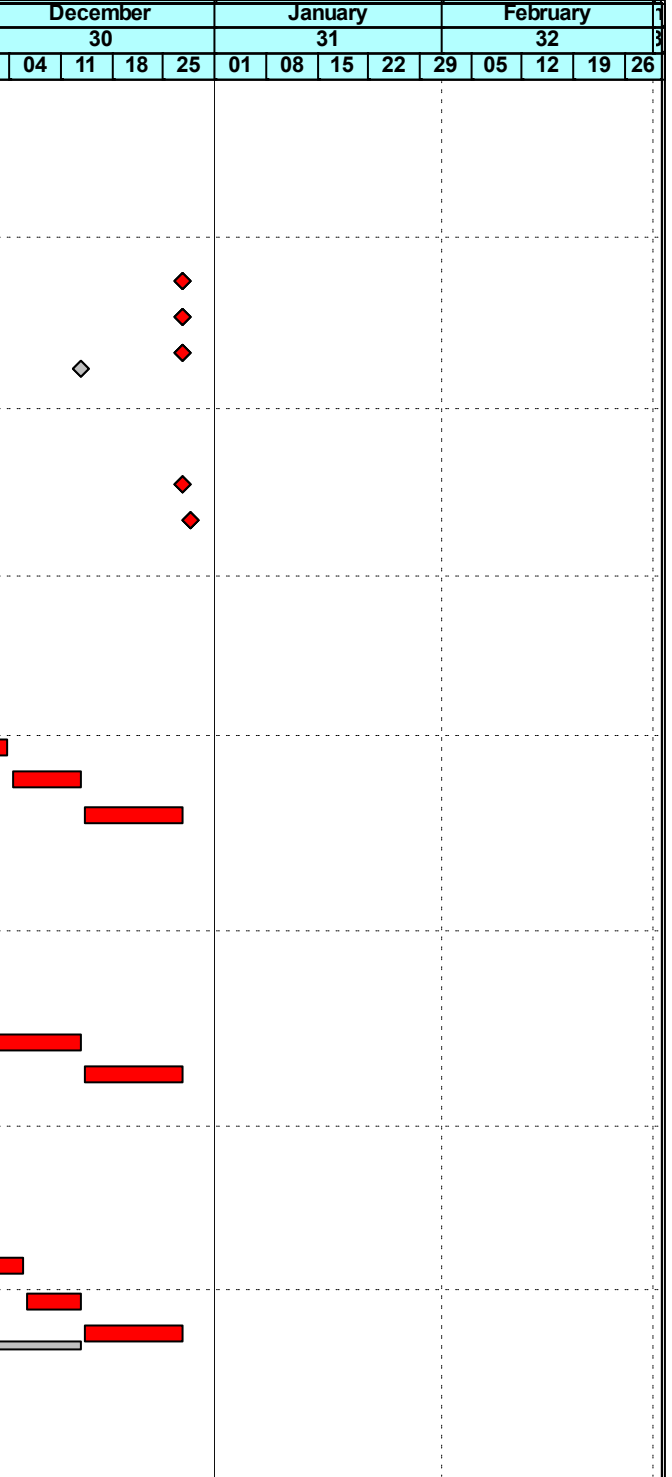



Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float
BP							



	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS

Date	Revision	Checked	Approved
04-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	November				December				January				February				
								29				30				31				32				
								0	06	13	20	27	04	11	18	25	01	08	15	22	29	05	12	19
KD08.TS.1040	Selection of Full Core by BD	19-Jun-23	02-Jul-23	1	07-Nov-23 A	07-Nov-23 A																		
KD08.TS.1060	Full Core to Proof Drill	03-Jul-23	16-Jul-23	18	26-Nov-23 A	13-Dec-23	-218																	
KD08.TS.1080	Obtain BA14 Acknowledgement / Satisfaction of CA, Completion As-built Drawings, Reports & Records	17-Jul-23	13-Aug-23	14	14-Dec-23	27-Dec-23	-218																	
SSHP																								
KD08.TS.1180	Obtain BA14 Acknowledgement / Satisfaction of CA, Completion As-built Drawings, Reports & Records	20-Dec-22	16-Jan-23	0	02-Dec-23	02-Dec-23	-193																	
KD09 (Section 5) (incl. BP for KD02 (Stage 5-1))																								
BP																								
KD09.TS.1020	Submit BA14	13-Aug-23	19-Aug-23	1	02-Nov-23 A	02-Nov-23 A																		
KD09.TS.1040	Selection of Full Core by BD	20-Aug-23	02-Sep-23	3	02-Dec-23	04-Dec-23	-199																	
KD09.TS.1060	Full Core to Proof Drill	03-Sep-23	16-Sep-23	10	05-Dec-23	14-Dec-23	-199																	
KD09.TS.1080	Obtain BA14 Acknowledgement / Satisfaction of CA, Completion As-built Drawings, Reports & Records	17-Sep-23	14-Oct-23	14	15-Dec-23	28-Dec-23	-199																	

	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS

		Date	Revision	Checked	Approved
		04-Mar-22	R0	KL	B
		02-Dec-22	R03D	KL	C
