


Zone 2B & 2C

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	December		January				February				March			April		
								18	25	31		32		33		34							
										01	08	15	22	29	05	12	19	26	04	11	18	25	01

Piling for Integrated Basement and U/G Road in Zone 2B & 2C

Contract Dates							
Key Dates							
KD for Zone 2B							
KD05	KD05 (Section 1) - 03 Jan 2023		13-Jul-23	0		02-Feb-24*	-395
KD06	KD06 (Section 2) - 12 Jun 2023		13-Sep-23	0		02-Feb-24*	-235
KD07	KD07 (Section 3) - 30 Sep 2023		13-Dec-23	0		23-Feb-24*	-146
KD for Zone 2C							
KD08	KD08 (Section 4) - 23 May 2023		13-Aug-23	0		02-Feb-24*	-255
KD09	KD09 (Section 5) - 12 Jun 2023		14-Oct-23	0		23-Feb-24*	-256
Construction Stage							
Pile Test							
KD05 (Section 1) (incl. BP for KD01 (Stage1-1))							
BP							
KD05.TS.1060	Full Core to Proof Drill	02-Jun-23	15-Jun-23	32	15-Dec-23 A	15-Jan-24 A	
KD05.TS.1080	Obtain BA14 Acknowledgement / Satisfaction of CA, Completion As-built Drawings, Reports & Records	16-Jun-23	13-Jul-23	14	20-Jan-24	02-Feb-24	-395
KD06 (Section 2)							
BP							
KD06.TS.1060	Full Core to Proof Drill	03-Aug-23	16-Aug-23	26	21-Dec-23 A	15-Jan-24 A	
KD06.TS.1080	Obtain BA14 Acknowledgement / Satisfaction of CA, Completion As-built Drawings, Reports & Records	17-Aug-23	13-Sep-23	14	20-Jan-24	02-Feb-24	-235
KD07 (Section 3) (incl. BP for KD03) (Stage 3-1)							
BP							
KD07.TS.1040	Selection of Full Core by BD	19-Oct-23	01-Nov-23	1	06-Jan-24 A	06-Jan-24 A	
KD07.TS.1060	Full Core to Proof Drill	02-Nov-23	15-Nov-23	12	22-Jan-24 A	02-Feb-24	-146
KD07.TS.1080	Obtain BA14 Acknowledgement / Satisfaction of CA, Completion As-built Drawings, Reports & Records	16-Nov-23	13-Dec-23	21	03-Feb-24	23-Feb-24	-146
KD08 (Section 4) (incl. BP for KD04 (Stage 4-1) & SSHP in KD09 (Section 5))							
BP							
KD08.TS.1060	Full Core to Proof Drill	03-Jul-23	16-Jul-23	58	24-Nov-23 A	20-Jan-24	-255
KD08.TS.1080	Obtain BA14 Acknowledgement / Satisfaction of CA, Completion As-built Drawings, Reports & Records	17-Jul-23	13-Aug-23	13	21-Jan-24	02-Feb-24	-255
SSHP							
KD08.TS.1180	Obtain BA14 Acknowledgement / Satisfaction of CA, Completion As-built Drawings, Reports & Records	20-Dec-22	16-Jan-23	0	20-Jan-24	20-Jan-24	-242
KD09 (Section 5) (incl. BP for KD02 (Stage 5-1))							
BP							
KD09.TS.1040	Selection of Full Core by BD	20-Aug-23	02-Sep-23	12	09-Jan-24 A	20-Jan-24	-256
KD09.TS.1060	Full Core to Proof Drill	03-Sep-23	16-Sep-23	24	10-Jan-24 A	02-Feb-24	-256
KD09.TS.1080	Obtain BA14 Acknowledgement / Satisfaction of CA, Completion As-built Drawings, Reports & Records	17-Sep-23	14-Oct-23	21	03-Feb-24	23-Feb-24	-256

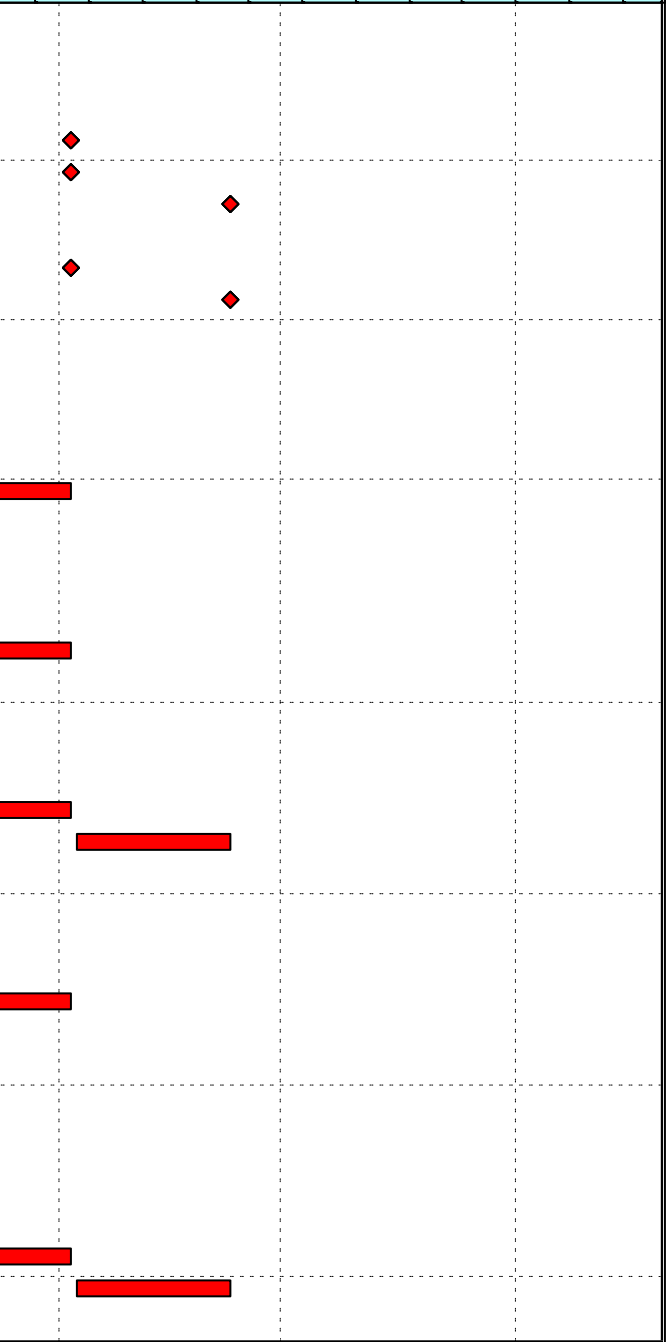

	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS



Date	Revision	Checked	Approved
04-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C
