


**Zone 2B & 2C**

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	January	February	March	April	May
									5	12	19	26	03

**Piling for Integrated Basement and U/G Road in Zone 2B & 2C**

Contract Dates									
Key Dates									
KD for Zone 2B									
KD05	KD05 (Section 1) - 03 Jan 2023		13-Jul-23	0		06-Feb-24 A		100%	
KD06	KD06 (Section 2) - 12 Jun 2023		13-Sep-23	0		06-Feb-24 A		100%	
KD07	KD07 (Section 3) - 30 Sep 2023		13-Dec-23	0		30-Apr-24*	-213	0%	
KD for Zone 2C									
KD08	KD08 (Section 4) - 23 May 2023		13-Aug-23	0		30-Apr-24*	-343	0%	
KD09	KD09 (Section 5) - 12 Jun 2023		14-Oct-23	0		30-Apr-24*	-323	0%	

Construction Stage									
Pile Test									
KD05 (Section 1) (incl. BP for KD01 (Stage1-1))									
BP									
KD05.TS.1080	Obtain BA14 Acknowledgement (Excl. P22&P19-BP13, P23-BP01 and P23-BP08.)	16-Jun-23	13-Jul-23	1	06-Feb-24 A	06-Feb-24 A		100%	
KD06 (Section 2)									
BP									
KD06.TS.1080	Obtain BA14 Acknowledgement / Satisfaction of CA, Completion As-built Drawings, Reports & Records	17-Aug-23	13-Sep-23	1	06-Feb-24 A	06-Feb-24 A		100%	
KD07 (Section 3) (incl. BP for KD03) (Stage 3-1)									
BP									
KD07.TS.1060	Full Core to Proof Drill	02-Nov-23	15-Nov-23	72	22-Jan-24 A	02-Apr-24	-213	0%	
KD07.TS.1080	Obtain BA14 Acknowledgement / Satisfaction of CA, Completion As-built Drawings, Reports & Records	16-Nov-23	13-Dec-23	28	03-Apr-24	30-Apr-24	-213	0%	
KD08 (Section 4) (incl. BP for KD04 (Stage 4-1) & SSHP in KD09 (Section 5))									
BP									
KD08.TS.1060	Full Core to Proof Drill	03-Jul-23	16-Jul-23	131	24-Nov-23 A	02-Apr-24	-343	0%	
KD08.TS.1080	Obtain BA14 Acknowledgement / Satisfaction of CA, Completion As-built Drawings, Reports & Records	17-Jul-23	13-Aug-23	28	03-Apr-24	30-Apr-24	-343	0%	
SSHP									
KD08.TS.1180	Obtain BA14 Acknowledgement / Satisfaction of CA, Completion As-built Drawings, Reports & Records	20-Dec-22	16-Jan-23	1	06-Feb-24 A	06-Feb-24 A		100%	
KD09 (Section 5) (incl. BP for KD02 (Stage 5-1))									
BP									
KD09.TS.1060	Full Core to Proof Drill	03-Sep-23	16-Sep-23	84	10-Jan-24 A	02-Apr-24	-323	0%	
KD09.TS.1080	Obtain BA14 Acknowledgement / Satisfaction of CA, Completion As-built Drawings, Reports & Records	17-Sep-23	14-Oct-23	28	03-Apr-24	30-Apr-24	-323	0%	

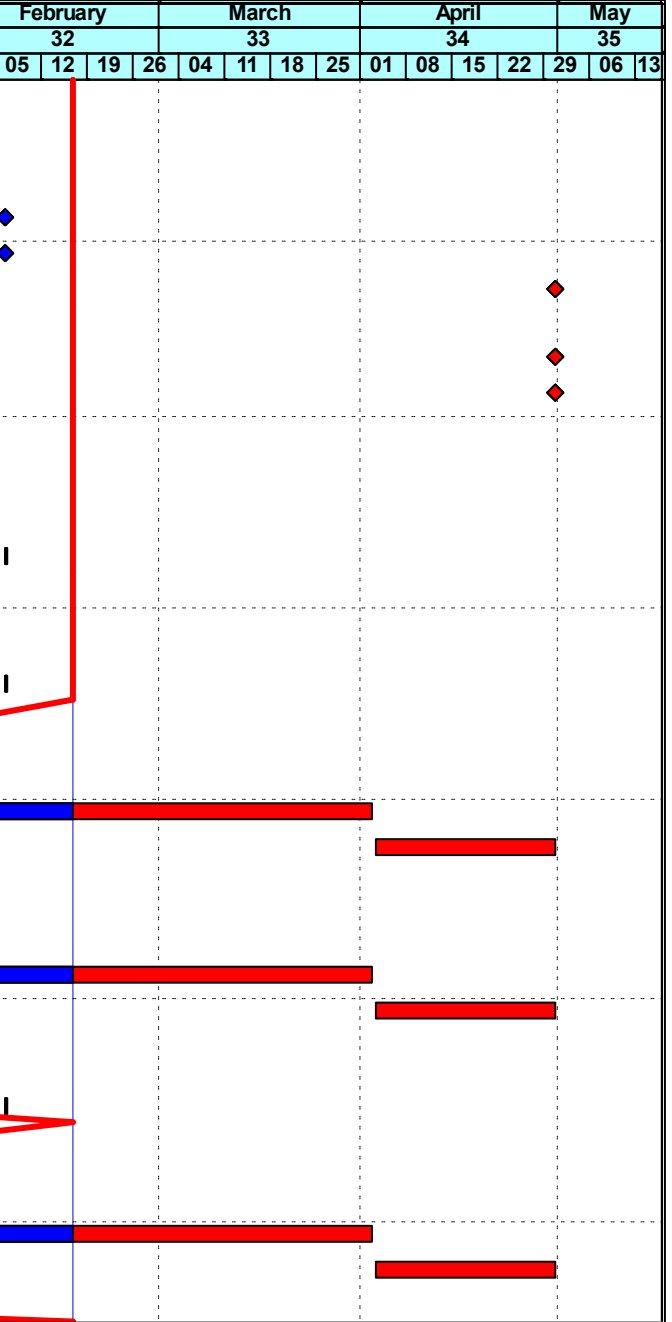

	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS
