

**Zone 2A**

Project Name: Foundation and ELS Works for Integrated Basement and Underground Road in Zone 2A of the West Kowloon Cultural District

3-Month Rolling Programme

Activity Description	Duration (Cal. Day)	Start Date	Finish Date	2021														
				August				September				October						
				6	13	20	27	3	10	17	24	1	8	15	22	29		
				W65	W66	W67	W68	W69	W70	W71	W72	W73	W74	W75	W76	W77		
Zone 2A-1 Foundation, ELS Works and Blinding to Formation (KD01)																		
Grouting Works (Trial 1)																		
Install Pump Wells	15	26-Jul-21	9-Aug-21															
Pumping Test	10	17-Aug-21	26-Aug-21															
ELS (Stage 1) - Grouting / Pipe Pile Works																		
King Post (8/64 Nos Completed) & Erection of Steel Column for Working Platform (11/41 Nos completed)	209	15-May-21	9-Dec-21															
Socketed H-Pile Works																		
Remaining Socketed H-Pile Works (22/53 Nos completed)	150	16-Jun-21	12-Nov-21															
Bored Pile Works																		
Bored Pile Construction (Total 32 Nos. 2~4 Workfront)																		
BP31L, BP33L, BP34I1, BP34G, BP31P, BP36F1, BP31R, BP33G, BP31M, BP36E1, BP31Q, BP33J, BP33M, BP32P, BP34F, BP35F1, BP33P, BP34K, BP34P, BP33F, BP35I1, BP34D, BP32D, BP36J1, BP35E1, BP35J1, BP35K1, BP33D, BP32E, BP34E (27 Nos. Cast; 2 Nos. completed RCD; 0 Nos. RCD in progress)	345	9-Nov-20	19-Oct-21															
Zone 2A-2 Foundation, ELS Works and Blinding to Formation (KD02)																		
Bored Pile Works																		
Additional Bored Pile Construction (Total 16 Nos.) BP15Y, BP16TA, BP13U, BP14Y, BP12M, BP12T, BP20XA, BP12Y, BP13Y, BP16WA. BP12K, BP13W, BP12P (11 Nos. Cast; 1 Nos. completed RCD; 1 Nos. RCD in progress)	236	23-Mar-21	13-Nov-21															
ELS (Stage 1) - Grouting / Pipe Pile Works																		
King Post (0/86 Nos Completed) & Erection of Steel Column for Working Platform (0/65 Nos Completed)	190	28-Aug-21	5-Mar-22															
Stage 1a & 1b grouting (812/1058 Nos Completed)	477	22-Oct-20	10-Feb-22															
Pipe Pile Construction (279/523 Nos Completed)	462	17-Nov-20	21-Feb-22															

- Actual
- Remaining Works
- Critical Remaining Works

3-Month Rolling Programme

Activity Description	Duration (Cal. Day)	Start Date	Finish Date	2021												
				September				October					November			
				3	10	17	24	1	8	15	22	29	6	12	19	26
				W69	W70	W71	W72	W73	W74	W75	W76	W77	W78	W79	W80	W81
Zone 2A-1 Foundation, ELS Works and Blinding to Formation (KD01)																
ELS (Stage 1) - Grouting / Pipe Pile Works																
King Post (8/64 Nos Completed) & Erection of Steel Column for Working Platform (11/41 Nos completed)	239	15-May-21	8-Jan-22													
Socketed H-Pile Works																
Remaining Socketed H-Pile Works (25/53 Nos completed)	161	16-Jun-21	23-Nov-21													
Bored Pile Works																
Bored Pile Construction (Total 32 Nos. 2~4 Workfront)																
BP31L, BP33L, BP34I1, BP34G, BP31P, BP36F1, BP31R, BP33G, BP31M, BP36E1, BP31Q, BP33J, BP33M, BP32P, BP34F, BP35F1, BP33P, BP34K, BP34P, BP33F, BP35I1, BP34D, BP32D, BP36J1, BP35E1, BP35J1, BP35K1, BP33D, BP32E, BP34E, BP33E (30 Nos. Cast; 0 Nos. completed RCD; 0 Nos. RCD in progress)	372	9-Nov-20	15-Nov-21													
Zone 2A-2 Foundation, ELS Works and Blinding to Formation (KD02)																
Bored Pile Works																
Additional Bored Pile Construction (Total 16 Nos.) BP15Y, BP16TA, BP13U, BP14Y, BP12M, BP12T, BP20XA, BP12Y, BP13Y, BP16WA. BP12K, BP13W, BP12P, BP12JA (13 Nos. Cast; 0 Nos. completed RCD; 1 Nos. RCD in progress)	236	23-Mar-21	10-Dec-21													
ELS (Stage 1) - Grouting / Pipe Pile Works																
King Post (0/86 Nos Completed) & Erection of Steel Column for Working Platform (0/65 Nos Completed)	189	25-Sep-21	1-Apr-22													
Stage 1a & 1b grouting (812/1058 Nos Completed)	504	22-Oct-20	9-Mar-22													
Pipe Pile Construction (313/523 Nos Completed)	488	17-Nov-20	19-Mar-22													

- Actual
- Remaining Works
- Critical Remaining Works


Project Name: Foundation and ELS Works for Integrated Basement and Underground Road in Zone 2A of the West Kowloon Cultural District


3-Month Rolling Programme

Activity Description	Duration (Cal. Day)	Start Date	Finish Date	2021													
				October					November				December				
				1	8	15	22	29	6	12	19	26	3	10	17	24	31
				W73	W74	W75	W76	W77	W78	W79	W80	W81	W82	W83	W84	W85	W86
Zone 2A-1 Foundation, ELS Works and Blinding to Formation (KD01)																	
ELS (Stage 1) - Grouting / Pipe Pile Works																	
King Post (8/64 Nos Completed) & Erection of Steel Column for Working Platform (11/41 Nos completed)	272	15-May-21	10-Feb-22														
Socketed H-Pile Works																	
Remaining Socketed H-Pile Works (27/53 Nos completed)	174	16-Jun-21	6-Dec-21														
Bored Pile Works																	
Bored Pile Construction (Total 32 Nos. 2~4 Workfront)																	
BP31L, BP33L, BP34I1, BP34G, BP31P, BP36F1, BP31R, BP33G, BP31M, BP36E1, BP31Q, BP33J, BP33M, BP32P, BP34F, BP35F1, BP33P, BP34K, BP34P, BP33F, BP35I1, BP34D, BP32D, BP36J1, BP35E1, BP35J1, BP35K1, BP33D, BP32E, BP34E, BP33E, BP35C1 (30 Nos. Cast; 1 Nos. completed RCD; 1 Nos. RCD in progress)	369	9-Nov-20	12-Nov-21														
Zone 2A-2 Foundation, ELS Works and Blinding to Formation (KD02)																	
Bored Pile Works																	
Additional Bored Pile Construction (Total 16 Nos.) BP15Y, BP16TA, BP13U, BP14Y, BP12M, BP12T, BP20XA, BP12Y, BP13Y, BP16WA. BP12K, BP13W, BP12P, BP12JA (14 Nos. Cast; 0 Nos. completed RCD; 0 Nos. RCD in progress)	292	23-Mar-21	18-Jan-22														
ELS (Stage 1) - Grouting / Pipe Pile Works																	
King Post (0/86 Nos Completed) & Erection of Steel Column for Working Platform (0/65 Nos Completed)	207	9-Oct-21	3-May-22														
Stage 1a & 1b grouting (812/1058 Nos Completed)	531	22-Oct-20	5-Apr-22														
Pipe Pile Construction (313/523 Nos Completed)	519	17-Nov-20	19-Apr-22														

- Actual
- Remaining Works
- Critical Remaining Works

**Zone 2B & 2C**

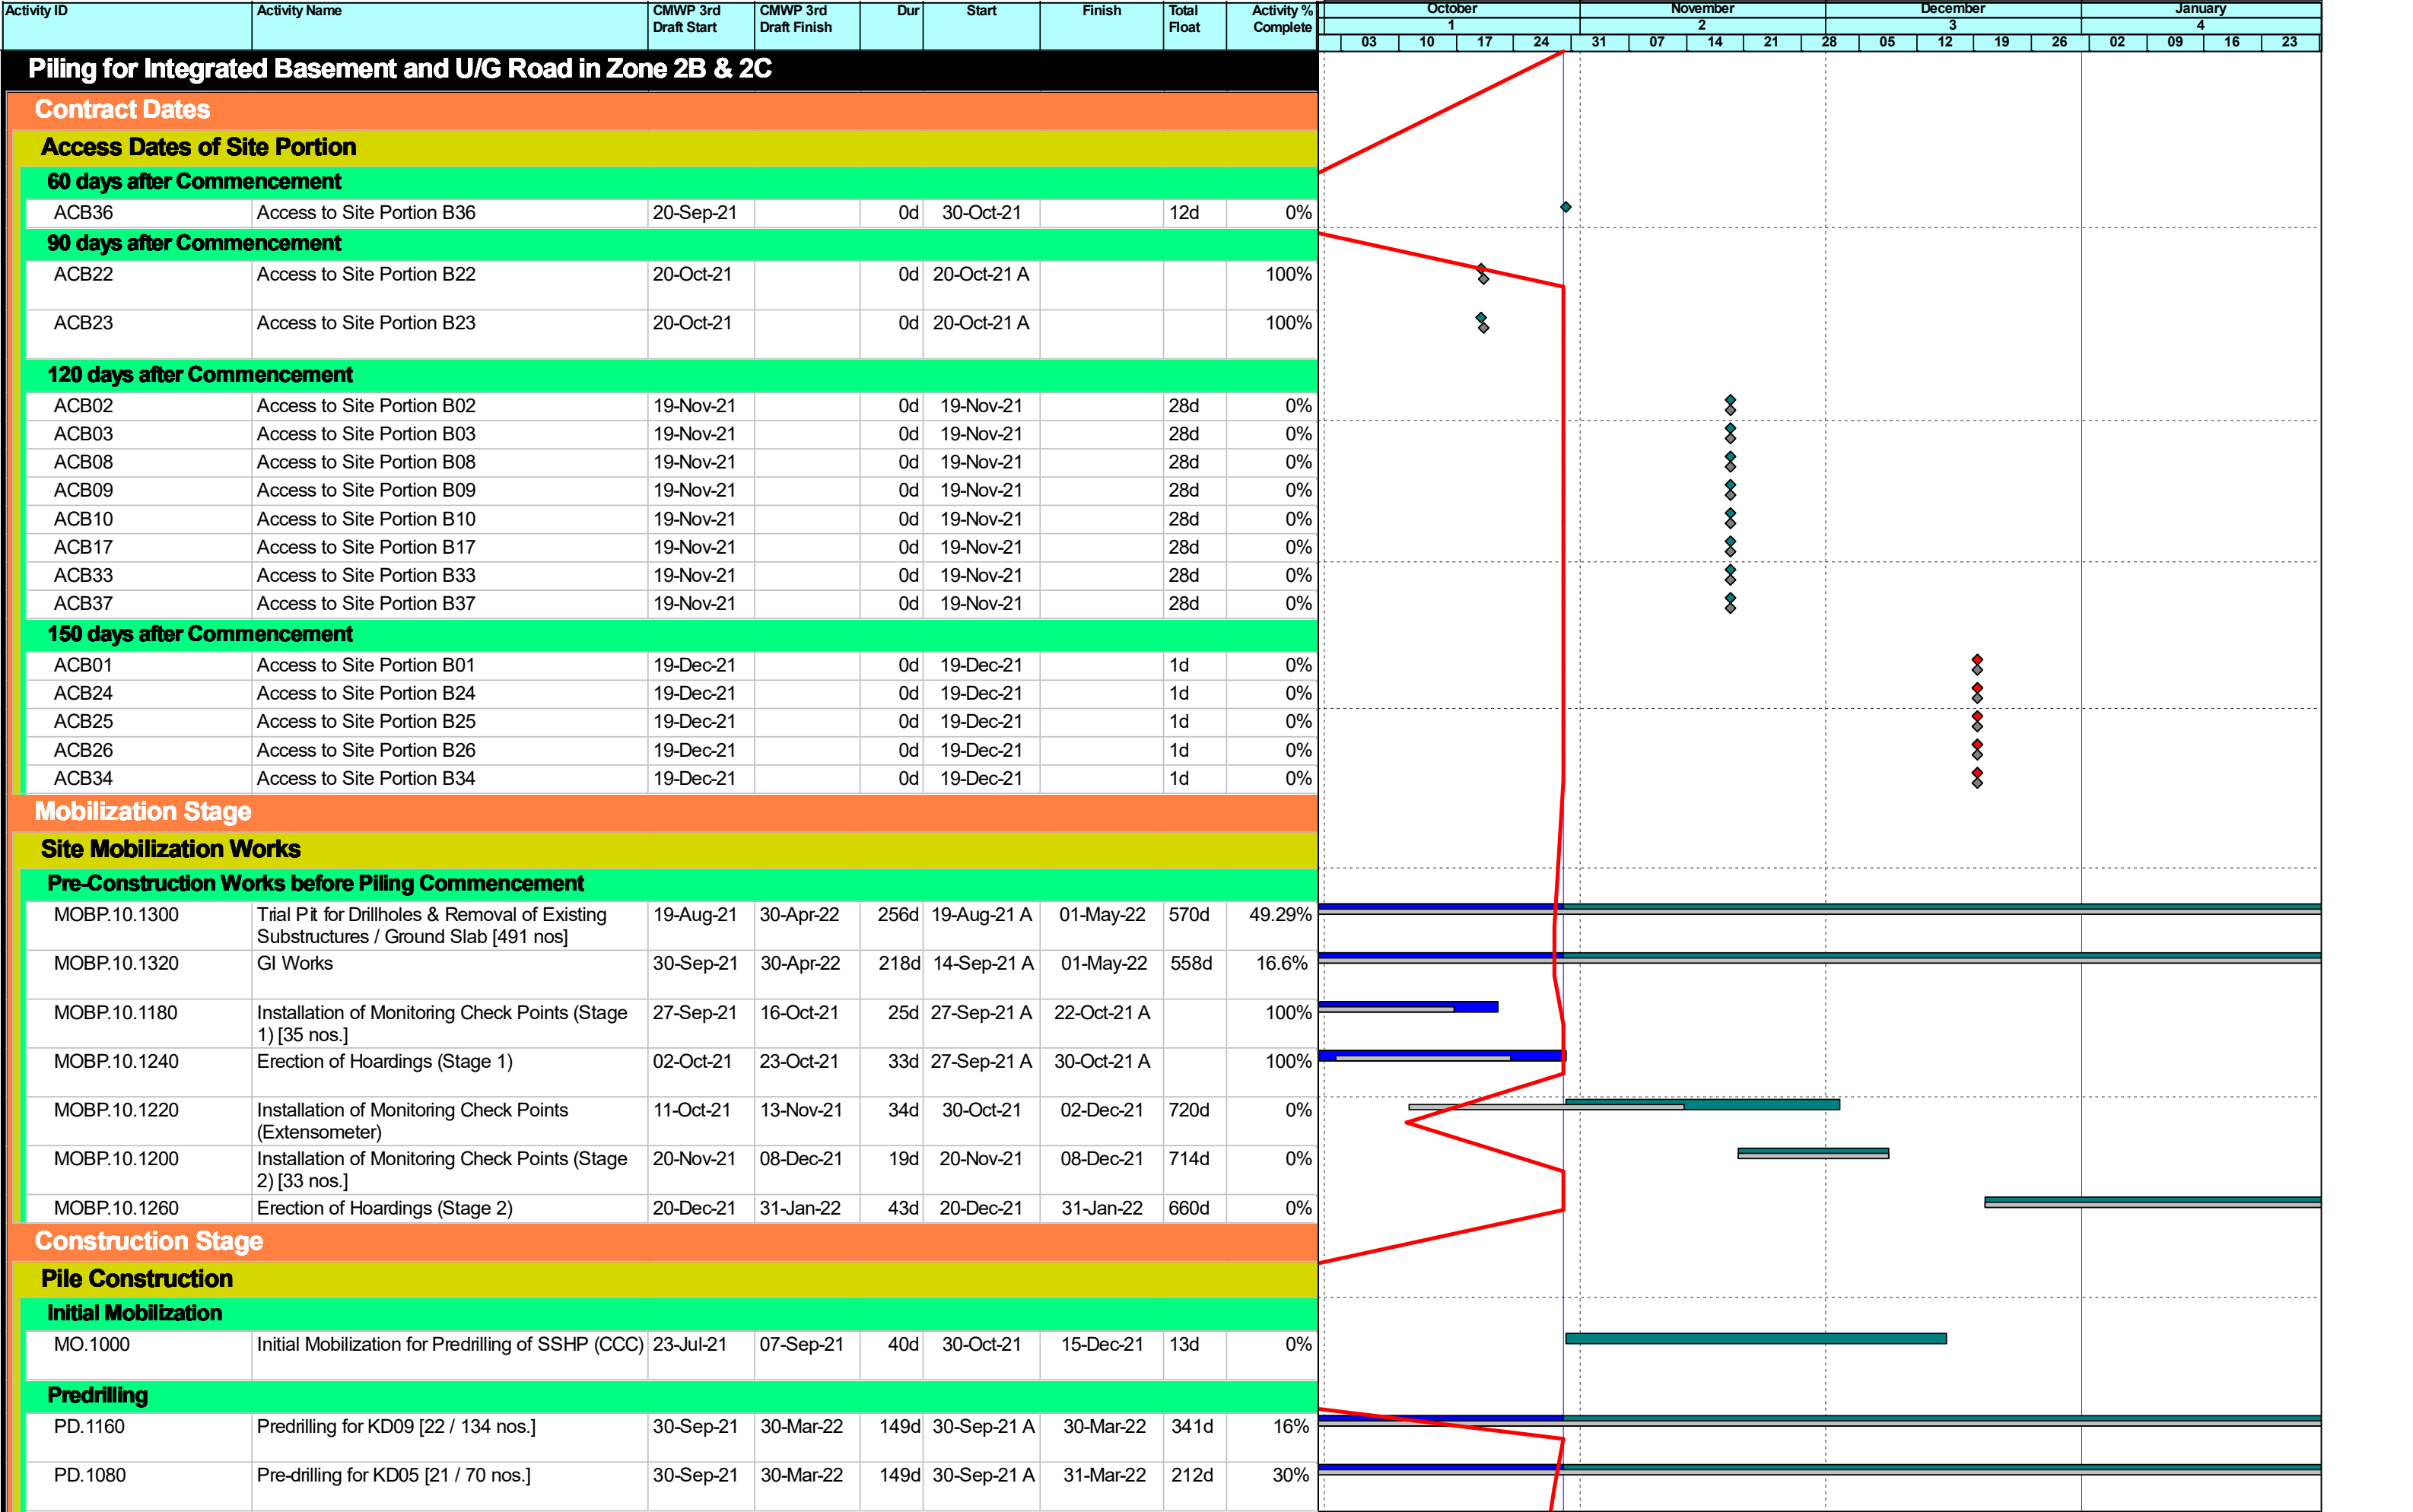

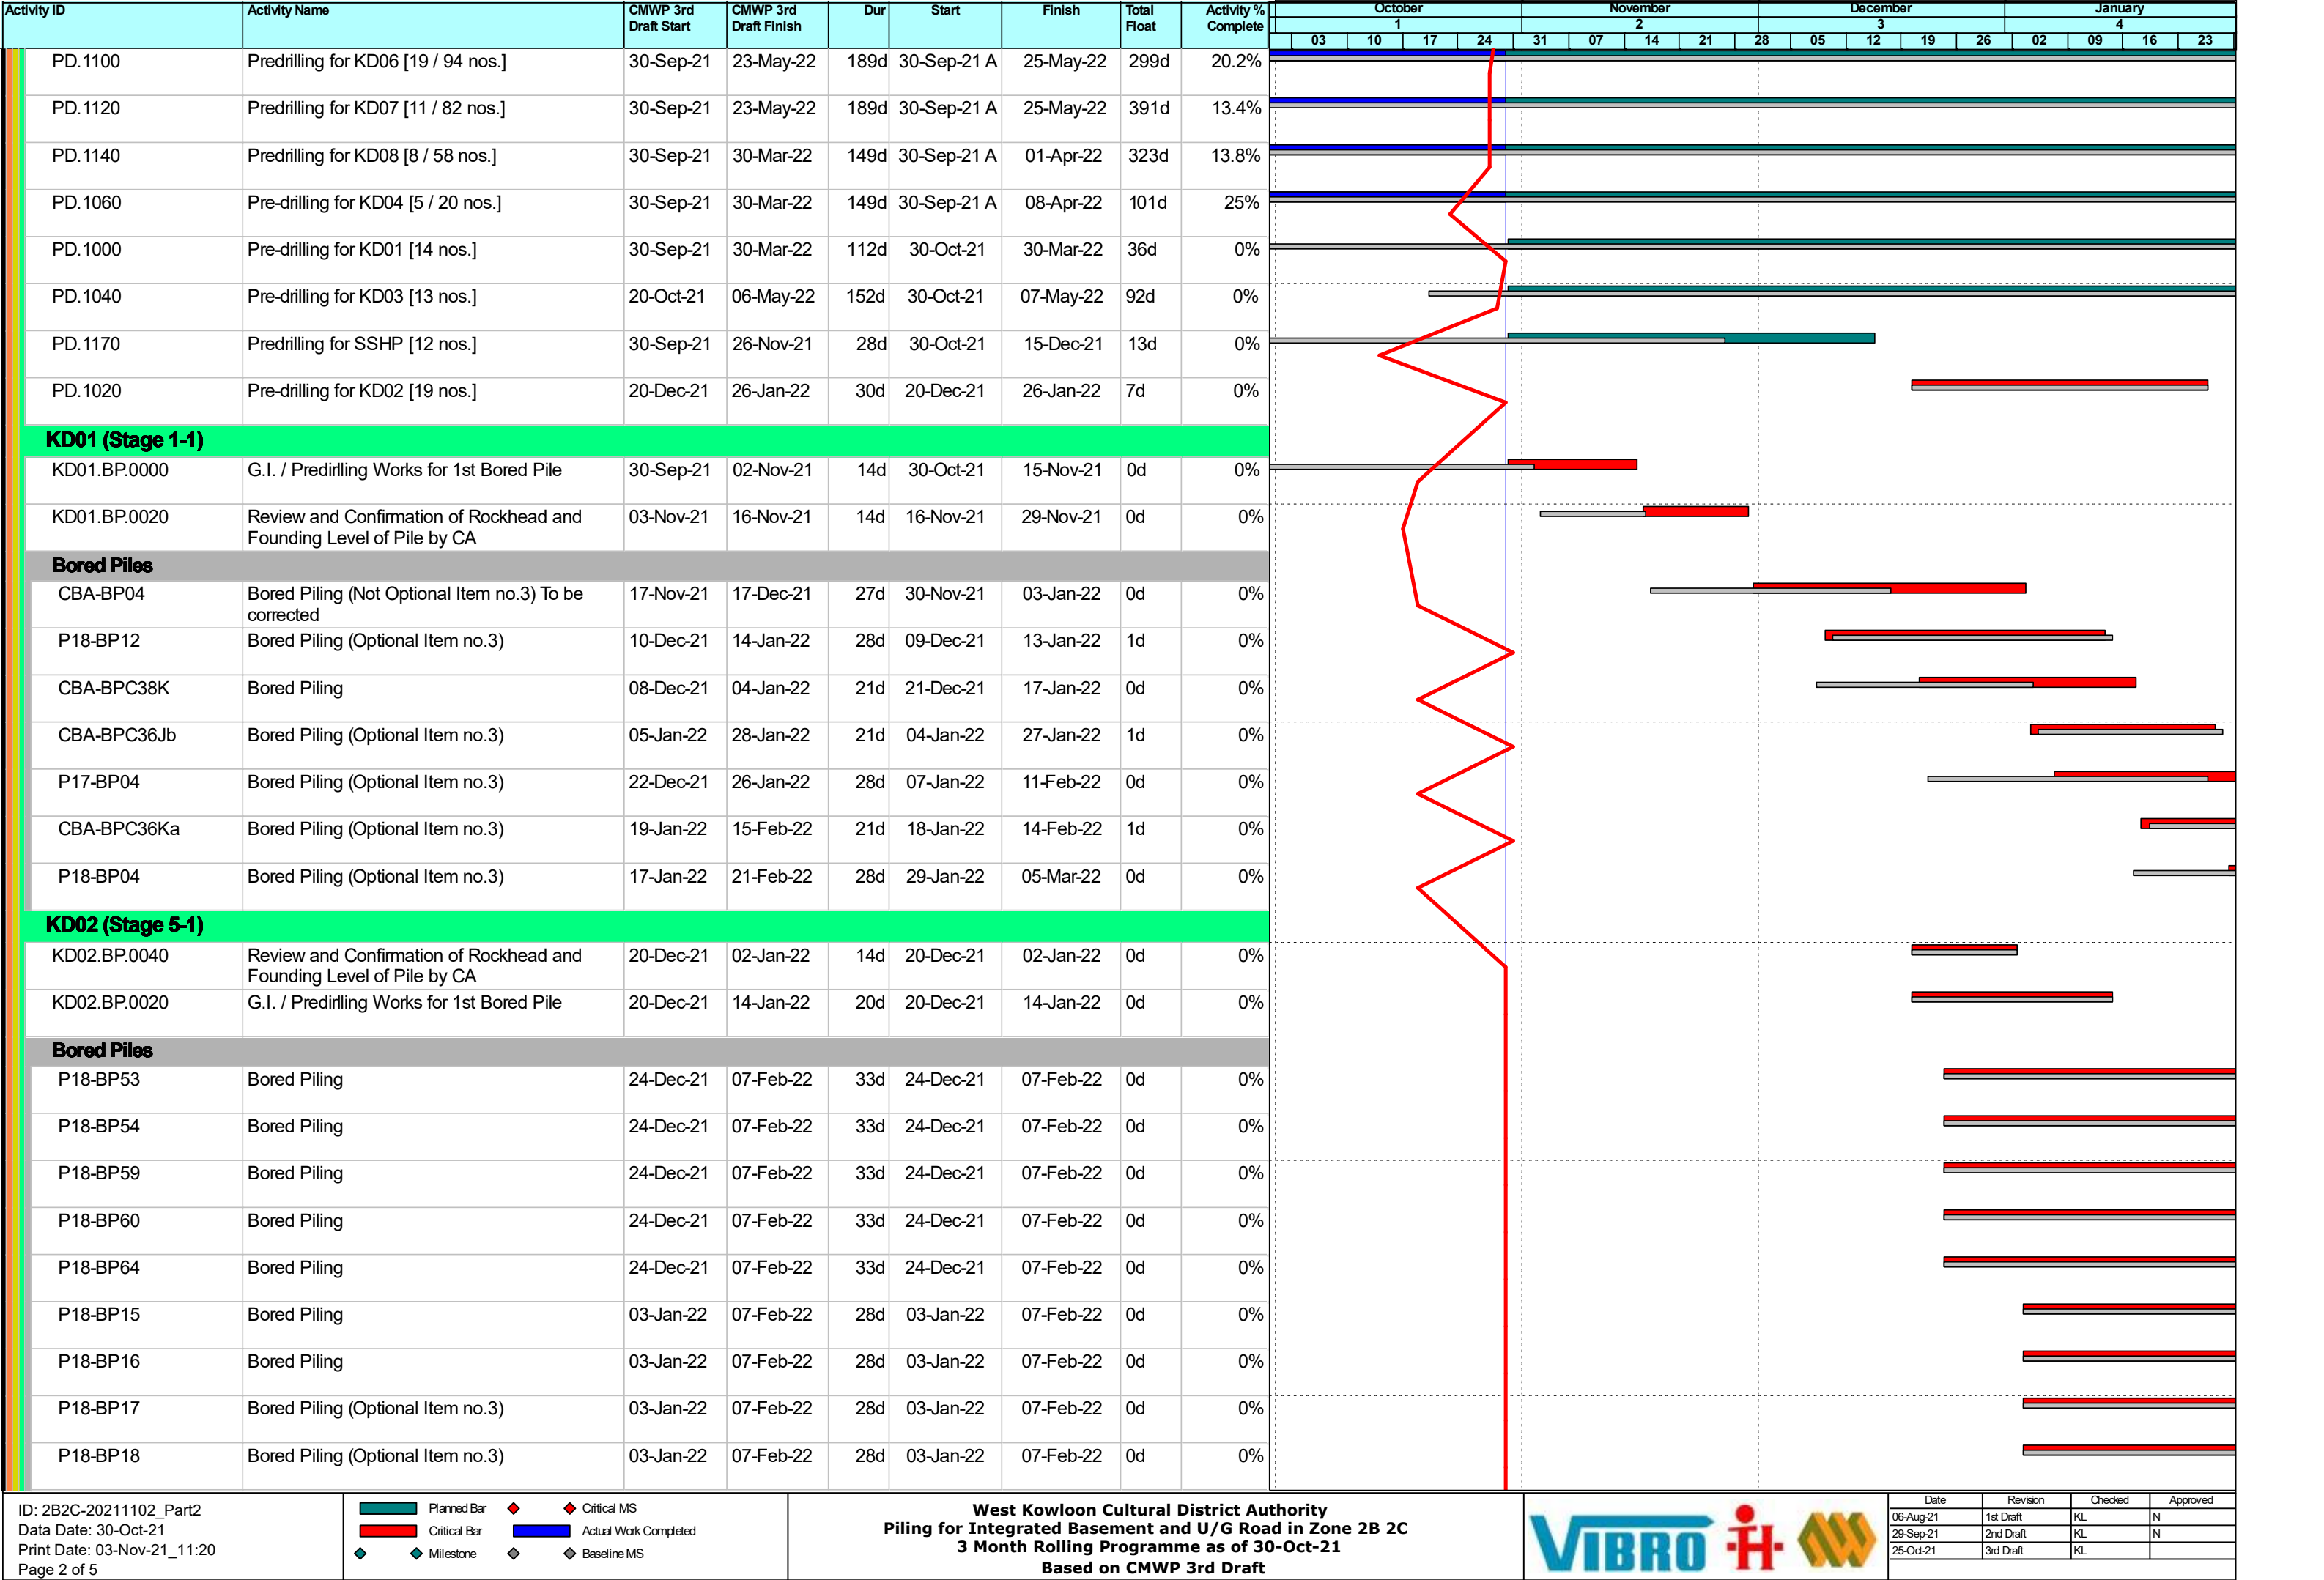



ID: 2B2C-20211102_Part2 Data Date: 30-Oct-21 Print Date: 03-Nov-21_11:20 Page 3 of 5	<div><div></div>Planned Bar</div> <div><div></div>Critical Bar</div> <div><div></div>Milestone</div>	<div><div></div>Critical MS</div> <div><div></div>Actual Work Completed</div> <div><div></div>Baseline MS</div>	<div>West Kowloon Cultural District Authority</div> <div>Piling for Integrated Basement and U/G Road in Zone 2B 2C</div> <div>3 Month Rolling Programme as of 30-Oct-21</div> <div>Based on CMWP 3rd Draft</div>	<div><div>VIBRO</div><div><div></div><div></div></div><div></div></div>	<table><tr><th>Date</th><th>Revision</th><th>Checked</th><th>Approved</th></tr><tr><td>06-Aug-21</td><td>1st Draft</td><td>KL</td><td>N</td></tr><tr><td>29-Sep-21</td><td>2nd Draft</td><td>KL</td><td>N</td></tr><tr><td>25-Oct-21</td><td>3rd Draft</td><td>KL</td><td></td></tr></table>	Date	Revision	Checked	Approved	06-Aug-21	1st Draft	KL	N	29-Sep-21	2nd Draft	KL	N	25-Oct-21	3rd Draft	KL	
	Date	Revision			Checked	Approved															
	06-Aug-21	1st Draft			KL	N															
	29-Sep-21	2nd Draft			KL	N															
	25-Oct-21	3rd Draft			KL																



