




Zone 2A

Project Name: Foundation and ELS Works for Integrated Basement and Underground Road in Zone 2A of the West Kowloon Cultural District

3-Month Rolling Programme

Activity Description	Duration (Cal. Day)	Start Date	Finish Date	2021												2022			
				November				December					January						
				6	12	19	26	3	10	17	24	31	7	14	21	28			
				W78	W79	W80	W81	W82	W83	W84	W85	W86	W87	W88	W89	W90			
Zone 2A-1 Foundation, ELS Works and Blinding to Formation (KD01)																			
ELS (Stage 1) - Grouting / Pipe Pile Works																			
King Post (8/64 Nos Completed) & Erection of Steel Column for Working Platform (11/41 Nos completed)	300	15-May-21	10-Mar-22																
Socketed H-Pile Works																			
Remaining Socketed H-Pile Works (27/53 Nos completed)	174	16-Jun-21	18-Dec-21																
Bored Pile Works																			
Bored Pile Construction (Total 32 Nos. 2~4 Workfront)																			
BP31L, BP33L, BP34I1, BP34G, BP31P, BP36F1, BP31R, BP33G, BP31M, BP36E1, BP31Q, BP33J, BP33M, BP32P, BP34F, BP35F1, BP33P, BP34K, BP34P, BP33F, BP35I1, BP34D, BP32D, BP36J1, BP35E1, BP35J1, BP35K1, BP33D, BP32E, BP34E, BP33E, BP35C1 (30 Nos. Cast; 1 Nos. completed RCD; 1 Nos. RCD in progress)	365	9-Nov-20	8-Nov-21																
Zone 2A-2 Foundation, ELS Works and Blinding to Formation (KD02)																			
Bored Pile Works																			
Additional Bored Pile Construction (Total 16 Nos.) BP15Y, BP16TA, BP13U, BP14Y, BP12M, BP12T, BP20XA, BP12Y, BP13Y, BP16WA. BP12K, BP13W, BP12P, BP12JA, BP12E (14 Nos. Cast; 0 Nos. completed RCD; 1 Nos. RCD in progress)	299	23-Mar-21	15-Jan-22																
ELS (Stage 1) - Grouting / Pipe Pile Works																			
King Post (0/86 Nos Completed) & Erection of Steel Column for Working Platform (0/65 Nos Completed)	194	20-Nov-21	1-Jun-22																
Stage 1a & 1b grouting (860/1058 Nos Completed)	561	22-Oct-20	5-May-22																
Pipe Pile Construction (374/523 Nos Completed)	547	17-Nov-20	17-May-22																

 - Actual
 - Remaining Works
 - Critical Remaining Works

Project Name: Foundation and ELS Works for Integrated Basement and Underground Road in Zone 2A of the West Kowloon Cultural District

3-Month Rolling Programme

Activity Description	Duration (Cal. Day)	Start Date	Finish Date	2021				2022							
				December				January				February			
				10	17	24	31	7	14	21	28	4	11	18	25
				W83	W84	W85	W86	W87	W88	W89	W90	W91	W92	W93	W94
Zone 2A-1 Foundation, ELS Works and Blinding to Formation (KD01)															
ELS (Stage 1) - Grouting / Pipe Pile Works															
King Post (8/64 Nos Completed) & Erection of Steel Column for Working Platform (13/41 Nos completed)	342	15-May-21	21-Apr-22												
Socketed H-Pile Works															
Remaining Socketed H-Pile Works (27/53 Nos completed)	218	16-Jun-21	19-Jan-22												
Zone 2A-2 Foundation, ELS Works and Blinding to Formation (KD02)															
Bored Pile Works															
Additional Bored Pile Construction (Total 16 Nos.) BP15Y, BP16TA, BP13U, BP14Y, BP12M, BP12T, BP20XA, BP12Y, BP13Y, BP16WA. BP12K, BP13W, BP12P, BP12JA, BP12E, BP17Y (14 Nos. Cast; 1 Nos. completed RCD)	290	23-Mar-21	6-Jan-22												
ELS (Stage 1) - Grouting / Pipe Pile Works															
King Post (0/86 Nos Completed) & Erection of Steel Column for Working Platform (0/65 Nos Completed)	208	18-Dec-21	13-Jul-22												
Stage 1a & 1b grouting (915/940 Nos Completed)	478	22-Oct-20	11-Feb-22												
Pipe Pile Construction (411/457 Nos Completed)	591	17-Nov-20	30-Jun-22												

- Actual
- Remaining Works
- Critical Remaining Works

Project Name: Foundation and ELS Works for Integrated Basement and Underground Road in Zone 2A of the West Kowloon Cultural District


3-Month Rolling Programme

Activity Description	Duration (Cal. Day)	Start Date	Finish Date	2022												
				January				February				March				
				7	14	21	28	4	11	18	25	4	11	18	25	
				W87	W88	W89	W90	W91	W92	W93	W94	W95	W96	W97	W98	
Zone 2A-1 Foundation, ELS Works and Blinding to Formation (KD01)																
ELS (Stage 1) - Grouting / Pipe Pile Works																
King Post (8/64 Nos Completed) & Erection of Steel Column for Working Platform (13/41 Nos completed)				356	15-May-21	5-May-22										
Socketed H-Pile Works																
Remaining Socketed H-Pile Works (53/53 Nos completed)				210	16-Jun-21	11-Jan-22										
Zone 2A-2 Foundation, ELS Works and Blinding to Formation (KD02)																
ELS (Stage 1) - Grouting / Pipe Pile Works																
King Post (0/86 Nos Completed) & Erection of Steel Column for Working Platform (0/65 Nos Completed)				193	15-Jan-22	26-Jul-22										
Stage 1a & 1b grouting (930/940 Nos Completed)				490	22-Oct-20	23-Feb-22										
Pipe Pile Construction (412/457 Nos Completed)				543	17-Nov-20	13-May-22										

- Actual
- Remaining Works
- Critical Remaining Works

Zone 2B & 2C

[illegible]

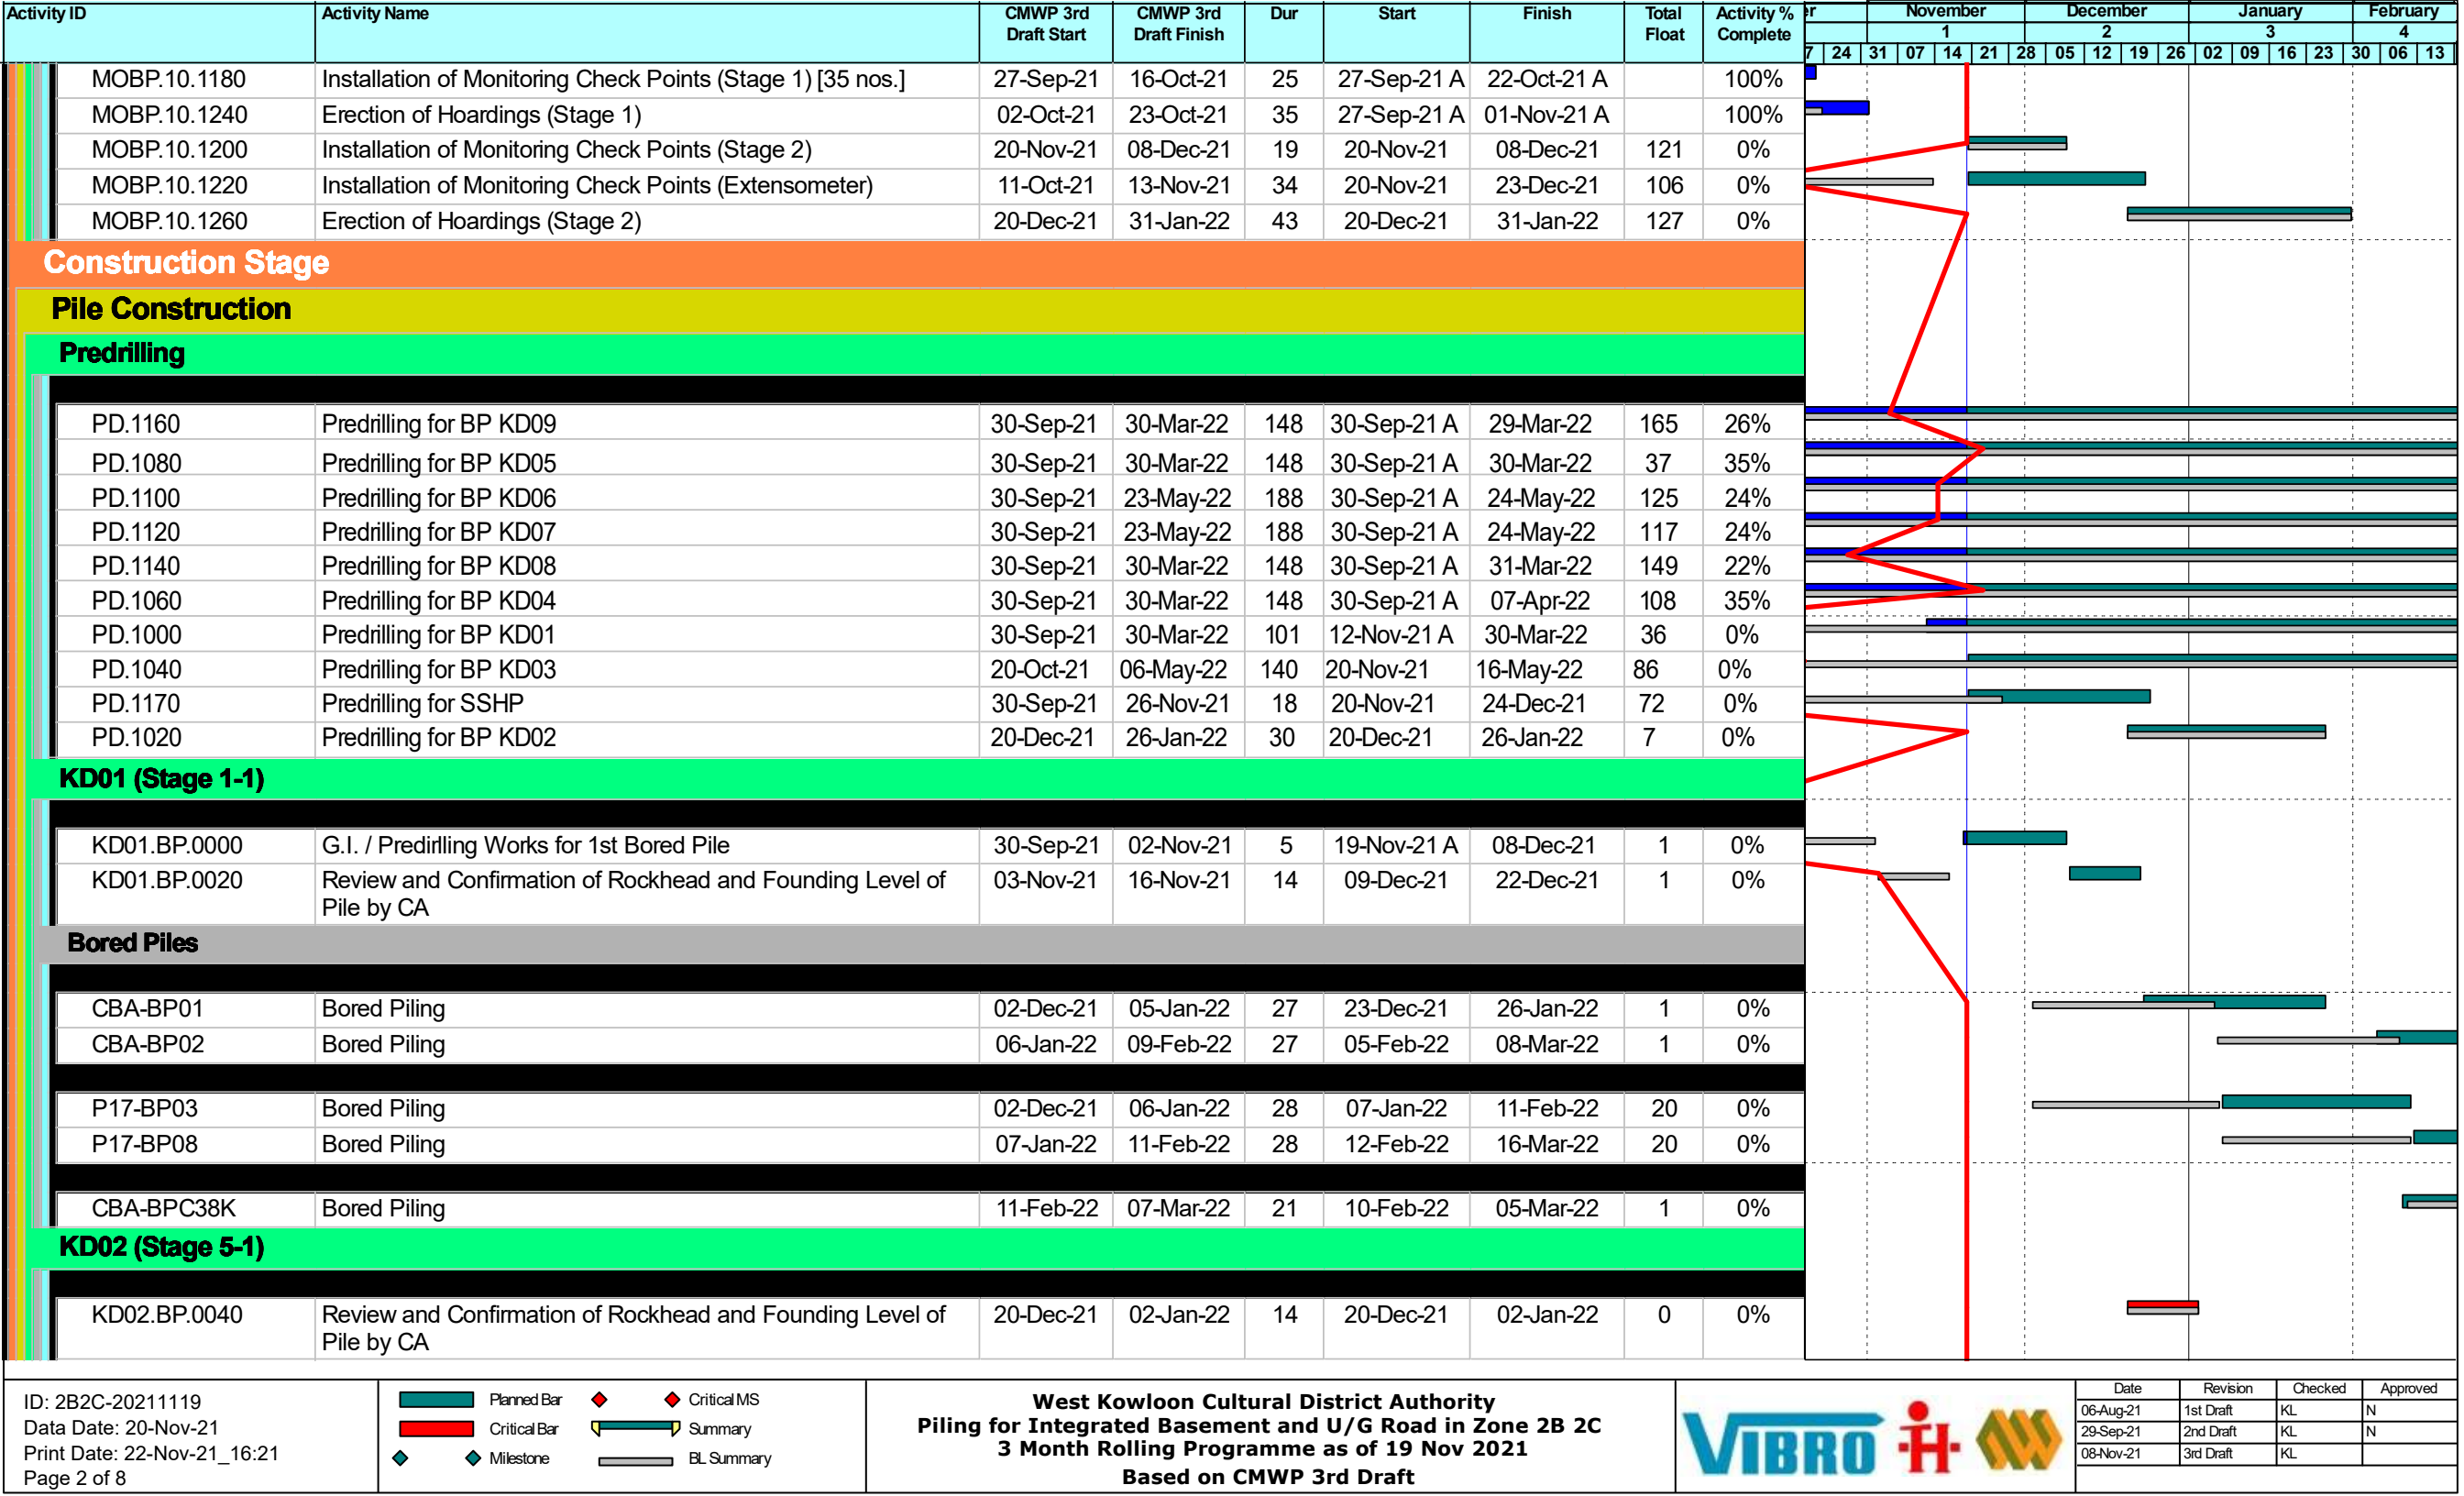


Activity ID	Activity Name	CMWP 3rd Draft Start	CMWP 3rd Draft Finish	Dur	Start	Finish	Total Float	Activity % Complete	Gantt Chart																										
									November				December				January				February														
									7	24	31	07	14	21	28	05	12	19	26	02	09	16	23	30	06	13									
KD02.BP.0020	G.I. / Predrilling Works for 1st Bored Pile	20-Dec-21	14-Jan-22	20	20-Dec-21	14-Jan-22	0	0%																											
Bored Piles																																			
P18-BP54	Bored Piling	24-Dec-21	07-Feb-22	33	24-Dec-21	07-Feb-22	0	0%																											
P18-BP60	Bored Piling	24-Dec-21	07-Feb-22	33	24-Dec-21	07-Feb-22	0	0%																											
P18-BP64	Bored Piling	24-Dec-21	07-Feb-22	33	24-Dec-21	07-Feb-22	0	0%																											
P18-BP15	Bored Piling	03-Jan-22	07-Feb-22	28	03-Jan-22	07-Feb-22	0	0%																											
P18-BP16	Bored Piling	03-Jan-22	07-Feb-22	28	03-Jan-22	07-Feb-22	0	0%																											
P18-BP23	Bored Piling	03-Jan-22	07-Feb-22	28	03-Jan-22	07-Feb-22	0	0%																											
P18-BP29	Bored Piling	03-Jan-22	07-Feb-22	28	03-Jan-22	07-Feb-22	0	0%																											
P18-BP35	Bored Piling	03-Jan-22	07-Feb-22	28	03-Jan-22	07-Feb-22	0	0%																											
P18-BP36	Bored Piling	03-Jan-22	07-Feb-22	28	03-Jan-22	07-Feb-22	0	0%																											
P18-BP42	Bored Piling	03-Jan-22	07-Feb-22	28	03-Jan-22	07-Feb-22	0	0%																											
P18-BP48	Bored Piling	03-Jan-22	07-Feb-22	28	03-Jan-22	07-Feb-22	0	0%																											
P18-BP22	Bored Piling	03-Jan-22	07-Feb-22	28	03-Jan-22	07-Feb-22	0	0%																											
KD03 (Stage 3-1)																																			
KD03.BP.0020	G.I. / Predrilling Works for 1st Bored Pile	20-Oct-21	13-Nov-21	12	20-Nov-21	03-Dec-21	13	0%																											
KD03.BP.0040	Review and Confirmation of Rockhead and Founding Level of Pile by CA	14-Nov-21	27-Nov-21	14	04-Dec-21	17-Dec-21	15	0%																											
Bored Piles																																			
P28&P29-BP01	Bored Piling	10-Dec-21	14-Jan-22	28	18-Dec-21	22-Jan-22	24	0%																											
P28&P29-BP06	Bored Piling	05-Jan-22	09-Feb-22	28	13-Jan-22	17-Feb-22	24	0%																											
P28&P29-BP09	Bored Piling	27-Jan-22	09-Mar-22	33	08-Feb-22	17-Mar-22	24	0%																											
KD04 (Stage 4-1)																																			
KD04.BP.0020	G.I. / Predrilling Works for 1st Bored Pile	30-Sep-21	02-Nov-21	25	30-Sep-21 A	01-Nov-21 A		0%																											
KD04.BP.0040	Review and Confirmation of Rockhead and Founding Level of Pile by CA	03-Nov-21	16-Nov-21	16	30-Oct-21 A	15-Nov-21 A		0%																											
Bored Piles																																			
P30-BP01	Bored Piling	17-Nov-21	18-Dec-21	40	01-Nov-21 A	16-Dec-21	18	35%																											
P30-BP01.10	Excavation			7	01-Nov-21 A	09-Nov-21 A		100%																											
P30-BP01.20	RCD Drilling			21	15-Nov-21 A	08-Dec-21	18	0%																											
P30-BP01.30	Airlifting, Cage Installation and Concreting			7	09-Dec-21	16-Dec-21	18	0%																											
P30-BP07	Bored Piling	09-Dec-21	13-Jan-22	28	17-Dec-21	21-Jan-22	18	0%																											
ID: 2B2C-20211119 Data Date: 20-Nov-21 Print Date: 22-Nov-21_16:21 Page 3 of 8										<div><div><div></div><div></div><div></div><div></div></div><div><div>Planned Bar</div><div>Critical Bar</div><div>Milestone</div><div></div></div><div><div></div><div></div><div></div><div></div></div><div><div>Critical MS</div><div>Summary</div><div>BL Summary</div></div></div> <div>West Kowloon Cultural District Authority Piling for Integrated Basement and U/G Road in Zone 2B 2C 3 Month Rolling Programme as of 19 Nov 2021 Based on CMWP 3rd Draft</div> <div><div>VIBRO</div><div></div><div></div></div> <table><tr><th>Date</th><th>Revision</th><th>Checked</th><th>Approved</th></tr><tr><td>06-Aug-21</td><td>1st Draft</td><td>KL</td><td>N</td></tr><tr><td>29-Sep-21</td><td>2nd Draft</td><td>KL</td><td>N</td></tr><tr><td>08-Nov-21</td><td>3rd Draft</td><td>KL</td><td></td></tr></table>										Date	Revision	Checked	Approved	06-Aug-21	1st Draft	KL	N	29-Sep-21	2nd Draft	KL	N	08-Nov-21	3rd Draft	KL	
Date	Revision	Checked	Approved																																
06-Aug-21	1st Draft	KL	N																																
29-Sep-21	2nd Draft	KL	N																																
08-Nov-21	3rd Draft	KL																																	

Activity ID	Activity Name	CMWP 3rd Draft Start	CMWP 3rd Draft Finish	Dur	Start	Finish	Total Float	Activity % Complete	November												December				January				February																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																												
									1						2						3				4																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																
									07	24	31	07	14	21	28	05	12	19	26	02	09	16	23	30	06	13																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																															
P30-BP08	Bored Piling	04-Jan-22	08-Feb-22	28	12-Jan-22	16-Feb-22	18	0%																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																	

Activity ID	Activity Name	CMWP 3rd Draft Start	CMWP 3rd Draft Finish	Dur	Start	Finish	Total Float	Activity % Complete	November												December				January				February																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																											
									1												2				3				4																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																											
									7	24	31	07	14	21	28	05	12	19	26	02	09	16	23	30	06	13																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																														
	CBA-BPC40M	Bored Piling	04-Jan-22	27-Jan-22	21	16-Dec-21	12-Jan-22	21	0%																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																															

Activity ID	Activity Name	CMWP 3rd Draft Start	CMWP 3rd Draft Finish	Dur	Start	Finish	Total Float	Activity % Complete	Gantt Chart																																													
									November							December						January				February																												
									1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31															
KD07 (Section 3)																																																						
Trial Pile (P30-BP76)																																																						
KD07.BP.0000	G.I. / Predirlling Works for 1st Bored Pile (with E1) [9 nos.]	22-Oct-21	13-Nov-21	21	19-Nov-21 A	13-Dec-21	3	0%																																														
KD07.BP.0020	Review and Confirmation of Rockhead and Founding Level of Pile by CA	14-Nov-21	27-Nov-21	14	14-Dec-21	27-Dec-21	3	0%																																														
P30-BP76	Bored Piling (Trial Pile for Schedule 1)	04-Dec-21	17-Feb-22	59	28-Dec-21	10-Mar-22	3	0%																																														
Trial Pile (P24&P27-BP34)																																																						
KD07.BP.0040	G.I. / Predirlling Works for 1st Bored Pile (with E2) [6 nos.]	30-Sep-21	22-Oct-21	28	30-Sep-21 A	05-Nov-21 A		0%																																														
KD07.BP.0060	Review and Confirmation of Rockhead and Founding Level of Pile by CA	23-Oct-21	05-Nov-21	29	05-Nov-21 A	03-Dec-21	82	0%																																														
P24&P27-BP34	Bored Piling (Trial Pile for Schedule 2)	20-Dec-21	29-Jan-22	33	20-Dec-21	29-Jan-22	51	0%																																														
KD08 (Section 4)																																																						
Trial Pile (P30-BP15)																																																						
KD08.BP.60	G.I. / Predirlling Works for 1st Bored Pile (with E3) [9 nos.]	30-Sep-21	29-Oct-21	30	30-Sep-21 A	08-Nov-21 A		0%																																														
KD08.BP.70	Review and Confirmation of Rockhead and Founding Level of Pile by CA	30-Oct-21	12-Nov-21	14	20-Nov-21	03-Dec-21	16	0%																																														
P30-BP15	Bored Piling (Trial Pile for Schedule 3)	09-Dec-21	13-Jan-22	28	14-Dec-21	18-Jan-22	5	0%																																														
Bored Piles																																																						
P30-BP05	Bored Piling	29-Nov-21	08-Jan-22	40	08-Nov-21 A	23-Dec-21	59	35%																																														
P30-BP05.10	Excavation			6	08-Nov-21 A	15-Nov-21 A		100%																																														
P30-BP05.20	RCD Drilling			24	20-Nov-21	17-Dec-21	59	0%																																														
P30-BP05.30	Airlifting, Cage Installation and Concreting			5	18-Dec-21	23-Dec-21	59	0%																																														
P26-BP15	Bored Piling	14-Jan-22	08-Mar-22	43	19-Jan-22	12-Mar-22	40	0%																																														
P30-BP11	Bored Piling	14-Jan-22	24-Feb-22	33	19-Jan-22	01-Mar-22	10	0%																																														
P30-BP12	Bored Piling	15-Feb-22	24-Mar-22	33	19-Feb-22	29-Mar-22	10	0%																																														
P30-BP19	Bored Piling	14-Jan-22	08-Mar-22	43	19-Jan-22	12-Mar-22	5	0%																																														
P30-BP45	Bored Piling	14-Jan-22	08-Mar-22	43	19-Jan-22	12-Mar-22	27	0%																																														
KD09 (Section 5)																																																						
Trial Piles (P23-BP68)																																																						
KD08.BP.80	G.I. / Predirlling Works for 1st Bored Pile (with E4) [8 nos.]	15-Sep-21	29-Oct-21	37	15-Sep-21 A	01-Nov-21 A		0%																																														
ID: 2B2C-20211119 Data Date: 20-Nov-21 Print Date: 22-Nov-21_16:21 Page 6 of 8									<div><div><div></div><div>Planned Bar</div></div><div><div></div><div>Critical Bar</div></div><div><div></div><div>Milestone</div></div><div><div></div><div>Critical MS</div></div><div><div></div><div>Summary</div></div><div><div></div><div>BL Summary</div></div></div>										<div>West Kowloon Cultural District Authority</div> <div>Piling for Integrated Basement and U/G Road in Zone 2B 2C</div> <div>3 Month Rolling Programme as of 19 Nov 2021</div> <div>Based on CMWP 3rd Draft</div>										<div><div>VIBRO</div><div></div><div></div></div> <table><tr><th>Date</th><th>Revision</th><th>Checked</th><th>Approved</th></tr><tr><td>06-Aug-21</td><td>1st Draft</td><td>KL</td><td>N</td></tr><tr><td>29-Sep-21</td><td>2nd Draft</td><td>KL</td><td>N</td></tr><tr><td>08-Nov-21</td><td>3rd Draft</td><td>KL</td><td></td></tr></table>										Date	Revision	Checked	Approved	06-Aug-21	1st Draft	KL	N	29-Sep-21	2nd Draft	KL	N	08-Nov-21	3rd Draft	KL	
Date	Revision	Checked	Approved																																																			
06-Aug-21	1st Draft	KL	N																																																			
29-Sep-21	2nd Draft	KL	N																																																			
08-Nov-21	3rd Draft	KL																																																				

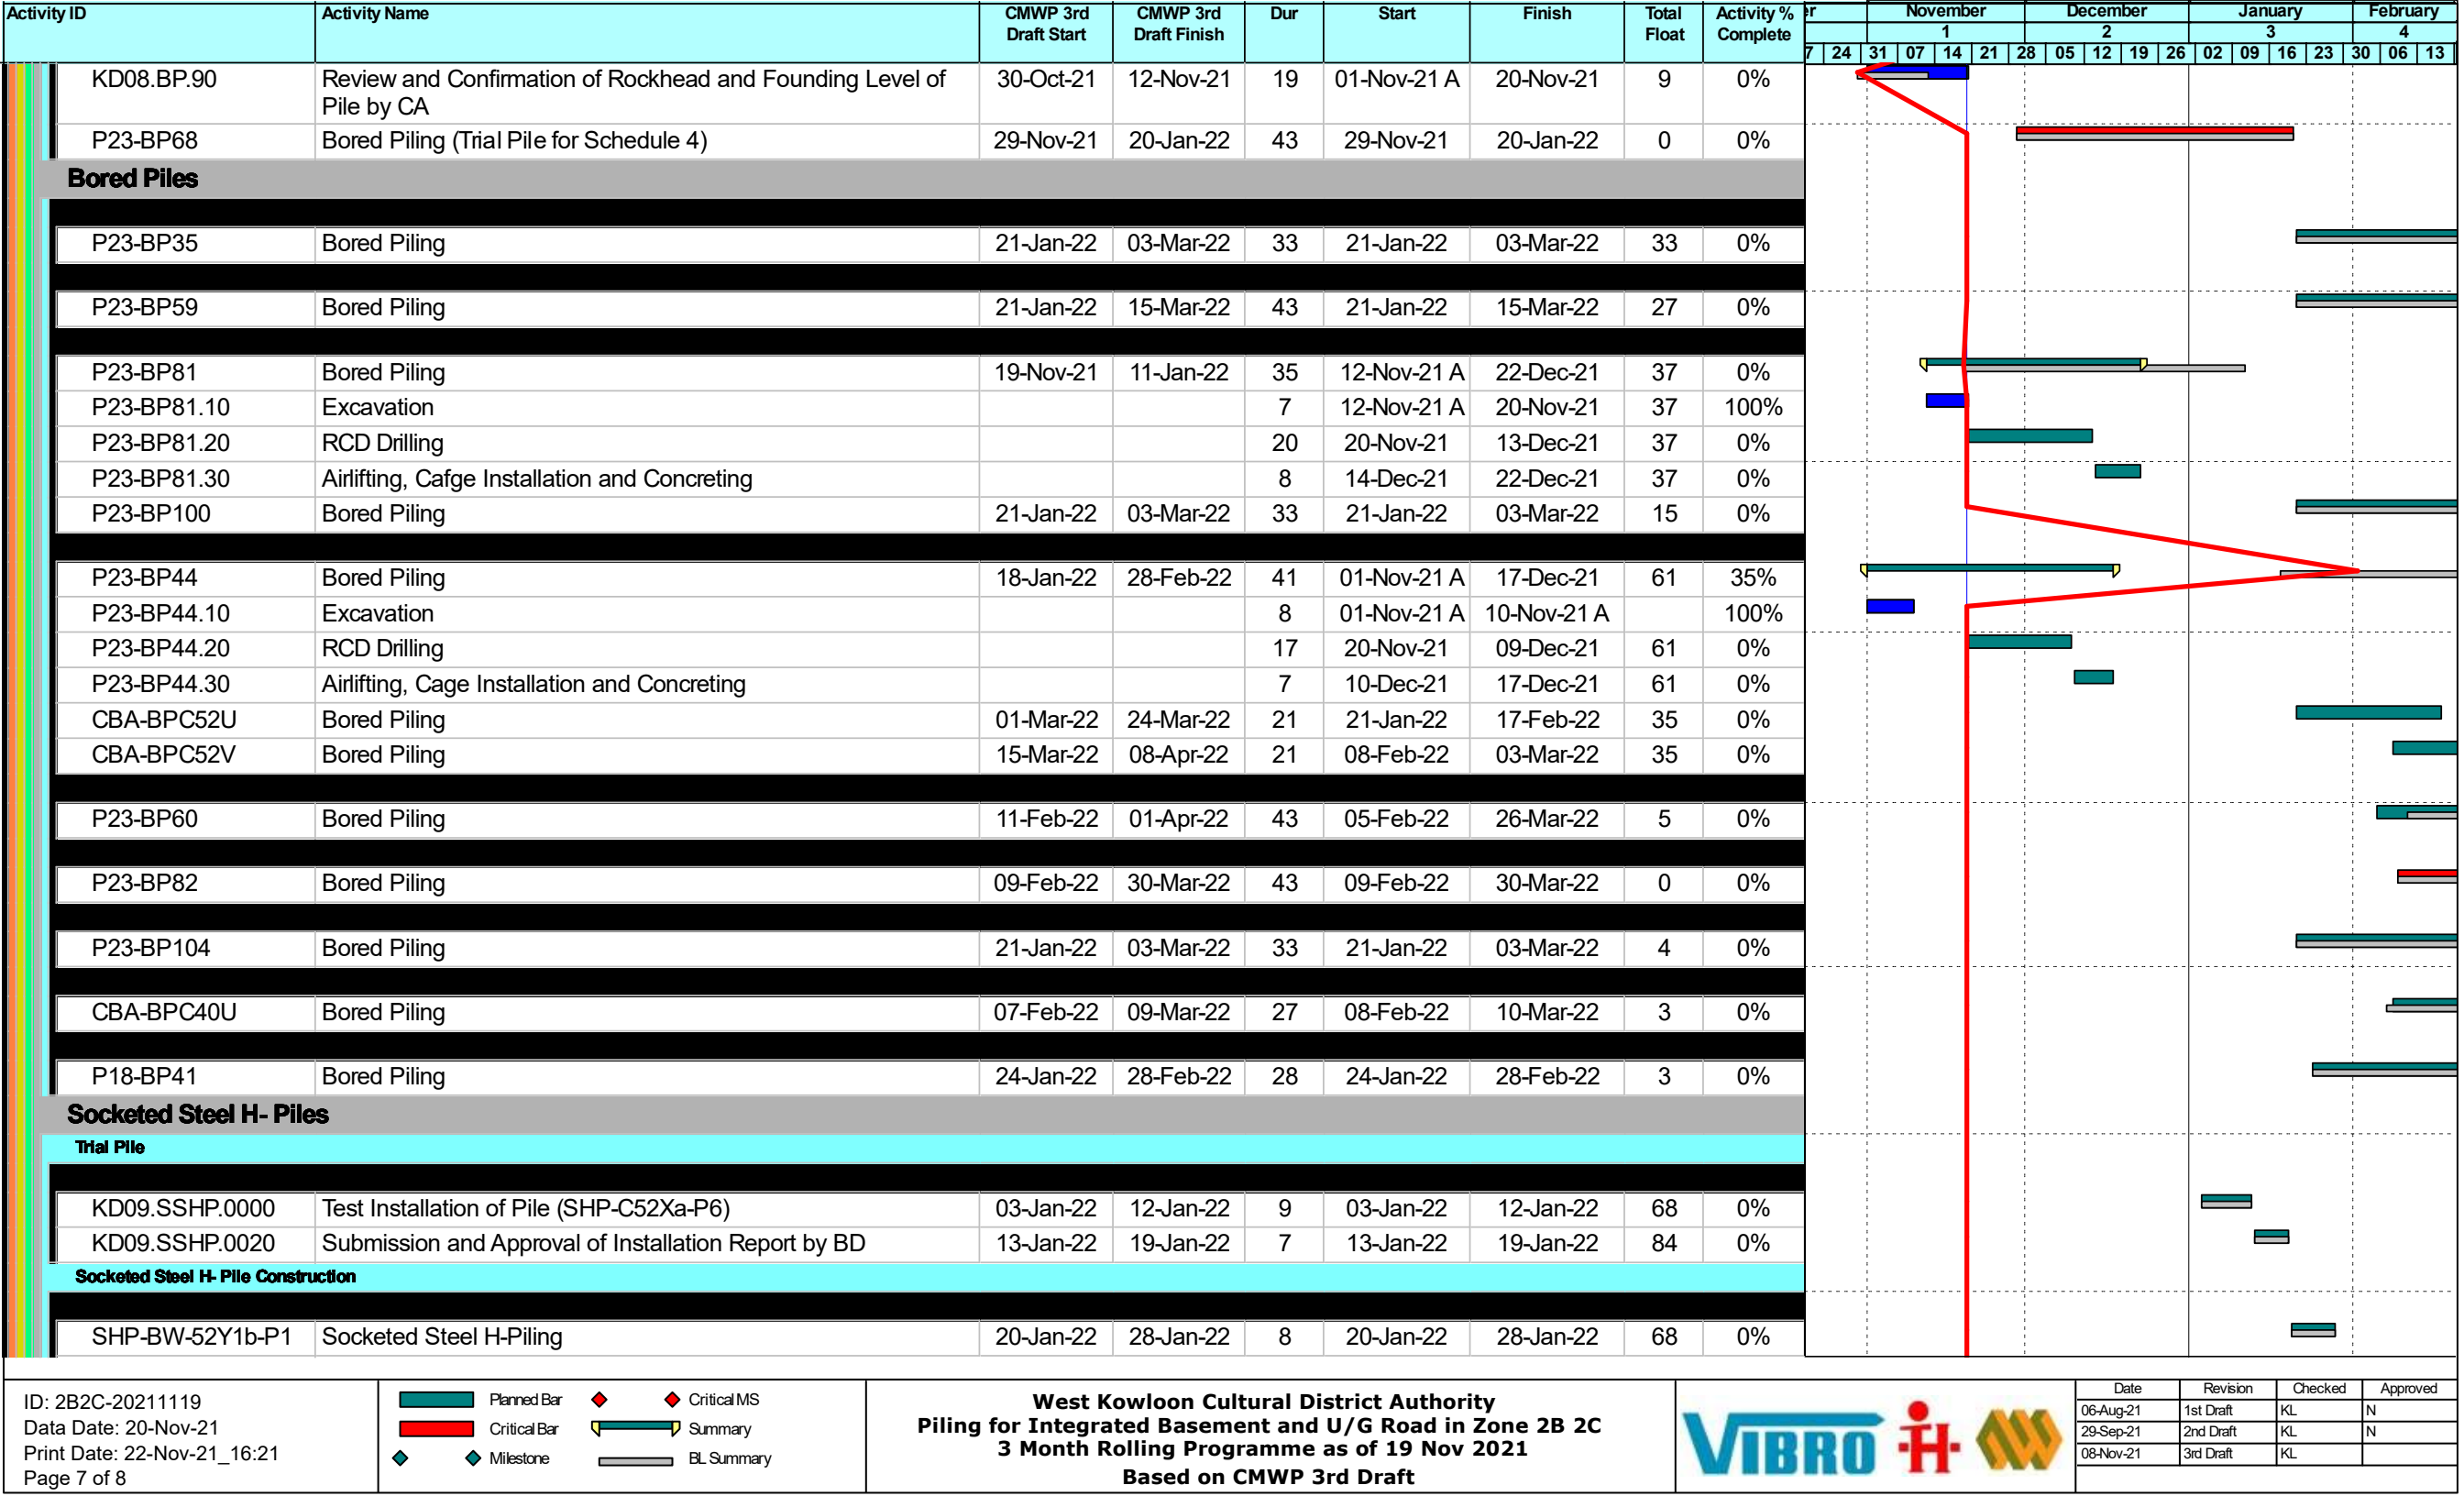

Activity ID	Activity Name	CMWP 3rd Draft Start	CMWP 3rd Draft Finish	Dur	Start	Finish	Total Float	Activity % Complete	Bar	November				December				January				February				
										1				2				3				4				
										7	24	31	07	14	21	28	05	12	19	26	02	09	16	23	30	06
<div><div></div><div></div><div></div><div></div><div></div><div></div><div></div></div>	SHP-BW-52Y1b-P2	Socketed Steel H-Piling	24-Jan-22	04-Feb-22	8	24-Jan-22	04-Feb-22	68	0%																	
	SHP-C52W-P1	Socketed Steel H-Piling	27-Jan-22	08-Feb-22	8	27-Jan-22	08-Feb-22	68	0%																	
	SHP-C52W-P2	Socketed Steel H-Piling	31-Jan-22	11-Feb-22	8	31-Jan-22	11-Feb-22	68	0%																	
	SHP-C52W-P3	Socketed Steel H-Piling	07-Feb-22	15-Feb-22	8	07-Feb-22	15-Feb-22	68	0%																	
	SHP-C52W-P4	Socketed Steel H-Piling	10-Feb-22	18-Feb-22	8	10-Feb-22	18-Feb-22	68	0%																	
	SHP-C52W-P5	Socketed Steel H-Piling	14-Feb-22	22-Feb-22	8	14-Feb-22	22-Feb-22	68	0%																	
	SHP-C52W-P6	Socketed Steel H-Piling	17-Feb-22	25-Feb-22	8	17-Feb-22	25-Feb-22	68	0%																	



[illegible]

Activity ID	Activity Name	CMWP 4th Draft Start	CMWP 4th Draft Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	December				January				February				March																
									-1				1				2				3																
									03	10	17	24	31	07	14	21	28	04	11	18	25	04	11	18	25												
	MOBP.06.1100	Application and Approval of Construction Noise Permit	26-Jul-21	30-Nov-21	159	26-Jul-21 A	01-Jan-22	102	100%																												
Major Resources Procurement for the Early Works																																					
	MOBP.07.1080	Steel Rebar Delivery (1st Batch), Testing of Rebar and Approval of Rebar	05-Oct-21	18-Nov-21	88	05-Oct-21 A	01-Jan-22	87	100%																												
	MOBP.07.1120	Preparation and Submission of Structural Steel H-Pile for Socketed H-Piling Works	23-Jul-21	18-Oct-21	162	23-Jul-21 A	01-Jan-22	57	100%																												
Pre-construction Submission for Mobilization																																					
General Submission																																					
	MOBP.08.1140	Approval of Site Management Plan	22-Aug-21	04-Oct-21	132	22-Aug-21 A	01-Jan-22	47	100%																												
Method Statement of Site Works																																					
	MOBP.08.1660	Approval of Method Statement for Large Diameter Bored Pile Construction (MTR Protection Zone)	28-Jul-21	04-Oct-21	157	28-Jul-21 A	01-Jan-22	47	100%																												
Site Mobilization Works																																					
Pre-Construction Works before Piling Commencement																																					
	MOBP.10.1120	Site Clearance	23-Jul-21	30-Apr-22	303	23-Jul-21 A	21-May-22	117	50%																												
	MOBP.10.1200	Installation of Monitoring Check Points (Stage 2) [33 nos.]	20-Nov-21	08-Dec-21	19	01-Jan-22	19-Jan-22	89	0%																												
	MOBP.10.1220	Installation of Monitoring Check Points (Extensometer)	11-Oct-21	13-Nov-21	55	20-Nov-21 A	13-Jan-22	76	50%																												
	MOBP.10.1260	Erection of Hoardings (Stage 2)	20-Dec-21	31-Jan-22	38	01-Jan-22	07-Feb-22	130	0%																												
	MOBP.10.1300	Trial Pit for Drillholes & Removal of Existing Substructures / Ground Slab [503 nos]	19-Aug-21	30-Apr-22	255	19-Aug-21 A	30-Apr-22	137	65%																												
Construction Stage																																					
Pile Construction																																					
Initial Mobilization																																					
ID: 2B2C-20211231_bw Data Date: 01-Jan-22 Print Date: 03-Jan-22_ 14:19 Page 2 of 20			<div><div></div>Planned Bar</div> <div><div></div>Critical Bar</div> <div><div></div>Baseline</div>		<div><div></div>Milestone</div> <div><div></div>Critical MS</div> <div><div></div>Baseline MS</div>		West Kowloon Cultural District Authority Piling for Integrated Basement and U/G Road in Zone 2B 2C 3 Month Rolling Programme as of 31 Dec 2021 Based on CMWP 4th Draft				<div><div>VIBRO</div><div></div><div></div></div>			<table><tr><th>Date</th><th>Revision</th><th>Checked</th><th>Approved</th></tr><tr><td>06-Aug-21</td><td>1st Draft</td><td>KL</td><td>N</td></tr><tr><td>29-Sep-21</td><td>2nd Draft</td><td>KL</td><td>N</td></tr><tr><td>25-Oct-21</td><td>3rd Draft</td><td>KL</td><td>C</td></tr><tr><td>26-Nov-21</td><td>4th Draft</td><td>KL</td><td></td></tr></table>				Date	Revision	Checked	Approved	06-Aug-21	1st Draft	KL	N	29-Sep-21	2nd Draft	KL	N	25-Oct-21	3rd Draft	KL	C	26-Nov-21	4th Draft	KL	
Date	Revision	Checked	Approved																																		
06-Aug-21	1st Draft	KL	N																																		
29-Sep-21	2nd Draft	KL	N																																		
25-Oct-21	3rd Draft	KL	C																																		
26-Nov-21	4th Draft	KL																																			

Activity ID	Activity Name	CMWP 4th Draft Start	CMWP 4th Draft Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	December				January				February				March			
									-1				1				2				3			
									03	10	17	24	31	07	14	21	28	04	11	18	25	04	11	18
MO.1010	Initial Mobilization for Predrilling of BP (CCD / KD05 / KD01)	23-Jul-21	07-Sep-21	174	23-Jul-21 A	21-Feb-22	68	80%																
MO.1020	Initial Mobilization for Predrilling of BP (CCE / KD06)	23-Jul-21	07-Sep-21	174	23-Jul-21 A	21-Feb-22	202	50%																
MO.1030	Initial Mobilization for Predrilling of BP (CCF / KD07 / KD03)	23-Jul-21	07-Sep-21	174	23-Jul-21 A	21-Feb-22	152	85%																
MO.1040	Initial Mobilization for Predrilling of BP (CCG / KD08 / KD04)	23-Jul-21	07-Sep-21	134	23-Jul-21 A	03-Jan-22	192	90%																
MO.1050	Initial Mobilization for Predrilling of BP (CCH / KD09 / KD02)	23-Jul-21	07-Sep-21	144	23-Jul-21 A	13-Jan-22	18	60%																
Predrilling																								
PD.1000	Predrilling for BP in KD01 [8 nos.]	30-Sep-21	30-Mar-22	148	30-Sep-21 A	30-Mar-22	24	87%																
PD.1020	Predrilling for BP in KD02 [4 nos.]	19-Nov-21	23-Dec-21	36	30-Nov-21 A	13-Jan-22	18	75%																
PD.1040	Predrilling for BP in KD03 [5 nos.]	20-Oct-21	06-May-22	160	20-Oct-21 A	06-May-22	93	80%																
PD.1060	Predrilling for BP in KD04 [3 nos.] incl. 1 additional no.	30-Sep-21	30-Mar-22	143	30-Sep-21 A	31-Mar-22	113	66%																
PD.1080	Predrilling for BP in KD05 [76 nos.]	30-Sep-21	30-Mar-22	149	30-Sep-21 A	31-Mar-22	29	55%																
PD.1100	Predrilling for BP in KD06 [95 nos.] incl. 5 additional nos.	30-Sep-21	23-May-22	187	30-Sep-21 A	23-May-22	119	40%																
PD.1120	Predrilling for BP in KD07 [90 nos.] incl. 2 additional nos.	30-Sep-21	23-May-22	188	30-Sep-21 A	24-May-22	210	71%																
PD.1140	Predrilling for BP in KD08 [74 nos.] incl. 1 additional no.	30-Sep-21	30-Mar-22	148	30-Sep-21 A	31-Mar-22	142	95%																
PD.1160	Predrilling for BP in KD09 [149 nos.] incl. 4 additional nos.	30-Sep-21	30-Mar-22	149	30-Sep-21 A	30-Mar-22	157	48%																
PD.1170	Predrilling for SSHP [12 nos.]	30-Sep-21	22-Oct-21	37	01-Dec-21 A	31-Jan-22 A		100%																
KD01 (Stage 1-1)																								
Bored Piles																								
CD01																								
02																								
P23-BP22.20	BP - RCD Drilling	23-Dec-21	17-Jan-22	17	27-Nov-21 A	17-Dec-21 A		100%																
P23-BP22.30	BP - Airlift, Cage Install and Concrete	18-Jan-22	26-Jan-22	17	18-Dec-21 A	10-Jan-22	101	12.5%																
CD07																								
01																								
CBA-BPC41K.10	BP - Excavation	19-Jan-22	25-Jan-22	6	19-Jan-22	25-Jan-22	14	0%																

ID: 2B2C-20211231_bw
Data Date: 01-Jan-22
Print Date: 03-Jan-22_ 14:19
Page 3 of 20

Planned Bar

Critical Bar

Baseline

Milestone

Critical MS

Baseline MS

West Kowloon Cultural District Authority

Piling for Integrated Basement and U/G Road in Zone 2B 2C

3 Month Rolling Programme as of 31 Dec 2021


Based on CMWP 4th Draft

VIBRO

Date	Revision	Checked	Approved
06-Aug-21	1st Draft	KL	N
29-Sep-21	2nd Draft	KL	N
25-Oct-21	3rd Draft	KL	C
26-Nov-21	4th Draft	KL	

<div>ID: 2B2C-20211231_bw Data Date: 01-Jan-22 Print Date: 03-Jan-22_14:19 Page 4 of 20</div>	<div><div><div></div>Planned Bar</div><div></div><div></div><div></div><div></div><div></div></div> <div><div></div>Milestone</div> <div></div> <div></div> <div></div> <div></div> <div></div> <div><div></div>Critical Bar</div> <div></div> <div></div> <div></div> <div></div> <div></div> <div><div></div>Critical MS</div> <div></div> <div></div> <div></div> <div></div> <div></div> <div><div></div>Baseline</div> <div></div> <div></div> <div></div> <div></div> <div></div> <div><div></div>Baseline MS</div> <div></div> <div></div> <div></div> <div></div> <div></div>	<div><div>West Kowloon Cultural District Authority</div><div>Piling for Integrated Basement and U/G Road in Zone 2B 2C</div><div>3 Month Rolling Programme as of 31 Dec 2021</div><div>Based on CMWP 4th Draft</div></div>	<div><div>VIBRO</div><div></div><div></div></div>	<table><tr><th>Date</th><th>Revision</th><th>Checked</th><th>Approved</th></tr><tr><td>06-Aug-21</td><td>1st Draft</td><td>KL</td><td>N</td></tr><tr><td>29-Sep-21</td><td>2nd Draft</td><td>KL</td><td>N</td></tr><tr><td>25-Oct-21</td><td>3rd Draft</td><td>KL</td><td>C</td></tr><tr><td>26-Nov-21</td><td>4th Draft</td><td>KL</td><td></td></tr></table>	Date	Revision	Checked	Approved	06-Aug-21	1st Draft	KL	N	29-Sep-21	2nd Draft	KL	N	25-Oct-21	3rd Draft	KL	C	26-Nov-21	4th Draft	KL	
Date	Revision	Checked	Approved																					
06-Aug-21	1st Draft	KL	N																					
29-Sep-21	2nd Draft	KL	N																					
25-Oct-21	3rd Draft	KL	C																					
26-Nov-21	4th Draft	KL																						

Activity ID	Activity Name	CMWP 4th Draft Start	CMWP 4th Draft Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	December				January				February				March			
									-1				1				2				3			
									03	10	17	24	31	07	14	21	28	04	11	18	25	04	11	18
01																								
P23-BP76.10	BP - Excavation	03-Dec-21	09-Dec-21	11	24-Dec-21 A	08-Jan-22	-10	0%																
P23-BP76.20	BP - RCD Drilling	10-Dec-21	30-Dec-21	16	10-Jan-22	27-Jan-22	-10	0%																
P23-BP76.30	BP - Airlift, Cage Install and Concrete	31-Dec-21	10-Jan-22	8	28-Jan-22	09-Feb-22	-10	0%																
02																								
P23-BP87.10	BP - Excavation	03-Dec-21	09-Dec-21	6	03-Jan-22	08-Jan-22	-10	0%																
P23-BP87.20	BP - RCD Drilling	10-Dec-21	10-Jan-22	24	10-Jan-22	09-Feb-22	-10	0%																
P23-BP87.30	BP - Airlift, Cage Install and Concrete	11-Jan-22	19-Jan-22	8	10-Feb-22	18-Feb-22	-10	0%																
03																								
P23-BP117.10	BP - Excavation	03-Dec-21	09-Dec-21	6	03-Jan-22	08-Jan-22	-10	0%																
P23-BP117.20	BP - RCD Drilling	10-Dec-21	10-Jan-22	24	10-Jan-22	09-Feb-22	-10	0%																
P23-BP117.30	BP - Airlift, Cage Install and Concrete	20-Jan-22	28-Jan-22	8	10-Feb-22	18-Feb-22	-10	0%																
KD03 (Stage 3-1)																								
KD03.BP.0040	Review and Confirmation of Rockhead and Founding Level of Pile by CA	14-Nov-21	27-Nov-21	14	01-Jan-22	14-Jan-22	4	0%																
Bored Piles																								
VD02																								
03																								
P28&29-BP08.10	BP - Excavation	18-Mar-22	24-Mar-22	6	18-Mar-22	24-Mar-22	37	0%																
P28&29-BP08.20	BP - RCD Drilling	25-Mar-22	12-Apr-22	15	25-Mar-22	12-Apr-22	37	0%																
VD06																								
01																								
P28&29-BP29.10	BP - Excavation	19-Jan-22	25-Jan-22	6	19-Jan-22	25-Jan-22	0	0%																
P28&29-BP29.20	BP - RCD Drilling	26-Jan-22	15-Feb-22	15	26-Jan-22	15-Feb-22	0	0%																
P28&29-BP29.30	BP - Airlift, Cage Install and Concrete	16-Feb-22	23-Feb-22	7	16-Feb-22	23-Feb-22	80	0%																
VD09																								
01																								
CBA-BPC54Jb.10	BP - Excavation	26-Feb-22	04-Mar-22	6	26-Feb-22	04-Mar-22	0	0%																
CBA-BPC54Jb.20	BP - RCD Drilling	05-Mar-22	11-Apr-22	31	05-Mar-22	11-Apr-22	0	0%																
KD04 (Stage 4-1)																								
KD04.BP.0040	Review and Confirmation of Rockhead and Founding Level of Pile by CA	03-Nov-21	16-Nov-21	77	30-Oct-21 A	14-Jan-22	83	0%																
KD05 (Section 1)																								
ID: 2B2C-20211231_bw Data Date: 01-Jan-22 Print Date: 03-Jan-22_ 14:19 Page 5 of 20		<div><div></div>Planned Bar<div></div>Critical Bar<div></div>Baseline</div> <div><div></div>Milestone<div></div>Critical MS<div></div>Baseline MS</div>			West Kowloon Cultural District Authority Piling for Integrated Basement and U/G Road in Zone 2B 2C 3 Month Rolling Programme as of 31 Dec 2021 Based on CMWP 4th Draft				<div>VIBRO</div> <div></div> <div></div>			Date	Revision	Checked	Approved									
												06-Aug-21	1st Draft	KL	N									
												29-Sep-21	2nd Draft	KL	N									
												25-Oct-21	3rd Draft	KL	C									
												26-Nov-21	4th Draft	KL										

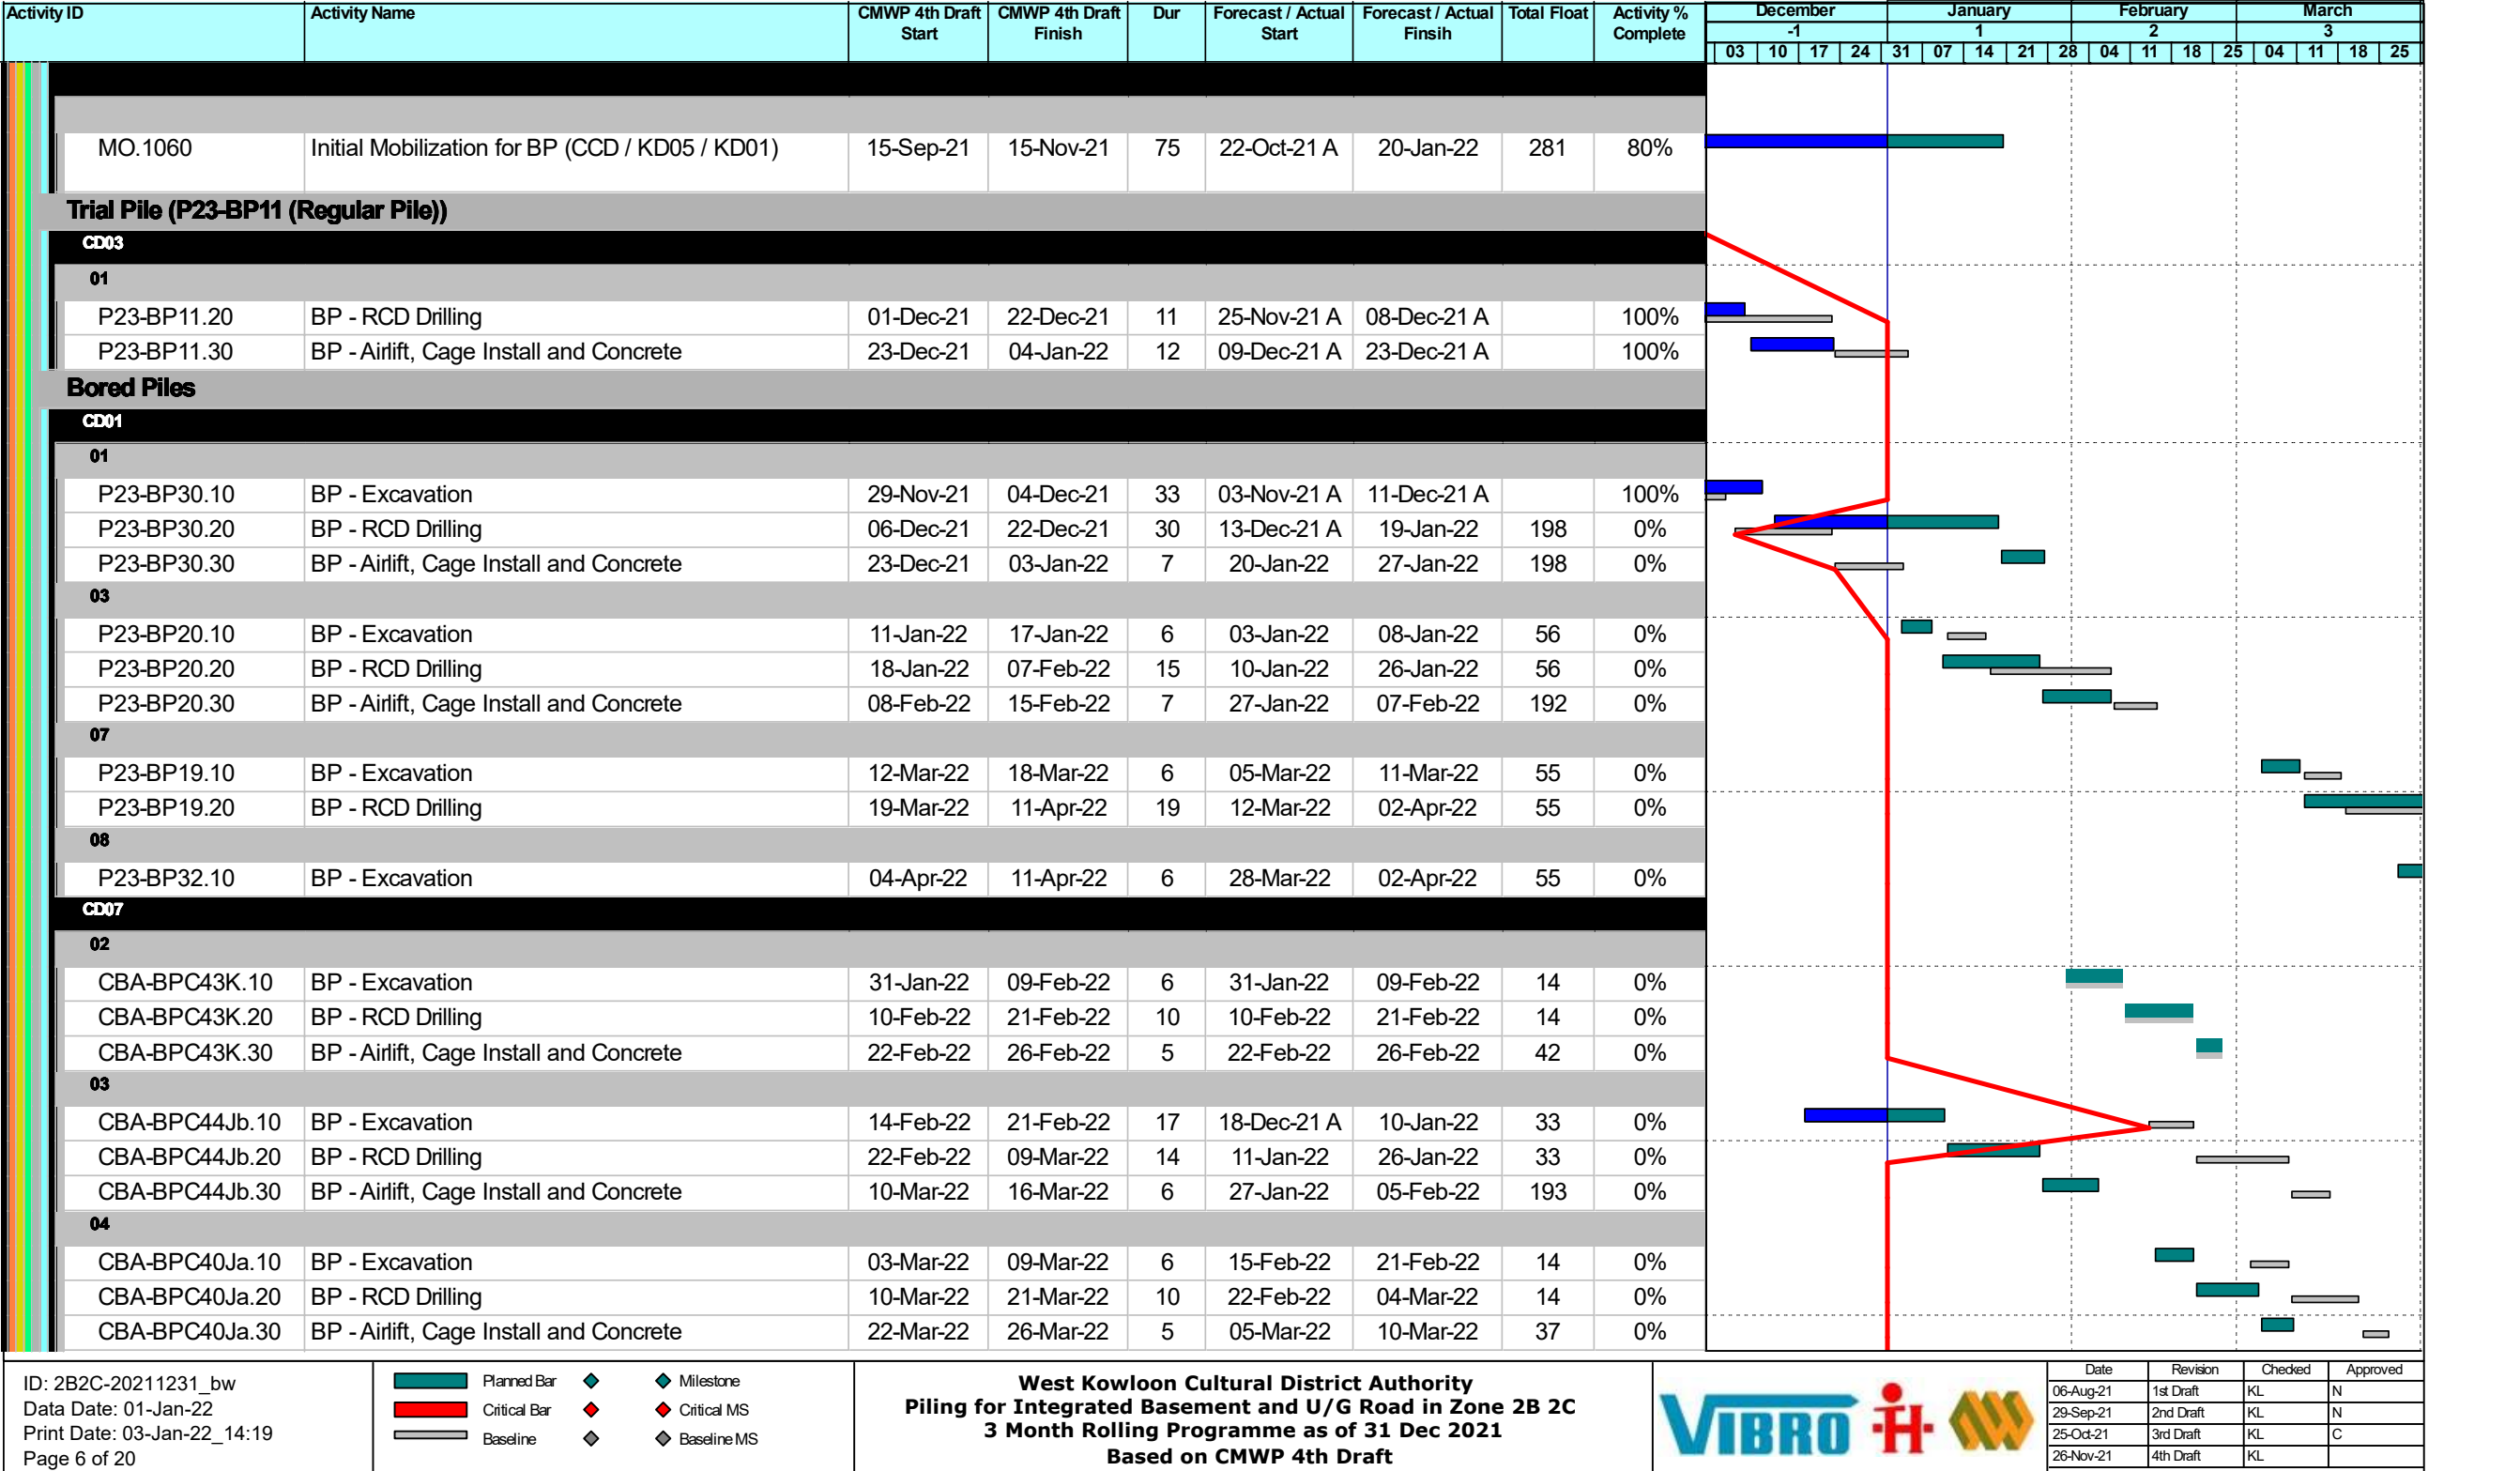

Activity ID	Activity Name	CMWP 4th Draft Start	CMWP 4th Draft Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	December				January				February				March				
									-1				1				2				3				
									03	10	17	24	31	07	14	21	28	04	11	18	25	04	11	18	25
05																									
CBA-BPC42K.10	BP - Excavation	15-Mar-22	21-Mar-22	6	26-Feb-22	04-Mar-22	14	0%																	
CBA-BPC42K.20	BP - RCD Drilling	22-Mar-22	01-Apr-22	10	05-Mar-22	16-Mar-22	14	0%																	
CBA-BPC42K.30	BP - Airlift, Cage Install and Concrete	02-Apr-22	08-Apr-22	5	17-Mar-22	22-Mar-22	32	0%																	
06																									
CBA-BPC44K.10	BP - Excavation	25-Mar-22	01-Apr-22	7	09-Mar-22	16-Mar-22	14	0%																	
CBA-BPC44K.20	BP - RCD Drilling	02-Apr-22	22-Apr-22	14	17-Mar-22	01-Apr-22	14	0%																	
13																									
CBA-BP01.10	BP - Excavation	25-Mar-22	01-Apr-22	7	09-Mar-22	16-Mar-22	14	0%																	
CBA-BP01.20	BP - RCD Drilling	02-Apr-22	22-Apr-22	14	17-Mar-22	01-Apr-22	14	0%																	
CD05																									
01																									
P22&P19-BP04.10	BP - Excavation	19-Nov-21	25-Nov-21	6	03-Jan-22	08-Jan-22	187	0%																	
P22&P19-BP04.20	BP - RCD Drilling	26-Nov-21	17-Dec-21	19	10-Jan-22	31-Jan-22	187	0%																	
P22&P19-BP04.30	BP - Airlift, Cage Install and Concrete	18-Dec-21	29-Dec-21	8	04-Feb-22	12-Feb-22	187	0%																	
02																									
P22&P19-BP05.10	BP - Excavation	11-Dec-21	17-Dec-21	7	09-Dec-21 A	17-Dec-21 A		100%																	
P22&P19-BP05.20	BP - RCD Drilling	18-Dec-21	12-Jan-22	29	18-Dec-21 A	24-Jan-22	9	0%																	
P22&P19-BP05.30	BP - Airlift, Cage Install and Concrete	13-Jan-22	21-Jan-22	8	25-Jan-22	05-Feb-22	42	0%																	
03																									
P17-BP05.10	BP - Excavation	06-Jan-22	12-Jan-22	6	18-Jan-22	24-Jan-22	9	0%																	
P17-BP05.20	BP - RCD Drilling	13-Jan-22	29-Jan-22	15	25-Jan-22	14-Feb-22	9	0%																	
P17-BP05.30	BP - Airlift, Cage Install and Concrete	31-Jan-22	10-Feb-22	7	15-Feb-22	22-Feb-22	35	0%																	
06																									
P22&P19-BP15.10	BP - Excavation	12-Mar-22	18-Mar-22	6	02-Mar-22	08-Mar-22	9	0%																	
P22&P19-BP15.20	BP - RCD Drilling	19-Mar-22	11-Apr-22	19	09-Mar-22	30-Mar-22	9	0%																	
11																									
P22&P19-BP26.10	BP - Excavation	06-Jan-22	12-Jan-22	6	18-Jan-22	24-Jan-22	88	0%																	
P22&P19-BP26.20	BP - RCD Drilling	13-Jan-22	18-Feb-22	29	25-Jan-22	02-Mar-22	88	0%																	
P22&P19-BP26.30	BP - Airlift, Cage Install and Concrete	19-Feb-22	28-Feb-22	8	03-Mar-22	11-Mar-22	132	0%																	
13																									
P22&P19-BP25.10	BP - Excavation	07-Mar-22	12-Mar-22	6	18-Mar-22	24-Mar-22	88	0%																	
P22&P19-BP25.20	BP - RCD Drilling	14-Mar-22	04-Apr-22	19	25-Mar-22	20-Apr-22	88	0%																	
CD04																									
01																									
P17-BP03.10	BP - Excavation	24-Nov-21	30-Nov-21	6	03-Jan-22	08-Jan-22	38	0%																	
P17-BP03.20	BP - RCD Drilling	01-Dec-21	17-Dec-21	15	10-Jan-22	26-Jan-22	38	0%																	

ID: 2B2C-20211231_bw
Data Date: 01-Jan-22
Print Date: 03-Jan-22_ 14:19
Page 7 of 20

Planned Bar

Critical Bar

Baseline

Milestone

Critical MS

Baseline MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 31 Dec 2021
Based on CMWP 4th Draft

VIBRO

Date	Revision	Checked	Approved
06-Aug-21	1st Draft	KL	N
29-Sep-21	2nd Draft	KL	N
25-Oct-21	3rd Draft	KL	C
26-Nov-21	4th Draft	KL	

Activity ID	Activity Name	CMWP 4th Draft Start	CMWP 4th Draft Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	December				January				February				March				
									-1				1				2				3				
									03	10	17	24	31	07	14	21	28	04	11	18	25	04	11	18	25
P17-BP03.30	BP - Airlift, Cage Install and Concrete	18-Dec-21	28-Dec-21	7	27-Jan-22	07-Feb-22	121	0%																	
	02																								
	P17-BP12.10	BP - Excavation	20-Dec-21	28-Dec-21	6	20-Jan-22	26-Jan-22	38	0%																
	P17-BP12.20	BP - RCD Drilling	29-Dec-21	15-Jan-22	15	27-Jan-22	16-Feb-22	38	0%																
	P17-BP12.30	BP - Airlift, Cage Install and Concrete	17-Jan-22	24-Jan-22	7	17-Feb-22	24-Feb-22	113	0%																
	03																								
	P17-BP10.10	BP - Excavation	10-Jan-22	15-Jan-22	6	10-Feb-22	16-Feb-22	38	0%																
	P17-BP10.20	BP - RCD Drilling	17-Jan-22	05-Feb-22	15	17-Feb-22	05-Mar-22	38	0%																
	P17-BP10.30	BP - Airlift, Cage Install and Concrete	07-Feb-22	14-Feb-22	7	07-Mar-22	14-Mar-22	105	0%																
	04																								
	P17-BP14.10	BP - Excavation	27-Jan-22	05-Feb-22	6	28-Feb-22	05-Mar-22	38	0%																
	P17-BP14.20	BP - RCD Drilling	07-Feb-22	28-Feb-22	19	07-Mar-22	28-Mar-22	38	0%																
	P17-BP14.30	BP - Airlift, Cage Install and Concrete	01-Mar-22	09-Mar-22	8	29-Mar-22	07-Apr-22	93	0%																
	05																								
	P17-BP16.10	BP - Excavation	22-Feb-22	28-Feb-22	6	22-Mar-22	28-Mar-22	38	0%																
	P17-BP16.20	BP - RCD Drilling	01-Mar-22	17-Mar-22	15	29-Mar-22	19-Apr-22	38	0%																
	CD03																								
	07																								
P23-BP05.10	BP - Excavation	29-Apr-22	06-May-22	10	23-Nov-21 A	04-Dec-21 A		100%																	
P23-BP05.20	BP - RCD Drilling	07-May-22	30-May-22	8	06-Dec-21 A	15-Dec-21 A		100%																	
P23-BP05.30	BP - Airlift, Cage Install and Concrete	31-May-22	09-Jun-22	20	16-Dec-21 A	11-Jan-22	212	0%																	
TD08																									
01																									
CBA-BPC40Jb.10	BP - Excavation	19-Nov-21	25-Nov-21	15	20-Dec-21 A	08-Jan-22	79	0%																	
CBA-BPC40Jb.20	BP - RCD Drilling	26-Nov-21	07-Dec-21	10	10-Jan-22	20-Jan-22	79	0%																	
CBA-BPC40Jb.30	BP - Airlift, Cage Install and Concrete	08-Dec-21	13-Dec-21	5	21-Jan-22	26-Jan-22	139	0%																	
02																									
CBA-BPC38Ja.10	BP - Excavation	01-Dec-21	07-Dec-21	6	14-Jan-22	20-Jan-22	79	0%																	
CBA-BPC38Ja.20	BP - RCD Drilling	08-Dec-21	18-Dec-21	10	21-Jan-22	04-Feb-22	79	0%																	
CBA-BPC38Ja.30	BP - Airlift, Cage Install and Concrete	20-Dec-21	24-Dec-21	5	05-Feb-22	10-Feb-22	134	0%																	
03																									
CBA-BPC38K.10	BP - Excavation	13-Dec-21	18-Dec-21	6	26-Jan-22	04-Feb-22	79	0%																	
CBA-BPC38K.20	BP - RCD Drilling	20-Dec-21	03-Jan-22	10	05-Feb-22	16-Feb-22	79	0%																	
CBA-BPC38K.30	BP - Airlift, Cage Install and Concrete	04-Jan-22	08-Jan-22	5	17-Feb-22	22-Feb-22	129	0%																	
04																									
CBA-BPC40M.10	BP - Excavation	24-Dec-21	03-Jan-22	6	10-Feb-22	16-Feb-22	79	0%																	
CBA-BPC40M.20	BP - RCD Drilling	04-Jan-22	14-Jan-22	10	17-Feb-22	28-Feb-22	79	0%																	

ID: 2B2C-20211231_bw
Data Date: 01-Jan-22
Print Date: 03-Jan-22_ 14:19
Page 8 of 20

Planned Bar

Critical Bar

Baseline

Milestone

Critical MS

Baseline MS

West Kowloon Cultural District Authority

Piling for Integrated Basement and U/G Road in Zone 2B 2C

3 Month Rolling Programme as of 31 Dec 2021


Based on CMWP 4th Draft


VIBRO


Date	Revision	Checked	Approved
06-Aug-21	1st Draft	KL	N
29-Sep-21	2nd Draft	KL	N
25-Oct-21	3rd Draft	KL	C
26-Nov-21	4th Draft	KL	





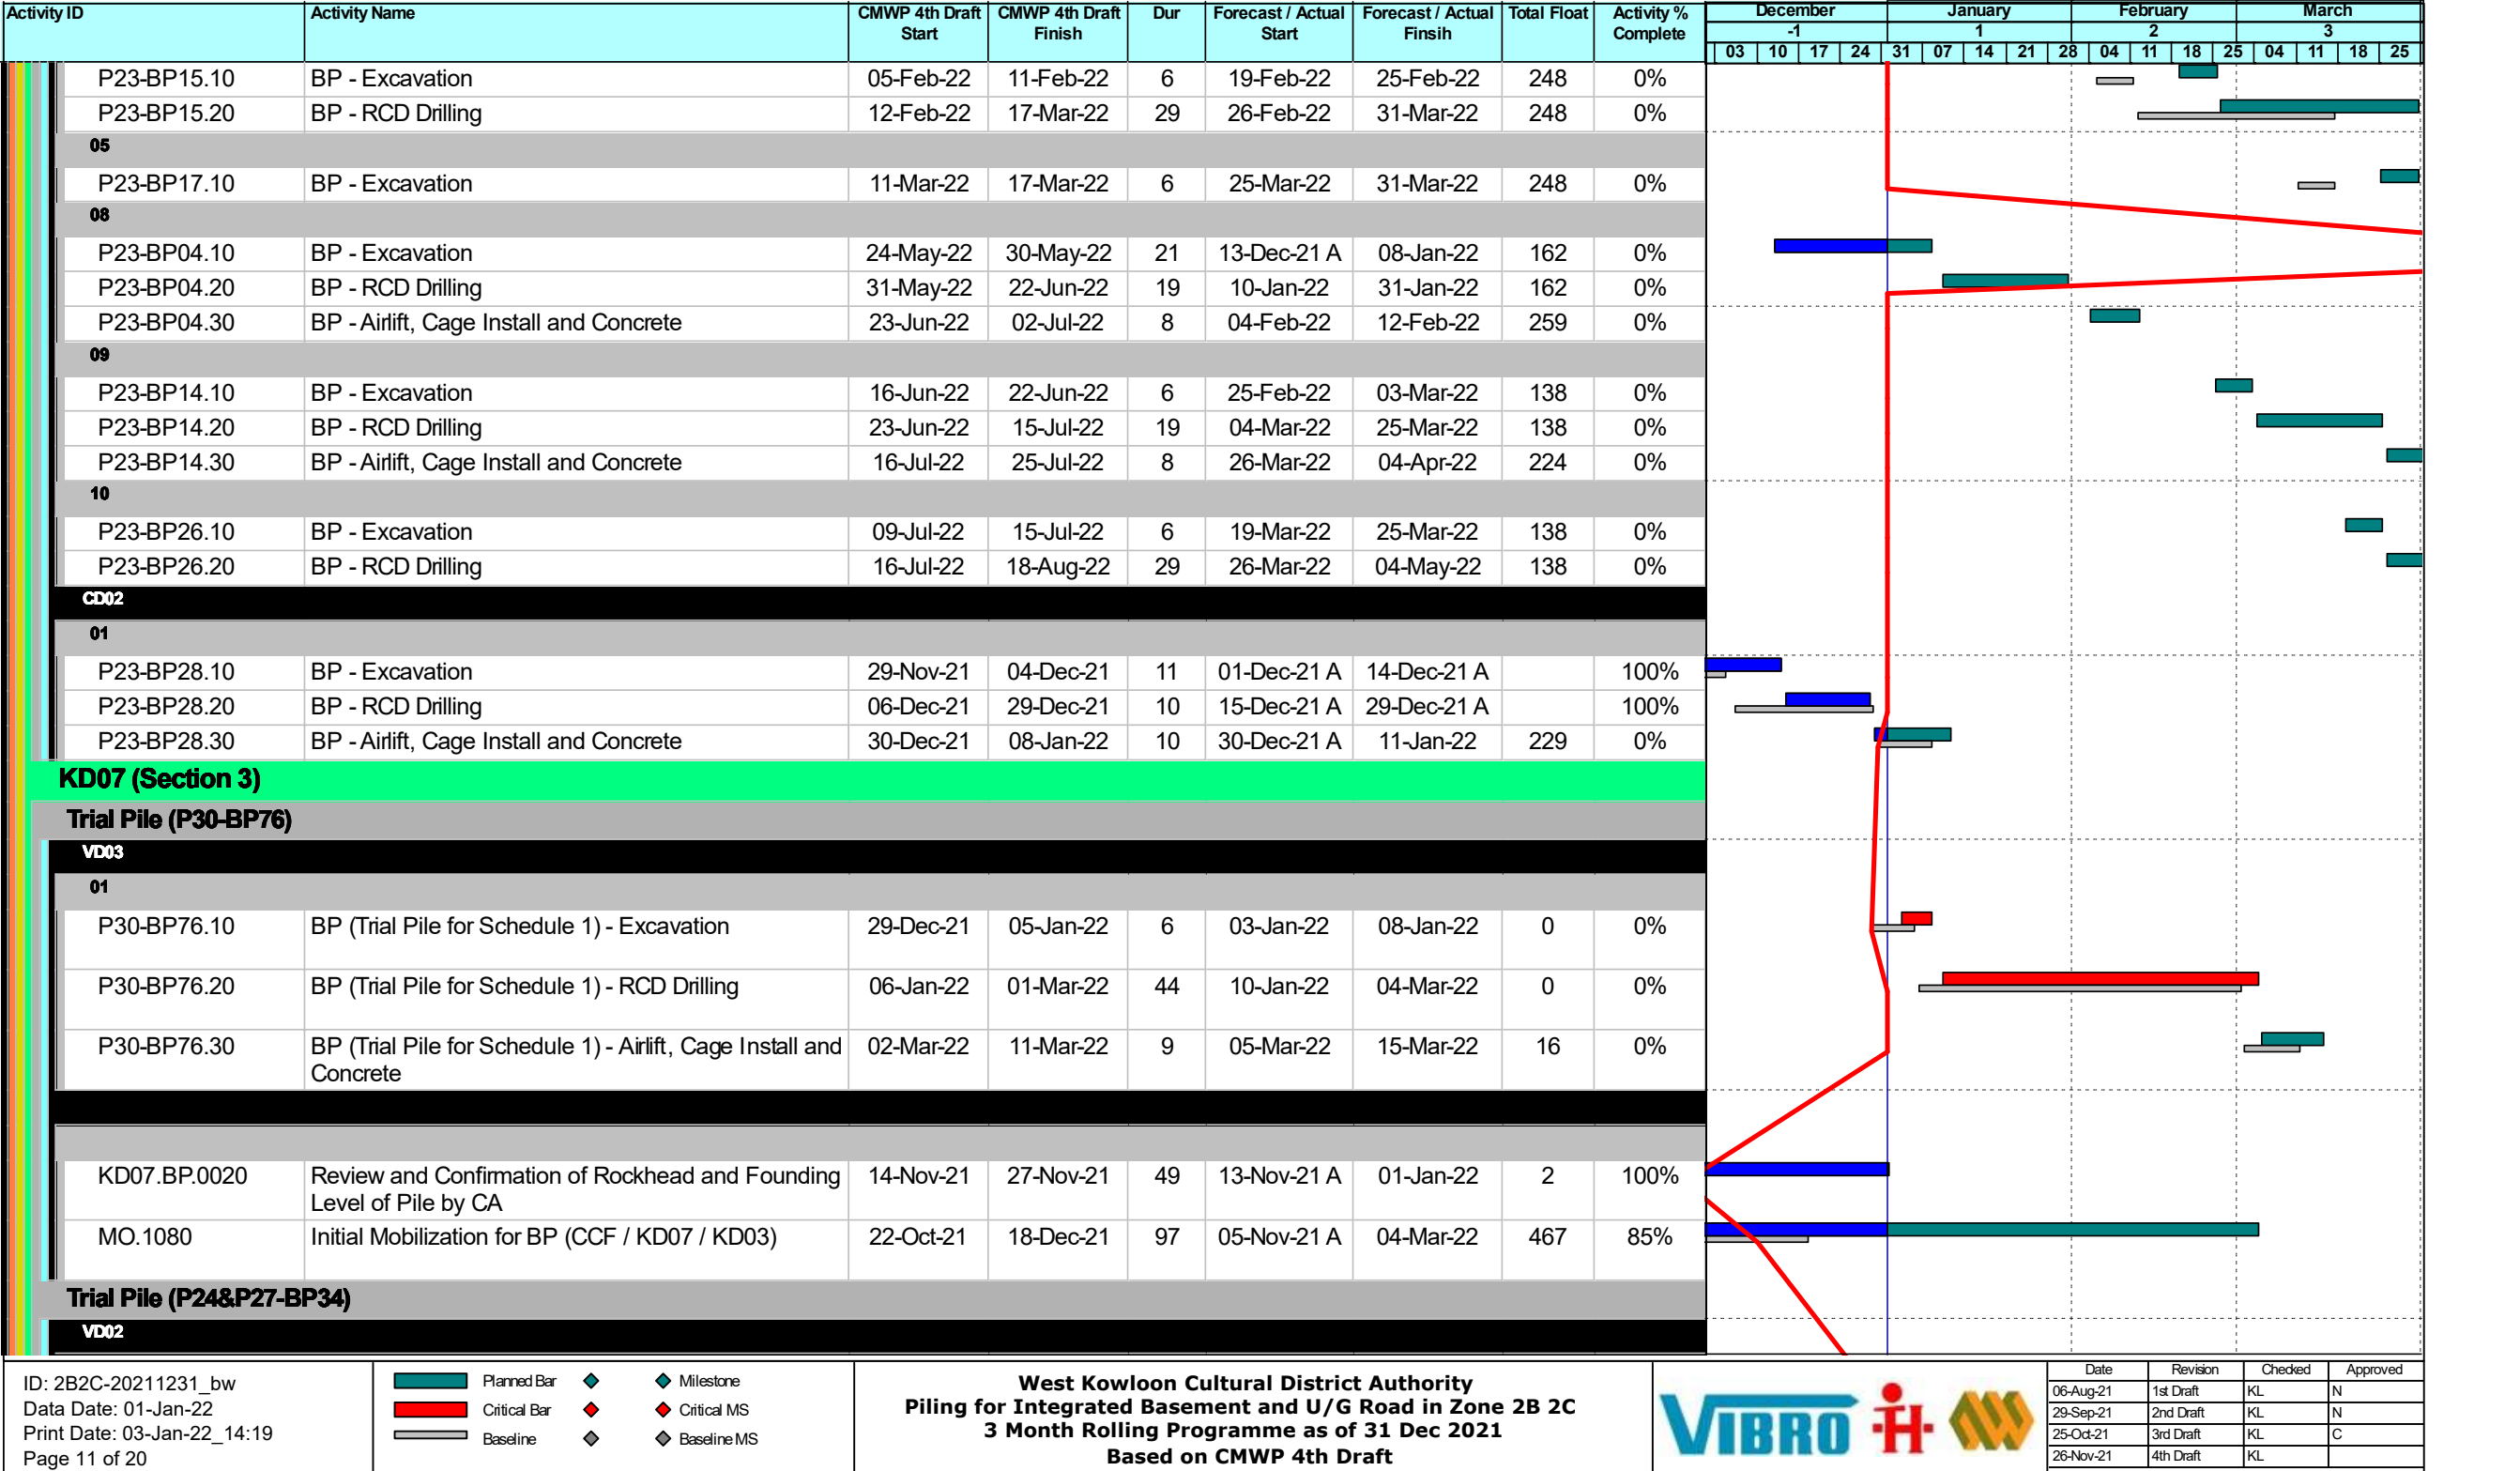

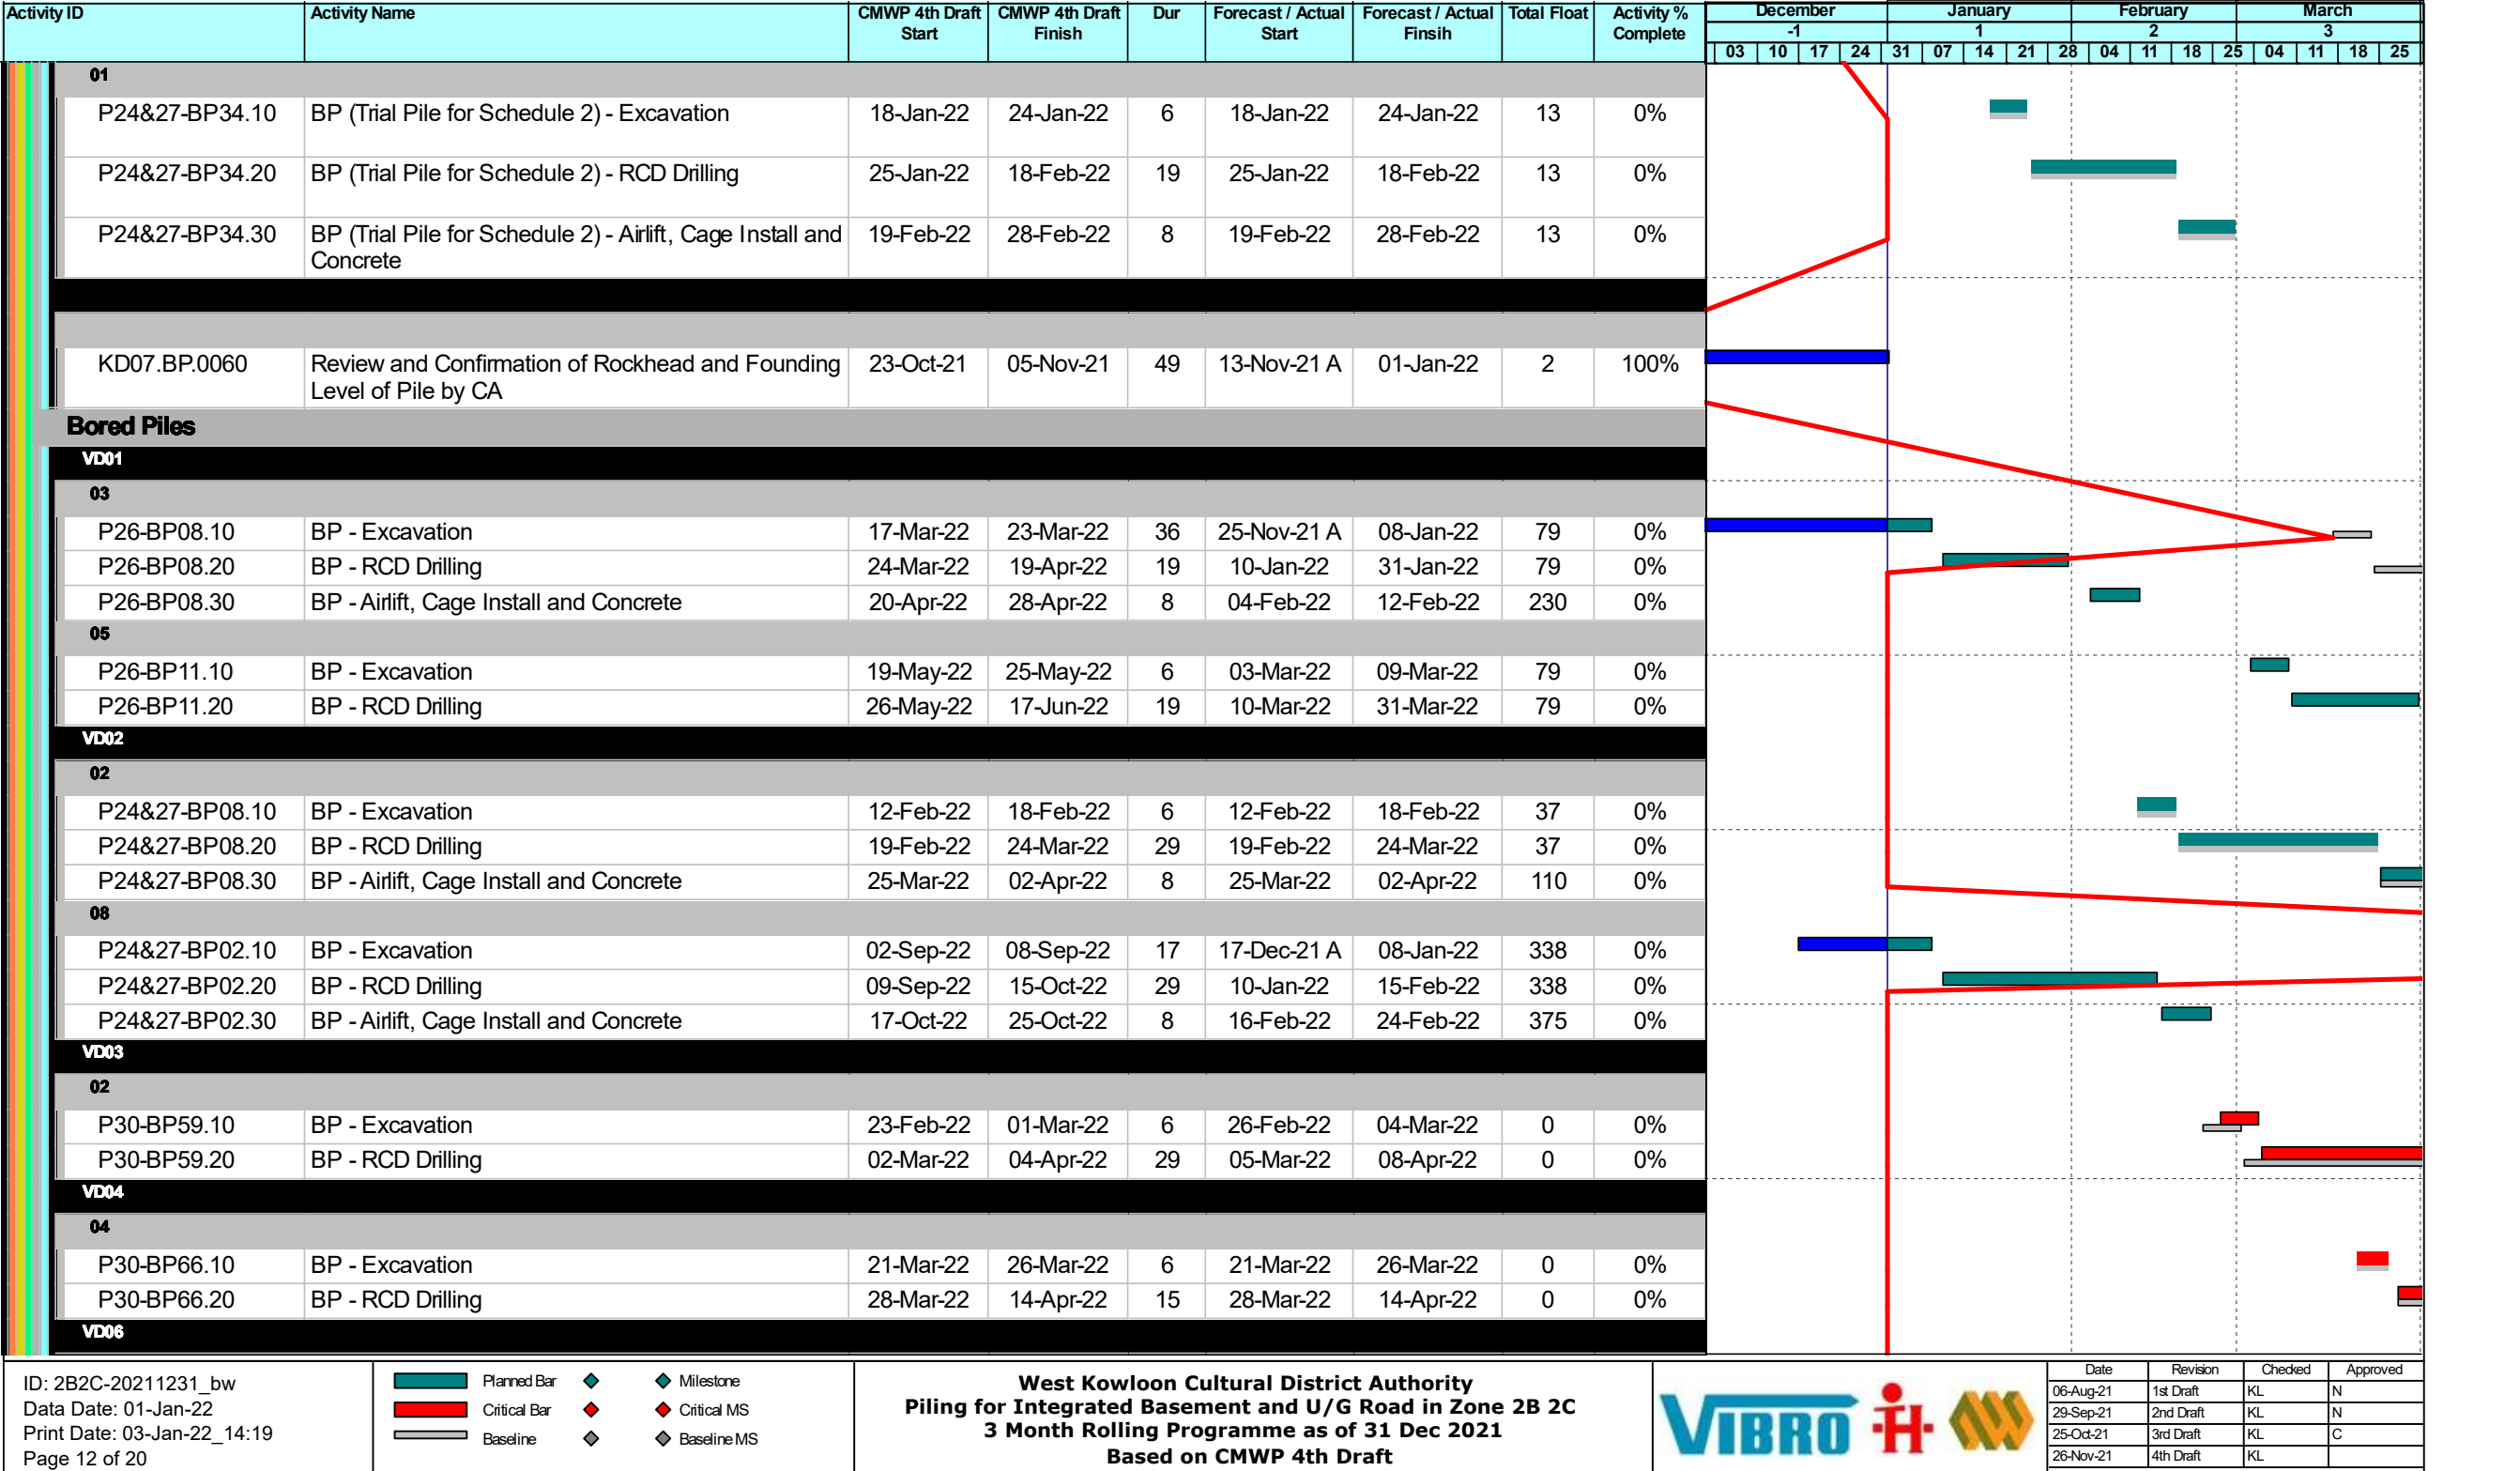Activity ID		Activity Name	CMWP 4th Draft Start	CMWP 4th Draft Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	December				January				February				March																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																		
										-1				1				2				3																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																		
										03	10	17	24	31	07	14	21	28	04	11	18	25	04	11	18	25																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																														
<div>2B2C-20211231_bw</div> <div>Data Date: 01-Jan-22</div> <div>Print Date: 03-Jan-22_ 14:19</div> <div>Page 9 of 20</div>		CBA-BPC40M.30	BP - Airlift, Cage Install and Concrete	15-Jan-22	20-Jan-22	5	01-Mar-22	05-Mar-22	124	0%																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																														</

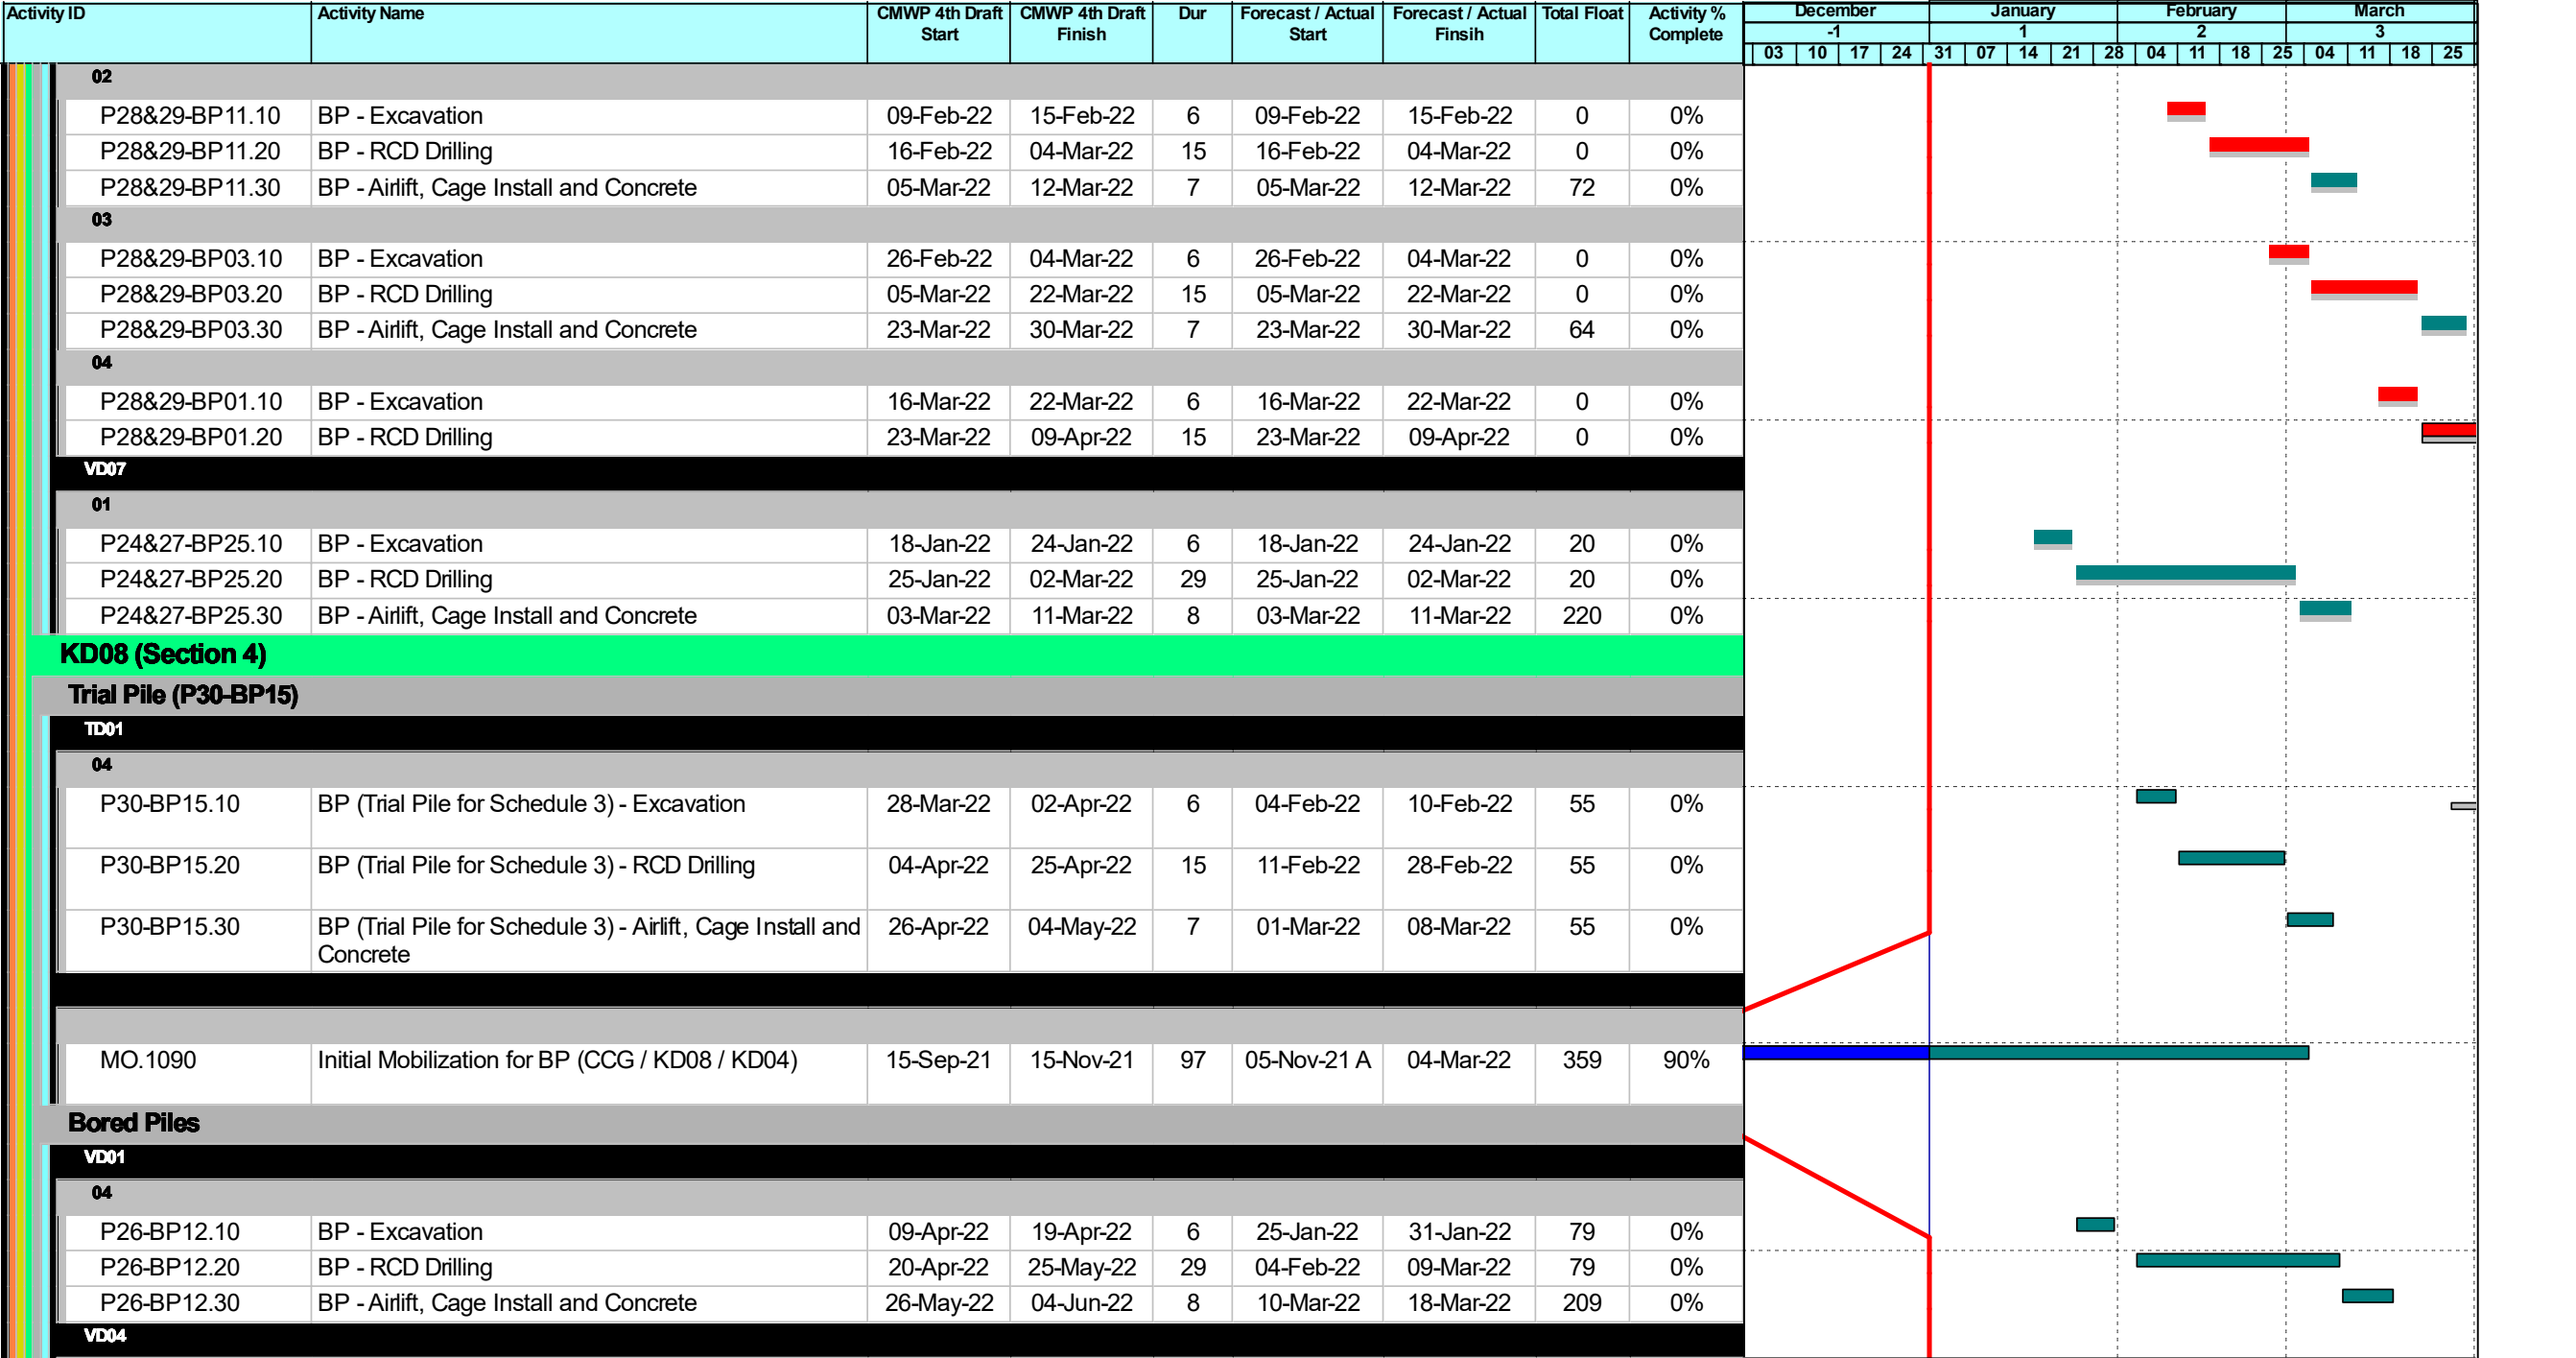
Activity ID	Activity Name	CMWP 4th Draft Start	CMWP 4th Draft Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	December				January				February				March			
									-1				1				2				3			
									03	10	17	24	31	07	14	21	28	04	11	18	25	04	11	18
<div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></</div></div>																								










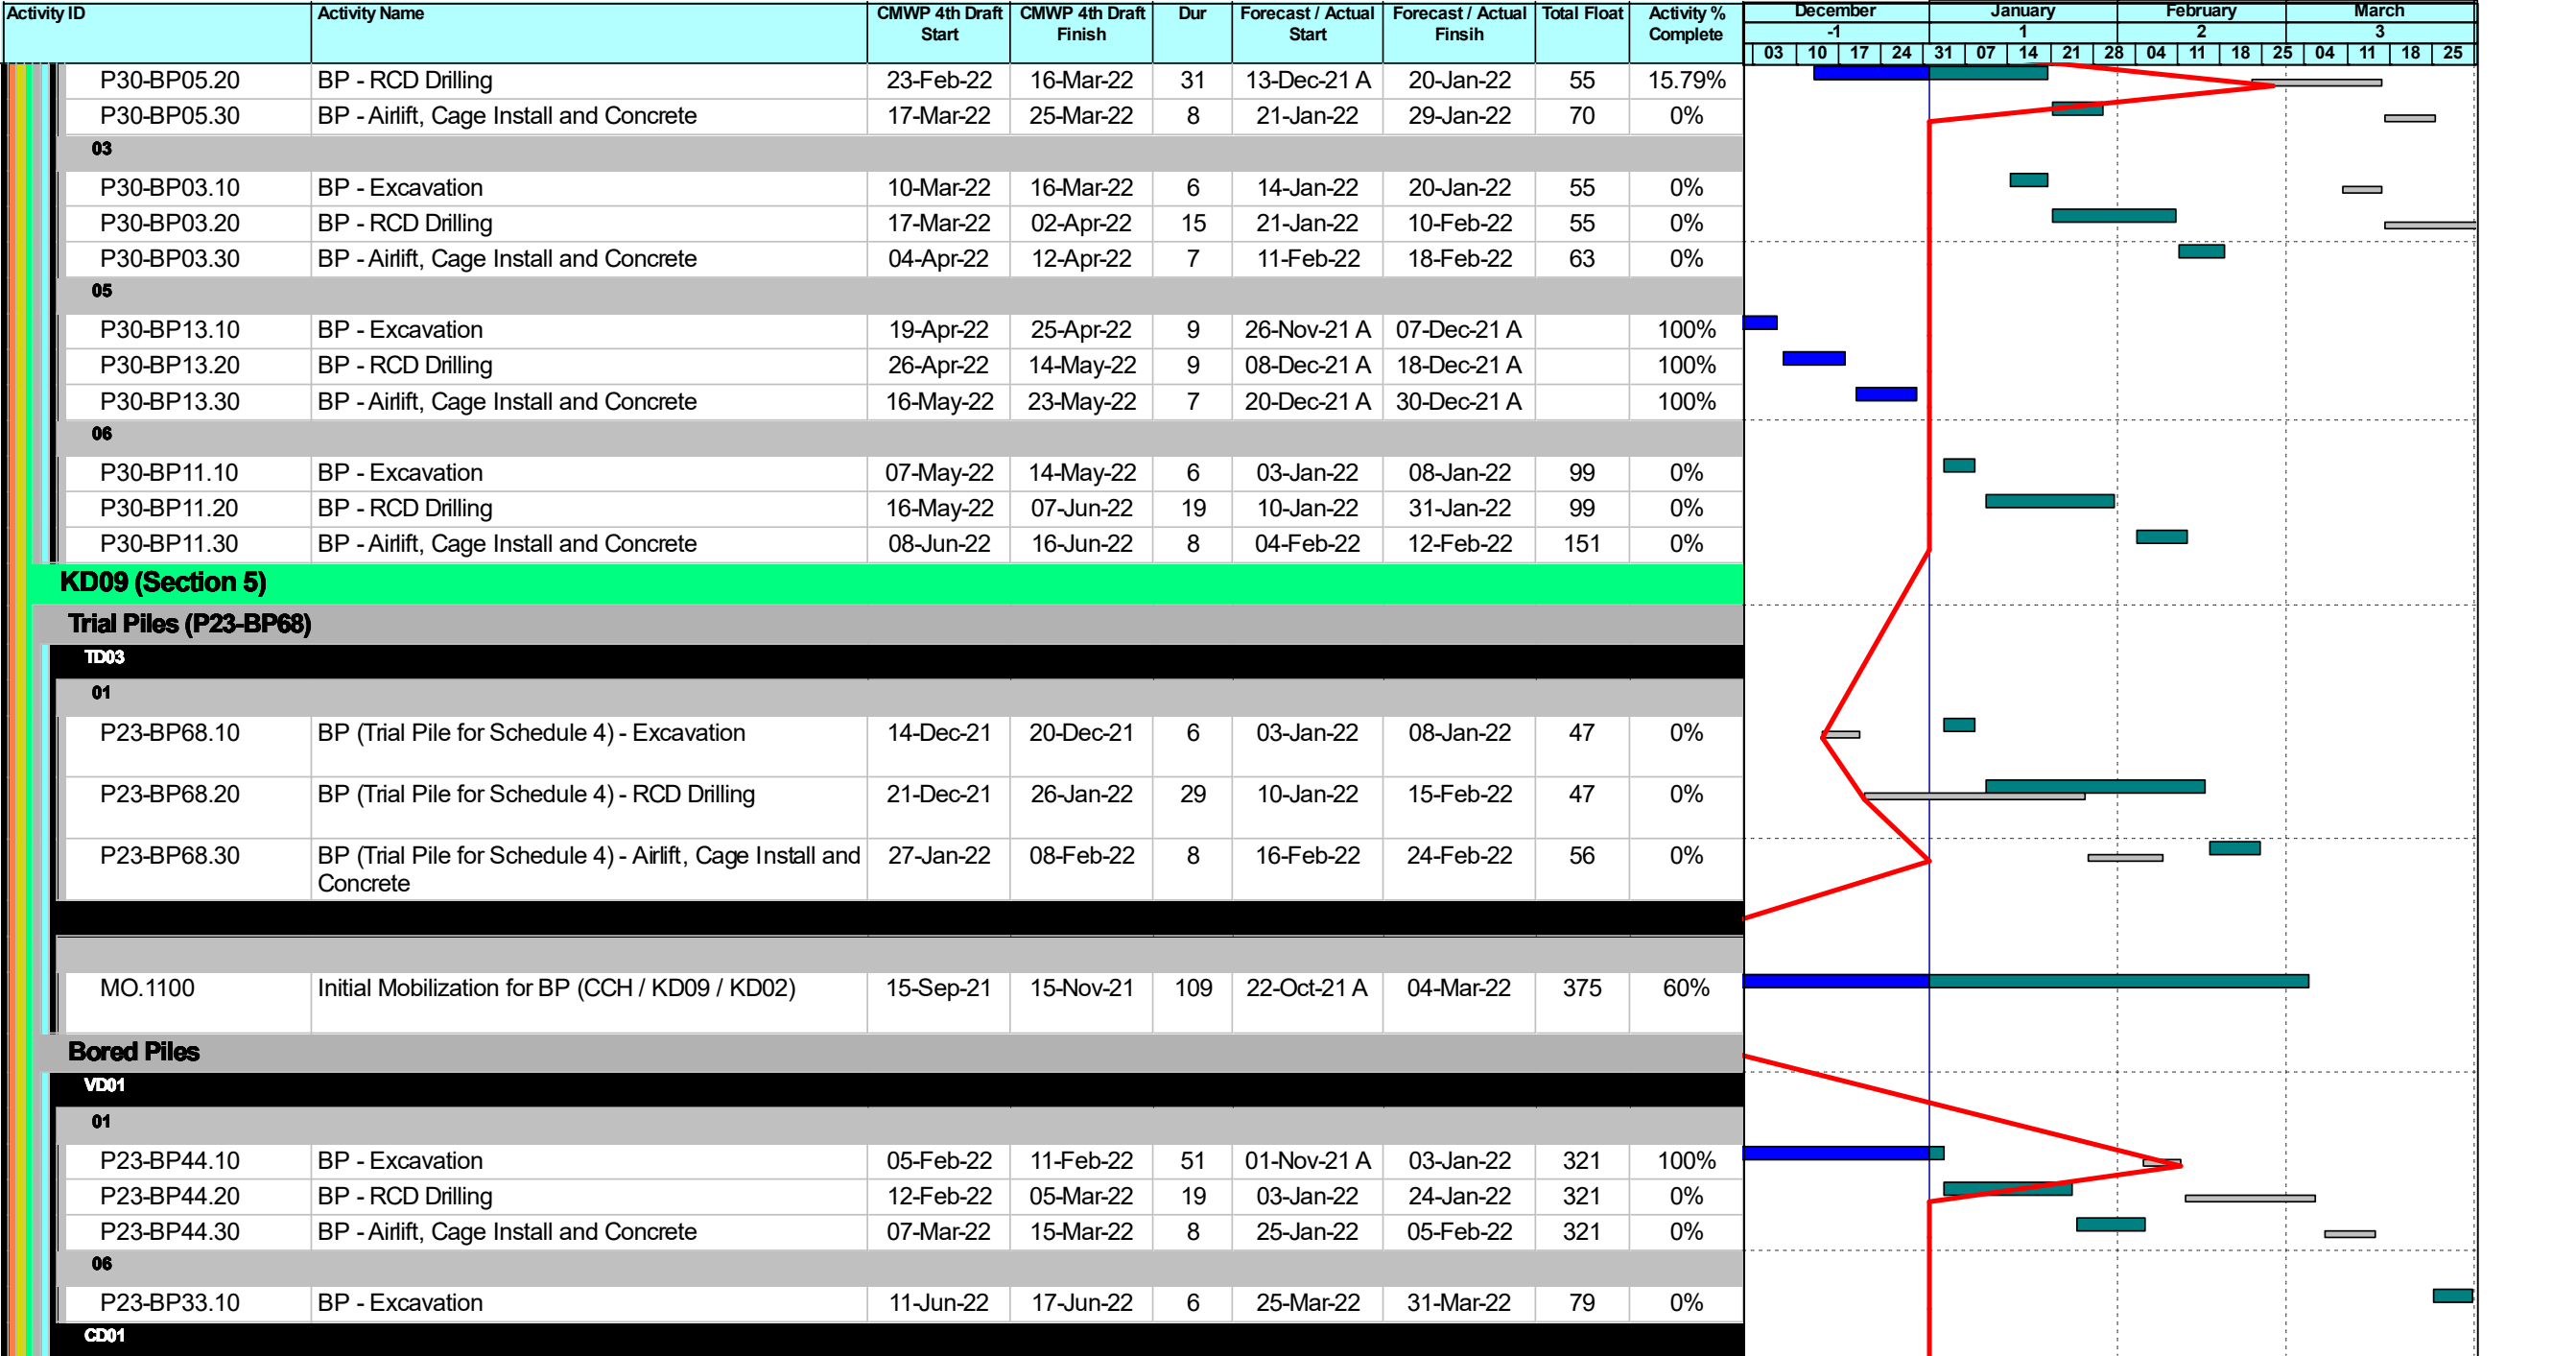

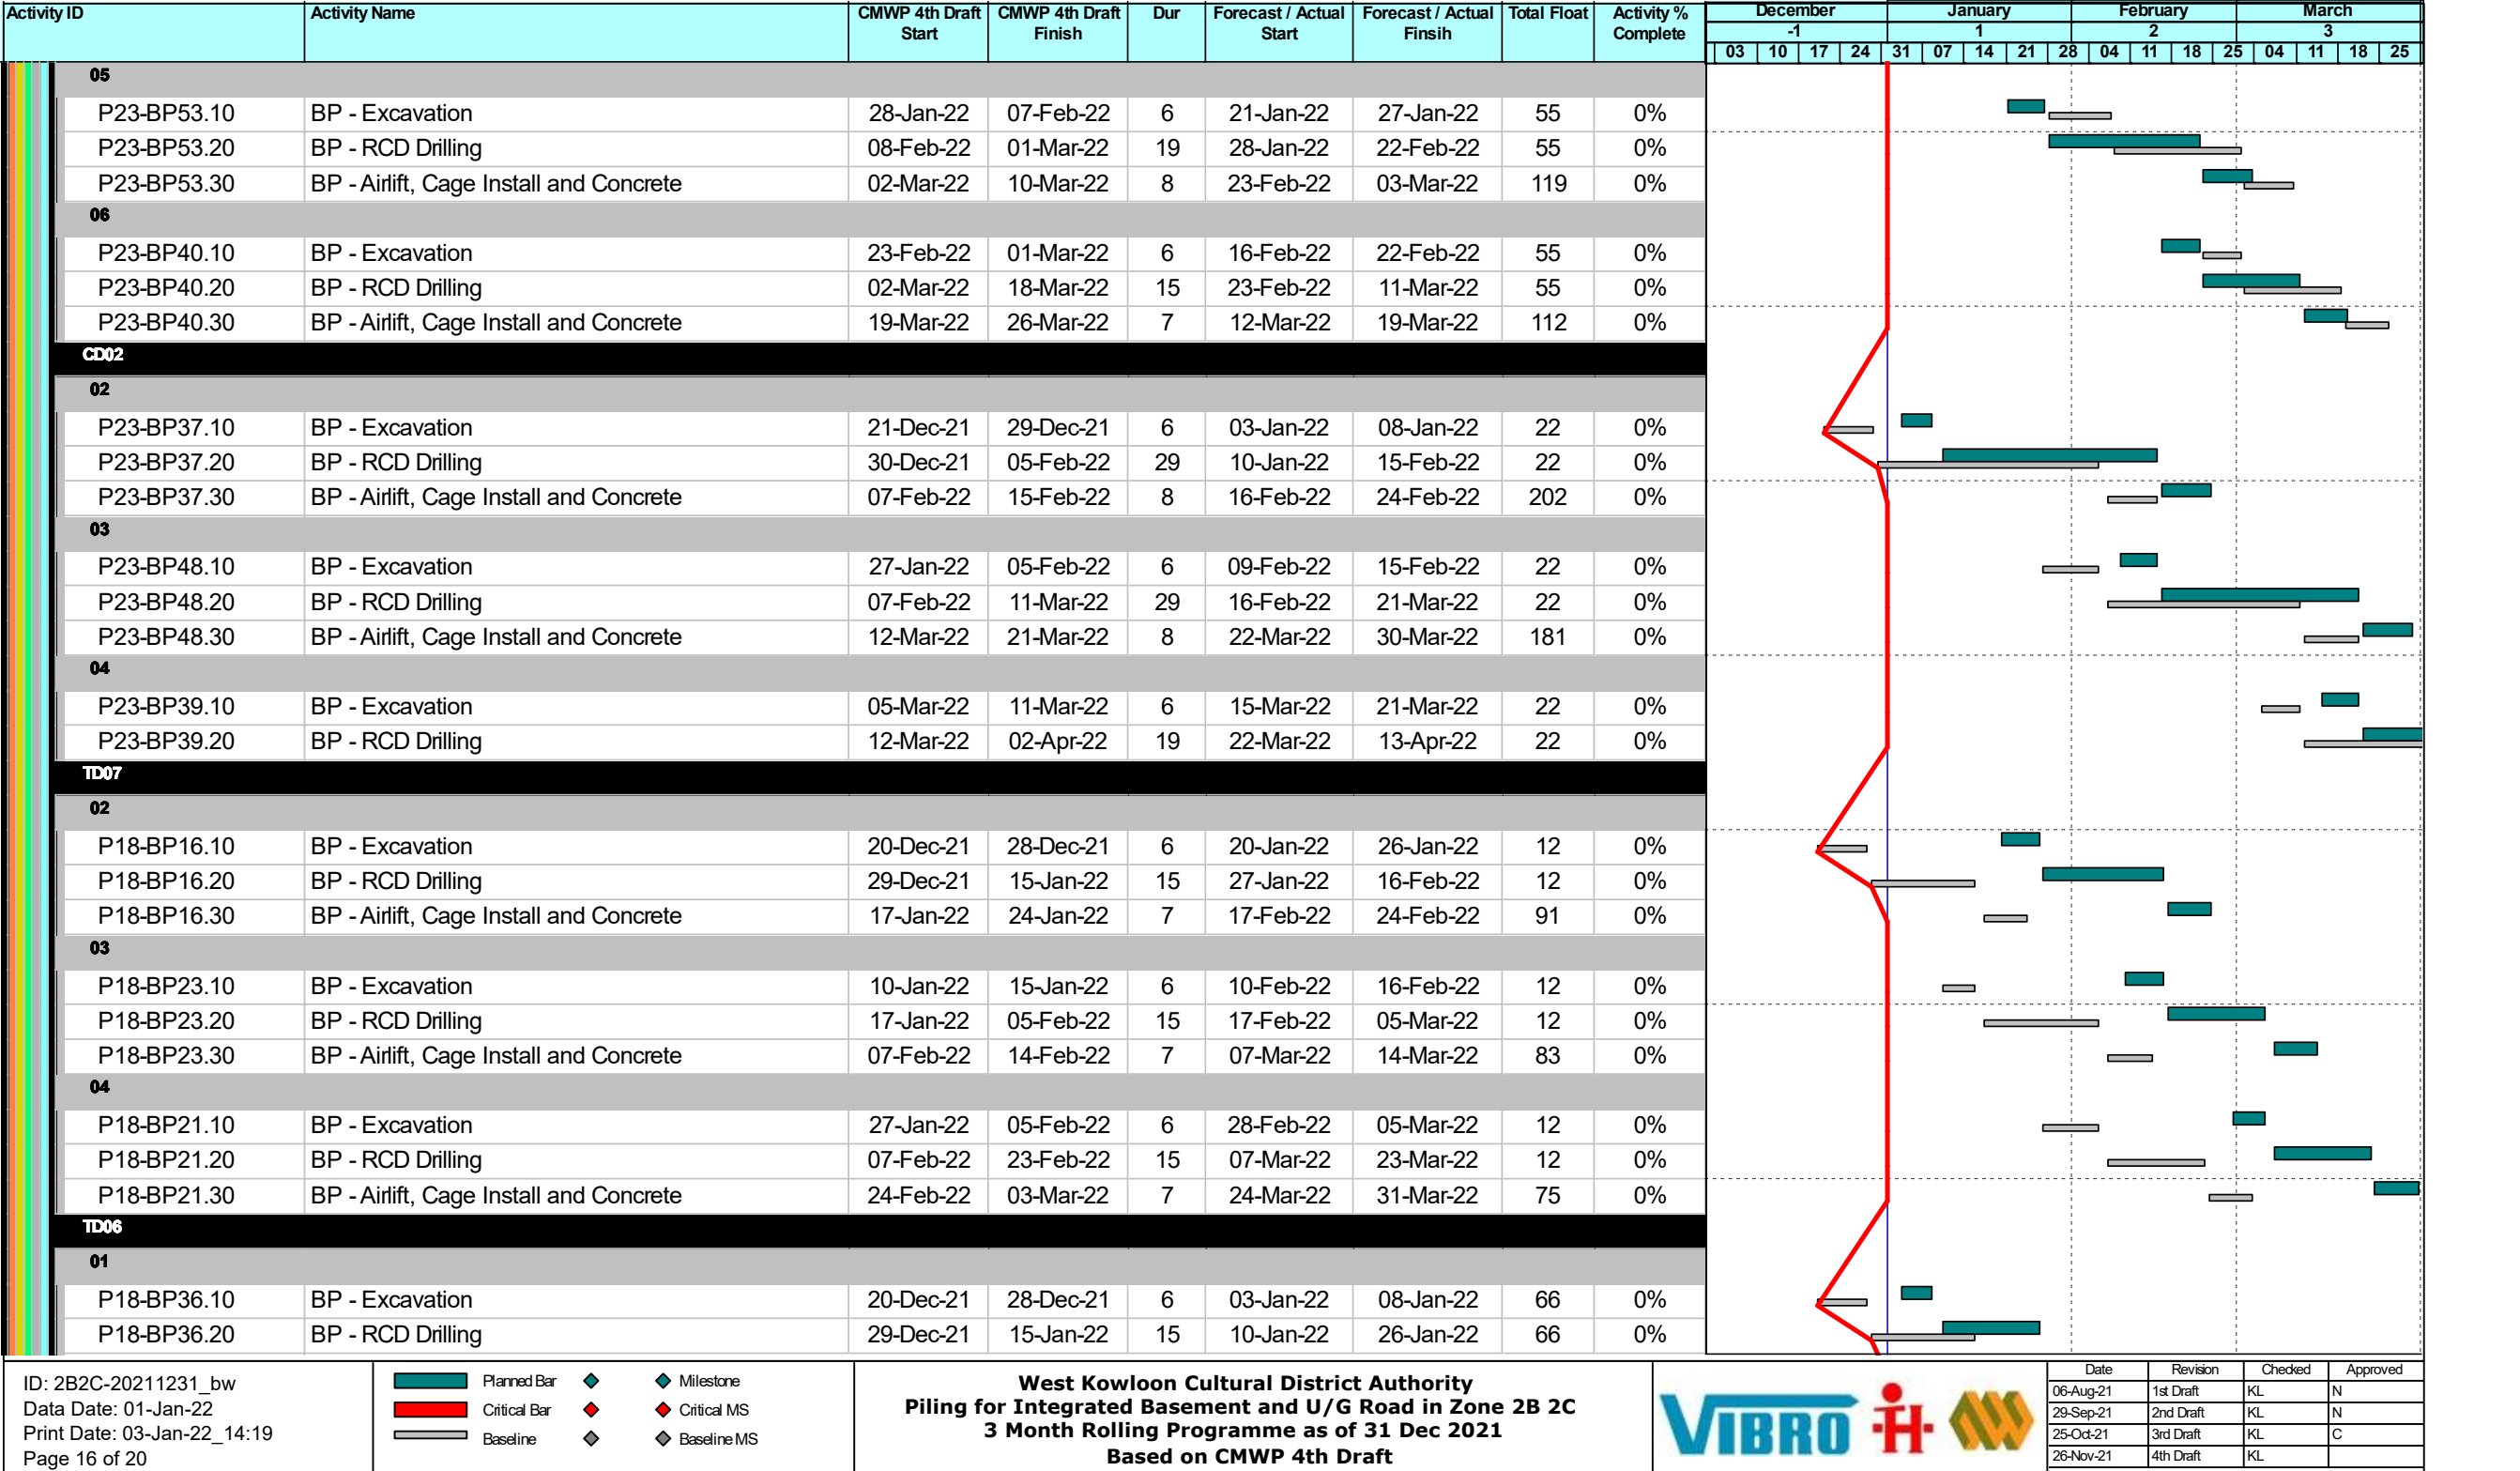


Activity ID	Activity Name	CMWP 4th Draft Start	CMWP 4th Draft Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	December				January				February				March																							
									-1				1				2				3																							
									03	10	17	24	31	07	14	21	28	04	11	18	25	04	11	18	25																			
01																																												
P30-BP41.10	BP - Excavation	19-Jan-22	25-Jan-22	6	19-Jan-22	25-Jan-22	0	0%																																				
P30-BP41.20	BP - RCD Drilling	26-Jan-22	15-Feb-22	15	26-Jan-22	15-Feb-22	0	0%																																				
P30-BP41.30	BP - Airlift, Cage Install and Concrete	16-Feb-22	23-Feb-22	7	16-Feb-22	23-Feb-22	159	0%																																				
02																																												
P30-BP47.10	BP - Excavation	09-Feb-22	15-Feb-22	6	09-Feb-22	15-Feb-22	0	0%																																				
P30-BP47.20	BP - RCD Drilling	16-Feb-22	04-Mar-22	15	16-Feb-22	04-Mar-22	0	0%																																				
P30-BP47.30	BP - Airlift, Cage Install and Concrete	05-Mar-22	12-Mar-22	7	05-Mar-22	12-Mar-22	151	0%																																				
03																																												
P30-BP58.10	BP - Excavation	26-Feb-22	04-Mar-22	6	26-Feb-22	04-Mar-22	0	0%																																				
P30-BP58.20	BP - RCD Drilling	05-Mar-22	26-Mar-22	19	05-Mar-22	26-Mar-22	0	0%																																				
P30-BP58.30	BP - Airlift, Cage Install and Concrete	28-Mar-22	06-Apr-22	8	28-Mar-22	06-Apr-22	139	0%																																				
VD05																																												
01																																												
P30-BP20.10	BP - Excavation	29-Nov-21	04-Dec-21	12	01-Dec-21 A	15-Dec-21 A		100%																																				
P30-BP20.20	BP - RCD Drilling	06-Dec-21	22-Dec-21	7	16-Dec-21 A	24-Dec-21 A		100%																																				
P30-BP20.30	BP - Airlift, Cage Install and Concrete	23-Dec-21	03-Jan-22	11	28-Dec-21 A	10-Jan-22	220	0%																																				
02																																												
P30-BP19.10	BP - Excavation	16-Dec-21	22-Dec-21	6	03-Jan-22	08-Jan-22	41	0%																																				
P30-BP19.20	BP - RCD Drilling	23-Dec-21	28-Jan-22	29	10-Jan-22	15-Feb-22	41	0%																																				
P30-BP19.30	BP - Airlift, Cage Install and Concrete	29-Jan-22	10-Feb-22	8	16-Feb-22	24-Feb-22	192	0%																																				
03																																												
P30-BP24.10	BP - Excavation	22-Jan-22	28-Jan-22	6	09-Feb-22	15-Feb-22	41	0%																																				
P30-BP24.20	BP - RCD Drilling	29-Jan-22	23-Feb-22	19	16-Feb-22	09-Mar-22	41	0%																																				
P30-BP24.30	BP - Airlift, Cage Install and Concrete	24-Feb-22	04-Mar-22	8	10-Mar-22	18-Mar-22	181	0%																																				
04																																												
P30-BP31.10	BP - Excavation	17-Feb-22	23-Feb-22	6	03-Mar-22	09-Mar-22	41	0%																																				
P30-BP31.20	BP - RCD Drilling	24-Feb-22	29-Mar-22	29	10-Mar-22	13-Apr-22	41	0%																																				
12																																												
P30-BP39.10	BP - Excavation	25-Aug-22	31-Aug-22	23	10-Dec-21 A	08-Jan-22	304	0%																																				
P30-BP39.20	BP - RCD Drilling	01-Sep-22	19-Sep-22	15	10-Jan-22	26-Jan-22	304	0%																																				
P30-BP39.30	BP - Airlift, Cage Install and Concrete	20-Sep-22	27-Sep-22	7	27-Jan-22	07-Feb-22	304	0%																																				
TD01																																												
01																																												
P30-BP01.30	BP - Airlift, Cage Install and Concrete	23-Feb-22	02-Mar-22	15	28-Nov-21 A	16-Dec-21 A		100%																																				
02																																												
P30-BP05.10	BP - Excavation	16-Feb-22	22-Feb-22	29	08-Nov-21 A	11-Dec-21 A		100%																																				
ID: 2B2C-20211231_bw		 Planned Bar		 Milestone													 Critical Bar		 Critical MS					 Baseline		 Baseline MS																		
Data Date: 01-Jan-22																							Date	Revision	Checked	Approved																		
Print Date: 03-Jan-22_14:19																							06-Aug-21	1st Draft	KL	N																		
Page 14 of 20																							29-Sep-21	2nd Draft	KL	N																		
																							25-Oct-21	3rd Draft	KL	C																		
																							26-Nov-21	4th Draft	KL																			






Activity ID	Activity Name	CMWP 4th Draft Start	CMWP 4th Draft Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	December				January				February				March			
									-1				1				2				3			
									03	10	17	24	31	07	14	21	28	04	11	18	25	04	11	18
<div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></</div>																								

Activity ID		Activity Name	CMWP 4th Draft Start	CMWP 4th Draft Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	December -1				January 1				February 2				March 3				
										03	10	17	24	31	07	14	21	28	04	11	18	25	04	11	18	25
	P23-BP107.20	BP - RCD Drilling	11-Jan-22	04-Feb-22	19	10-Feb-22	03-Mar-22	176	0%																	
	P23-BP107.30	BP - Airlift, Cage Install and Concrete	05-Feb-22	14-Feb-22	8	04-Mar-22	12-Mar-22	251	0%																	
	05																									
	P23-BP75.10	BP - Excavation	26-Jan-22	04-Feb-22	6	25-Feb-22	03-Mar-22	176	0%																	
	P23-BP75.20	BP - RCD Drilling	05-Feb-22	26-Feb-22	19	04-Mar-22	25-Mar-22	176	0%																	
	P23-BP75.30	BP - Airlift, Cage Install and Concrete	28-Feb-22	08-Mar-22	8	26-Mar-22	04-Apr-22	240	0%																	
06																										
	P23-BP73.10	BP - Excavation	21-Feb-22	26-Feb-22	6	19-Mar-22	25-Mar-22	176	0%																	
	P23-BP73.20	BP - RCD Drilling	28-Feb-22	21-Mar-22	19	26-Mar-22	21-Apr-22	176	0%																	
	10																									
	P23-BP115.10	BP - Excavation	04-Jan-22	10-Jan-22	6	31-Jan-22	09-Feb-22	99	0%																	
	P23-BP115.20	BP - RCD Drilling	11-Jan-22	04-Feb-22	19	10-Feb-22	03-Mar-22	99	0%																	
	P23-BP115.30	BP - Airlift, Cage Install and Concrete	05-Feb-22	14-Feb-22	8	04-Mar-22	12-Mar-22	227	0%																	
11																										
	P23-BP108.10	BP - Excavation	26-Jan-22	04-Feb-22	6	25-Feb-22	03-Mar-22	99	0%																	
	P23-BP108.20	BP - RCD Drilling	05-Feb-22	10-Mar-22	29	04-Mar-22	07-Apr-22	99	0%																	
	12																									
	P23-BP74.10	BP - Excavation	04-Mar-22	10-Mar-22	6	31-Mar-22	07-Apr-22	99	0%																	
TD03																										
02																										
	P23-BP101.10	BP - Excavation	20-Jan-22	26-Jan-22	6	09-Feb-22	15-Feb-22	47	0%																	
	P23-BP101.20	BP - RCD Drilling	27-Jan-22	21-Feb-22	19	16-Feb-22	09-Mar-22	47	0%																	
	P23-BP101.30	BP - Airlift, Cage Install and Concrete	22-Feb-22	02-Mar-22	8	10-Mar-22	18-Mar-22	198	0%																	
03																										
	P23-BP110.10	BP - Excavation	15-Feb-22	21-Feb-22	6	03-Mar-22	09-Mar-22	47	0%																	
	P23-BP110.20	BP - RCD Drilling	22-Feb-22	15-Mar-22	19	10-Mar-22	31-Mar-22	47	0%																	
	04																									
	P23-BP109.10	BP - Excavation	09-Mar-22	15-Mar-22	6	25-Mar-22	31-Mar-22	47	0%																	
14																										
	P23-BP90.10	BP - Excavation	27-Apr-22	04-May-22	18	16-Dec-21 A	08-Jan-22	181	0%																	
	P23-BP90.20	BP - RCD Drilling	05-May-22	09-Jun-22	29	10-Jan-22	15-Feb-22	181	0%																	
	P23-BP90.30	BP - Airlift, Cage Install and Concrete	10-Jun-22	18-Jun-22	8	16-Feb-22	24-Feb-22	257	0%																	
TD02																										
01																										
	P23-BP81.10	BP - Excavation	20-Dec-21	28-Dec-21	26	12-Nov-21 A	13-Dec-21 A		100%																	
	P23-BP81.20	BP - RCD Drilling	29-Dec-21	04-Feb-22	4	14-Dec-21 A	18-Dec-21 A		100%																	
	P23-BP81.30	BP - Airlift, Cage Install and Concrete	05-Feb-22	14-Feb-22	17	20-Dec-21 A	11-Jan-22	275	0%																	
ID: 2B2C-20211231_bw		 Planned Bar		 Milestone		<div>West Kowloon Cultural District Authority</div> <div>Piling for Integrated Basement and U/G Road in Zone 2B 2C</div> <div>3 Month Rolling Programme as of 31 Dec 2021</div> <div>Based on CMWP 4th Draft</div>												Date	Revision	Checked	Approved					
Data Date: 01-Jan-22		 Critical Bar		 Critical MS														06-Aug-21	1st Draft	KL	N					
Print Date: 03-Jan-22_14:19		 Baseline		 Baseline MS														29-Sep-21	2nd Draft	KL	N					
Page 18 of 20																		25-Oct-21	3rd Draft	KL	C					
																		26-Nov-21	4th Draft	KL						

Activity ID	Activity Name	CMWP 4th Draft Start	CMWP 4th Draft Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	December				January				February				March				
									-1				1				2				3				
									03	10	17	24	31	07	14	21	28	04	11	18	25	04	11	18	25
02																									
P23-BP59.10	BP - Excavation	26-Jan-22	04-Feb-22	21	03-Dec-21 A	30-Dec-21 A		100%																	
P23-BP59.20	BP - RCD Drilling	05-Feb-22	10-Mar-22	30	31-Dec-21 A	08-Feb-22	112	0%																	
P23-BP59.30	BP - Airlift, Cage Install and Concrete	11-Mar-22	19-Mar-22	8	09-Feb-22	17-Feb-22	254	0%																	
03																									
P23-BP71.10	BP - Excavation	04-Mar-22	10-Mar-22	6	29-Jan-22	08-Feb-22	112	0%																	
P23-BP71.20	BP - RCD Drilling	11-Mar-22	14-Apr-22	29	09-Feb-22	14-Mar-22	112	0%																	
P23-BP71.30	BP - Airlift, Cage Install and Concrete	19-Apr-22	27-Apr-22	8	15-Mar-22	23-Mar-22	233	0%																	
04																									
P23-BP83.10	BP - Excavation	08-Apr-22	14-Apr-22	6	08-Mar-22	14-Mar-22	112	0%																	
P23-BP83.20	BP - RCD Drilling	19-Apr-22	24-May-22	29	15-Mar-22	21-Apr-22	112	0%																	
10																									
P23-BP94.10	BP - Excavation	26-Jan-22	04-Feb-22	6	03-Jan-22	08-Jan-22	55	0%																	
P23-BP94.20	BP - RCD Drilling	05-Feb-22	10-Mar-22	29	10-Jan-22	15-Feb-22	55	0%																	
P23-BP94.30	BP - Airlift, Cage Install and Concrete	11-Mar-22	19-Mar-22	8	16-Feb-22	24-Feb-22	225	0%																	
11																									
P23-BP113.10	BP - Excavation	04-Mar-22	10-Mar-22	6	09-Feb-22	15-Feb-22	55	0%																	
P23-BP113.20	BP - RCD Drilling	11-Mar-22	01-Apr-22	19	16-Feb-22	09-Mar-22	55	0%																	
P23-BP113.30	BP - Airlift, Cage Install and Concrete	02-Apr-22	12-Apr-22	8	10-Mar-22	18-Mar-22	214	0%																	
12																									
P23-BP111.10	BP - Excavation	26-Mar-22	01-Apr-22	6	03-Mar-22	09-Mar-22	55	0%																	
P23-BP111.20	BP - RCD Drilling	02-Apr-22	28-Apr-22	19	10-Mar-22	31-Mar-22	55	0%																	
13																									
P23-BP92.10	BP - Excavation	22-Apr-22	28-Apr-22	6	25-Mar-22	31-Mar-22	55	0%																	
Socketed Steel H- Piles																									
Trial Pile																									
KD09.SSHP.0000	Test Installation of Pile (SHP-C52Xa-P6)	17-Jan-22	26-Jan-22	9	17-Jan-22	26-Jan-22	19	0%																	
KD09.SSHP.0020	Submission and Approval of Installation Report by BD	27-Jan-22	02-Feb-22	7	27-Jan-22	02-Feb-22	26	0%																	
Socketed Steel H-Pile Construction																									
SHP-BW-52Y1b-P	Socketed Steel H-Piling	04-Feb-22	12-Feb-22	8	04-Feb-22	12-Feb-22	93	0%																	
SHP-BW-52Y1b-P:	Socketed Steel H-Piling	08-Feb-22	16-Feb-22	8	08-Feb-22	16-Feb-22	93	0%																	

Activity ID		Activity Name	CMWP 4th Draft Start	CMWP 4th Draft Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	December				January				February				March				
										-1				1				2				3				
										03	10	17	24	31	07	14	21	28	04	11	18	25	04	11	18	25
<div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div></div>	SHP-C52W-P1	Socketed Steel H-Piling	11-Feb-22	19-Feb-22	8	11-Feb-22	19-Feb-22	93	0%																	
	SHP-C52W-P2	Socketed Steel H-Piling	15-Feb-22	23-Feb-22	8	15-Feb-22	23-Feb-22	93	0%																	
	SHP-C52W-P3	Socketed Steel H-Piling	18-Feb-22	26-Feb-22	8	18-Feb-22	26-Feb-22	93	0%																	
	SHP-C52W-P4	Socketed Steel H-Piling	22-Feb-22	02-Mar-22	8	22-Feb-22	02-Mar-22	93	0%																	
	SHP-C52W-P5	Socketed Steel H-Piling	25-Feb-22	05-Mar-22	8	25-Feb-22	05-Mar-22	93	0%																	
	SHP-C52W-P6	Socketed Steel H-Piling	01-Mar-22	09-Mar-22	8	01-Mar-22	09-Mar-22	93	0%																	
	SHP-C52X-P1	Socketed Steel H-Piling	04-Mar-22	12-Mar-22	8	04-Mar-22	12-Mar-22	93	0%																	
	SHP-C52X-P2	Socketed Steel H-Piling	08-Mar-22	16-Mar-22	8	08-Mar-22	16-Mar-22	93	0%																	
	SHP-C52X-P3	Socketed Steel H-Piling	11-Mar-22	19-Mar-22	8	11-Mar-22	19-Mar-22	93	0%																	
	SHP-C52X-P4	Socketed Steel H-Piling	15-Mar-22	23-Mar-22	8	15-Mar-22	23-Mar-22	93	0%																	
	SHP-C52X-P5	Socketed Steel H-Piling	18-Mar-22	26-Mar-22	8	18-Mar-22	26-Mar-22	93	0%																	
	SHP-C52X-P6	Socketed Steel H-Piling	22-Mar-22	30-Mar-22	8	22-Mar-22	30-Mar-22	93	0%																	
	SHP-C52Xa-P1	Socketed Steel H-Piling	25-Mar-22	02-Apr-22	8	25-Mar-22	02-Apr-22	93	0%																	
	SHP-C52Xa-P2	Socketed Steel H-Piling	29-Mar-22	07-Apr-22	8	29-Mar-22	07-Apr-22	93	0%																	

Date	Revision	Checked	Approved
06-Aug-21	1st Draft	KL	N
29-Sep-21	2nd Draft	KL	N
25-Oct-21	3rd Draft	KL	C
26-Nov-21	4th Draft	KL	B

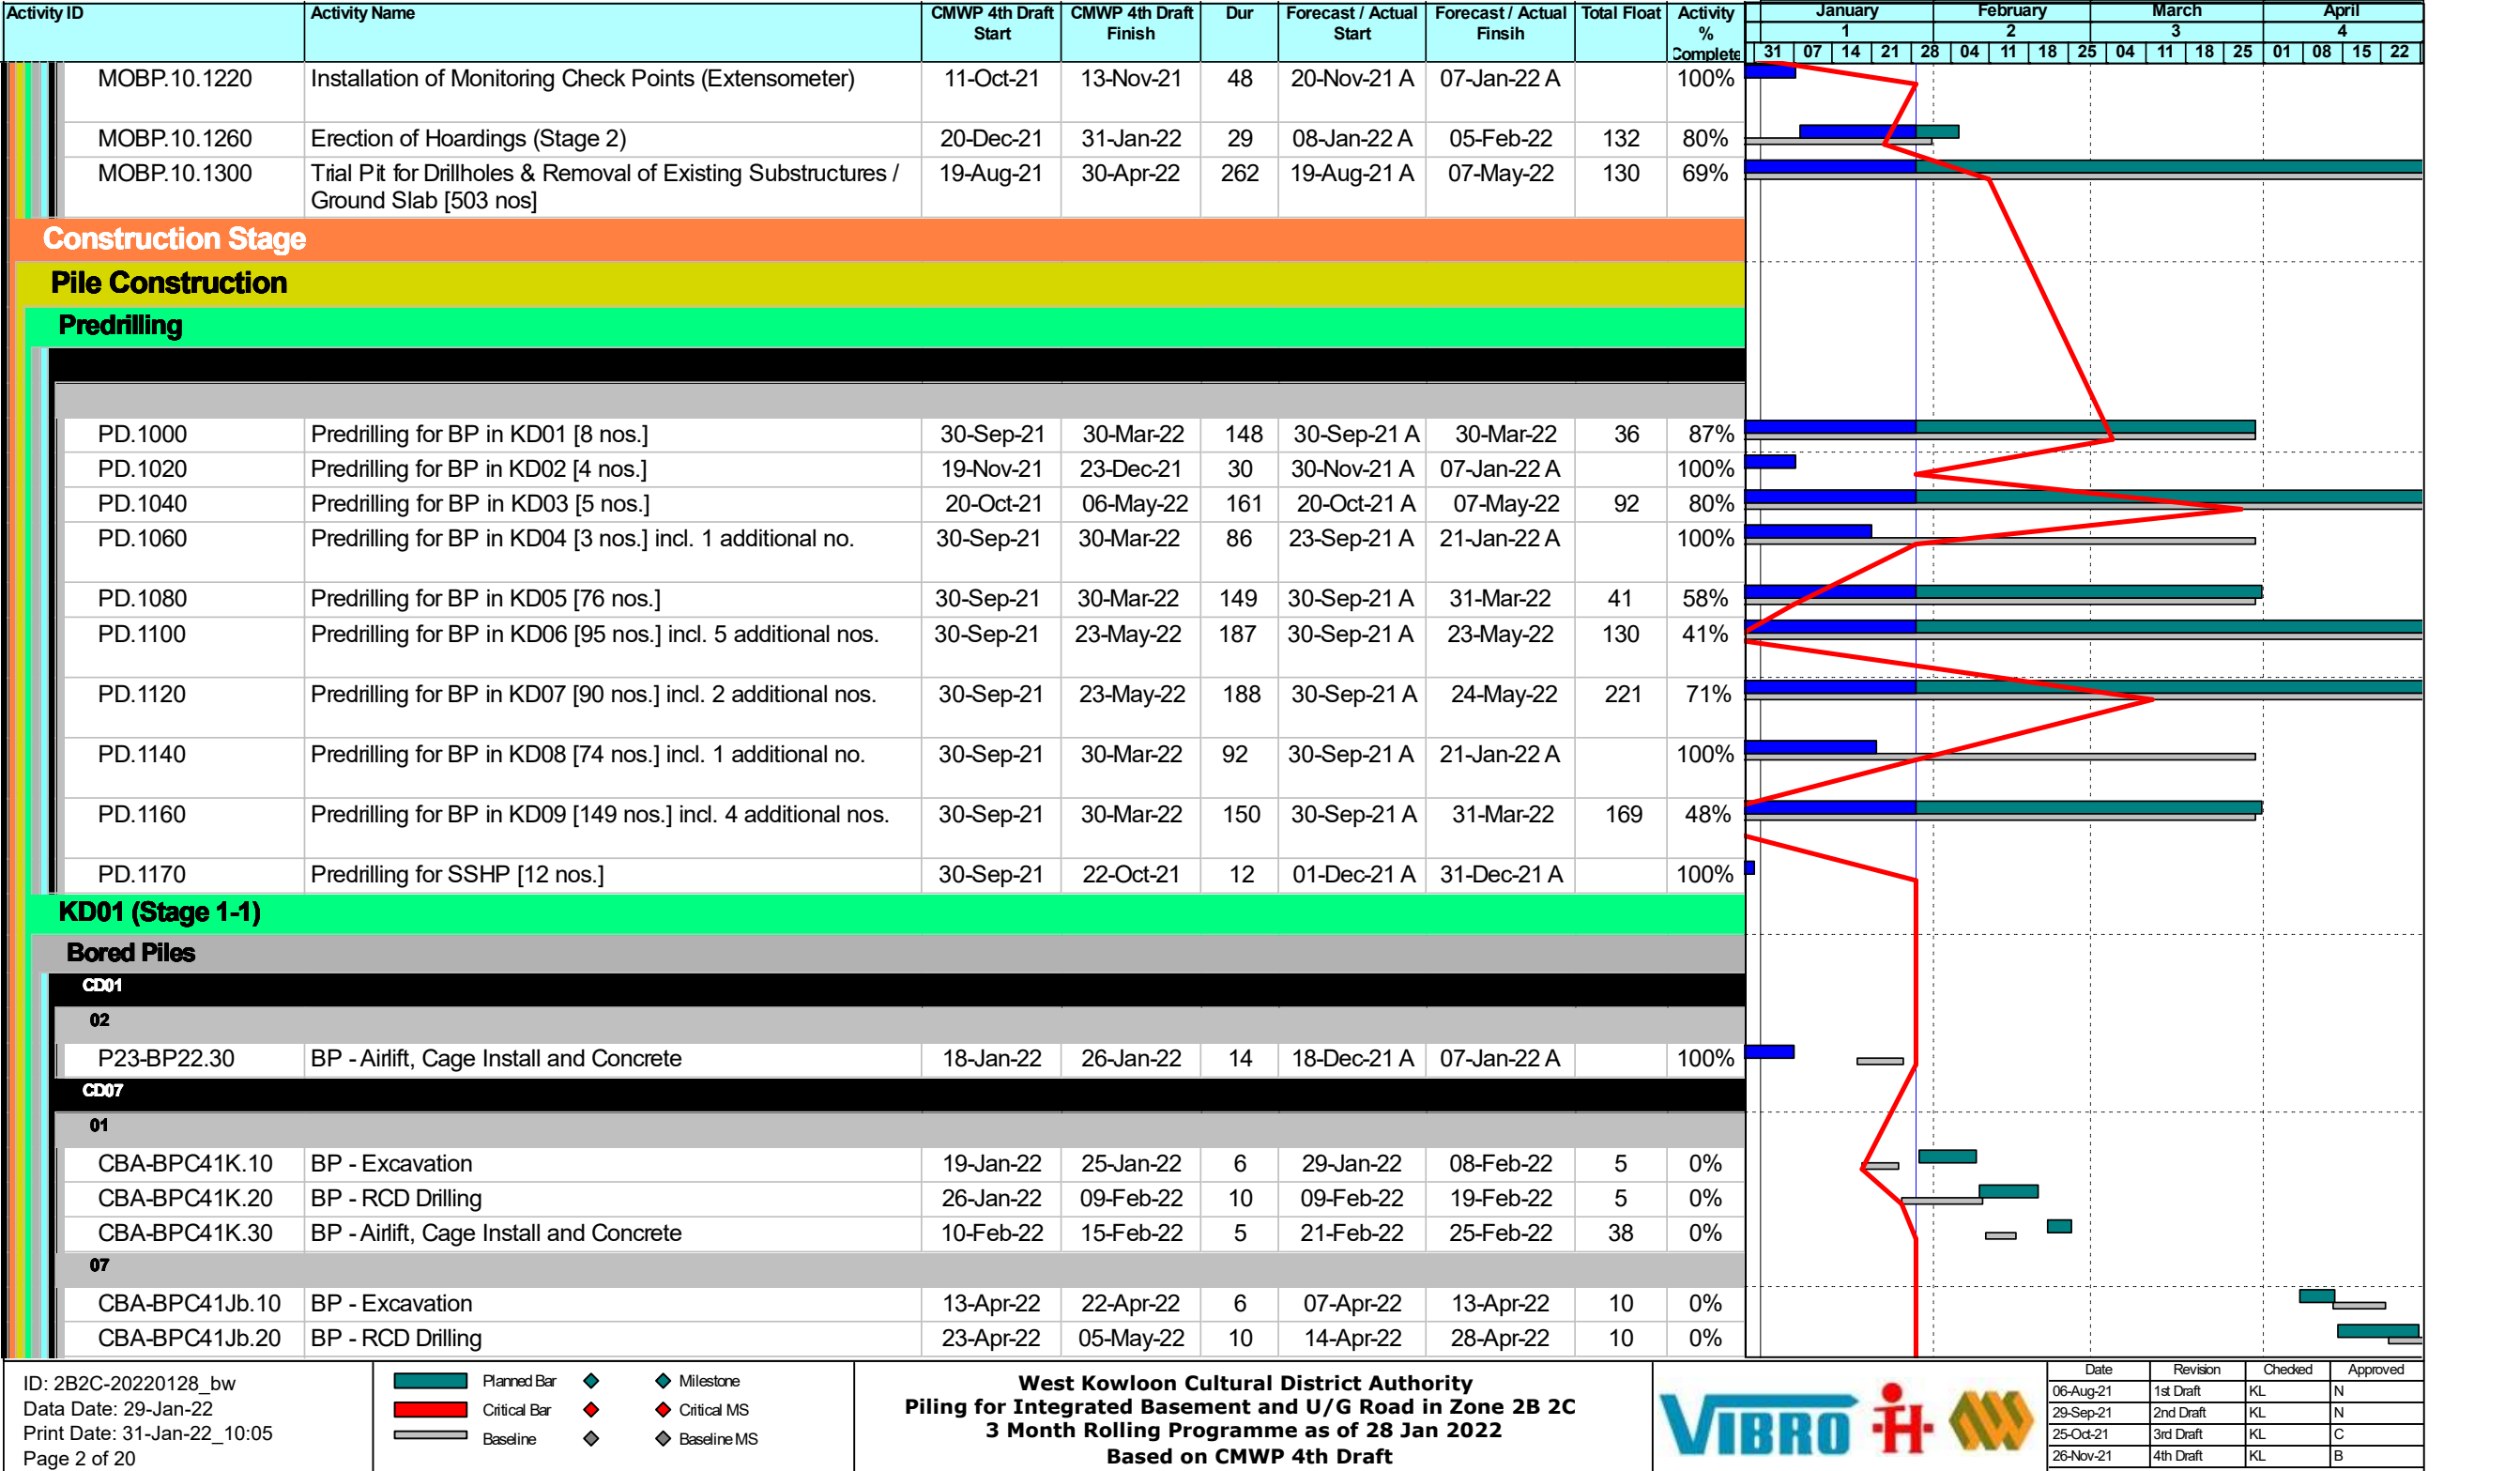

Activity ID	Activity Name	CMWP 4th Draft Start	CMWP 4th Draft Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	January				February				March				April				
									1				2				3				4				
									31	07	14	21	28	04	11	18	25	04	11	18	25	01	08	15	22
14																									
CBA-BP04.10	BP - Excavation	12-Apr-22	22-Apr-22	7	06-Apr-22	13-Apr-22	5	0%																	
CBA-BP04.20	BP - RCD Drilling	23-Apr-22	11-May-22	14	14-Apr-22	04-May-22	5	0%																	
CD05																									
04																									
P22&P19-BP11.10	BP - Excavation	24-Jan-22	29-Jan-22	6	19-Feb-22	25-Feb-22	18	0%																	
P22&P19-BP11.20	BP - RCD Drilling	31-Jan-22	24-Feb-22	19	26-Feb-22	19-Mar-22	18	0%																	
P22&P19-BP11.30	BP - Airlift, Cage Install and Concrete	25-Feb-22	05-Mar-22	8	21-Mar-22	29-Mar-22	29	0%																	
05																									
P22&P19-BP21.10	BP - Excavation	18-Feb-22	24-Feb-22	6	14-Mar-22	19-Mar-22	18	0%																	
P22&P19-BP21.20	BP - RCD Drilling	25-Feb-22	18-Mar-22	19	21-Mar-22	12-Apr-22	18	0%																	
P22&P19-BP21.30	BP - Airlift, Cage Install and Concrete	19-Mar-22	28-Mar-22	8	13-Apr-22	25-Apr-22	18	0%																	
07																									
P22&P19-BP29.10	BP - Excavation	04-Apr-22	11-Apr-22	12	22-Jan-22 A	08-Feb-22	52	0%																	
P22&P19-BP29.20	BP - RCD Drilling	12-Apr-22	07-May-22	19	09-Feb-22	02-Mar-22	52	0%																	
P22&P19-BP29.30	BP - Airlift, Cage Install and Concrete	10-May-22	18-May-22	8	03-Mar-22	11-Mar-22	52	0%																	
CD03																									
06																									
P23-BP06.10	BP - Excavation	02-Apr-22	09-Apr-22	34	24-Dec-21 A	08-Feb-22	52	0%																	
P23-BP06.20	BP - RCD Drilling	11-Apr-22	06-May-22	19	09-Feb-22	02-Mar-22	52	0%																	
P23-BP06.30	BP - Airlift, Cage Install and Concrete	07-May-22	17-May-22	8	03-Mar-22	11-Mar-22	52	0%																	
KD02 (Stage 5-1)																									
KD02.BP.0040	Review and Confirmation of Rockhead and Founding Level of the 1st Pile by CA	19-Nov-21	02-Dec-21	63	03-Dec-21 A	03-Feb-22	-42	57.14%																	
Bored Piles																									
CD01																									
04																									
P23-BP43.10	BP - Excavation	03-Dec-21	09-Dec-21	9	21-Dec-21 A	04-Jan-22 A		100%																	
P23-BP43.20	BP - RCD Drilling	10-Dec-21	30-Dec-21	13	05-Jan-22 A	20-Jan-22 A		100%																	
P23-BP43.30	BP - Airlift, Cage Install and Concrete	31-Dec-21	10-Jan-22	17	21-Jan-22 A	12-Feb-22	-5	0%																	
TD04																									
01																									
P23-BP76.10	BP - Excavation	03-Dec-21	09-Dec-21	34	24-Dec-21 A	08-Feb-22	-33	0%																	
P23-BP76.20	BP - RCD Drilling	10-Dec-21	30-Dec-21	16	09-Feb-22	26-Feb-22	-33	0%																	
P23-BP76.30	BP - Airlift, Cage Install and Concrete	31-Dec-21	10-Jan-22	8	28-Feb-22	08-Mar-22	-33	0%																	
ID: 2B2C-20220128_bw																									
Data Date: 29-Jan-22																									
Print Date: 31-Jan-22_10:05																									
Page 3 of 20																									
<div><div><div></div><div></div><div></div></div><div><div>Planned Bar</div><div>Critical Bar</div><div>Baseline</div></div><div><div>◆</div><div>◆</div><div>◆</div></div><div><div>Milestone</div><div>Critical MS</div><div>Baseline MS</div></div></div>																									
West Kowloon Cultural District Authority																									
Piling for Integrated Basement and U/G Road in Zone 2B 2C																									
3 Month Rolling Programme as of 28 Jan 2022																									
Based on CMWP 4th Draft																									
VIBRO																									
Date										Revision															
06-Aug-21										1st Draft															
29-Sep-21										2nd Draft															
25-Oct-21										3rd Draft															
26-Nov-21										4th Draft															
Checked										Approved															
KL										N															
KL										N															
KL										C															
KL										B															

Activity ID	Activity Name	CMWP 4th Draft Start	CMWP 4th Draft Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	January				February				March				April																
									1				2				3				4																
									31	07	14	21	28	04	11	18	25	04	11	18	25	01	08	15	22												
02																																					
P23-BP87.10	BP - Excavation	03-Dec-21	09-Dec-21	28	04-Jan-22 A	08-Feb-22	-33	0%																													
P23-BP87.20	BP - RCD Drilling	10-Dec-21	10-Jan-22	24	09-Feb-22	08-Mar-22	-33	0%																													
P23-BP87.30	BP - Airlift, Cage Install and Concrete	11-Jan-22	19-Jan-22	8	09-Mar-22	17-Mar-22	-33	0%																													
03																																					
P23-BP117.10	BP - Excavation	03-Dec-21	09-Dec-21	23	10-Jan-22 A	08-Feb-22	-33	0%																													
P23-BP117.20	BP - RCD Drilling	10-Dec-21	10-Jan-22	24	09-Feb-22	08-Mar-22	-33	0%																													
P23-BP117.30	BP - Airlift, Cage Install and Concrete	20-Jan-22	28-Jan-22	8	09-Mar-22	17-Mar-22	-33	0%																													
KD03 (Stage 3-1)																																					
KD03.BP.0040	Review and Confirmation of Rockhead and Founding Level of the 1st Pile by CA	14-Nov-21	27-Nov-21	14	29-Jan-22	11-Feb-22	-3	0%																													
Bored Piles																																					
VD02																																					
03																																					
P28&29-BP08.10	BP - Excavation	18-Mar-22	24-Mar-22	6	30-Mar-22	06-Apr-22	27	0%																													
P28&29-BP08.20	BP - RCD Drilling	25-Mar-22	12-Apr-22	15	07-Apr-22	27-Apr-22	27	0%																													
P28&29-BP08.30	BP - Airlift, Cage Install and Concrete	13-Apr-22	23-Apr-22	7	28-Apr-22	06-May-22	93	0%																													
VD06																																					
01																																					
P28&29-BP29.10	BP - Excavation	19-Jan-22	25-Jan-22	6	29-Jan-22	08-Feb-22	0	0%																													
P28&29-BP29.20	BP - RCD Drilling	26-Jan-22	15-Feb-22	15	12-Feb-22	01-Mar-22	-3	0%																													
P28&29-BP29.30	BP - Airlift, Cage Install and Concrete	16-Feb-22	23-Feb-22	7	02-Mar-22	09-Mar-22	68	0%																													
VD09																																					
01																																					
CBA-BPC54Jb.10	BP - Excavation	26-Feb-22	04-Mar-22	6	26-Feb-22	04-Mar-22	0	0%																													
CBA-BPC54Jb.20	BP - RCD Drilling	05-Mar-22	11-Apr-22	31	05-Mar-22	11-Apr-22	0	0%																													
CBA-BPC54Jb.30	BP - Airlift, Cage Install and Concrete	12-Apr-22	21-Apr-22	6	12-Apr-22	21-Apr-22	99	0%																													
02																																					
CBA-BPC54Ka.10	BP - Excavation	04-Apr-22	11-Apr-22	6	12-Apr-22	21-Apr-22	-6	0%																													
CBA-BPC54Ka.20	BP - RCD Drilling	12-Apr-22	25-May-22	33	22-Apr-22	01-Jun-22	-6	0%																													
KD04 (Stage 4-1)																																					
KD04.BP.0040	Review and Confirmation of Rockhead and Founding Level of the 1st Pile by CA	03-Nov-21	16-Nov-21	105	30-Oct-21 A	11-Feb-22	55	0%																													
ID: 2B2C-20220128_bw Data Date: 29-Jan-22 Print Date: 31-Jan-22_10:05 Page 4 of 20		<div><div></div>Planned Bar</div> <div><div></div>Critical Bar</div> <div><div></div>Baseline</div>		<div><div></div>Milestone</div> <div><div></div>Critical MS</div> <div><div></div>Baseline MS</div>		West Kowloon Cultural District Authority Piling for Integrated Basement and U/G Road in Zone 2B 2C 3 Month Rolling Programme as of 28 Jan 2022 Based on CMWP 4th Draft				<div>VIBRO</div> <div></div> <div></div>				<table><tr><th>Date</th><th>Revision</th><th>Checked</th><th>Approved</th></tr><tr><td>06-Aug-21</td><td>1st Draft</td><td>KL</td><td>N</td></tr><tr><td>29-Sep-21</td><td>2nd Draft</td><td>KL</td><td>N</td></tr><tr><td>25-Oct-21</td><td>3rd Draft</td><td>KL</td><td>C</td></tr><tr><td>26-Nov-21</td><td>4th Draft</td><td>KL</td><td>B</td></tr></table>				Date	Revision	Checked	Approved	06-Aug-21	1st Draft	KL	N	29-Sep-21	2nd Draft	KL	N	25-Oct-21	3rd Draft	KL	C	26-Nov-21	4th Draft	KL	B
Date	Revision	Checked	Approved																																		
06-Aug-21	1st Draft	KL	N																																		
29-Sep-21	2nd Draft	KL	N																																		
25-Oct-21	3rd Draft	KL	C																																		
26-Nov-21	4th Draft	KL	B																																		

ID: 2B2C-20220128_bw
Data Date: 29-Jan-22
Print Date: 31-Jan-22_10:05
Page 5 of 20

Planned Bar

Critical Bar

Baseline

Milestone

Critical MS

Baseline MS


West Kowloon Cultural District Authority


Piling for Integrated Basement and U/G Road in Zone 2B 2C

3 Month Rolling Programme as of 28 Jan 2022

Based on CMWP 4th Draft

VIBRO





Date	Revision	Checked	Approved
06-Aug-21	1st Draft	KL	N
29-Sep-21	2nd Draft	KL	N
25-Oct-21	3rd Draft	KL	C
26-Nov-21	4th Draft	KL	B

Activity ID	Activity Name	CMWP 4th Draft Start	CMWP 4th Draft Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	January 1				February 2				March 3				April 4						
									1				2				3				4						
									31	07	14	21	28	04	11	18	25	04	11	18	25	01	08	15	22		
04																											
CBA-BPC40Ja.10	BP - Excavation	03-Mar-22	09-Mar-22	6	25-Feb-22	03-Mar-22	5	0%																			
CBA-BPC40Ja.20	BP - RCD Drilling	10-Mar-22	21-Mar-22	10	04-Mar-22	15-Mar-22	5	0%																			
CBA-BPC40Ja.30	BP - Airlift, Cage Install and Concrete	22-Mar-22	26-Mar-22	5	16-Mar-22	21-Mar-22	28	0%																			
05																											
CBA-BPC42K.10	BP - Excavation	15-Mar-22	21-Mar-22	6	09-Mar-22	15-Mar-22	5	0%																			
CBA-BPC42K.20	BP - RCD Drilling	22-Mar-22	01-Apr-22	10	16-Mar-22	26-Mar-22	5	0%																			
CBA-BPC42K.30	BP - Airlift, Cage Install and Concrete	02-Apr-22	08-Apr-22	5	28-Mar-22	01-Apr-22	23	0%																			
06																											
CBA-BPC44K.10	BP - Excavation	25-Mar-22	01-Apr-22	7	19-Mar-22	26-Mar-22	5	0%																			
CBA-BPC44K.20	BP - RCD Drilling	02-Apr-22	22-Apr-22	14	28-Mar-22	13-Apr-22	5	0%																			
CBA-BPC44K.30	BP - Airlift, Cage Install and Concrete	23-Apr-22	29-Apr-22	6	14-Apr-22	23-Apr-22	14	0%																			
08																											
CBA-BPC43J.10	BP - Excavation	28-Apr-22	05-May-22	6	22-Apr-22	28-Apr-22	68	0%																			
13																											
CBA-BP01.10	BP - Excavation	25-Mar-22	01-Apr-22	7	19-Mar-22	26-Mar-22	5	0%																			
CBA-BP01.20	BP - RCD Drilling	02-Apr-22	22-Apr-22	14	28-Mar-22	13-Apr-22	5	0%																			
CBA-BP01.30	BP - Airlift, Cage Install and Concrete	23-Apr-22	29-Apr-22	6	14-Apr-22	23-Apr-22	13	0%																			
15																											
CBA-BP06.10	BP - Excavation	04-May-22	11-May-22	6	27-Apr-22	04-May-22	93	0%																			
CD05																											
01																											
P22&P19-BP04.10	BP - Excavation	19-Nov-21	25-Nov-21	28	04-Jan-22 A	08-Feb-22	18	0%																			
P22&P19-BP04.20	BP - RCD Drilling	26-Nov-21	17-Dec-21	19	09-Feb-22	02-Mar-22	18	0%																			
P22&P19-BP04.30	BP - Airlift, Cage Install and Concrete	18-Dec-21	29-Dec-21	8	03-Mar-22	11-Mar-22	164	0%																			
02																											
P22&P19-BP05.20	BP - RCD Drilling	18-Dec-21	12-Jan-22	7	18-Dec-21 A	29-Dec-21 A		100%																			
P22&P19-BP05.30	BP - Airlift, Cage Install and Concrete	13-Jan-22	21-Jan-22	13	30-Dec-21 A	15-Jan-22 A		100%																			
03																											
P17-BP05.10	BP - Excavation	06-Jan-22	12-Jan-22	6	29-Jan-22	08-Feb-22	18	0%																			
P17-BP05.20	BP - RCD Drilling	13-Jan-22	29-Jan-22	15	09-Feb-22	25-Feb-22	18	0%																			
P17-BP05.30	BP - Airlift, Cage Install and Concrete	31-Jan-22	10-Feb-22	7	26-Feb-22	05-Mar-22	41	0%																			
06																											
P22&P19-BP15.10	BP - Excavation	12-Mar-22	18-Mar-22	6	14-Mar-22	19-Mar-22	77	0%																			
P22&P19-BP15.20	BP - RCD Drilling	19-Mar-22	11-Apr-22	19	21-Mar-22	12-Apr-22	77	0%																			
P22&P19-BP15.30	BP - Airlift, Cage Install and Concrete	12-Apr-22	23-Apr-22	8	26-Apr-22	05-May-22	99	0%																			
08																											

ID: 2B2C-20220128_bw
Data Date: 29-Jan-22
Print Date: 31-Jan-22_10:05
Page 6 of 20

Planned Bar

Critical Bar

Baseline

Milestone

Critical MS

Baseline MS

West Kowloon Cultural District Authority

Piling for Integrated Basement and U/G Road in Zone 2B 2C

3 Month Rolling Programme as of 28 Jan 2022

Based on CMWP 4th Draft

VIBRO

Date	Revision	Checked	Approved
06-Aug-21	1st Draft	KL	N
29-Sep-21	2nd Draft	KL	N
25-Oct-21	3rd Draft	KL	C
26-Nov-21	4th Draft	KL	B

[illegible]

ID: 2B2C-20220128_bw
Data Date: 29-Jan-22
Print Date: 31-Jan-22_10:05
Page 8 of 20

Planned Bar

Critical Bar

Baseline

Milestone

Critical MS

Baseline MS

West Kowloon Cultural District Authority




Piling for Integrated Basement and U/G Road in Zone 2B 2C



3 Month Rolling Programme as of 28 Jan 2022


Based on CMWP 4th Draft


VIBRO

Date	Revision	Checked	Approved
06-Aug-21	1st Draft	KL	N
29-Sep-21	2nd Draft	KL	N
25-Oct-21	3rd Draft	KL	C
26-Nov-21	4th Draft	KL	B

Activity ID		Activity Name	CMWP 4th Draft Start	CMWP 4th Draft Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	January				February				March				April			
										1				2				3				4			
										31	07	14	21	28	04	11	18	25	04	11	18	25	01	08	15
	P18-BP10.30	BP - Airlift, Cage Install and Concrete	14-Dec-21	21-Dec-21	7	26-Feb-22	05-Mar-22	76	0%																
05																									
	P18-BP02.10	BP - Excavation	17-Feb-22	23-Feb-22	6	14-Apr-22	23-Apr-22	-11	0%																
	P18-BP02.20	BP - RCD Drilling	24-Feb-22	12-Mar-22	15	25-Apr-22	13-May-22	-11	0%																
KD06 (Section 2)																									
Bored Piles																									
VD01																									
02																									
	P23-BP23.30	BP - Airlift, Cage Install and Concrete	24-Mar-22	31-Mar-22	25	14-Dec-21 A	15-Jan-22 A		100%																
VD07																									
02																									
	P24&27-BP27.10	BP - Excavation	24-Feb-22	02-Mar-22	6	08-Mar-22	14-Mar-22	10	0%																
	P24&27-BP27.20	BP - RCD Drilling	03-Mar-22	24-Mar-22	19	15-Mar-22	06-Apr-22	10	0%																
	P24&27-BP27.30	BP - Airlift, Cage Install and Concrete	25-Mar-22	02-Apr-22	8	07-Apr-22	19-Apr-22	199	0%																
03																									
	P24&27-BP28.10	BP - Excavation	18-Mar-22	24-Mar-22	6	30-Mar-22	06-Apr-22	10	0%																
	P24&27-BP28.20	BP - RCD Drilling	25-Mar-22	20-Apr-22	19	07-Apr-22	03-May-22	10	0%																
VD10																									
09																									
	CBA-BPC49J.10	BP - Excavation	19-Apr-22	25-Apr-22	6	19-Apr-22	25-Apr-22	21	0%																
	CBA-BPC49J.20	BP - RCD Drilling	26-Apr-22	02-Jun-22	31	26-Apr-22	02-Jun-22	21	0%																
CD08																									
01																									
	CBA-BPC45Jb.10	BP - Excavation	09-Aug-22	16-Aug-22	27	05-Jan-22 A	08-Feb-22	4	4.29%																
	CBA-BPC45Jb.20	BP - RCD Drilling	17-Aug-22	01-Sep-22	14	09-Feb-22	24-Feb-22	4	0%																
	CBA-BPC45Jb.30	BP - Airlift, Cage Install and Concrete	02-Sep-22	08-Sep-22	6	25-Feb-22	03-Mar-22	299	0%																
CD06																									
01																									
	P24&27-BP30.10	BP - Excavation	28-Dec-21	04-Jan-22	6	29-Jan-22	08-Feb-22	-27	0%																
	P24&27-BP30.20	BP - RCD Drilling	05-Jan-22	21-Jan-22	15	09-Feb-22	25-Feb-22	-27	0%																
	P24&27-BP30.30	BP - Airlift, Cage Install and Concrete	22-Jan-22	29-Jan-22	7	26-Feb-22	05-Mar-22	161	0%																
02																									
	P22&P19-BP22.10	BP - Excavation	15-Jan-22	21-Jan-22	6	19-Feb-22	25-Feb-22	-27	0%																
	P22&P19-BP22.20	BP - RCD Drilling	22-Jan-22	16-Feb-22	19	26-Feb-22	19-Mar-22	-27	0%																
	P22&P19-BP22.30	BP - Airlift, Cage Install and Concrete	17-Feb-22	25-Feb-22	8	21-Mar-22	29-Mar-22	149	0%																
03																									
ID: 2B2C-20220128_bw		Planned Bar		Milestone		West Kowloon Cultural District Authority Piling for Integrated Basement and U/G Road in Zone 2B 2C 3 Month Rolling Programme as of 28 Jan 2022 Based on CMWP 4th Draft				  				Date	Revision	Checked	Approved								
Data Date: 29-Jan-22		Critical Bar		Critical MS										06-Aug-21	1st Draft	KL	N								
Print Date: 31-Jan-22_10:05		Baseline		Baseline MS										29-Sep-21	2nd Draft	KL	N								
Page 9 of 20														25-Oct-21	3rd Draft	KL	C								
														26-Nov-21	4th Draft	KL	B								

ID: 2B2C-20220128_bw Data Date: 29-Jan-22 Print Date: 31-Jan-22_10:05 Page 10 of 20	<div><div><div></div><div>Planned Bar</div></div><div><div></div><div>Critical Bar</div></div><div><div></div><div>Baseline</div></div><div><div></div><div>Milestone</div></div><div><div></div><div>Critical MS</div></div><div><div></div><div>Baseline MS</div></div></div>	<div>West Kowloon Cultural District Authority</div> <div>Piling for Integrated Basement and U/G Road in Zone 2B 2C</div> <div>3 Month Rolling Programme as of 28 Jan 2022</div> <div>Based on CMWP 4th Draft</div>	<div><div>VIBRO</div><div></div><div></div></div>	<table><tr><th>Date</th><th>Revision</th><th>Checked</th><th>Approved</th></tr><tr><td>06-Aug-21</td><td>1st Draft</td><td>KL</td><td>N</td></tr><tr><td>29-Sep-21</td><td>2nd Draft</td><td>KL</td><td>N</td></tr><tr><td>25-Oct-21</td><td>3rd Draft</td><td>KL</td><td>C</td></tr><tr><td>26-Nov-21</td><td>4th Draft</td><td>KL</td><td>B</td></tr></table>	Date	Revision	Checked	Approved	06-Aug-21	1st Draft	KL	N	29-Sep-21	2nd Draft	KL	N	25-Oct-21	3rd Draft	KL	C	26-Nov-21	4th Draft	KL	B
Date	Revision	Checked	Approved																					
06-Aug-21	1st Draft	KL	N																					
29-Sep-21	2nd Draft	KL	N																					
25-Oct-21	3rd Draft	KL	C																					
26-Nov-21	4th Draft	KL	B																					

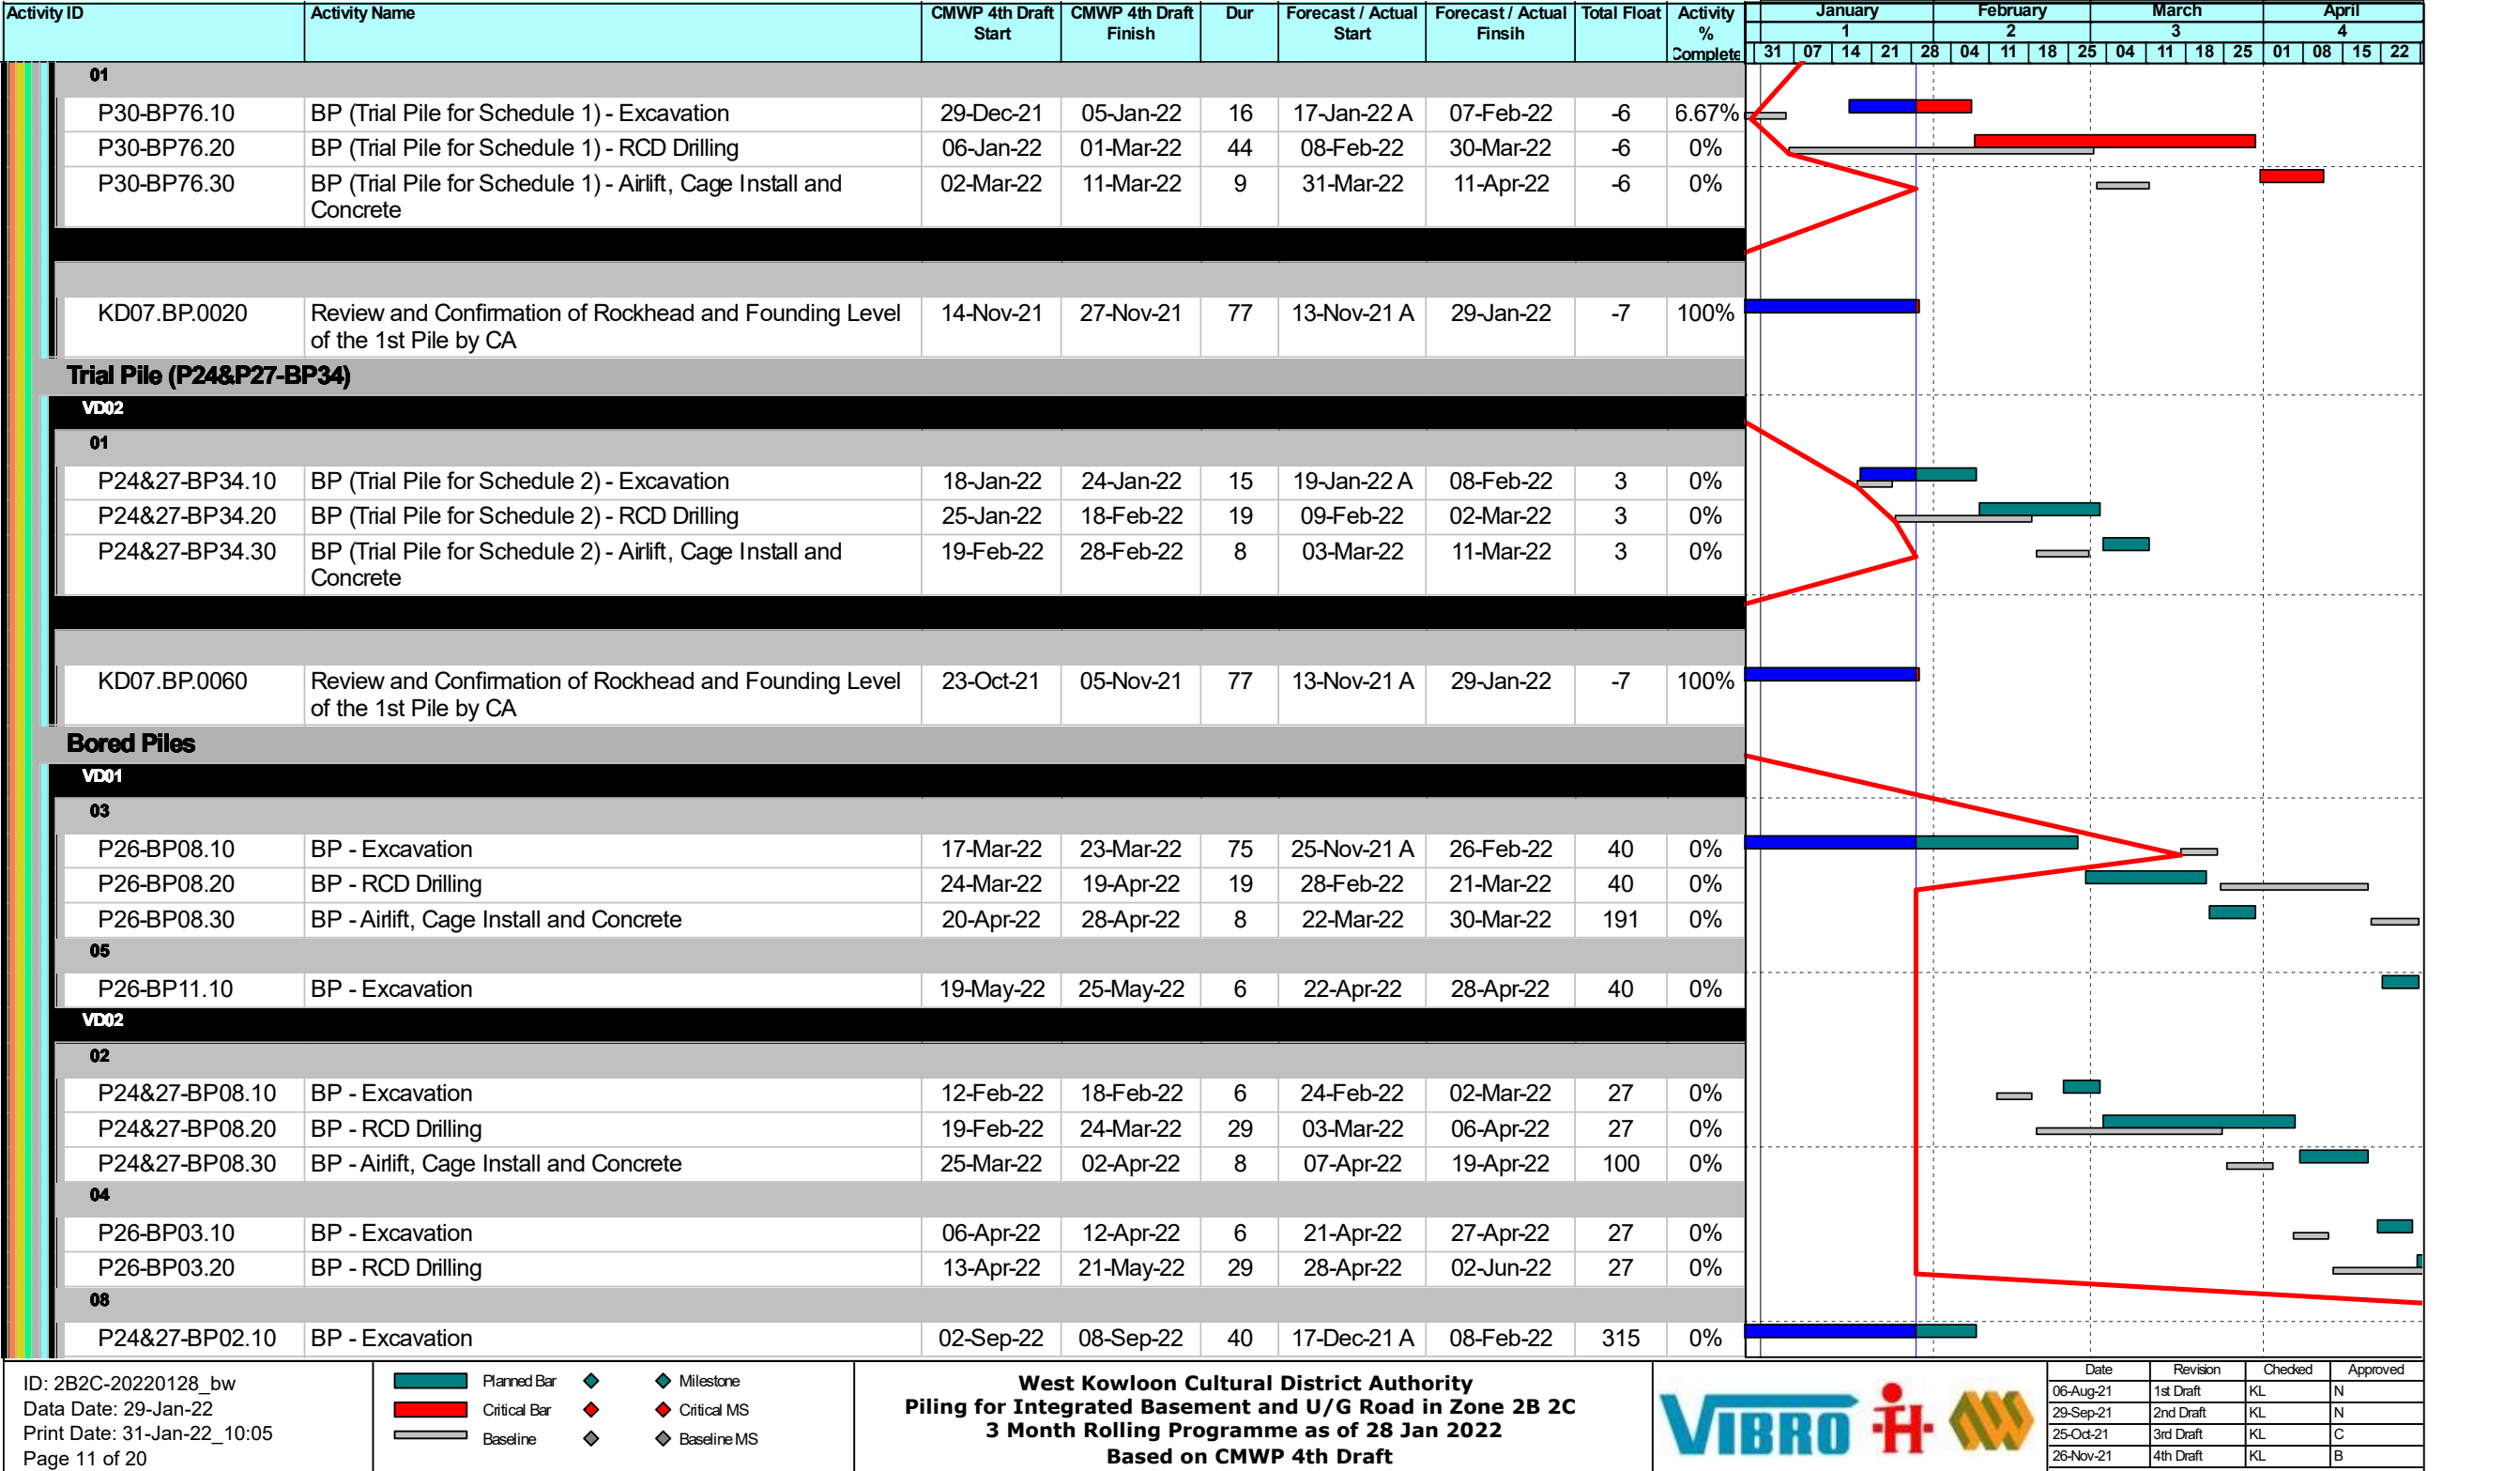

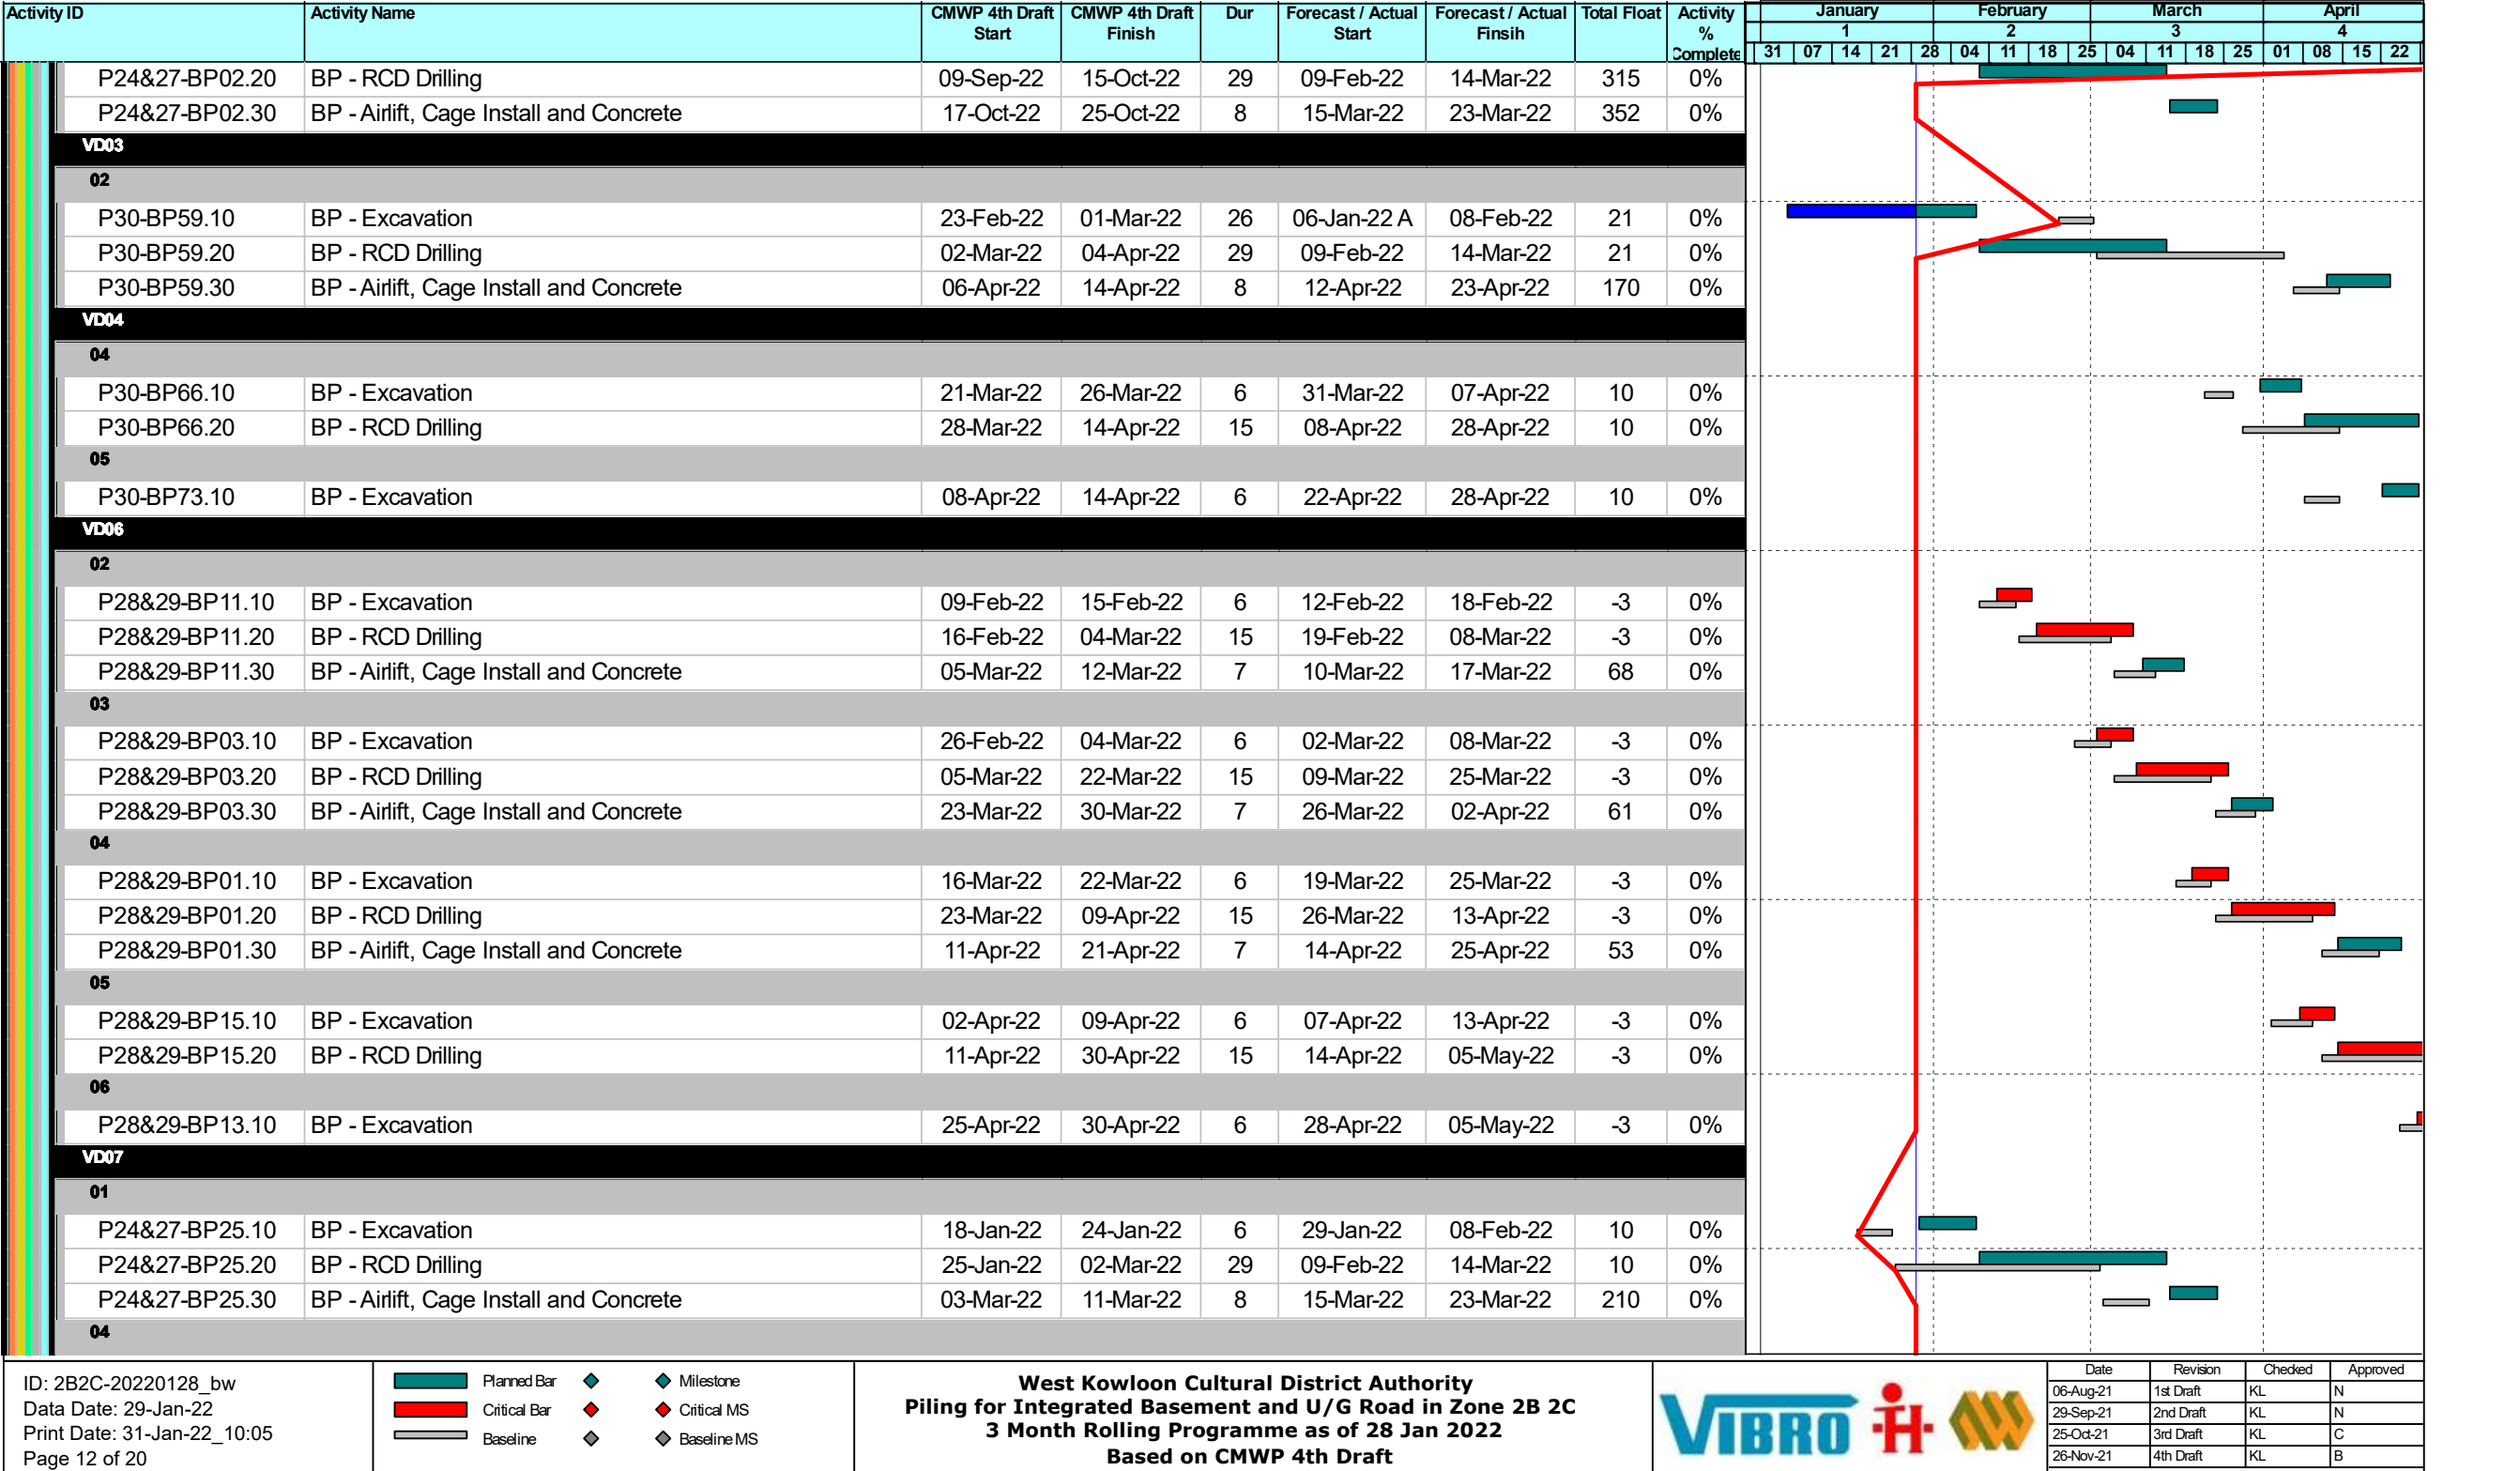

Activity ID	Activity Name	CMWP 4th Draft Start	CMWP 4th Draft Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	January				February				March				April					
									1				2				3				4					
									31	07	14	21	28	04	11	18	25	04	11	18	25	01	08	15	22	
P24&27-BP19.10	BP - Excavation	11-Apr-22	20-Apr-22	6	26-Apr-22	03-May-22	10	0%																		
KD08 (Section 4)																										
Trial Pile (P30-BP15)																										
TD01																										
04																										
P30-BP15.10	BP (Trial Pile for Schedule 3) - Excavation	28-Mar-22	02-Apr-22	6	19-Feb-22	25-Feb-22	46	0%																		
P30-BP15.20	BP (Trial Pile for Schedule 3) - RCD Drilling	04-Apr-22	25-Apr-22	15	26-Feb-22	15-Mar-22	46	0%																		
P30-BP15.30	BP (Trial Pile for Schedule 3) - Airlift, Cage Install and Concrete	26-Apr-22	04-May-22	7	16-Mar-22	23-Mar-22	61	0%																		
Bored Piles																										
VD01																										
04																										
P26-BP12.10	BP - Excavation	09-Apr-22	19-Apr-22	6	15-Mar-22	21-Mar-22	40	0%																		
P26-BP12.20	BP - RCD Drilling	20-Apr-22	25-May-22	29	22-Mar-22	28-Apr-22	40	0%																		
VD03																										
03																										
P30-BP44.10	BP - Excavation	29-Mar-22	04-Apr-22	6	24-Mar-22	30-Mar-22	7	0%																		
P30-BP44.20	BP - RCD Drilling	06-Apr-22	14-May-22	29	31-Mar-22	10-May-22	7	0%																		
VD04																										
01																										
P30-BP41.10	BP - Excavation	19-Jan-22	25-Jan-22	6	29-Jan-22	08-Feb-22	10	0%																		
P30-BP41.20	BP - RCD Drilling	26-Jan-22	15-Feb-22	15	09-Feb-22	25-Feb-22	10	0%																		
P30-BP41.30	BP - Airlift, Cage Install and Concrete	16-Feb-22	23-Feb-22	7	26-Feb-22	05-Mar-22	224	0%																		
02																										
P30-BP47.10	BP - Excavation	09-Feb-22	15-Feb-22	6	19-Feb-22	25-Feb-22	10	0%																		
P30-BP47.20	BP - RCD Drilling	16-Feb-22	04-Mar-22	15	26-Feb-22	15-Mar-22	10	0%																		
P30-BP47.30	BP - Airlift, Cage Install and Concrete	05-Mar-22	12-Mar-22	7	16-Mar-22	23-Mar-22	216	0%																		
03																										
P30-BP58.10	BP - Excavation	26-Feb-22	04-Mar-22	6	09-Mar-22	15-Mar-22	10	0%																		
P30-BP58.20	BP - RCD Drilling	05-Mar-22	26-Mar-22	19	16-Mar-22	07-Apr-22	10	0%																		
P30-BP58.30	BP - Airlift, Cage Install and Concrete	28-Mar-22	06-Apr-22	8	08-Apr-22	20-Apr-22	204	0%																		
10																										
P30-BP60.10	BP - Excavation	13-Jul-22	19-Jul-22	31	30-Dec-21 A	08-Feb-22	130	0%																		
P30-BP60.20	BP - RCD Drilling	20-Jul-22	10-Aug-22	19	09-Feb-22	02-Mar-22	130	0%																		
P30-BP60.30	BP - Airlift, Cage Install and Concrete	11-Aug-22	19-Aug-22	8	03-Mar-22	11-Mar-22	210	0%																		
VD05																										
01																										

ID: 2B2C-20220128_bw
Data Date: 29-Jan-22
Print Date: 31-Jan-22_10:06
Page 13 of 20

Planned Bar

Critical Bar

Baseline

Milestone

Critical MS

Baseline MS

West Kowloon Cultural District Authority

Piling for Integrated Basement and U/G Road in Zone 2B 2C

3 Month Rolling Programme as of 28 Jan 2022

Based on CMWP 4th Draft

VIBRO

Date	Revision	Checked	Approved
06-Aug-21	1st Draft	KL	N
29-Sep-21	2nd Draft	KL	N
25-Oct-21	3rd Draft	KL	C
26-Nov-21	4th Draft	KL	B

Activity ID		Activity Name	CMWP 4th Draft Start	CMWP 4th Draft Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	January				February				March				April							
										1				2				3				4							
										31	07	14	21	28	04	11	18	25	04	11	18	25	01	08	15	22			
<div>2B2C-20220128_bw</div> <div>Data Date: 29-Jan-22</div> <div>Print Date: 31-Jan-22_10:06</div> <div>Page 14 of 20</div>	P30-BP20.30	BP - Airlift, Cage Install and Concrete	23-Dec-21	03-Jan-22	8	28-Dec-21 A	07-Jan-22 A		100%																				
	02																												
	P30-BP19.10	BP - Excavation	16-Dec-21	22-Dec-21	6	29-Jan-22	08-Feb-22	46	0%																				
	P30-BP19.20	BP - RCD Drilling	23-Dec-21	28-Jan-22	29	09-Feb-22	14-Mar-22	46	0%																				
	P30-BP19.30	BP - Airlift, Cage Install and Concrete	29-Jan-22	10-Feb-22	8	15-Mar-22	23-Mar-22	243	0%																				
	03																												
	P30-BP24.10	BP - Excavation	22-Jan-22	28-Jan-22	6	08-Mar-22	14-Mar-22	46	0%																				
	P30-BP24.20	BP - RCD Drilling	29-Jan-22	23-Feb-22	19	15-Mar-22	06-Apr-22	46	0%																				
	P30-BP24.30	BP - Airlift, Cage Install and Concrete	24-Feb-22	04-Mar-22	8	07-Apr-22	19-Apr-22	232	0%																				
	04																												
	P30-BP31.10	BP - Excavation	17-Feb-22	23-Feb-22	6	30-Mar-22	06-Apr-22	46	0%																				
	P30-BP31.20	BP - RCD Drilling	24-Feb-22	29-Mar-22	29	07-Apr-22	16-May-22	46	0%																				
	06																												
	P30-BP33.10	BP - Excavation	11-Apr-22	20-Apr-22	12	22-Jan-22 A	08-Feb-22	281	0%																				
	P30-BP33.20	BP - RCD Drilling	21-Apr-22	10-May-22	15	09-Feb-22	25-Feb-22	281	0%																				
	P30-BP33.30	BP - Airlift, Cage Install and Concrete	11-May-22	18-May-22	7	26-Feb-22	05-Mar-22	281	0%																				
	12																												
	P30-BP39.10	BP - Excavation	25-Aug-22	31-Aug-22	16	10-Dec-21 A	31-Dec-21 A		100%																				
	P30-BP39.20	BP - RCD Drilling	01-Sep-22	19-Sep-22	6	03-Jan-22 A	10-Jan-22 A		100%																				
	P30-BP39.30	BP - Airlift, Cage Install and Concrete	20-Sep-22	27-Sep-22	9	11-Jan-22 A	21-Jan-22 A		100%																				
	13																												
	P30-BP21.10	BP - Excavation	13-Sep-22	19-Sep-22	24	08-Jan-22 A	08-Feb-22	218	0%																				
	P30-BP21.20	BP - RCD Drilling	20-Sep-22	08-Oct-22	15	09-Feb-22	25-Feb-22	218	0%																				
	P30-BP21.30	BP - Airlift, Cage Install and Concrete	10-Oct-22	17-Oct-22	7	26-Feb-22	05-Mar-22	258	0%																				
	TBM																												
	02																												
	P30-BP05.30	BP - Airlift, Cage Install and Concrete	17-Mar-22	25-Mar-22	9	28-Dec-21 A	08-Jan-22 A		100%																				
	03																												
	P30-BP03.10	BP - Excavation	10-Mar-22	16-Mar-22	6	29-Jan-22	08-Feb-22	46	0%																				
	P30-BP03.20	BP - RCD Drilling	17-Mar-22	02-Apr-22	15	09-Feb-22	25-Feb-22	46	0%																				
	P30-BP03.30	BP - Airlift, Cage Install and Concrete	04-Apr-22	12-Apr-22	7	26-Feb-22	05-Mar-22	69	0%																				
	05																												
	P30-BP13.30	BP - Airlift, Cage Install and Concrete	16-May-22	23-May-22	7	20-Dec-21 A	30-Dec-21 A		100%																				
	06																												
	P30-BP11.10	BP - Excavation	07-May-22	14-May-22	6	09-Mar-22	15-Mar-22	46	0%																				
	P30-BP11.20	BP - RCD Drilling	16-May-22	07-Jun-22	19	16-Mar-22	07-Apr-22	46	0%																				
	P30-BP11.30	BP - Airlift, Cage Install and Concrete	08-Jun-22	16-Jun-22	8	08-Apr-22	20-Apr-22	98	0%																				

ID: 2B2C-20220128_bw

Data Date: 29-Jan-22

Print Date: 31-Jan-22_10:06

Page 14 of 20

Planned Bar

Critical Bar

Baseline

Milestone

Critical MS

Baseline MS

West Kowloon Cultural District Authority

Piling for Integrated Basement and U/G Road in Zone 2B 2C

3 Month Rolling Programme as of 28 Jan 2022

Based on CMWP 4th Draft

VIBRO

Date	Revision	Checked	Approved
06-Aug-21	1st Draft	KL	N
29-Sep-21	2nd Draft	KL	N
25-Oct-21	3rd Draft	KL	C
26-Nov-21	4th Draft	KL	B

Activity ID	Activity Name	CMWP 4th Draft Start	CMWP 4th Draft Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	January				February				March				April				
									1				2				3				4				
									31	07	14	21	28	04	11	18	25	04	11	18	25	01	08	15	22
TD09																									
02																									
CBA-BPC52Va.10	BP - Excavation	23-Apr-22	29-Apr-22	6	23-Apr-22	29-Apr-22	0	0%																	
KD09 (Section 5)																									
Trial Piles (P23-BP68)																									
TD03																									
01																									
P23-BP68.10	BP (Trial Pile for Schedule 4) - Excavation	14-Dec-21	20-Dec-21	11	24-Jan-22 A	08-Feb-22	24	0%																	
P23-BP68.20	BP (Trial Pile for Schedule 4) - RCD Drilling	21-Dec-21	26-Jan-22	29	09-Feb-22	14-Mar-22	24	0%																	
P23-BP68.30	BP (Trial Pile for Schedule 4) - Airlift, Cage Install and Concrete	27-Jan-22	08-Feb-22	8	15-Mar-22	23-Mar-22	52	0%																	
Bored Piles																									
VD01																									
01																									
P23-BP44.10	BP - Excavation	05-Feb-22	11-Feb-22	77	01-Nov-21 A	05-Feb-22	40	100%																	
P23-BP44.20	BP - RCD Drilling	12-Feb-22	05-Mar-22	19	05-Feb-22	26-Feb-22	40	0%																	
P23-BP44.30	BP - Airlift, Cage Install and Concrete	07-Mar-22	15-Mar-22	8	28-Feb-22	08-Mar-22	202	0%																	
CD01																									
05																									
P23-BP53.10	BP - Excavation	28-Jan-22	07-Feb-22	6	19-Feb-22	25-Feb-22	67	0%																	
P23-BP53.20	BP - RCD Drilling	08-Feb-22	01-Mar-22	19	26-Feb-22	19-Mar-22	67	0%																	
P23-BP53.30	BP - Airlift, Cage Install and Concrete	02-Mar-22	10-Mar-22	8	21-Mar-22	29-Mar-22	270	0%																	
06																									
P23-BP40.10	BP - Excavation	23-Feb-22	01-Mar-22	6	14-Mar-22	19-Mar-22	67	0%																	
P23-BP40.20	BP - RCD Drilling	02-Mar-22	18-Mar-22	15	21-Mar-22	07-Apr-22	67	0%																	
P23-BP40.30	BP - Airlift, Cage Install and Concrete	19-Mar-22	26-Mar-22	7	08-Apr-22	19-Apr-22	263	0%																	
09																									
P23-BP64.10	BP - Excavation	26-Apr-22	03-May-22	6	31-Mar-22	07-Apr-22	67	0%																	
P23-BP64.20	BP - RCD Drilling	04-May-22	26-May-22	19	08-Apr-22	04-May-22	67	0%																	
10																									
P23-BP62.10	BP - Excavation	20-May-22	26-May-22	6	27-Apr-22	04-May-22	67	0%																	
14																									
P23-BP63.10	BP - Excavation	26-Apr-22	03-May-22	16	18-Jan-22 A	08-Feb-22	131	0%																	
P23-BP63.20	BP - RCD Drilling	04-May-22	26-May-22	19	09-Feb-22	02-Mar-22	131	0%																	
P23-BP63.30	BP - Airlift, Cage Install and Concrete	27-May-22	06-Jun-22	8	03-Mar-22	11-Mar-22	149	0%																	
15																									
P23-BP52.10	BP - Excavation	20-May-22	26-May-22	6	24-Feb-22	02-Mar-22	131	0%																	

ID: 2B2C-20220128_bw
Data Date: 29-Jan-22
Print Date: 31-Jan-22_10:06
Page 15 of 20

Planned Bar

Critical Bar

Baseline

Milestone

Critical MS

Baseline MS

West Kowloon Cultural District Authority

Piling for Integrated Basement and U/G Road in Zone 2B 2C







3 Month Rolling Programme as of 28 Jan 2022

Based on CMWP 4th Draft




VIBRO

Date	Revision	Checked	Approved
06-Aug-21	1st Draft	KL	N
29-Sep-21	2nd Draft	KL	N
25-Oct-21	3rd Draft	KL	C
26-Nov-21	4th Draft	KL	B

Activity ID		Activity Name	CMWP 4th Draft Start	CMWP 4th Draft Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	January				February				March				April			
										1				2				3				4			
										31	07	14	21	28	04	11	18	25	04	11	18	25	01	08	15
	P23-BP52.20	BP - RCD Drilling	27-May-22	18-Jun-22	19	03-Mar-22	24-Mar-22	131	0%																
	P23-BP52.30	BP - Airlift, Cage Install and Concrete	20-Jun-22	28-Jun-22	8	25-Mar-22	02-Apr-22	138	0%																
	17																								
	P23-BP42.10	BP - Excavation	30-Jun-22	07-Jul-22	6	06-Apr-22	12-Apr-22	244	0%																
	P23-BP42.20	BP - RCD Drilling	08-Jul-22	25-Jul-22	15	13-Apr-22	04-May-22	244	0%																
	CD02																								
	02																								
	P23-BP37.10	BP - Excavation	21-Dec-21	29-Dec-21	6	29-Jan-22	08-Feb-22	18	0%																
	P23-BP37.20	BP - RCD Drilling	30-Dec-21	05-Feb-22	29	09-Feb-22	14-Mar-22	18	0%																
	P23-BP37.30	BP - Airlift, Cage Install and Concrete	07-Feb-22	15-Feb-22	8	15-Mar-22	23-Mar-22	242	0%																
	03																								
	P23-BP48.10	BP - Excavation	27-Jan-22	05-Feb-22	6	08-Mar-22	14-Mar-22	18	0%																
	P23-BP48.20	BP - RCD Drilling	07-Feb-22	11-Mar-22	29	15-Mar-22	21-Apr-22	18	0%																
	P23-BP48.30	BP - Airlift, Cage Install and Concrete	12-Mar-22	21-Mar-22	8	22-Apr-22	30-Apr-22	221	0%																
	04																								
	P23-BP39.10	BP - Excavation	05-Mar-22	11-Mar-22	6	12-Apr-22	21-Apr-22	18	0%																
	P23-BP39.20	BP - RCD Drilling	12-Mar-22	02-Apr-22	19	22-Apr-22	16-May-22	18	0%																
	08																								
	P23-BP51.10	BP - Excavation	22-Jun-22	28-Jun-22	23	10-Jan-22 A	08-Feb-22	143	0%																
	P23-BP51.20	BP - RCD Drilling	29-Jun-22	21-Jul-22	19	09-Feb-22	02-Mar-22	143	0%																
	P23-BP51.30	BP - Airlift, Cage Install and Concrete	22-Jul-22	30-Jul-22	8	03-Mar-22	11-Mar-22	292	0%																
TD07																									
02																									
P18-BP16.10	BP - Excavation	20-Dec-21	28-Dec-21	6	19-Feb-22	25-Feb-22	-11	0%																	
	P18-BP16.20	BP - RCD Drilling	29-Dec-21	15-Jan-22	15	26-Feb-22	15-Mar-22	-11	0%																
	P18-BP16.30	BP - Airlift, Cage Install and Concrete	17-Jan-22	24-Jan-22	7	16-Mar-22	23-Mar-22	68	0%																
	03																								
	P18-BP23.10	BP - Excavation	10-Jan-22	15-Jan-22	6	09-Mar-22	15-Mar-22	-11	0%																
	P18-BP23.20	BP - RCD Drilling	17-Jan-22	05-Feb-22	15	16-Mar-22	01-Apr-22	-11	0%																
	P18-BP23.30	BP - Airlift, Cage Install and Concrete	07-Feb-22	14-Feb-22	7	02-Apr-22	11-Apr-22	60	0%																
	04																								
	P18-BP21.10	BP - Excavation	27-Jan-22	05-Feb-22	6	26-Mar-22	01-Apr-22	-11	0%																
	P18-BP21.20	BP - RCD Drilling	07-Feb-22	23-Feb-22	15	02-Apr-22	23-Apr-22	-11	0%																
	P18-BP21.30	BP - Airlift, Cage Install and Concrete	24-Feb-22	03-Mar-22	7	25-Apr-22	03-May-22	52	0%																
	TD06																								
	01																								
	P18-BP36.10	BP - Excavation	20-Dec-21	28-Dec-21	6	29-Jan-22	08-Feb-22	43	0%																

ID: 2B2C-20220128_bw		Planned Bar		Milestone
Data Date: 29-Jan-22		Critical Bar		Critical MS
Print Date: 31-Jan-22_10:06		Baseline		Baseline MS
Page 16 of 20				

West Kowloon Cultural District Authority			
Piling for Integrated Basement and U/G Road in Zone 2B 2C			
3 Month Rolling Programme as of 28 Jan 2022			
Based on CMWP 4th Draft			

			Date	Revision	Checked	Approved
			06-Aug-21	1st Draft	KL	N
			29-Sep-21	2nd Draft	KL	N
			25-Oct-21	3rd Draft	KL	C
			26-Nov-21	4th Draft	KL	B

Activity ID		Activity Name	CMWP 4th Draft Start	CMWP 4th Draft Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	January				February				March				April			
										1				2				3				4			
										31	07	14	21	28	04	11	18	25	04	11	18	25	01	08	15
<div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div>																									

Activity ID		Activity Name	CMWP 4th Draft Start	CMWP 4th Draft Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	January 1				February 2				March 3				April 4			
										1				2				3				4			
										31	07	14	21	28	04	11	18	25	04	11	18	25	01	08	15
<div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <																									

Activity ID		Activity Name	CMWP 4th Draft Start	CMWP 4th Draft Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	Gantt Chart																								
										January 1				February 2				March 3				April 4												
										31	07	14	21	28	04	11	18	25	04	11	18	25	01	08	15	22								
<div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div>	P23-BP59.30	BP - Airlift, Cage Install and Concrete	11-Mar-22	19-Mar-22	8	08-Mar-22	16-Mar-22	231	0%																									
	03																																	
	P23-BP71.10	BP - Excavation	04-Mar-22	10-Mar-22	6	01-Mar-22	07-Mar-22	89	0%																									
	P23-BP71.20	BP - RCD Drilling	11-Mar-22	14-Apr-22	29	08-Mar-22	11-Apr-22	89	0%																									
	P23-BP71.30	BP - Airlift, Cage Install and Concrete	19-Apr-22	27-Apr-22	8	12-Apr-22	23-Apr-22	210	0%																									
	04																																	
	P23-BP83.10	BP - Excavation	08-Apr-22	14-Apr-22	6	04-Apr-22	11-Apr-22	89	0%																									
	P23-BP83.20	BP - RCD Drilling	19-Apr-22	24-May-22	29	12-Apr-22	20-May-22	89	0%																									
	10																																	
	P23-BP94.10	BP - Excavation	26-Jan-22	04-Feb-22	16	18-Jan-22 A	08-Feb-22	32	0%																									
	P23-BP94.20	BP - RCD Drilling	05-Feb-22	10-Mar-22	29	09-Feb-22	14-Mar-22	32	0%																									
	P23-BP94.30	BP - Airlift, Cage Install and Concrete	11-Mar-22	19-Mar-22	8	15-Mar-22	23-Mar-22	202	0%																									
	11																																	
	P23-BP113.10	BP - Excavation	04-Mar-22	10-Mar-22	6	08-Mar-22	14-Mar-22	32	0%																									
	P23-BP113.20	BP - RCD Drilling	11-Mar-22	01-Apr-22	19	15-Mar-22	06-Apr-22	32	0%																									
	P23-BP113.30	BP - Airlift, Cage Install and Concrete	02-Apr-22	12-Apr-22	8	07-Apr-22	19-Apr-22	191	0%																									
	12																																	
	P23-BP111.10	BP - Excavation	26-Mar-22	01-Apr-22	6	30-Mar-22	06-Apr-22	32	0%																									
	P23-BP111.20	BP - RCD Drilling	02-Apr-22	28-Apr-22	19	07-Apr-22	03-May-22	32	0%																									
	13																																	
	P23-BP92.10	BP - Excavation	22-Apr-22	28-Apr-22	6	26-Apr-22	03-May-22	32	0%																									
	Optional Item no. 3																																	
	TD07																																	
	15																																	
	P18-BP18.10	BP (Optional Item no.3) - Excavation	28-Apr-22	05-May-22	6	28-Apr-22	05-May-22	32	0%																									
TD06																																		
17																																		
P18-BP30.10	BP (Optional Item no.3) - Excavation	28-Apr-22	05-May-22	6	28-Apr-22	05-May-22	140	0%																										
Socketed Steel H- Piles																																		
Trial Pile																																		
KD09.SSHP.0000	Test Installation of Pile (SHP-C52Xa-P6)	17-Jan-22	26-Jan-22	9	04-Feb-22	14-Feb-22	6	0%																										
KD09.SSHP.0020	Submission and Approval of Installation Report by BD	27-Jan-22	02-Feb-22	7	15-Feb-22	21-Feb-22	7	0%																										
Socketed Steel H-Pile Construction																																		

ID: 2B2C-20220128_bw Data Date: 29-Jan-22 Print Date: 31-Jan-22_10:06 Page 19 of 20	<div><div></div>Planned Bar</div> <div><div></div>Critical Bar</div> <div><div></div>Baseline</div> <div><div></div>Milestone</div> <div><div></div>Critical MS</div> <div><div></div>Baseline MS</div>	<div>West Kowloon Cultural District Authority</div> <div>Piling for Integrated Basement and U/G Road in Zone 2B 2C</div> <div>3 Month Rolling Programme as of 28 Jan 2022</div> <div>Based on CMWP 4th Draft</div>	<div>VIBRO</div> <div></div> <div></div> <table><tr><td>Date</td><td>Revision</td><td>Checked</td><td>Approved</td></tr><tr><td>06-Aug-21</td><td>1st Draft</td><td>KL</td><td>N</td></tr><tr><td>29-Sep-21</td><td>2nd Draft</td><td>KL</td><td>N</td></tr><tr><td>25-Oct-21</td><td>3rd Draft</td><td>KL</td><td>C</td></tr><tr><td>26-Nov-21</td><td>4th Draft</td><td>KL</td><td>B</td></tr></table>	Date	Revision	Checked	Approved	06-Aug-21	1st Draft	KL	N	29-Sep-21	2nd Draft	KL	N	25-Oct-21	3rd Draft	KL	C	26-Nov-21	4th Draft	KL	B
Date	Revision	Checked	Approved																				
06-Aug-21	1st Draft	KL	N																				
29-Sep-21	2nd Draft	KL	N																				
25-Oct-21	3rd Draft	KL	C																				
26-Nov-21	4th Draft	KL	B																				

Activity ID	Activity Name	CMWP 4th Draft Start	CMWP 4th Draft Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	January				February				March				April				
									1				2				3				4				
									31	07	14	21	28	04	11	18	25	04	11	18	25	01	08	15	22
	SHP-BW-52Y1b-P	Socketed Steel H-Piling	04-Feb-22	12-Feb-22	8	22-Feb-22	02-Mar-22	78	0%																
	SHP-BW-52Y1b-P	Socketed Steel H-Piling	08-Feb-22	16-Feb-22	8	25-Feb-22	05-Mar-22	78	0%																
	SHP-C52W-P1	Socketed Steel H-Piling	11-Feb-22	19-Feb-22	8	01-Mar-22	09-Mar-22	78	0%																
	SHP-C52W-P2	Socketed Steel H-Piling	15-Feb-22	23-Feb-22	8	04-Mar-22	12-Mar-22	78	0%																
	SHP-C52W-P3	Socketed Steel H-Piling	18-Feb-22	26-Feb-22	8	08-Mar-22	16-Mar-22	78	0%																
	SHP-C52W-P4	Socketed Steel H-Piling	22-Feb-22	02-Mar-22	8	11-Mar-22	19-Mar-22	78	0%																
	SHP-C52W-P5	Socketed Steel H-Piling	25-Feb-22	05-Mar-22	8	15-Mar-22	23-Mar-22	78	0%																
	SHP-C52W-P6	Socketed Steel H-Piling	01-Mar-22	09-Mar-22	8	18-Mar-22	26-Mar-22	78	0%																
	SHP-C52X-P1	Socketed Steel H-Piling	04-Mar-22	12-Mar-22	8	22-Mar-22	30-Mar-22	78	0%																
	SHP-C52X-P2	Socketed Steel H-Piling	08-Mar-22	16-Mar-22	8	25-Mar-22	02-Apr-22	78	0%																
	SHP-C52X-P3	Socketed Steel H-Piling	11-Mar-22	19-Mar-22	8	29-Mar-22	07-Apr-22	78	0%																
	SHP-C52X-P4	Socketed Steel H-Piling	15-Mar-22	23-Mar-22	8	01-Apr-22	11-Apr-22	78	0%																
	SHP-C52X-P5	Socketed Steel H-Piling	18-Mar-22	26-Mar-22	8	06-Apr-22	14-Apr-22	78	0%																
	SHP-C52X-P6	Socketed Steel H-Piling	22-Mar-22	30-Mar-22	8	09-Apr-22	21-Apr-22	78	0%																
	SHP-C52Xa-P1	Socketed Steel H-Piling	25-Mar-22	02-Apr-22	8	13-Apr-22	25-Apr-22	78	0%																
	SHP-C52Xa-P2	Socketed Steel H-Piling	29-Mar-22	07-Apr-22	8	20-Apr-22	28-Apr-22	78	0%																
	SHP-C52Xa-P3	Socketed Steel H-Piling	01-Apr-22	11-Apr-22	8	23-Apr-22	03-May-22	78	0%																
	SHP-C52Xa-P4	Socketed Steel H-Piling	06-Apr-22	14-Apr-22	8	27-Apr-22	06-May-22	78	0%																
