

Zone 2A

3-Month Rolling Programme




Activity Description	Duration (Cal. Day)	Start Date	Finish Date	2022																
				February				March				April					May			
				4	11	18	25	4	11	18	25	1	8	15	22	29	6	13	20	27
				W91	W92	W93	W94	W95	W96	W97	W98	W99	W100	W101	W102	W103	W104	W105	W106	W107
Zone 2A-1 Foundation, ELS Works and Blinding to Formation (KD01)																				
ELS (Stage 1) - Grouting / Pipe Pile Works																				
King Post (8/64 Nos Completed) & Erection of Steel Column for Working Platform (13/41 Nos completed)	393	15-May-21	11-Jun-22																	
Zone 2A-2 Foundation, ELS Works and Blinding to Formation (KD02)																				
ELS (Stage 1) - Grouting / Pipe Pile Works																				
King Post (0/86 Nos Completed) & Erection of Steel Column for Working Platform (0/65 Nos Completed)	186	26-Feb-22	30-Aug-22																	
Stage 1a & 1b grouting (936/940 Nos Completed)	499	22-Oct-20	4-Mar-22																	
Pipe Pile Construction (424.5/457 Nos Completed)	530	17-Nov-20	30-Apr-22																	

- Actual
- Remaining Works
- Critical Remaining Works

Project Name: Foundation and ELS Works for Integrated Basement and Underground Road in Zone 2A of the West Kowloon Cultural District

3-Month Rolling Programme

Activity Description	Duration (Cal. Day)	Start Date	Finish Date	2022																			
				March				April					May				June						
				4	11	18	25	1	8	15	22	29	6	13	20	27	3	10	17	24			
				W95	W96	W97	W98	W99	W100	W101	W102	W103	W104	W105	W106	W107	W108	W109	W110	W111			
Zone 2A-1 Foundation, ELS Works and Blinding to Formation (KD01)																							
ELS (Stage 1) - Grouting / Pipe Pile Works																							
King Post (8/64 Nos Completed) & Erection of Steel Column for Working Platform (13/41 Nos completed)				423				15-May-21				11-Jul-22											
Stage 2 grouting (221/314 Nos Completed)				343				28-Sep-21				5-Sep-22											
Pumping Test				62				1-Jun-22				1-Aug-22											
Zone 2A-2 Foundation, ELS Works and Blinding to Formation (KD02)																							
ELS (Stage 1) - Grouting / Pipe Pile Works																							
King Post (0/86 Nos Completed) & Erection of Steel Column for Working Platform (0/65 Nos Completed)				187				26-Mar-22				28-Sep-22											
Pipe Pile Construction (433.5/457 Nos Completed)				544				17-Nov-20				14-May-22											
Stage 2 grouting (393/470 Nos Completed)				305				2-Oct-21				2-Aug-22											

-  - Actual
-  - Remaining Works
-  - Critical Remaining Works


3-Month Rolling Programme

Activity Description	Duration (Cal. Day)	Start Date	Finish Date	2022																
				April					May				June				July			
				1	8	15	22	29	6	13	20	27	3	10	17	24	1	8	15	22
				W99	W100	W101	W102	W103	W104	W105	W106	W107	W108	W109	W110	W111	W112	W113	W114	W115
Zone 2A-1 Foundation, ELS Works and Blinding to Formation (KD01)																				
ELS (Stage 1) - Grouting / Pipe Pile Works																				
King Post (8/64 Nos Completed) & Erection of Steel Column for Working Platform (11/41 Nos completed)	446	15-May-21	3-Aug-22																	
Stage 2 grouting (221/314 Nos Completed)	345	28-Sep-21	7-Sep-22																	
Pumping Test																				
Installation of Pump Wells (0/24 Nos completed)	61	4-Jun-22	3-Aug-22																	
Zone 2A-2 Foundation, ELS Works and Blinding to Formation (KD02)																				
ELS (Stage 1) - Grouting / Pipe Pile Works																				
King Post (0/86 Nos Completed) & Erection of Steel Column for Working Platform (0/65 Nos Completed)	185	23-Apr-22	24-Oct-22																	
Pipe Pile Construction (452/461 Nos Completed)	540	17-Nov-20	10-May-22																	
Stage 2 grouting (405/475 Nos Completed)	292	2-Oct-21	20-Jul-22																	
Pumping Test																				
Installation of Pump Wells (3/102 Nos completed)	57	11-Apr-22	6-Jun-22																	
Baseline Monitoring	1	7-Jun-22	7-Jun-22																	
Pumping Test	14	21-Jul-22	3-Aug-22																	

- Actual
- Remaining Works
- Critical Remaining Works


Zone 2B & 2C

Activity ID	Activity Name	CMWP 4th Draft Start	CMWP 4th Draft Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	Activity	January	February	March	April	May																																		
										21	28	04	11	18	25	04	11	18	25	01	08	15	22	29	06	13																						
Piling for Integrated Basement and U/G Road in Zone 2B & 2C																																																
Contract Dates																																																
Key Dates																																																
KD for Zone 2C																																																
KD02	KD02 (Stage 5-1) - 200 days after Commencement (7 Feb 2022)		06-Feb-22	0		04-Apr-22*	-56	0%																																								
Optional Works subjected to CA's Instruction																																																
CO3A	Last CAI date for Optional Works Item No.3 (within 280 Days after Commencement)	28-Apr-22		0	28-Apr-22		2	0%																																								
Access Dates of Site Portion																																																
120 days after Commencement																																																
ACB10	Access to Site Portion B10	19-Nov-21		0	19-Feb-22		-63	0%																																								
150 days after Commencement																																																
ACB34	Access to Site Portion B34	19-Dec-21		0	11-Feb-22 A			100%																																								
270 days after Commencement																																																
ACB12	Access to Site Portion B12	18-Apr-22		0	18-Apr-22		28	0%																																								
ACB35	Access to Site Portion B35 (To be agreed with the Zone 2A contractor)	18-Apr-22		0	18-Apr-22		28	0%																																								
Mobilization Stage																																																
Site Mobilization Works																																																
Pre-Construction Works before Piling Commencement																																																
MOBP.10.1200	Installation of Monitoring Check Points (Stage 2) [33 nos.]	20-Nov-21	08-Dec-21	59	10-Jan-22 A	09-Mar-22	40	0%																																								
MOBP.10.1260	Erection of Hoardings (Stage 2)	20-Dec-21	31-Jan-22	50	08-Jan-22 A	26-Feb-22	111	80%																																								
ID: 2B2C-20220218_w Data Date: 19-Feb-22 Print Date: 21-Feb-22_11:53 Page 1 of 19										<div><div></div><div></div><div></div></div> <div>Planned BarCritical BarBaseline</div> <div><div></div><div></div><div></div></div> <div>MilestoneCritical MSBaseline MS</div>					West Kowloon Cultural District Authority Piling for Integrated Basement and U/G Road in Zone 2B 2C 3 Month Rolling Programme as of 18 Feb 2022 Based on CMWP 4th Draft					<div><div></div><div></div><div></div></div> <div>VIBRO</div>					<table><tr><th>Date</th><th>Revision</th><th>Checked</th><th>Approved</th></tr><tr><td>06-Aug-21</td><td>1st Draft</td><td>KL</td><td>N</td></tr><tr><td>29-Sep-21</td><td>2nd Draft</td><td>KL</td><td>N</td></tr><tr><td>25-Oct-21</td><td>3rd Draft</td><td>KL</td><td>C</td></tr><tr><td>26-Nov-21</td><td>4th Draft</td><td>KL</td><td>B</td></tr></table>				Date	Revision	Checked	Approved	06-Aug-21	1st Draft	KL	N	29-Sep-21	2nd Draft	KL	N	25-Oct-21	3rd Draft	KL	C	26-Nov-21	4th Draft	KL	B
Date	Revision	Checked	Approved																																													
06-Aug-21	1st Draft	KL	N																																													
29-Sep-21	2nd Draft	KL	N																																													
25-Oct-21	3rd Draft	KL	C																																													
26-Nov-21	4th Draft	KL	B																																													

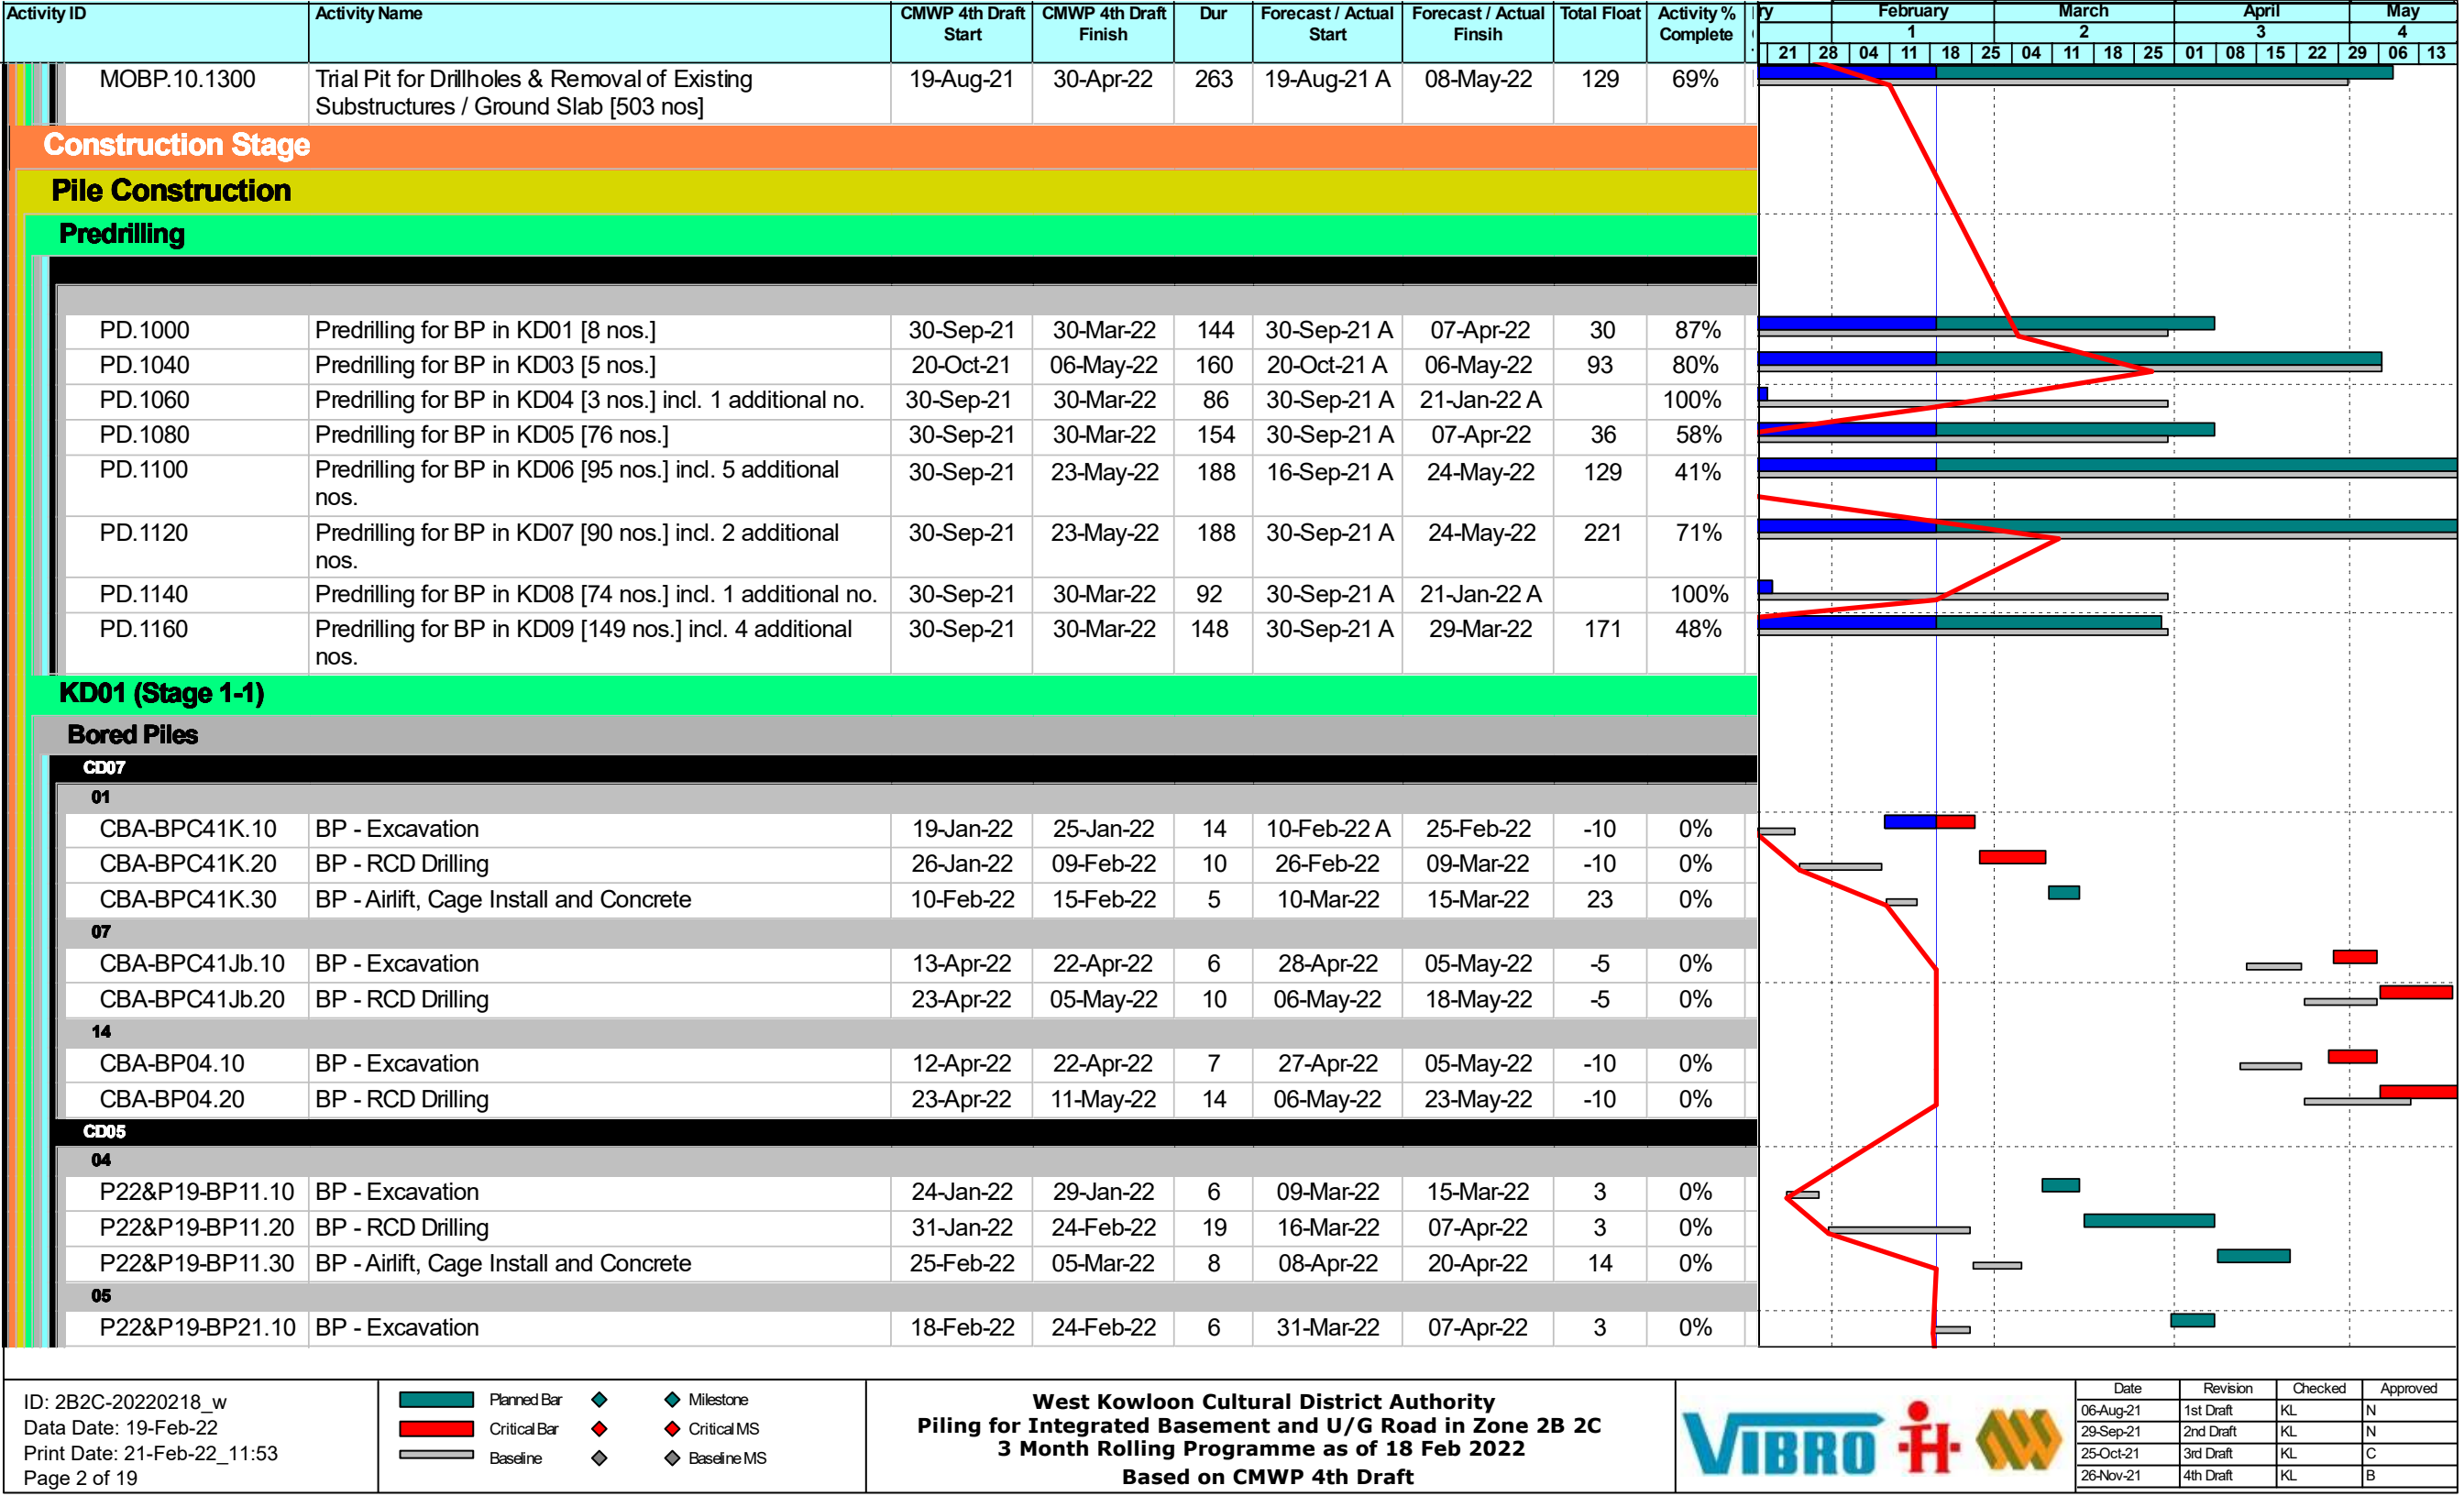

Activity ID	Activity Name	CMWP 4th Draft Start	CMWP 4th Draft Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	Activity % Complete	Gantt Chart																																				
										January				February				March				April				May																				
										21	28	04	11	18	25	04	11	18	25	01	08	15	22	29	06	13																				
CD03	P22&P19-BP21.20	BP - RCD Drilling	25-Feb-22	18-Mar-22	19	08-Apr-22	04-May-22	3	0%																																					
	P22&P19-BP21.30	BP - Airlift, Cage Install and Concrete	19-Mar-22	28-Mar-22	8	05-May-22	14-May-22	3	0%																																					
	07																																													
	P22&P19-BP29.10	BP - Excavation	04-Apr-22	11-Apr-22	27	22-Jan-22 A	25-Feb-22	37	0%																																					
	P22&P19-BP29.20	BP - RCD Drilling	12-Apr-22	07-May-22	19	26-Feb-22	19-Mar-22	37	0%																																					
	P22&P19-BP29.30	BP - Airlift, Cage Install and Concrete	10-May-22	18-May-22	8	21-Mar-22	29-Mar-22	37	0%																																					
	CD03																																													
	06																																													
	P23-BP06.20	BP - RCD Drilling	11-Apr-22	06-May-22	23	17-Jan-22 A	16-Feb-22 A		100%																																					
	P23-BP06.30	BP - Airlift, Cage Install and Concrete	07-May-22	17-May-22	10	17-Feb-22 A	28-Feb-22	62	0%																																					
KD02 (Stage 5-1)																																														
Bored Piles																																														
CD01																																														
04																																														
P23-BP43.20	BP - RCD Drilling	10-Dec-21	30-Dec-21	13	05-Jan-22 A	20-Jan-22 A		100%																																						
P23-BP43.30	BP - Airlift, Cage Install and Concrete	31-Dec-21	10-Jan-22	14	21-Jan-22 A	10-Feb-22 A		100%																																						
TD04																																														
01																																														
P23-BP76.10	BP - Excavation	03-Dec-21	09-Dec-21	21	24-Dec-21 A	21-Jan-22 A		100%																																						
P23-BP76.20	BP - RCD Drilling	10-Dec-21	30-Dec-21	19	22-Jan-22 A	17-Feb-22 A		100%																																						
P23-BP76.30	BP - Airlift, Cage Install and Concrete	31-Dec-21	10-Jan-22	9	18-Feb-22 A	28-Feb-22	-26	0%																																						
02																																														
P23-BP87.10	BP - Excavation	03-Dec-21	09-Dec-21	29	04-Jan-22 A	10-Feb-22 A		100%																																						
P23-BP87.20	BP - RCD Drilling	10-Dec-21	10-Jan-22	5	11-Feb-22 A	17-Feb-22 A		100%																																						
P23-BP87.30	BP - Airlift, Cage Install and Concrete	11-Jan-22	19-Jan-22	17	18-Feb-22 A	09-Mar-22	-26	0%																																						
03																																														
P23-BP117.10	BP - Excavation	03-Dec-21	09-Dec-21	38	10-Jan-22 A	25-Feb-22	-48	0%																																						
P23-BP117.20	BP - RCD Drilling	10-Dec-21	10-Jan-22	24	26-Feb-22	25-Mar-22	-48	0%																																						
P23-BP117.30	BP - Airlift, Cage Install and Concrete	20-Jan-22	28-Jan-22	8	26-Mar-22	04-Apr-22	-48	0%																																						
KD03 (Stage 3-1)																																														
KD03.BP.0040																																														
KD03.BP.0040	Review and Confirmation of Rockhead and Founding Level of Pile by CA	14-Nov-21	27-Nov-21	14	19-Feb-22	04-Mar-22	-24	0%																																						
Bored Piles																																														
VD02																																														
03																																														
P28&29-BP08.10	BP - Excavation	18-Mar-22	24-Mar-22	6	21-Apr-22	27-Apr-22	12	0%																																						
P28&29-BP08.20	BP - RCD Drilling	25-Mar-22	12-Apr-22	15	28-Apr-22	17-May-22	12	0%																																						
ID: 2B2C-20220218_w Data Date: 19-Feb-22 Print Date: 21-Feb-22_11:53 Page 3 of 19														West Kowloon Cultural District Authority Piling for Integrated Basement and U/G Road in Zone 2B 2C 3 Month Rolling Programme as of 18 Feb 2022 Based on CMWP 4th Draft								<table><tr><th>Date</th><th>Revision</th><th>Checked</th><th>Approved</th></tr><tr><td>06-Aug-21</td><td>1st Draft</td><td>KL</td><td>N</td></tr><tr><td>29-Sep-21</td><td>2nd Draft</td><td>KL</td><td>N</td></tr><tr><td>25-Oct-21</td><td>3rd Draft</td><td>KL</td><td>C</td></tr><tr><td>26-Nov-21</td><td>4th Draft</td><td>KL</td><td>B</td></tr></table>				Date	Revision	Checked	Approved	06-Aug-21	1st Draft	KL	N	29-Sep-21	2nd Draft	KL	N	25-Oct-21	3rd Draft	KL	C	26-Nov-21	4th Draft	KL	B	
Date	Revision	Checked	Approved																																											
06-Aug-21	1st Draft	KL	N																																											
29-Sep-21	2nd Draft	KL	N																																											
25-Oct-21	3rd Draft	KL	C																																											
26-Nov-21	4th Draft	KL	B																																											

[illegible]

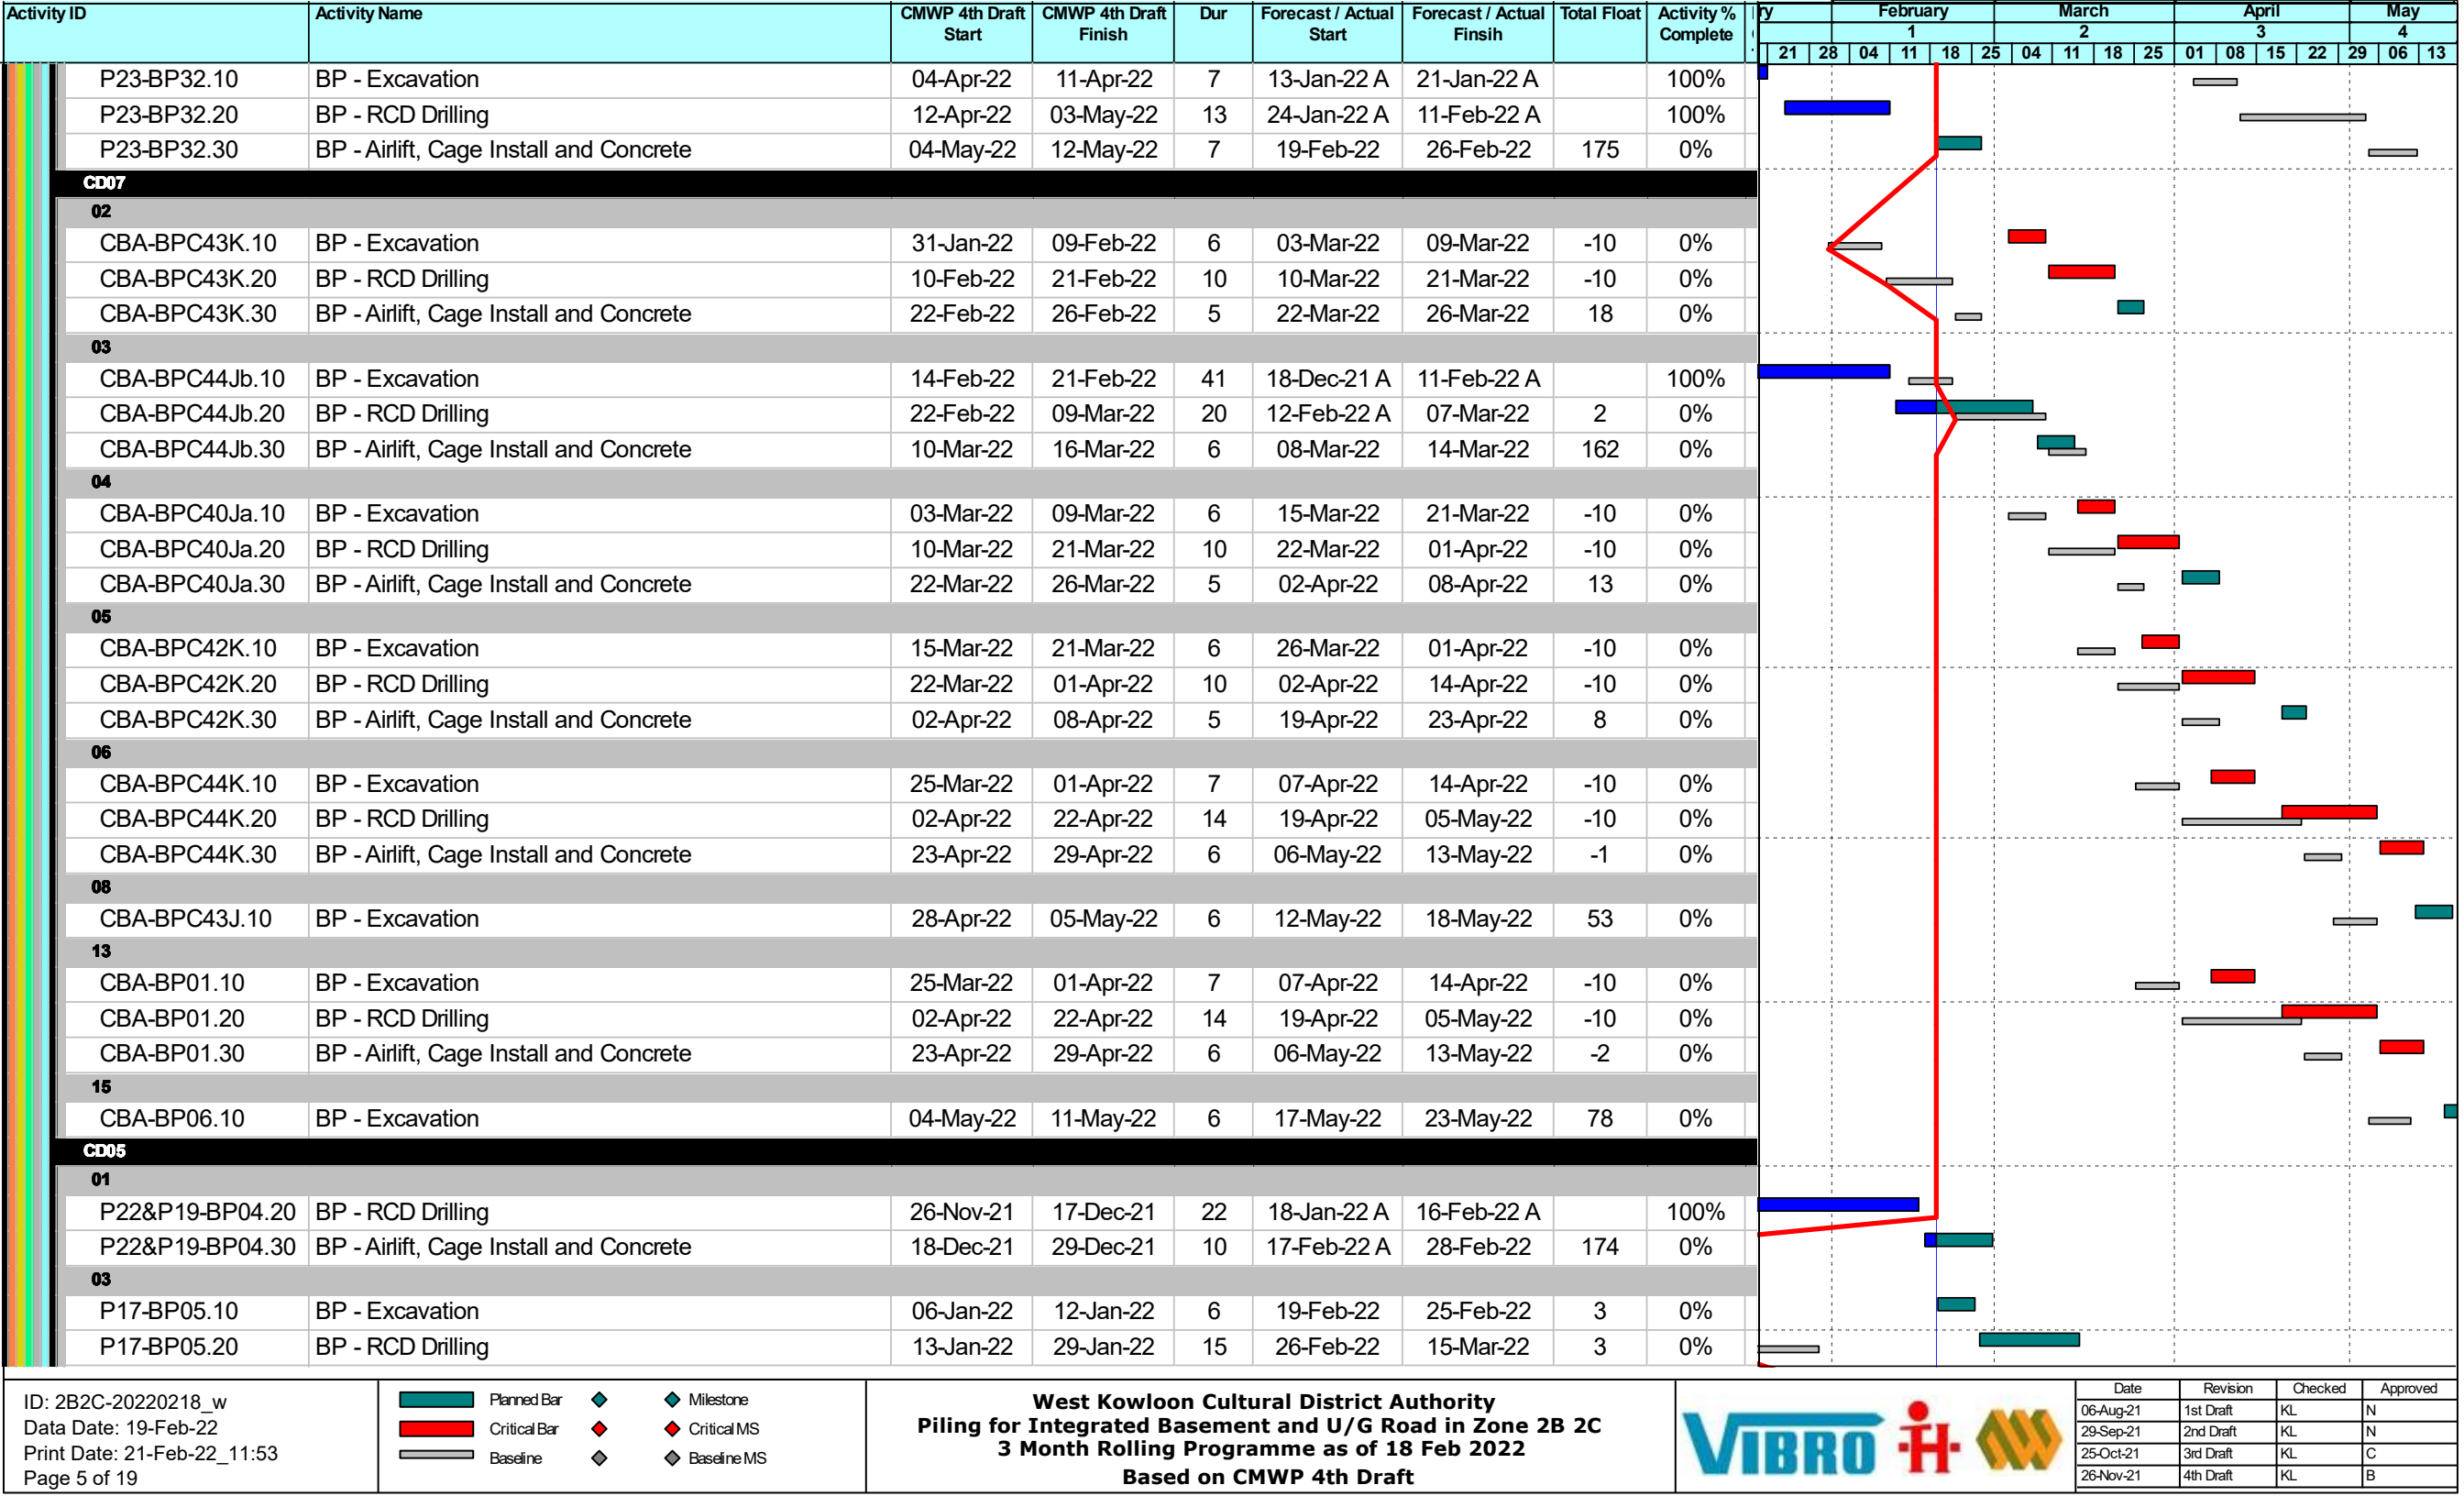

Activity ID	Activity Name	CMWP 4th Draft Start	CMWP 4th Draft Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity % Complete	Activity %
-------------	---------------	----------------------	-----------------------	-----	-------------------------	--------------------------	-------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	------------

Activity ID	Activity Name	CMWP 4th Draft Start	CMWP 4th Draft Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	Activity % Complete	Gantt Chart																						
										January					February					March					April				May			
										21	28	04	11	18	25	04	11	18	25	01	08	15	22	29	06	13						
	CBA-BPC38Ja.10	BP - Excavation	01-Dec-21	07-Dec-21	28	21-Jan-22 A	25-Feb-22	161	0%																							
	CBA-BPC38Ja.20	BP - RCD Drilling	08-Dec-21	18-Dec-21	10	26-Feb-22	09-Mar-22	161	0%																							
	CBA-BPC38Ja.30	BP - Airlift, Cage Install and Concrete	20-Dec-21	24-Dec-21	5	10-Mar-22	15-Mar-22	161	0%																							
03																																
	CBA-BPC38K.10	BP - Excavation	13-Dec-21	18-Dec-21	22	28-Dec-21 A	24-Jan-22 A		100%																							
	CBA-BPC38K.20	BP - RCD Drilling	20-Dec-21	03-Jan-22	16	25-Jan-22 A	16-Feb-22 A		100%																							
	CBA-BPC38K.30	BP - Airlift, Cage Install and Concrete	04-Jan-22	08-Jan-22	7	17-Feb-22 A	24-Feb-22	127	0%																							
04																																
	CBA-BPC40M.10	BP - Excavation	24-Dec-21	03-Jan-22	6	19-Feb-22	25-Feb-22	71	0%																							
	CBA-BPC40M.20	BP - RCD Drilling	04-Jan-22	14-Jan-22	10	26-Feb-22	09-Mar-22	71	0%																							
	CBA-BPC40M.30	BP - Airlift, Cage Install and Concrete	15-Jan-22	20-Jan-22	5	10-Mar-22	15-Mar-22	116	0%																							
05																																
	CBA-BPC40O.10	BP - Excavation	08-Jan-22	14-Jan-22	6	03-Mar-22	09-Mar-22	71	0%																							
	CBA-BPC40O.20	BP - RCD Drilling	15-Jan-22	26-Jan-22	10	10-Mar-22	21-Mar-22	71	0%																							
	CBA-BPC40O.30	BP - Airlift, Cage Install and Concrete	27-Jan-22	04-Feb-22	5	22-Mar-22	26-Mar-22	111	0%																							
06																																
	CBA-BPC39Jb.10	BP - Excavation	20-Jan-22	26-Jan-22	6	15-Mar-22	21-Mar-22	71	0%																							
	CBA-BPC39Jb.20	BP - RCD Drilling	27-Jan-22	10-Feb-22	10	22-Mar-22	01-Apr-22	71	0%																							
	CBA-BPC39Jb.30	BP - Airlift, Cage Install and Concrete	11-Feb-22	16-Feb-22	5	02-Apr-22	08-Apr-22	106	0%																							
07																																
	CBA-BPC38Jb.10	BP - Excavation	04-Feb-22	10-Feb-22	6	26-Mar-22	01-Apr-22	71	0%																							
	CBA-BPC38Jb.20	BP - RCD Drilling	11-Feb-22	22-Feb-22	10	02-Apr-22	14-Apr-22	71	0%																							
	CBA-BPC38Jb.30	BP - Airlift, Cage Install and Concrete	23-Feb-22	28-Feb-22	5	19-Apr-22	23-Apr-22	101	0%																							
08																																
	CBA-BPC38Ka.10	BP - Excavation	16-Feb-22	22-Feb-22	6	08-Apr-22	14-Apr-22	71	0%																							
	CBA-BPC38Ka.20	BP - RCD Drilling	23-Feb-22	05-Mar-22	10	19-Apr-22	29-Apr-22	71	0%																							
	CBA-BPC38Ka.30	BP - Airlift, Cage Install and Concrete	07-Mar-22	11-Mar-22	5	30-Apr-22	06-May-22	96	0%																							
09																																
	CBA-BPC40K.10	BP - Excavation	28-Feb-22	05-Mar-22	6	23-Apr-22	29-Apr-22	71	0%																							
	CBA-BPC40K.20	BP - RCD Drilling	07-Mar-22	17-Mar-22	10	30-Apr-22	13-May-22	71	0%																							
	CBA-BPC40K.30	BP - Airlift, Cage Install and Concrete	18-Mar-22	23-Mar-22	5	14-May-22	19-May-22	91	0%																							
TD07																																
01																																
	P18-BP10.10	BP - Excavation	19-Nov-21	25-Nov-21	6	19-Feb-22	25-Feb-22	-26	0%																							
	P18-BP10.20	BP - RCD Drilling	26-Nov-21	13-Dec-21	15	26-Feb-22	15-Mar-22	-26	0%																							
	P18-BP10.30	BP - Airlift, Cage Install and Concrete	14-Dec-21	21-Dec-21	7	16-Mar-22	23-Mar-22	61	0%																							
05																																
	P18-BP02.10	BP - Excavation	17-Feb-22	23-Feb-22	6	06-May-22	13-May-22	-26	0%																							
ID: 2B2C-20220218_w Data Date: 19-Feb-22 Print Date: 21-Feb-22_11:53 Page 7 of 19		<div><div>Planned Bar</div><div>Critical Bar</div><div>Baseline</div></div> <div><div>Milestone</div><div>Critical MS</div><div>Baseline MS</div></div>			West Kowloon Cultural District Authority Piling for Integrated Basement and U/G Road in Zone 2B 2C 3 Month Rolling Programme as of 18 Feb 2022 Based on CMWP 4th Draft						<div><div>VIBRO</div><div></div><div></div></div>				Date				Revision		Checked		Approved									
															06-Aug-21				1st Draft		KL		N									
															29-Sep-21				2nd Draft		KL		N									
															25-Oct-21				3rd Draft		KL		C									
															26-Nov-21				4th Draft		KL		B									







Activity ID	Activity Name	CMWP 4th Draft Start	CMWP 4th Draft Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	Activity % Complete	Calendar																			
										January				February					March					April				May	
										21	28	04	11	18	25	04	11	18	25	01	08	15	22	29	06	13			
<div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <																													

Activity ID	Activity Name	CMWP 4th Draft Start	CMWP 4th Draft Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	Activity % Complete	Schedule																								
										January					February					March					April					May				
										21	28	04	11	18	25	04	11	18	25	01	08	15	22	29	06	13								
P22&P19-BP22.30	BP - Airlift, Cage Install and Concrete	17-Feb-22	25-Feb-22	8	08-Apr-22	20-Apr-22	134	0%																										
03																																		
P22&P19-BP23.10	BP - Excavation	10-Feb-22	16-Feb-22	6	31-Mar-22	07-Apr-22	-23	0%																										
P22&P19-BP23.20	BP - RCD Drilling	17-Feb-22	10-Mar-22	19	08-Apr-22	04-May-22	-23	0%																										
P22&P19-BP23.30	BP - Airlift, Cage Install and Concrete	11-Mar-22	19-Mar-22	8	05-May-22	14-May-22	123	0%																										
04																																		
P22&P19-BP28.10	BP - Excavation	04-Mar-22	10-Mar-22	6	27-Apr-22	04-May-22	-23	0%																										
P22&P19-BP28.20	BP - RCD Drilling	11-Mar-22	01-Apr-22	19	05-May-22	27-May-22	-23	0%																										
CD05																																		
12																																		
P22&P19-BP24.10	BP - Excavation	12-Feb-22	18-Feb-22	6	25-Mar-22	31-Mar-22	63	0%																										
P22&P19-BP24.20	BP - RCD Drilling	19-Feb-22	12-Mar-22	19	01-Apr-22	27-Apr-22	63	0%																										
P22&P19-BP24.30	BP - Airlift, Cage Install and Concrete	14-Mar-22	22-Mar-22	8	28-Apr-22	07-May-22	96	0%																										
CD03																																		
02																																		
P23-BP10.10	BP - Excavation	16-Dec-21	22-Dec-21	6	19-Feb-22	25-Feb-22	76	0%																										
P23-BP10.20	BP - RCD Drilling	23-Dec-21	17-Jan-22	19	26-Feb-22	19-Mar-22	76	0%																										
P23-BP10.30	BP - Airlift, Cage Install and Concrete	18-Jan-22	26-Jan-22	8	21-Mar-22	29-Mar-22	261	0%																										
03																																		
P23-BP25.10	BP - Excavation	11-Jan-22	17-Jan-22	6	14-Mar-22	19-Mar-22	76	0%																										
P23-BP25.20	BP - RCD Drilling	18-Jan-22	11-Feb-22	19	21-Mar-22	12-Apr-22	76	0%																										
P23-BP25.30	BP - Airlift, Cage Install and Concrete	12-Feb-22	21-Feb-22	8	13-Apr-22	25-Apr-22	250	0%																										
04																																		
P23-BP15.10	BP - Excavation	05-Feb-22	11-Feb-22	6	06-Apr-22	12-Apr-22	76	0%																										
P23-BP15.20	BP - RCD Drilling	12-Feb-22	17-Mar-22	29	13-Apr-22	21-May-22	76	0%																										
05																																		
P23-BP17.10	BP - Excavation	11-Mar-22	17-Mar-22	16	08-Feb-22 A	25-Feb-22	124	0%																										
P23-BP17.20	BP - RCD Drilling	18-Mar-22	09-Apr-22	19	26-Feb-22	19-Mar-22	124	0%																										
P23-BP17.30	BP - Airlift, Cage Install and Concrete	11-Apr-22	22-Apr-22	8	21-Mar-22	29-Mar-22	277	0%																										
08																																		
P23-BP04.30	BP - Airlift, Cage Install and Concrete	23-Jun-22	02-Jul-22	7	15-Jan-22 A	24-Jan-22 A		100%																										
09																																		
P23-BP14.10	BP - Excavation	16-Jun-22	22-Jun-22	6	16-May-22	21-May-22	76	0%																										
KD07 (Section 3)																																		
Trial Pile (P30-BP76)																																		
VD03																																		
01																																		
P30-BP76.10	BP (Trial Pile for Schedule 1) - Excavation	29-Dec-21	05-Jan-22	31	17-Jan-22 A	24-Feb-22	-21	16.67%																										
P30-BP76.20	BP (Trial Pile for Schedule 1) - RCD Drilling	06-Jan-22	01-Mar-22	44	25-Feb-22	21-Apr-22	-21	0%																										
ID: 2B2C-20220218_w																																		
Data Date: 19-Feb-22																																		
Print Date: 21-Feb-22_11:53																																		
Page 9 of 19																																		

Activity ID										Activity Name	CMWP 4th Draft Start	CMWP 4th Draft Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	
<div>Trial Pile (P24&P27-BP34)</div>																		
<div>VD02</div>																		
<div>01</div>																		
<div>P24&27-BP34.10BP (Trial Pile for Schedule 2) - Excavation18-Jan-2224-Jan-223019-Jan-22 A25-Feb-22-120%</div>																		
<div>P24&27-BP34.20BP (Trial Pile for Schedule 2) - RCD Drilling25-Jan-2218-Feb-221926-Feb-2219-Mar-22-120%</div>																		
<div>P24&27-BP34.30BP (Trial Pile for Schedule 2) - Airlift, Cage Install and Concrete19-Feb-2228-Feb-22821-Mar-2229-Mar-22-120%</div>																		
<div>KD07.BP.0060Review and Confirmation of Rockhead and Founding Level of Pile by CA23-Oct-2105-Nov-218913-Nov-21 A10-Feb-22 A100%</div>																		
<div>Bored Piles</div>																		
<div>VD01</div>																		
<div>03</div>																		
<div>P26-BP08.10BP - Excavation17-Mar-2223-Mar-228725-Nov-21 A12-Mar-22280%</div>																		
<div>P26-BP08.20BP - RCD Drilling24-Mar-2219-Apr-221914-Mar-2204-Apr-22280%</div>																		
<div>P26-BP08.30BP - Airlift, Cage Install and Concrete20-Apr-2228-Apr-22806-Apr-2214-Apr-221790%</div>																		
<div>05</div>																		
<div>P26-BP11.10BP - Excavation19-May-2225-May-22607-May-2214-May-22280%</div>																		
<div>P26-BP11.20BP - RCD Drilling26-May-2217-Jun-221916-May-2207-Jun-22280%</div>																		
<div>VD02</div>																		
<div>02</div>																		
<div>P24&27-BP08.10BP - Excavation12-Feb-2218-Feb-22614-Mar-2219-Mar-22120%</div>																		
<div>P24&27-BP08.20BP - RCD Drilling19-Feb-2224-Mar-222921-Mar-2227-Apr-22120%</div>																		
<div>P24&27-BP08.30BP - Airlift, Cage Install and Concrete25-Mar-2202-Apr-22828-Apr-2207-May-22850%</div>																		
<div>04</div>																		
<div>P26-BP03.10BP - Excavation06-Apr-2212-Apr-22611-May-2217-May-22120%</div>																		
<div>P26-BP03.20BP - RCD Drilling13-Apr-2221-May-222918-May-2221-Jun-22120%</div>																		
<div>08</div>																		
<div>P24&27-BP02.10BP - Excavation02-Sep-2208-Sep-225517-Dec-21 A25-Feb-223000%</div>																		
<div>P24&27-BP02.20BP - RCD Drilling09-Sep-2215-Oct-222926-Feb-2231-Mar-223000%</div>																		
<div>P24&27-BP02.30BP - Airlift, Cage Install and Concrete17-Oct-2225-Oct-22801-Apr-2211-Apr-223370%</div>																		
<div>VD03</div>																		
<div>02</div>																		
<div>ID: 2B2C-20220218_w Data Date: 19-Feb-22 Print Date: 21-Feb-22_11:53 Page 10 of 19</div>																		
<div>West Kowloon Cultural District Authority Piling for Integrated Basement and U/G Road in Zone 2B 2C 3 Month Rolling Programme as of 18 Feb 2022 Based on CMWP 4th Draft</div>																		
<div>VIBRO logo</div>																		
<div>DateRevisionCheckedApproved 06-Aug-211st DraftKLNB 29-Sep-212nd DraftKLN 25-Oct-213rd DraftKLC 26-Nov-214th DraftKLB</div>																		

[illegible]

Activity ID	Activity Name	CMWP 4th Draft Start	CMWP 4th Draft Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	Activity % Complete	Gantt Chart																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																													
										February				March				April				May																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																	
										1	18	25	2	9	16	23	30	6	13	20	27																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																		
P24&27-BP19.10	BP - Excavation	11-Apr-22	20-Apr-22	6	16-May-22	21-May-22	-5	0%																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																															</

Activity ID	Activity Name	CMWP 4th Draft Start	CMWP 4th Draft Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	Activity	January				February				March				April				May			
										1				2				3				4							
										21	28	04	11	18	25	04	11	18	25	01	08	15	22	29	06	13			
	P30-BP60.30	BP - Airlift, Cage Install and Concrete	11-Aug-22	19-Aug-22	15	11-Feb-22 A	28-Feb-22	286	0%																				
VD05																													
02																													
	P30-BP19.10	BP - Excavation	16-Dec-21	22-Dec-21	6	19-Feb-22	25-Feb-22	31	0%																				
	P30-BP19.20	BP - RCD Drilling	23-Dec-21	28-Jan-22	29	26-Feb-22	31-Mar-22	31	0%																				
	P30-BP19.30	BP - Airlift, Cage Install and Concrete	29-Jan-22	10-Feb-22	8	01-Apr-22	11-Apr-22	228	0%																				
03																													
	P30-BP24.10	BP - Excavation	22-Jan-22	28-Jan-22	6	25-Mar-22	31-Mar-22	31	0%																				
	P30-BP24.20	BP - RCD Drilling	29-Jan-22	23-Feb-22	19	01-Apr-22	27-Apr-22	31	0%																				
	P30-BP24.30	BP - Airlift, Cage Install and Concrete	24-Feb-22	04-Mar-22	8	28-Apr-22	07-May-22	217	0%																				
04																													
	P30-BP31.10	BP - Excavation	17-Feb-22	23-Feb-22	6	21-Apr-22	27-Apr-22	31	0%																				
	P30-BP31.20	BP - RCD Drilling	24-Feb-22	29-Mar-22	29	28-Apr-22	02-Jun-22	31	0%																				
06																													
	P30-BP33.10	BP - Excavation	11-Apr-22	20-Apr-22	27	22-Jan-22 A	25-Feb-22	108	0%																				
	P30-BP33.20	BP - RCD Drilling	21-Apr-22	10-May-22	15	26-Feb-22	15-Mar-22	108	0%																				
	P30-BP33.30	BP - Airlift, Cage Install and Concrete	11-May-22	18-May-22	7	16-Mar-22	23-Mar-22	206	0%																				
12																													
	P30-BP39.30	BP - Airlift, Cage Install and Concrete	20-Sep-22	27-Sep-22	9	11-Jan-22 A	21-Jan-22 A		100%																				
13																													
	P30-BP21.10	BP - Excavation	13-Sep-22	19-Sep-22	39	08-Jan-22 A	25-Feb-22	203	0%																				
	P30-BP21.20	BP - RCD Drilling	20-Sep-22	08-Oct-22	15	26-Feb-22	15-Mar-22	203	0%																				
	P30-BP21.30	BP - Airlift, Cage Install and Concrete	10-Oct-22	17-Oct-22	7	16-Mar-22	23-Mar-22	243	0%																				
TD01																													
03																													
	P30-BP03.10	BP - Excavation	10-Mar-22	16-Mar-22	6	19-Feb-22	25-Feb-22	31	0%																				
	P30-BP03.20	BP - RCD Drilling	17-Mar-22	02-Apr-22	15	26-Feb-22	15-Mar-22	31	0%																				
	P30-BP03.30	BP - Airlift, Cage Install and Concrete	04-Apr-22	12-Apr-22	7	16-Mar-22	23-Mar-22	84	0%																				
06																													
	P30-BP11.10	BP - Excavation	07-May-22	14-May-22	6	26-Mar-22	01-Apr-22	31	0%																				
	P30-BP11.20	BP - RCD Drilling	16-May-22	07-Jun-22	19	02-Apr-22	28-Apr-22	31	0%																				
	P30-BP11.30	BP - Airlift, Cage Install and Concrete	08-Jun-22	16-Jun-22	8	29-Apr-22	10-May-22	83	0%																				
TD09																													
02																													
	CBA-BPC52Va.10	BP - Excavation	23-Apr-22	29-Apr-22	6	23-Apr-22	29-Apr-22	0	0%																				
	CBA-BPC52Va.20	BP - RCD Drilling	30-Apr-22	13-May-22	10	30-Apr-22	13-May-22	0	0%																				
	CBA-BPC52Va.30	BP - Airlift, Cage Install and Concrete	14-May-22	19-May-22	5	14-May-22	19-May-22	148	0%																				
KD09 (Section 5)																													
Trial Piles (P23-BP68)																													
ID: 2B2C-20220218_w		 Planned Bar		 Milestone										 Critical Bar		 Critical MS					 Baseline		 Baseline MS						
Data Date: 19-Feb-22																													
Print Date: 21-Feb-22_11:53																													
Page 13 of 19																													
																				Date		Revision	Checked	Approved					
																				06-Aug-21		1st Draft	KL	N					
																				29-Sep-21		2nd Draft	KL	N					
																				25-Oct-21		3rd Draft	KL	C					
																				26-Nov-21		4th Draft	KL	B					

Activity ID	Activity Name	CMWP 4th Draft Start	CMWP 4th Draft Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	Activity	January	February	March	April	May
										01	02	03	04	05
										21	28	04	11	18
										25	04	11	18	25
										01	08	15	22	29
										06	13			
TD03														
01														
P23-BP68.10	BP (Trial Pile for Schedule 4) - Excavation	14-Dec-21	20-Dec-21	26	24-Jan-22 A	25-Feb-22	9	0%						
P23-BP68.20	BP (Trial Pile for Schedule 4) - RCD Drilling	21-Dec-21	26-Jan-22	29	26-Feb-22	31-Mar-22	9	0%						
P23-BP68.30	BP (Trial Pile for Schedule 4) - Airlift, Cage Install and Concrete	27-Jan-22	08-Feb-22	8	01-Apr-22	11-Apr-22	37	0%						
Bored Piles														
VD01														
01														
P23-BP44.10	BP - Excavation	05-Feb-22	11-Feb-22	66	01-Nov-21 A	20-Jan-22 A		100%						
P23-BP44.20	BP - RCD Drilling	12-Feb-22	05-Mar-22	41	21-Jan-22 A	12-Mar-22	28	0%						
P23-BP44.30	BP - Airlift, Cage Install and Concrete	07-Mar-22	15-Mar-22	8	14-Mar-22	22-Mar-22	190	0%						
CD01														
05														
P23-BP53.10	BP - Excavation	28-Jan-22	07-Feb-22	6	09-Mar-22	15-Mar-22	18	0%						
P23-BP53.20	BP - RCD Drilling	08-Feb-22	01-Mar-22	19	16-Mar-22	07-Apr-22	18	0%						
P23-BP53.30	BP - Airlift, Cage Install and Concrete	02-Mar-22	10-Mar-22	8	08-Apr-22	20-Apr-22	255	0%						
06														
P23-BP40.10	BP - Excavation	23-Feb-22	01-Mar-22	6	31-Mar-22	07-Apr-22	18	0%						
P23-BP40.20	BP - RCD Drilling	02-Mar-22	18-Mar-22	15	08-Apr-22	28-Apr-22	18	0%						
P23-BP40.30	BP - Airlift, Cage Install and Concrete	19-Mar-22	26-Mar-22	7	29-Apr-22	07-May-22	248	0%						
09														
P23-BP64.10	BP - Excavation	26-Apr-22	03-May-22	6	22-Apr-22	28-Apr-22	18	0%						
P23-BP64.20	BP - RCD Drilling	04-May-22	26-May-22	19	29-Apr-22	23-May-22	18	0%						
10														
P23-BP62.10	BP - Excavation	20-May-22	26-May-22	6	17-May-22	23-May-22	18	0%						
13														
P23-BP54.10	BP - Excavation	19-Jul-22	25-Jul-22	9	16-Feb-22 A	25-Feb-22	277	0%						
P23-BP54.20	BP - RCD Drilling	26-Jul-22	16-Aug-22	19	26-Feb-22	19-Mar-22	277	0%						
P23-BP54.30	BP - Airlift, Cage Install and Concrete	17-Aug-22	25-Aug-22	8	21-Mar-22	29-Mar-22	277	0%						
14														
P23-BP63.10	BP - Excavation	26-Apr-22	03-May-22	31	18-Jan-22 A	25-Feb-22	116	0%						
P23-BP63.20	BP - RCD Drilling	04-May-22	26-May-22	19	26-Feb-22	19-Mar-22	116	0%						
P23-BP63.30	BP - Airlift, Cage Install and Concrete	27-May-22	06-Jun-22	8	21-Mar-22	29-Mar-22	134	0%						
CD02														
02														
P23-BP37.10	BP - Excavation	21-Dec-21	29-Dec-21	6	19-Feb-22	25-Feb-22	3	0%						
P23-BP37.20	BP - RCD Drilling	30-Dec-21	05-Feb-22	29	26-Feb-22	31-Mar-22	3	0%						
P23-BP37.30	BP - Airlift, Cage Install and Concrete	07-Feb-22	15-Feb-22	8	01-Apr-22	11-Apr-22	227	0%						
ID: 2B2C-20220218_w Data Date: 19-Feb-22 Print Date: 21-Feb-22_11:53 Page 14 of 19										<div><div><div></div><div></div><div></div></div><div><div>Planned Bar</div><div>Critical Bar</div><div>Baseline</div></div><div><div></div><div></div><div></div></div><div><div>Milestone</div><div>Critical MS</div><div>Baseline MS</div></div></div> <div><div>West Kowloon Cultural District Authority</div><div>Piling for Integrated Basement and U/G Road in Zone 2B 2C</div><div>3 Month Rolling Programme as of 18 Feb 2022</div><div>Based on CMWP 4th Draft</div></div> <div><div>VIBRO</div><div></div></div>				

Activity ID	Activity Name	CMWP 4th Draft Start	CMWP 4th Draft Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete		January	February				March				April				May																										
											1	8	15	22	1	8	15	22	1	8	15	22	29	5	12																								
											21	28	04	11	18	25	04	11	18	25	01	08	15	22	29	06	13																						
03																																																	
P23-BP48.10	BP - Excavation	27-Jan-22	05-Feb-22	6	25-Mar-22	31-Mar-22	3	0%																																									
P23-BP48.20	BP - RCD Drilling	07-Feb-22	11-Mar-22	29	01-Apr-22	11-May-22	3	0%																																									
P23-BP48.30	BP - Airlift, Cage Install and Concrete	12-Mar-22	21-Mar-22	8	12-May-22	20-May-22	206	0%																																									
04																																																	
P23-BP39.10	BP - Excavation	05-Mar-22	11-Mar-22	6	04-May-22	11-May-22	3	0%																																									
P23-BP39.20	BP - RCD Drilling	12-Mar-22	02-Apr-22	19	12-May-22	02-Jun-22	3	0%																																									
08																																																	
P23-BP51.10	BP - Excavation	22-Jun-22	28-Jun-22	38	10-Jan-22 A	25-Feb-22	128	0%																																									
P23-BP51.20	BP - RCD Drilling	29-Jun-22	21-Jul-22	19	26-Feb-22	19-Mar-22	128	0%																																									
P23-BP51.30	BP - Airlift, Cage Install and Concrete	22-Jul-22	30-Jul-22	8	21-Mar-22	29-Mar-22	277	0%																																									
TD09																																																	
03																																																	
CBA-BPC52U.10	BP - Excavation	06-May-22	13-May-22	6	06-May-22	13-May-22	0	0%																																									
CBA-BPC52U.20	BP - RCD Drilling	14-May-22	25-May-22	10	14-May-22	25-May-22	0	0%																																									
TD07																																																	
02																																																	
P18-BP16.10	BP - Excavation	20-Dec-21	28-Dec-21	6	09-Mar-22	15-Mar-22	-26	0%																																									
P18-BP16.20	BP - RCD Drilling	29-Dec-21	15-Jan-22	15	16-Mar-22	01-Apr-22	-26	0%																																									
P18-BP16.30	BP - Airlift, Cage Install and Concrete	17-Jan-22	24-Jan-22	7	02-Apr-22	11-Apr-22	53	0%																																									
03																																																	
P18-BP23.10	BP - Excavation	10-Jan-22	15-Jan-22	6	26-Mar-22	01-Apr-22	-26	0%																																									
P18-BP23.20	BP - RCD Drilling	17-Jan-22	05-Feb-22	15	02-Apr-22	23-Apr-22	-26	0%																																									
P18-BP23.30	BP - Airlift, Cage Install and Concrete	07-Feb-22	14-Feb-22	7	25-Apr-22	03-May-22	45	0%																																									
04																																																	
P18-BP21.10	BP - Excavation	27-Jan-22	05-Feb-22	6	14-Apr-22	23-Apr-22	-26	0%																																									
P18-BP21.20	BP - RCD Drilling	07-Feb-22	23-Feb-22	15	25-Apr-22	13-May-22	-26	0%																																									
P18-BP21.30	BP - Airlift, Cage Install and Concrete	24-Feb-22	03-Mar-22	7	14-May-22	21-May-22	37	0%																																									
TD06																																																	
01																																																	
P18-BP36.10	BP - Excavation	20-Dec-21	28-Dec-21	6	19-Feb-22	25-Feb-22	28	0%																																									
P18-BP36.20	BP - RCD Drilling	29-Dec-21	15-Jan-22	15	26-Feb-22	15-Mar-22	28	0%																																									
P18-BP36.30	BP - Airlift, Cage Install and Concrete	17-Jan-22	24-Jan-22	7	16-Mar-22	23-Mar-22	170	0%																																									
02																																																	
P18-BP40.10	BP - Excavation	10-Jan-22	15-Jan-22	6	09-Mar-22	15-Mar-22	28	0%																																									
P18-BP40.20	BP - RCD Drilling	17-Jan-22	05-Feb-22	15	16-Mar-22	01-Apr-22	28	0%																																									
P18-BP40.30	BP - Airlift, Cage Install and Concrete	07-Feb-22	14-Feb-22	7	02-Apr-22	11-Apr-22	162	0%																																									
03																																																	
P18-BP38.10	BP - Excavation	27-Jan-22	05-Feb-22	6	26-Mar-22	01-Apr-22	28	0%																																									
ID: 2B2C-20220218_w Data Date: 19-Feb-22 Print Date: 21-Feb-22_11:53 Page 15 of 19										<div><div><div></div><div></div><div></div></div><div><div>Planned Bar</div><div>Critical Bar</div><div>Baseline</div></div><div><div></div><div></div><div></div></div><div><div>Milestone</div><div>Critical MS</div><div>Baseline MS</div></div></div> <div><div>West Kowloon Cultural District Authority</div><div>Piling for Integrated Basement and U/G Road in Zone 2B 2C</div><div>3 Month Rolling Programme as of 18 Feb 2022</div><div>Based on CMWP 4th Draft</div></div> <div><div>VIBRO</div><div></div><div></div></div> <table><tr><td>Date</td><td>Revision</td><td>Checked</td><td>Approved</td></tr><tr><td>06-Aug-21</td><td>1st Draft</td><td>KL</td><td>N</td></tr><tr><td>29-Sep-21</td><td>2nd Draft</td><td>KL</td><td>N</td></tr><tr><td>25-Oct-21</td><td>3rd Draft</td><td>KL</td><td>C</td></tr><tr><td>26-Nov-21</td><td>4th Draft</td><td>KL</td><td>B</td></tr></table>										Date	Revision	Checked	Approved	06-Aug-21	1st Draft	KL	N	29-Sep-21	2nd Draft	KL	N	25-Oct-21	3rd Draft	KL	C	26-Nov-21	4th Draft	KL	B										
Date	Revision	Checked	Approved																																														
06-Aug-21	1st Draft	KL	N																																														
29-Sep-21	2nd Draft	KL	N																																														
25-Oct-21	3rd Draft	KL	C																																														
26-Nov-21	4th Draft	KL	B																																														

[illegible]

[illegible]

Activity ID	Activity Name	CMWP 4th Draft Start	CMWP 4th Draft Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	Activity	February				March				April				May	
										21	28	04	11	18	25	04	11	18	25	01	08	15	22
04																							
P23-BP83.10	BP - Excavation	08-Apr-22	14-Apr-22	6	26-Apr-22	03-May-22	74	0%															
P23-BP83.20	BP - RCD Drilling	19-Apr-22	24-May-22	29	04-May-22	08-Jun-22	74	0%															
10																							
P23-BP94.10	BP - Excavation	26-Jan-22	04-Feb-22	31	18-Jan-22 A	25-Feb-22	17	0%															
P23-BP94.20	BP - RCD Drilling	05-Feb-22	10-Mar-22	29	26-Feb-22	31-Mar-22	17	0%															
P23-BP94.30	BP - Airlift, Cage Install and Concrete	11-Mar-22	19-Mar-22	8	01-Apr-22	11-Apr-22	187	0%															
11																							
P23-BP113.10	BP - Excavation	04-Mar-22	10-Mar-22	6	25-Mar-22	31-Mar-22	17	0%															
P23-BP113.20	BP - RCD Drilling	11-Mar-22	01-Apr-22	19	01-Apr-22	27-Apr-22	17	0%															
P23-BP113.30	BP - Airlift, Cage Install and Concrete	02-Apr-22	12-Apr-22	8	28-Apr-22	07-May-22	176	0%															
12																							
P23-BP111.10	BP - Excavation	26-Mar-22	01-Apr-22	6	21-Apr-22	27-Apr-22	17	0%															
P23-BP111.20	BP - RCD Drilling	02-Apr-22	28-Apr-22	19	28-Apr-22	21-May-22	17	0%															
13																							
P23-BP92.10	BP - Excavation	22-Apr-22	28-Apr-22	6	16-May-22	21-May-22	17	0%															
Optional Item no. 3																							
TD07																							
15																							
P18-BP18.10	BP (Optional Item no.3) - Excavation	28-Apr-22	05-May-22	6	28-Apr-22	05-May-22	32	0%															
P18-BP18.20	BP (Optional Item no.3) - RCD Drilling	06-May-22	24-May-22	15	06-May-22	24-May-22	32	0%															
TD06																							
17																							
P18-BP30.10	BP (Optional Item no.3) - Excavation	28-Apr-22	05-May-22	6	28-Apr-22	05-May-22	140	0%															
P18-BP30.20	BP (Optional Item no.3) - RCD Drilling	06-May-22	24-May-22	15	06-May-22	24-May-22	140	0%															
Socketed Steel H- Piles																							
Trial Pile																							
KD09.SSHP.0000	Test Installation of Pile (SHP-C52Xa-P6)	17-Jan-22	26-Jan-22	9	15-Feb-22 A	24-Feb-22	-3	44.44%															
KD09.SSHP.0020	Submission and Approval of Installation Report by BD	27-Jan-22	02-Feb-22	7	25-Feb-22	03-Mar-22	-3	0%															
Socketed Steel H- Pile Construction																							
SHP-BW-52Y1b-P'	Socketed Steel H-Piling	04-Feb-22	12-Feb-22	8	04-Mar-22	12-Mar-22	69	0%															
SHP-BW-52Y1b-P'	Socketed Steel H-Piling	08-Feb-22	16-Feb-22	8	08-Mar-22	16-Mar-22	69	0%															
SHP-C52W-P1	Socketed Steel H-Piling	11-Feb-22	19-Feb-22	8	11-Mar-22	19-Mar-22	69	0%															
SHP-C52W-P2	Socketed Steel H-Piling	15-Feb-22	23-Feb-22	8	15-Mar-22	23-Mar-22	69	0%															
SHP-C52W-P3	Socketed Steel H-Piling	18-Feb-22	26-Feb-22	8	18-Mar-22	26-Mar-22	69	0%															

ID: 2B2C-20220218_w
Data Date: 19-Feb-22
Print Date: 21-Feb-22_11:53
Page 18 of 19

Planned Bar

Critical Bar

Baseline

Milestone

Critical MS

Baseline MS

West Kowloon Cultural District Authority

Piling for Integrated Basement and U/G Road in Zone 2B 2C

3 Month Rolling Programme as of 18 Feb 2022

Based on CMWP 4th Draft

VIBRO

Date	Revision	Checked	Approved
06-Aug-21	1st Draft	KL	N
29-Sep-21	2nd Draft	KL	N
25-Oct-21	3rd Draft	KL	C
26-Nov-21	4th Draft	KL	B

Activity ID	Activity Name	CMWP 4th Draft Start	CMWP 4th Draft Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	Activity	January					February					March					April					May				
										1					2					3					4									
										21	28	04	11	18	25	04	11	18	25	01	08	15	22	29	06	13								
<div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div></div>	SHP-C52W-P4	Socketed Steel H-Piling	22-Feb-22	02-Mar-22	8	22-Mar-22	30-Mar-22	69	0%																									
	SHP-C52W-P5	Socketed Steel H-Piling	25-Feb-22	05-Mar-22	8	25-Mar-22	02-Apr-22	69	0%																									
	SHP-C52W-P6	Socketed Steel H-Piling	01-Mar-22	09-Mar-22	8	29-Mar-22	07-Apr-22	69	0%																									
	SHP-C52X-P1	Socketed Steel H-Piling	04-Mar-22	12-Mar-22	8	01-Apr-22	11-Apr-22	69	0%																									
	SHP-C52X-P2	Socketed Steel H-Piling	08-Mar-22	16-Mar-22	8	06-Apr-22	14-Apr-22	69	0%																									
	SHP-C52X-P3	Socketed Steel H-Piling	11-Mar-22	19-Mar-22	8	09-Apr-22	21-Apr-22	69	0%																									
	SHP-C52X-P4	Socketed Steel H-Piling	15-Mar-22	23-Mar-22	8	13-Apr-22	25-Apr-22	69	0%																									
	SHP-C52X-P5	Socketed Steel H-Piling	18-Mar-22	26-Mar-22	8	20-Apr-22	28-Apr-22	69	0%																									
	SHP-C52X-P6	Socketed Steel H-Piling	22-Mar-22	30-Mar-22	8	23-Apr-22	03-May-22	69	0%																									
	SHP-C52Xa-P1	Socketed Steel H-Piling	25-Mar-22	02-Apr-22	8	27-Apr-22	06-May-22	69	0%																									
	SHP-C52Xa-P2	Socketed Steel H-Piling	29-Mar-22	07-Apr-22	8	30-Apr-22	11-May-22	69	0%																									
	SHP-C52Xa-P3	Socketed Steel H-Piling	01-Apr-22	11-Apr-22	8	05-May-22	14-May-22	69	0%																									
	SHP-C52Xa-P4	Socketed Steel H-Piling	06-Apr-22	14-Apr-22	8	10-May-22	18-May-22	69	0%																									
	SHP-C52Xa-P5	Socketed Steel H-Piling	09-Apr-22	21-Apr-22	8	13-May-22	21-May-22	69	0%																									



Activity ID	Activity Name	CMWP Rev.0 Start	CMWP Rev.0 Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	March 1				April 2				May 3				June 4						
									25	04	11	18	25	01	08	15	22	29	06	13	20	27	03	10	17	4	
Piling for Integrated Basement and U/G Road in Zone 2B & 2C																											
Contract Dates																											
Key Dates																											
KD for Zone 2B																											
KD01	KD01 (Stage 1-1) - 300 days after Commencement (18 May 2022)		18-May-22	0		31-May-22*	-13	0%																			
KD for Zone 2C																											
KD02	KD02 (Stage 5-1) - 200 days after Commencement (7 Feb 2022)		06-Feb-22	0		17-Mar-22 A		100%																			
Optional Works subjected to CA's Instruction																											
CO3A	Last CAI date for Optional Works Item No.3 (within 280 Days after Commencement)	28-Apr-22		0	28-Apr-22		2	0%																			
Access Dates of Site Portion																											
120 days after Commencement																											
ACB10	Access to Site Portion B10	19-Nov-21		0	26-Mar-22		-65	0%																			
270 days after Commencement																											
ACB12	Access to Site Portion B12	18-Apr-22		0	18-Apr-22		29	0%																			
ACB35	Access to Site Portion B35 (To be agreed with the Zone 2A contractor)	18-Apr-22		0	18-Apr-22		29	0%																			
Mobilization Stage																											
Site Mobilization Works																											
Pre-Construction Works before Piling Commencement																											
MOBP.10.1260	Erection of Hoardings (Stage 2)	20-Dec-21	31-Jan-22	55	08-Jan-22 A	04-Mar-22 A		100%																			
MOBP.10.1300	Trial Pit for Drillholes & Removal of Existing Substructures / Ground Slab [503 nos]	19-Aug-21	30-Apr-22	255	19-Aug-21 A	30-Apr-22	137	82%																			
									</																		

Activity ID	Activity Name	CMWP Rev.0 Start	CMWP Rev.0 Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	March					April				May				June																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																		
									1					2				3				4																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																		
									25	04	11	18	25	01	08	15	22	29	06	13	20	27	03	10	17	4																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																														
Construction Stage																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																								</








Activity ID	Activity Name	CMWP Rev.0 Start	CMWP Rev.0 Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	March 1				April 2				May 3				June 4									
									25	04	11	18	25	01	08	15	22	29	06	13	20	27	03	10	17	4				
07																														
P22&P19-BP29.20	BP - RCD Drilling	12-Apr-22	07-May-22	5	21-Feb-22 A	26-Feb-22 A		100%																						
P22&P19-BP29.30	BP - Airlift, Cage Install and Concrete	10-May-22	18-May-22	12	28-Feb-22 A	14-Mar-22 A		100%																						
CD03																														
06																														
P23-BP06.30	BP - Airlift, Cage Install and Concrete	07-May-22	17-May-22	10	17-Feb-22 A	01-Mar-22 A		100%																						
KD02 (Stage 5-1)																														
Bored Piles																														
TD04																														
01																														
P23-BP76.30	BP - Airlift, Cage Install and Concrete	31-Dec-21	10-Jan-22	23	18-Feb-22 A	17-Mar-22 A		100%																						
02																														
P23-BP87.30	BP - Airlift, Cage Install and Concrete	11-Jan-22	19-Jan-22	11	18-Feb-22 A	03-Mar-22 A		100%																						
03																														
P23-BP117.10	BP - Excavation	03-Dec-21	09-Dec-21	68	10-Jan-22 A	01-Apr-22	31	0%																						
P23-BP117.20	BP - RCD Drilling	10-Dec-21	10-Jan-22	24	02-Apr-22	05-May-22	31	0%																						
P23-BP117.30	BP - Airlift, Cage Install and Concrete	20-Jan-22	28-Jan-22	8	06-May-22	16-May-22	194	0%																						
KD03 (Stage 3-1)																														
KD03.BP.0040	Review and Confirmation of Rockhead and Founding Level of Pile by CA	14-Nov-21	27-Nov-21	14	26-Mar-22	08-Apr-22	-59	0%																						
Bored Piles																														
VD02																														
03																														
P28&29-BP08.10	BP - Excavation	18-Mar-22	24-Mar-22	6	05-May-22	12-May-22	1	0%																						
P28&29-BP08.20	BP - RCD Drilling	25-Mar-22	12-Apr-22	15	13-May-22	30-May-22	1	0%																						
P28&29-BP08.30	BP - Airlift, Cage Install and Concrete	13-Apr-22	23-Apr-22	7	31-May-22	08-Jun-22	67	0%																						
VD06																														
01																														
P28&29-BP29.10	BP - Excavation	19-Jan-22	25-Jan-22	6	26-Mar-22	01-Apr-22	-45	0%																						
P28&29-BP29.20	BP - RCD Drilling	26-Jan-22	15-Feb-22	15	09-Apr-22	29-Apr-22	-50	0%																						
P28&29-BP29.30	BP - Airlift, Cage Install and Concrete	16-Feb-22	23-Feb-22	7	30-Apr-22	10-May-22	21	0%																						
VD09																														
01																														
CBA-BPC54Jb.10	BP - Excavation	26-Feb-22	04-Mar-22	6	09-Apr-22	19-Apr-22	-35	0%																						
CBA-BPC54Jb.20	BP - RCD Drilling	05-Mar-22	11-Apr-22	31	20-Apr-22	27-May-22	-35	0%																						
CBA-BPC54Jb.30	BP - Airlift, Cage Install and Concrete	12-Apr-22	21-Apr-22	6	28-May-22	04-Jun-22	64	0%																						
02																														
ID: 2B2C-20220325_bw Data Date: 26-Mar-22 Print Date: 28-Mar-22_12:40 Page 3 of 22									<div><div><div>Planned Bar</div><div>Critical Bar</div><div>Baseline</div></div><div><div>Milestone</div><div>Critical MS</div><div>Baseline MS</div></div></div>									<div>West Kowloon Cultural District Authority</div> <div>Piling for Integrated Basement and U/G Road in Zone 2B 2C</div> <div>3 Month Rolling Programme as of 25 Mar 2022</div> <div>Based on CMWP Rev.0</div>									<div><div>Date</div><div>Revision</div><div>Checked</div><div>Approved</div></div> <div><div>01-Mar-22</div><div>Rev.0</div><div>KL</div><div>B</div></div>			

Activity ID	Activity Name	CMWP Rev.0 Start	CMWP Rev.0 Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	March 1				April 2				May 3				June 4						
									25	04	11	18	25	01	08	15	22	29	06	13	20	27	03	10	17	4	
CBA-BPC54Ka.10	BP - Excavation	04-Apr-22	11-Apr-22	6	04-Jun-22	10-Jun-22	-46	0%																			
CBA-BPC54Ka.20	BP - RCD Drilling	12-Apr-22	25-May-22	33	11-Jun-22	20-Jul-22	-46	0%																			
KD04 (Stage 4-1)																											
KD04.BP.0040	Review and Confirmation of Rockhead and Founding Level of Pile by CA	03-Nov-21	16-Nov-21	150	30-Oct-21 A	28-Mar-22	10	78.57%																			
Bored Piles																											
TD01																											
07																											
P30-BP06.10	BP - Excavation	31-May-22	07-Jun-22	6	28-May-22	04-Jun-22	17	0%																			
P30-BP06.20	BP - RCD Drilling	08-Jun-22	29-Jun-22	19	06-Jun-22	27-Jun-22	17	0%																			
TD09																											
01																											
CBA-BPC54V.10	BP - Excavation	08-Apr-22	14-Apr-22	6	08-Apr-22	14-Apr-22	0	0%																			
CBA-BPC54V.20	BP - RCD Drilling	19-Apr-22	29-Apr-22	10	19-Apr-22	29-Apr-22	0	0%																			
CBA-BPC54V.30	BP - Airlift, Cage Install and Concrete	30-Apr-22	06-May-22	5	30-Apr-22	06-May-22	93	0%																			
KD05 (Section 1)																											
Bored Piles																											
CD01																											
03																											
P23-BP20.10	BP - Excavation	11-Jan-22	17-Jan-22	6	26-Mar-22	01-Apr-22	3	0%																			
P23-BP20.20	BP - RCD Drilling	18-Jan-22	07-Feb-22	15	02-Apr-22	23-Apr-22	3	0%																			
P23-BP20.30	BP - Airlift, Cage Install and Concrete	08-Feb-22	15-Feb-22	7	25-Apr-22	03-May-22	124	0%																			
07																											
P23-BP19.20	BP - RCD Drilling	19-Mar-22	11-Apr-22	9	17-Feb-22 A	28-Feb-22 A		100%																			
P23-BP19.30	BP - Airlift, Cage Install and Concrete	12-Apr-22	23-Apr-22	16	01-Mar-22 A	19-Mar-22 A		100%																			
12																											
P23-BP21.10	BP - Excavation	30-Jun-22	07-Jul-22	13	03-Mar-22 A	18-Mar-22 A		100%																			
P23-BP21.20	BP - RCD Drilling	08-Jul-22	25-Jul-22	21	19-Mar-22 A	13-Apr-22	130	0%																			
P23-BP21.30	BP - Airlift, Cage Install and Concrete	26-Jul-22	02-Aug-22	7	14-Apr-22	25-Apr-22	130	0%																			
CD07																											
02																											
CBA-BPC43K.10	BP - Excavation	31-Jan-22	09-Feb-22	6	26-Mar-22	01-Apr-22	-11	0%																			
CBA-BPC43K.20	BP - RCD Drilling	10-Feb-22	21-Feb-22	10	02-Apr-22	14-Apr-22	-11	0%																			
CBA-BPC43K.30	BP - Airlift, Cage Install and Concrete	22-Feb-22	26-Feb-22	5	19-Apr-22	23-Apr-22	121	0%																			
03																											
CBA-BPC44Jb.30	BP - Airlift, Cage Install and Concrete	10-Mar-22	16-Mar-22	10	22-Feb-22 A	05-Mar-22 A		100%																			
04																											
ID: 2B2C-20220325_bw Data Date: 26-Mar-22 Print Date: 28-Mar-22_12:40 Page 4 of 22		<div><div></div>Planned Bar</div> <div><div></div>Critical Bar</div> <div><div></div>Baseline</div>			<div><div></div>Milestone</div> <div><div></div>Critical MS</div> <div><div></div>Baseline MS</div>			West Kowloon Cultural District Authority Piling for Integrated Basement and U/G Road in Zone 2B 2C 3 Month Rolling Programme as of 25 Mar 2022 Based on CMWP Rev.0							<div>VIBRO</div> <div></div> <div></div>			Date 01-Mar-22		Revision Rev.0		Checked KL		Approved B			

Activity ID	Activity Name	CMWP Rev.0 Start	CMWP Rev.0 Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	March				April				May				June							
									1				2				3				4							
									25	04	11	18	25	01	08	15	22	29	06	13	20	27	03	10	17	24		
	CBA-BPC40Ja.10	BP - Excavation	03-Mar-22	09-Mar-22	6	08-Apr-22	14-Apr-22	-11	0%																			
	CBA-BPC40Ja.20	BP - RCD Drilling	10-Mar-22	21-Mar-22	10	19-Apr-22	29-Apr-22	-11	0%																			
	CBA-BPC40Ja.30	BP - Airlift, Cage Install and Concrete	22-Mar-22	26-Mar-22	5	30-Apr-22	06-May-22	116	0%																			
	05																											
	CBA-BPC42K.10	BP - Excavation	15-Mar-22	21-Mar-22	6	23-Apr-22	29-Apr-22	-11	0%																			
	CBA-BPC42K.20	BP - RCD Drilling	22-Mar-22	01-Apr-22	10	30-Apr-22	13-May-22	-11	0%																			
	CBA-BPC42K.30	BP - Airlift, Cage Install and Concrete	02-Apr-22	08-Apr-22	5	14-May-22	19-May-22	111	0%																			
	06																											
	CBA-BPC44K.10	BP - Excavation	25-Mar-22	01-Apr-22	24	07-Mar-22 A	02-Apr-22	-1	0%																			
	CBA-BPC44K.20	BP - RCD Drilling	02-Apr-22	22-Apr-22	14	04-Apr-22	23-Apr-22	-1	0%																			
	CBA-BPC44K.30	BP - Airlift, Cage Install and Concrete	23-Apr-22	29-Apr-22	6	25-Apr-22	30-Apr-22	125	0%																			
	08																											
	CBA-BPC43J.10	BP - Excavation	28-Apr-22	05-May-22	6	19-May-22	25-May-22	57	0%																			
	CBA-BPC43J.20	BP - RCD Drilling	06-May-22	18-May-22	10	26-May-22	07-Jun-22	57	0%																			
	CBA-BPC43J.30	BP - Airlift, Cage Install and Concrete	19-May-22	24-May-22	5	08-Jun-22	13-Jun-22	80	0%																			
	09																											
	CBA-BP02.10	BP - Excavation	11-May-22	18-May-22	7	30-May-22	07-Jun-22	57	0%																			
	CBA-BP02.20	BP - RCD Drilling	19-May-22	04-Jun-22	14	08-Jun-22	23-Jun-22	57	0%																			
	CBA-BP02.30	BP - Airlift, Cage Install and Concrete	06-Jun-22	11-Jun-22	6	24-Jun-22	30-Jun-22	71	0%																			
	10																											
	CBA-BP05.10	BP - Excavation	28-May-22	04-Jun-22	6	17-Jun-22	23-Jun-22	57	0%																			
	CBA-BP05.20	BP - RCD Drilling	06-Jun-22	16-Jun-22	10	24-Jun-22	06-Jul-22	57	0%																			
	11																											
	CBA-BPC40Ka.10	BP - Excavation	10-Jun-22	16-Jun-22	15	16-Mar-22 A	01-Apr-22	131	0%																			
	CBA-BPC40Ka.20	BP - RCD Drilling	17-Jun-22	28-Jun-22	10	02-Apr-22	14-Apr-22	131	0%																			
	CBA-BPC40Ka.30	BP - Airlift, Cage Install and Concrete	29-Jun-22	05-Jul-22	5	19-Apr-22	23-Apr-22	131	0%																			
	13																											
	CBA-BP01.10	BP - Excavation	25-Mar-22	01-Apr-22	7	26-Mar-22	02-Apr-22	-1	0%																			
	CBA-BP01.20	BP - RCD Drilling	02-Apr-22	22-Apr-22	14	04-Apr-22	23-Apr-22	-1	0%																			
	CBA-BP01.30	BP - Airlift, Cage Install and Concrete	23-Apr-22	29-Apr-22	6	25-Apr-22	30-Apr-22	7	0%																			
15																												
CBA-BP06.10	BP - Excavation	04-May-22	11-May-22	6	05-May-22	12-May-22	87	0%																				
CBA-BP06.20	BP - RCD Drilling	12-May-22	23-May-22	10	13-May-22	24-May-22	87	0%																				
CBA-BP06.30	BP - Airlift, Cage Install and Concrete	24-May-22	28-May-22	5	25-May-22	30-May-22	96	0%																				
16																												
CBA-BP03.10	BP - Excavation	16-May-22	23-May-22	7	17-May-22	24-May-22	87	0%																				
CBA-BP03.20	BP - RCD Drilling	24-May-22	09-Jun-22	14	25-May-22	10-Jun-22	87	0%																				
CBA-BP03.30	BP - Airlift, Cage Install and Concrete	10-Jun-22	16-Jun-22	6	11-Jun-22	17-Jun-22	87	0%																				

Activity ID	Activity Name	CMWP Rev.0 Start	CMWP Rev.0 Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	March				April				May				June												
									1				2				3				4												
									25	04	11	18	25	01	08	15	22	29	06	13	20	27	03	10	17	4							
CD05																																	
03																																	
P17-BP05.10	BP - Excavation	06-Jan-22	12-Jan-22	6	26-Mar-22	01-Apr-22	-8	0%																									
P17-BP05.20	BP - RCD Drilling	13-Jan-22	29-Jan-22	15	02-Apr-22	23-Apr-22	-8	0%																									
P17-BP05.30	BP - Airlift, Cage Install and Concrete	31-Jan-22	10-Feb-22	7	25-Apr-22	03-May-22	4	0%																									
06																																	
P22&P19-BP15.10	BP - Excavation	12-Mar-22	18-Mar-22	6	12-May-22	18-May-22	32	0%																									
P22&P19-BP15.20	BP - RCD Drilling	19-Mar-22	11-Apr-22	19	19-May-22	10-Jun-22	32	0%																									
P22&P19-BP15.30	BP - Airlift, Cage Install and Concrete	12-Apr-22	23-Apr-22	8	11-Jun-22	20-Jun-22	85	0%																									
08																																	
P17-BP01.10	BP - Excavation	30-Apr-22	07-May-22	6	04-Jun-22	10-Jun-22	32	0%																									
P17-BP01.20	BP - RCD Drilling	10-May-22	26-May-22	15	11-Jun-22	28-Jun-22	32	0%																									
09																																	
P17-BP09.10	BP - Excavation	20-May-22	26-May-22	6	22-Jun-22	28-Jun-22	32	0%																									
11																																	
P22&P19-BP26.10	BP - Excavation	06-Jan-22	12-Jan-22	6	26-Mar-22	01-Apr-22	33	0%																									
P22&P19-BP26.20	BP - RCD Drilling	13-Jan-22	18-Feb-22	29	02-Apr-22	12-May-22	33	0%																									
P22&P19-BP26.30	BP - Airlift, Cage Install and Concrete	19-Feb-22	28-Feb-22	8	13-May-22	21-May-22	77	0%																									
13																																	
P22&P19-BP25.10	BP - Excavation	07-Mar-22	12-Mar-22	6	28-May-22	04-Jun-22	33	0%																									
P22&P19-BP25.20	BP - RCD Drilling	14-Mar-22	04-Apr-22	19	06-Jun-22	27-Jun-22	33	0%																									
14																																	
P22&P19-BP10.10	BP - Excavation	29-Mar-22	04-Apr-22	6	21-Jun-22	27-Jun-22	33	0%																									
CD04																																	
01																																	
P17-BP03.10	BP - Excavation	24-Nov-21	30-Nov-21	6	26-Mar-22	01-Apr-22	-30	0%																									
P17-BP03.20	BP - RCD Drilling	01-Dec-21	17-Dec-21	15	02-Apr-22	23-Apr-22	-30	0%																									
P17-BP03.30	BP - Airlift, Cage Install and Concrete	18-Dec-21	28-Dec-21	7	25-Apr-22	03-May-22	53	0%																									
02																																	
P17-BP12.10	BP - Excavation	20-Dec-21	28-Dec-21	6	14-Apr-22	23-Apr-22	-30	0%																									
P17-BP12.20	BP - RCD Drilling	29-Dec-21	15-Jan-22	15	25-Apr-22	13-May-22	-30	0%																									
P17-BP12.30	BP - Airlift, Cage Install and Concrete	17-Jan-22	24-Jan-22	7	14-May-22	21-May-22	45	0%																									
03																																	
P17-BP10.10	BP - Excavation	10-Jan-22	15-Jan-22	6	06-May-22	13-May-22	-30	0%																									
P17-BP10.20	BP - RCD Drilling	17-Jan-22	05-Feb-22	15	14-May-22	31-May-22	-30	0%																									
P17-BP10.30	BP - Airlift, Cage Install and Concrete	07-Feb-22	14-Feb-22	7	01-Jun-22	09-Jun-22	37	0%																									
04																																	
P17-BP14.10	BP - Excavation	27-Jan-22	05-Feb-22	6	25-May-22	31-May-22	-30	0%																									
P17-BP14.20	BP - RCD Drilling	07-Feb-22	28-Feb-22	19	01-Jun-22	23-Jun-22	-30	0%																									
ID: 2B2C-20220325_bw																																	
Data Date: 26-Mar-22																																	
Print Date: 28-Mar-22_12:40																																	
Page 6 of 22																																	
<div><div><div></div><div>Planned Bar</div></div><div><div></div><div>Critical Bar</div></div><div><div></div><div>Baseline</div></div><div><div></div><div>Milestone</div></div><div><div></div><div>Critical MS</div></div><div><div></div><div>Baseline MS</div></div></div>										<div>West Kowloon Cultural District Authority</div> <div>Piling for Integrated Basement and U/G Road in Zone 2B 2C</div> <div>3 Month Rolling Programme as of 25 Mar 2022</div> <div>Based on CMWP Rev.0</div>										<div><div>VIBRO</div><div><div></div><div></div><div></div></div></div>										<div><div>Date</div><div>Revision</div><div>Checked</div><div>Approved</div></div> <div><div>01-Mar-22</div><div>Rev.0</div><div>KL</div><div>B</div></div>			

Activity ID	Activity Name	CMWP Rev.0 Start	CMWP Rev.0 Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	March				April				May				June							
									1				2				3				4							
									25	04	11	18	25	01	08	15	22	29	06	13	20	27	03	10	17	4		
<div></div>	P17-BP14.30	BP - Airlift, Cage Install and Concrete	01-Mar-22	09-Mar-22	8	24-Jun-22	04-Jul-22	25	0%	<div></div>																		
	05									<div></div>																		
	P17-BP16.10	BP - Excavation	22-Feb-22	28-Feb-22	6	17-Jun-22	23-Jun-22	-30	0%	<div></div>																		
	P17-BP16.20	BP - RCD Drilling	01-Mar-22	17-Mar-22	15	24-Jun-22	12-Jul-22	-30	0%	<div></div>																		
	14									<div></div>																		
	P17-BP17.10	BP - Excavation	09-Jun-22	15-Jun-22	6	09-Jun-22	15-Jun-22	0	0%	<div></div>																		
	P17-BP17.20	BP - RCD Drilling	16-Jun-22	04-Jul-22	15	16-Jun-22	04-Jul-22	0	0%	<div></div>																		
	TD08									<div></div>																		
	02									<div></div>																		
	CBA-BPC38Ja.10	BP - Excavation	01-Dec-21	07-Dec-21	38	21-Jan-22 A	10-Mar-22 A		100%	<div></div>																		
	CBA-BPC38Ja.20	BP - RCD Drilling	08-Dec-21	18-Dec-21	3	11-Mar-22 A	15-Mar-22 A		100%	<div></div>																		
	CBA-BPC38Ja.30	BP - Airlift, Cage Install and Concrete	20-Dec-21	24-Dec-21	7	16-Mar-22 A	24-Mar-22 A		100%	<div></div>																		
	03									<div></div>																		
	CBA-BPC38K.30	BP - Airlift, Cage Install and Concrete	04-Jan-22	08-Jan-22	20	17-Feb-22 A	12-Mar-22 A		100%	<div></div>																		
	04									<div></div>																		
	CBA-BPC40M.10	BP - Excavation	24-Dec-21	03-Jan-22	17	14-Mar-22 A	01-Apr-22	101	0%	<div></div>																		
	CBA-BPC40M.20	BP - RCD Drilling	04-Jan-22	14-Jan-22	10	02-Apr-22	14-Apr-22	101	0%	<div></div>																		
	CBA-BPC40M.30	BP - Airlift, Cage Install and Concrete	15-Jan-22	20-Jan-22	5	19-Apr-22	23-Apr-22	116	0%	<div></div>																		
	05									<div></div>																		
	CBA-BPC40O.10	BP - Excavation	08-Jan-22	14-Jan-22	6	08-Apr-22	14-Apr-22	101	0%	<div></div>																		
	CBA-BPC40O.20	BP - RCD Drilling	15-Jan-22	26-Jan-22	10	19-Apr-22	29-Apr-22	101	0%	<div></div>																		
	CBA-BPC40O.30	BP - Airlift, Cage Install and Concrete	27-Jan-22	04-Feb-22	5	30-Apr-22	06-May-22	111	0%	<div></div>																		
	06									<div></div>																		
	CBA-BPC39Jb.10	BP - Excavation	20-Jan-22	26-Jan-22	6	23-Apr-22	29-Apr-22	101	0%	<div></div>																		
	CBA-BPC39Jb.20	BP - RCD Drilling	27-Jan-22	10-Feb-22	10	30-Apr-22	13-May-22	101	0%	<div></div>																		
	CBA-BPC39Jb.30	BP - Airlift, Cage Install and Concrete	11-Feb-22	16-Feb-22	5	14-May-22	19-May-22	106	0%	<div></div>																		
	07									<div></div>																		
	CBA-BPC38Jb.10	BP - Excavation	04-Feb-22	10-Feb-22	6	06-May-22	13-May-22	101	0%	<div></div>																		
	CBA-BPC38Jb.20	BP - RCD Drilling	11-Feb-22	22-Feb-22	10	14-May-22	25-May-22	101	0%	<div></div>																		
	CBA-BPC38Jb.30	BP - Airlift, Cage Install and Concrete	23-Feb-22	28-Feb-22	5	26-May-22	31-May-22	101	0%	<div></div>																		
	08									<div></div>																		
	CBA-BPC38Ka.10	BP - Excavation	16-Feb-22	22-Feb-22	7	25-Mar-22 A	01-Apr-22	131	0%	<div></div>																		
	CBA-BPC38Ka.20	BP - RCD Drilling	23-Feb-22	05-Mar-22	10	02-Apr-22	14-Apr-22	131	0%	<div></div>																		
CBA-BPC38Ka.30	BP - Airlift, Cage Install and Concrete	07-Mar-22	11-Mar-22	5	19-Apr-22	23-Apr-22	131	0%	<div></div>																			
09									<div></div>																			
CBA-BPC40K.10	BP - Excavation	28-Feb-22	05-Mar-22	18	26-Feb-22 A	19-Mar-22 A		100%	<div></div>																			
CBA-BPC40K.20	BP - RCD Drilling	07-Mar-22	17-Mar-22	15	21-Mar-22 A	07-Apr-22	137	0%	<div></div>																			
CBA-BPC40K.30	BP - Airlift, Cage Install and Concrete	18-Mar-22	23-Mar-22	5	08-Apr-22	13-Apr-22	137	0%	<div></div>																			
11									<div></div>																			
ID: 2B2C-20220325_bw Data Date: 26-Mar-22 Print Date: 28-Mar-22_12:40 Page 7 of 22		<div></div> Planned Bar <div></div> Critical Bar <div></div> Baseline <div></div> Milestone <div></div> Critical MS <div></div> Baseline MS				West Kowloon Cultural District Authority Piling for Integrated Basement and U/G Road in Zone 2B 2C 3 Month Rolling Programme as of 25 Mar 2022 Based on CMWP Rev.0				<div></div> <div></div> <div></div>				Date 01-Mar-22		Revision Rev.0		Checked KL		Approved B								

ID: 2B2C-20220325_bw Data Date: 26-Mar-22 Print Date: 28-Mar-22_12:40 Page 8 of 22	 Planned Bar  Critical Bar  Baseline  Milestone  Critical MS  Baseline MS	<p align="center"> West Kowloon Cultural District Authority Piling for Integrated Basement and U/G Road in Zone 2B 2C 3 Month Rolling Programme as of 25 Mar 2022 Based on CMWP Rev.0 </p>		Date	Revision	Checked	Approved
				01-Mar-22	Rev.0	KL	B

[illegible]

Activity ID	Activity Name	CMWP Rev.0 Start	CMWP Rev.0 Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	March				April				May				June																
									1				2				3				4																
									25	04	11	18	25	01	08	15	22	29	06	13	20	27	03	10	17	4											
	CBA-BPC45K.10	BP - Excavation	14-Nov-22	21-Nov-22	10	22-Feb-22 A	05-Mar-22 A		100%																												
	CBA-BPC45K.20	BP - RCD Drilling	22-Nov-22	07-Dec-22	3	07-Mar-22 A	10-Mar-22 A		100%																												
	CBA-BPC45K.30	BP - Airlift, Cage Install and Concrete	08-Dec-22	14-Dec-22	12	11-Mar-22 A	25-Mar-22 A		100%																												
CD06																																					
01																																					
	P24&27-BP30.10	BP - Excavation	28-Dec-21	04-Jan-22	6	26-Mar-22	01-Apr-22	-53	0%																												
	P24&27-BP30.20	BP - RCD Drilling	05-Jan-22	21-Jan-22	15	02-Apr-22	23-Apr-22	-53	0%																												
	P24&27-BP30.30	BP - Airlift, Cage Install and Concrete	22-Jan-22	29-Jan-22	7	25-Apr-22	03-May-22	116	0%																												
02																																					
	P22&P19-BP22.10	BP - Excavation	15-Jan-22	21-Jan-22	6	14-Apr-22	23-Apr-22	-53	0%																												
	P22&P19-BP22.20	BP - RCD Drilling	22-Jan-22	16-Feb-22	19	25-Apr-22	18-May-22	-53	0%																												
	P22&P19-BP22.30	BP - Airlift, Cage Install and Concrete	17-Feb-22	25-Feb-22	8	19-May-22	27-May-22	104	0%																												
03																																					
	P22&P19-BP23.10	BP - Excavation	10-Feb-22	16-Feb-22	6	12-May-22	18-May-22	-53	0%																												
	P22&P19-BP23.20	BP - RCD Drilling	17-Feb-22	10-Mar-22	19	19-May-22	10-Jun-22	-53	0%																												
	P22&P19-BP23.30	BP - Airlift, Cage Install and Concrete	11-Mar-22	19-Mar-22	8	11-Jun-22	20-Jun-22	93	0%																												
04																																					
	P22&P19-BP28.10	BP - Excavation	04-Mar-22	10-Mar-22	6	04-Jun-22	10-Jun-22	-53	0%																												
	P22&P19-BP28.20	BP - RCD Drilling	11-Mar-22	01-Apr-22	19	11-Jun-22	04-Jul-22	-53	0%																												
CD05																																					
12																																					
	P22&P19-BP24.10	BP - Excavation	12-Feb-22	18-Feb-22	6	05-May-22	12-May-22	33	0%																												
	P22&P19-BP24.20	BP - RCD Drilling	19-Feb-22	12-Mar-22	19	13-May-22	04-Jun-22	33	0%																												
	P22&P19-BP24.30	BP - Airlift, Cage Install and Concrete	14-Mar-22	22-Mar-22	8	06-Jun-22	14-Jun-22	66	0%																												
16																																					
	P22&P19-BP09.10	BP - Excavation	19-May-22	25-May-22	20	10-Mar-22 A	01-Apr-22	247	0%																												
	P22&P19-BP09.20	BP - RCD Drilling	26-May-22	17-Jun-22	19	02-Apr-22	28-Apr-22	247	0%																												
	P22&P19-BP09.30	BP - Airlift, Cage Install and Concrete	18-Jun-22	27-Jun-22	8	29-Apr-22	10-May-22	247	0%																												
17																																					
	P22&P19-BP03.10	BP - Excavation	11-Jun-22	17-Jun-22	11	28-Feb-22 A	12-Mar-22 A		100%																												
	P22&P19-BP03.20	BP - RCD Drilling	18-Jun-22	11-Jul-22	8	14-Mar-22 A	23-Mar-22 A		100%																												
	P22&P19-BP03.30	BP - Airlift, Cage Install and Concrete	12-Jul-22	20-Jul-22	10	24-Mar-22 A	04-Apr-22	272	0%																												
CD03																																					
02																																					
	P23-BP10.10	BP - Excavation	16-Dec-21	22-Dec-21	18	23-Feb-22 A	16-Mar-22 A		100%																												
	P23-BP10.20	BP - RCD Drilling	23-Dec-21	17-Jan-22	27	17-Mar-22 A	21-Apr-22	52	0%																												
	P23-BP10.30	BP - Airlift, Cage Install and Concrete	18-Jan-22	26-Jan-22	8	22-Apr-22	30-Apr-22	237	0%																												
03																																					
	P23-BP25.10	BP - Excavation	11-Jan-22	17-Jan-22	6	12-Apr-22	21-Apr-22	52	0%																												
ID: 2B2C-20220325_bw Data Date: 26-Mar-22 Print Date: 28-Mar-22_12:40 Page 10 of 22										<div><div><div></div><div></div><div></div></div><div><div>Planned Bar</div><div>Critical Bar</div><div>Baseline</div></div><div><div></div><div></div><div></div></div><div><div>Milestone</div><div>Critical MS</div><div>Baseline MS</div></div></div> <div><div>West Kowloon Cultural District Authority</div><div>Piling for Integrated Basement and U/G Road in Zone 2B 2C</div><div>3 Month Rolling Programme as of 25 Mar 2022</div><div>Based on CMWP Rev.0</div></div> <div><div>VIBRO</div><div></div><div></div></div> <table><tr><td>Date</td><td>Revision</td><td>Checked</td><td>Approved</td></tr><tr><td>01-Mar-22</td><td>Rev.0</td><td>KL</td><td>B</td></tr></table>										Date	Revision	Checked	Approved	01-Mar-22	Rev.0	KL	B										
Date	Revision	Checked	Approved																																		
01-Mar-22	Rev.0	KL	B																																		

Activity ID		Activity Name	CMWP Rev.0 Start	CMWP Rev.0 Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete
P23-BP25.20	BP - RCD Drilling	18-Jan-22	11-Feb-22	19	22-Apr-22	16-May-22	52	0%	
P23-BP25.30	BP - Airlift, Cage Install and Concrete	12-Feb-22	21-Feb-22	8	17-May-22	25-May-22	226	0%	
KD07 (Section 3)									
Trial Pile (P30-BP76)									
VD03									
01									
P30-BP76.10	BP (Trial Pile for Schedule 1) - Excavation	29-Dec-21	05-Jan-22	53	17-Jan-22 A	23-Mar-22 A	-	100%	
P30-BP76.20	BP (Trial Pile for Schedule 1) - RCD Drilling	06-Jan-22	01-Mar-22	46	24-Mar-22 A	23-May-22	-46	0%	
P30-BP76.30	BP (Trial Pile for Schedule 1) - Airlift, Cage Install and Concrete	02-Mar-22	11-Mar-22	9	24-May-22	02-Jun-22	-46	0%	
Trial Pile (P24&P27-BP34)									
VD02									
01									
P24&27-BP34.10	BP (Trial Pile for Schedule 2) - Excavation	18-Jan-22	24-Jan-22	36	19-Jan-22 A	05-Mar-22 A	-	100%	
P24&27-BP34.20	BP (Trial Pile for Schedule 2) - RCD Drilling	25-Jan-22	18-Feb-22	10	07-Mar-22 A	18-Mar-22 A	-	100%	
P24&27-BP34.30	BP (Trial Pile for Schedule 2) - Airlift, Cage Install and Concrete	19-Feb-22	28-Feb-22	14	19-Mar-22 A	04-Apr-22	-17	0%	
Bored Piles									
VD01									
03									
P26-BP08.20	BP - RCD Drilling	24-Mar-22	19-Apr-22	53	14-Jan-22 A	21-Mar-22 A	-	100%	
P26-BP08.30	BP - Airlift, Cage Install and Concrete	20-Apr-22	28-Apr-22	19	14-Mar-22 A	04-Apr-22	248	0%	
05									
P26-BP11.10	BP - Excavation	19-May-22	25-May-22	6	05-May-22	12-May-22	45	0%	
P26-BP11.20	BP - RCD Drilling	26-May-22	17-Jun-22	19	13-May-22	04-Jun-22	45	0%	
P26-BP11.30	BP - Airlift, Cage Install and Concrete	18-Jun-22	27-Jun-22	8	06-Jun-22	14-Jun-22	310	0%	
08									
P26-BP06.10	BP - Excavation	22-Jul-22	28-Jul-22	6	21-Jun-22	27-Jun-22	45	0%	
VD02									

ID: 2B2C-20220325_bw
Data Date: 26-Mar-22
Print Date: 28-Mar-22_12:40
Page 11 of 22

Planned Bar

Critical Bar

Baseline

Milestone

Critical MS

Baseline MS

West Kowloon Cultural District Authority

Piling for Integrated Basement and U/G Road in Zone 2B 2C


3 Month Rolling Programme as of 25 Mar 2022

Based on CMWP Rev.0

VIBRO

Date01-Mar-22RevisionRev.0CheckedKLABApprovedB


Activity ID	Activity Name	CMWP Rev.0 Start	CMWP Rev.0 Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	March							April				May				June					
									1							2				3				4					
									25	04	11	18	25	01	08	15	22	29	06	13	20	27	03	10	17	4			
02																													
P24&27-BP08.10	BP - Excavation	12-Feb-22	18-Feb-22	6	26-Mar-22	01-Apr-22	1	0%																					
P24&27-BP08.20	BP - RCD Drilling	19-Feb-22	24-Mar-22	29	02-Apr-22	12-May-22	1	0%																					
P24&27-BP08.30	BP - Airlift, Cage Install and Concrete	25-Mar-22	02-Apr-22	8	13-May-22	21-May-22	74	0%																					
04																													
P26-BP03.10	BP - Excavation	06-Apr-22	12-Apr-22	6	24-May-22	30-May-22	1	0%																					
P26-BP03.20	BP - RCD Drilling	13-Apr-22	21-May-22	29	31-May-22	05-Jul-22	1	0%																					
08																													
P24&27-BP02.20	BP - RCD Drilling	09-Sep-22	15-Oct-22	7	19-Feb-22 A	28-Feb-22 A		100%																					
P24&27-BP02.30	BP - Airlift, Cage Install and Concrete	17-Oct-22	25-Oct-22	16	01-Mar-22 A	19-Mar-22 A		100%																					
VD03																													
02																													
P30-BP59.10	BP - Excavation	23-Feb-22	01-Mar-22	71	06-Jan-22 A	01-Apr-22	5	0%																					
P30-BP59.20	BP - RCD Drilling	02-Mar-22	04-Apr-22	29	02-Apr-22	12-May-22	5	0%																					
P30-BP59.30	BP - Airlift, Cage Install and Concrete	06-Apr-22	14-Apr-22	8	13-May-22	21-May-22	197	0%																					
09																													
P30-BP57.10	BP - Excavation	25-Oct-22	31-Oct-22	19	11-Mar-22 A	01-Apr-22	329	0%																					
P30-BP57.20	BP - RCD Drilling	01-Nov-22	03-Dec-22	29	02-Apr-22	12-May-22	329	0%																					
P30-BP57.30	BP - Airlift, Cage Install and Concrete	05-Dec-22	13-Dec-22	8	13-May-22	21-May-22	329	0%																					
VD04																													
04																													
P30-BP66.10	BP - Excavation	21-Mar-22	26-Mar-22	6	30-May-22	06-Jun-22	10	0%																					
P30-BP66.20	BP - RCD Drilling	28-Mar-22	14-Apr-22	15	07-Jun-22	23-Jun-22	10	0%																					
P30-BP66.30	BP - Airlift, Cage Install and Concrete	19-Apr-22	26-Apr-22	7	24-Jun-22	02-Jul-22	152	0%																					
05																													
P30-BP73.10	BP - Excavation	08-Apr-22	14-Apr-22	6	17-Jun-22	23-Jun-22	10	0%																					
P30-BP73.20	BP - RCD Drilling	19-Apr-22	06-May-22	15	24-Jun-22	12-Jul-22	10	0%																					
11																													
P30-BP72.10	BP - Excavation	04-Aug-22	10-Aug-22	47	07-Feb-22 A	01-Apr-22	134	0%																					
P30-BP72.20	BP - RCD Drilling	11-Aug-22	27-Aug-22	15	02-Apr-22	23-Apr-22	134	0%																					
P30-BP72.30	BP - Airlift, Cage Install and Concrete	29-Aug-22	05-Sep-22	7	25-Apr-22	03-May-22	336	0%																					
13																													
P30-BP67.10	BP - Excavation	14-Sep-22	20-Sep-22	23	14-Feb-22 A	12-Mar-22 A		100%																					
P30-BP67.20	BP - RCD Drilling	21-Sep-22	10-Oct-22	26	14-Mar-22 A	13-Apr-22	159	0%																					
P30-BP67.30	BP - Airlift, Cage Install and Concrete	11-Oct-22	18-Oct-22	7	14-Apr-22	25-Apr-22	205	0%																					
VD06																													
02																													
P28&29-BP11.10	BP - Excavation	09-Feb-22	15-Feb-22	6	09-Apr-22	19-Apr-22	-50	0%																					
P28&29-BP11.20	BP - RCD Drilling	16-Feb-22	04-Mar-22	15	20-Apr-22	07-May-22	-50	0%																					

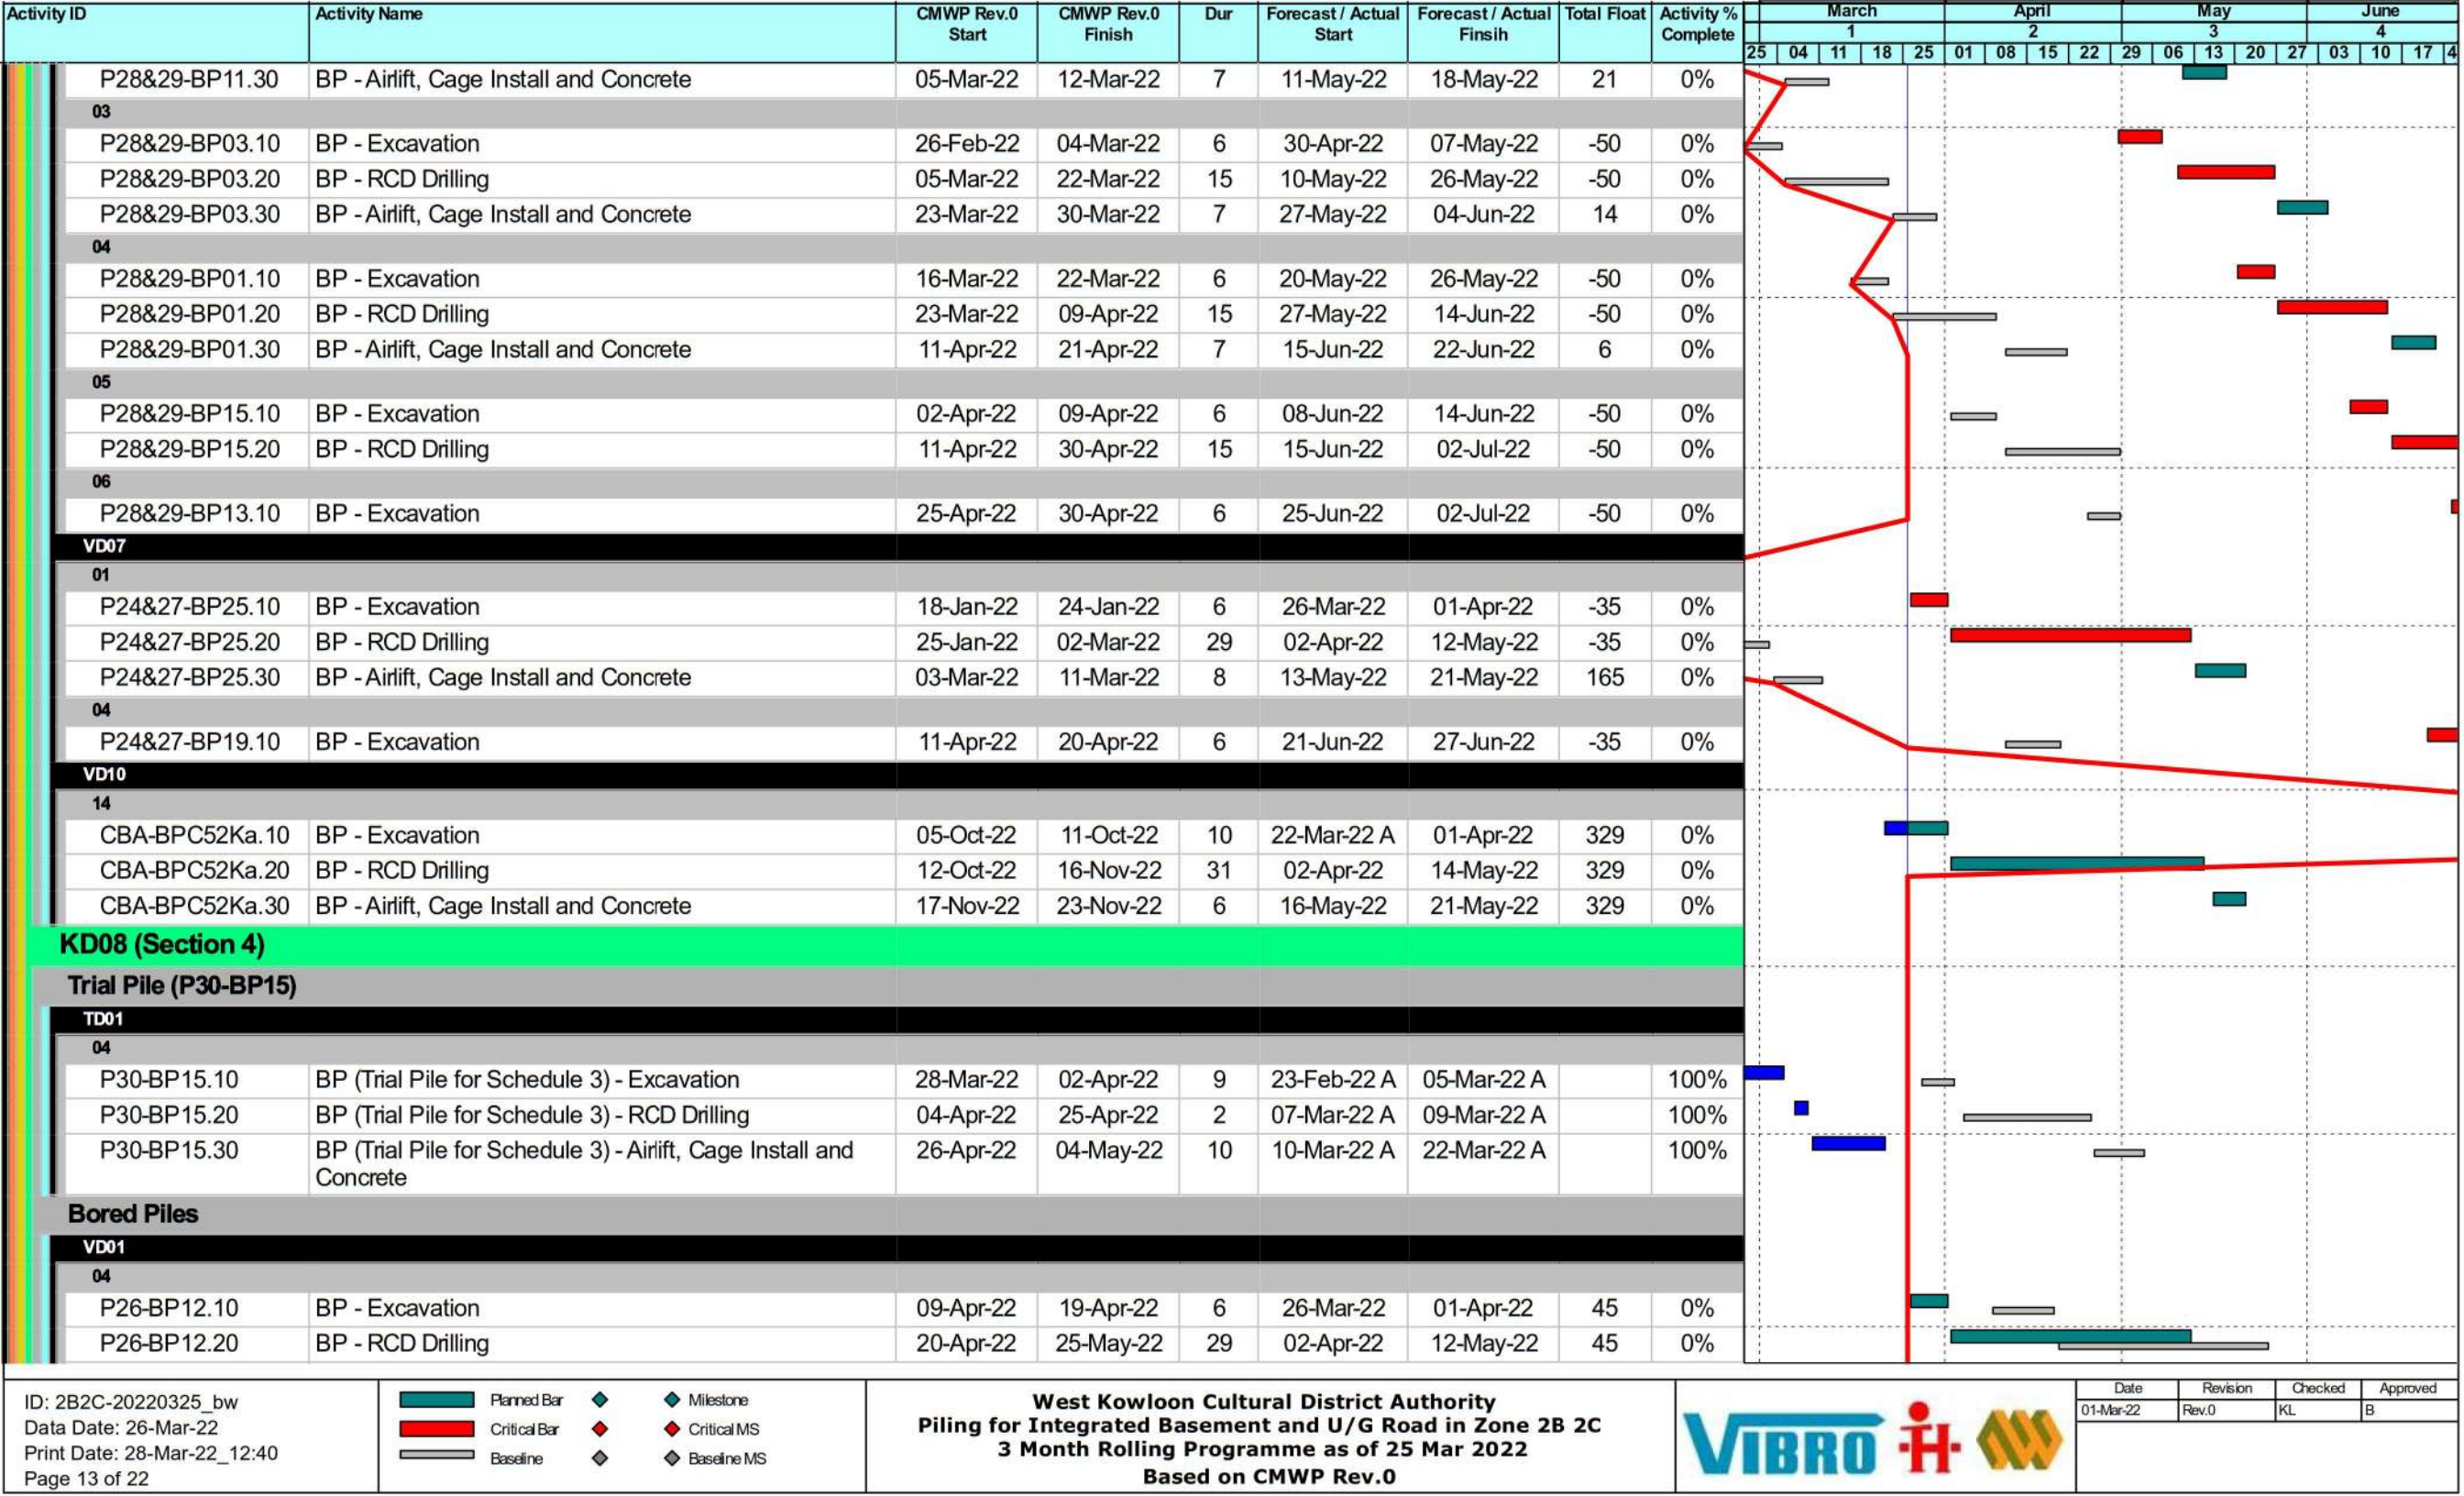

Activity ID	Activity Name	CMWP Rev.0 Start	CMWP Rev.0 Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	March				April				May				June																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																											
									1				2				3				4																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																											
									25	04	11	18	25	01	08	15	22	29	06	13	20	27	03	10	17	4																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																						
P26-BP12.30	BP - Airlift, Cage Install and Concrete	26-May-22	04-Jun-22	8	13-May-22	21-May-22	221	0%																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																								</

[illegible]

Activity ID	Activity Name	CMWP Rev.0 Start	CMWP Rev.0 Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	March				April				May				June																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																					
									1				2				3				4																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																					
									25	04	11	18	25	01	08	15	22	29	06	13	20	27	03	10	17	24																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																
KD09 (Section 5)	SHP-BW-52Y1a-P	Socketed Steel H Piling	13-Apr-22	26-Apr-22	22	23-Mar-22 A	21-Apr-22	94	0%																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																	

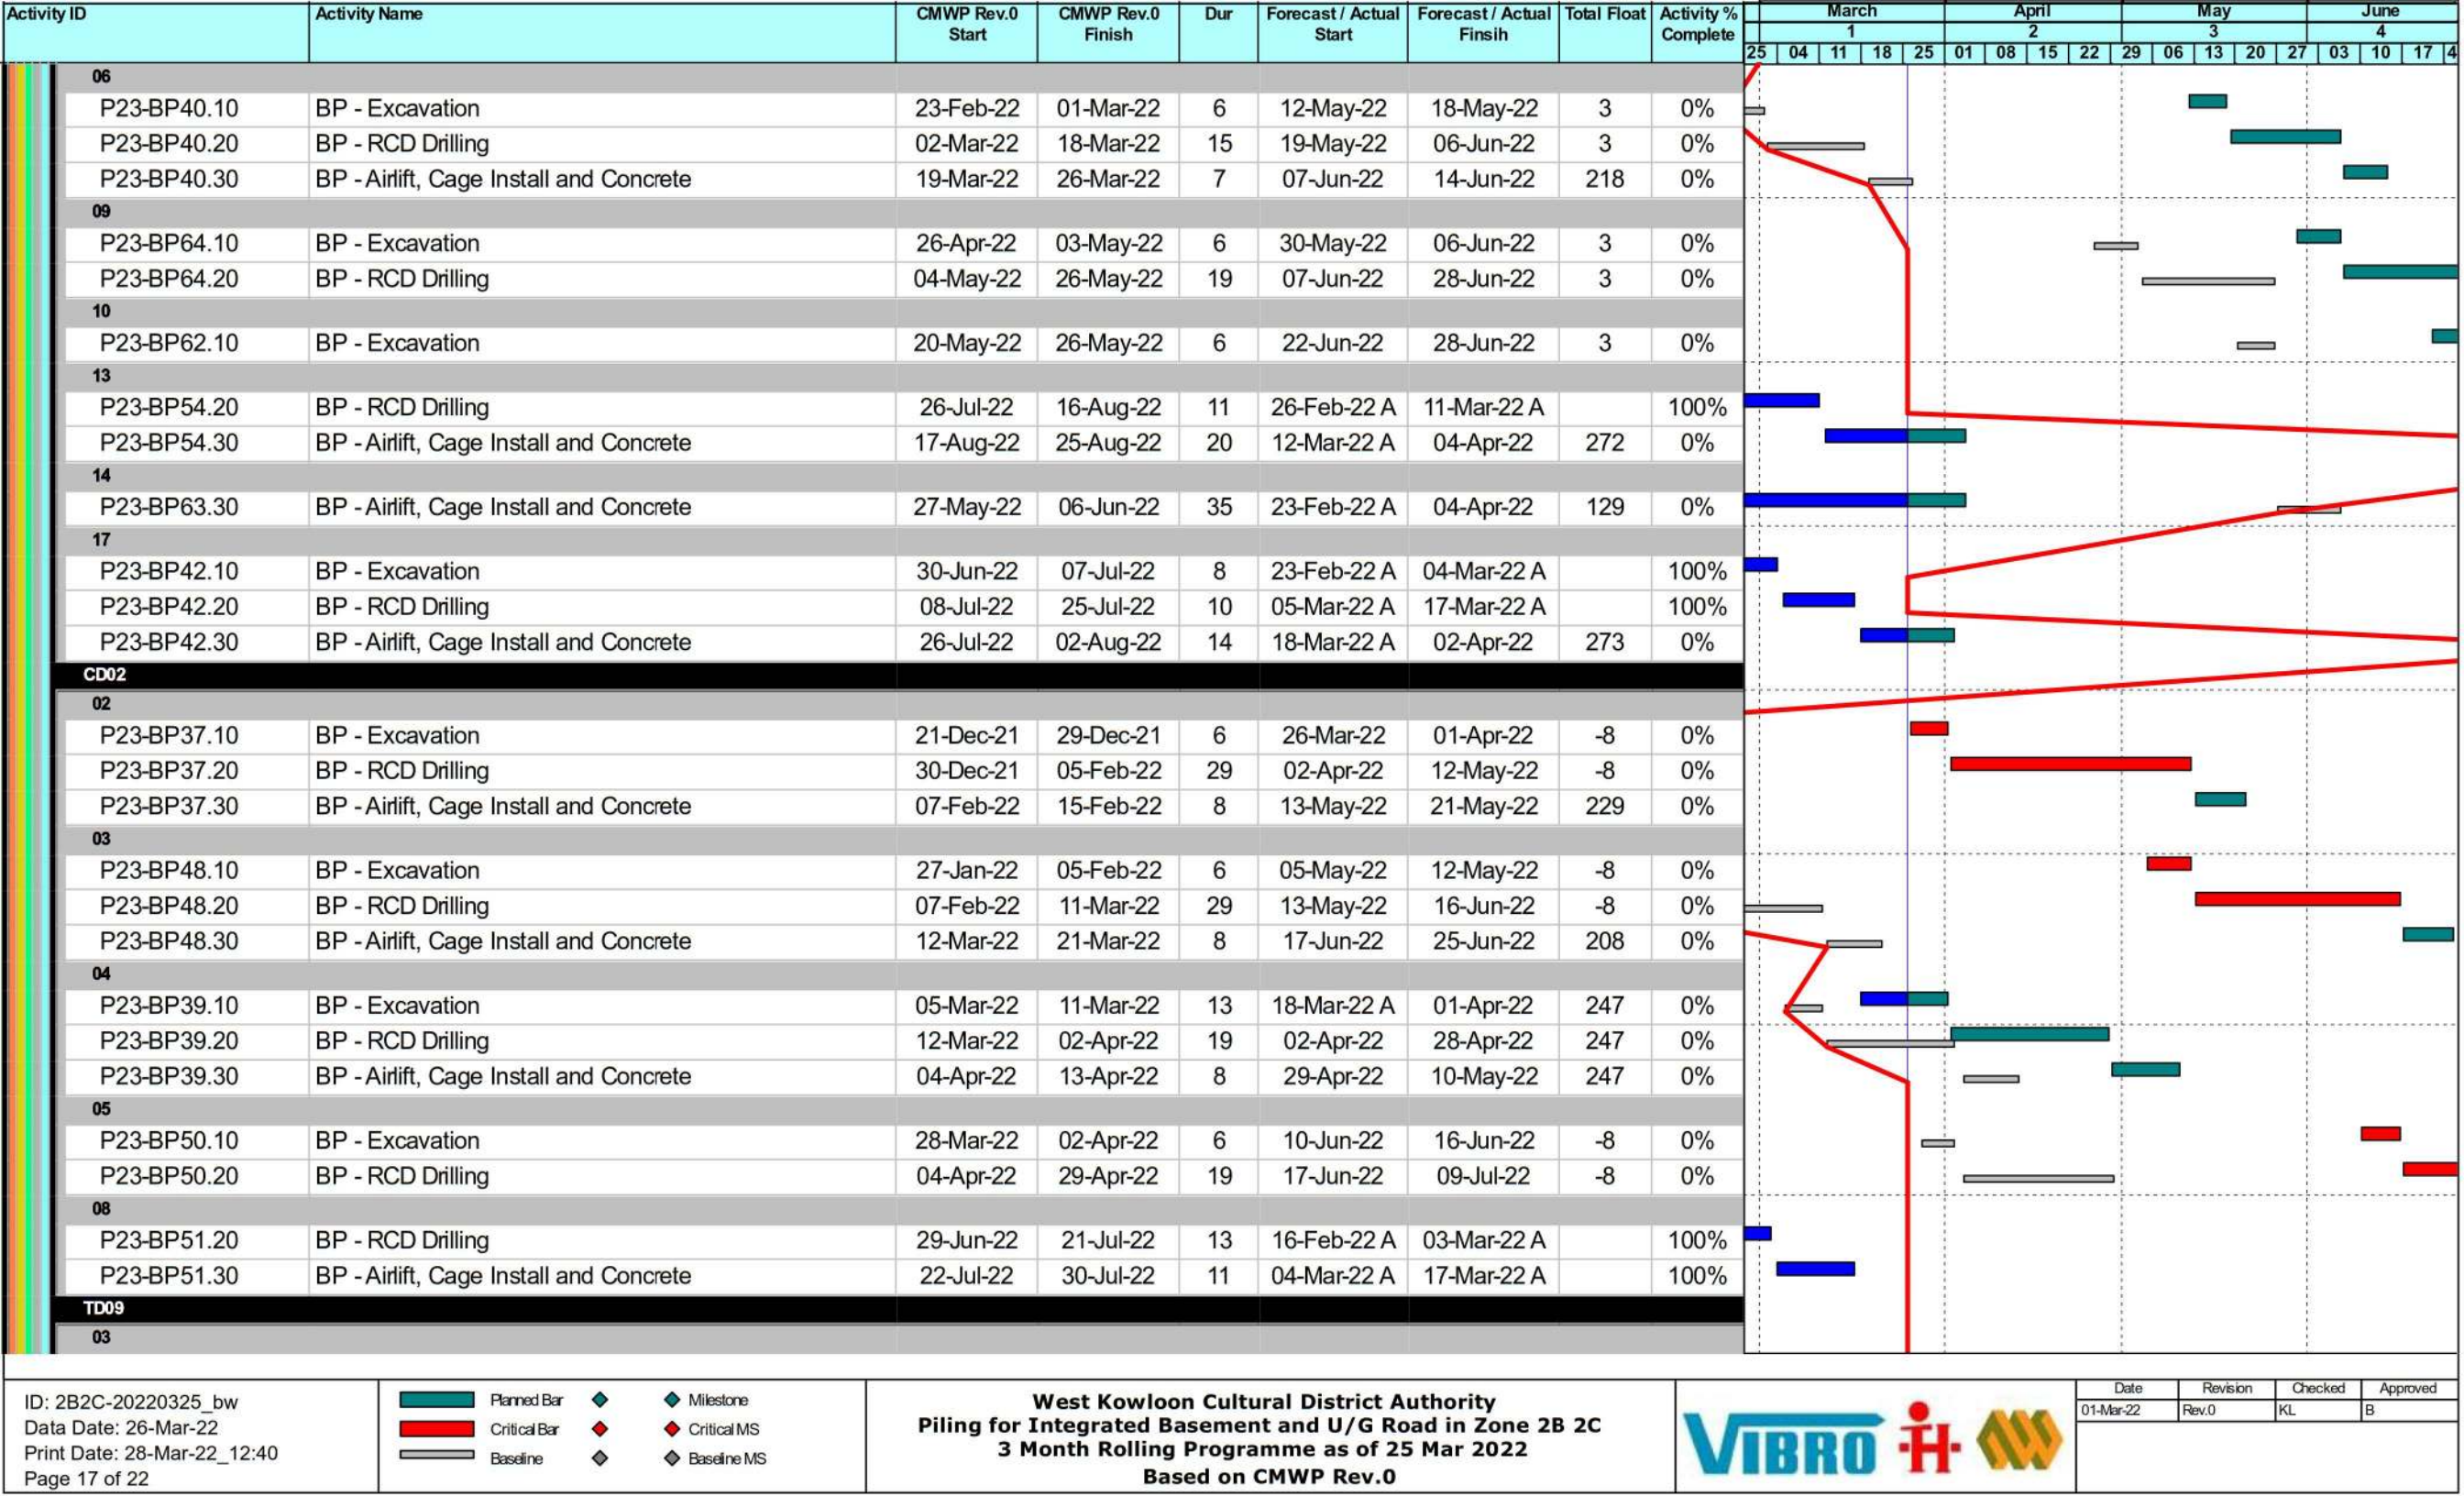

Activity ID									
Activity Name		CMWP Rev.0 Start	CMWP Rev.0 Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	
<div>March 1 April 2 May 3 June 4</div> <div>25 04 11 18 25 01 08 15 22 29 06 13 20 27 03 10 17 4</div>									
CBA-BPC52U.10	BP - Excavation	06-May-22	13-May-22	6	06-May-22	13-May-22	0	0%	
CBA-BPC52U.20	BP - RCD Drilling	14-May-22	25-May-22	10	14-May-22	25-May-22	0	0%	
CBA-BPC52U.30	BP - Airlift, Cage Install and Concrete	26-May-22	31-May-22	5	26-May-22	31-May-22	143	0%	
TD08									
14									
CBA-BPC40P.10	BP - Excavation	17-Jun-22	23-Jun-22	6	17-Jun-22	23-Jun-22	142	0%	
CBA-BPC40P.20	BP - RCD Drilling	24-Jun-22	06-Jul-22	10	24-Jun-22	06-Jul-22	142	0%	
TD07									
02									
P18-BP16.10	BP - Excavation	20-Dec-21	28-Dec-21	6	14-Apr-22	23-Apr-22	-56	0%	
P18-BP16.20	BP - RCD Drilling	29-Dec-21	15-Jan-22	15	25-Apr-22	13-May-22	-56	0%	
P18-BP16.30	BP - Airlift, Cage Install and Concrete	17-Jan-22	24-Jan-22	7	14-May-22	21-May-22	23	0%	
03									
P18-BP23.10	BP - Excavation	10-Jan-22	15-Jan-22	6	06-May-22	13-May-22	-56	0%	
P18-BP23.20	BP - RCD Drilling	17-Jan-22	05-Feb-22	15	14-May-22	31-May-22	-56	0%	
P18-BP23.30	BP - Airlift, Cage Install and Concrete	07-Feb-22	14-Feb-22	7	01-Jun-22	09-Jun-22	15	0%	
04									
P18-BP21.10	BP - Excavation	27-Jan-22	05-Feb-22	6	25-May-22	31-May-22	-56	0%	
P18-BP21.20	BP - RCD Drilling	07-Feb-22	23-Feb-22	15	01-Jun-22	18-Jun-22	-56	0%	
P18-BP21.30	BP - Airlift, Cage Install and Concrete	24-Feb-22	03-Mar-22	7	20-Jun-22	27-Jun-22	7	0%	
TD06									
01									
P18-BP36.10	BP - Excavation	20-Dec-21	28-Dec-21	6	26-Mar-22	01-Apr-22	-2	0%	
P18-BP36.20	BP - RCD Drilling	29-Dec-21	15-Jan-22	15	02-Apr-22	23-Apr-22	-2	0%	
P18-BP36.30	BP - Airlift, Cage Install and Concrete	17-Jan-22	24-Jan-22	7	25-Apr-22	03-May-22	140	0%	
02									
P18-BP40.10	BP - Excavation	10-Jan-22	15-Jan-22	6	14-Apr-22	23-Apr-22	-2	0%	
P18-BP40.20	BP - RCD Drilling	17-Jan-22	05-Feb-22	15	25-Apr-22	13-May-22	-2	0%	
P18-BP40.30	BP - Airlift, Cage Install and Concrete	07-Feb-22	14-Feb-22	7	14-May-22	21-May-22	132	0%	
03									
P18-BP38.10	BP - Excavation	27-Jan-22	05-Feb-22	6	06-May-22	13-May-22	-2	0%	
P18-BP38.20	BP - RCD Drilling	07-Feb-22	28-Feb-22	19	14-May-22	06-Jun-22	-2	0%	
P18-BP38.30	BP - Airlift, Cage Install and Concrete	01-Mar-22	09-Mar-22	8	07-Jun-22	15-Jun-22	120	0%	
04									
P18-BP33.10	BP - Excavation	22-Feb-22	28-Feb-22	6	30-May-22	06-Jun-22	-2	0%	
P18-BP33.20	BP - RCD Drilling	01-Mar-22	17-Mar-22	15	07-Jun-22	23-Jun-22	-2	0%	
P18-BP33.30	BP - Airlift, Cage Install and Concrete	18-Mar-22	25-Mar-22	7	24-Jun-22	02-Jul-22	113	0%	
05									
P18-BP28.10	BP - Excavation	11-Mar-22	17-Mar-22	6	17-Jun-22	23-Jun-22	-2	0%	

ID: 2B2C-20220325_bw
Data Date: 26-Mar-22
Print Date: 28-Mar-22_12:40
Page 18 of 22

Planned BarCritical BarBaseline

MilestoneCritical MSBaseline MS

West Kowloon Cultural District Authority

Piling for Integrated Basement and U/G Road in Zone 2B 2C

3 Month Rolling Programme as of 25 Mar 2022

Based on CMWP Rev.0

VIBRO

•H•

Date

01-Mar-22

Revision


Rev.0

Checked

KL


Approved

B

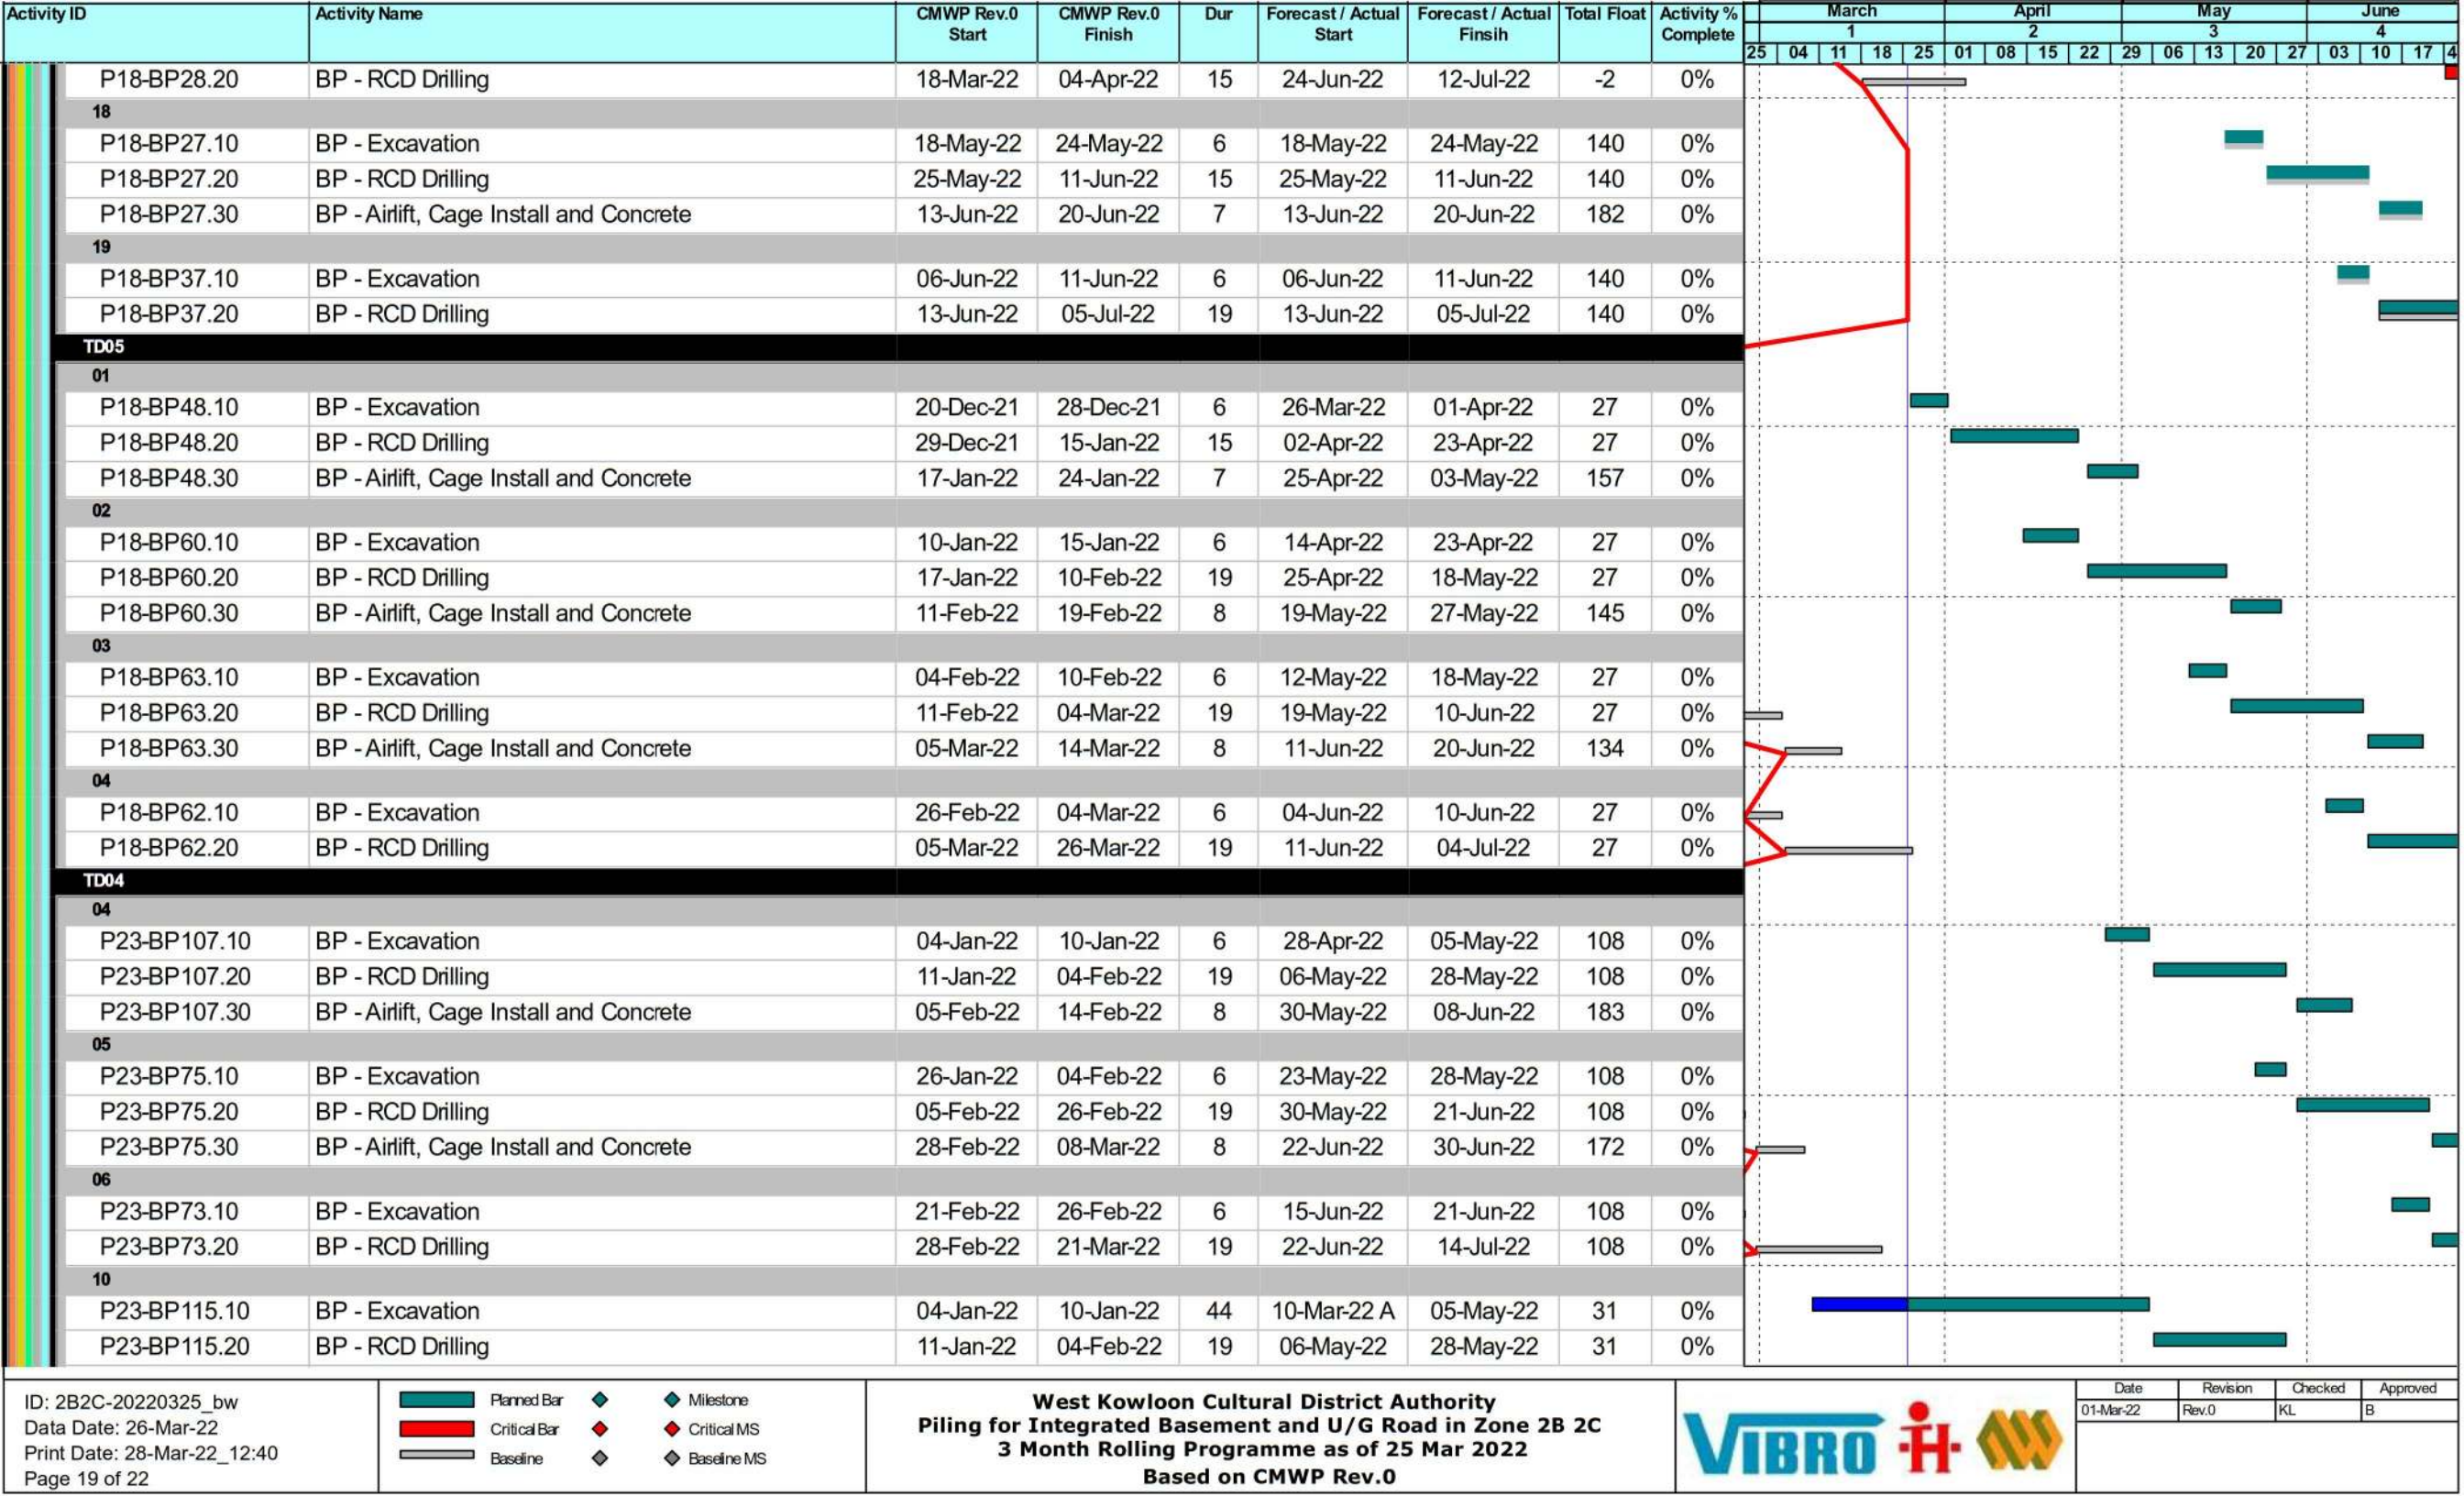

[illegible]

Activity ID	Activity Name	CMWP Rev.0 Start	CMWP Rev.0 Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	March				April				May				June			
									1				2				3				4			
									25	04	11	18	25	01	08	15	22	29	06	13	20	27	03	10
<div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><</div>																								

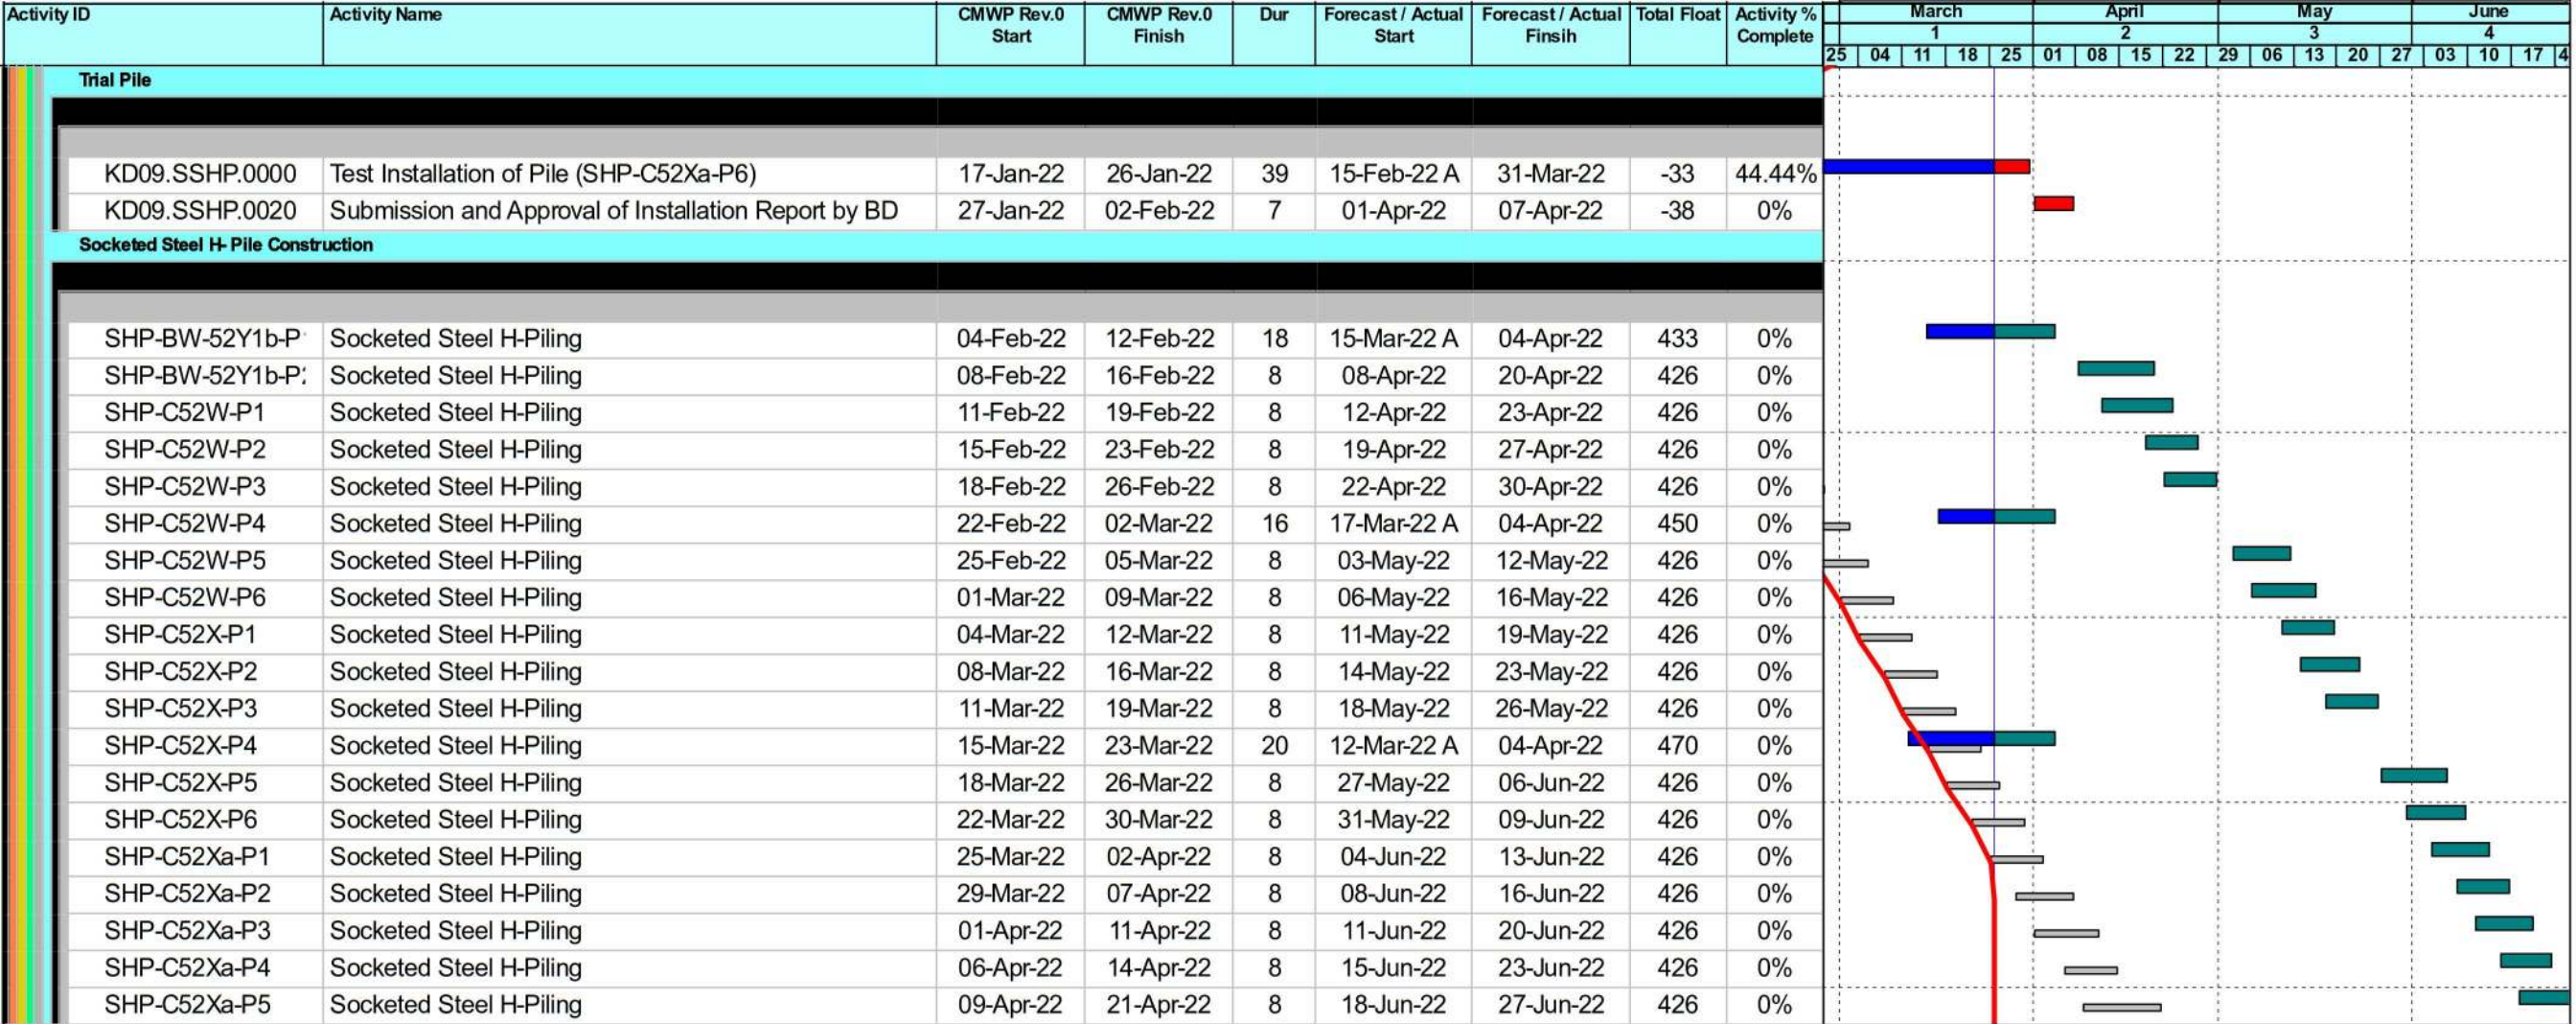

Activity ID	Activity Name	CMWP Rev.0 Start	CMWP Rev.0 Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete																												
									April				May				June				July															
									1				2				3				4															
									25	01	08	15	22	29	06	13	20	27	03	10	17	24	01	08	15	22										
Piling for Integrated Basement and U/G Road in Zone 2B & 2C																																				
Contract Dates																																				
Key Dates																																				
KD for Zone 2B																																				
KD01	KD01 (Stage 1-1) - 300 days after Commencement (18 May 2022)			18-May-22	0		24-Jun-22*	-37	0%																											
Optional Works subjected to CA's Instruction																																				
CO3A	Last CAI date for Optional Works Item No.3 (within 280 Days after Commencement)		28-Apr-22		0	28-Apr-22		2	0%																											
Access Dates of Site Portion																																				
120 days after Commencement																																				
ACB10	Access to Site Portion B10		19-Nov-21		0	23-Apr-22		-93	0%																											
270 days after Commencement																																				
ACB12	Access to Site Portion B12		18-Apr-22		0	23-Apr-22		24	0%																											
ACB35	Access to Site Portion B35 (To be agreed with the Zone 2A contractor)		18-Apr-22		0	23-Apr-22		24	0%																											
Mobilization Stage																																				
Site Mobilization Works																																				
Pre-Construction Works before Piling Commencement																																				
MOBP.10.1300	Trial Pit for Drillholes & Removal of Existing Substructures / Ground Slab [503 nos]		19-Aug-21	30-Apr-22	262	19-Aug-21 A	07-May-22	130	87%																											
Construction Stage																																				
Pile Construction																																				
Predrilling																																				
PD.1000	Predrilling for BP in KD01 [8 nos.]		30-Sep-21	30-Mar-22	143	30-Sep-21 A	25-Mar-22 A		100%																											
PD.1040	Predrilling for BP in KD03 [5 nos.]		20-Oct-21	06-May-22	128	20-Oct-21 A	25-Mar-22 A		100%																											
PD.1080	Predrilling for BP in KD05 [76 nos.]		30-Sep-21	30-Mar-22	172	30-Sep-21 A	03-May-22	6	58%																											
PD.1100	Predrilling for BP in KD06 [95 nos.] incl. 5 additional nos.		30-Sep-21	23-May-22	203	30-Sep-21 A	11-Jun-22	103	55%																											
PD.1120	Predrilling for BP in KD07 [90 nos.] incl. 2 additional nos.		30-Sep-21	23-May-22	200	30-Sep-21 A	11-Jun-22	195	85%																											
PD.1160	Predrilling for BP in KD09 [149 nos.] incl. 4 additional nos.		30-Sep-21	30-Mar-22	175	30-Sep-21 A	05-May-22	131	70%																											
ID: 2B2C-20220422_bw Data Date: 23-Apr-22 Print Date: 25-Apr-22_14:33 Page 1 of 21									<div><div></div>Planned Bar</div> <div><div></div>Critical Bar</div> <div><div></div>Baseline</div> <div><div></div>Milestone</div> <div><div></div>Critical MS</div> <div><div></div>Baseline MS</div>									<div>West Kowloon Cultural District Authority</div> <div>Piling for Integrated Basement and U/G Road in Zone 2B 2C</div> <div>3 Month Rolling Programme as of 22 Apr 2022</div> <div>Based on CMWP Rev.0</div>									<div><div>VIBRO</div><div></div><div></div></div> <div><div>Date</div>4-Mar-22</div> <div><div>Revision</div>Rev.0</div> <div><div>Checked</div>KL</div> <div><div>Approved</div>B</div>									

Activity ID	Activity Name	CMWP Rev.0 Start	CMWP Rev.0 Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete																															
									April 1					May 2					June 3				July 4																
									25	01	08	15	22	29	06	13	20	27	03	10	17	24	01	08	15	22													
KD01 (Stage 1-1)																																							
Bored Piles																																							
CBA-BP04.10	BP - Excavation	12-Apr-22	22-Apr-22	7	12-May-22	19-May-22	-21	0%																															
CBA-BP04.20	BP - RCD Drilling	23-Apr-22	11-May-22	14	20-May-22	06-Jun-22	-21	0%																															
CBA-BP04.30	BP - Airlift, Cage Install and Concrete	12-May-22	18-May-22	6	07-Jun-22	13-Jun-22	-21	0%																															
CBA-BPC41Jb.10	BP - Excavation	13-Apr-22	22-Apr-22	6	31-May-22	07-Jun-22	-31	0%																															
CBA-BPC41Jb.20	BP - RCD Drilling	23-Apr-22	05-May-22	10	08-Jun-22	18-Jun-22	-31	0%																															
CBA-BPC41Jb.30	BP - Airlift, Cage Install and Concrete	06-May-22	12-May-22	5	20-Jun-22	24-Jun-22	-31	0%																															
P22&P19-BP11.10	BP - Excavation	24-Jan-22	29-Jan-22	8	17-Mar-22 A	26-Mar-22 A		100%																															
P22&P19-BP11.20	BP - RCD Drilling	31-Jan-22	24-Feb-22	8	28-Mar-22 A	07-Apr-22 A		100%																															
P22&P19-BP11.30	BP - Airlift, Cage Install and Concrete	25-Feb-22	05-Mar-22	39	08-Apr-22 A	28-May-22	-9	0%																															
P22&P19-BP21.10	BP - Excavation	18-Feb-22	24-Feb-22	15	22-Mar-22 A	09-Apr-22 A		100%																															
P22&P19-BP21.20	BP - RCD Drilling	25-Feb-22	18-Mar-22	4	11-Apr-22 A	19-Apr-22 A		100%																															
P22&P19-BP21.30	BP - Airlift, Cage Install and Concrete	19-Mar-22	28-Mar-22	11	20-Apr-22 A	03-May-22	12	0%																															
KD02 (Stage 5-1)																																							
Bored Piles																																							
P23-BP117.10	BP - Excavation	03-Dec-21	09-Dec-21	80	10-Jan-22 A	21-Apr-22 A		100%																															
P23-BP117.20	BP - RCD Drilling	10-Dec-21	10-Jan-22	25	22-Apr-22 A	23-May-22	36	0%																															
P23-BP117.30	BP - Airlift, Cage Install and Concrete	20-Jan-22	28-Jan-22	8	24-May-22	01-Jun-22	180	0%																															
KD03 (Stage 3-1)																																							
Bored Piles																																							
CBA-BPC54Jb.10	BP - Excavation	26-Feb-22	04-Mar-22	6	23-Apr-22	29-Apr-22	-44	0%																															
CBA-BPC54Jb.20	BP - RCD Drilling	05-Mar-22	11-Apr-22	31	30-Apr-22	08-Jun-22	-44	0%																															
CBA-BPC54Jb.30	BP - Airlift, Cage Install and Concrete	12-Apr-22	21-Apr-22	6	09-Jun-22	15-Jun-22	55	0%																															
CBA-BPC54Ka.10	BP - Excavation	04-Apr-22	11-Apr-22	6	28-Jun-22	05-Jul-22	-66	0%																															
CBA-BPC54Ka.20	BP - RCD Drilling	12-Apr-22	25-May-22	33	06-Jul-22	12-Aug-22	-66	0%																															
P28&29-BP08.10	BP - Excavation	18-Mar-22	24-Mar-22	24	21-Mar-22 A	22-Apr-22 A		100%																															
P28&29-BP08.20	BP - RCD Drilling	25-Mar-22	12-Apr-22	15	23-Apr-22	12-May-22	82	0%																															
P28&29-BP08.30	BP - Airlift, Cage Install and Concrete	13-Apr-22	23-Apr-22	7	13-May-22	20-May-22	82	0%																															
ID: 2B2C-20220422_bw Data Date: 23-Apr-22 Print Date: 25-Apr-22_14:33 Page 2 of 21									<div><div><div></div><div></div><div></div></div><div><div>Planned Bar</div><div>Critical Bar</div><div>Baseline</div></div><div><div>◆ Milestone</div><div>◆ Critical MS</div><div>◆ Baseline MS</div></div></div>									<div>West Kowloon Cultural District Authority</div> <div>Piling for Integrated Basement and U/G Road in Zone 2B 2C</div> <div>3 Month Rolling Programme as of 22 Apr 2022</div> <div>Based on CMWP Rev.0</div>									<div><div>VIBRO</div><div><div></div><div></div><div></div></div></div>									<div>Date</div> <div>4-Mar-22</div>	<div>Revision</div> <div>Rev.0</div>	<div>Checked</div> <div>KL</div>	<div>Approved</div> <div>B</div>

Activity ID		Activity Name	CMWP Rev.0 Start	CMWP Rev.0 Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete																												
										April 1							May 2							June 3							July 4						
										25	01	08	15	22	29	06	13	20	27	03	10	17	24	01	08	15	22										
	P28&29-BP29.10	BP - Excavation	19-Jan-22	25-Jan-22	6	23-Apr-22	29-Apr-22	-65	0%																												
	P28&29-BP29.20	BP - RCD Drilling	26-Jan-22	15-Feb-22	15	30-Apr-22	19-May-22	-65	0%																												
	P28&29-BP29.30	BP - Airlift, Cage Install and Concrete	16-Feb-22	23-Feb-22	7	20-May-22	27-May-22	6	0%																												
KD04 (Stage 4-1)																																					
Bored Piles																																					
	CBA-BPC54V.10	BP - Excavation	08-Apr-22	14-Apr-22	6	23-Apr-22	29-Apr-22	-10	0%																												
	CBA-BPC54V.20	BP - RCD Drilling	19-Apr-22	29-Apr-22	10	30-Apr-22	13-May-22	-10	0%																												
	CBA-BPC54V.30	BP - Airlift, Cage Install and Concrete	30-Apr-22	06-May-22	5	14-May-22	19-May-22	83	0%																												
	P30-BP06.10	BP - Excavation	31-May-22	07-Jun-22	6	06-Jun-22	11-Jun-22	31	0%																												
	P30-BP06.20	BP - RCD Drilling	08-Jun-22	29-Jun-22	19	13-Jun-22	05-Jul-22	31	0%																												
	P30-BP06.30	BP - Airlift, Cage Install and Concrete	30-Jun-22	09-Jul-22	8	06-Jul-22	14-Jul-22	37	0%																												
KD05 (Section 1)																																					
Bored Piles																																					
	CBA-BP01.10	BP - Excavation	25-Mar-22	01-Apr-22	7	23-Apr-22	30-Apr-22	-21	0%																												
	CBA-BP01.20	BP - RCD Drilling	02-Apr-22	22-Apr-22	14	03-May-22	19-May-22	-21	0%																												
	CBA-BP01.30	BP - Airlift, Cage Install and Concrete	23-Apr-22	29-Apr-22	6	20-May-22	26-May-22	-13	0%																												
	CBA-BP02.10	BP - Excavation	11-May-22	18-May-22	7	23-Jun-22	30-Jun-22	37	0%																												
	CBA-BP02.20	BP - RCD Drilling	19-May-22	04-Jun-22	14	02-Jul-22	18-Jul-22	37	0%																												
	CBA-BP02.30	BP - Airlift, Cage Install and Concrete	06-Jun-22	11-Jun-22	6	19-Jul-22	25-Jul-22	51	0%																												
	CBA-BP03.10	BP - Excavation	16-May-22	23-May-22	7	10-Jun-22	17-Jun-22	67	0%																												
	CBA-BP03.20	BP - RCD Drilling	24-May-22	09-Jun-22	14	18-Jun-22	05-Jul-22	67	0%																												
	CBA-BP03.30	BP - Airlift, Cage Install and Concrete	10-Jun-22	16-Jun-22	6	06-Jul-22	12-Jul-22	67	0%																												
	CBA-BP05.10	BP - Excavation	28-May-22	04-Jun-22	6	12-Jul-22	18-Jul-22	37	0%																												
	CBA-BP05.20	BP - RCD Drilling	06-Jun-22	16-Jun-22	10	19-Jul-22	29-Jul-22	37	0%																												
	CBA-BP06.10	BP - Excavation	04-May-22	11-May-22	6	30-May-22	06-Jun-22	67	0%																												
	CBA-BP06.20	BP - RCD Drilling	12-May-22	23-May-22	10	07-Jun-22	17-Jun-22	67	0%																												
	CBA-BP06.30	BP - Airlift, Cage Install and Concrete	24-May-22	28-May-22	5	18-Jun-22	23-Jun-22	76	0%																												
	CBA-BPC38Ja.30	BP - Airlift, Cage Install and Concrete	20-Dec-21	24-Dec-21	7	16-Mar-22 A	24-Mar-22 A		100%																												
	CBA-BPC38Jb.10	BP - Excavation	04-Feb-22	10-Feb-22	6	19-May-22	25-May-22	91	0%																												
	CBA-BPC38Jb.20	BP - RCD Drilling	11-Feb-22	22-Feb-22	10	26-May-22	07-Jun-22	91	0%																												
	CBA-BPC38Jb.30	BP - Airlift, Cage Install and Concrete	23-Feb-22	28-Feb-22	5	08-Jun-22	13-Jun-22	91	0%																												
	CBA-BPC38Ka.10	BP - Excavation	16-Feb-22	22-Feb-22	27	25-Mar-22 A	29-Apr-22	111	0%																												
	CBA-BPC38Ka.20	BP - RCD Drilling	23-Feb-22	05-Mar-22	10	30-Apr-22	13-May-22	111	0%																												
CBA-BPC38Ka.30	BP - Airlift, Cage Install and Concrete	07-Mar-22	11-Mar-22	5	14-May-22	19-May-22	111	0%																													

ID: 2B2C-20220422_bw
Data Date: 23-Apr-22
Print Date: 25-Apr-22_14:33
Page 3 of 21

Planned Bar

Critical Bar

Baseline

Milestone

Critical MS

Baseline MS

West Kowloon Cultural District Authority

Piling for Integrated Basement and U/G Road in Zone 2B 2C

3 Month Rolling Programme as of 22 Apr 2022

Based on CMWP Rev.0

VIBRO

Date

Revision

Checked

Approved

4-Mar-22










Rev.0

KL

B










Activity ID		Activity Name	CMWP Rev.0 Start	CMWP Rev.0 Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete																												
										April							May							June							July						
										25	01	08	15	22	29	06	13	20	27	03	10	17	24	01	08	15	22										
	CBA-BPC39Jb.10	BP - Excavation	20-Jan-22	26-Jan-22	29	04-Apr-22 A	13-May-22	91	0%																												
	CBA-BPC39Jb.20	BP - RCD Drilling	27-Jan-22	10-Feb-22	10	14-May-22	25-May-22	91	0%																												
	CBA-BPC39Jb.30	BP - Airlift, Cage Install and Concrete	11-Feb-22	16-Feb-22	5	26-May-22	31-May-22	96	0%																												
	CBA-BPC39K.10	BP - Excavation	06-Jun-22	11-Jun-22	7	22-Apr-22 A	29-Apr-22	111	0%																												
	CBA-BPC39K.20	BP - RCD Drilling	13-Jun-22	23-Jun-22	10	30-Apr-22	13-May-22	111	0%																												
	CBA-BPC39K.30	BP - Airlift, Cage Install and Concrete	24-Jun-22	29-Jun-22	5	18-Jun-22	23-Jun-22	82	0%																												
	CBA-BPC40Ja.10	BP - Excavation	03-Mar-22	09-Mar-22	15	31-Mar-22 A	22-Apr-22 A		100%																												
	CBA-BPC40Ja.20	BP - RCD Drilling	10-Mar-22	21-Mar-22	26	23-Apr-22 A	25-May-22	-31	0%																												
	CBA-BPC40Ja.30	BP - Airlift, Cage Install and Concrete	22-Mar-22	26-Mar-22	5	26-May-22	31-May-22	96	0%																												
	CBA-BPC40K.20	BP - RCD Drilling	07-Mar-22	17-Mar-22	4	21-Mar-22 A	25-Mar-22 A		100%																												
	CBA-BPC40K.30	BP - Airlift, Cage Install and Concrete	18-Mar-22	23-Mar-22	6	26-Mar-22 A	02-Apr-22 A		100%																												
	CBA-BPC40Ka.10	BP - Excavation	10-Jun-22	16-Jun-22	20	16-Mar-22 A	09-Apr-22 A		100%																												
	CBA-BPC40Ka.20	BP - RCD Drilling	17-Jun-22	28-Jun-22	1	09-Apr-22 A	11-Apr-22 A		100%																												
	CBA-BPC40Ka.30	BP - Airlift, Cage Install and Concrete	29-Jun-22	05-Jul-22	12	12-Apr-22 A	28-Apr-22	127	0%																												
	CBA-BPC40M.10	BP - Excavation	24-Dec-21	03-Jan-22	14	14-Mar-22 A	30-Mar-22 A		100%																												
	CBA-BPC40M.20	BP - RCD Drilling	04-Jan-22	14-Jan-22	0	31-Mar-22 A	31-Mar-22 A		100%																												
	CBA-BPC40M.30	BP - Airlift, Cage Install and Concrete	15-Jan-22	20-Jan-22	9	01-Apr-22 A	13-Apr-22 A		100%																												
	CBA-BPC40Na.10	BP - Excavation	12-May-22	18-May-22	6	12-May-22	18-May-22	82	0%																												
	CBA-BPC40Na.20	BP - RCD Drilling	19-May-22	30-May-22	10	19-May-22	30-May-22	82	0%																												
	CBA-BPC40Na.30	BP - Airlift, Cage Install and Concrete	31-May-22	06-Jun-22	5	31-May-22	06-Jun-22	87	0%																												
	CBA-BPC40O.10	BP - Excavation	08-Jan-22	14-Jan-22	6	23-Apr-22	29-Apr-22	91	0%																												
	CBA-BPC40O.20	BP - RCD Drilling	15-Jan-22	26-Jan-22	10	30-Apr-22	13-May-22	91	0%																												
	CBA-BPC40O.30	BP - Airlift, Cage Install and Concrete	27-Jan-22	04-Feb-22	5	14-May-22	19-May-22	101	0%																												
	CBA-BPC42K.10	BP - Excavation	15-Mar-22	21-Mar-22	6	19-May-22	25-May-22	-31	0%																												
	CBA-BPC42K.20	BP - RCD Drilling	22-Mar-22	01-Apr-22	10	26-May-22	07-Jun-22	-31	0%																												
	CBA-BPC42K.30	BP - Airlift, Cage Install and Concrete	02-Apr-22	08-Apr-22	5	08-Jun-22	13-Jun-22	91	0%																												
	CBA-BPC43J.10	BP - Excavation	28-Apr-22	05-May-22	52	13-Apr-22 A	18-Jun-22	37	0%																												
ID: 2B2C-20220422_bw Data Date: 23-Apr-22 Print Date: 25-Apr-22_14:33 Page 4 of 21		<div><div></div>Planned Bar</div> <div><div></div>Critical Bar</div> <div><div></div>Baseline</div>		<div><div></div>Milestone</div> <div><div></div>Critical MS</div> <div><div></div>Baseline MS</div>		West Kowloon Cultural District Authority Piling for Integrated Basement and U/G Road in Zone 2B 2C 3 Month Rolling Programme as of 22 Apr 2022 Based on CMWP Rev.0						<div>VIBRO</div> <div></div> <div></div>				Date 4-Mar-22		Revision Rev.0	Checked KL	Approved B																	

Activity ID		Activity Name	CMWP Rev.0 Start	CMWP Rev.0 Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete																												
										April					May					June					July												
										25	01	08	15	22	29	06	13	20	27	03	10	17	24	01	08	15	22										
	CBA-BPC43J.20	BP - RCD Drilling	06-May-22	18-May-22	10	20-Jun-22	30-Jun-22	37	0%																												
	CBA-BPC43J.30	BP - Airlift, Cage Install and Concrete	19-May-22	24-May-22	5	02-Jul-22	07-Jul-22	60	0%																												
	CBA-BPC43K.10	BP - Excavation	31-Jan-22	09-Feb-22	6	23-Apr-22	29-Apr-22	-31	0%																												
	CBA-BPC43K.20	BP - RCD Drilling	10-Feb-22	21-Feb-22	10	30-Apr-22	13-May-22	-31	0%																												
	CBA-BPC43K.30	BP - Airlift, Cage Install and Concrete	22-Feb-22	26-Feb-22	5	14-May-22	19-May-22	101	0%																												
	CBA-BPC44K.10	BP - Excavation	25-Mar-22	01-Apr-22	17	07-Mar-22 A	26-Mar-22 A		100%																												
	CBA-BPC44K.20	BP - RCD Drilling	02-Apr-22	22-Apr-22	3	28-Mar-22 A	31-Mar-22 A		100%																												
	CBA-BPC44K.30	BP - Airlift, Cage Install and Concrete	23-Apr-22	29-Apr-22	7	01-Apr-22 A	11-Apr-22 A		100%																												
	P17-BP01.10	BP - Excavation	30-Apr-22	07-May-22	6	06-Jun-22	11-Jun-22	31	0%																												
	P17-BP01.20	BP - RCD Drilling	10-May-22	26-May-22	15	13-Jun-22	29-Jun-22	31	0%																												
	P17-BP01.30	BP - Airlift, Cage Install and Concrete	27-May-22	04-Jun-22	7	30-Jun-22	08-Jul-22	54	0%																												
	P17-BP02.10	BP - Excavation	11-Mar-22	17-Mar-22	6	12-Jul-22	18-Jul-22	-35	0%																												
	P17-BP02.20	BP - RCD Drilling	18-Mar-22	04-Apr-22	15	19-Jul-22	04-Aug-22	-35	0%																												
	P17-BP03.10	BP - Excavation	24-Nov-21	30-Nov-21	6	23-Apr-22	29-Apr-22	-35	0%																												
	P17-BP03.20	BP - RCD Drilling	01-Dec-21	17-Dec-21	15	30-Apr-22	19-May-22	-35	0%																												
	P17-BP03.30	BP - Airlift, Cage Install and Concrete	18-Dec-21	28-Dec-21	7	20-May-22	27-May-22	97	0%																												
	P17-BP05.10	BP - Excavation	06-Jan-22	12-Jan-22	6	23-Apr-22	29-Apr-22	-9	0%																												
	P17-BP05.20	BP - RCD Drilling	13-Jan-22	29-Jan-22	15	30-Apr-22	19-May-22	-9	0%																												
	P17-BP05.30	BP - Airlift, Cage Install and Concrete	31-Jan-22	10-Feb-22	7	20-May-22	27-May-22	104	0%																												
	P17-BP07.10	BP - Excavation	15-Jul-22	21-Jul-22	6	15-Jul-22	21-Jul-22	0	0%																												
	P17-BP07.20	BP - RCD Drilling	22-Jul-22	08-Aug-22	15	22-Jul-22	08-Aug-22	0	0%																												
	P17-BP09.10	BP - Excavation	20-May-22	26-May-22	6	23-Jun-22	29-Jun-22	31	0%																												
	P17-BP09.20	BP - RCD Drilling	27-May-22	18-Jun-22	19	30-Jun-22	22-Jul-22	31	0%																												
	P17-BP10.10	BP - Excavation	10-Jan-22	15-Jan-22	10	28-Mar-22 A	09-Apr-22 A		100%																												
	P17-BP10.20	BP - RCD Drilling	17-Jan-22	05-Feb-22	4	11-Apr-22 A	19-Apr-22 A		100%																												
	P17-BP10.30	BP - Airlift, Cage Install and Concrete	07-Feb-22	14-Feb-22	10	20-Apr-22 A	30-Apr-22	125	0%																												
	P17-BP12.10	BP - Excavation	20-Dec-21	28-Dec-21	6	13-May-22	19-May-22	-35	0%																												
	P17-BP12.20	BP - RCD Drilling	29-Dec-21	15-Jan-22	15	20-May-22	07-Jun-22	-35	0%																												
	P17-BP12.30	BP - Airlift, Cage Install and Concrete	17-Jan-22	24-Jan-22	7	08-Jun-22	15-Jun-22	89	0%																												
	P17-BP14.10	BP - Excavation	27-Jan-22	05-Feb-22	6	31-May-22	07-Jun-22	-35	0%																												
	P17-BP14.20	BP - RCD Drilling	07-Feb-22	28-Feb-22	19	08-Jun-22	29-Jun-22	-35	0%																												
	P17-BP14.30	BP - Airlift, Cage Install and Concrete	01-Mar-22	09-Mar-22	8	30-Jun-22	09-Jul-22	20	0%																												

ID: 2B2C-20220422_bw Data Date: 23-Apr-22 Print Date: 25-Apr-22_14:33 Page 5 of 21	 Planned Bar	 Critical Bar	 Baseline	 Milestone	 Critical MS	 Baseline MS					
	<div>West Kowloon Cultural District Authority</div> <div>Piling for Integrated Basement and U/G Road in Zone 2B 2C</div> <div>3 Month Rolling Programme as of 22 Apr 2022</div> <div>Based on CMWP Rev.0</div>						  	<div>Date</div> <div>4-Mar-22</div>	<div>Revision</div> <div>Rev.0</div>	<div>Checked</div> <div>KL</div>	<div>Approved</div> <div>B</div>

Activity ID		Activity Name	CMWP Rev.0 Start	CMWP Rev.0 Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	April 1							May 2							June 3							July 4																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																												
										25	01	08	15	22	29	06	13	20	27	03	10	17	24	01	08	15	22	29	06	13	20	27	03	10	17	24	01	08	15	22																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																			
	P17-BP15.10	BP - Excavation	27-Jun-22	04-Jul-22	6	27-Jun-22	04-Jul-22	0	0%																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																		

Activity ID		Activity Name	CMWP Rev.0 Start	CMWP Rev.0 Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete																												
										April 1							May 2					June 3				July 4											
										25	01	08	15	22	29	06	13	20	27	03	10	17	24	01	08	15	22										
<div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div>																																					

ID: 2B2C-20220422_bw Data Date: 23-Apr-22 Print Date: 25-Apr-22_14:33 Page 8 of 21	 Planned Bar  Critical Bar  Baseline  Milestone  Critical MS  Baseline MS	<p align="center"> West Kowloon Cultural District Authority Piling for Integrated Basement and U/G Road in Zone 2B 2C 3 Month Rolling Programme as of 22 Apr 2022 Based on CMWP Rev.0 </p>	  	Date	Revision	Checked	Approved
				4-Mar-22	Rev.0	KL	B

Activity ID		Activity Name	CMWP Rev.0 Start	CMWP Rev.0 Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete																												
										April 1							May 2							June 3							July 4						
										25	01	08	15	22	29	06	13	20	27	03	10	17	24	01	08	15	22										
	P23-BP07.20	BP - RCD Drilling	22-Jun-22	14-Jul-22	19	22-Jun-22	14-Jul-22	22	0%																												
	P23-BP07.30	BP - Airlift, Cage Install and Concrete	15-Jul-22	23-Jul-22	8	15-Jul-22	23-Jul-22	137	0%																												
	P23-BP10.20	BP - RCD Drilling	23-Dec-21	17-Jan-22	14	17-Mar-22 A	02-Apr-22 A		100%																												
	P23-BP10.30	BP - Airlift, Cage Install and Concrete	18-Jan-22	26-Jan-22	8	23-Apr-22	03-May-22	236	0%																												
	P23-BP12.10	BP - Excavation	29-Jun-22	06-Jul-22	6	22-Jun-22	28-Jun-22	35	0%																												
	P23-BP12.20	BP - RCD Drilling	07-Jul-22	28-Jul-22	19	29-Jun-22	21-Jul-22	35	0%																												
	P23-BP12.30	BP - Airlift, Cage Install and Concrete	29-Jul-22	06-Aug-22	8	22-Jul-22	30-Jul-22	179	0%																												
	P23-BP13.10	BP - Excavation	09-Jan-23	14-Jan-23	14	11-Apr-22 A	29-Apr-22	232	0%																												
	P23-BP13.20	BP - RCD Drilling	16-Jan-23	04-Feb-23	15	30-Apr-22	19-May-22	232	0%																												
	P23-BP13.30	BP - Airlift, Cage Install and Concrete	06-Feb-23	13-Feb-23	7	20-May-22	27-May-22	232	0%																												
	P23-BP14.10	BP - Excavation	16-Jun-22	22-Jun-22	6	22-Jun-22	28-Jun-22	64	0%																												
	P23-BP14.20	BP - RCD Drilling	23-Jun-22	15-Jul-22	19	29-Jun-22	21-Jul-22	64	0%																												
	P23-BP14.30	BP - Airlift, Cage Install and Concrete	16-Jul-22	25-Jul-22	8	22-Jul-22	30-Jul-22	155	0%																												
	P23-BP15.10	BP - Excavation	05-Feb-22	11-Feb-22	6	18-May-22	24-May-22	64	0%																												
	P23-BP15.20	BP - RCD Drilling	12-Feb-22	17-Mar-22	29	25-May-22	28-Jun-22	64	0%																												
	P23-BP15.30	BP - Airlift, Cage Install and Concrete	18-Mar-22	26-Mar-22	8	29-Jun-22	08-Jul-22	198	0%																												
	P23-BP17.30	BP - Airlift, Cage Install and Concrete	11-Apr-22	22-Apr-22	13	08-Mar-22 A	23-Mar-22 A		100%																												
	P23-BP18.10	BP - Excavation	27-Sep-22	05-Oct-22	11	26-Mar-22 A	09-Apr-22 A		100%																												
	P23-BP18.20	BP - RCD Drilling	06-Oct-22	27-Oct-22	27	11-Apr-22 A	17-May-22	233	0%																												
	P23-BP18.30	BP - Airlift, Cage Install and Concrete	28-Oct-22	05-Nov-22	8	18-May-22	26-May-22	233	0%																												
	P23-BP25.10	BP - Excavation	11-Jan-22	17-Jan-22	6	23-Apr-22	29-Apr-22	64	0%																												
	P23-BP25.20	BP - RCD Drilling	18-Jan-22	11-Feb-22	19	30-Apr-22	24-May-22	64	0%																												
	P23-BP25.30	BP - Airlift, Cage Install and Concrete	12-Feb-22	21-Feb-22	8	25-May-22	02-Jun-22	219	0%																												
	P23-BP26.10	BP - Excavation	09-Jul-22	15-Jul-22	6	15-Jul-22	21-Jul-22	64	0%																												
	P23-BP26.20	BP - RCD Drilling	16-Jul-22	18-Aug-22	29	22-Jul-22	24-Aug-22	64	0%																												
	P24&27-BP06.10	BP - Excavation	08-Jul-22	14-Jul-22	6	08-Jul-22	14-Jul-22	51	0%																												
	P24&27-BP06.20	BP - RCD Drilling	15-Jul-22	17-Aug-22	29	15-Jul-22	17-Aug-22	51	0%																												
	P24&27-BP09.10	BP - Excavation	23-Jul-22	29-Jul-22	6	04-Jul-22	09-Jul-22	54	0%																												
	P24&27-BP09.20	BP - RCD Drilling	30-Jul-22	01-Sep-22	29	11-Jul-22	12-Aug-22	54	0%																												
	P24&27-BP27.10	BP - Excavation	24-Feb-22	02-Mar-22	6	30-May-22	06-Jun-22	-55	0%																												
	P24&27-BP27.20	BP - RCD Drilling	03-Mar-22	24-Mar-22	19	07-Jun-22	28-Jun-22	-55	0%																												
	P24&27-BP27.30	BP - Airlift, Cage Install and Concrete	25-Mar-22	02-Apr-22	8	29-Jun-22	08-Jul-22	134	0%																												
P24&27-BP28.10	BP - Excavation	18-Mar-22	24-Mar-22	6	22-Jun-22	28-Jun-22	-55	0%																													

ID: 2B2C-20220422_bw Data Date: 23-Apr-22 Print Date: 25-Apr-22_14:33 Page 9 of 21	<div></div> Planned Bar	<div></div> Milestone	<div>West Kowloon Cultural District Authority</div> <div>Piling for Integrated Basement and U/G Road in Zone 2B 2C</div> <div>3 Month Rolling Programme as of 22 Apr 2022</div> <div>Based on CMWP Rev.0</div>			<div>VIBRO</div> <div></div> <div></div>	Date	Revision	Checked	Approved
	<div></div> Critical Bar	<div></div> Critical MS					4-Mar-22	Rev.0	KL	B
	<div></div> Baseline	<div></div> Baseline MS								

Activity ID		Activity Name	CMWP Rev.0 Start	CMWP Rev.0 Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete																													
										April 1							May 2							June 3							July 4							
										25	01	08	15	22	29	06	13	20	27	03	10	17	24	01	08	15	22											
KD07 (Section 3)																																						
Trial Pile (P30-BP76)																																						
P30-BP76.10		BP (Trial Pile for Schedule 1) - Excavation	29-Dec-21	05-Jan-22	53	17-Jan-22 A	23-Mar-22 A		100%																													
P30-BP76.20		BP (Trial Pile for Schedule 1) - RCD Drilling	06-Jan-22	01-Mar-22	66	24-Mar-22 A	16-Jun-22	-66	0%																													
P30-BP76.30		BP (Trial Pile for Schedule 1) - Airlift, Cage Install and Concrete	02-Mar-22	11-Mar-22	9	17-Jun-22	27-Jun-22	-66	0%																													
Trial Pile (P24&P27-BP34)																																						
P24&27-BP34.30		BP (Trial Pile for Schedule 2) - Airlift, Cage Install and Concrete	19-Feb-22	28-Feb-22	8	19-Mar-22 A	29-Mar-22 A		100%																													
Bored Piles																																						
CBA-BPC52Ka.10		BP - Excavation	05-Oct-22	11-Oct-22	30	22-Mar-22 A	29-Apr-22	309	0%																													
CBA-BPC52Ka.20		BP - RCD Drilling	12-Oct-22	16-Nov-22	31	30-Apr-22	08-Jun-22	309	0%																													
CBA-BPC52Ka.30		BP - Airlift, Cage Install and Concrete	17-Nov-22	23-Nov-22	6	09-Jun-22	15-Jun-22	309	0%																													
P24&27-BP01.10		BP - Excavation	26-Aug-22	01-Sep-22	96	19-Apr-22 A	12-Aug-22	54	0%																													
P24&27-BP08.10		BP - Excavation	12-Feb-22	18-Feb-22	6	23-Apr-22	29-Apr-22	129	0%																													
P24&27-BP08.20		BP - RCD Drilling	19-Feb-22	24-Mar-22	29	30-Apr-22	06-Jun-22	129	0%																													
P24&27-BP08.30		BP - Airlift, Cage Install and Concrete	25-Mar-22	02-Apr-22	8	07-Jun-22	15-Jun-22	309	0%																													
P24&27-BP14.10		BP - Excavation	16-May-22	21-May-22	23	30-Mar-22 A	29-Apr-22	54	0%																													
P24&27-BP14.20		BP - RCD Drilling	23-May-22	14-Jun-22	19	30-Apr-22	24-May-22	54	0%																													
P24&27-BP14.30		BP - Airlift, Cage Install and Concrete	15-Jun-22	23-Jun-22	8	25-May-22	02-Jun-22	171	0%																													
P24&27-BP19.10		BP - Excavation	11-Apr-22	20-Apr-22	6	15-Jul-22	21-Jul-22	-55	0%																													
P24&27-BP19.20		BP - RCD Drilling	21-Apr-22	26-May-22	29	22-Jul-22	24-Aug-22	-55	0%																													
P24&27-BP25.10		BP - Excavation	18-Jan-22	24-Jan-22	6	23-Apr-22	29-Apr-22	-55	0%																													
P24&27-BP25.20		BP - RCD Drilling	25-Jan-22	02-Mar-22	29	30-Apr-22	06-Jun-22	-55	0%																													
P24&27-BP25.30		BP - Airlift, Cage Install and Concrete	03-Mar-22	11-Mar-22	8	07-Jun-22	15-Jun-22	145	0%																													
P26-BP01.10		BP - Excavation	16-May-22	21-May-22	6	05-Jul-22	11-Jul-22	129	0%																													

ID: 2B2C-20220422_bw Data Date: 23-Apr-22 Print Date: 25-Apr-22_14:33 Page 10 of 21	Planned Bar	Milestone	<div>West Kowloon Cultural District Authority</div> <div>Piling for Integrated Basement and U/G Road in Zone 2B 2C</div> <div>3 Month Rolling Programme as of 22 Apr 2022</div> <div>Based on CMWP Rev.0</div>					Date	Revision	Checked	Approved
	Critical Bar	Critical MS						4-Mar-22	Rev.0	KL	B
	Baseline	Baseline MS									

Activity ID		Activity Name	CMWP Rev.0 Start	CMWP Rev.0 Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete																		
										April 1						May 2				June 3				July 4			
										25	01	08	15	22	29	06	13	20	27	03	10	17	24	01	08	15	22
	P26-BP01.20	BP - RCD Drilling	23-May-22	14-Jul-22	44	12-Jul-22	31-Aug-22	129	0%																		
	P26-BP03.10	BP - Excavation	06-Apr-22	12-Apr-22	6	30-May-22	06-Jun-22	129	0%																		
	P26-BP03.20	BP - RCD Drilling	13-Apr-22	21-May-22	29	07-Jun-22	11-Jul-22	129	0%																		
	P26-BP03.30	BP - Airlift, Cage Install and Concrete	23-May-22	31-May-22	8	12-Jul-22	20-Jul-22	233	0%																		
	P26-BP06.10	BP - Excavation	22-Jul-22	28-Jul-22	6	15-Jul-22	21-Jul-22	35	0%																		
	P26-BP06.20	BP - RCD Drilling	29-Jul-22	31-Aug-22	29	22-Jul-22	24-Aug-22	35	0%																		
	P26-BP08.30	BP - Airlift, Cage Install and Concrete	20-Apr-22	28-Apr-22	17	14-Mar-22 A	02-Apr-22 A		100%																		
	P26-BP10.10	BP - Excavation	29-Sep-22	07-Oct-22	18	06-Apr-22 A	29-Apr-22	203	0%																		
	P26-BP10.20	BP - RCD Drilling	08-Oct-22	29-Oct-22	19	30-Apr-22	24-May-22	203	0%																		
	P26-BP10.30	BP - Airlift, Cage Install and Concrete	31-Oct-22	08-Nov-22	8	25-May-22	02-Jun-22	203	0%																		
	P26-BP11.10	BP - Excavation	19-May-22	25-May-22	6	30-May-22	06-Jun-22	35	0%																		
	P26-BP11.20	BP - RCD Drilling	26-May-22	17-Jun-22	19	07-Jun-22	28-Jun-22	35	0%																		
	P26-BP11.30	BP - Airlift, Cage Install and Concrete	18-Jun-22	27-Jun-22	8	29-Jun-22	08-Jul-22	290	0%																		
	P28&29-BP01.10	BP - Excavation	16-Mar-22	22-Mar-22	6	08-Jun-22	14-Jun-22	-65	0%																		
	P28&29-BP01.20	BP - RCD Drilling	23-Mar-22	09-Apr-22	15	15-Jun-22	02-Jul-22	-65	0%																		
	P28&29-BP01.30	BP - Airlift, Cage Install and Concrete	11-Apr-22	21-Apr-22	7	04-Jul-22	11-Jul-22	-9	0%																		
	P28&29-BP03.10	BP - Excavation	26-Feb-22	04-Mar-22	6	20-May-22	26-May-22	-65	0%																		
	P28&29-BP03.20	BP - RCD Drilling	05-Mar-22	22-Mar-22	15	27-May-22	14-Jun-22	-65	0%																		
	P28&29-BP03.30	BP - Airlift, Cage Install and Concrete	23-Mar-22	30-Mar-22	7	15-Jun-22	22-Jun-22	-1	0%																		
	P28&29-BP05.10	BP - Excavation	08-Jun-22	14-Jun-22	6	18-May-22	24-May-22	54	0%																		
	P28&29-BP05.20	BP - RCD Drilling	15-Jun-22	07-Jul-22	19	25-May-22	16-Jun-22	54	0%																		
	P28&29-BP05.30	BP - Airlift, Cage Install and Concrete	08-Jul-22	16-Jul-22	8	17-Jun-22	25-Jun-22	160	0%																		
	P28&29-BP09.10	BP - Excavation	30-Jun-22	07-Jul-22	6	10-Jun-22	16-Jun-22	54	0%																		
	P28&29-BP09.20	BP - RCD Drilling	08-Jul-22	29-Jul-22	19	17-Jun-22	09-Jul-22	54	0%																		
	P28&29-BP09.30	BP - Airlift, Cage Install and Concrete	30-Jul-22	08-Aug-22	8	11-Jul-22	19-Jul-22	149	0%																		
	P28&29-BP11.10	BP - Excavation	09-Feb-22	15-Feb-22	6	30-Apr-22	07-May-22	-65	0%																		
	P28&29-BP11.20	BP - RCD Drilling	16-Feb-22	04-Mar-22	15	10-May-22	26-May-22	-65	0%																		
	P28&29-BP11.30	BP - Airlift, Cage Install and Concrete	05-Mar-22	12-Mar-22	7	28-May-22	06-Jun-22	6	0%																		
	P28&29-BP13.10	BP - Excavation	25-Apr-22	30-Apr-22	6	14-Jul-22	20-Jul-22	-65	0%																		
	P28&29-BP13.20	BP - RCD Drilling	03-May-22	20-May-22	15	21-Jul-22	06-Aug-22	-65	0%																		
	P28&29-BP15.10	BP - Excavation	02-Apr-22	09-Apr-22	6	25-Jun-22	02-Jul-22	-65	0%																		
	P28&29-BP15.20	BP - RCD Drilling	11-Apr-22	30-Apr-22	15	04-Jul-22	20-Jul-22	-65	0%																		
	P28&29-BP15.30	BP - Airlift, Cage Install and Concrete	03-May-22	11-May-22	7	21-Jul-22	28-Jul-22	-17	0%																		
	P30-BP57.10	BP - Excavation	25-Oct-22	31-Oct-22	22	11-Mar-22 A	07-Apr-22 A		100%																		
ID: 2B2C-20220422_bw Data Date: 23-Apr-22 Print Date: 25-Apr-22_14:33 Page 11 of 21		<div>Planned Bar</div> <div>Critical Bar</div> <div>Baseline</div>	<div>Milestone</div> <div>Critical MS</div> <div>Baseline MS</div>	West Kowloon Cultural District Authority Piling for Integrated Basement and U/G Road in Zone 2B 2C 3 Month Rolling Programme as of 22 Apr 2022 Based on CMWP Rev.0				<div>VIBRO</div> <div>•</div> <div></div>				<div>Date</div> <div>4-Mar-22</div>	<div>Revision</div> <div>Rev.0</div>	<div>Checked</div> <div>KL</div>	<div>Approved</div> <div>B</div>												

Activity ID		Activity Name	CMWP Rev.0 Start	CMWP Rev.0 Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	Gantt Chart																	
										April 1					May 2					June 3				July 4			
										25	01	08	15	22	29	06	13	20	27	03	10	17	24	01	08	15	22
<div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div>	P30-BP57.20	BP - RCD Drilling	01-Nov-22	03-Dec-22	39	08-Apr-22 A	28-May-22	315	0%																		
	P30-BP57.30	BP - Airlift, Cage Install and Concrete	05-Dec-22	13-Dec-22	8	30-May-22	08-Jun-22	315	0%																		
	P30-BP59.10	BP - Excavation	23-Feb-22	01-Mar-22	91	06-Jan-22 A	29-Apr-22	-15	0%																		
	P30-BP59.20	BP - RCD Drilling	02-Mar-22	04-Apr-22	29	30-Apr-22	06-Jun-22	-15	0%																		
	P30-BP59.30	BP - Airlift, Cage Install and Concrete	06-Apr-22	14-Apr-22	8	07-Jun-22	15-Jun-22	177	0%																		
	P30-BP66.10	BP - Excavation	21-Mar-22	26-Mar-22	6	31-May-22	07-Jun-22	9	0%																		
	P30-BP66.20	BP - RCD Drilling	28-Mar-22	14-Apr-22	15	08-Jun-22	24-Jun-22	9	0%																		
	P30-BP66.30	BP - Airlift, Cage Install and Concrete	19-Apr-22	26-Apr-22	7	25-Jun-22	04-Jul-22	151	0%																		
	P30-BP67.20	BP - RCD Drilling	21-Sep-22	10-Oct-22	15	14-Mar-22 A	31-Mar-22 A		100%																		
	P30-BP67.30	BP - Airlift, Cage Install and Concrete	11-Oct-22	18-Oct-22	12	01-Apr-22 A	20-Apr-22 A		100%																		
	P30-BP72.10	BP - Excavation	04-Aug-22	10-Aug-22	54	07-Feb-22 A	12-Apr-22 A		100%																		
	P30-BP72.20	BP - RCD Drilling	11-Aug-22	27-Aug-22	21	13-Apr-22 A	12-May-22	120	0%																		
	P30-BP72.30	BP - Airlift, Cage Install and Concrete	29-Aug-22	05-Sep-22	7	13-May-22	20-May-22	322	0%																		
	P30-BP73.10	BP - Excavation	08-Apr-22	14-Apr-22	52	22-Apr-22 A	24-Jun-22	9	0%																		
	P30-BP73.20	BP - RCD Drilling	19-Apr-22	06-May-22	15	25-Jun-22	13-Jul-22	9	0%																		
	P30-BP73.30	BP - Airlift, Cage Install and Concrete	07-May-22	16-May-22	7	14-Jul-22	21-Jul-22	143	0%																		
	KD08 (Section 4)																										
	Bored Piles																										
		CBA-BPC52Va.10	BP - Excavation	23-Apr-22	29-Apr-22	6	06-May-22	13-May-22	-10	0%																	
		CBA-BPC52Va.20	BP - RCD Drilling	30-Apr-22	13-May-22	10	14-May-22	25-May-22	-10	0%																	
	CBA-BPC52Va.30	BP - Airlift, Cage Install and Concrete	14-May-22	19-May-22	5	26-May-22	31-May-22	138	0%																		
	P26-BP12.10	BP - Excavation	09-Apr-22	19-Apr-22	6	23-Apr-22	29-Apr-22	35	0%																		
	P26-BP12.20	BP - RCD Drilling	20-Apr-22	25-May-22	29	30-Apr-22	06-Jun-22	35	0%																		
	P26-BP12.30	BP - Airlift, Cage Install and Concrete	26-May-22	04-Jun-22	8	07-Jun-22	15-Jun-22	201	0%																		
	P26-BP15.10	BP - Excavation	19-May-22	25-May-22	6	31-May-22	07-Jun-22	-10	0%																		
	P26-BP15.20	BP - RCD Drilling	26-May-22	02-Jul-22	31	08-Jun-22	14-Jul-22	-10	0%																		
	P26-BP15.30	BP - Airlift, Cage Install and Concrete	04-Jul-22	09-Jul-22	6	15-Jul-22	21-Jul-22	107	0%																		
	P26-BP16.10	BP - Excavation	24-Jun-22	02-Jul-22	7	07-Jul-22	14-Jul-22	-10	0%																		
	P26-BP16.20	BP - RCD Drilling	04-Jul-22	19-Jul-22	14	15-Jul-22	30-Jul-22	-10	0%																		
	P30-BP02.10	BP - Excavation	23-Jun-22	29-Jun-22	6	28-Jun-22	05-Jul-22	31	0%																		
	P30-BP02.20	BP - RCD Drilling	30-Jun-22	18-Jul-22	15	06-Jul-22	22-Jul-22	31	0%																		

ID: 2B2C-20220422_bw Data Date: 23-Apr-22 Print Date: 25-Apr-22_14:33 Page 12 of 21	<div></div> Planned Bar	<div></div> Milestone	<div><div>West Kowloon Cultural District Authority</div><div>Piling for Integrated Basement and U/G Road in Zone 2B 2C</div><div>3 Month Rolling Programme as of 22 Apr 2022</div><div>Based on CMWP Rev.0</div></div>	<div><div>VIBRO</div><div></div><div></div></div>	Date	Revision	Checked	Approved
	<div></div> Critical Bar	<div></div> Critical MS			4-Mar-22	Rev.0	KL	B
	<div></div> Baseline	<div></div> Baseline MS						

Activity ID	Activity Name	CMWP Rev.0 Start	CMWP Rev.0 Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete		April					May				June				July																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																										
										1					2				3				4																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																										
									25	01	08	15	22	29	06	13	20	27	03	10	17	24	01	08	15	22																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																							
<div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div> <div></div>	P30-BP03.10	BP - Excavation	10-Mar-22	16-Mar-22	16	08-Apr-22 A	29-Apr-22	31	0%																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																								

Activity ID		Activity Name	CMWP Rev.0 Start	CMWP Rev.0 Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	Gantt Chart																
										April 1					May 2					June 3				July 4		
										25	01	08	15	22	29	06	13	20	27	03	10	17	24	01	08	15
<div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></</div></div>																										

Activity ID	Activity Name	CMWP Rev.0 Start	CMWP Rev.0 Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	Gantt Chart																
									April					May					June				July		
									1	2	3	4	1	2	3	4	1	2	3	4	1	2			
25	01	08	15	22	29	06	13	20	27	03	10	17	24	01	08	15	22								
KD09 (Section 5)	SHP-C52Xb-P1	Socketed Steel H Piling	15-Jun-22	24-Jun-22	9	28-Jun-22	08-Jul-22	78	0%																
	SHP-C52Xb-P2	Socketed Steel H Piling	20-Jun-22	29-Jun-22	9	04-Jul-22	13-Jul-22	78	0%																
	SHP-C52Xb-P3	Socketed Steel H Piling	24-Jun-22	05-Jul-22	9	08-Jul-22	18-Jul-22	78	0%																
	SHP-C52Xb-P4	Socketed Steel H Piling	29-Jun-22	09-Jul-22	12	22-Mar-22 A	06-Apr-22 A		100%																
	SHP-C52Xb-P5	Socketed Steel H Piling	05-Jul-22	14-Jul-22	9	19-Jul-22	28-Jul-22	78	0%																
	SHP-C52Xc-P4	Socketed Steel H Piling	28-Jul-22	06-Aug-22	15	13-Apr-22 A	04-May-22	169	0%																
	SHP-C53W-P4	Socketed Steel H Piling	25-Aug-22	03-Sep-22	16	12-Apr-22 A	04-May-22	194	0%																
	SHP-C53X-P4	Socketed Steel H Piling	23-Sep-22	05-Oct-22	12	25-Mar-22 A	09-Apr-22 A		100%																
	SHP-C53Xa-P3	Socketed Steel H Piling	27-Jun-22	07-Jul-22	9	27-Jun-22	07-Jul-22	75	0%																
	SHP-C53Xa-P4	Socketed Steel H Piling	02-Jul-22	12-Jul-22	10	30-Mar-22 A	12-Apr-22 A		100%																
	SHP-C53Xa-P5	Socketed Steel H Piling	07-Jul-22	16-Jul-22	9	08-Jul-22	18-Jul-22	75	0%																
	SHP-C53Xa-P6	Socketed Steel H Piling	12-Jul-22	21-Jul-22	9	13-Jul-22	22-Jul-22	75	0%																
	SHP-C54Wa-P4	Socketed Steel H Piling	05-Aug-22	15-Aug-22	18	09-Apr-22 A	04-May-22	162	0%																
	SHP-C54Xa-P4	Socketed Steel H Piling	02-Sep-22	13-Sep-22	20	07-Apr-22 A	04-May-22	486	0%																
	SHP-C54Xb-P4	Socketed Steel H Piling	03-Oct-22	13-Oct-22	12	04-Apr-22 A	22-Apr-22 A		100%																
	KD09 (Section 5)																								
	Trial Piles (P23-BP68)																								
	P23-BP68.30	BP (Trial Pile for Schedule 4) - Airlift, Cage Install and Concrete	27-Jan-22	08-Feb-22	8	22-Mar-22 A	31-Mar-22 A		100%																
Bored Piles																									
CBA-BPC40P.10	BP - Excavation	17-Jun-22	23-Jun-22	6	06-Jun-22	11-Jun-22	152	0%																	
CBA-BPC40P.20	BP - RCD Drilling	24-Jun-22	06-Jul-22	10	13-Jun-22	23-Jun-22	152	0%																	
CBA-BPC40P.30	BP - Airlift, Cage Install and Concrete	07-Jul-22	12-Jul-22	5	24-Jun-22	29-Jun-22	182	0%																	
CBA-BPC40Pa.10	BP - Excavation	02-Aug-22	08-Aug-22	6	21-Jul-22	27-Jul-22	152	0%																	
CBA-BPC40Q.10	BP - Excavation	28-Jun-22	06-Jul-22	7	16-Jun-22	23-Jun-22	152	0%																	
CBA-BPC40Q.20	BP - RCD Drilling	07-Jul-22	22-Jul-22	14	24-Jun-22	11-Jul-22	152	0%																	
CBA-BPC40Q.30	BP - Airlift, Cage Install and Concrete	23-Jul-22	29-Jul-22	6	12-Jul-22	18-Jul-22	173	0%																	
CBA-BPC40S.10	BP - Excavation	15-Jul-22	22-Jul-22	7	04-Jul-22	11-Jul-22	152	0%																	
CBA-BPC40S.20	BP - RCD Drilling	23-Jul-22	08-Aug-22	14	12-Jul-22	27-Jul-22	152	0%																	
CBA-BPC52U.10	BP - Excavation	06-May-22	13-May-22	6	19-May-22	25-May-22	-10	0%																	
CBA-BPC52U.20	BP - RCD Drilling	14-May-22	25-May-22	10	26-May-22	07-Jun-22	-10	0%																	
ID: 2B2C-20220422_bw Data Date: 23-Apr-22 Print Date: 25-Apr-22_14:33 Page 15 of 21		<div><div></div>Planned Bar</div> <div><div></div>Critical Bar</div> <div><div></div>Baseline</div>		<div><div></div>Milestone</div> <div><div></div>Critical MS</div> <div><div></div>Baseline MS</div>		West Kowloon Cultural District Authority Piling for Integrated Basement and U/G Road in Zone 2B 2C 3 Month Rolling Programme as of 22 Apr 2022 Based on CMWP Rev.0				<div>VIBRO</div> <div></div> <div></div>				<table><tr><td>Date</td><td>Revision</td><td>Checked</td><td>Approved</td></tr><tr><td>4-Mar-22</td><td>Rev.0</td><td>KL</td><td>B</td></tr></table>				Date	Revision	Checked	Approved	4-Mar-22	Rev.0	KL	B
Date	Revision	Checked	Approved																						
4-Mar-22	Rev.0	KL	B																						

Activity ID		Activity Name	CMWP Rev.0 Start	CMWP Rev.0 Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete																												
										April					May					June					July												
										25	01	08	15	22	29	06	13	20	27	03	10	17	24	01	08	15	22										
	CBA-BPC52U.30	BP - Airlift, Cage Install and Concrete	26-May-22	31-May-22	5	08-Jun-22	13-Jun-22	133	0%																												
	P18-BP16.10	BP - Excavation	20-Dec-21	28-Dec-21	6	13-May-22	19-May-22	-76	0%																												
	P18-BP16.20	BP - RCD Drilling	29-Dec-21	15-Jan-22	15	20-May-22	07-Jun-22	-76	0%																												
	P18-BP16.30	BP - Airlift, Cage Install and Concrete	17-Jan-22	24-Jan-22	7	08-Jun-22	15-Jun-22	3	0%																												
	P18-BP19.10	BP - Excavation	16-Jul-22	22-Jul-22	6	16-Jul-22	22-Jul-22	140	0%																												
	P18-BP21.10	BP - Excavation	27-Jan-22	05-Feb-22	6	18-Jun-22	24-Jun-22	-76	0%																												
	P18-BP21.20	BP - RCD Drilling	07-Feb-22	23-Feb-22	15	25-Jun-22	13-Jul-22	-76	0%																												
	P18-BP21.30	BP - Airlift, Cage Install and Concrete	24-Feb-22	03-Mar-22	7	14-Jul-22	21-Jul-22	-13	0%																												
	P18-BP23.10	BP - Excavation	10-Jan-22	15-Jan-22	6	31-May-22	07-Jun-22	-76	0%																												
	P18-BP23.20	BP - RCD Drilling	17-Jan-22	05-Feb-22	15	08-Jun-22	24-Jun-22	-76	0%																												
	P18-BP23.30	BP - Airlift, Cage Install and Concrete	07-Feb-22	14-Feb-22	7	25-Jun-22	04-Jul-22	-5	0%																												
	P18-BP27.10	BP - Excavation	18-May-22	24-May-22	6	18-May-22	24-May-22	140	0%																												
	P18-BP27.20	BP - RCD Drilling	25-May-22	11-Jun-22	15	25-May-22	11-Jun-22	140	0%																												
	P18-BP27.30	BP - Airlift, Cage Install and Concrete	13-Jun-22	20-Jun-22	7	13-Jun-22	20-Jun-22	182	0%																												
	P18-BP28.10	BP - Excavation	11-Mar-22	17-Mar-22	6	12-Jul-22	18-Jul-22	-22	0%																												
	P18-BP28.20	BP - RCD Drilling	18-Mar-22	04-Apr-22	15	19-Jul-22	04-Aug-22	-22	0%																												
	P18-BP33.10	BP - Excavation	22-Feb-22	28-Feb-22	6	23-Jun-22	29-Jun-22	-22	0%																												
	P18-BP33.20	BP - RCD Drilling	01-Mar-22	17-Mar-22	15	30-Jun-22	18-Jul-22	-22	0%																												
	P18-BP33.30	BP - Airlift, Cage Install and Concrete	18-Mar-22	25-Mar-22	7	19-Jul-22	26-Jul-22	93	0%																												
	P18-BP35.10	BP - Excavation	28-Jun-22	05-Jul-22	6	28-Jun-22	05-Jul-22	140	0%																												
	P18-BP35.20	BP - RCD Drilling	06-Jul-22	22-Jul-22	15	06-Jul-22	22-Jul-22	140	0%																												
	P18-BP36.10	BP - Excavation	20-Dec-21	28-Dec-21	6	23-Apr-22	29-Apr-22	-22	0%																												
	P18-BP36.20	BP - RCD Drilling	29-Dec-21	15-Jan-22	15	30-Apr-22	19-May-22	-22	0%																												
	P18-BP36.30	BP - Airlift, Cage Install and Concrete	17-Jan-22	24-Jan-22	7	20-May-22	27-May-22	120	0%																												
	P18-BP37.10	BP - Excavation	06-Jun-22	11-Jun-22	6	06-Jun-22	11-Jun-22	140	0%																												
	P18-BP37.20	BP - RCD Drilling	13-Jun-22	05-Jul-22	19	13-Jun-22	05-Jul-22	140	0%																												
	P18-BP37.30	BP - Airlift, Cage Install and Concrete	06-Jul-22	14-Jul-22	8	06-Jul-22	14-Jul-22	170	0%																												
	P18-BP38.10	BP - Excavation	27-Jan-22	05-Feb-22	6	31-May-22	07-Jun-22	-22	0%																												
	P18-BP38.20	BP - RCD Drilling	07-Feb-22	28-Feb-22	19	08-Jun-22	29-Jun-22	-22	0%																												
	P18-BP38.30	BP - Airlift, Cage Install and Concrete	01-Mar-22	09-Mar-22	8	30-Jun-22	09-Jul-22	100	0%																												
	P18-BP40.10	BP - Excavation	10-Jan-22	15-Jan-22	6	13-May-22	19-May-22	-22	0%																												
	P18-BP40.20	BP - RCD Drilling	17-Jan-22	05-Feb-22	15	20-May-22	07-Jun-22	-22	0%																												
	P18-BP40.30	BP - Airlift, Cage Install and Concrete	07-Feb-22	14-Feb-22	7	08-Jun-22	15-Jun-22	112	0%																												
	P18-BP48.10	BP - Excavation	20-Dec-21	28-Dec-21	6	23-Apr-22	29-Apr-22	7	0%																												
	P18-BP48.20	BP - RCD Drilling	29-Dec-21	15-Jan-22	15	30-Apr-22	19-May-22	7	0%																												
	P18-BP48.30	BP - Airlift, Cage Install and Concrete	17-Jan-22	24-Jan-22	7	20-May-22	27-May-22	137	0%																												
	P18-BP60.10	BP - Excavation	10-Jan-22	15-Jan-22	6	13-May-22	19-May-22	7	0%																												
ID: 2B2C-20220422_bw Data Date: 23-Apr-22 Print Date: 25-Apr-22_14:33 Page 16 of 21		<div><div></div>Planned Bar</div> <div><div></div>Critical Bar</div> <div><div></div>Baseline</div>		<div><div></div>Milestone</div> <div><div></div>Critical MS</div> <div><div></div>Baseline MS</div>		West Kowloon Cultural District Authority Piling for Integrated Basement and U/G Road in Zone 2B 2C 3 Month Rolling Programme as of 22 Apr 2022 Based on CMWP Rev.0						<div><div>VIBRO</div><div></div><div></div></div>				Date		Revision		Checked		Approved															
																4-Mar-22		Rev.0		KL		B															

Activity ID		Activity Name	CMWP Rev.0 Start	CMWP Rev.0 Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete																
										April					May					June				July	
										1	2	3	4	1	2	3	4	1	2	3	4	1	2		
			25	01	08	15	22	29	06	13	20	27	03	10	17	24	01	08	15	22					
<div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><</div>																									

Activity ID		Activity Name	CMWP Rev.0 Start	CMWP Rev.0 Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete																													
										April							May							June							July							
										25	01	08	15	22	29	06	13	20	27	03	10	17	24	01	08	15	22											
		P23-BP115.30	BP - Airlift, Cage Install and Concrete	05-Feb-22	14-Feb-22	9	07-Apr-22 A	21-Apr-22 A		100%																												
		P23-BP33.10	BP - Excavation	11-Jun-22	17-Jun-22	25	04-Mar-22 A	02-Apr-22 A		100%																												
		P23-BP33.20	BP - RCD Drilling	18-Jun-22	06-Jul-22	11	04-Apr-22 A	21-Apr-22 A		100%																												
		P23-BP33.30	BP - Airlift, Cage Install and Concrete	07-Jul-22	14-Jul-22	8	22-Apr-22 A	30-Apr-22	253	0%																												
		P23-BP37.10	BP - Excavation	21-Dec-21	29-Dec-21	6	23-Apr-22	29-Apr-22	1	0%																												
		P23-BP37.20	BP - RCD Drilling	30-Dec-21	05-Feb-22	29	30-Apr-22	06-Jun-22	1	0%																												
		P23-BP37.30	BP - Airlift, Cage Install and Concrete	07-Feb-22	15-Feb-22	8	07-Jun-22	15-Jun-22	209	0%																												
		P23-BP39.10	BP - Excavation	05-Mar-22	11-Mar-22	10	18-Mar-22 A	30-Mar-22 A		100%																												
		P23-BP39.20	BP - RCD Drilling	12-Mar-22	02-Apr-22	7	31-Mar-22 A	09-Apr-22 A		100%																												
		P23-BP39.30	BP - Airlift, Cage Install and Concrete	04-Apr-22	13-Apr-22	16	11-Apr-22 A	03-May-22	252	0%																												
		P23-BP40.10	BP - Excavation	23-Feb-22	01-Mar-22	6	06-Jun-22	11-Jun-22	198	0%																												
		P23-BP40.20	BP - RCD Drilling	02-Mar-22	18-Mar-22	15	13-Jun-22	29-Jun-22	198	0%																												
		P23-BP40.30	BP - Airlift, Cage Install and Concrete	19-Mar-22	26-Mar-22	7	30-Jun-22	08-Jul-22	198	0%																												
		P23-BP41.10	BP - Excavation	13-Jun-22	18-Jun-22	12	13-Apr-22 A	29-Apr-22	232	0%																												
		P23-BP41.20	BP - RCD Drilling	20-Jun-22	07-Jul-22	15	30-Apr-22	19-May-22	232	0%																												
		P23-BP41.30	BP - Airlift, Cage Install and Concrete	08-Jul-22	15-Jul-22	7	20-May-22	27-May-22	232	0%																												
		P23-BP42.30	BP - Airlift, Cage Install and Concrete	26-Jul-22	02-Aug-22	15	18-Mar-22 A	06-Apr-22 A		100%																												
		P23-BP48.10	BP - Excavation	27-Jan-22	05-Feb-22	6	30-May-22	06-Jun-22	1	0%																												
		P23-BP48.20	BP - RCD Drilling	07-Feb-22	11-Mar-22	29	07-Jun-22	11-Jul-22	1	0%																												
		P23-BP48.30	BP - Airlift, Cage Install and Concrete	12-Mar-22	21-Mar-22	8	12-Jul-22	20-Jul-22	188	0%																												
		P23-BP50.10	BP - Excavation	28-Mar-22	02-Apr-22	6	05-Jul-22	11-Jul-22	1	0%																												
		P23-BP50.20	BP - RCD Drilling	04-Apr-22	29-Apr-22	19	12-Jul-22	02-Aug-22	1	0%																												
		P23-BP52.10	BP - Excavation	20-May-22	26-May-22	6	23-Apr-22	29-Apr-22	85	0%																												
		P23-BP52.20	BP - RCD Drilling	27-May-22	18-Jun-22	19	30-Apr-22	24-May-22	85	0%																												
		P23-BP52.30	BP - Airlift, Cage Install and Concrete	20-Jun-22	28-Jun-22	8	25-May-22	02-Jun-22	92	0%																												
		P23-BP53.10	BP - Excavation	28-Jan-22	07-Feb-22	6	13-May-22	19-May-22	198	0%																												
		P23-BP53.20	BP - RCD Drilling	08-Feb-22	01-Mar-22	19	20-May-22	11-Jun-22	198	0%																												
		P23-BP53.30	BP - Airlift, Cage Install and Concrete	02-Mar-22	10-Mar-22	8	13-Jun-22	21-Jun-22	205	0%																												
		P23-BP54.30	BP - Airlift, Cage Install and Concrete	17-Aug-22	25-Aug-22	18	12-Mar-22 A	02-Apr-22 A		100%																												
ID: 2B2C-20220422_bw Data Date: 23-Apr-22 Print Date: 25-Apr-22_14:33 Page 18 of 21		<div><div></div>Planned Bar</div> <div><div></div>Critical Bar</div> <div><div></div>Baseline</div>		<div><div></div>Milestone</div> <div><div></div>Critical MS</div> <div><div></div>Baseline MS</div>		West Kowloon Cultural District Authority Piling for Integrated Basement and U/G Road in Zone 2B 2C 3 Month Rolling Programme as of 22 Apr 2022 Based on CMWP Rev.0						<div><div>VIBRO</div><div></div><div></div></div>			<div><div>Date</div>4-Mar-22</div> <div><div>Revision</div>Rev.0</div> <div><div>Checked</div>KL</div> <div><div>Approved</div>B</div>																							

Activity ID		Activity Name	CMWP Rev.0 Start	CMWP Rev.0 Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete																		
										April 1						May 2					June 3				July 4		
										25	01	08	15	22	29	06	13	20	27	03	10	17	24	01	08	15	22
	P23-BP57.10	BP - Excavation	14-Jun-22	20-Jun-22	7	22-Apr-22 A	29-Apr-22	217	0%																		
	P23-BP57.20	BP - RCD Drilling	21-Jun-22	25-Jul-22	29	30-Apr-22	06-Jun-22	217	0%																		
	P23-BP57.30	BP - Airlift, Cage Install and Concrete	26-Jul-22	03-Aug-22	8	07-Jun-22	15-Jun-22	217	0%																		
	P23-BP58.10	BP - Excavation	28-May-22	04-Jun-22	6	15-Jul-22	21-Jul-22	25	0%																		
	P23-BP58.20	BP - RCD Drilling	06-Jun-22	09-Jul-22	29	22-Jul-22	24-Aug-22	25	0%																		
	P23-BP60.10	BP - Excavation	15-Jul-22	21-Jul-22	10	19-Apr-22 A	29-Apr-22	217	0%																		
	P23-BP60.20	BP - RCD Drilling	22-Jul-22	24-Aug-22	29	30-Apr-22	06-Jun-22	217	0%																		
	P23-BP60.30	BP - Airlift, Cage Install and Concrete	25-Aug-22	02-Sep-22	8	07-Jun-22	15-Jun-22	217	0%																		
	P23-BP62.10	BP - Excavation	20-May-22	26-May-22	19	04-Apr-22 A	29-Apr-22	227	0%																		
	P23-BP62.20	BP - RCD Drilling	27-May-22	18-Jun-22	19	30-Apr-22	24-May-22	227	0%																		
	P23-BP62.30	BP - Airlift, Cage Install and Concrete	20-Jun-22	28-Jun-22	8	25-May-22	02-Jun-22	227	0%																		
	P23-BP63.30	BP - Airlift, Cage Install and Concrete	27-May-22	06-Jun-22	32	23-Feb-22 A	01-Apr-22 A		100%																		
	P23-BP64.10	BP - Excavation	26-Apr-22	03-May-22	18	06-Apr-22 A	29-Apr-22	227	0%																		
	P23-BP64.20	BP - RCD Drilling	04-May-22	26-May-22	19	30-Apr-22	24-May-22	227	0%																		
	P23-BP64.30	BP - Airlift, Cage Install and Concrete	27-May-22	06-Jun-22	8	25-May-22	02-Jun-22	227	0%																		
	P23-BP67.10	BP - Excavation	19-Jul-22	25-Jul-22	6	10-Jun-22	16-Jun-22	122	0%																		
	P23-BP67.20	BP - RCD Drilling	26-Jul-22	27-Aug-22	29	17-Jun-22	21-Jul-22	122	0%																		
	P23-BP67.30	BP - Airlift, Cage Install and Concrete	29-Aug-22	06-Sep-22	8	22-Jul-22	30-Jul-22	155	0%																		
	P23-BP70.10	BP - Excavation	30-Nov-22	06-Dec-22	20	19-Mar-22 A	13-Apr-22 A		100%																		
	P23-BP70.20	BP - RCD Drilling	07-Dec-22	12-Jan-23	34	14-Apr-22 A	28-May-22	223	0%																		
	P23-BP70.30	BP - Airlift, Cage Install and Concrete	13-Jan-23	21-Jan-23	8	30-May-22	08-Jun-22	223	0%																		
	P23-BP71.10	BP - Excavation	04-Mar-22	10-Mar-22	6	23-Apr-22	29-Apr-22	47	0%																		
	P23-BP71.20	BP - RCD Drilling	11-Mar-22	14-Apr-22	29	30-Apr-22	06-Jun-22	47	0%																		
	P23-BP71.30	BP - Airlift, Cage Install and Concrete	19-Apr-22	27-Apr-22	8	07-Jun-22	15-Jun-22	168	0%																		
	P23-BP73.10	BP - Excavation	21-Feb-22	26-Feb-22	6	02-Jul-22	08-Jul-22	94	0%																		
	P23-BP73.20	BP - RCD Drilling	28-Feb-22	21-Mar-22	19	09-Jul-22	30-Jul-22	94	0%																		
	P23-BP74.10	BP - Excavation	04-Mar-22	10-Mar-22	6	21-Jun-22	27-Jun-22	36	0%																		
	P23-BP74.20	BP - RCD Drilling	11-Mar-22	01-Apr-22	19	28-Jun-22	20-Jul-22	36	0%																		
	P23-BP74.30	BP - Airlift, Cage Install and Concrete	02-Apr-22	12-Apr-22	8	21-Jul-22	29-Jul-22	132	0%																		
	P23-BP75.10	BP - Excavation	26-Jan-22	04-Feb-22	6	09-Jun-22	15-Jun-22	94	0%																		
P23-BP75.20	BP - RCD Drilling	05-Feb-22	26-Feb-22	19	16-Jun-22	08-Jul-22	94	0%																			
P23-BP75.30	BP - Airlift, Cage Install and Concrete	28-Feb-22	08-Mar-22	8	09-Jul-22	18-Jul-22	158	0%																			

ID: 2B2C-20220422_bw Data Date: 23-Apr-22 Print Date: 25-Apr-22_14:33 Page 19 of 21	<div></div> Planned Bar	<div></div> Milestone	<div>West Kowloon Cultural District Authority</div> <div>Piling for Integrated Basement and U/G Road in Zone 2B 2C</div> <div>3 Month Rolling Programme as of 22 Apr 2022</div> <div>Based on CMWP Rev.0</div>			<div>VIBRO</div> <div></div> <div></div>	Date	Revision	Checked	Approved
	<div></div> Critical Bar	<div></div> Critical MS					4-Mar-22	Rev.0	KL	B
	<div></div> Baseline	<div></div> Baseline MS								

ID: 2B2C-20220422_bw Data Date: 23-Apr-22 Print Date: 25-Apr-22_14:33 Page 20 of 21	<div><div></div>Planned Bar</div> <div><div></div>Critical Bar</div> <div><div></div>Baseline</div>	<div><div></div>Milestone</div> <div><div></div>Critical MS</div> <div><div></div>Baseline MS</div>	<div>West Kowloon Cultural District Authority</div> <div>Piling for Integrated Basement and U/G Road in Zone 2B 2C</div> <div>3 Month Rolling Programme as of 22 Apr 2022</div> <div>Based on CMWP Rev.0</div>	<div>VIBRO</div> <div></div> <div></div>	<div>Date</div> <div>4-Mar-22</div>	<div>Revision</div> <div>Rev.0</div>	<div>Checked</div> <div>KL</div>	<div>Approved</div> <div>B</div>	

Activity ID		Activity Name	CMWP Rev.0 Start	CMWP Rev.0 Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete																		
										April 1					May 2					June 3				July 4			
										25	01	08	15	22	29	06	13	20	27	03	10	17	24	01	08	15	22
KD09.SSHP.0020		Submission and Approval of Installation Report by BD	27-Jan-22	02-Feb-22	7	23-Apr-22	29-Apr-22	-60	0%																		
		Socketed Steel H-Pile Construction																									
SHP-BW-52Y1b-P1		Socketed Steel H-Piling	04-Feb-22	12-Feb-22	17	15-Mar-22 A	04-Apr-22 A		100%																		
SHP-BW-52Y1b-P2		Socketed Steel H-Piling	08-Feb-22	16-Feb-22	8	30-Apr-22	11-May-22	426	0%																		
SHP-C52W-P1		Socketed Steel H-Piling	11-Feb-22	19-Feb-22	8	05-May-22	14-May-22	426	0%																		
SHP-C52W-P2		Socketed Steel H-Piling	15-Feb-22	23-Feb-22	8	10-May-22	18-May-22	426	0%																		
SHP-C52W-P3		Socketed Steel H-Piling	18-Feb-22	26-Feb-22	26	20-Apr-22 A	21-May-22	426	0%																		
SHP-C52W-P4		Socketed Steel H-Piling	22-Feb-22	02-Mar-22	12	17-Mar-22 A	31-Mar-22 A		100%																		
SHP-C52W-P5		Socketed Steel H-Piling	25-Feb-22	05-Mar-22	8	23-May-22	31-May-22	426	0%																		
SHP-C52W-P6		Socketed Steel H-Piling	01-Mar-22	09-Mar-22	8	26-May-22	04-Jun-22	426	0%																		
SHP-C52X-P1		Socketed Steel H-Piling	04-Mar-22	12-Mar-22	8	30-May-22	08-Jun-22	426	0%																		
SHP-C52X-P2		Socketed Steel H-Piling	08-Mar-22	16-Mar-22	8	02-Jun-22	11-Jun-22	426	0%																		
SHP-C52X-P3		Socketed Steel H-Piling	11-Mar-22	19-Mar-22	45	21-Apr-22 A	15-Jun-22	426	0%																		
SHP-C52X-P4		Socketed Steel H-Piling	15-Mar-22	23-Mar-22	14	12-Mar-22 A	29-Mar-22 A		100%																		
SHP-C52X-P5		Socketed Steel H-Piling	18-Mar-22	26-Mar-22	8	16-Jun-22	24-Jun-22	426	0%																		
SHP-C52X-P6		Socketed Steel H-Piling	22-Mar-22	30-Mar-22	8	20-Jun-22	28-Jun-22	426	0%																		
SHP-C52Xa-P1		Socketed Steel H-Piling	25-Mar-22	02-Apr-22	8	23-Jun-22	02-Jul-22	426	0%																		
SHP-C52Xa-P2		Socketed Steel H-Piling	29-Mar-22	07-Apr-22	8	27-Jun-22	06-Jul-22	426	0%																		
SHP-C52Xa-P3		Socketed Steel H-Piling	01-Apr-22	11-Apr-22	8	30-Jun-22	09-Jul-22	426	0%																		
SHP-C52Xa-P4		Socketed Steel H-Piling	06-Apr-22	14-Apr-22	8	05-Jul-22	13-Jul-22	426	0%																		
SHP-C52Xa-P5		Socketed Steel H-Piling	09-Apr-22	21-Apr-22	8	08-Jul-22	16-Jul-22	426	0%																		
ID: 2B2C-20220422_bw		<div><div></div>Planned Bar</div>		<div><div></div>Milestone</div>		<div>West Kowloon Cultural District Authority</div> <div>Piling for Integrated Basement and U/G Road in Zone 2B 2C</div> <div>3 Month Rolling Programme as of 22 Apr 2022</div> <div>Based on CMWP Rev.0</div>						<div>VIBRO</div> <div></div> <div></div>			Date	Revision	Checked	Approved									
Data Date: 23-Apr-22		4-Mar-22	Rev.0	KL	B																						
Print Date: 25-Apr-22_14:33																											
Page 21 of 21		<div><div></div>Critical Bar</div>		<div><div></div>Critical MS</div>																							
		<div><div></div>Baseline</div>		<div><div></div>Baseline MS</div>																							
