

Zone 2A

Project Name: Foundation and ELS Works for Integrated Basement and Underground Road in Zone 2A of the West Kowloon Cultural District

3-Month Rolling Programme

Activity Description	Duration (Cal. Day)	Start Date	Finish Date	2023															
				February				March					April				May		
				3	10	17	24	3	10	17	24	31	7	14	21	28	5	12	19
Zone 2A A&A Works																			
WEK B1/F																			
Sand Removal	63	17-Dec-22	17-Feb-23	■	■	■	■	■	■										
WEK G/F																			
Dismantling the Metal Roof Trusses at the Subcontractor's Works Area	8	28-Feb-23	7-Mar-23				■	■											

■ - Actual
■ - Remaining Works

Project Name: Foundation and ELS Works for Integrated Basement and Underground Road in Zone 2A of the West Kowloon Cultural District

3-Month Rolling Programme

Activity Description	Duration (Cal. Day)	Start Date	Finish Date	2023															
				March					April				May				June		
				3	10	17	24	31	7	14	21	28	5	12	19	26	2	9	16
W147	W148	W149	W150	W151	W152	W153	W154	W155	W156	W157	W158	W159	W160	W161	W162	W163	W164		
Zone 2A A&A Works																			
WEK G/F																			
Dismantling the Metal Roof Trusses at the Subcontractor's Works Area	8	28-Feb-23	7-Mar-23																

- Actual
 - Remaining Works

The Contruction Programme of Zone 2A

3-Month Rolling Programme

Activity Description	Duration (Cal. Day)	Start Date	Finish Date	2023																	
				April					May				June				July				
				1	8	15	22	29	6	13	20	27	3	10	17	24	1	8	15	22	29
W1	W2	W3	W4	W5	W6	W7	W8	W9	W10	W11	W12	W13	W14	W15	W16	W17	W18				
Zone 2A																					
Maintenance Work	30	1-Apr-23	30-Apr-23	■	■	■	■	■													

■ - Actual

Zone 2B & 2C

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finish	Total Float	February 20				March 21				April 22				May 23				
								28	04	11	18	25	04	11	18	25	01	08	15	22	29	06	13	20

Piling for Integrated Basement and U/G Road in Zone 2B & 2C

Contract Dates							
Optional Works subjected to CA's Instruction							
CO1A	Last CAI date for Optional Works Item No.1A (within 560 Days after Commencement)	02-Feb-23		0	02-Feb-23 A		
CO1B	Last CAI date for Optional Works Item No.1B (within 560 Days after Commencement)	02-Feb-23		0	02-Feb-23 A		
CO2B	Last CAI date for Optional Works Item No.2B (330 Days to 660 Days after Commencement)	13-May-23		0	13-May-23	11	
CO2D	Last CAI date for Optional Works Item No.2D (330 Days to 580 Days after Commencement)	22-Feb-23		0	22-Feb-23 A		
CO2E	Last CAI date for Optional Works Item No.2E (330 Days to 600 Days after Commencement)	14-Mar-23		0	14-Mar-23	71	

Construction Stage

Pile Construction


KD05 (Section 1)

Affected Bpred Piles - Drainage Diversion

CD04							
05							
P17-BP13.10	BP IAR-N - Excavation	03-Feb-23	09-Feb-23	6	25-Feb-23	03-Mar-23	-129
P17-BP13.20	BP IAR-N - RCD Drilling	10-Feb-23	27-Feb-23	15	02-Mar-23	18-Mar-23	-129
P17-BP13.30	BP IAR-N - Airlift, Cage Install and Concrete	28-Feb-23	07-Mar-23	7	20-Mar-23	27-Mar-23	-129
CD07							
04							
P17-BP19.10	BP - Excavation	27-Jan-23	03-Feb-23	6	25-Feb-23	03-Mar-23	-131
P17-BP19.20	BP - RCD Drilling	04-Feb-23	21-Feb-23	15	04-Mar-23	21-Mar-23	-131
P17-BP19.30	BP - Airlift, Cage Install and Concrete	22-Feb-23	01-Mar-23	7	22-Mar-23	29-Mar-23	-131
CD08							
01							
P17-BP20.10	BP - Excavation	17-Feb-23	23-Feb-23	6	25-Feb-23	03-Mar-23	-134
P17-BP20.20	BP - RCD Drilling	24-Feb-23	13-Mar-23	15	04-Mar-23	21-Mar-23	-134
P17-BP20.30	BP - Airlift, Cage Install and Concrete	14-Mar-23	21-Mar-23	7	22-Mar-23	29-Mar-23	-131
02							
P17-BP21.10	BP IAR-N - Excavation	07-Mar-23	13-Mar-23	6	01-Mar-23	07-Mar-23	-134
P17-BP21.20	BP IAR-N - RCD Drilling	14-Mar-23	30-Mar-23	15	08-Mar-23	24-Mar-23	-134
P17-BP21.30	BP IAR-N - Airlift, Cage Install and Concrete	31-Mar-23	12-Apr-23	7	25-Mar-23	01-Apr-23	-134
03							
P17-BP18.10	BP IAR-N - Excavation	24-Mar-23	30-Mar-23	6	01-Mar-23	07-Mar-23	-134
P17-BP18.20	BP IAR-N - RCD Drilling	31-Mar-23	21-Apr-23	15	08-Mar-23	24-Mar-23	-134
P17-BP18.30	BP IAR-N - Airlift, Cage Install and Concrete	22-Apr-23	29-Apr-23	7	25-Mar-23	01-Apr-23	-134

Affected Bpred Piles - Gantry Gate A

CD06							
08							
CBA-BP01.10	BP - Excavation	20-Jan-23	31-Jan-23	7	25-Feb-23	04-Mar-23	-130
CBA-BP01.20	BP - RCD Drilling	01-Feb-23	16-Feb-23	14	06-Mar-23	21-Mar-23	-130
CBA-BP01.30	BP - Airlift, Cage Install and Concrete	17-Feb-23	23-Feb-23	6	22-Mar-23	28-Mar-23	-130
CD07							
02							
P22&P19-BP26.:	BP - RCD Drilling	16-Jul-22	03-Dec-22	212	16-Jul-22 A	30-Mar-23	-140

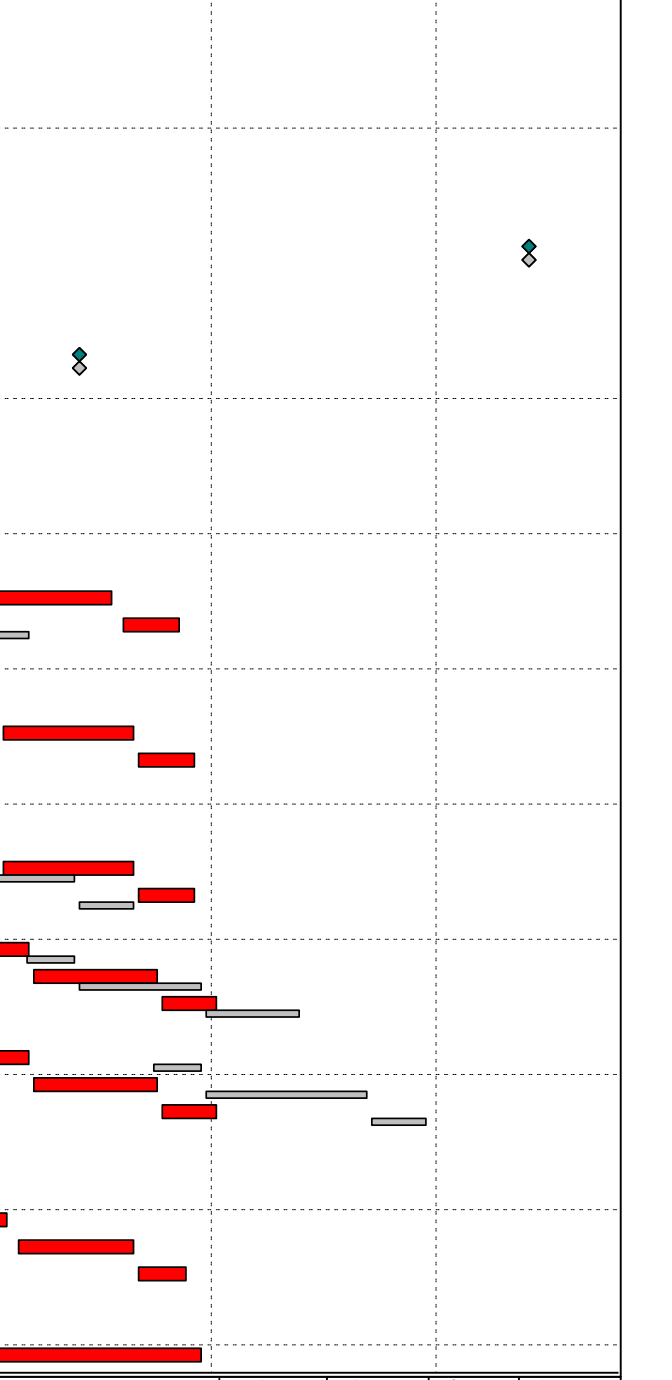


ID: 2BC-20230224_bw
 Data Date: 25-Feb-23
 Print Date: 27-Feb-23_10:20
 Page 1 of 15

■ Planned	◆ Planned MS
■ Critical	◆ Critical MS
■ Actual	◆ Actual MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 24 February 2023
Based on CMWP Rev.0 (3rd Draft)



Date	Revision	Checked	Approved
4-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C

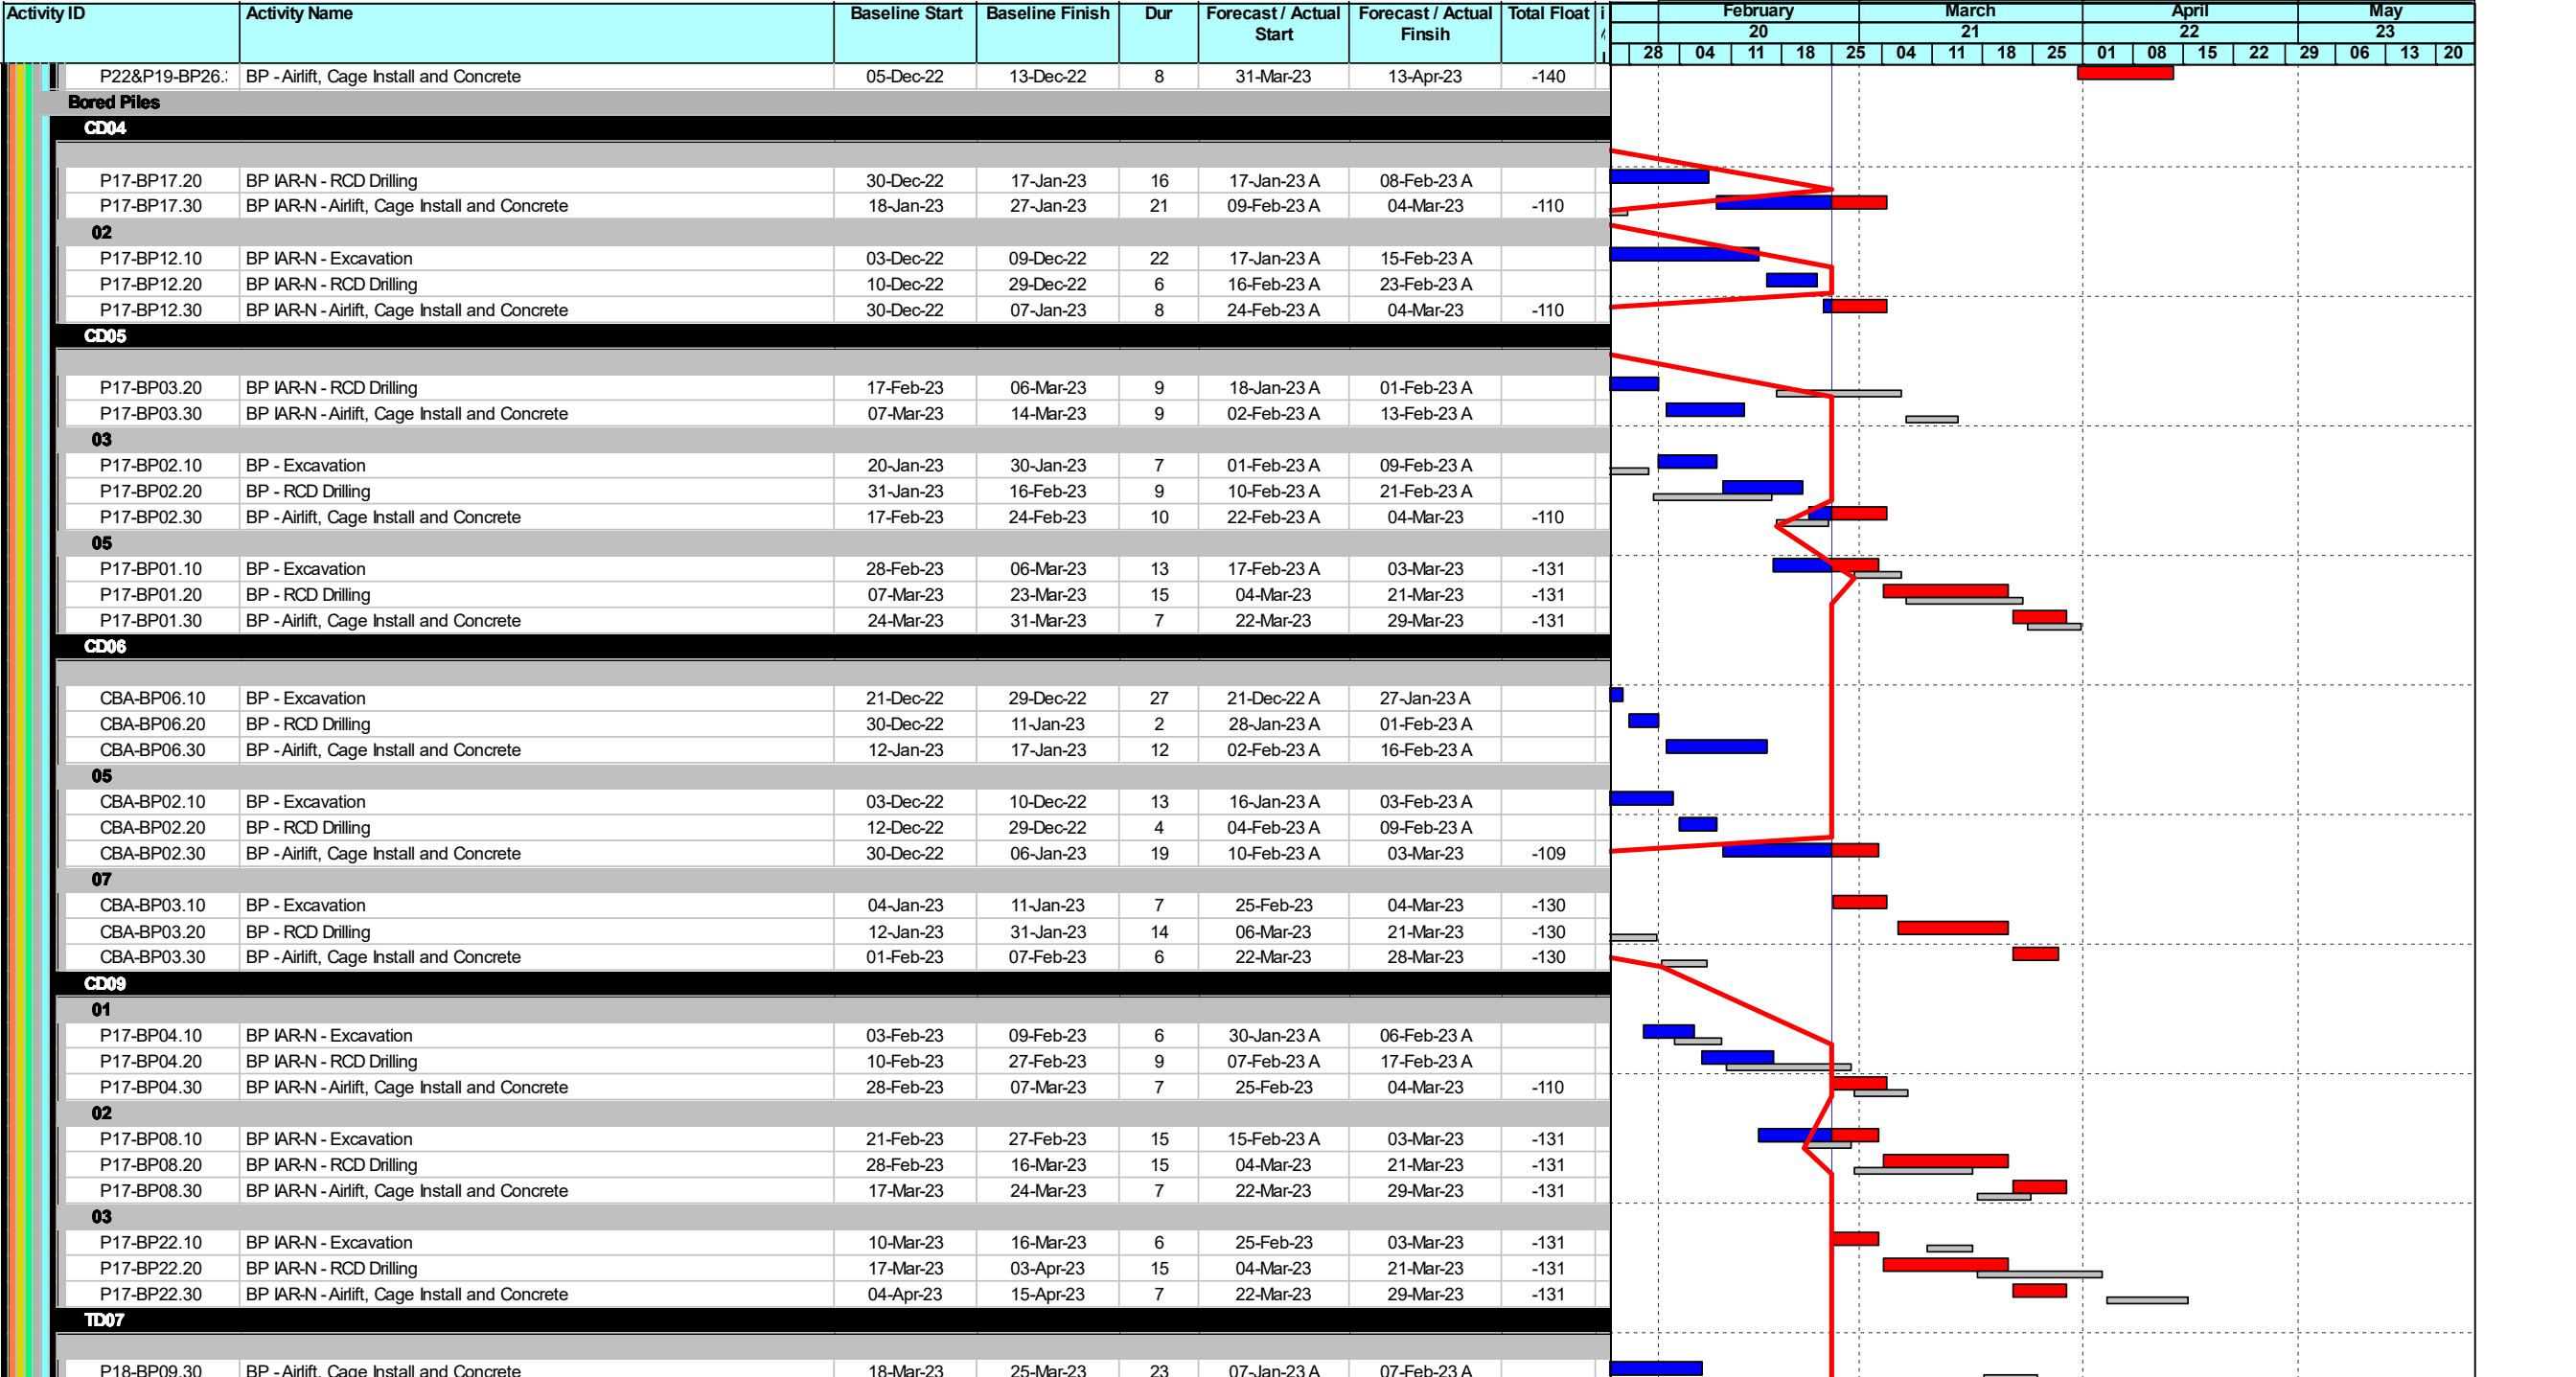

ID: 2BC-20230224_bw
 Data Date: 25-Feb-23
 Print Date: 27-Feb-23_10:20
 Page 2 of 15

	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 24 February 2023
 Based on CMWP Rev.0 (3rd Draft)



Date	Revision	Checked	Approved
4-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	February				March				April				May			
								20				21				22				23			
								28	04	11	18	25	04	11	18	25	01	08	15	22	29	06	13

P18-BP12.20	BP IAR-S - RCD Drilling	18-Mar-23	04-Apr-23	20	05-Jan-23 A	01-Feb-23 A	
P18-BP12.30	BP IAR-S - Airlift, Cage Install and Concrete	06-Apr-23	17-Apr-23	7	02-Feb-23 A	10-Feb-23 A	
04							
P18-BP01.10	BP - Excavation	15-Dec-22	21-Dec-22	6	25-Feb-23	03-Mar-23	-142
P18-BP01.20	BP - RCD Drilling	22-Dec-22	16-Jan-23	19	04-Mar-23	25-Mar-23	-142
P18-BP01.30	BP - Airlift, Cage Install and Concrete	17-Jan-23	27-Jan-23	8	27-Mar-23	04-Apr-23	-136
06							
P18-BP04.10	BP IAR-S - Excavation	04-Feb-23	10-Feb-23	6	25-Feb-23	03-Mar-23	-142
P18-BP04.20	BP IAR-S - RCD Drilling	11-Feb-23	28-Feb-23	15	04-Mar-23	21-Mar-23	-142
P18-BP04.30	BP IAR-S - Airlift, Cage Install and Concrete	01-Mar-23	08-Mar-23	7	22-Mar-23	29-Mar-23	-131
09							
P18-BP07.10	BP IAR-S - Excavation	11-Mar-23	17-Mar-23	6	10-Mar-23	16-Mar-23	-142
P18-BP07.20	BP IAR-S - RCD Drilling	18-Mar-23	04-Apr-23	15	17-Mar-23	03-Apr-23	-142
P18-BP07.30	BP IAR-S - Airlift, Cage Install and Concrete	06-Apr-23	17-Apr-23	7	04-Apr-23	15-Apr-23	-142
TD09							
08							
CBA-BPC36Jb.1i	BP IAR-N - Excavation	31-Mar-23	11-Apr-23	6	04-Apr-23	14-Apr-23	-156
CBA-BPC36Jb.2i	BP IAR-N - RCD Drilling	12-Apr-23	22-Apr-23	10	15-Apr-23	26-Apr-23	-156
CBA-BPC36Jb.3i	BP IAR-N - Airlift, Cage Install and Concrete	24-Apr-23	28-Apr-23	5	27-Apr-23	03-May-23	-156
09							
CBA-BPC36Ka.1	BP IAR-N - Excavation	31-Mar-23	11-Apr-23	41	22-Feb-23 A	14-Apr-23	-156
CBA-BPC36Ka.2	BP IAR-N - RCD Drilling	12-Apr-23	22-Apr-23	10	15-Apr-23	26-Apr-23	-156
CBA-BPC36Ka.3	BP IAR-N - Airlift, Cage Install and Concrete	24-Apr-23	28-Apr-23	5	27-Apr-23	03-May-23	-156

KD06 (Section 2)

Bored Piles

VD09


CBA-BPC49K.30	BP - Airlift, Cage Install and Concrete	20-May-23	27-May-23	12	16-Jan-23 A	02-Feb-23 A	
05							
CBA-BPC48K.10	BP - Excavation	16-Feb-23	23-Feb-23	26	03-Feb-23 A	04-Mar-23	1
CBA-BPC48K.20	BP - RCD Drilling	24-Feb-23	11-Mar-23	14	06-Mar-23	21-Mar-23	1
CBA-BPC48K.30	BP - Airlift, Cage Install and Concrete	13-Mar-23	18-Mar-23	6	22-Mar-23	28-Mar-23	1

VD11

03							
CBA-BPC51K.10	BP - Excavation	09-Feb-23	15-Feb-23	20	31-Dec-22 A	27-Jan-23 A	
CBA-BPC51K.20	BP - RCD Drilling	16-Feb-23	23-Mar-23	1	28-Jan-23 A	31-Jan-23 A	
CBA-BPC51K.30	BP - Airlift, Cage Install and Concrete	24-Mar-23	30-Mar-23	16	01-Feb-23 A	20-Feb-23 A	

VD14

04							
P24&P27-BP33.	BP - Excavation	04-Jan-23	10-Jan-23	21	03-Jan-23 A	31-Jan-23 A	
P24&P27-BP33.:	BP - RCD Drilling	11-Jan-23	04-Feb-23	40	01-Feb-23 A	18-Mar-23	-73
P24&P27-BP33.:	BP - Airlift, Cage Install and Concrete	06-Feb-23	14-Feb-23	8	20-Mar-23	28-Mar-23	1
05							
P24&P27-BP15.	BP - Excavation	30-Jan-23	04-Feb-23	6	13-Mar-23	18-Mar-23	-73
P24&P27-BP15.:	BP - RCD Drilling	06-Feb-23	27-Feb-23	19	20-Mar-23	14-Apr-23	-73
P24&P27-BP15.:	BP - Airlift, Cage Install and Concrete	28-Feb-23	08-Mar-23	8	15-Apr-23	24-Apr-23	-18
06							
P24&P27-BP22.	BP - Excavation	21-Feb-23	27-Feb-23	6	04-Apr-23	14-Apr-23	-73
P24&P27-BP22.:	BP - RCD Drilling	28-Feb-23	21-Mar-23	19	15-Apr-23	08-May-23	-73
P24&P27-BP22.:	BP - Airlift, Cage Install and Concrete	22-Mar-23	30-Mar-23	8	09-May-23	17-May-23	-37

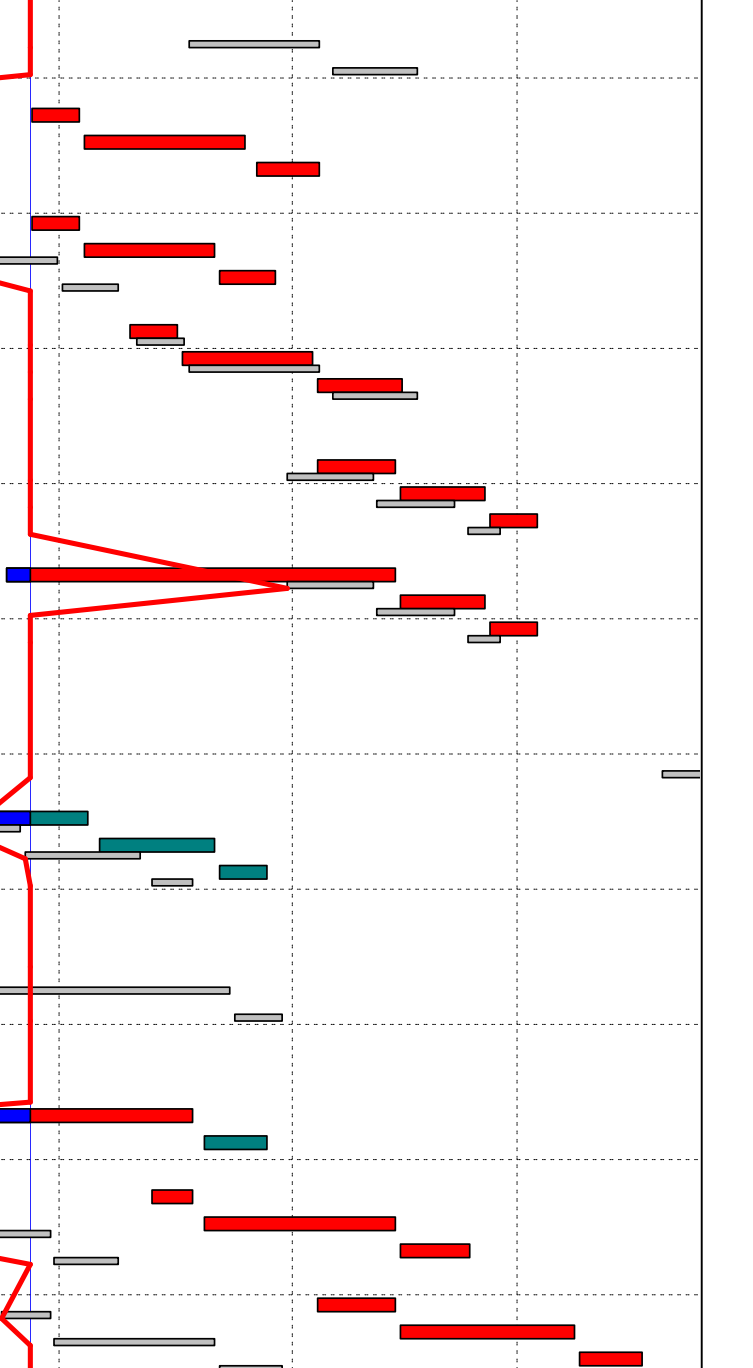


ID: 2BC-20230224_bw
 Data Date: 25-Feb-23
 Print Date: 27-Feb-23_10:20
 Page 3 of 15







	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS

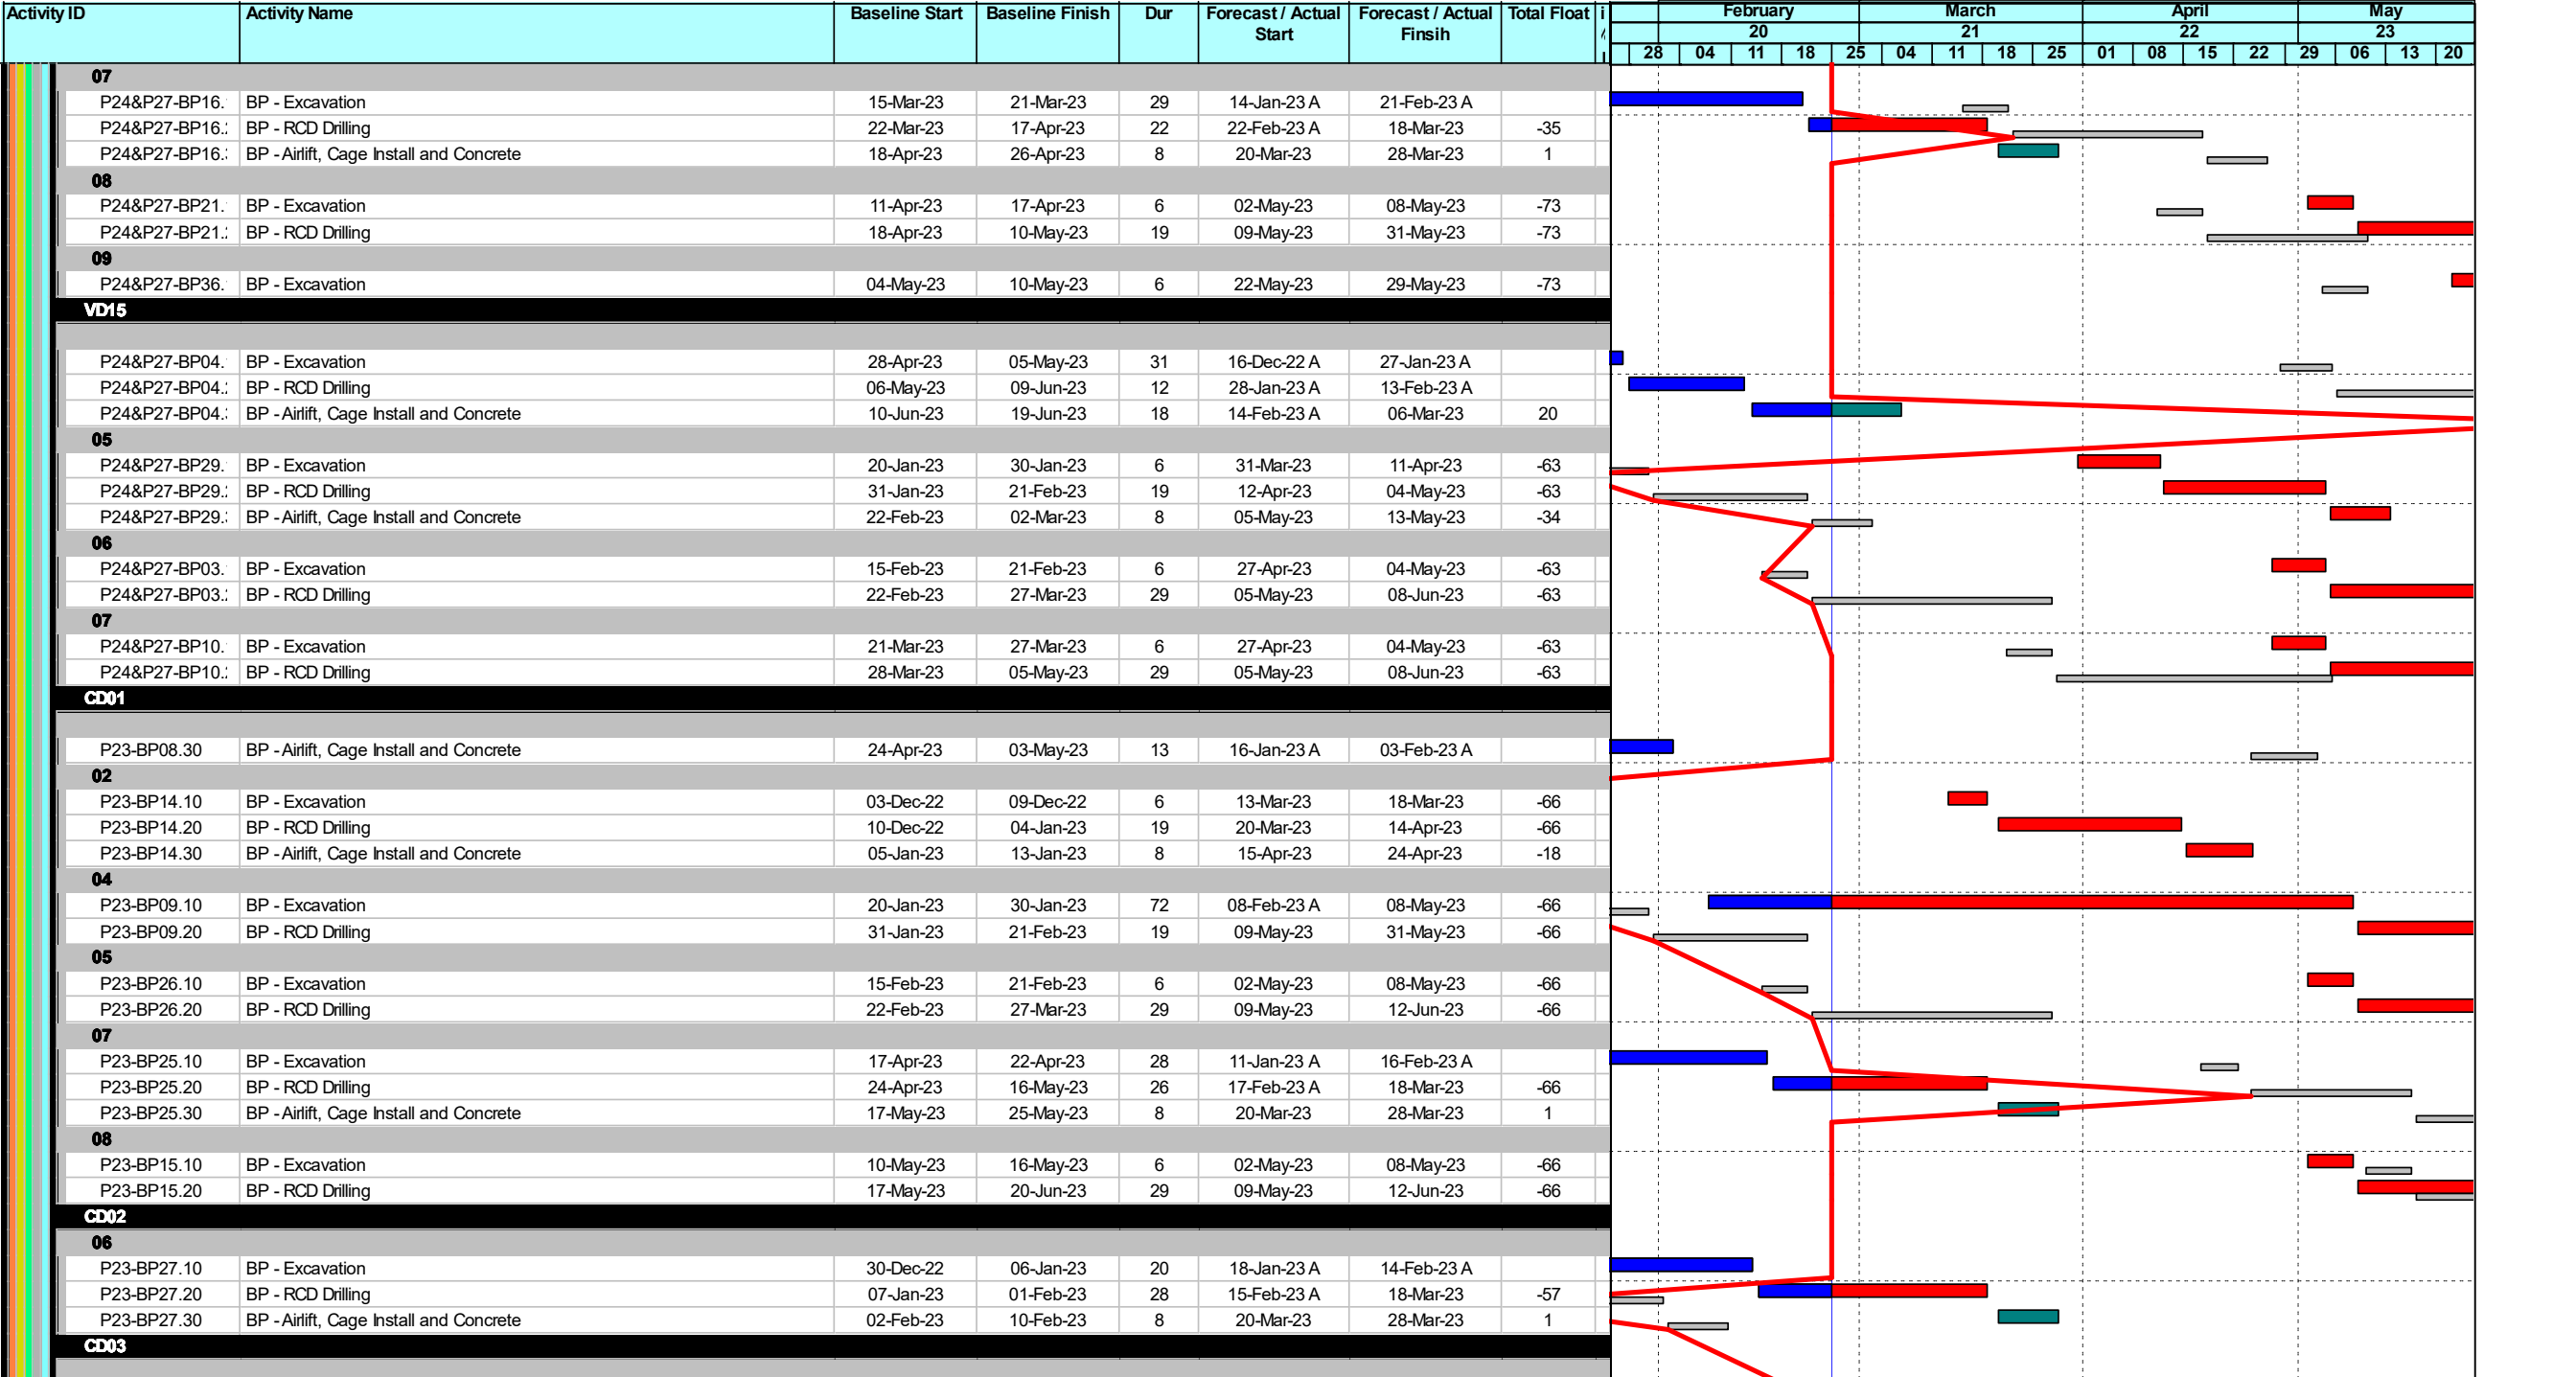West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 24 February 2023
Based on CMWP Rev.0 (3rd Draft)



Date	Revision	Checked	Approved
4-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C





	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 24 February 2023
Based on CMWP Rev.0 (3rd Draft)



Date	Revision	Checked	Approved
4-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C

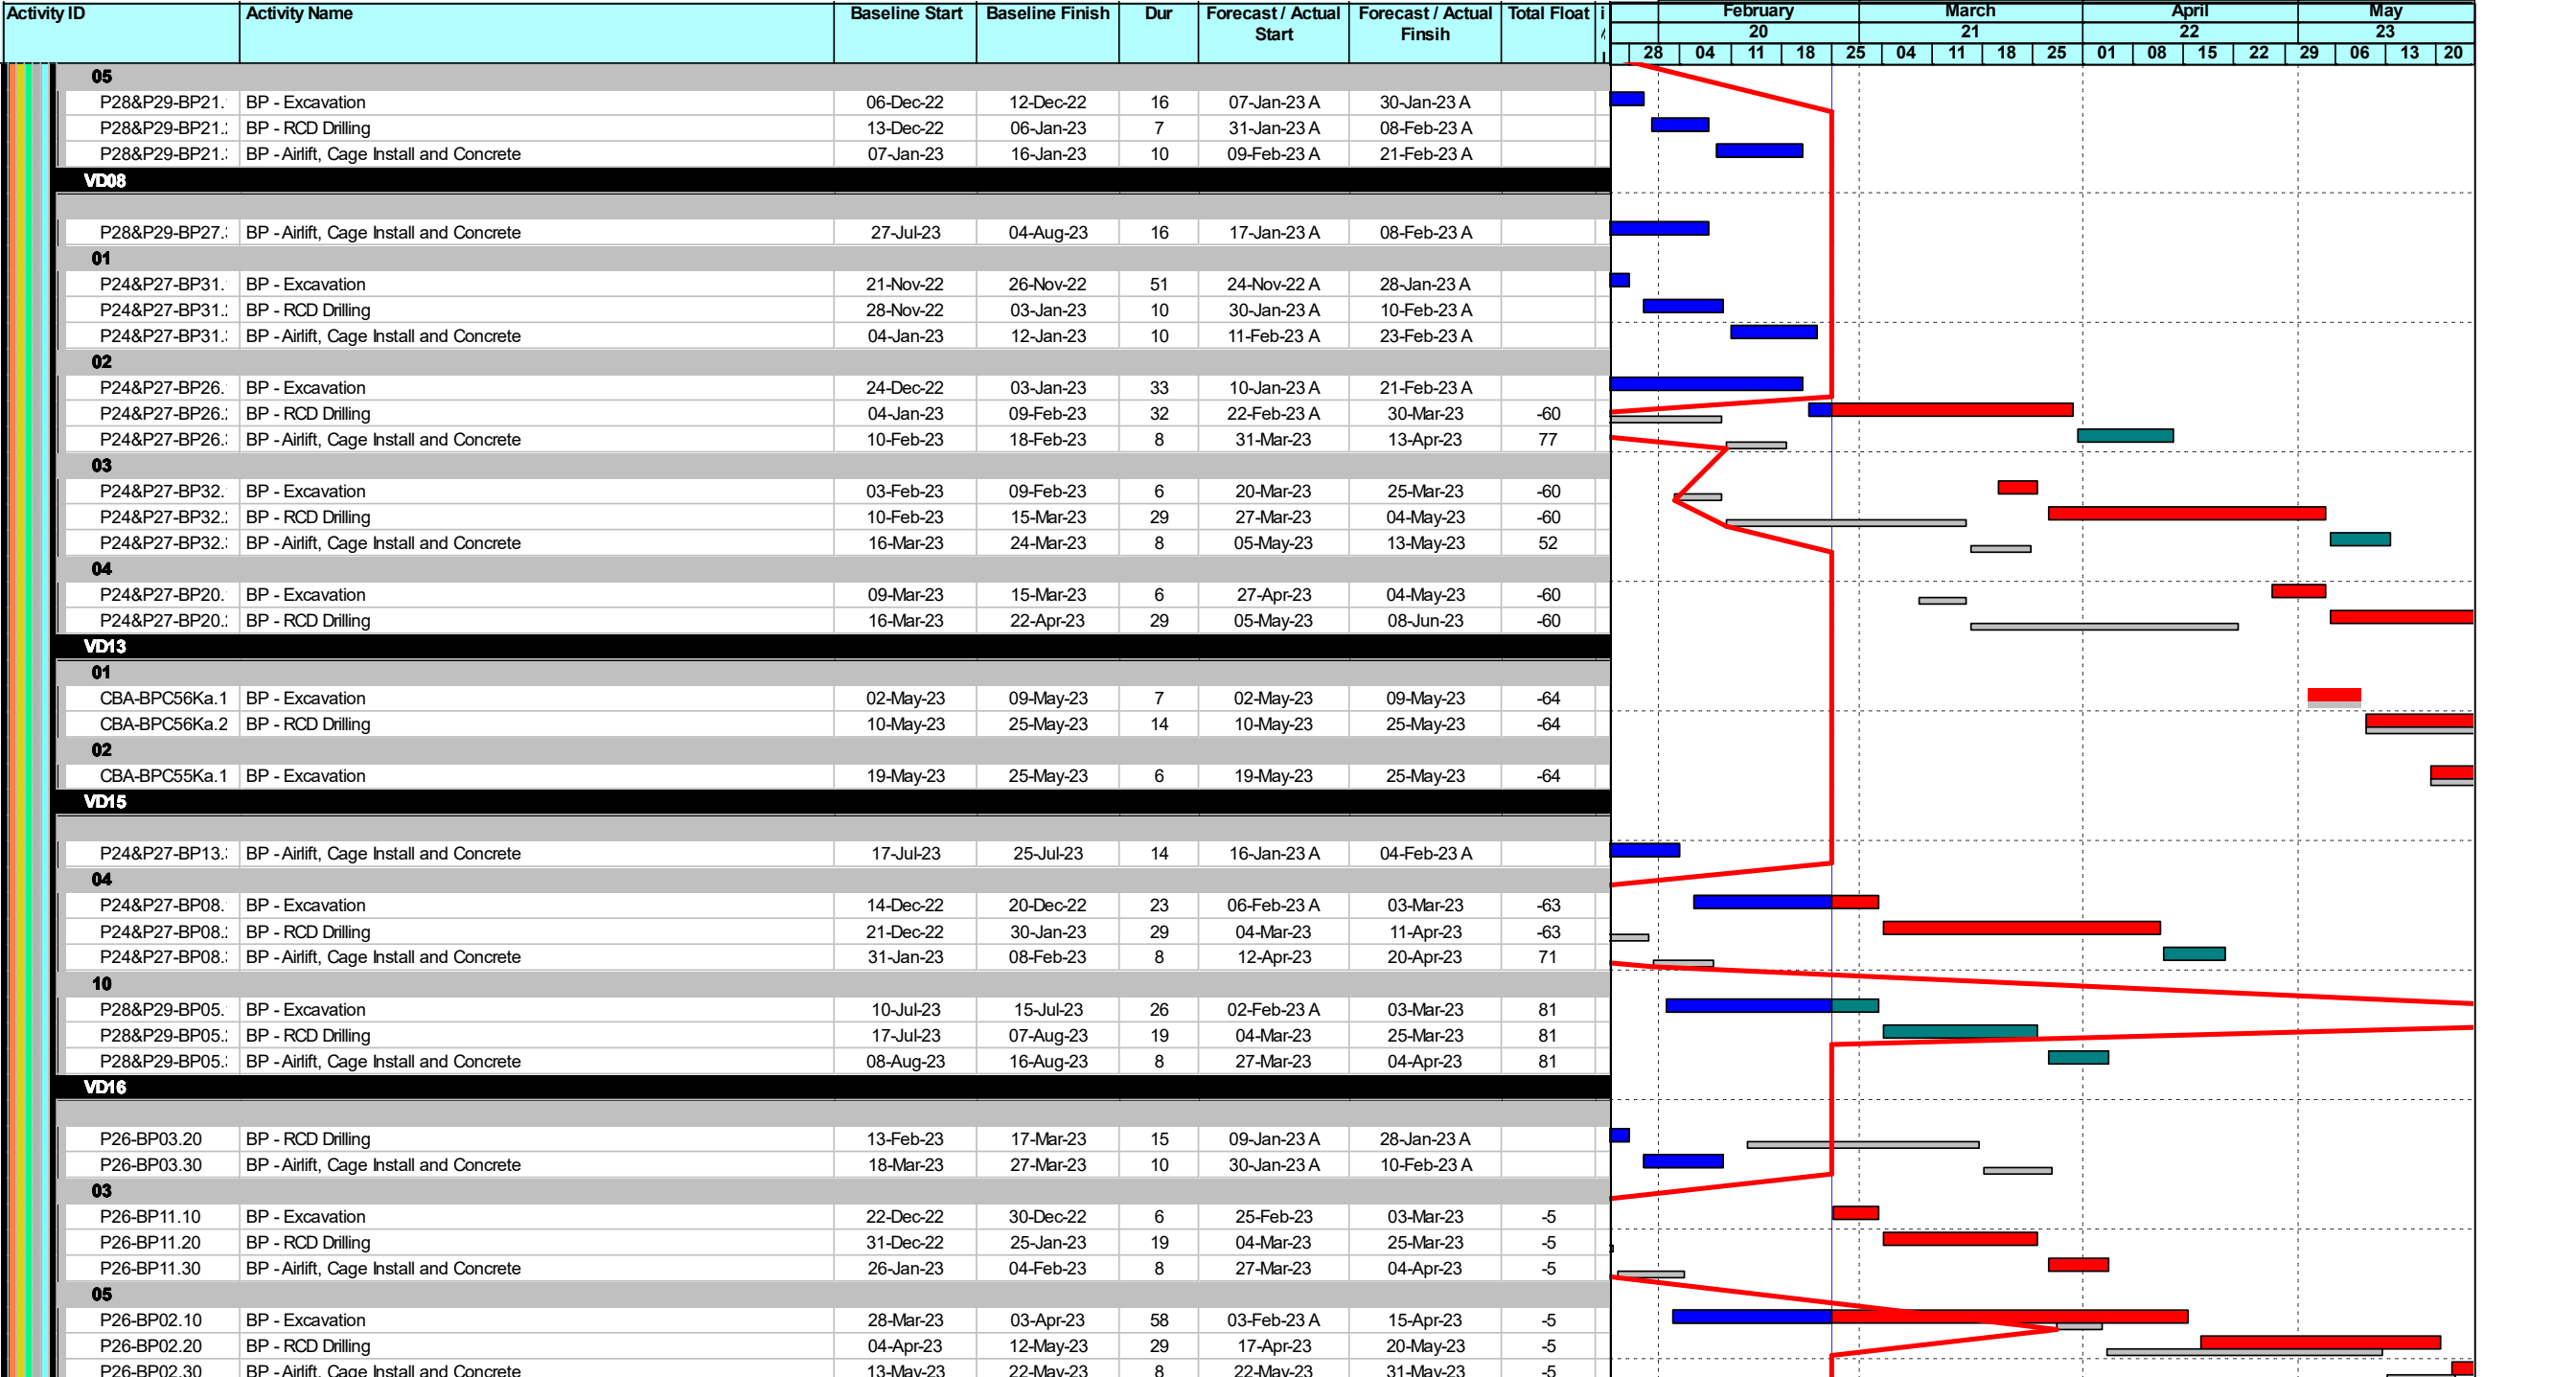

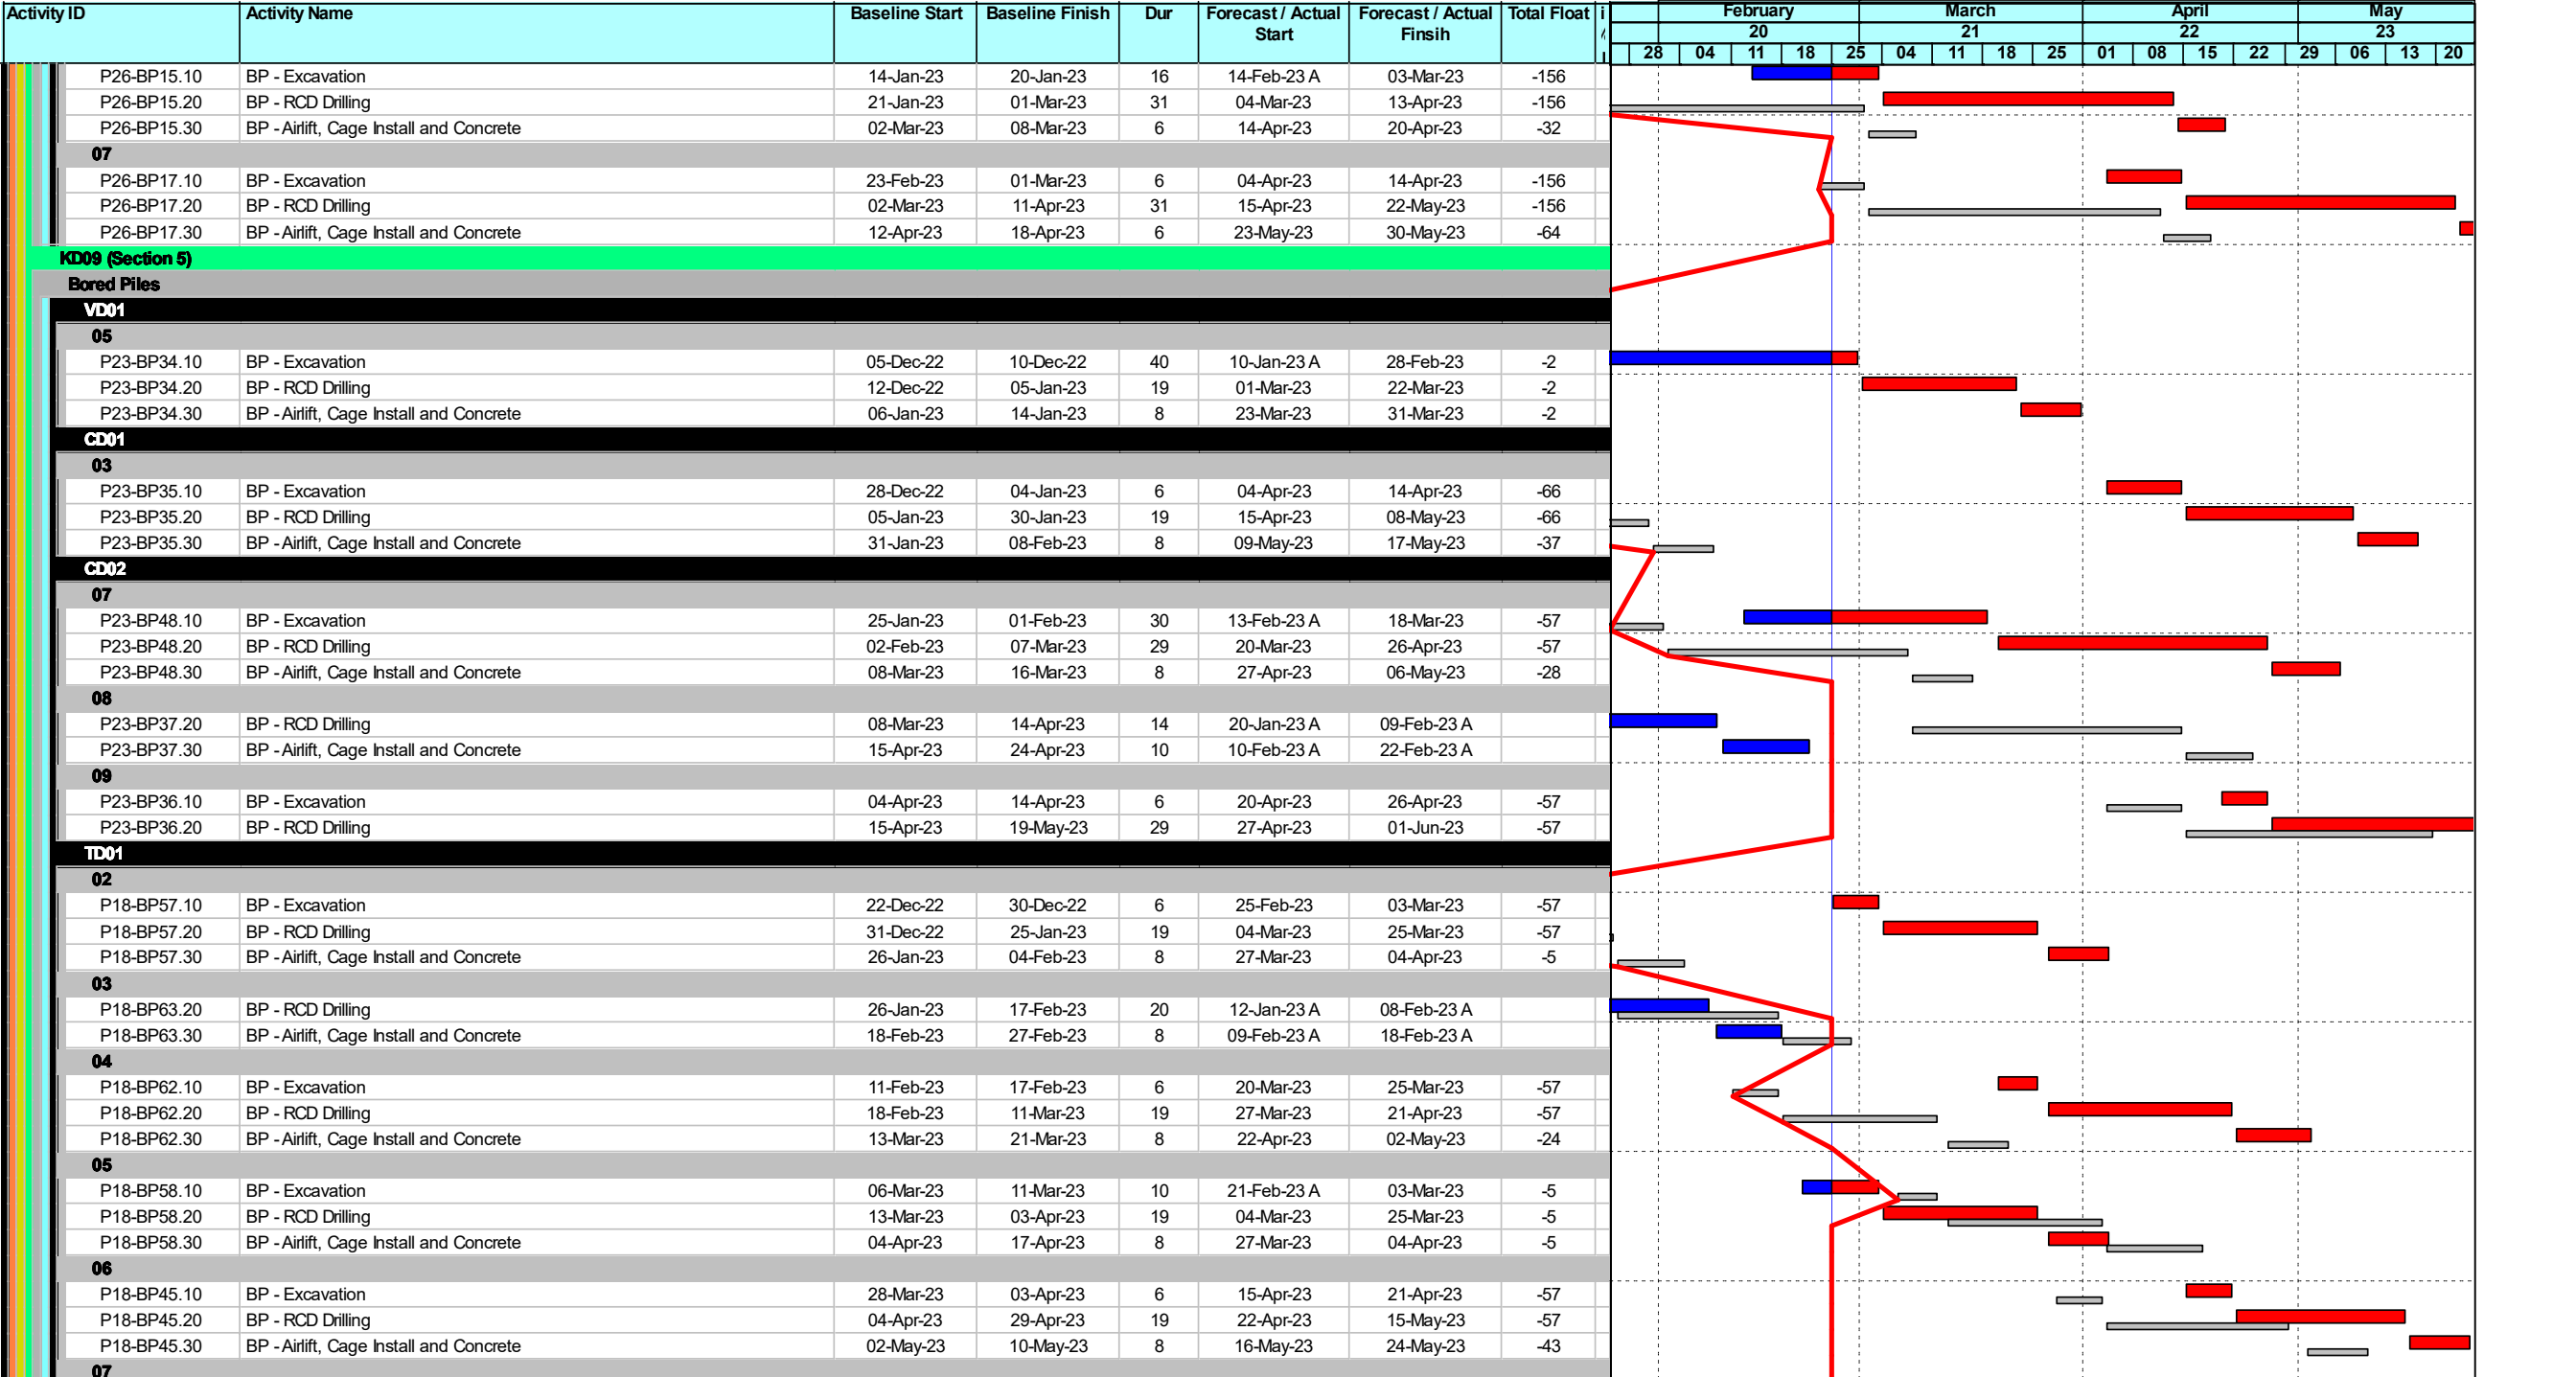








	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 24 February 2023
Based on CMWP Rev.0 (3rd Draft)

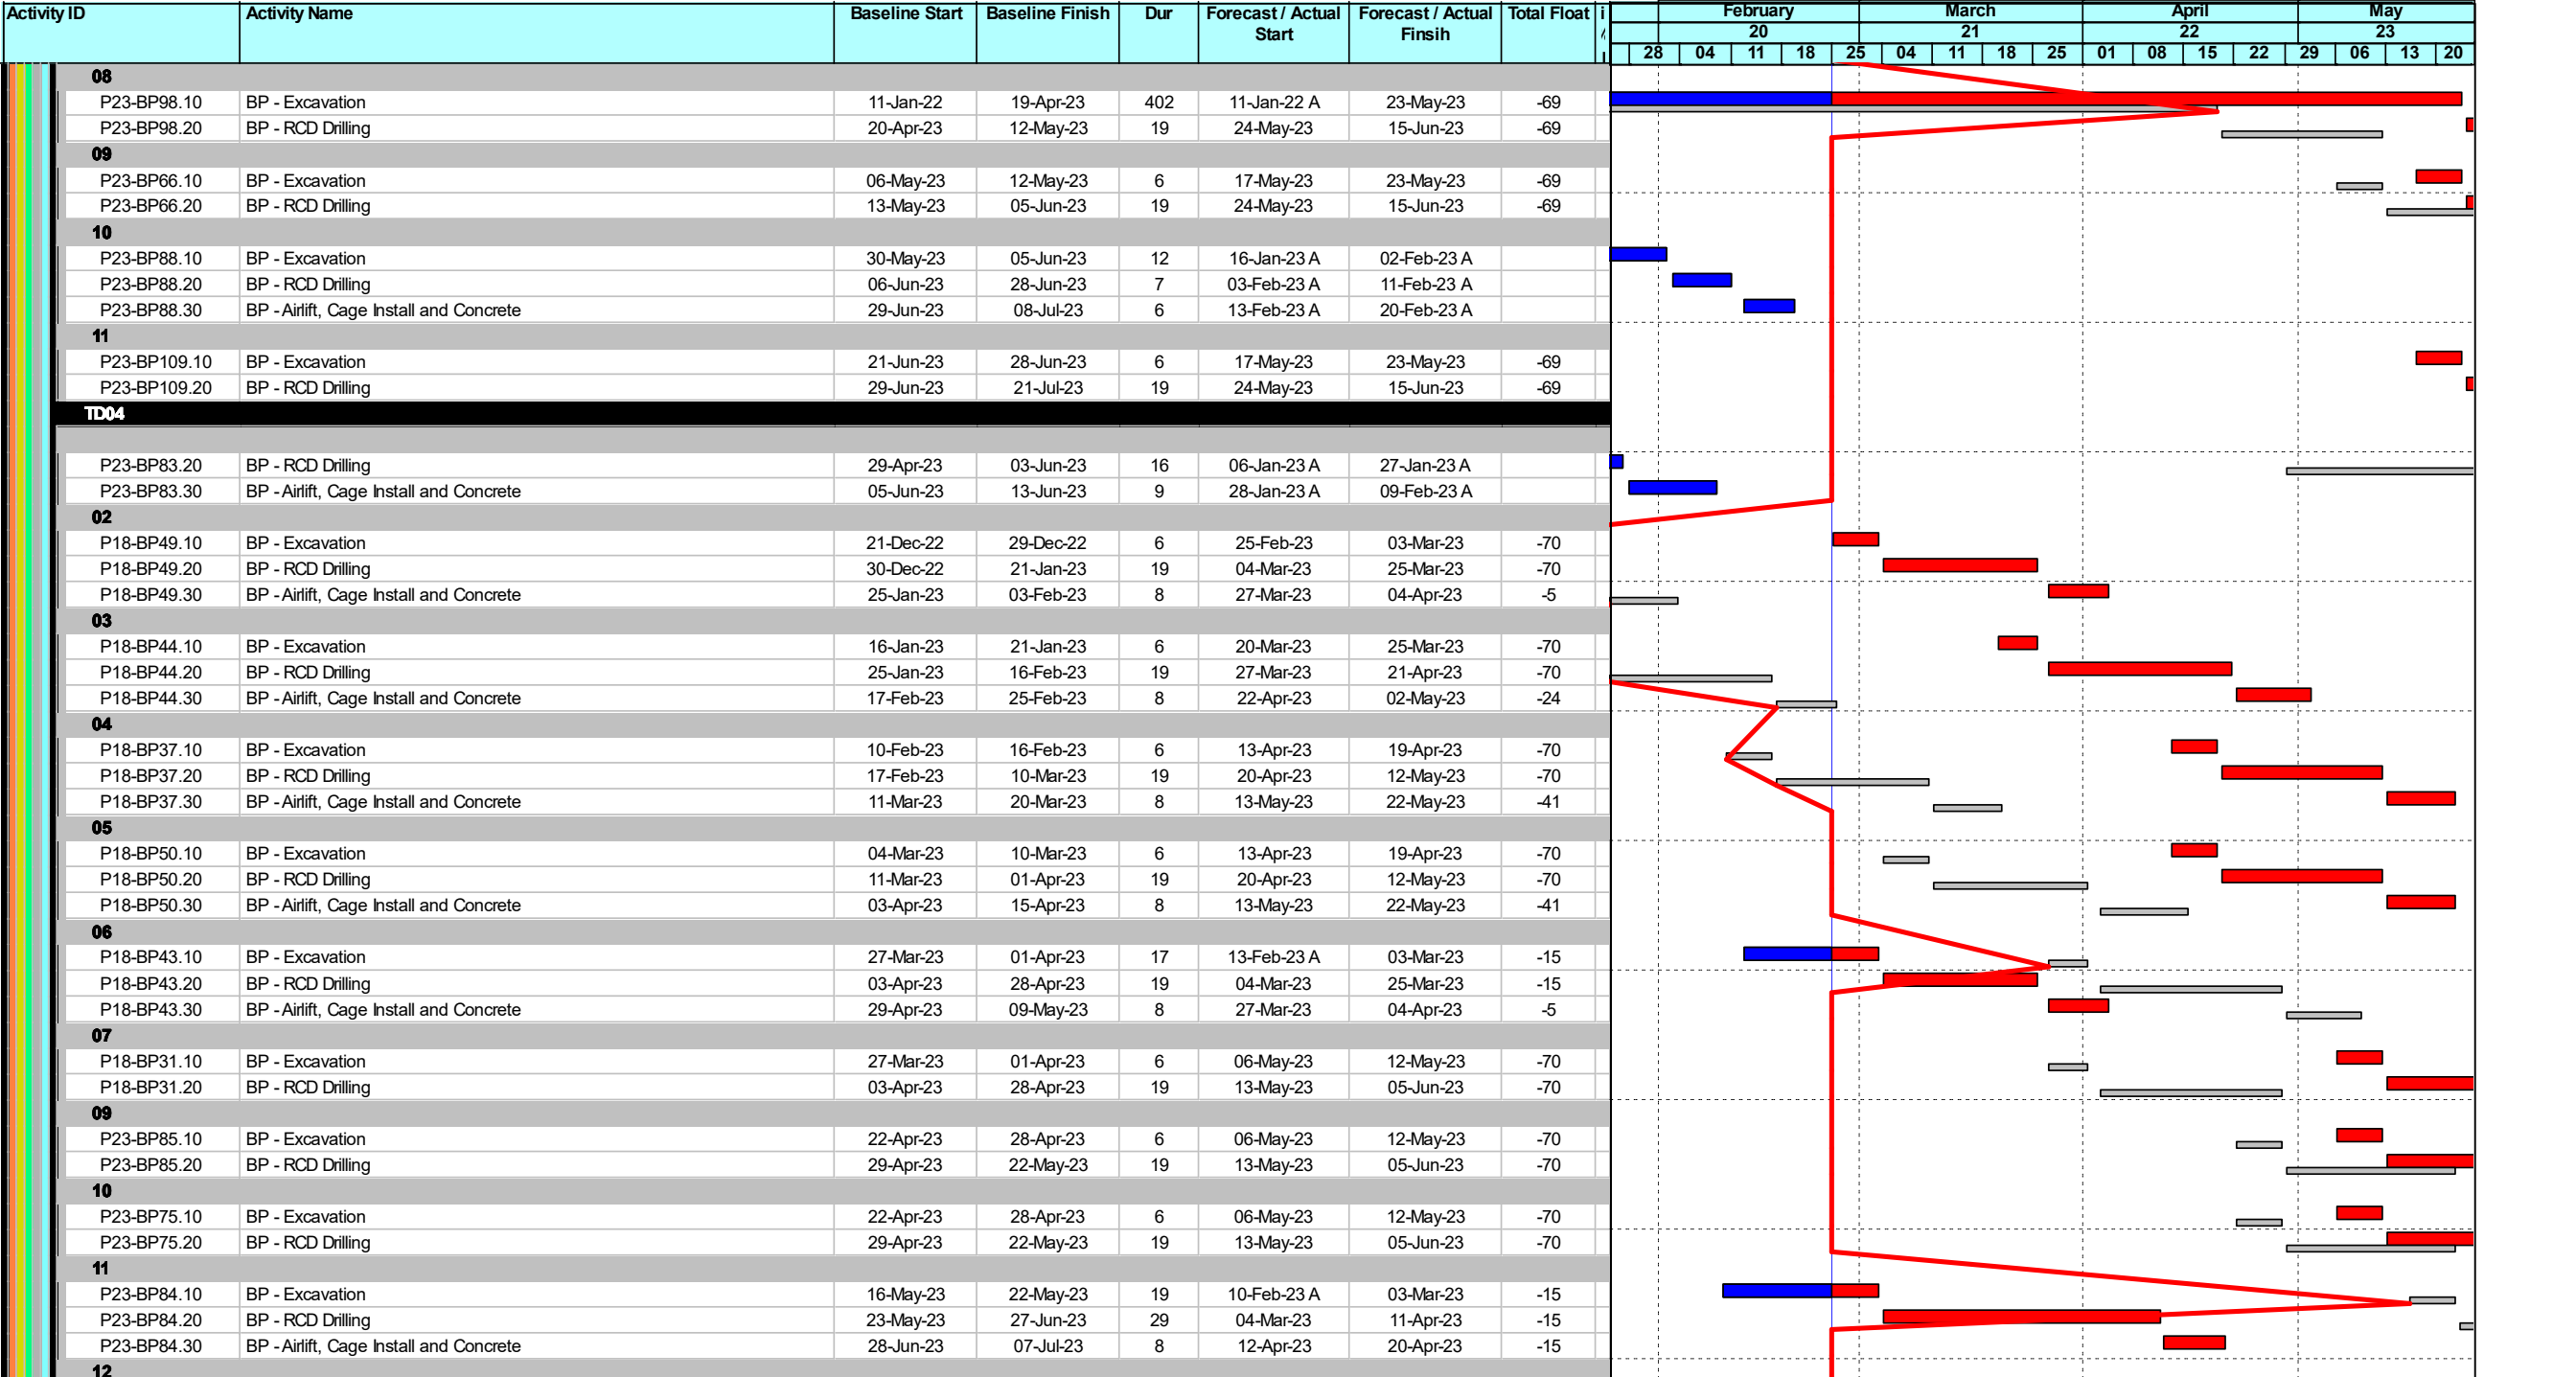

Date	Revision	Checked	Approved
4-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C



	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 24 February 2023
 Based on CMWP Rev.0 (3rd Draft)



Date	Revision	Checked	Approved
4-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Gantt Chart															
								February 20				March 21				April 22				May 23			
								28	04	11	18	25	04	11	18	25	01	08	15	22	29	06	13
S4.AT.0000	Attendance at Section 4 Area (optional works item no. 2D) (Duration TBC)	22-Feb-23	13-Mar-23	20	25-Feb-23	16-Mar-23	68																
S5.AT.0000	Attendance at Section 5 Area (optional works item no. 2E) (Duration TBC)	14-Mar-23	02-Apr-23	20	14-Mar-23	02-Apr-23	71																



	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 24 February 2023
 Based on CMWP Rev.0 (3rd Draft)



Date	Revision	Checked	Approved
4-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	March					April				May				June		
								21					22				23				24		
								25	04	11	18	25	01	08	15	22	29	06	13	20	27	03	10

Piling for Integrated Basement and U/G Road in Zone 2B & 2C

Contract Dates							
Optional Works subjected to CA's Instruction							
CO2B	Last CAI date for Optional Works Item No.2B (330 Days to 660 Days after Commencement)	13-May-23		0	13-May-23		11
CO2E	Last CAI date for Optional Works Item No.2E (330 Days to 600 Days after Commencement)	14-Mar-23		0	14-Mar-23 A		

Construction Stage

Pile Construction

KD05 (Section 1)

Bored Piles - Drainage Diversion

CD04

05

P17-BP13.10	BP IAR-N - Excavation	03-Feb-23	09-Feb-23	10	27-Feb-23 A	10-Mar-23 A	
P17-BP13.20	BP IAR-N - RCD Drilling	10-Feb-23	27-Feb-23	8	11-Mar-23 A	21-Mar-23 A	
P17-BP13.30	BP IAR-N - Airlift, Cage Install and Concrete	28-Feb-23	07-Mar-23	10	22-Mar-23 A	01-Apr-23	-134

CD07

04

P17-BP19.10	BP - Excavation	27-Jan-23	03-Feb-23	6	25-Mar-23	31-Mar-23	-203
P17-BP19.20	BP - RCD Drilling	04-Feb-23	21-Feb-23	15	01-Apr-23	22-Apr-23	-203
P17-BP19.30	BP - Airlift, Cage Install and Concrete	22-Feb-23	01-Mar-23	6	24-Apr-23	29-Apr-23	-154

CD08

01

P17-BP20.10	BP - Excavation	17-Feb-23	23-Feb-23	4	19-Apr-23	22-Apr-23	-203
P17-BP20.20	BP - RCD Drilling	24-Feb-23	13-Mar-23	15	24-Apr-23	11-May-23	-203
P17-BP20.30	BP - Airlift, Cage Install and Concrete	14-Mar-23	21-Mar-23	7	12-May-23	19-May-23	-170

02

P17-BP21.10	BP IAR-N - Excavation	07-Mar-23	13-Mar-23	4	12-May-23	16-May-23	-203
P17-BP21.20	BP IAR-N - RCD Drilling	14-Mar-23	30-Mar-23	15	17-May-23	03-Jun-23	-203
P17-BP21.30	BP IAR-N - Airlift, Cage Install and Concrete	31-Mar-23	12-Apr-23	7	05-Jun-23	12-Jun-23	-189

03

P17-BP18.10	BP IAR-N - Excavation	24-Mar-23	30-Mar-23	4	31-May-23	03-Jun-23	-203
P17-BP18.20	BP IAR-N - RCD Drilling	31-Mar-23	21-Apr-23	15	05-Jun-23	21-Jun-23	-203
P17-BP18.30	BP IAR-N - Airlift, Cage Install and Concrete	22-Apr-23	29-Apr-23	7	23-Jun-23	30-Jun-23	-203

Bored Piles - Gantry Gate A

CD06


08

CBA-BP01.10	BP - Excavation	20-Jan-23	31-Jan-23	7	15-Apr-23	22-Apr-23	-168
CBA-BP01.20	BP - RCD Drilling	01-Feb-23	16-Feb-23	14	24-Apr-23	10-May-23	-168
CBA-BP01.30	BP - Airlift, Cage Install and Concrete	17-Feb-23	23-Feb-23	6	11-May-23	17-May-23	-168

CD07

02

P22&P19-BP26.:	BP - RCD Drilling	16-Jul-22	03-Dec-22	213	16-Jul-22 A	31-Mar-23	-141
----------------	-------------------	-----------	-----------	-----	-------------	-----------	------

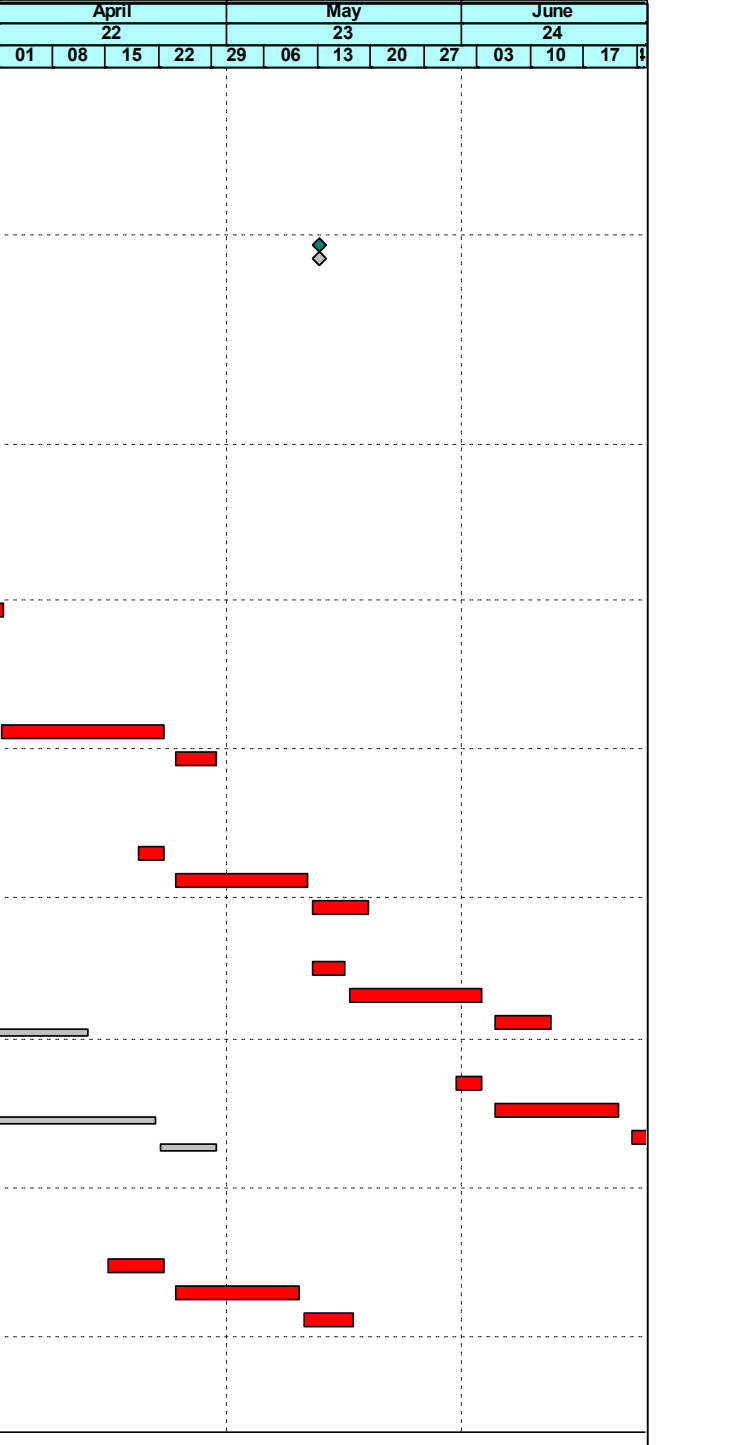








ID: 2BC-20230324_bw
 Data Date: 25-Mar-23
 Print Date: 24-Mar-23_17:18
 Page 1 of 14

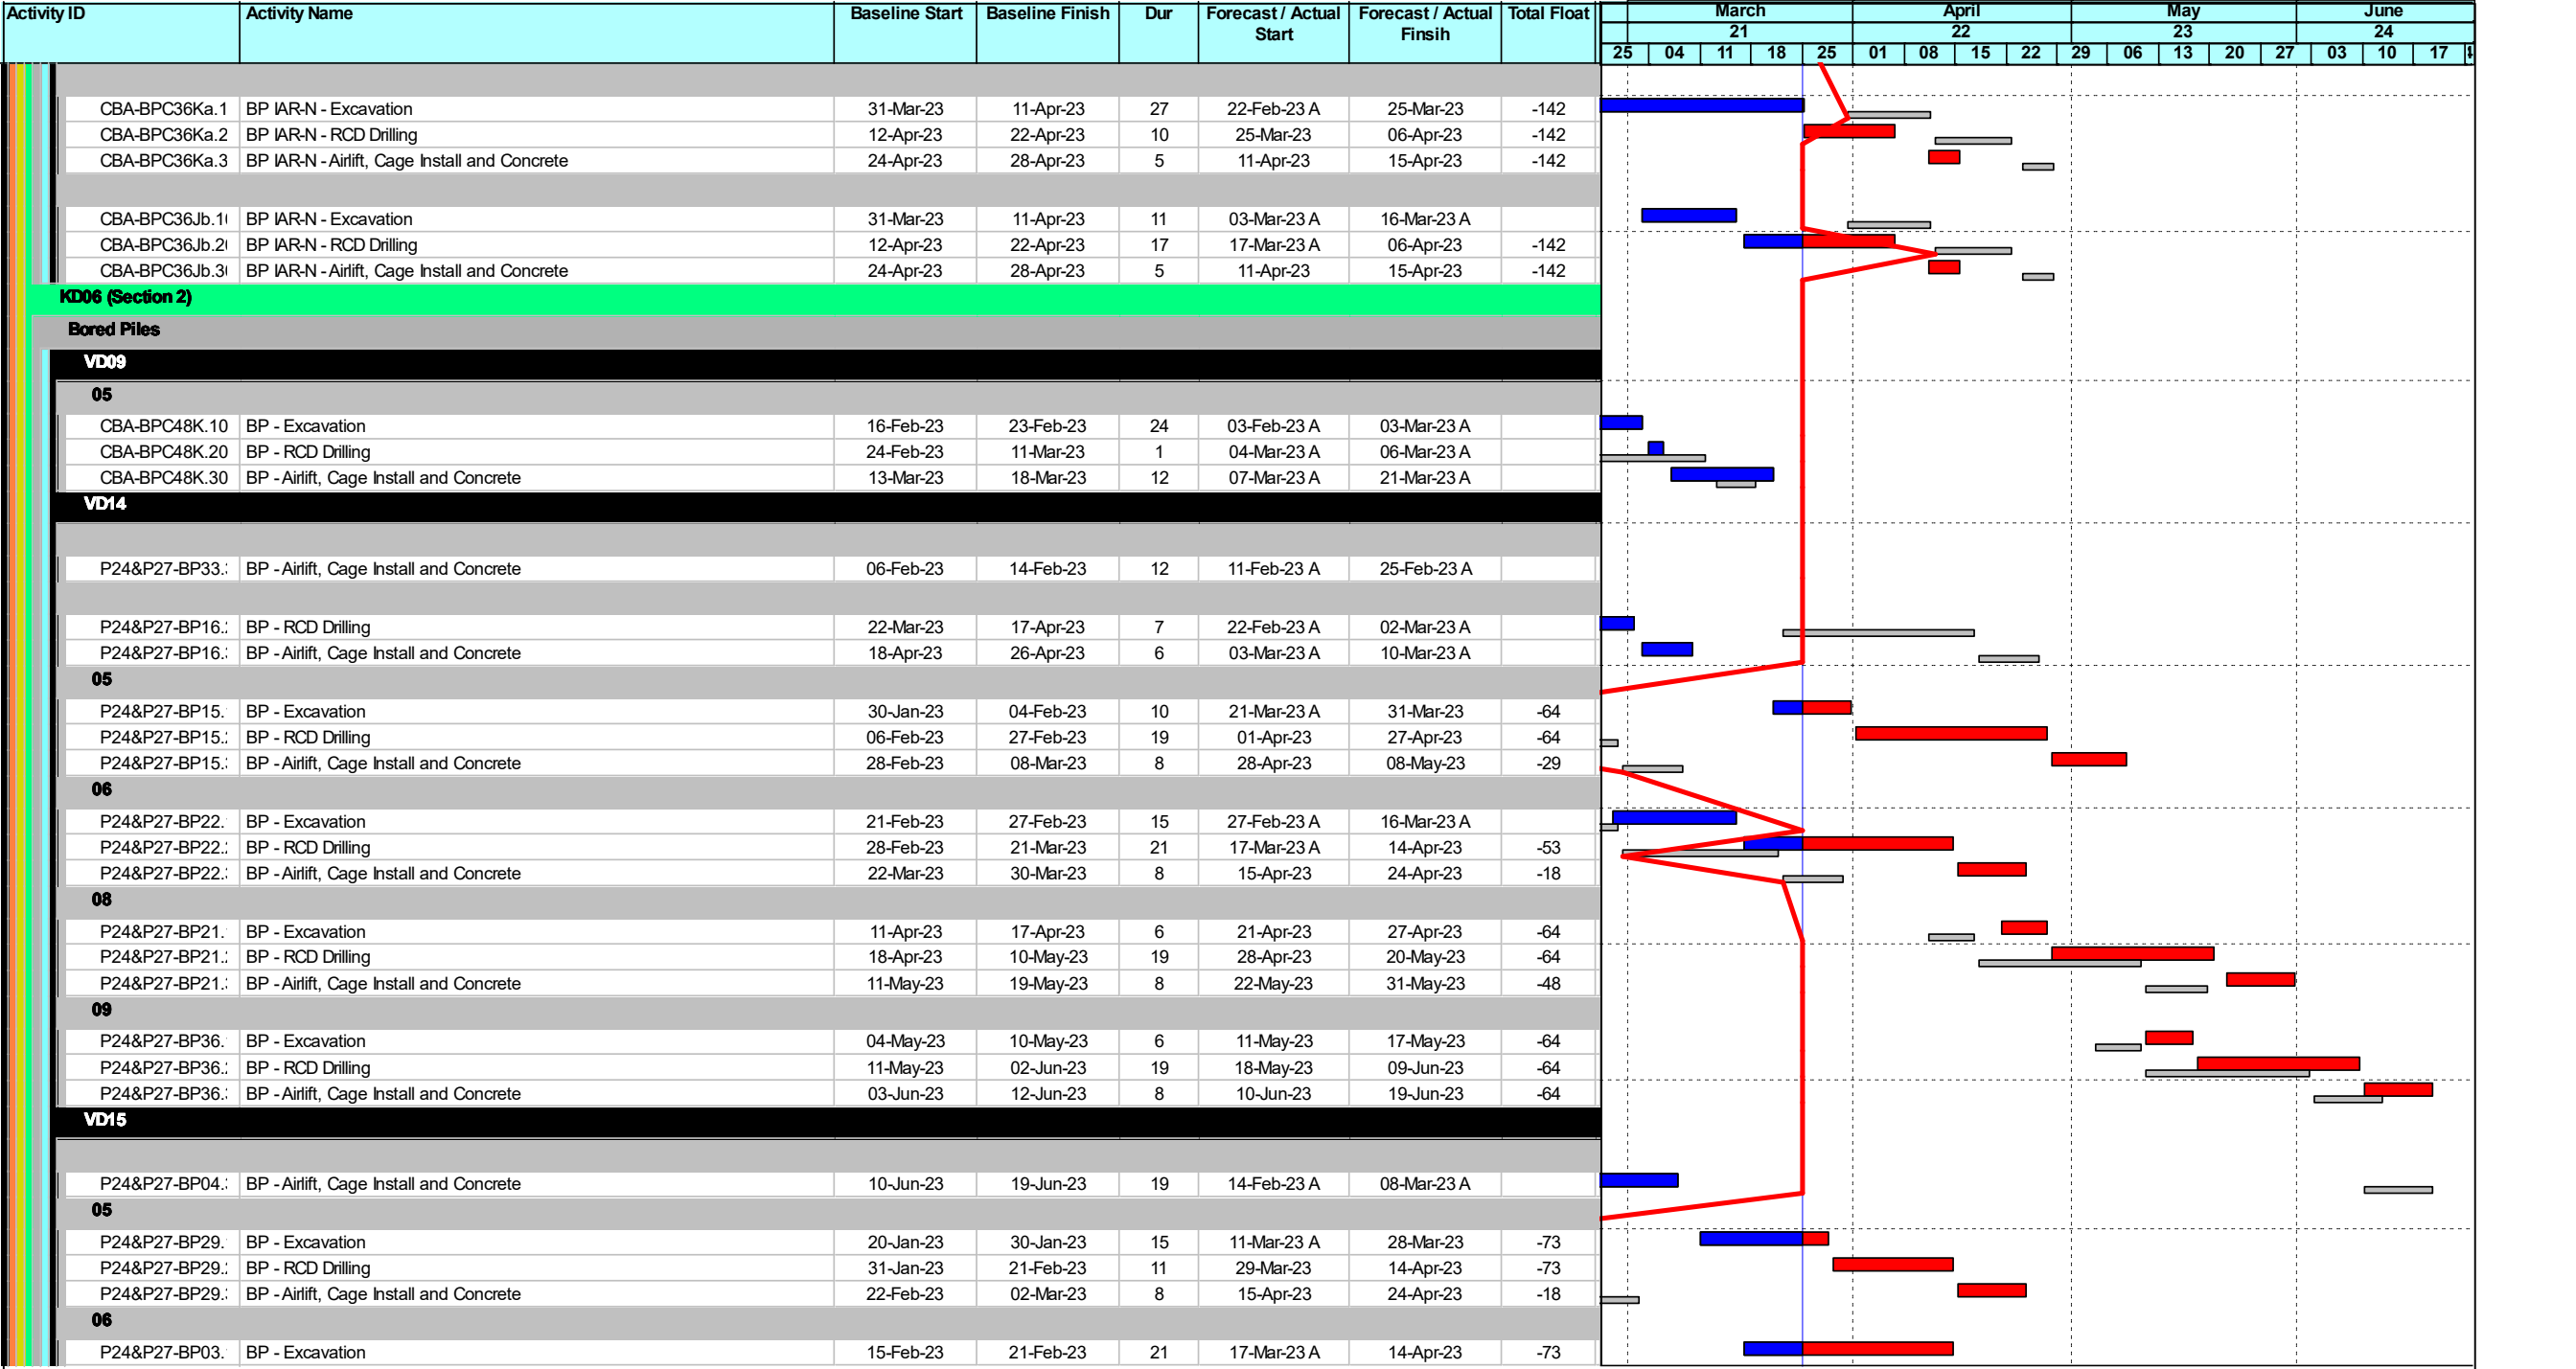■	Planned	◆	Planned MS
■	Critical	◆	Critical MS
■	Actual	◆	Actual MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 24 March 2023
Based on CMWP Rev.0 (3rd Draft)

Date	Revision	Checked	Approved
4-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C




	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 24 March 2023
Based on CMWP Rev.0 (3rd Draft)



Date	Revision	Checked	Approved
4-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C

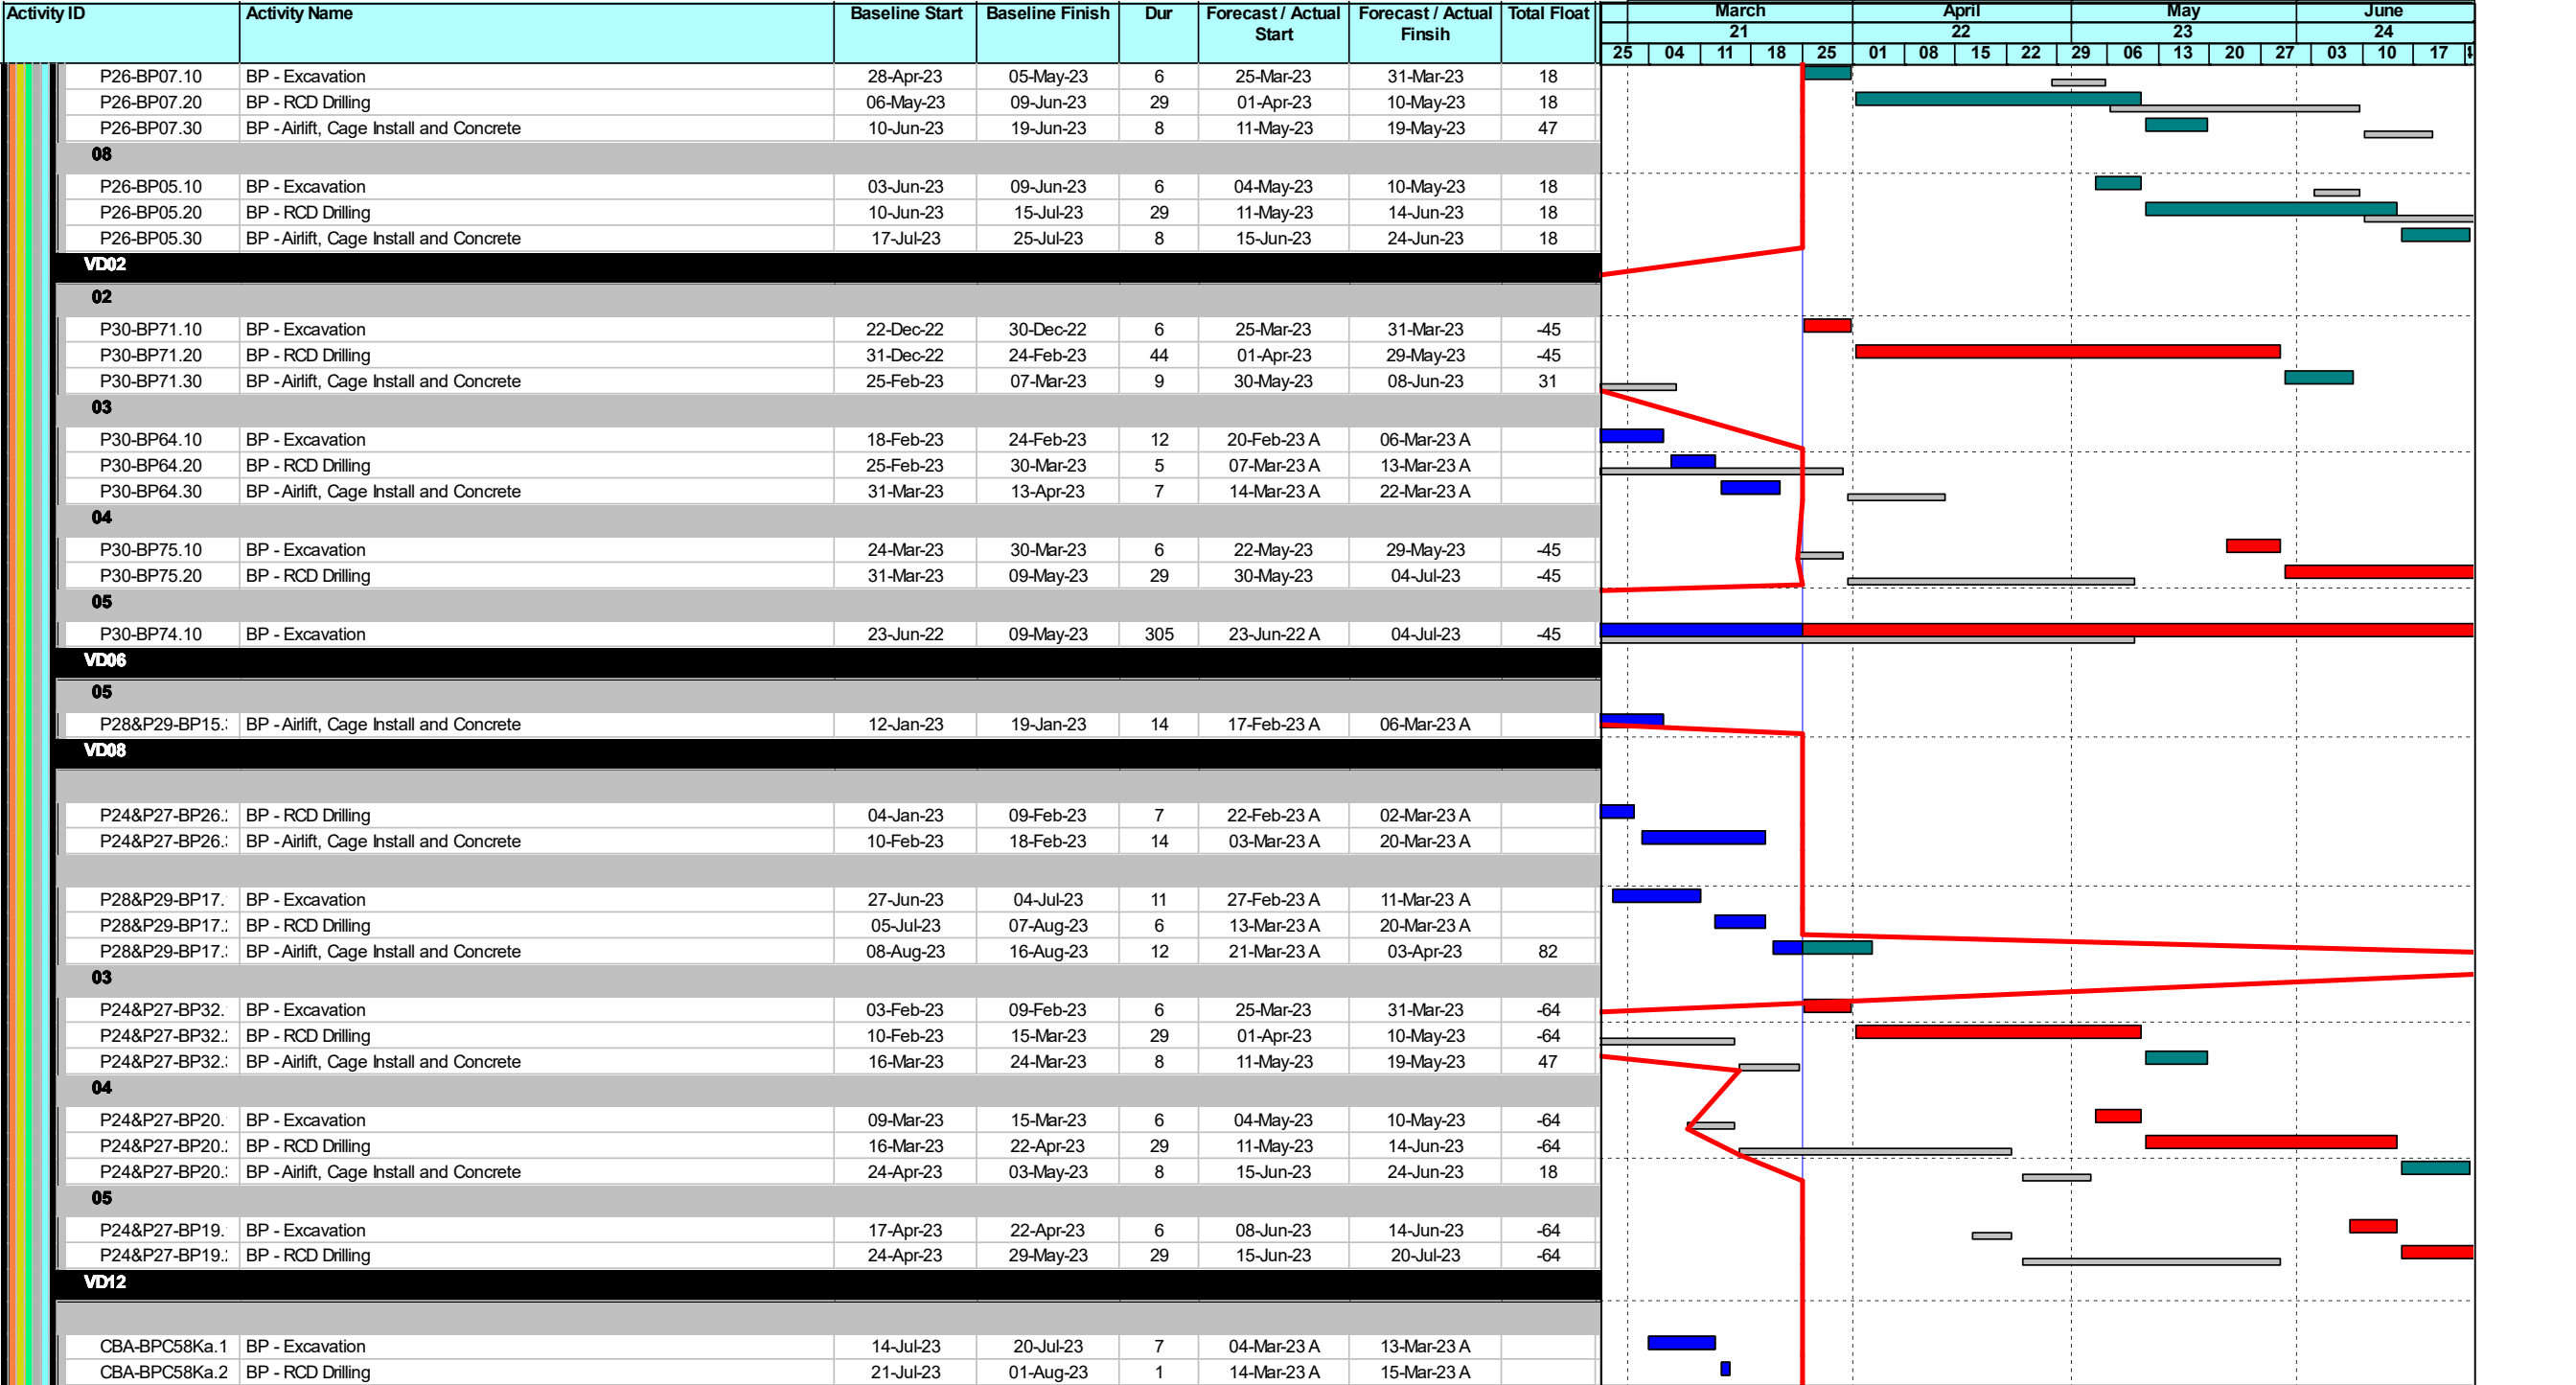








	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS

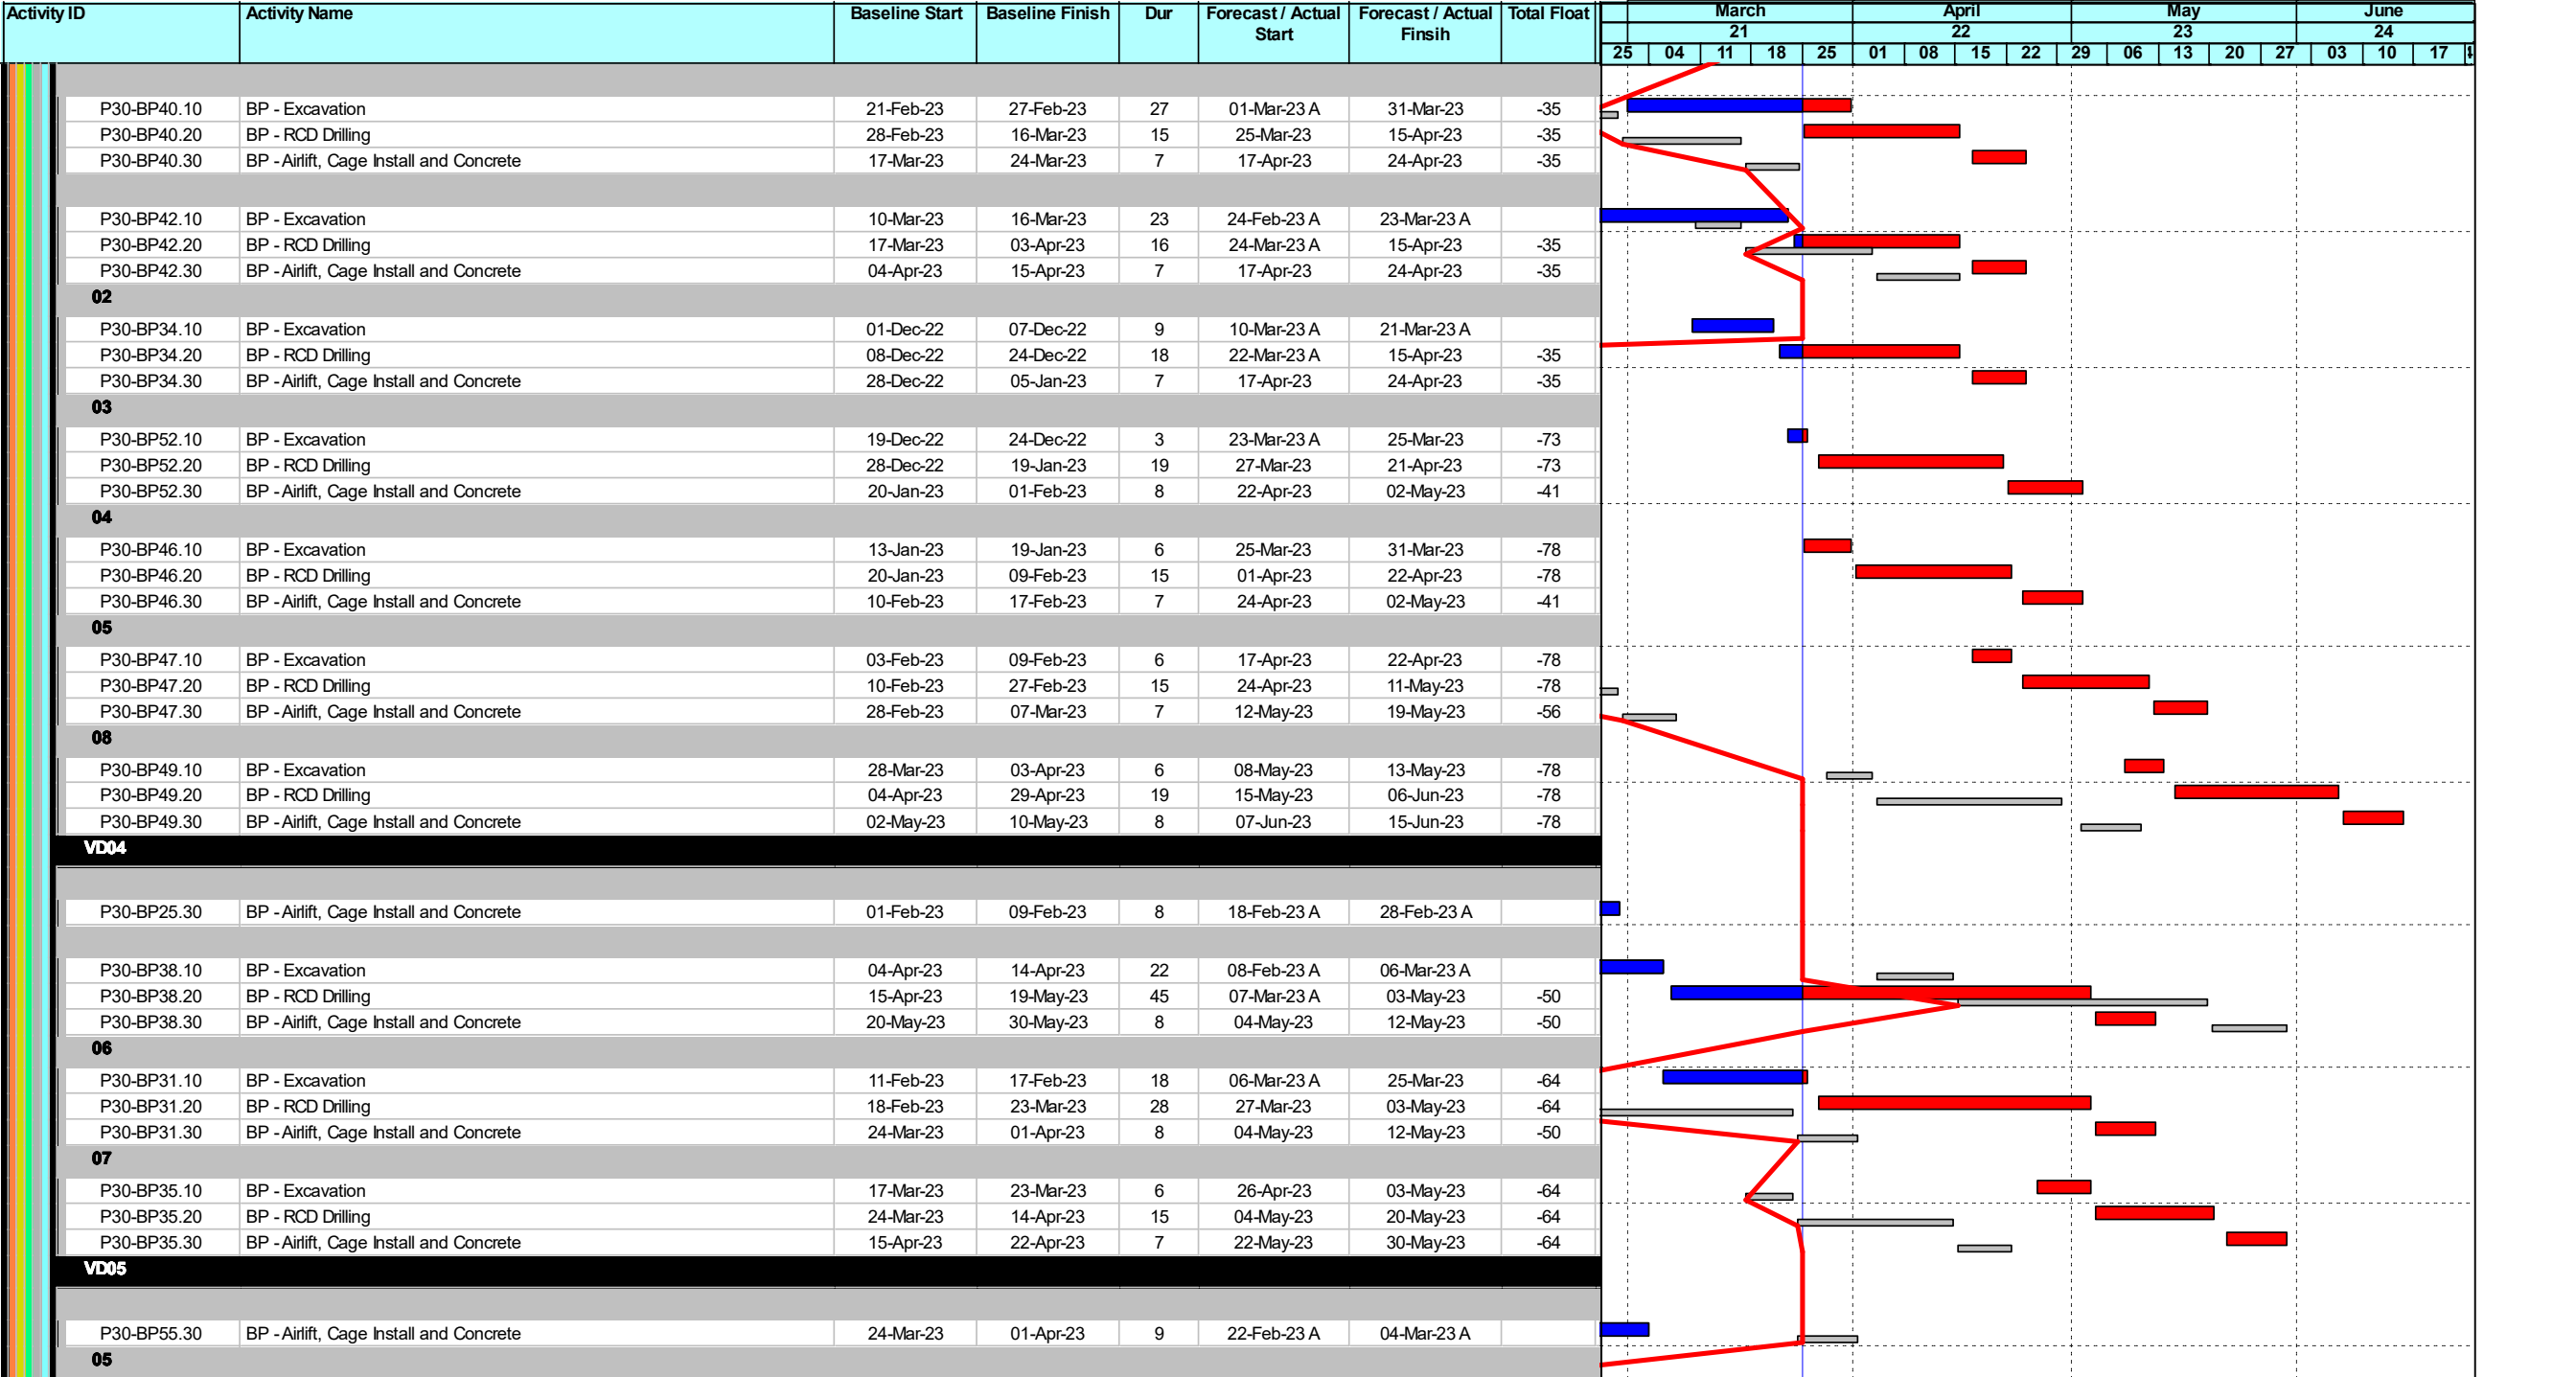West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 24 March 2023
Based on CMWP Rev.0 (3rd Draft)



Date	Revision	Checked	Approved
4-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C










	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 24 March 2023
Based on CMWP Rev.0 (3rd Draft)

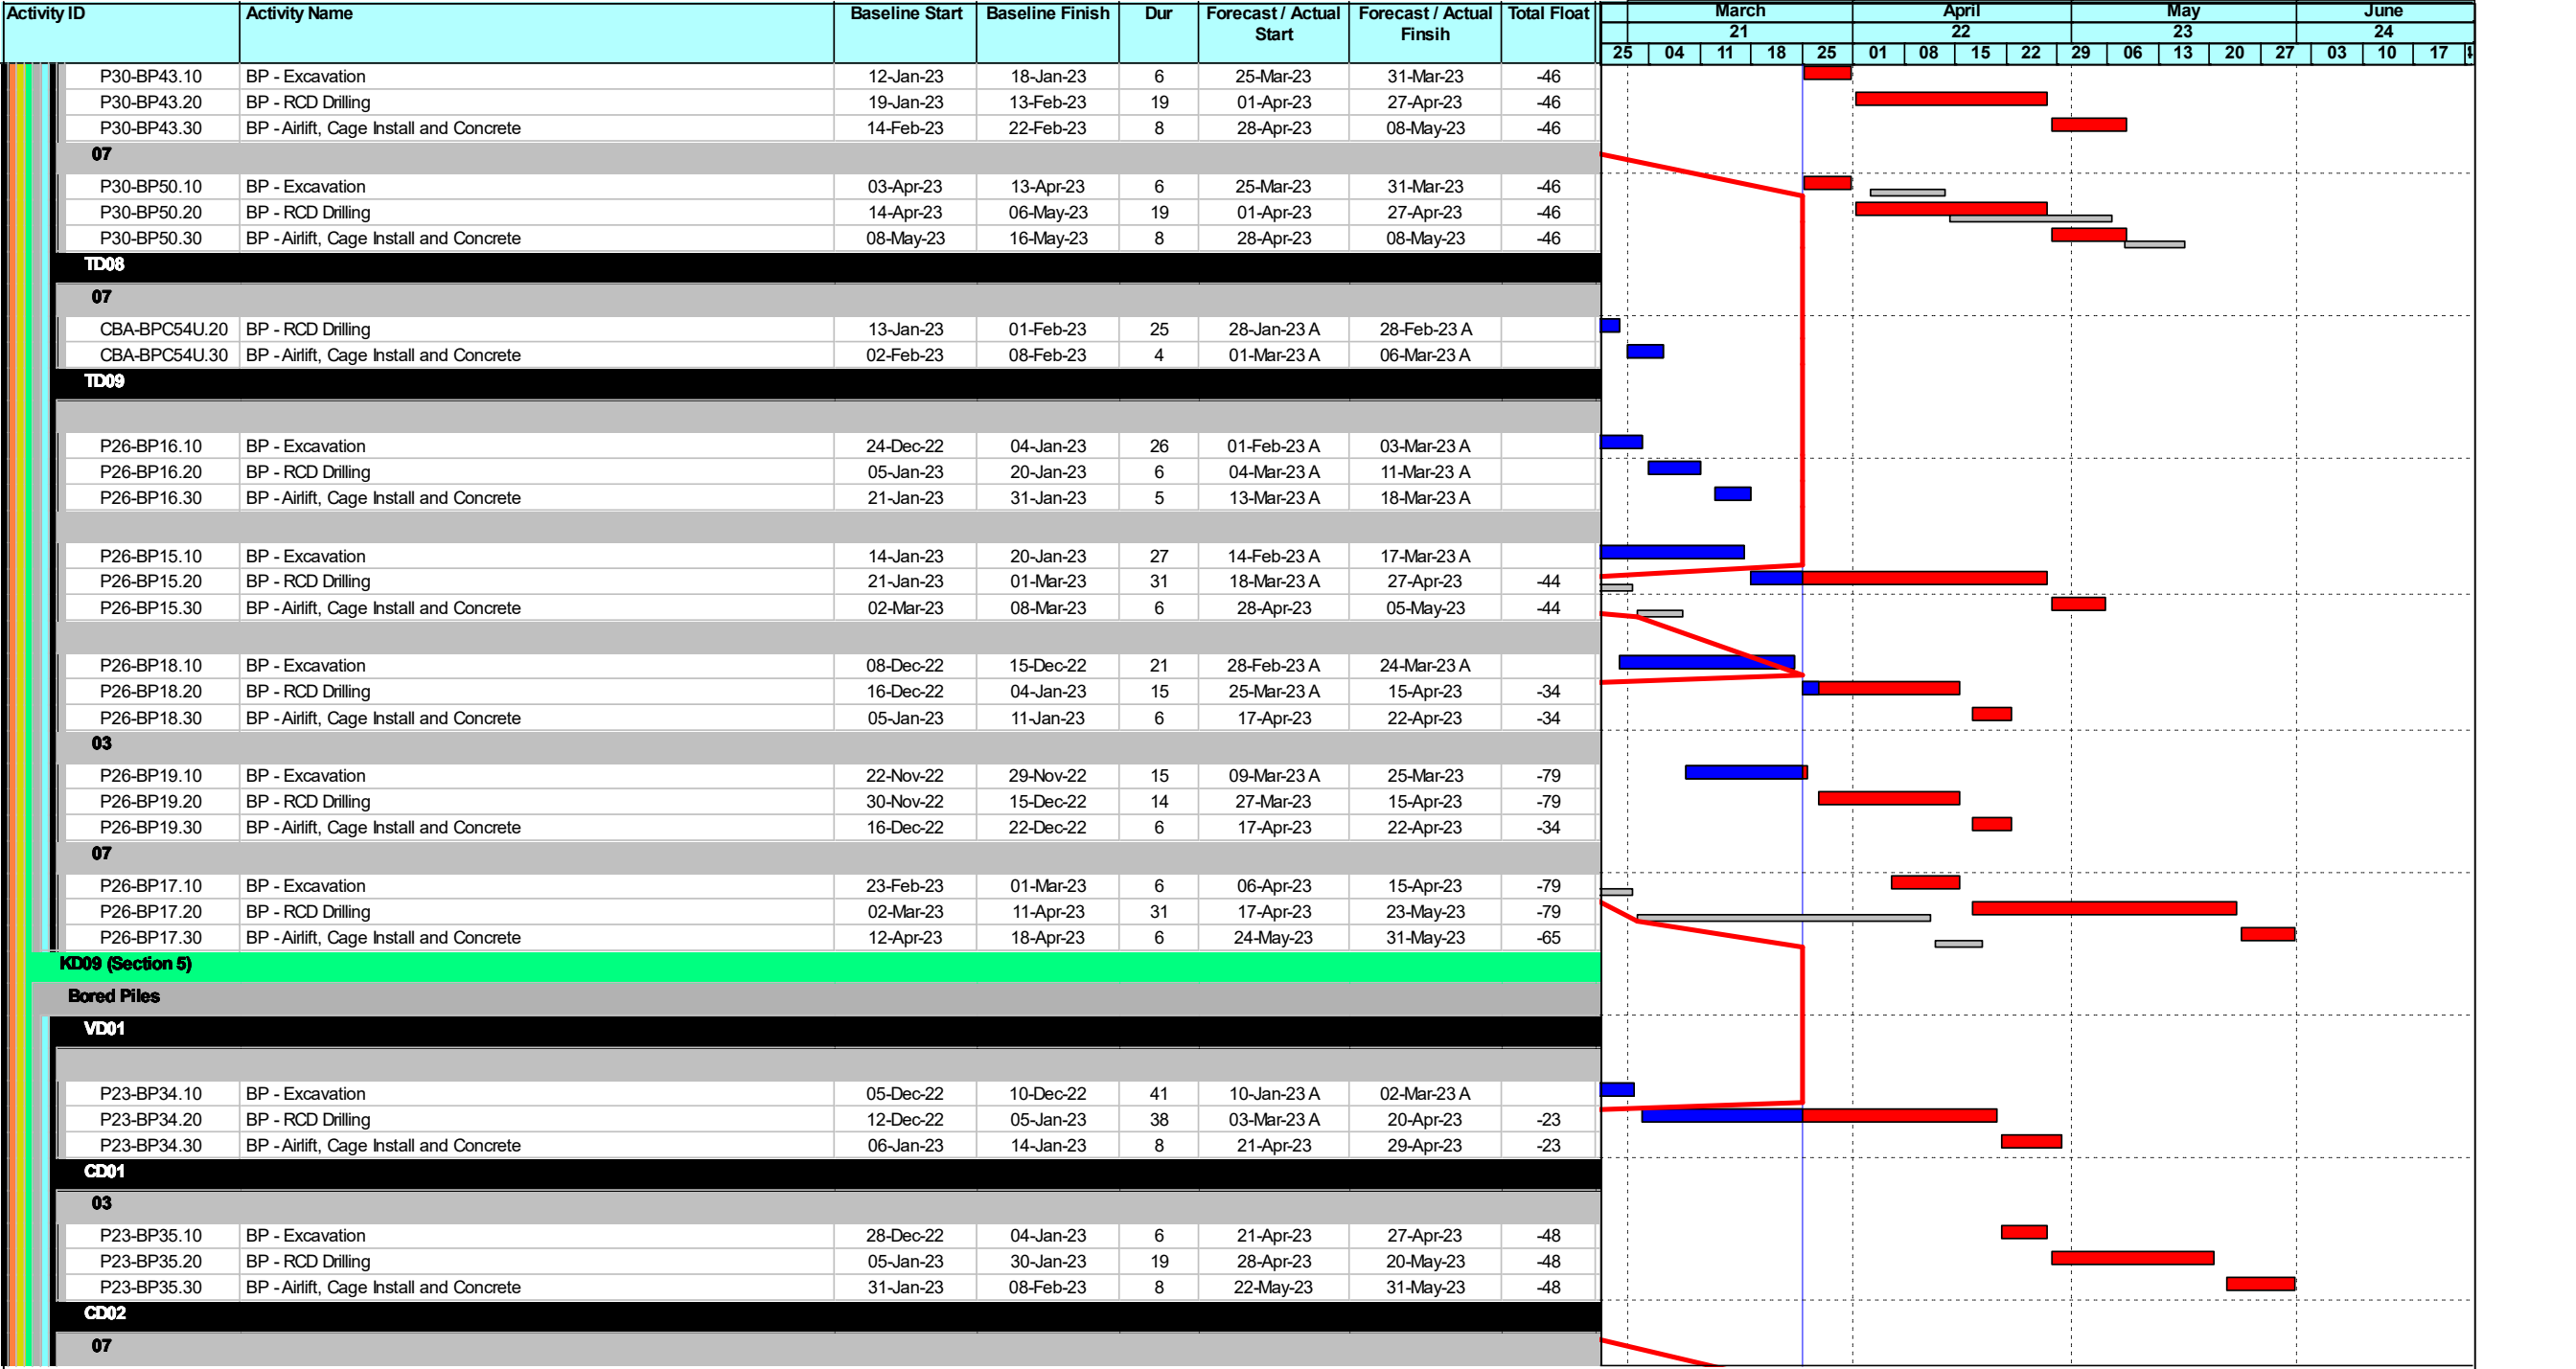

Date	Revision	Checked	Approved
4-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C










	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 24 March 2023
 Based on CMWP Rev.0 (3rd Draft)

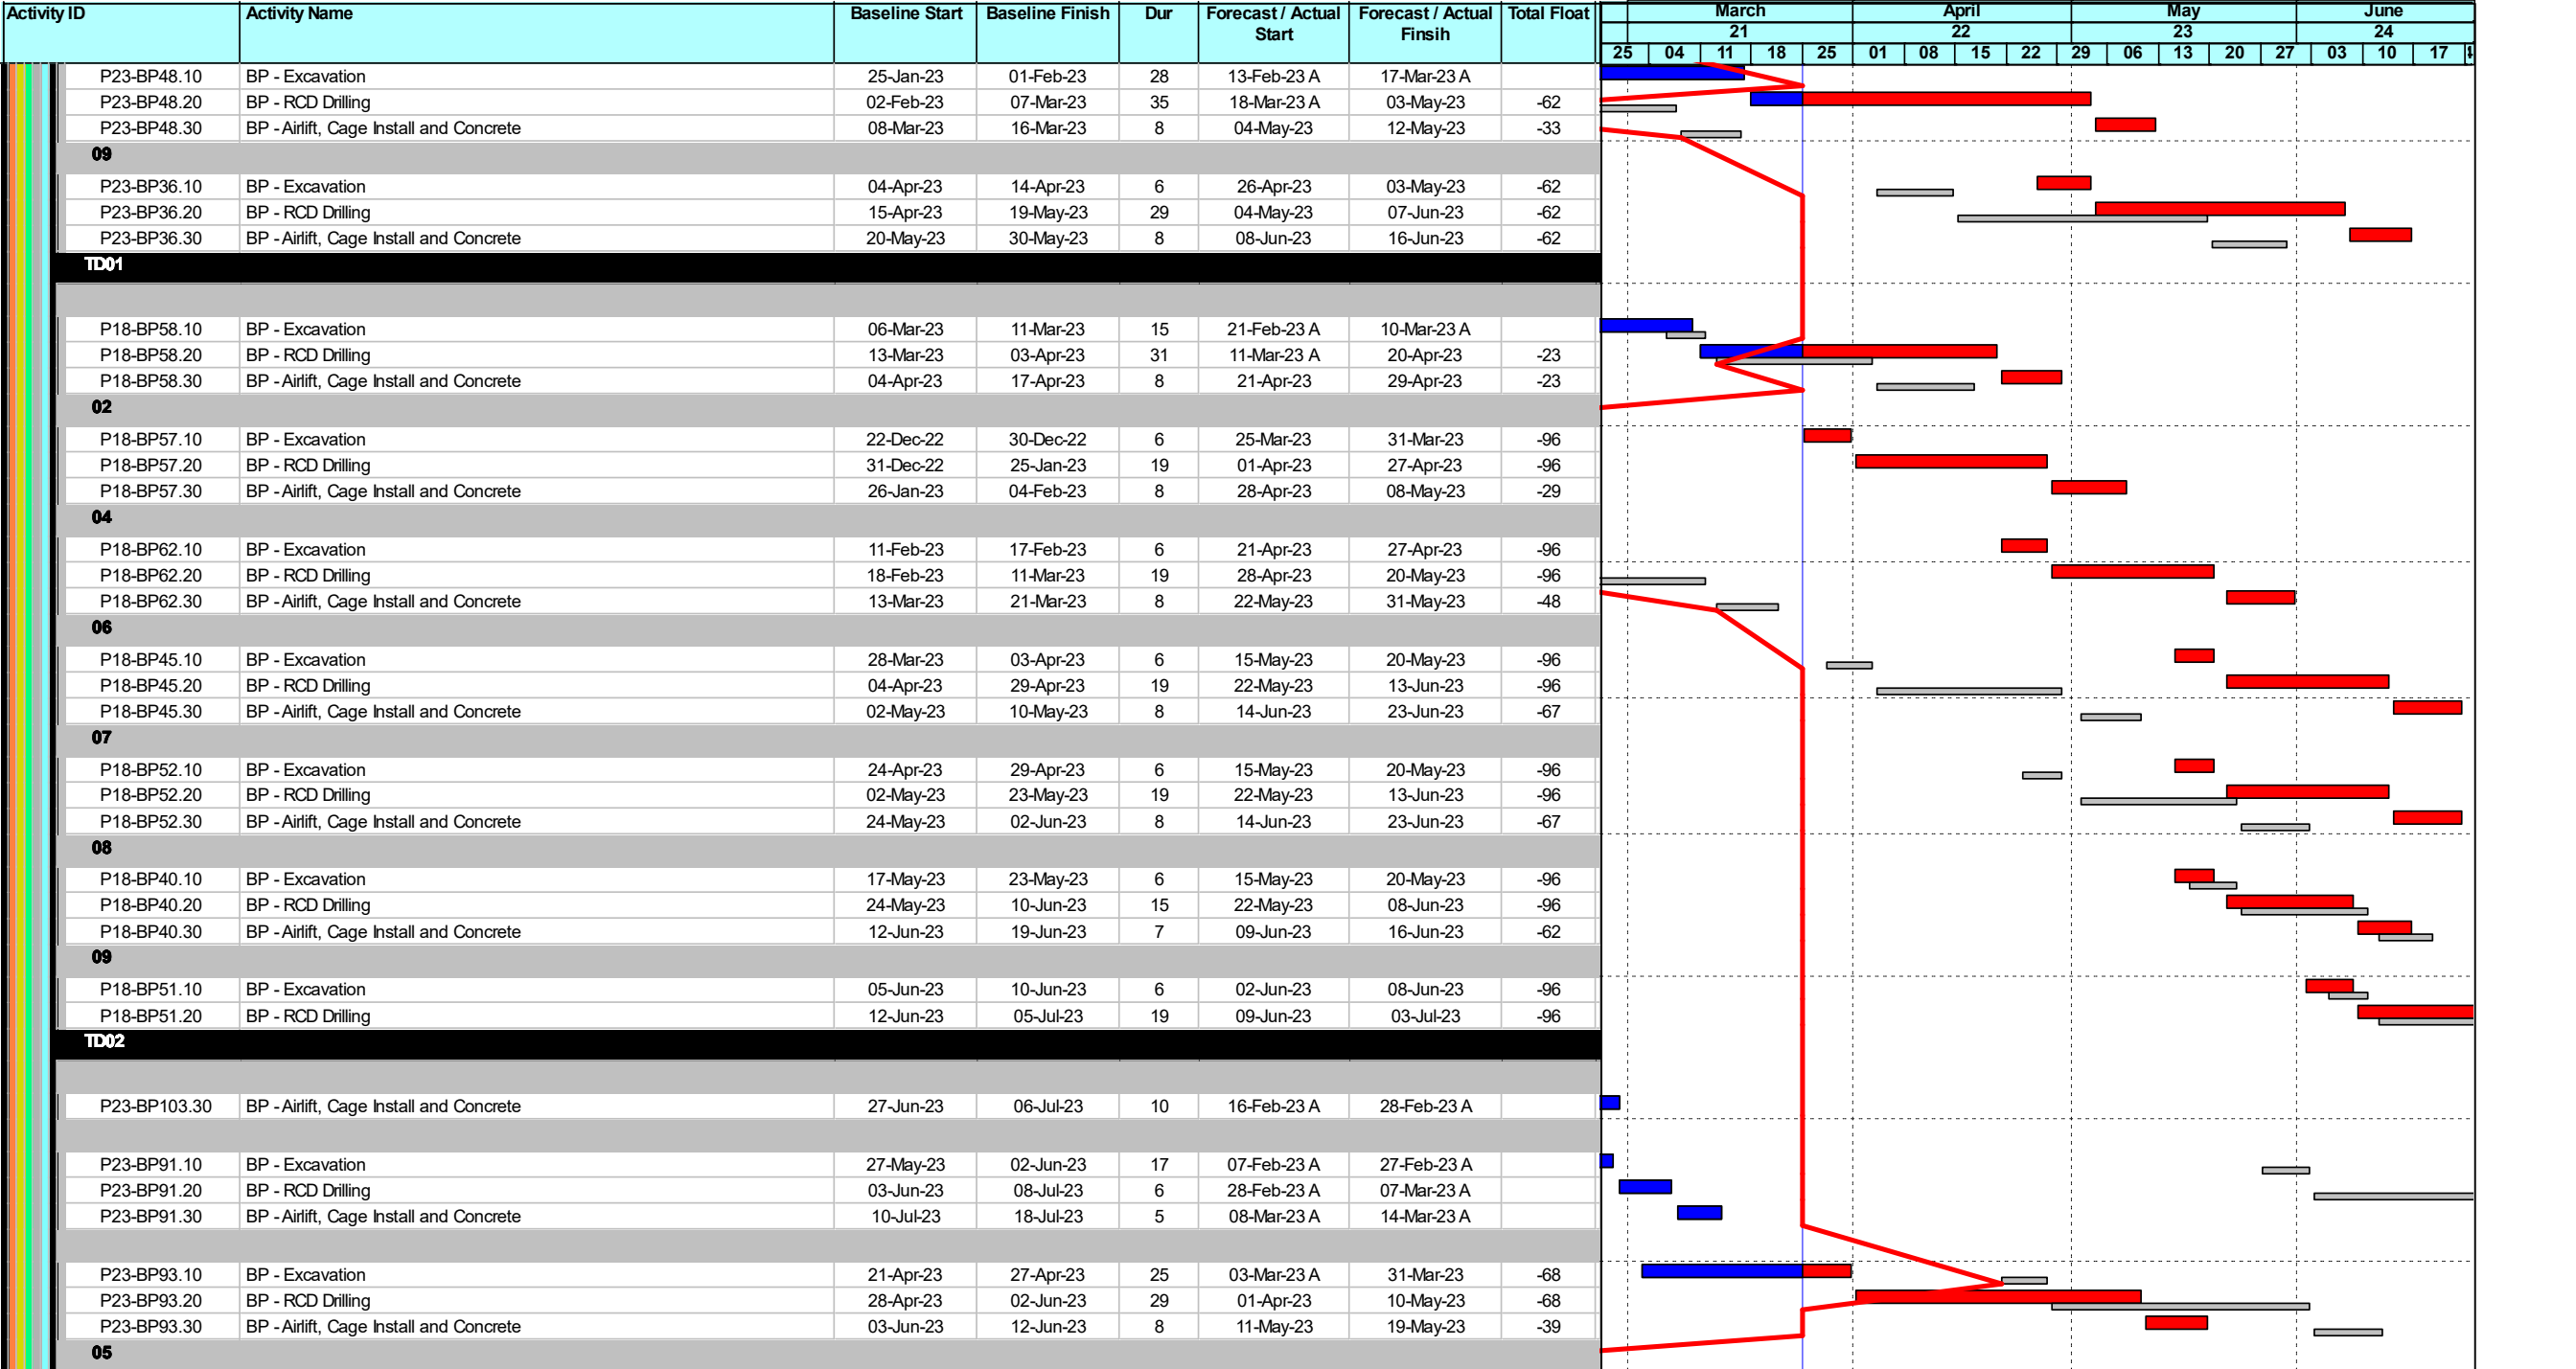

Date	Revision	Checked	Approved
4-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C










	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 24 March 2023
Based on CMWP Rev.0 (3rd Draft)

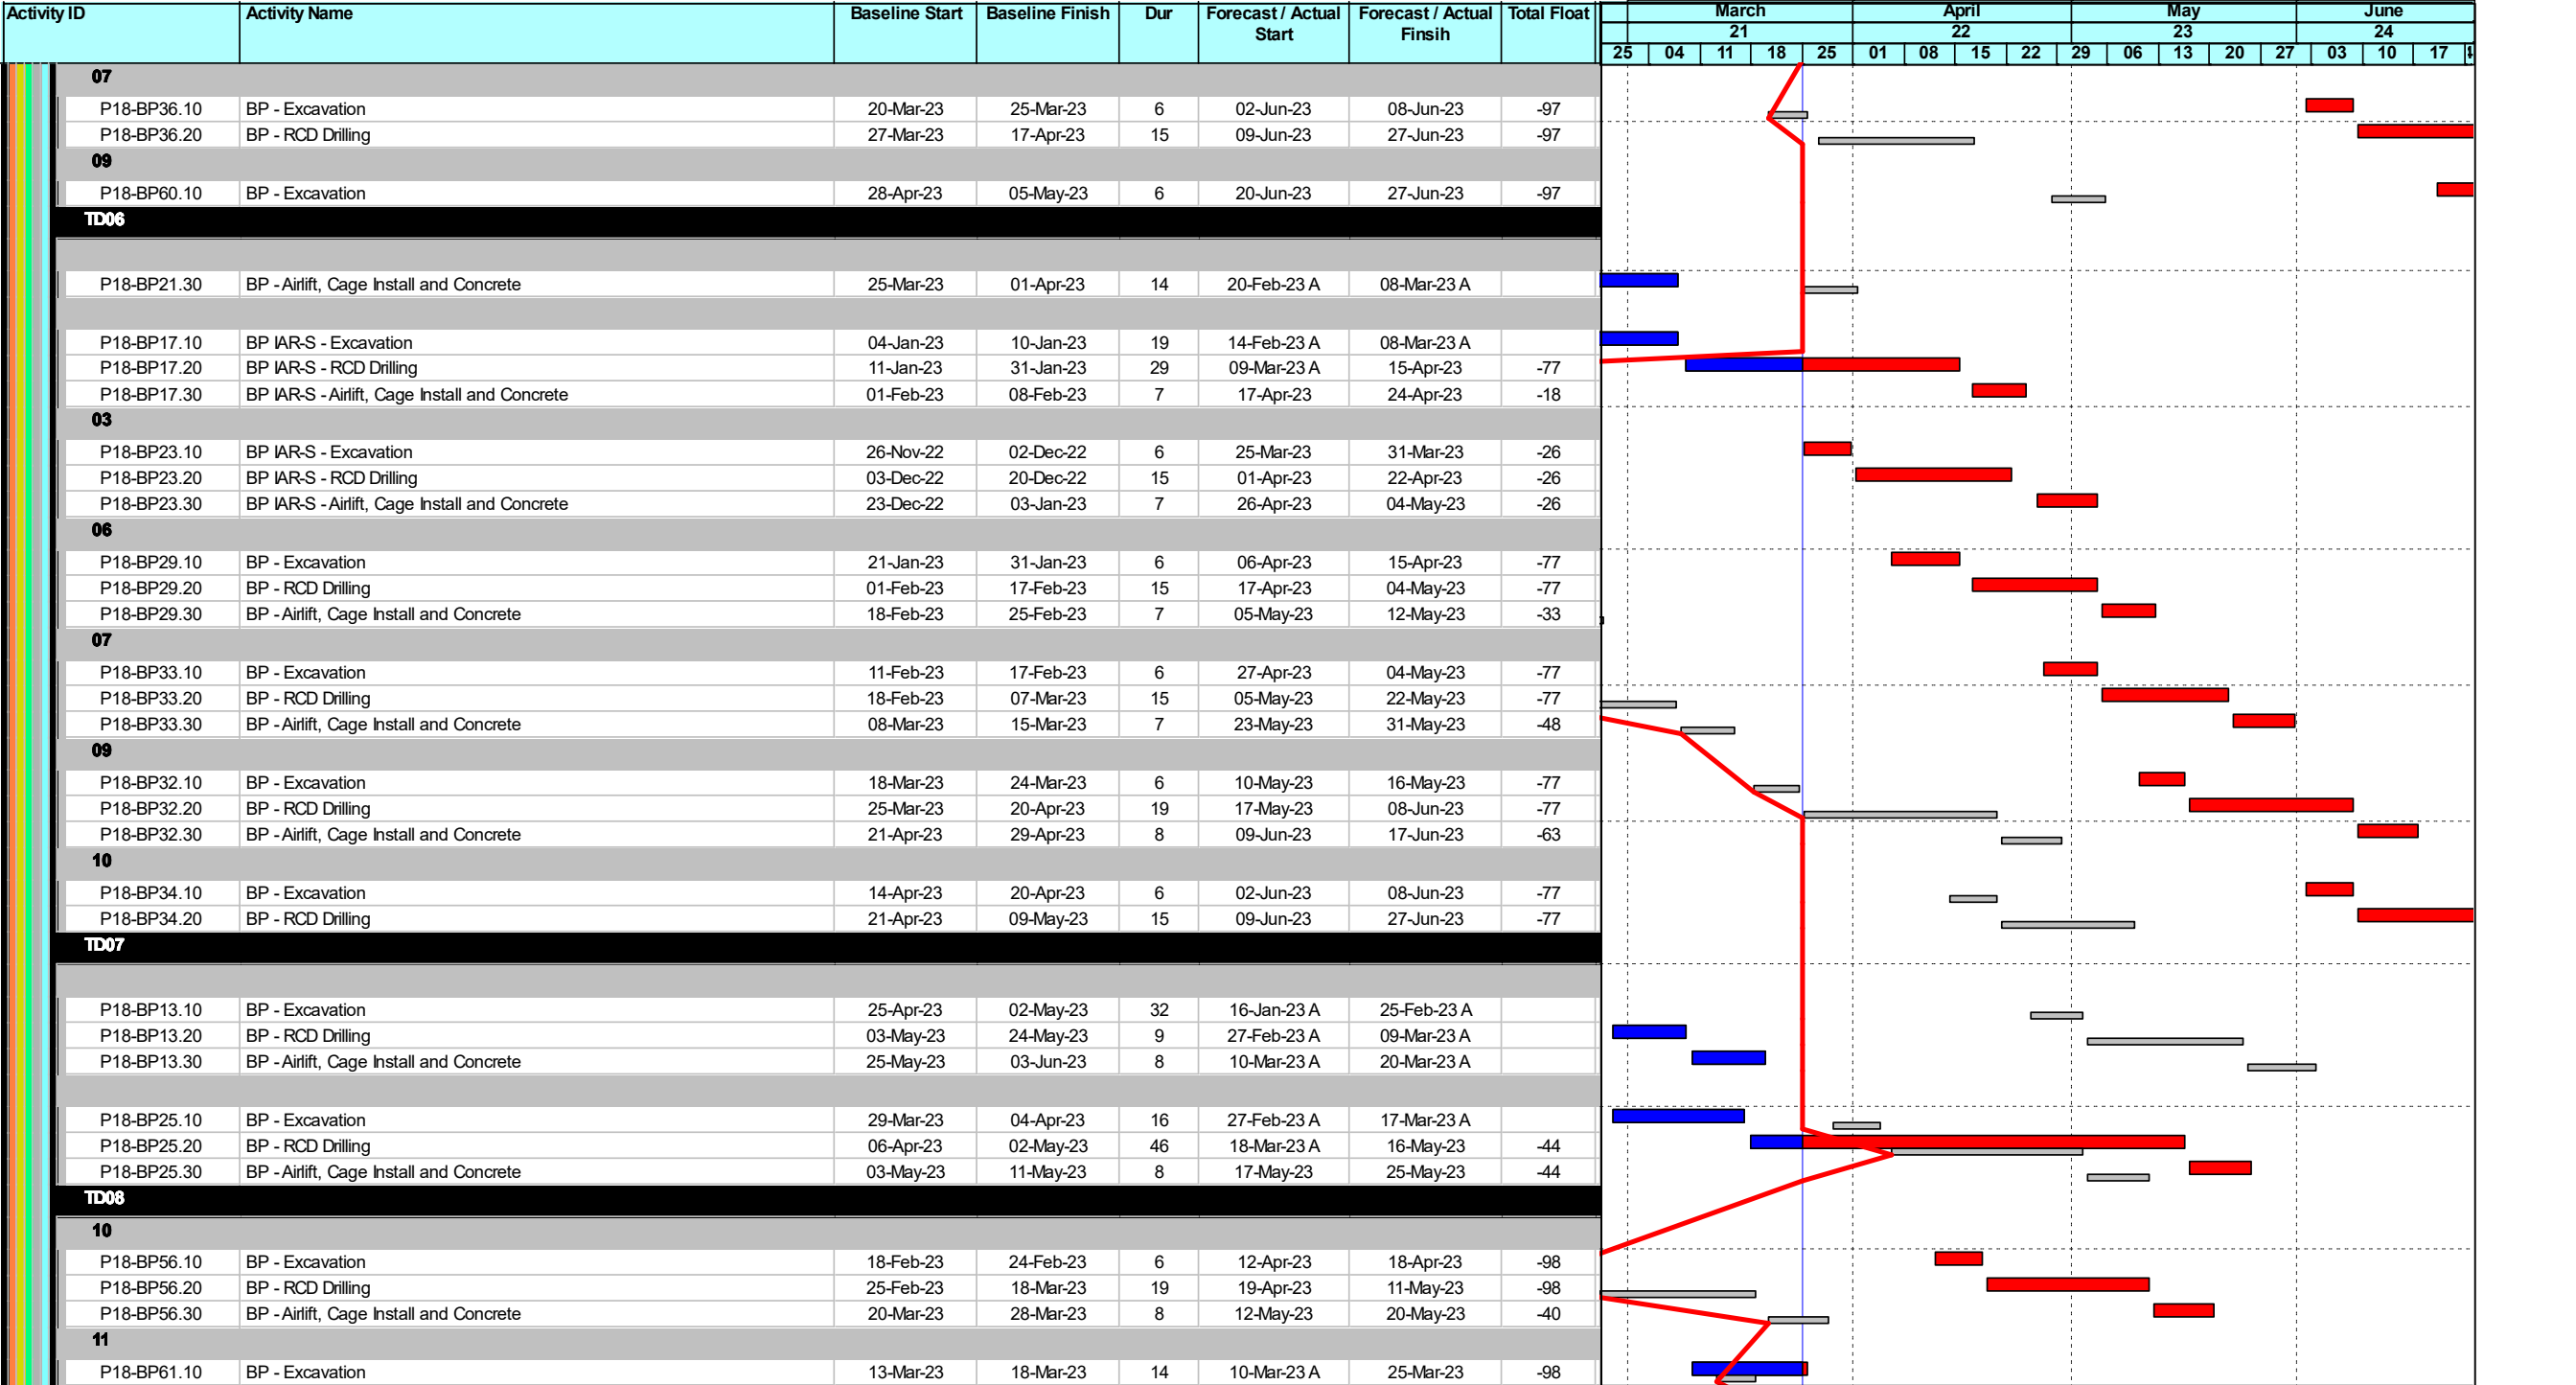

Date	Revision	Checked	Approved
4-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C



	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 24 March 2023
 Based on CMWP Rev.0 (3rd Draft)



Date	Revision	Checked	Approved
4-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	March				April				May				June			
								21				22				23				24			
								25	04	11	18	25	01	08	15	22	29	06	13	20	27	03	10
KD08.TS.1000	Sonic Logging Test and Interfacing Coring (All BP)	04-Jul-22	11-Jun-23	359	04-Jul-22 A	27-Jun-23	-98																
SSHP																							
KD08.TS.1120	Submit BA14	15-Nov-22	21-Nov-22	7	25-Mar-23	31-Mar-23	-4																
KD08.TS.1140	Selection of Pile for Static Load Test	22-Nov-22	05-Dec-22	14	01-Apr-23	14-Apr-23	-4																
KD08.TS.1160	Static Load Test of Selected Pile	06-Dec-22	19-Dec-22	14	15-Apr-23	28-Apr-23	-4																
KD08.TS.1180	Obtain BA14 Acknowledgement / Satisfaction of CA, Completion As-built Drawings, Reports & Records	20-Dec-22	16-Jan-23	28	29-Apr-23	26-May-23	-4																
KD09 (Section 5) (incl. BP for KD02 (Stage 5-1))																							
BP																							
KD09.TS.1000	Sonic Logging Test and Interfacing Coring (All BP)	23-May-22	12-Aug-23	447	23-May-22 A	12-Aug-23	-124																
Attendance to Other Project Contractors (optional works item no. 2A to 2E)																							
S2.AT.0000	Attendance at Section 2 Area (optional works item no. 2B) (Duration TBC)	13-May-23	01-Jun-23	20	13-May-23	01-Jun-23	11																
S4.AT.0000	Attendance at Section 4 Area (optional works item no. 2D) (not exercised)	22-Feb-23	13-Mar-23	19	22-Feb-23 A	13-Mar-23 A																	
S5.AT.0000	Attendance at Section 5 Area (optional works item no. 2E) (not exercised)	14-Mar-23	02-Apr-23	19	14-Mar-23 A	02-Apr-23 A																	

	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 24 March 2023
Based on CMWP Rev.0 (3rd Draft)



Date	Revision	Checked	Approved
4-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	March			April				May			June			July
								21			22				23			24			25
								11	18	25	01	08	15	22	29	06	13	20	27	03	10

Piling for Integrated Basement and U/G Road In Zone 2B & 2C

Contract Dates

Optional Works subjected to CA's Instruction

CO2B	Last CAI date for Optional Works Item No.2B (330 Days to 660 Days after Commencement)	13-May-23	0	13-May-23	11
CO2C	Last CAI date for Optional Works Item No.2C (330 Days to 710 Days after Commencement)	02-Jul-23	0	02-Jul-23	71
CO2E	Last CAI date for Optional Works Item No.2E (330 Days to 600 Days after Commencement)	14-Mar-23	0	14-Mar-23 A	

Construction Stage

File Construction

KD05 (Section 1)

Bored Piles - Drainage Diversion

CD04

05

P17-BP13.10	BP IAR-N - Excavation	03-Feb-23	09-Feb-23	10	27-Feb-23 A	10-Mar-23 A	
P17-BP13.20	BP IAR-N - RCD Drilling	10-Feb-23	27-Feb-23	8	11-Mar-23 A	21-Mar-23 A	
P17-BP13.30	BP IAR-N - Airlift, Cage Install and Concrete	28-Feb-23	07-Mar-23	20	22-Mar-23 A	18-Apr-23	-144

CD07

04

P17-BP19.10	BP - Excavation	27-Jan-23	03-Feb-23	6	11-Apr-23	17-Apr-23	-204
P17-BP19.20	BP - RCD Drilling	04-Feb-23	21-Feb-23	15	18-Apr-23	05-May-23	-204
P17-BP19.30	BP - Airlift, Cage Install and Concrete	22-Feb-23	01-Mar-23	6	06-May-23	12-May-23	-164

CD08

01

P17-BP20.10	BP - Excavation	17-Feb-23	23-Feb-23	4	28-Apr-23	03-May-23	-204
P17-BP20.20	BP - RCD Drilling	24-Feb-23	13-Mar-23	15	04-May-23	20-May-23	-204
P17-BP20.30	BP - Airlift, Cage Install and Concrete	14-Mar-23	21-Mar-23	7	22-May-23	30-May-23	-178

02

P17-BP21.10	BP IAR-N - Excavation	07-Mar-23	13-Mar-23	4	17-May-23	20-May-23	-204
P17-BP21.20	BP IAR-N - RCD Drilling	14-Mar-23	30-Mar-23	15	22-May-23	08-Jun-23	-204
P17-BP21.30	BP IAR-N - Airlift, Cage Install and Concrete	31-Mar-23	12-Apr-23	7	09-Jun-23	16-Jun-23	-193

03

P17-BP18.10	BP IAR-N - Excavation	24-Mar-23	30-Mar-23	4	31-May-23	03-Jun-23	-204
P17-BP18.20	BP IAR-N - RCD Drilling	31-Mar-23	21-Apr-23	15	05-Jun-23	21-Jun-23	-204
P17-BP18.30	BP IAR-N - Airlift, Cage Install and Concrete	22-Apr-23	29-Apr-23	7	23-Jun-23	30-Jun-23	-204

Bored Piles - Gantry Gate A

CD06


08

CBA-BP01.10	BP - Excavation	20-Jan-23	31-Jan-23	16	27-Mar-23 A	18-Apr-23	-164
CBA-BP01.20	BP - RCD Drilling	01-Feb-23	16-Feb-23	14	19-Apr-23	05-May-23	-164
CBA-BP01.30	BP - Airlift, Cage Install and Concrete	17-Feb-23	23-Feb-23	6	06-May-23	12-May-23	-164

CD07

02

P22&P19-BP26.:	BP - RCD Drilling	16-Jul-22	03-Dec-22	223	16-Jul-22 A	17-Apr-23	-151
P22&P19-BP26.:	BP - Airlift, Cage Install and Concrete	05-Dec-22	13-Dec-22	8	18-Apr-23	26-Apr-23	-151

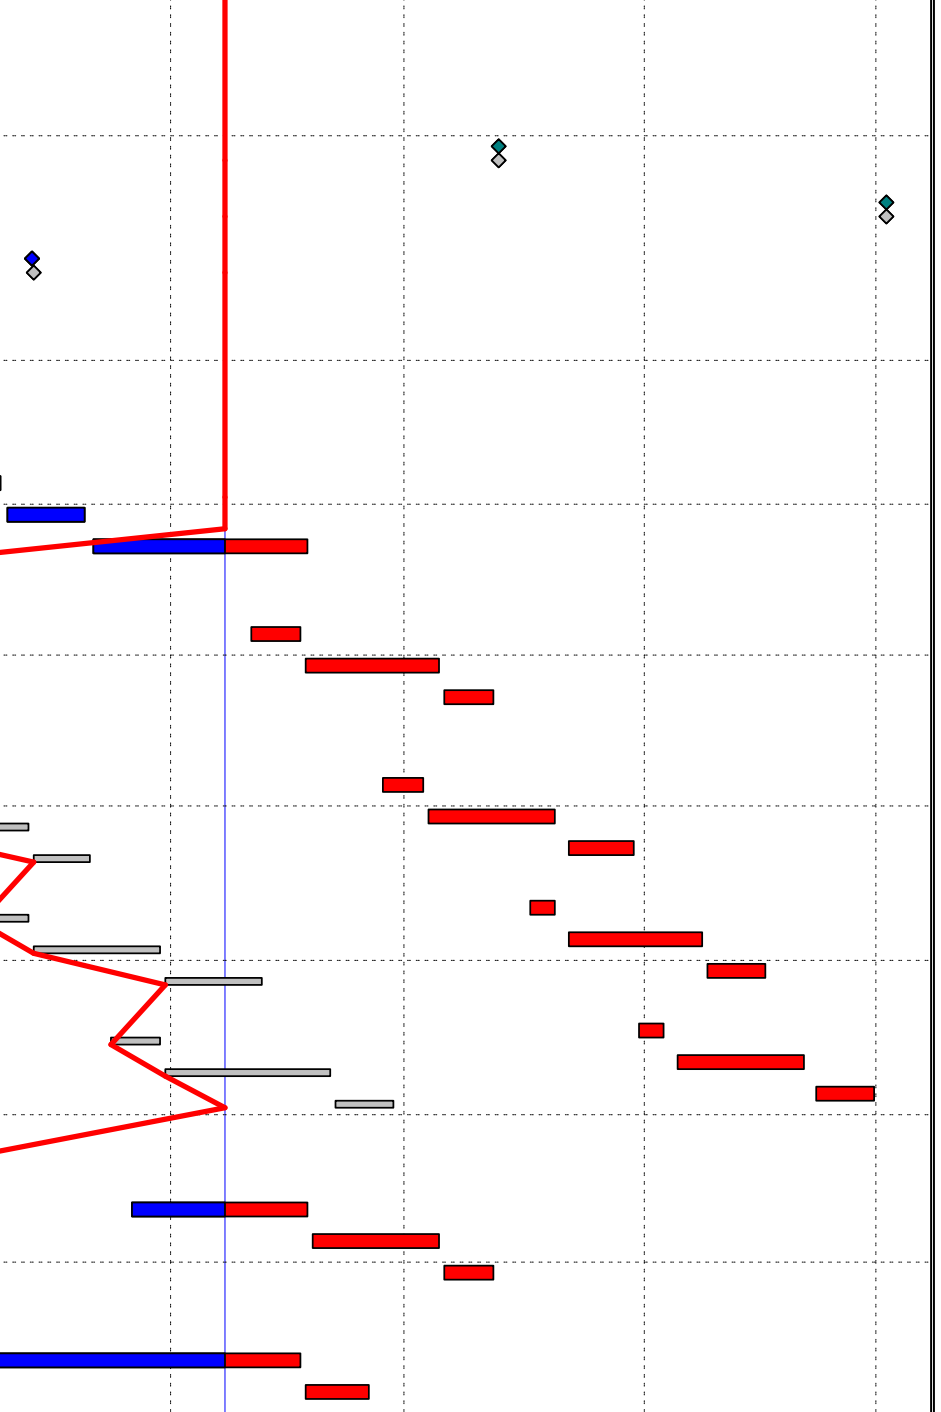


	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS

Date	Revision	Checked	Approved
04-Mar-23	R0	KL	B
02-Dec-23	R03D	KL	C

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	March			April				May			June			July
								21			22				23			24			25
								11	18	25	01	08	15	22	29	06	13	20	27	03	10


Bored Piles							
CD05							
05							
P17-BP01.20	BP - RCD Drilling	07-Mar-23	23-Mar-23	8	04-Mar-23 A	14-Mar-23 A	
P17-BP01.30	BP - Airlift, Cage Install and Concrete	24-Mar-23	31-Mar-23	26	15-Mar-23 A	18-Apr-23	-144
CD06							
05							
CBA-BP02.30	BP - Airlift, Cage Install and Concrete	30-Dec-22	06-Jan-23	25	10-Feb-23 A	11-Mar-23 A	
07							
CBA-BP03.10	BP - Excavation	04-Jan-23	11-Jan-23	12	13-Mar-23 A	27-Mar-23 A	
CBA-BP03.20	BP - RCD Drilling	12-Jan-23	31-Jan-23	2	28-Mar-23 A	30-Mar-23 A	
CBA-BP03.30	BP - Airlift, Cage Install and Concrete	01-Feb-23	07-Feb-23	11	31-Mar-23 A	17-Apr-23	-143
CD09							
02							
P17-BP08.30	BP IAR-N - Airlift, Cage Install and Concrete	17-Mar-23	24-Mar-23	10	07-Mar-23 A	18-Mar-23 A	
03							
P17-BP22.10	BP IAR-N - Excavation	10-Mar-23	16-Mar-23	12	06-Mar-23 A	20-Mar-23 A	
P17-BP22.20	BP IAR-N - RCD Drilling	17-Mar-23	03-Apr-23	29	21-Mar-23 A	27-Apr-23	-159
P17-BP22.30	BP IAR-N - Airlift, Cage Install and Concrete	04-Apr-23	15-Apr-23	7	28-Apr-23	06-May-23	-159
TD07							
04							
P18-BP01.10	BP - Excavation	15-Dec-22	21-Dec-22	6	11-Apr-23	17-Apr-23	-176
P18-BP01.20	BP - RCD Drilling	22-Dec-22	16-Jan-23	15	18-Apr-23	05-May-23	-176
P18-BP01.30	BP - Airlift, Cage Install and Concrete	17-Jan-23	27-Jan-23	3	06-May-23	09-May-23	-161
06							
P18-BP04.10	BP IAR-S - Excavation	04-Feb-23	10-Feb-23	13	10-Mar-23 A	25-Mar-23 A	
P18-BP04.20	BP IAR-S - RCD Drilling	11-Feb-23	28-Feb-23	30	27-Mar-23 A	05-May-23	-176
P18-BP04.30	BP IAR-S - Airlift, Cage Install and Concrete	01-Mar-23	08-Mar-23	3	06-May-23	09-May-23	-161
09							
P18-BP07.10	BP IAR-S - Excavation	11-Mar-23	17-Mar-23	6	28-Apr-23	05-May-23	-176
P18-BP07.20	BP IAR-S - RCD Drilling	18-Mar-23	04-Apr-23	15	06-May-23	23-May-23	-176
P18-BP07.30	BP IAR-S - Airlift, Cage Install and Concrete	06-Apr-23	17-Apr-23	3	24-May-23	27-May-23	-176
TD09							
CBA-BPC36Ka.1	BP IAR-N - Excavation	31-Mar-23	11-Apr-23	37	22-Feb-23 A	11-Apr-23	-152
CBA-BPC36Ka.2	BP IAR-N - RCD Drilling	12-Apr-23	22-Apr-23	10	11-Apr-23	21-Apr-23	-152
CBA-BPC36Ka.3	BP IAR-N - Airlift, Cage Install and Concrete	24-Apr-23	28-Apr-23	5	22-Apr-23	27-Apr-23	-152
CBA-BPC36Jb.10	BP IAR-N - Excavation	31-Mar-23	11-Apr-23	11	03-Mar-23 A	16-Mar-23 A	
CBA-BPC36Jb.20	BP IAR-N - RCD Drilling	12-Apr-23	22-Apr-23	27	17-Mar-23 A	21-Apr-23	-152
CBA-BPC36Jb.30	BP IAR-N - Airlift, Cage Install and Concrete	24-Apr-23	28-Apr-23	5	22-Apr-23	27-Apr-23	-152

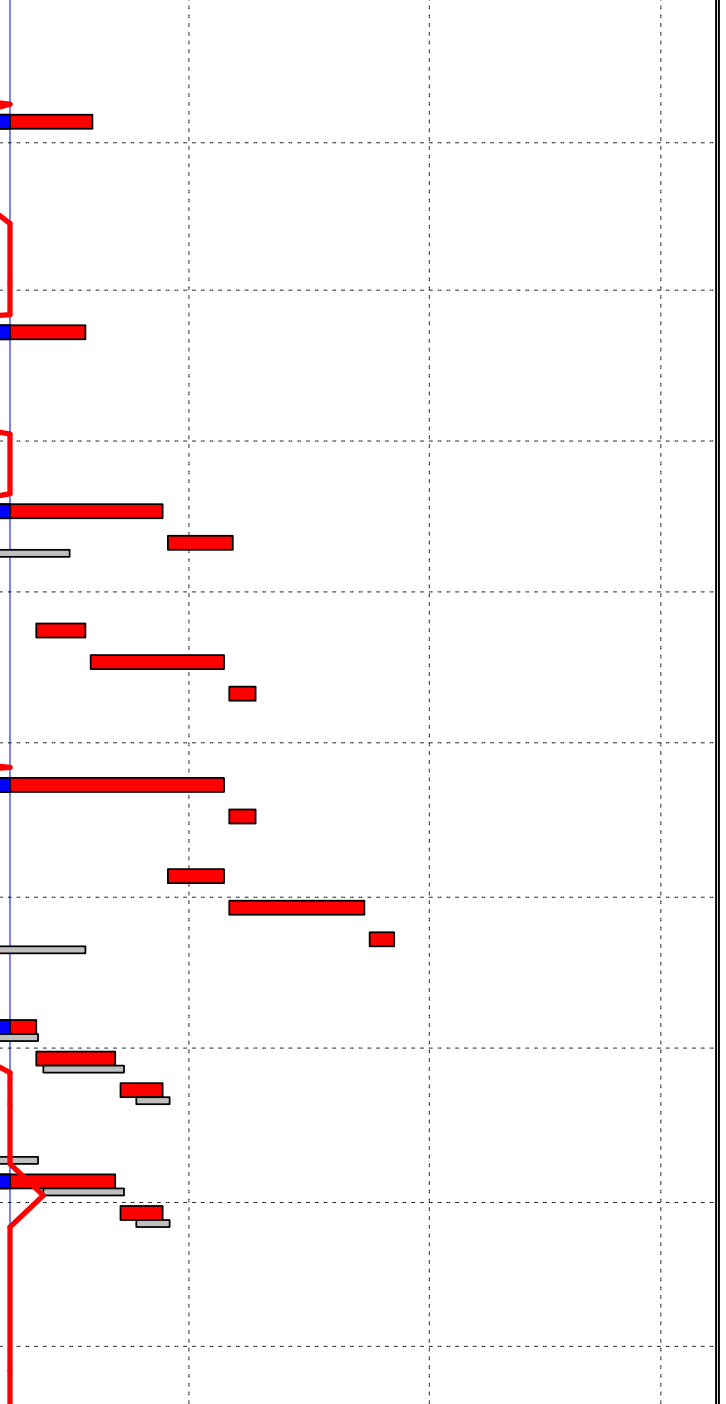


KD06 (Section 2)							
Bored Piles							
VD09							
05							
CBA-BPC48K.30	BP - Airlift, Cage Install and Concrete	13-Mar-23	18-Mar-23	12	07-Mar-23 A	21-Mar-23 A	
VD14							

Planned	Planned MS
Critical	Critical MS
Actual	Actual MS

Date	Revision	Checked	Approved
04-Mar-23	R0	KL	B
02-Dec-23	R03D	KL	C

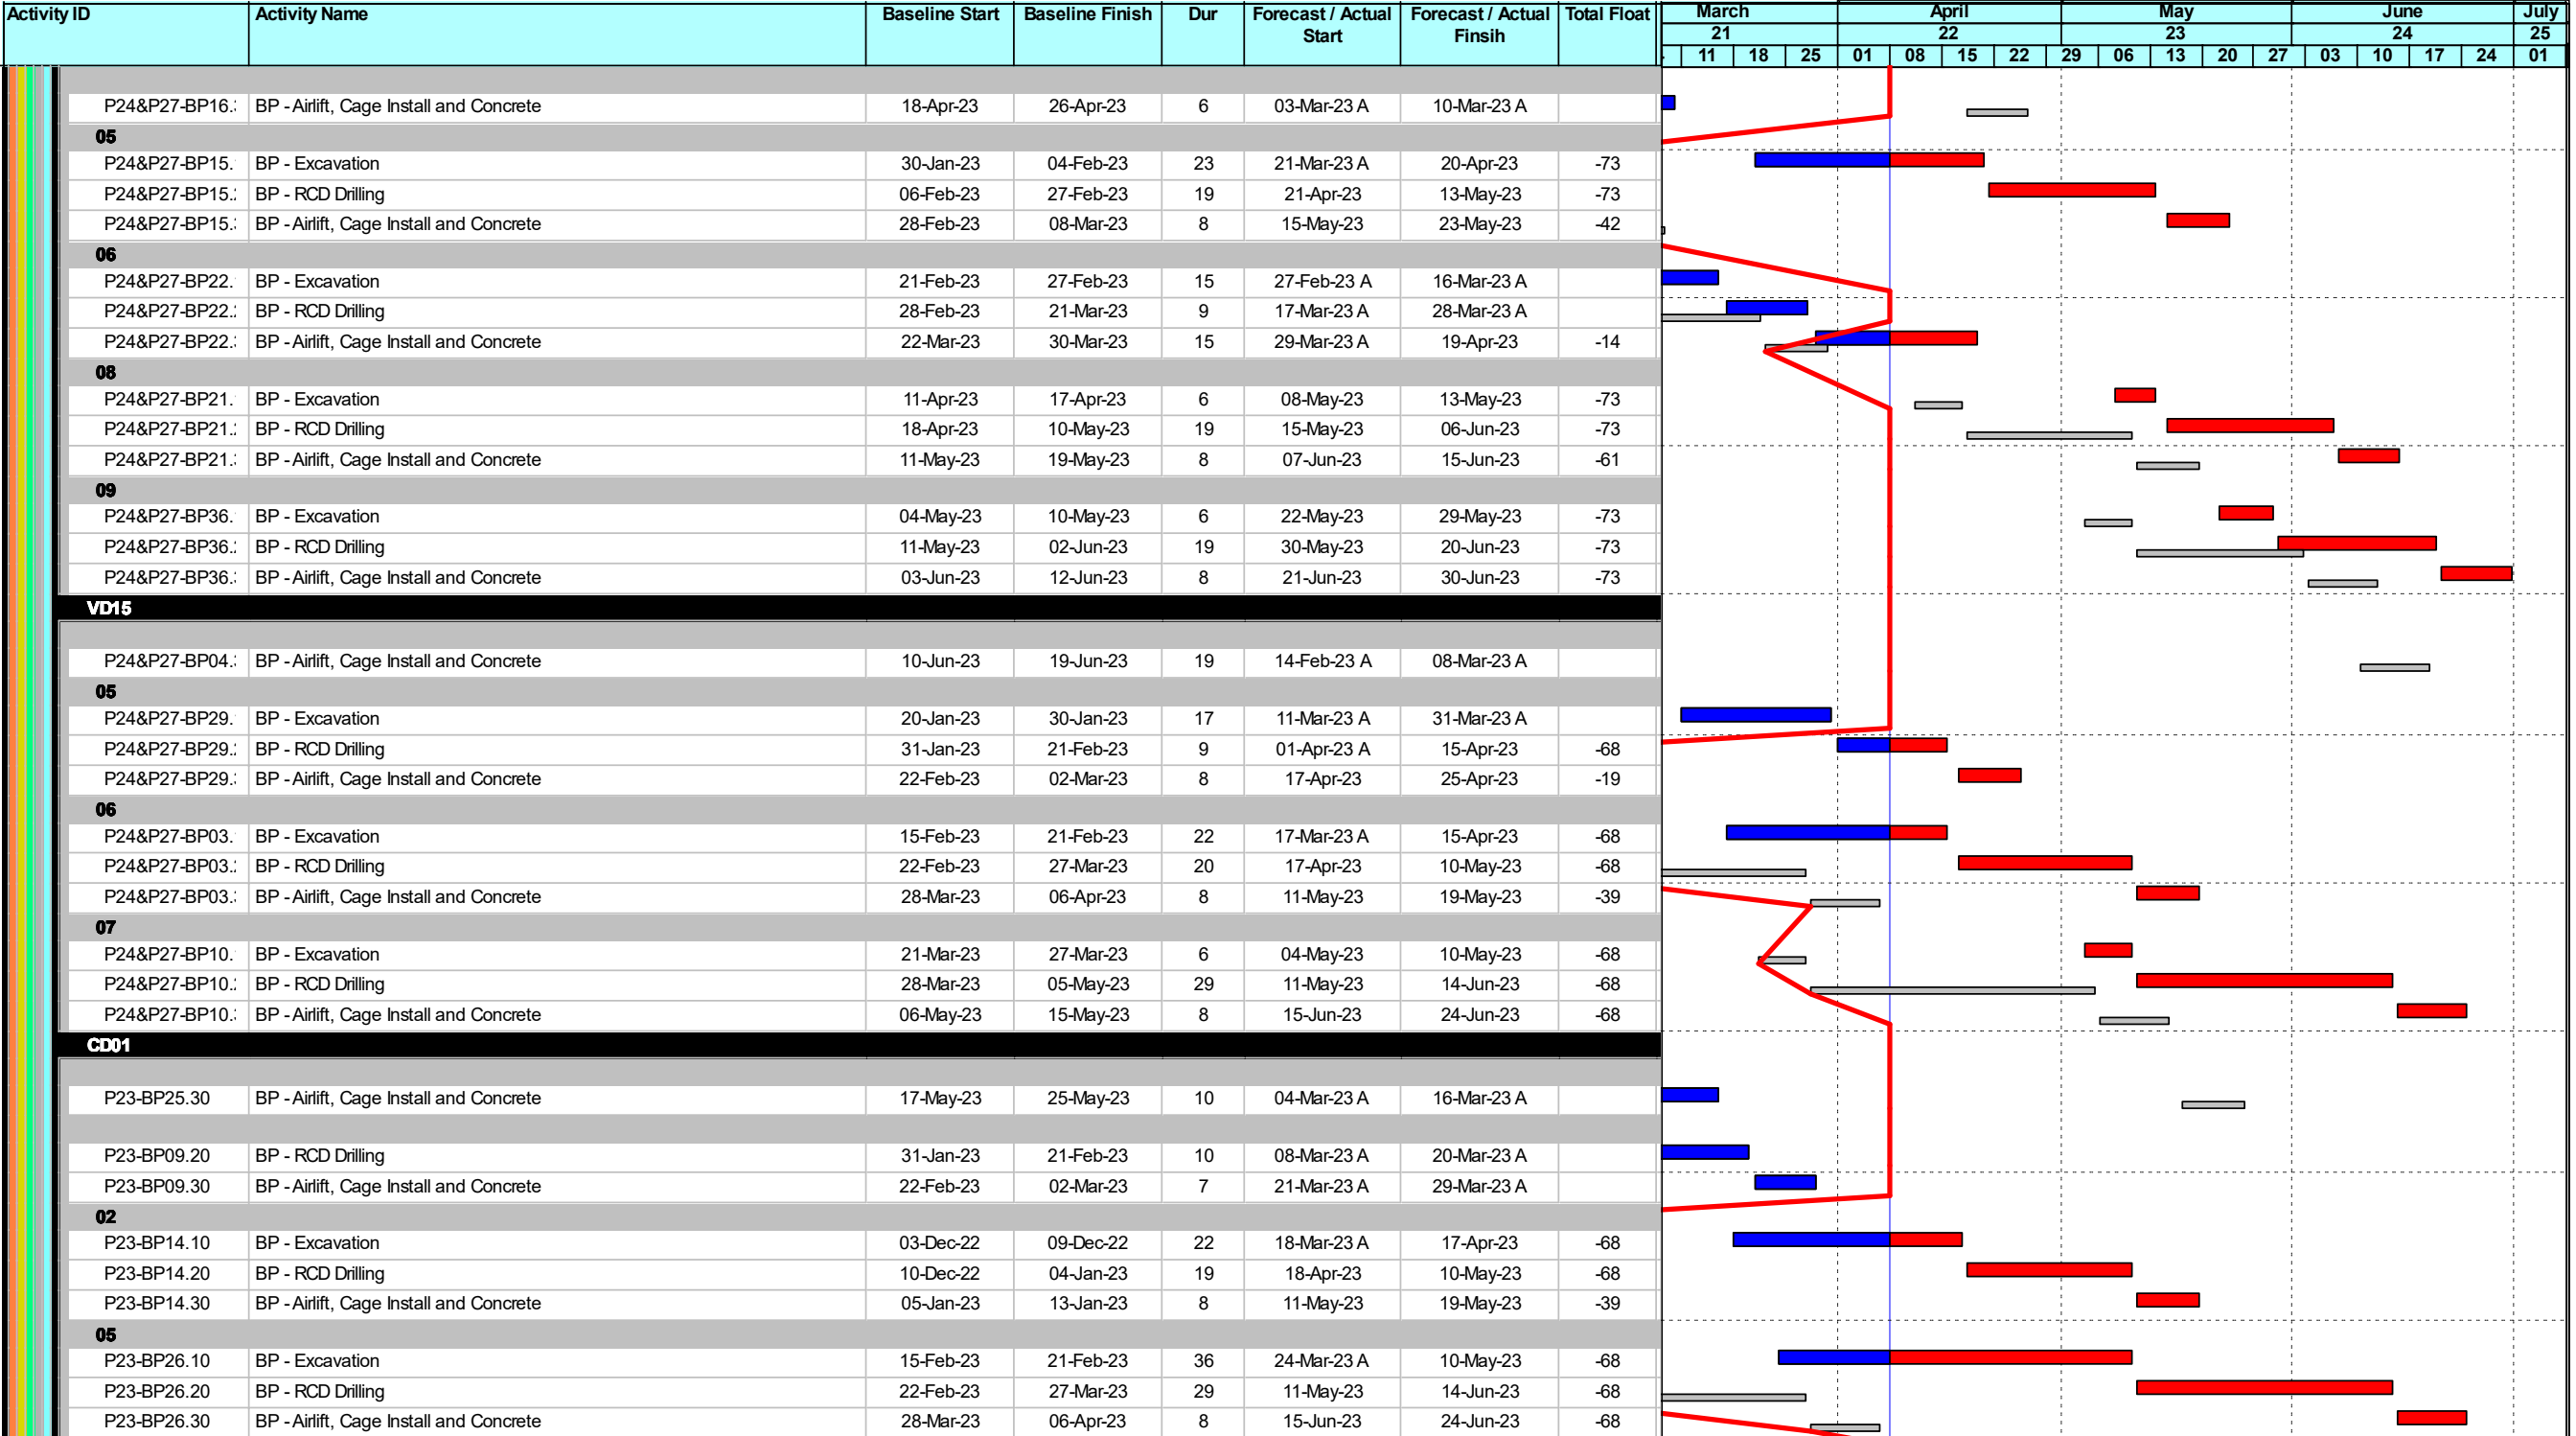


	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 7 April 2023
 Based on CMWP Rev.0 (3rd Draft)




Date	Revision	Checked	Approved
04-Mar-23	R0	KL	B
02-Dec-23	R03D	KL	C

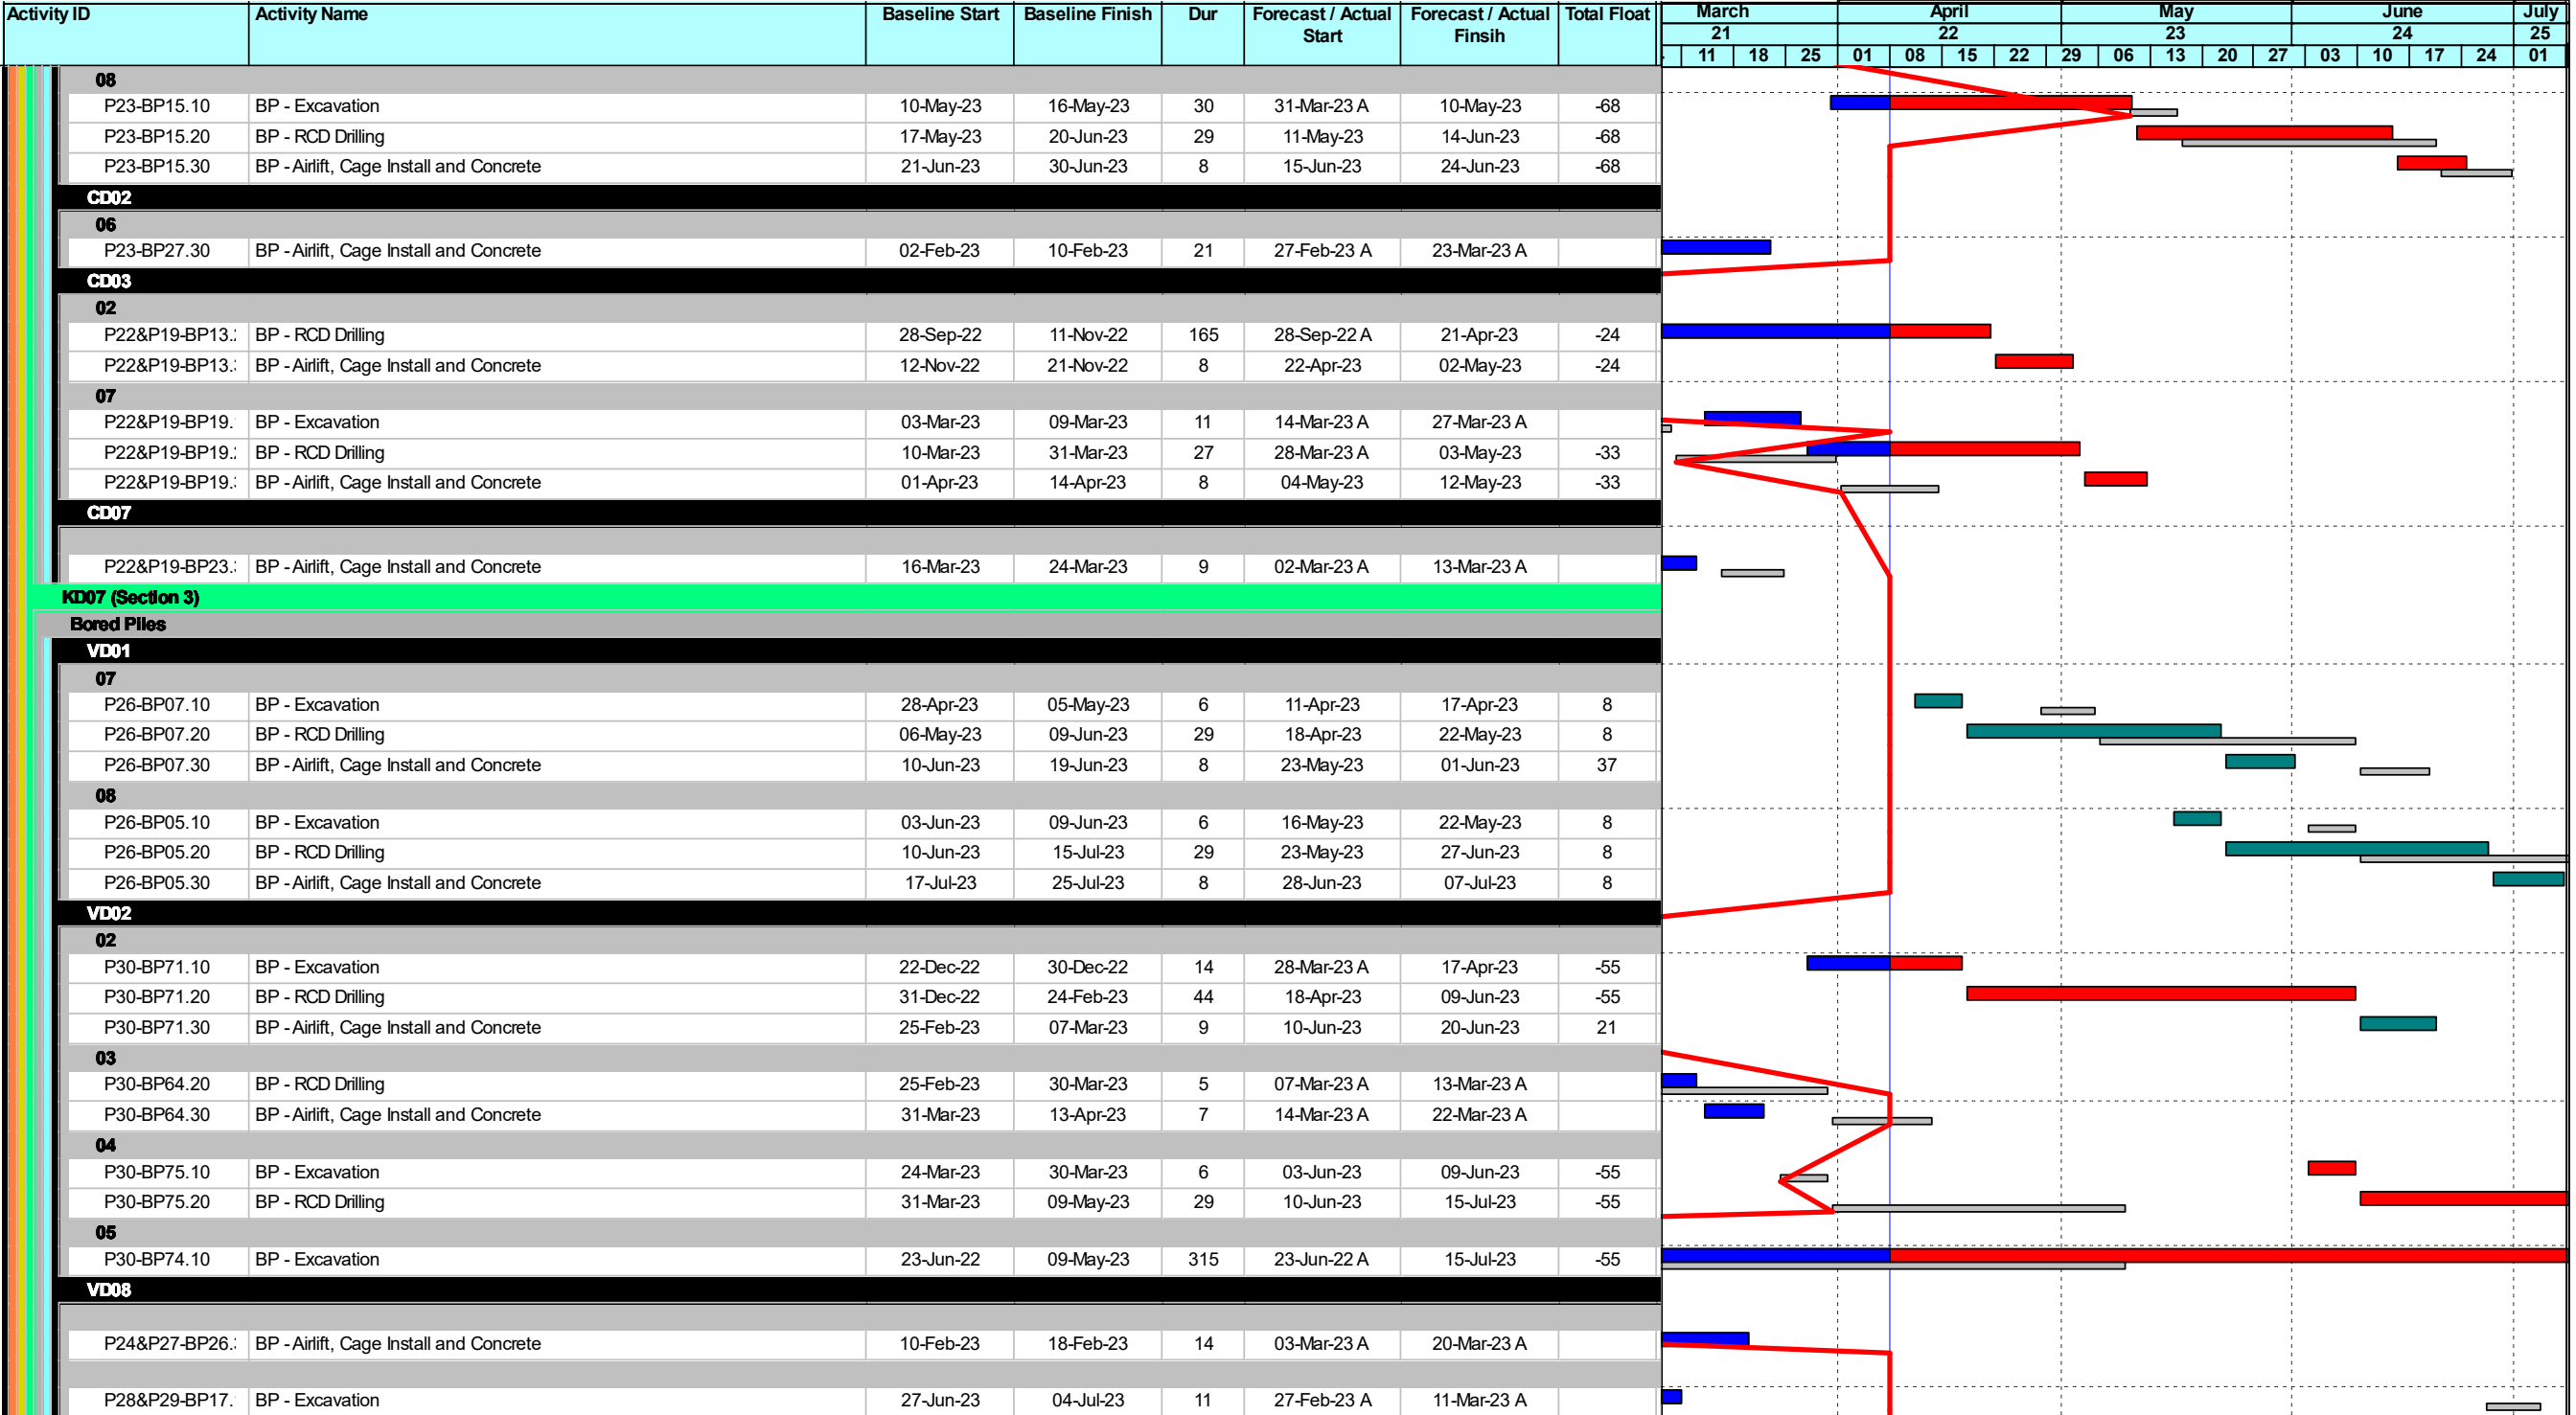





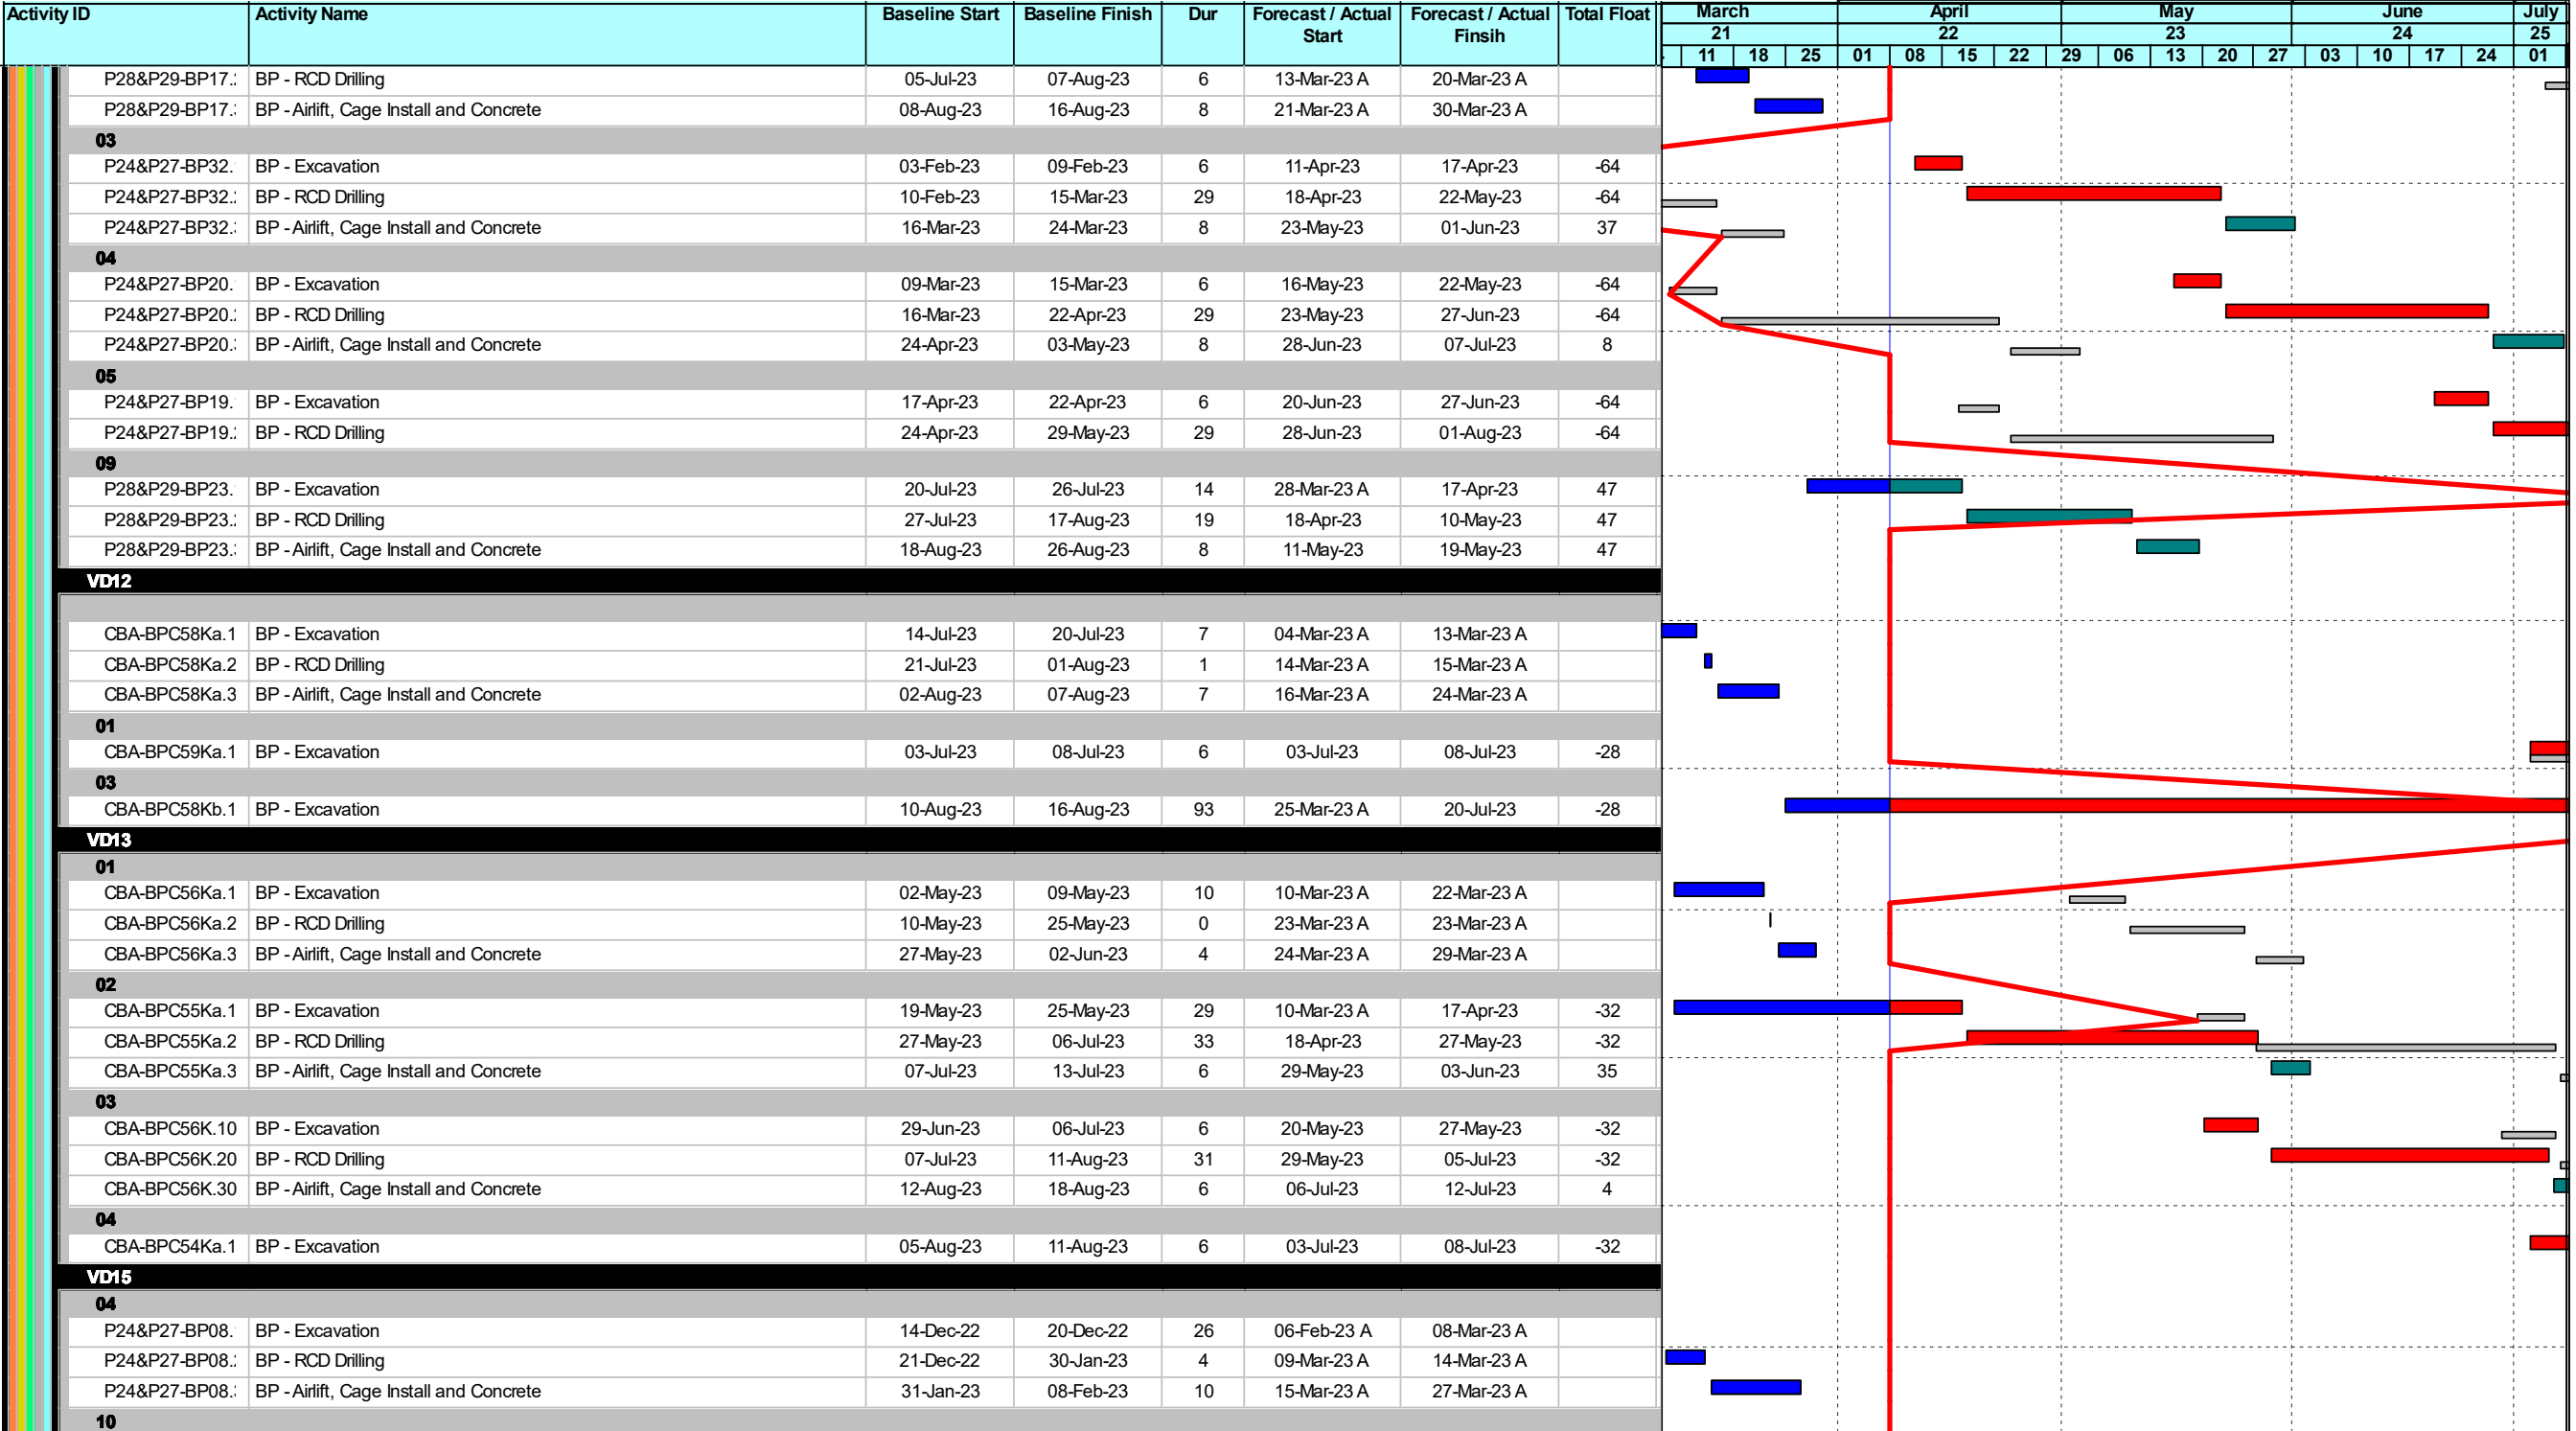

	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 7 April 2023
 Based on CMWP Rev.0 (3rd Draft)


Date	Revision	Checked	Approved
04-Mar-23	R0	KL	B
02-Dec-23	R03D	KL	C







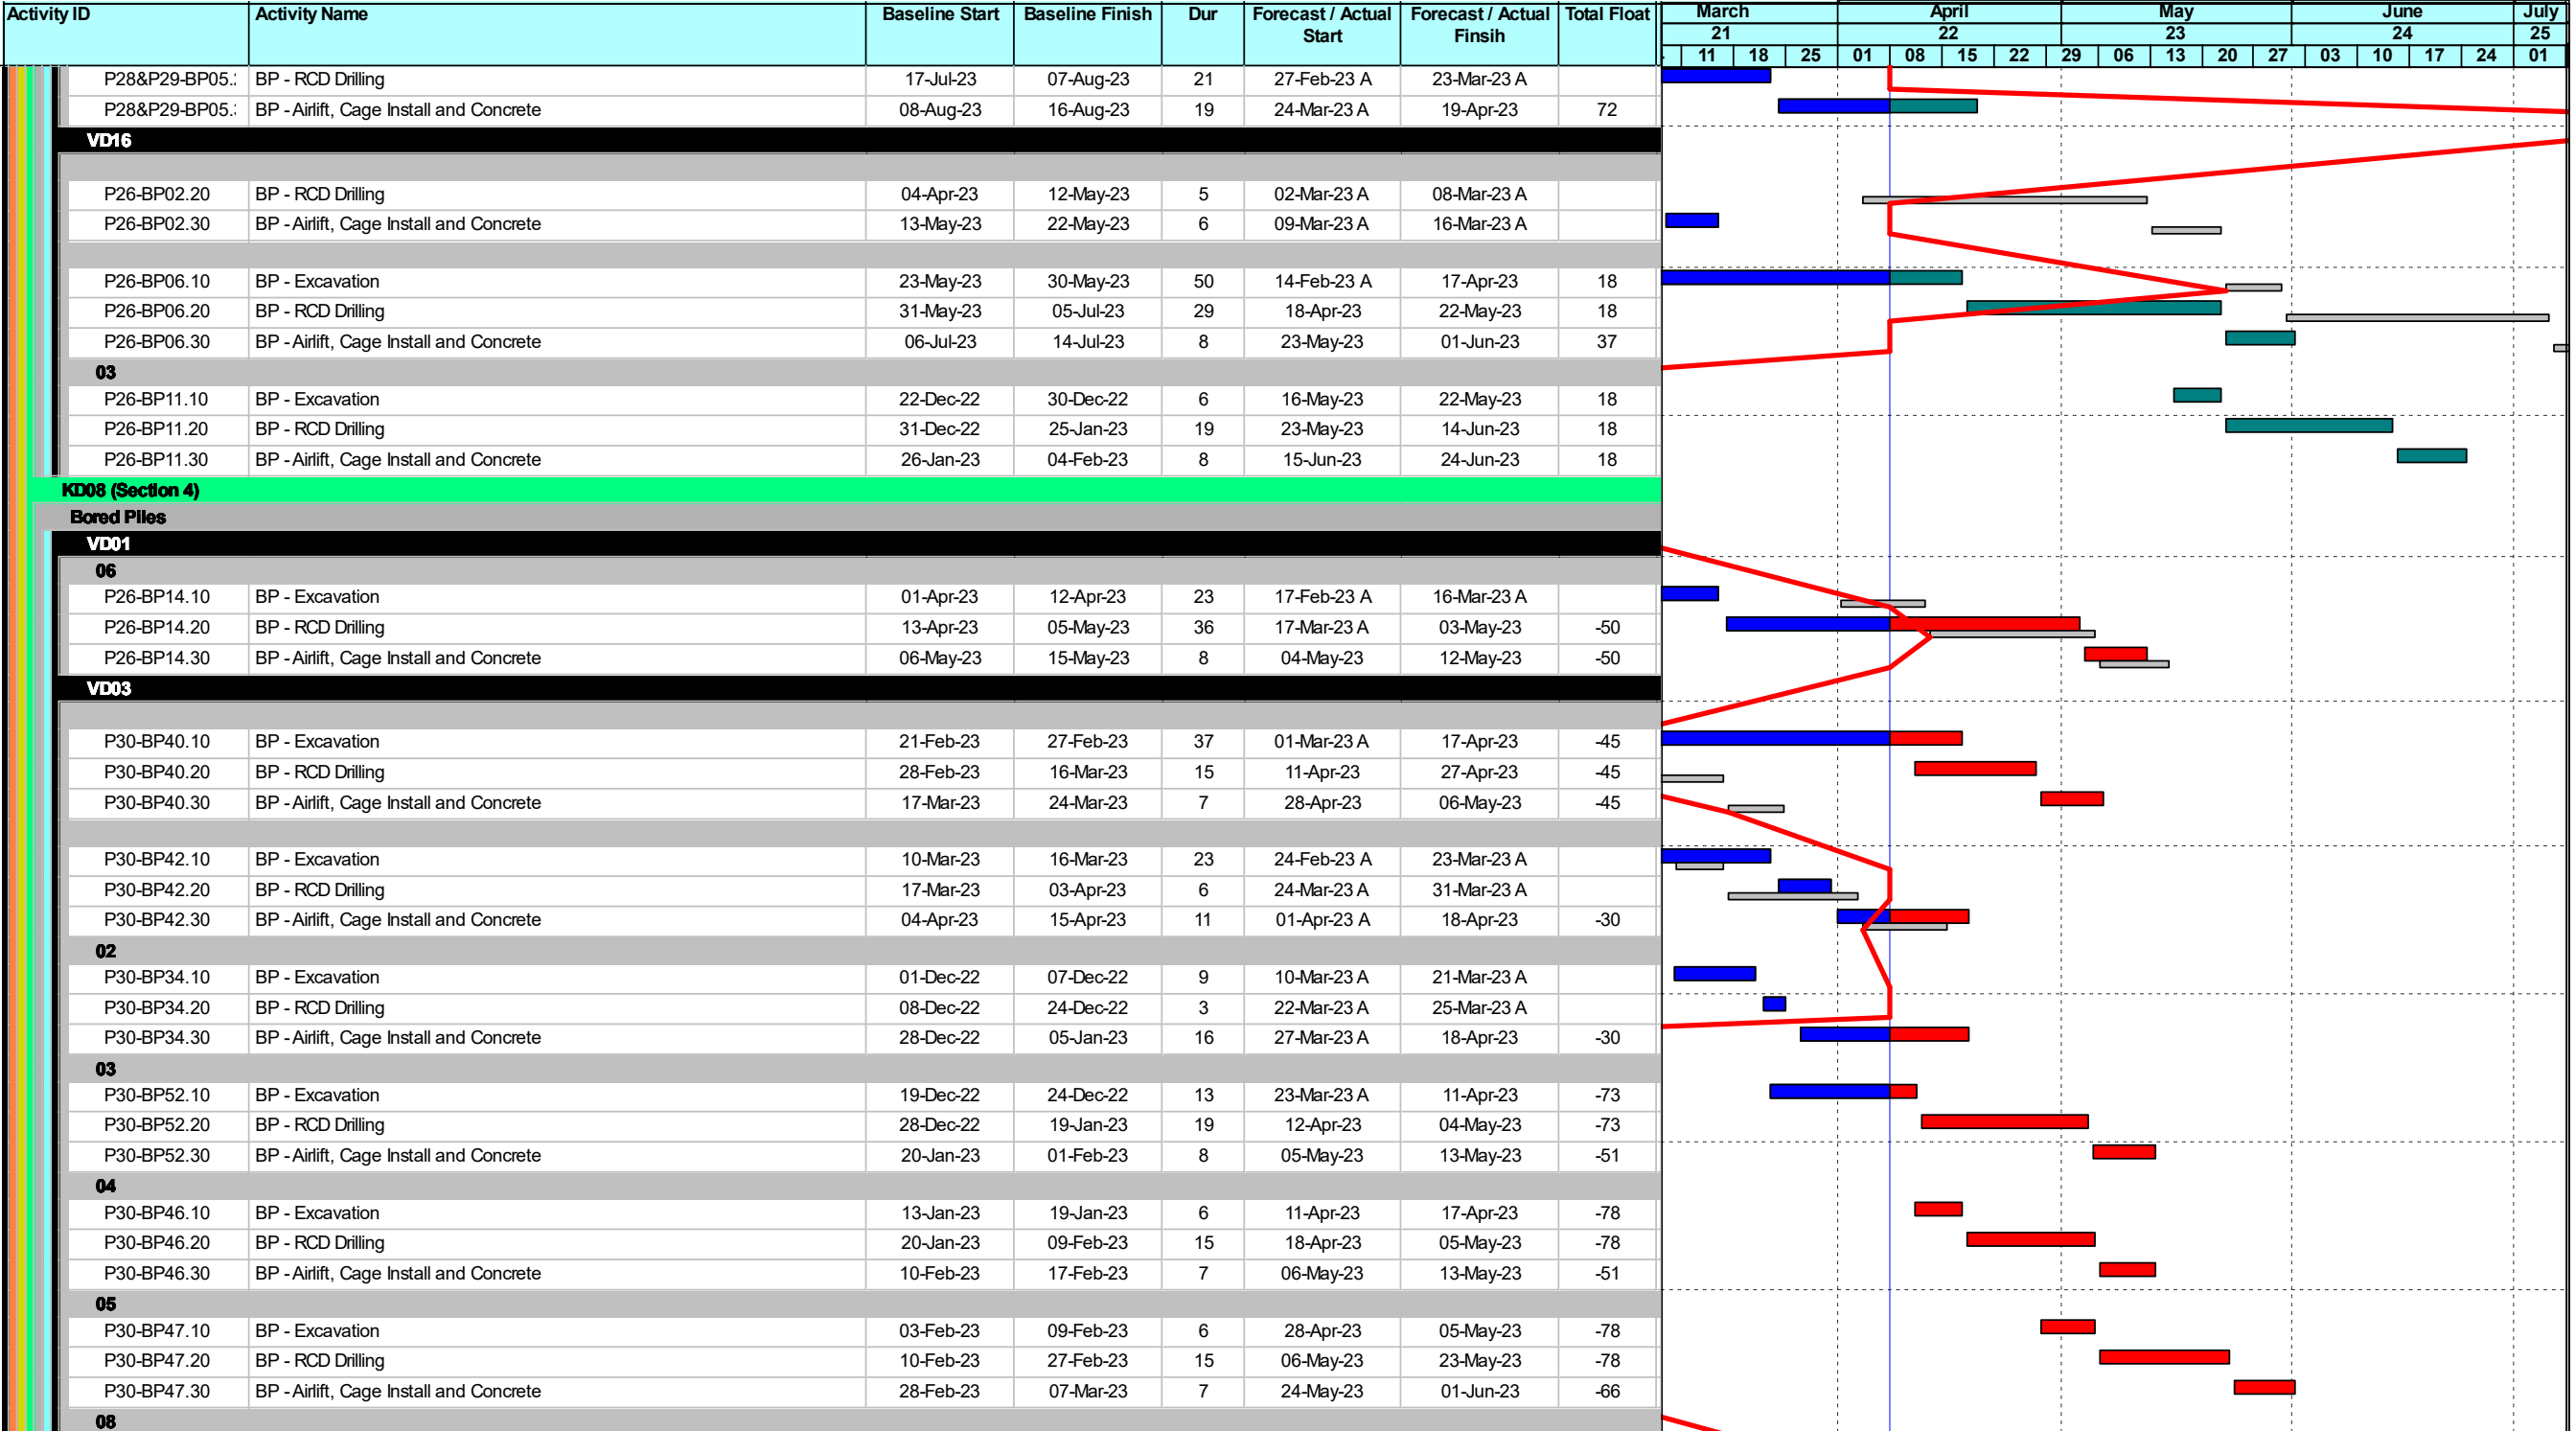

	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 7 April 2023
 Based on CMWP Rev.0 (3rd Draft)


	Date	Revision	Checked	Approved
	04-Mar-23	R0	KL	B
	02-Dec-23	R03D	KL	C



	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 7 April 2023
 Based on CMWP Rev.0 (3rd Draft)

			Date	Revision	Checked	Approved
			04-Mar-23	R0	KL	B
			02-Dec-23	R03D	KL	C

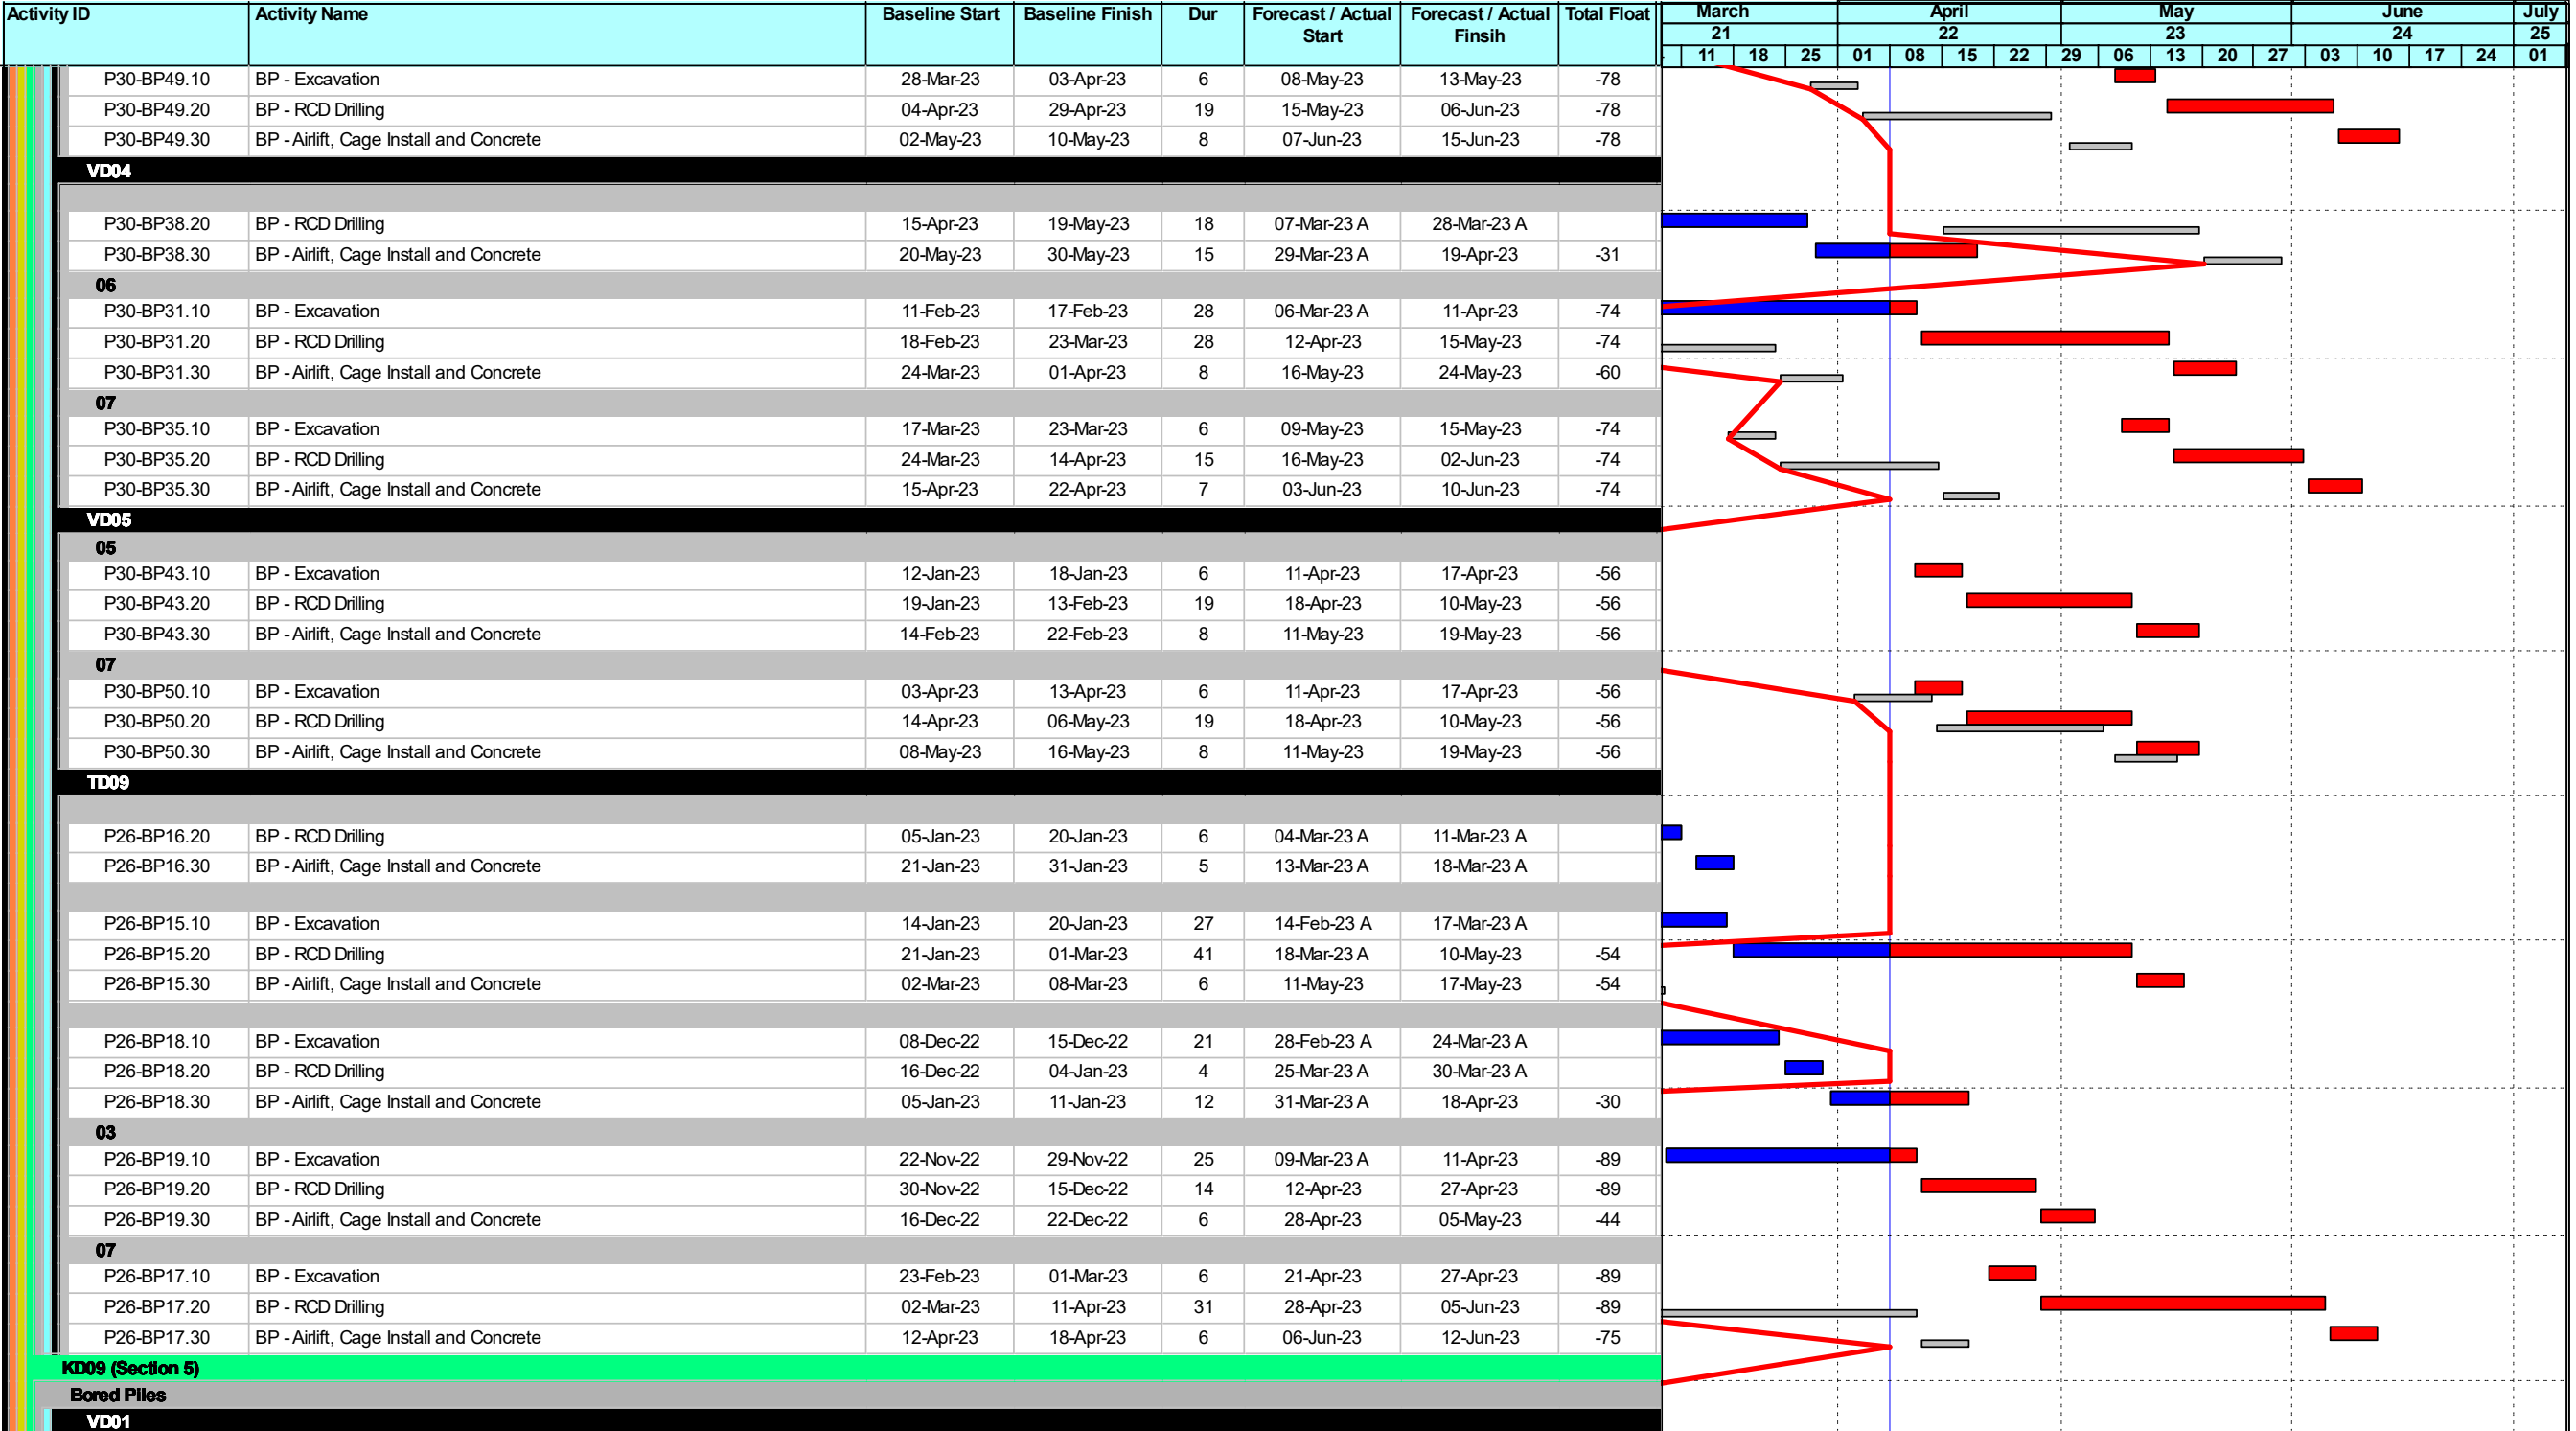


	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 7 April 2023
 Based on CMWP Rev.0 (3rd Draft)




Date	Revision	Checked	Approved
04-Mar-23	R0	KL	B
02-Dec-23	R03D	KL	C

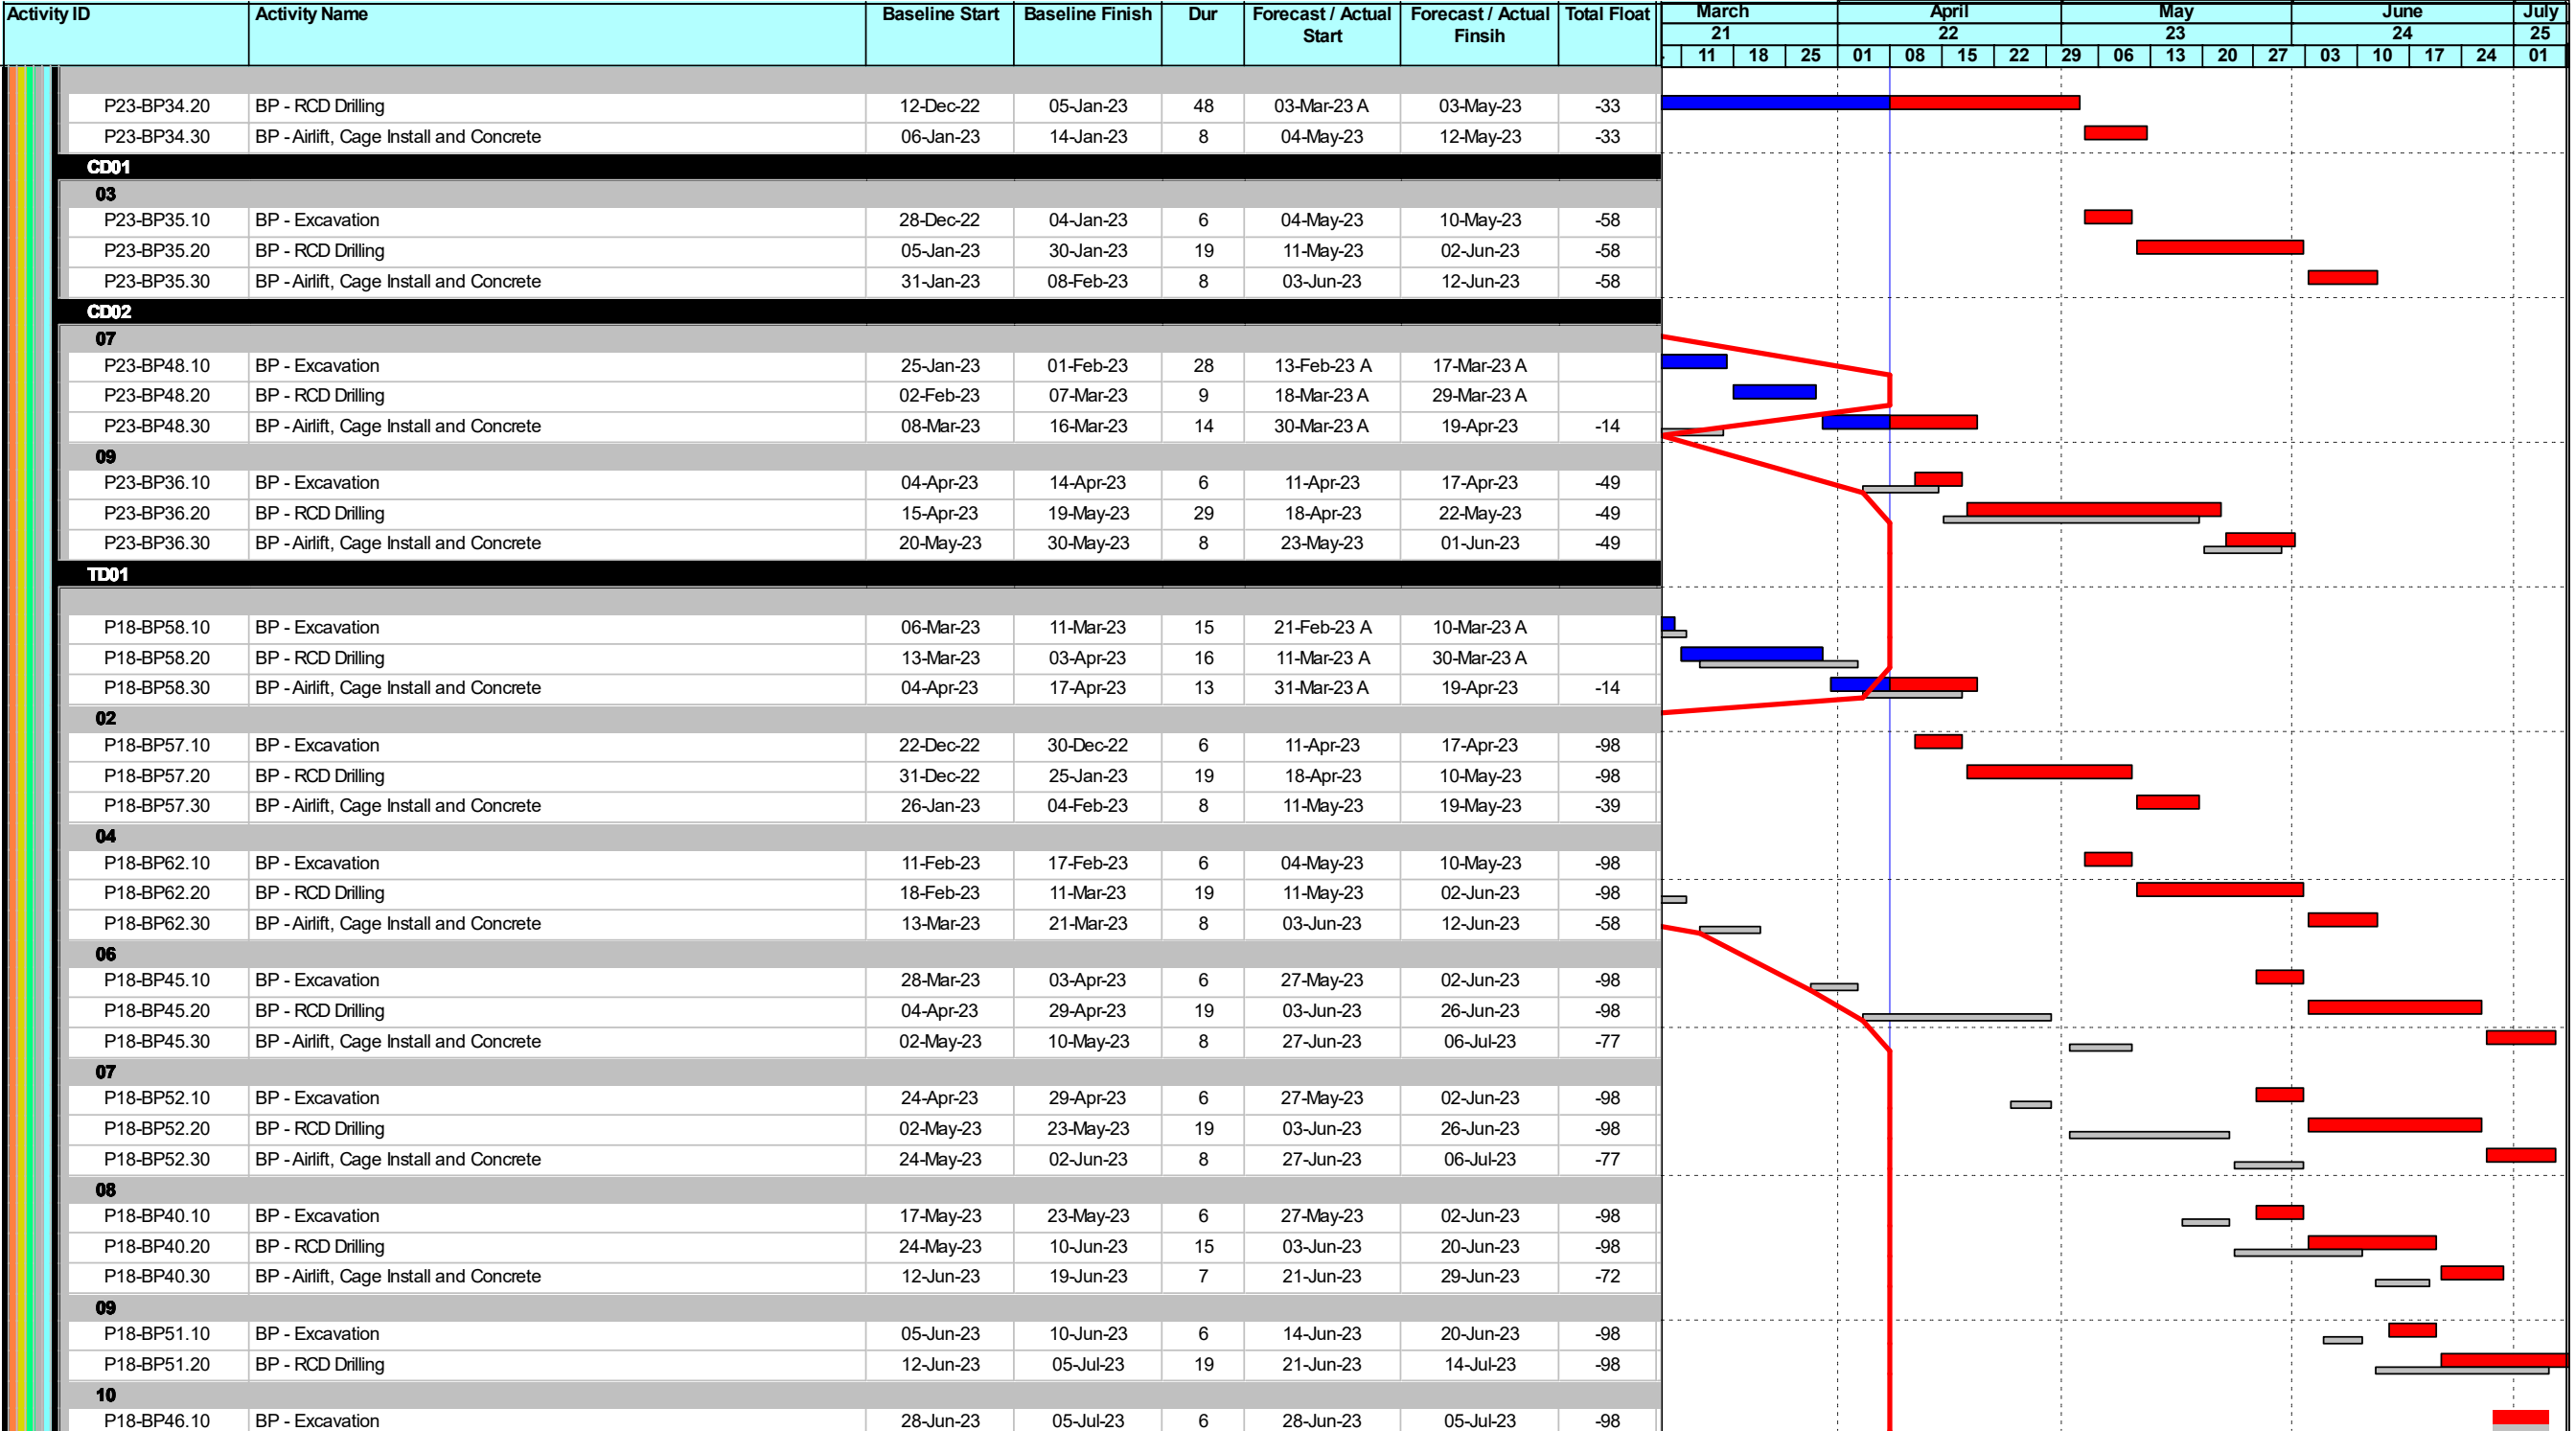





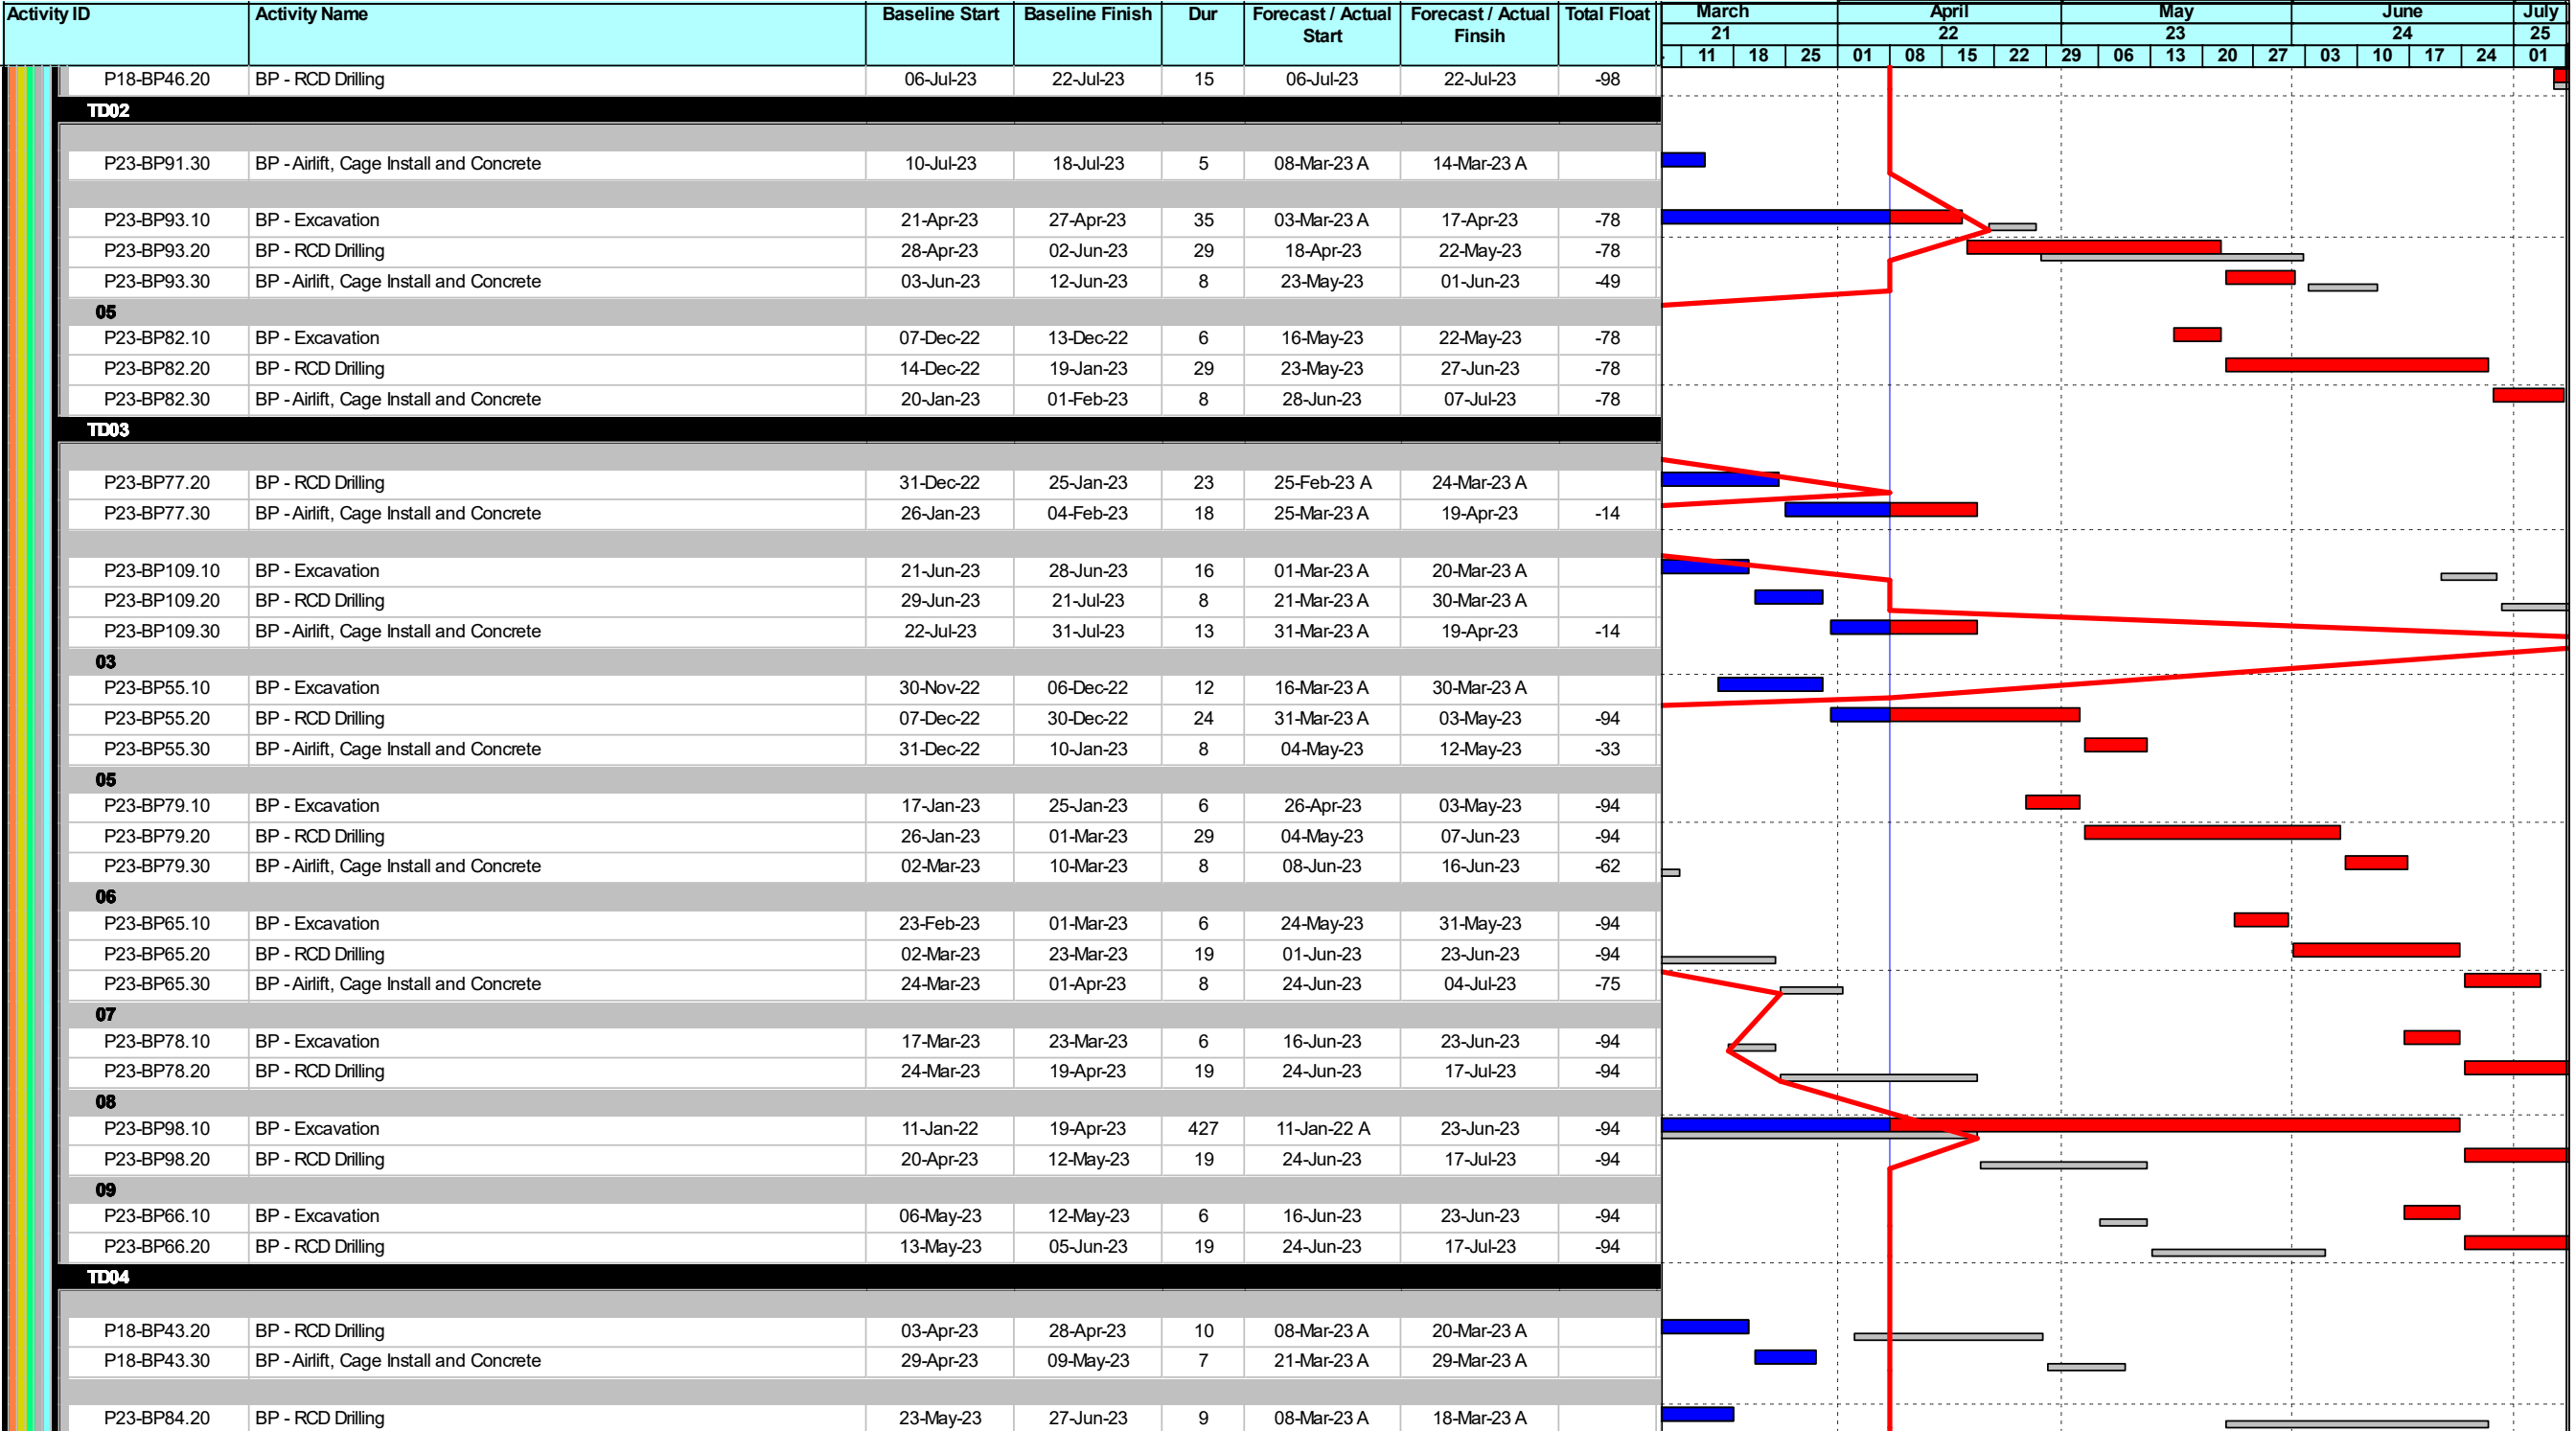

Planned	Planned MS
Critical	Critical MS
Actual	Actual MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 7 April 2023
 Based on CMWP Rev.0 (3rd Draft)


Date	Revision	Checked	Approved
04-Mar-23	R0	KL	B
02-Dec-23	R03D	KL	C







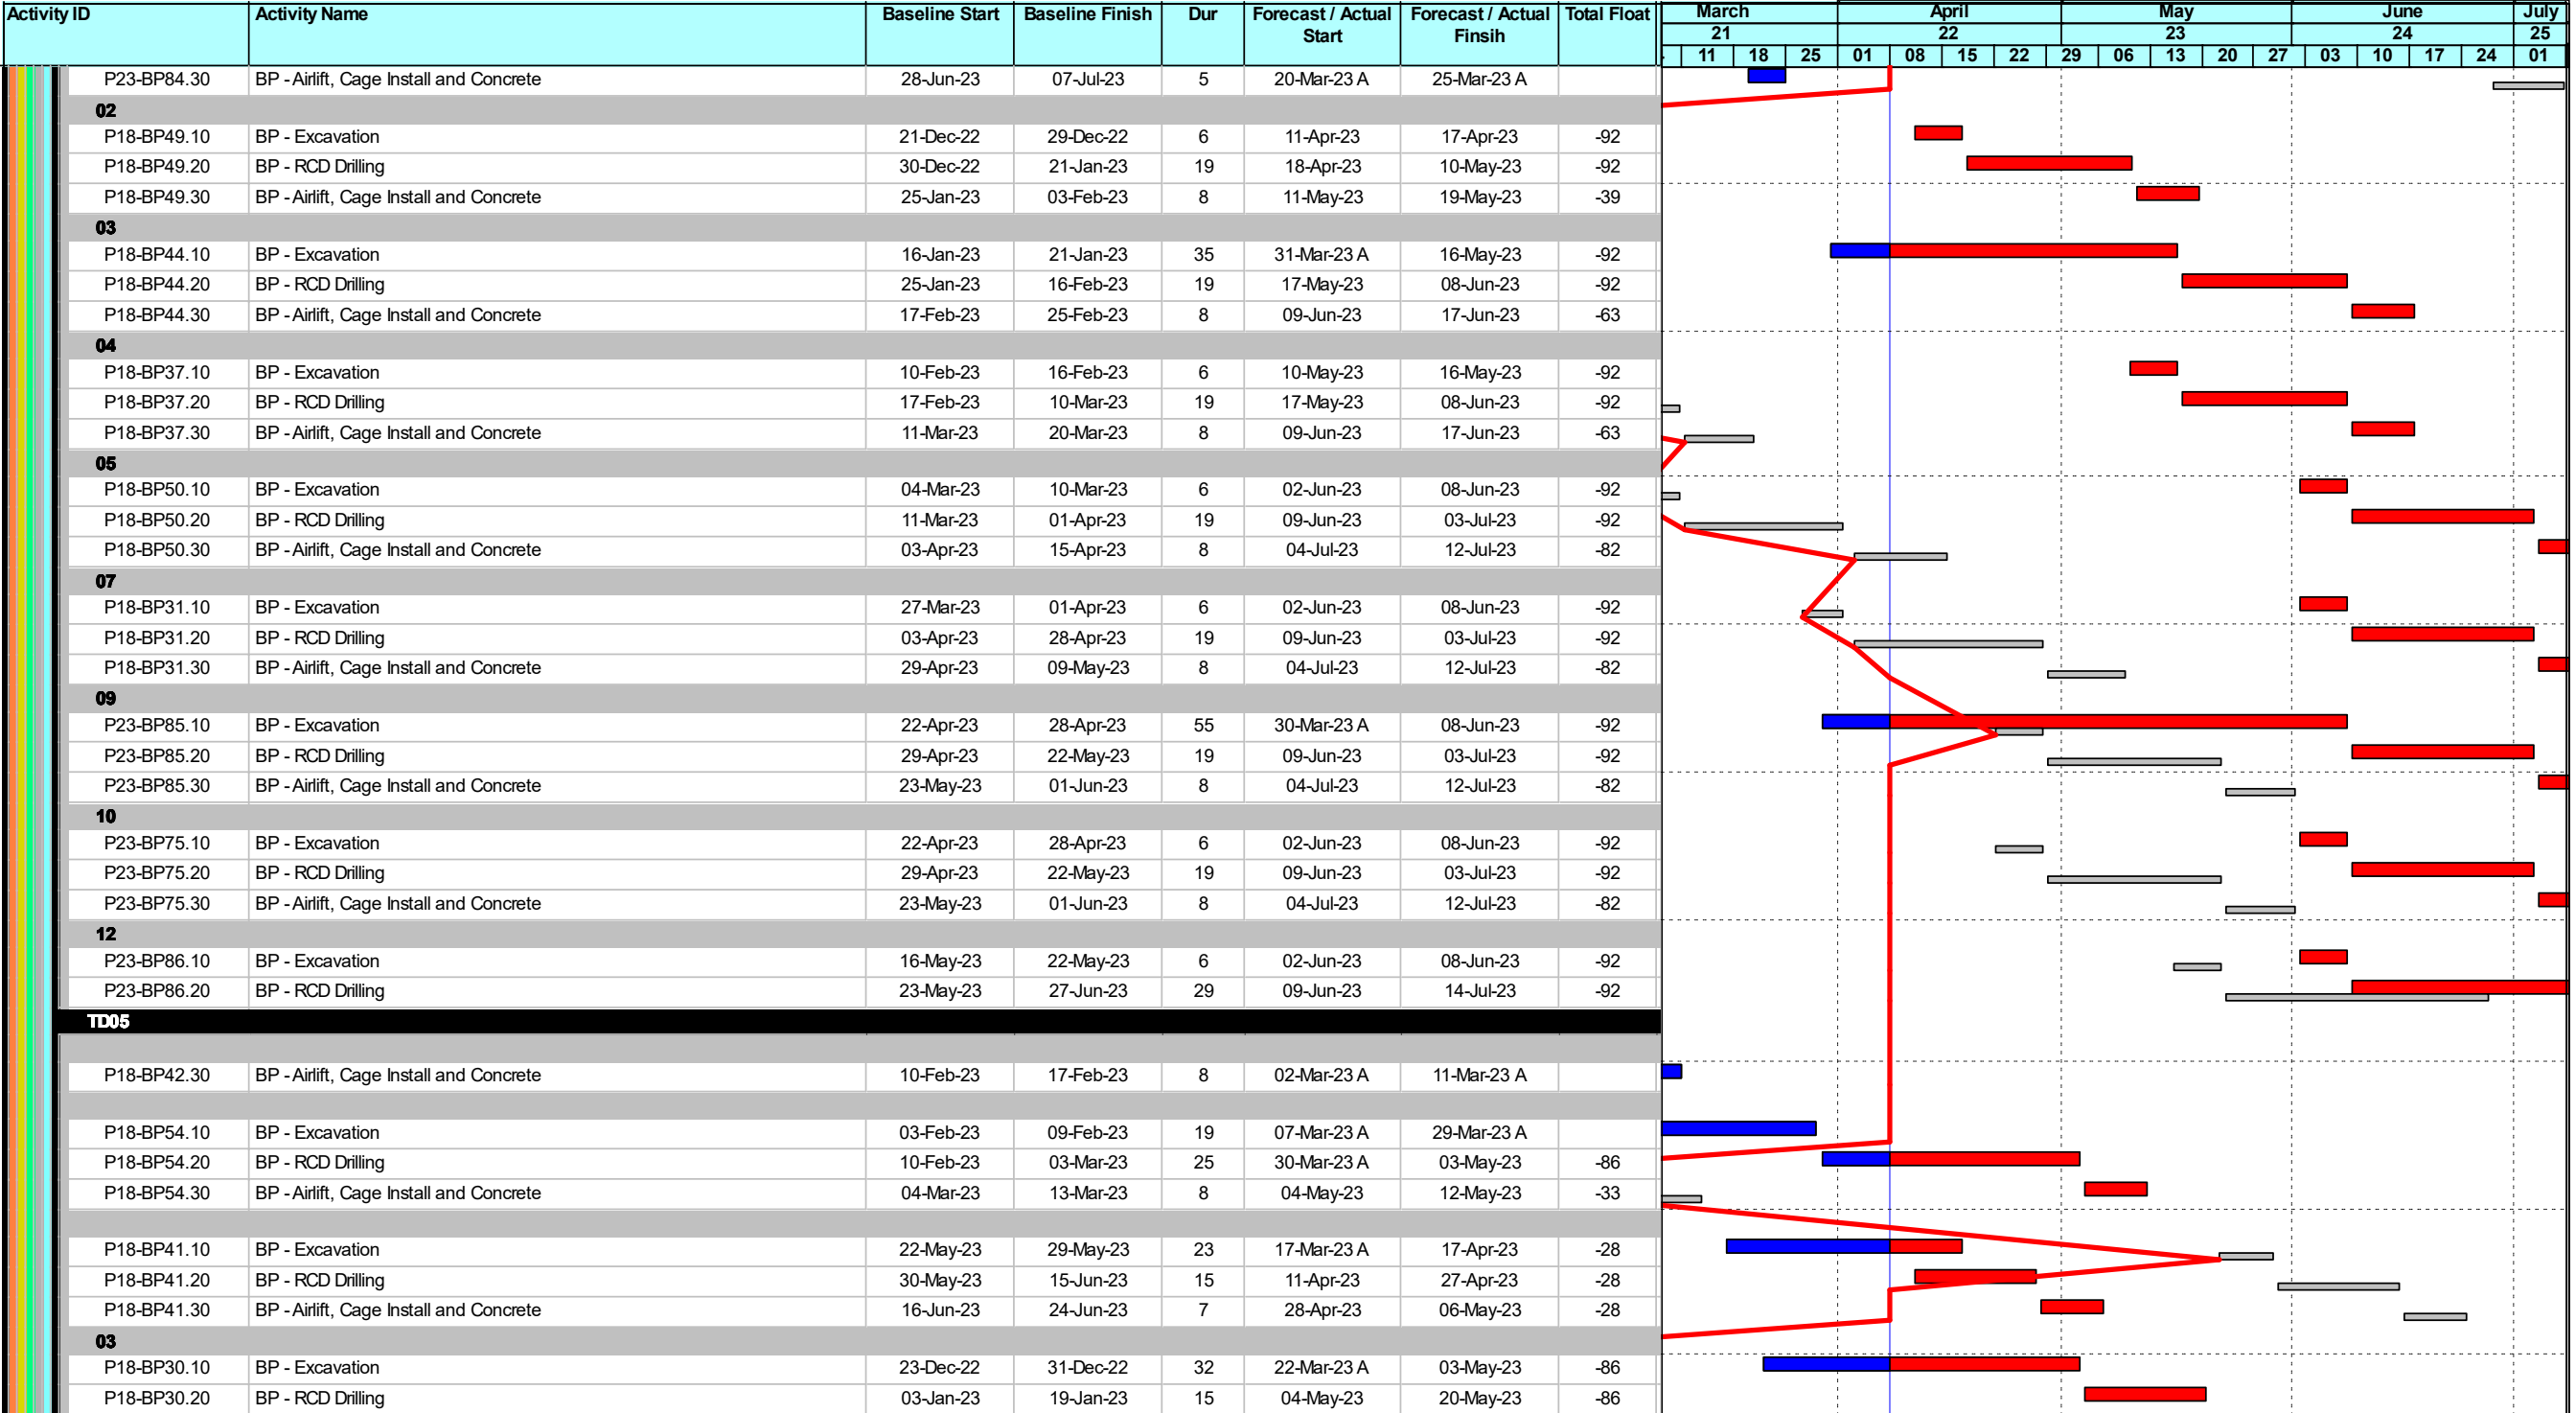

	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 7 April 2023
 Based on CMWP Rev.0 (3rd Draft)


			
Date	Revision	Checked	Approved
04-Mar-23	R0	KL	B
02-Dec-23	R03D	KL	C



	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 7 April 2023
 Based on CMWP Rev.0 (3rd Draft)


			
Date	Revision	Checked	Approved
04-Mar-23	R0	KL	B
02-Dec-23	R03D	KL	C

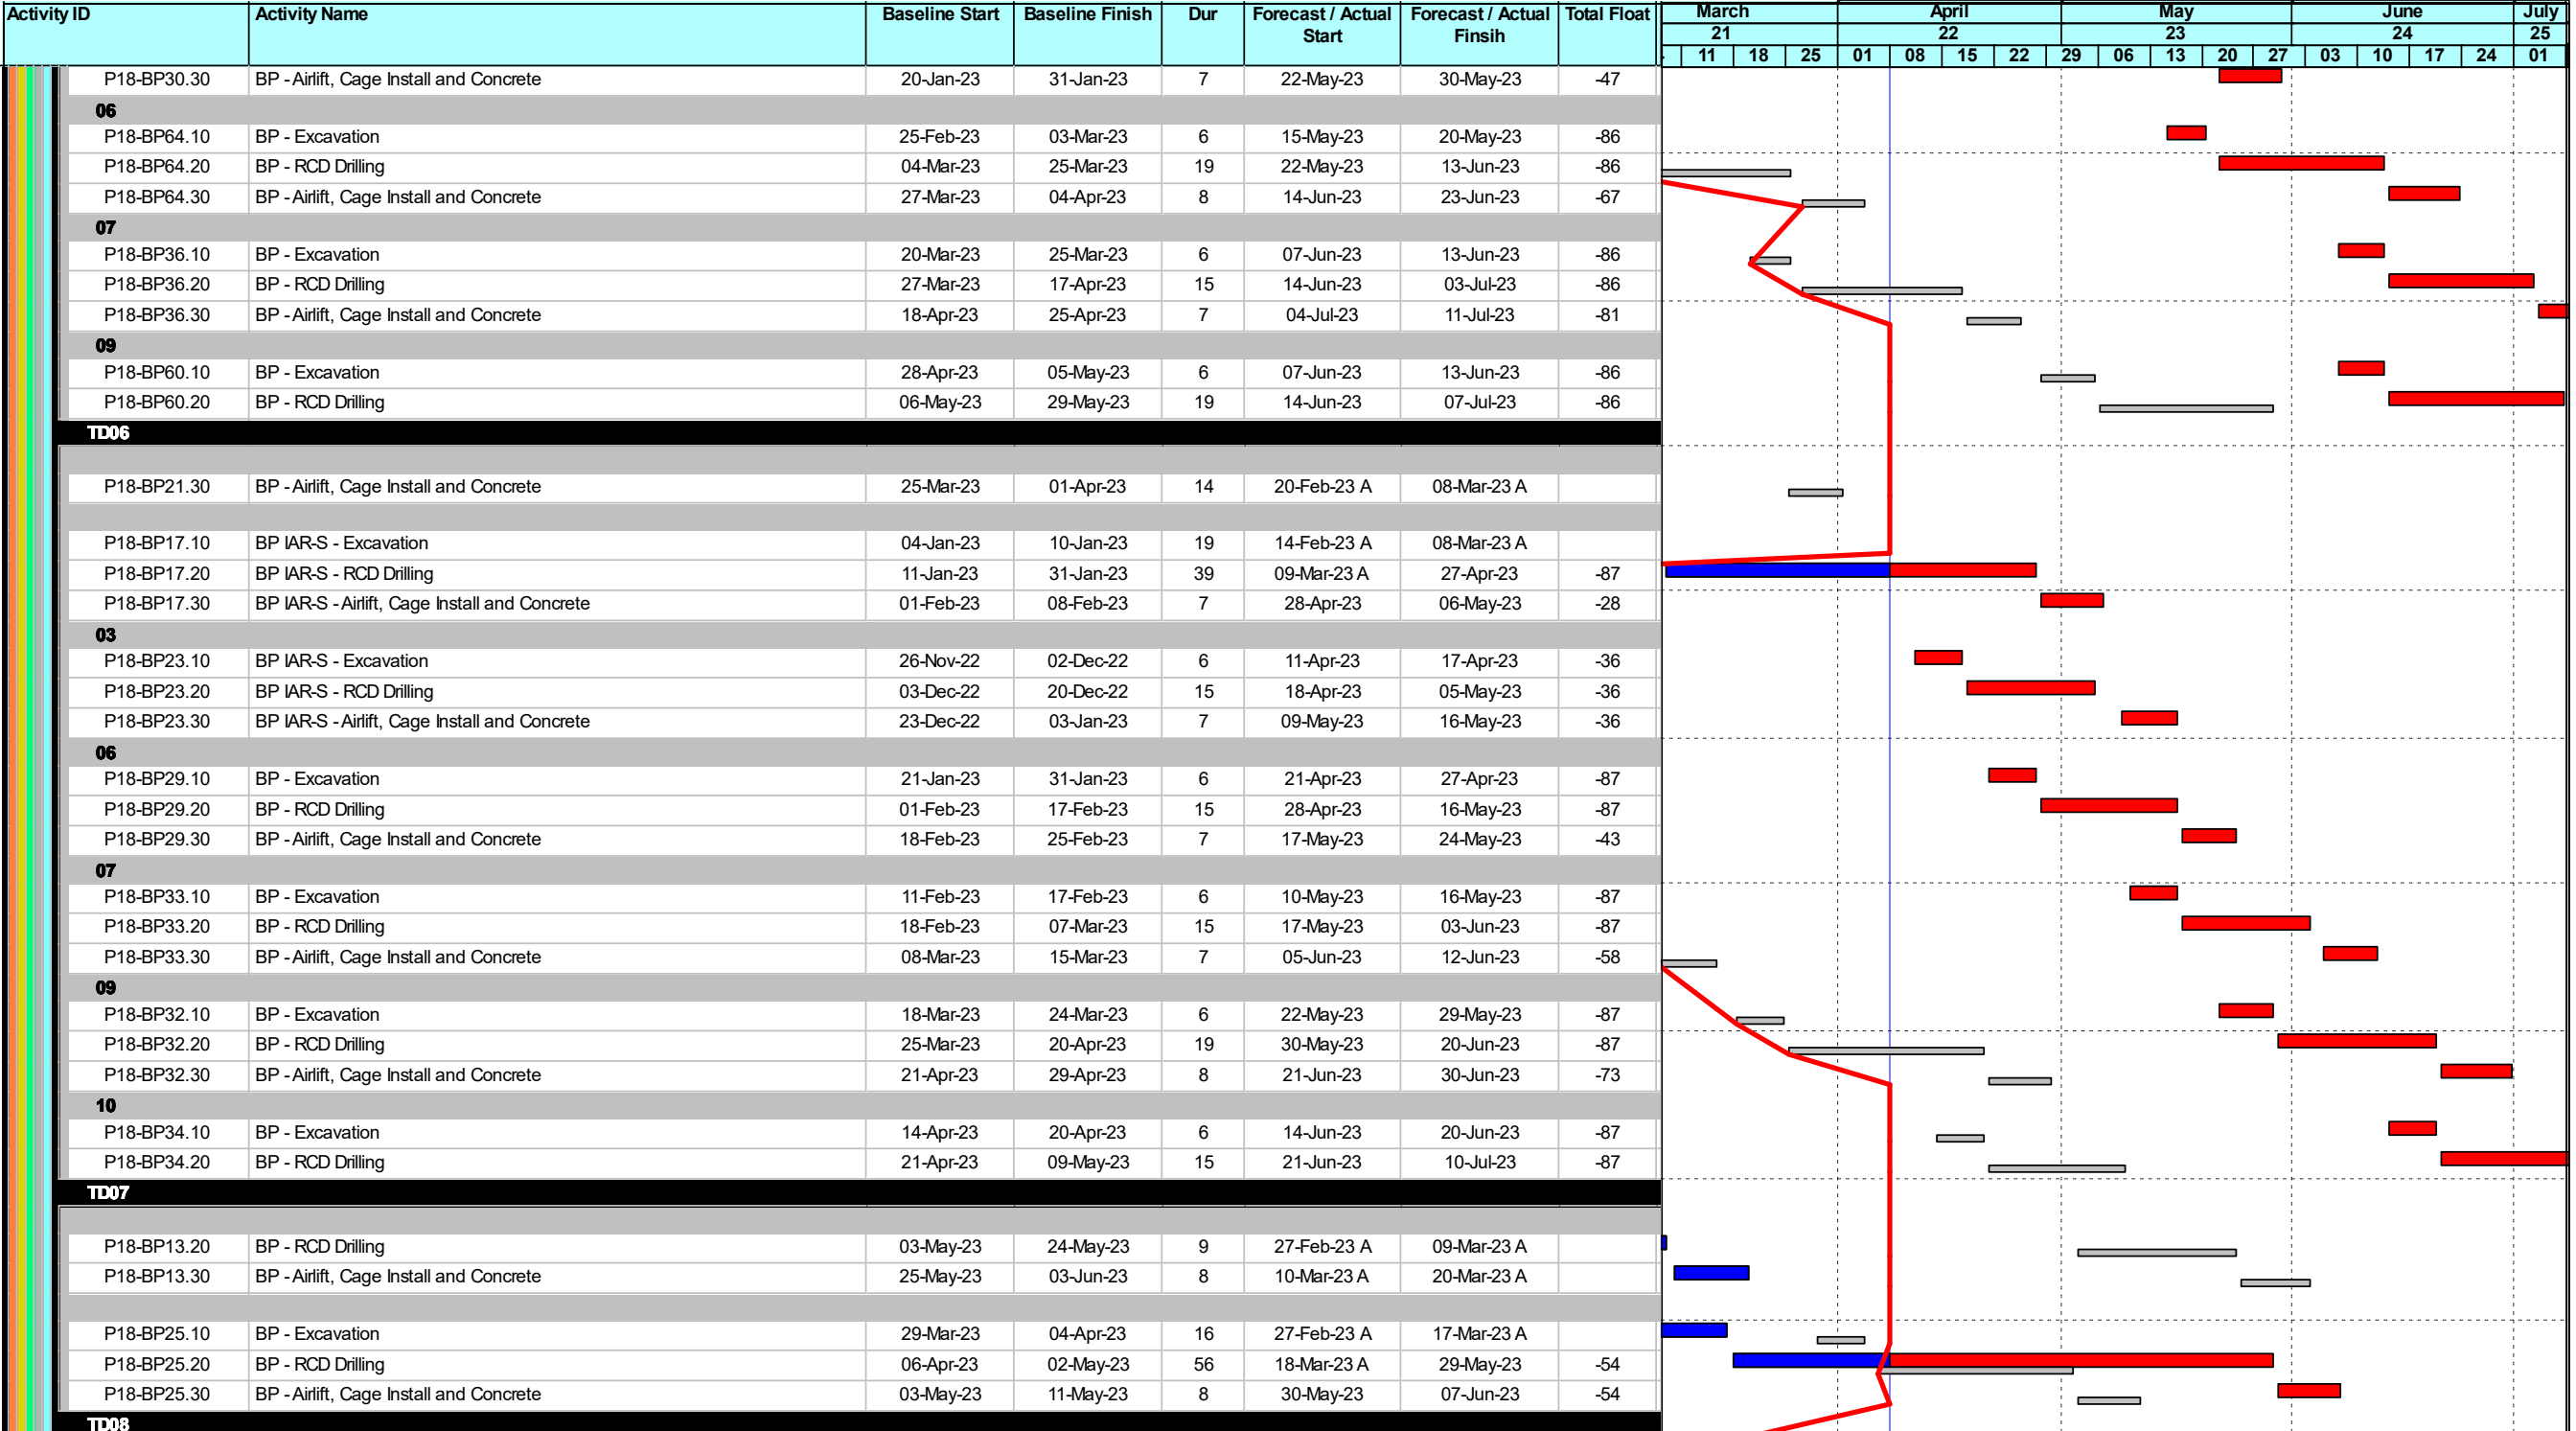

	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 7 April 2023
Based on CMWP Rev.0 (3rd Draft)

			Date	Revision	Checked	Approved
			04-Mar-23	R0	KL	B
			02-Dec-23	R03D	KL	C

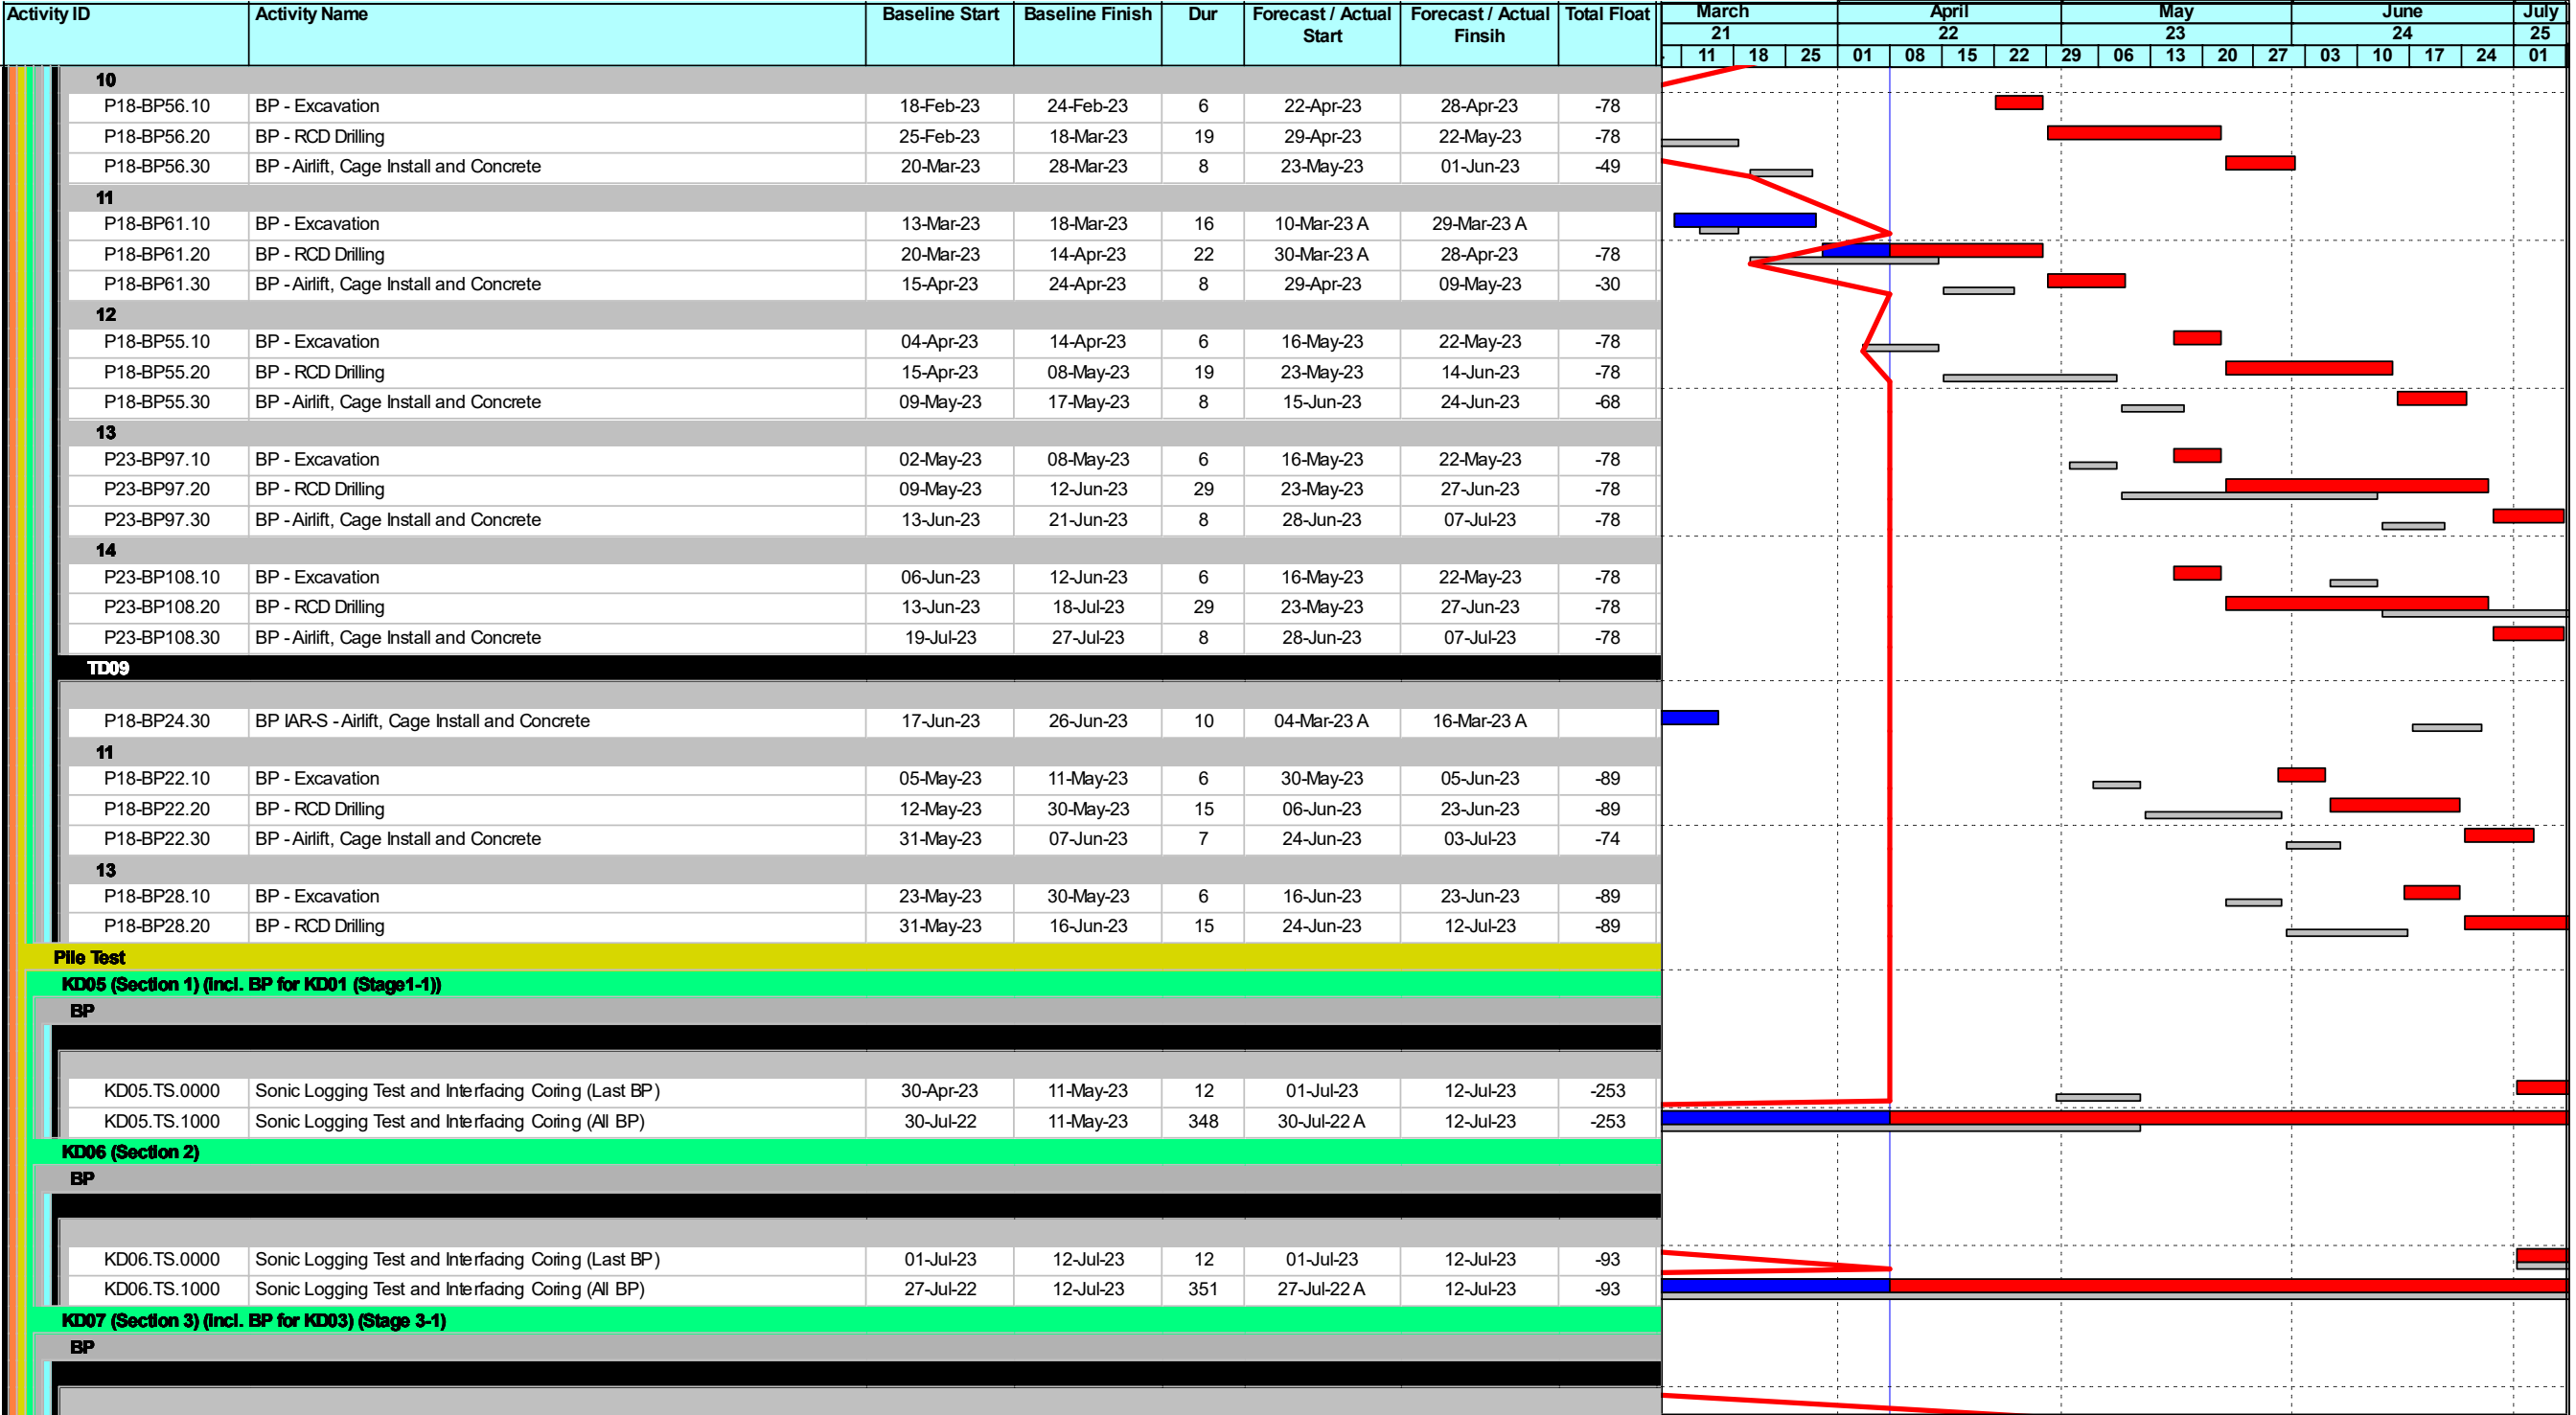







	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 7 April 2023
 Based on CMWP Rev.0 (3rd Draft)

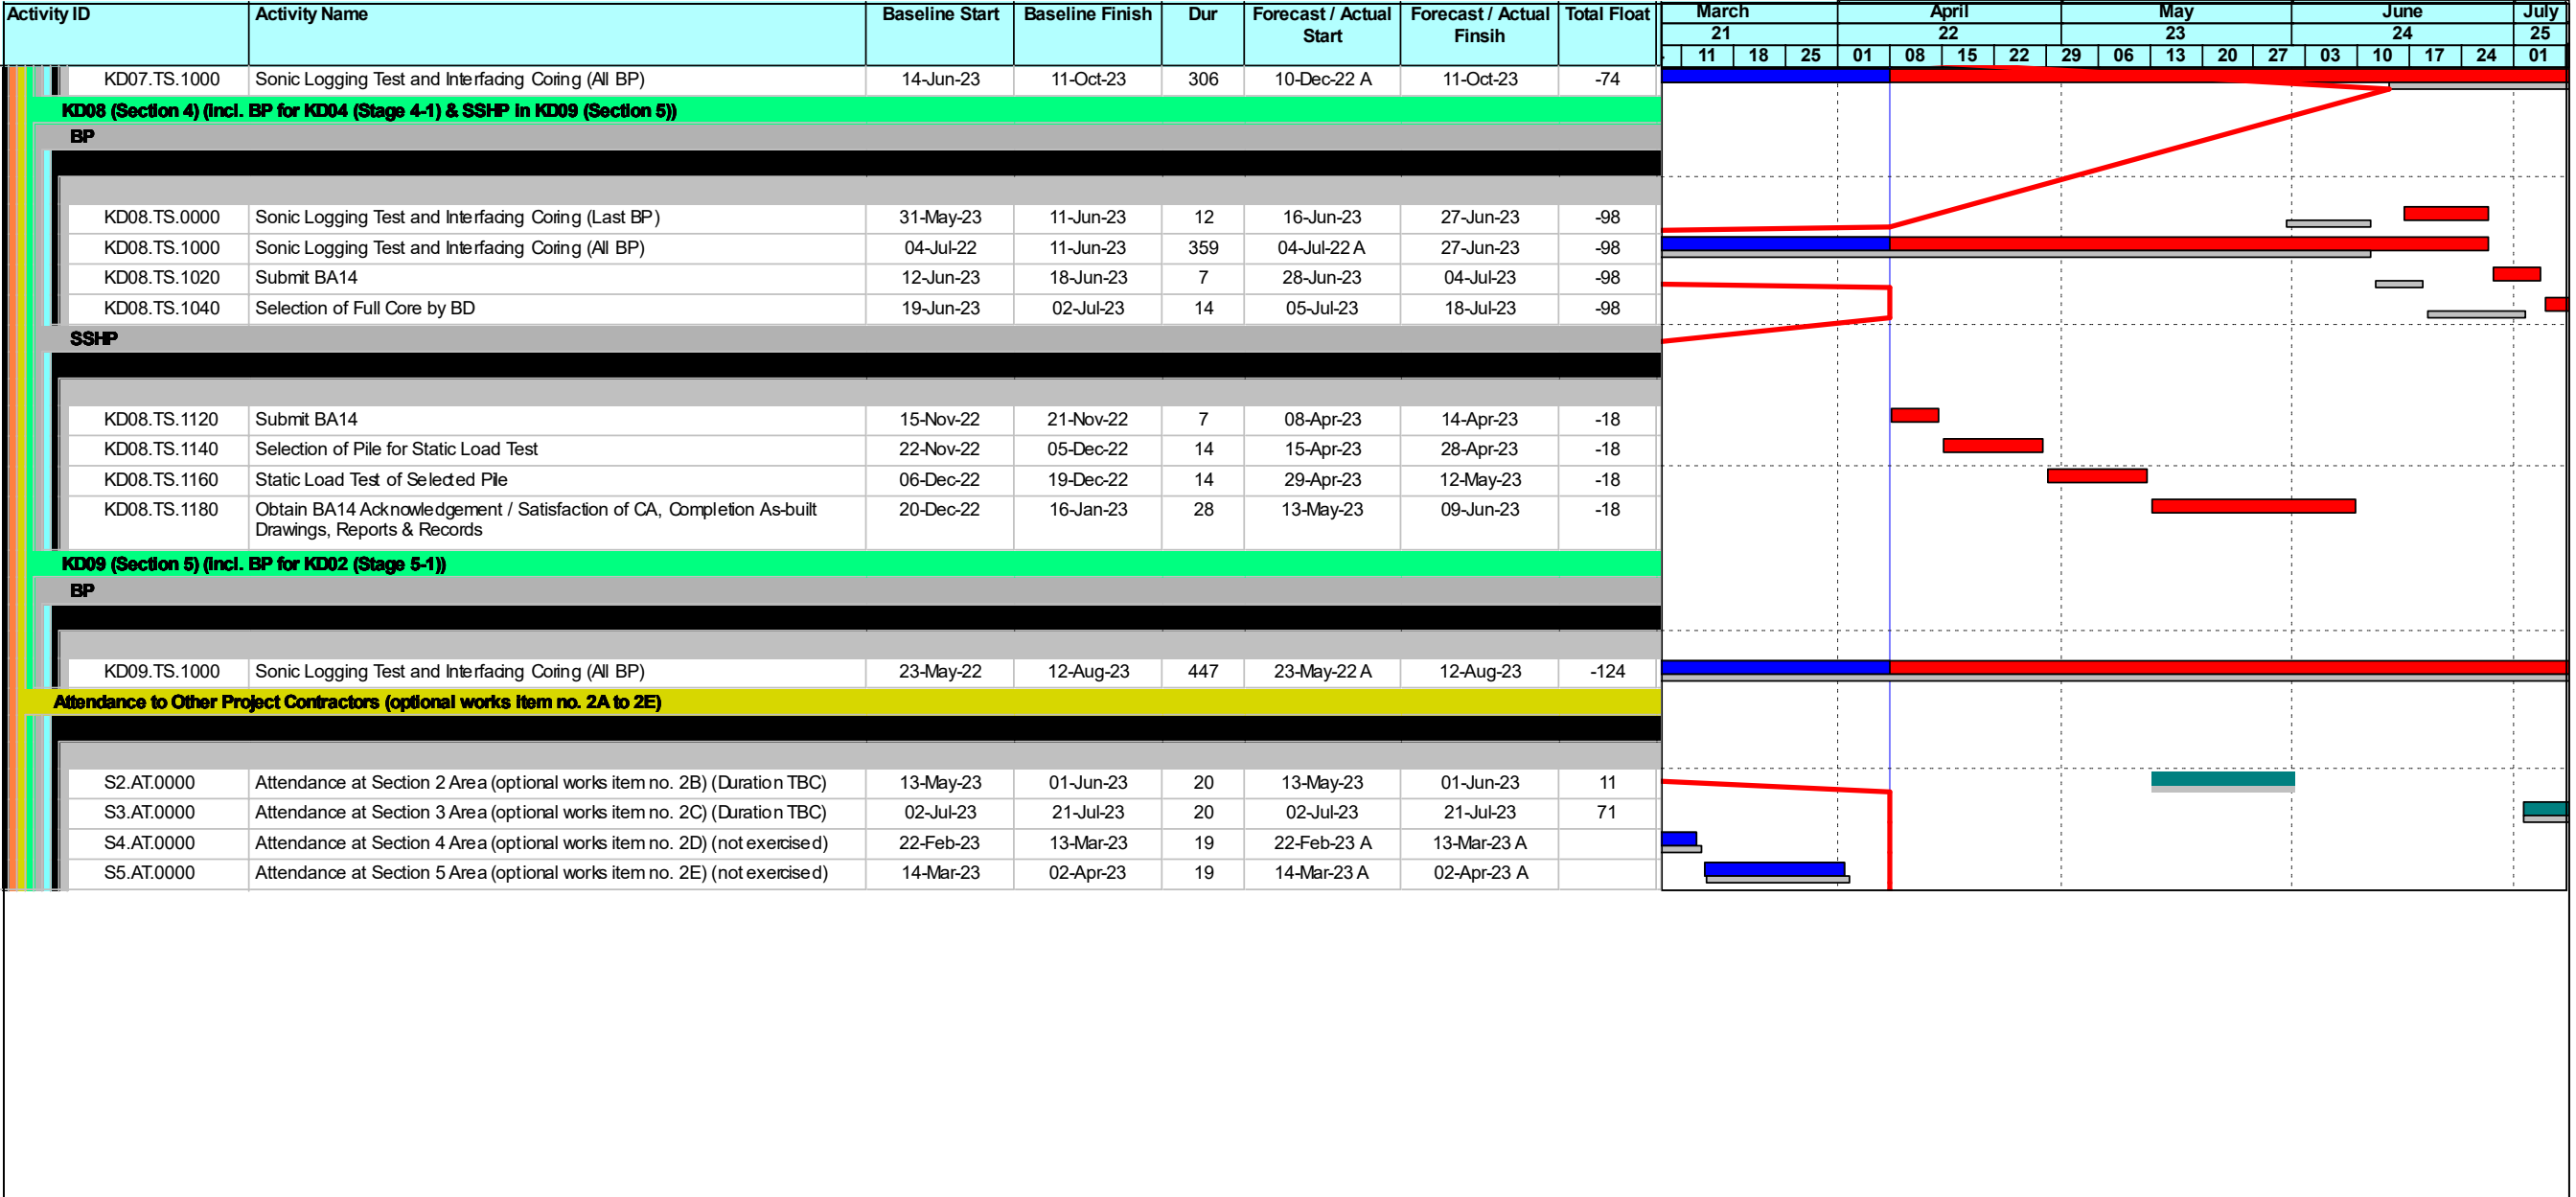

Date	Revision	Checked	Approved
04-Mar-23	R0	KL	B
02-Dec-23	R03D	KL	C



	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 7 April 2023
 Based on CMWP Rev.0 (3rd Draft)

		Date	Revision	Checked	Approved
		04-Mar-23	R0	KL	B
		02-Dec-23	R03D	KL	C
