

Zone 2B & 2C

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	May 23				June 24				July 25				August 26				
								29	06	13	20	27	03	10	17	24	01	08	15	22	29	05	12	19

Piling for Integrated Basement and U/G Road In Zone 2B & 2C

Contract Dates

Optional Works subjected to CA's Instruction

CO2B	Last CAI date for Optional Works Item No.2B (330 Days to 660 Days after Commencement)	13-May-23		0	13-May-23 A		
CO2C	Last CAI date for Optional Works Item No.2C (330 Days to 710 Days after Commencement)	02-Jul-23		0	02-Jul-23	71	

Construction Stage

PILE CONSTRUCTION

KD05 (Section 1)

Bored Piles - Drainage Diversion

CD07

04

P17-BP19.10	BP - Excavation	27-Jan-23	03-Feb-23	9	27-Apr-23 A	09-May-23 A	
P17-BP19.20	BP - RCD Drilling	04-Feb-23	21-Feb-23	5	10-May-23 A	16-May-23 A	
P17-BP19.30	BP - Airlift, Cage Install and Concrete	22-Feb-23	01-Mar-23	7	17-May-23 A	25-May-23 A	

CD08

P17-BP21.10	BP IAR-N - Excavation	07-Mar-23	13-Mar-23	15	11-Apr-23 A	28-Apr-23 A	
P17-BP21.20	BP IAR-N - RCD Drilling	14-Mar-23	30-Mar-23	5	29-Apr-23 A	06-May-23 A	
P17-BP21.30	BP IAR-N - Airlift, Cage Install and Concrete	31-Mar-23	12-Apr-23	7	08-May-23 A	16-May-23 A	

01

P17-BP20.10	BP - Excavation	17-Feb-23	23-Feb-23	4	27-May-23	31-May-23	-201
P17-BP20.20	BP - RCD Drilling	24-Feb-23	13-Mar-23	15	01-Jun-23	17-Jun-23	-201
P17-BP20.30	BP - Airlift, Cage Install and Concrete	14-Mar-23	21-Mar-23	7	19-Jun-23	27-Jun-23	-201

03

P17-BP18.10	BP IAR-N - Excavation	24-Mar-23	30-Mar-23	11	20-May-23 A	02-Jun-23	-203
P17-BP18.20	BP IAR-N - RCD Drilling	31-Mar-23	21-Apr-23	15	03-Jun-23 A	20-Jun-23	-203
P17-BP18.30	BP IAR-N - Airlift, Cage Install and Concrete	22-Apr-23	29-Apr-23	7	21-Jun-23 A	29-Jun-23	-203

Bored Piles - Gantry Gate A

CD06

08

CBA-BP01.30	BP - Airlift, Cage Install and Concrete	17-Feb-23	23-Feb-23	9	24-Apr-23 A	05-May-23 A	
-------------	---	-----------	-----------	---	-------------	-------------	--

CD07

02

P22&P19-BP26.:	BP - RCD Drilling	16-Jul-22	03-Dec-22	261	16-Jul-22 A	02-Jun-23	-189
P22&P19-BP26.:	BP - Airlift, Cage Install and Concrete	05-Dec-22	13-Dec-22	8	03-Jun-23	12-Jun-23	-189

Bored Piles


CD09

03

P17-BP22.30	BP IAR-N - Airlift, Cage Install and Concrete	04-Apr-23	15-Apr-23	7	20-Apr-23 A	28-Apr-23 A	
-------------	---	-----------	-----------	---	-------------	-------------	--

TD07

P18-BP04.30	BP IAR-S - Airlift, Cage Install and Concrete	01-Mar-23	08-Mar-23	11	19-Apr-23 A	03-May-23 A	
P18-BP01.20	BP - RCD Drilling	22-Dec-22	16-Jan-23	21	26-Apr-23 A	22-May-23 A	

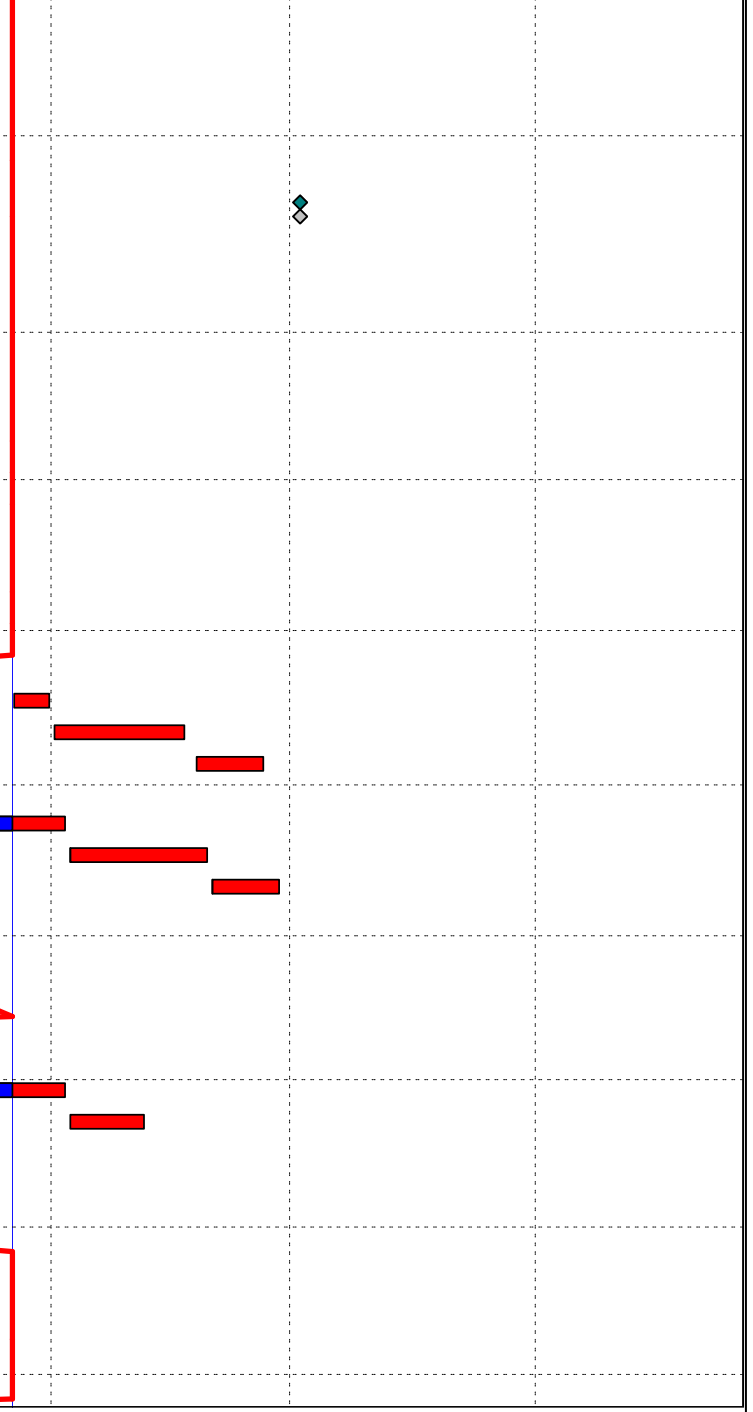

	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS


West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 26 May 2023
Based on CMWP Rev.0 (3rd Draft)







	Date	Revision	Checked	Approved
	04-Mar-22	R0	KL	B
	02-Dec-22	R03D	KL	C

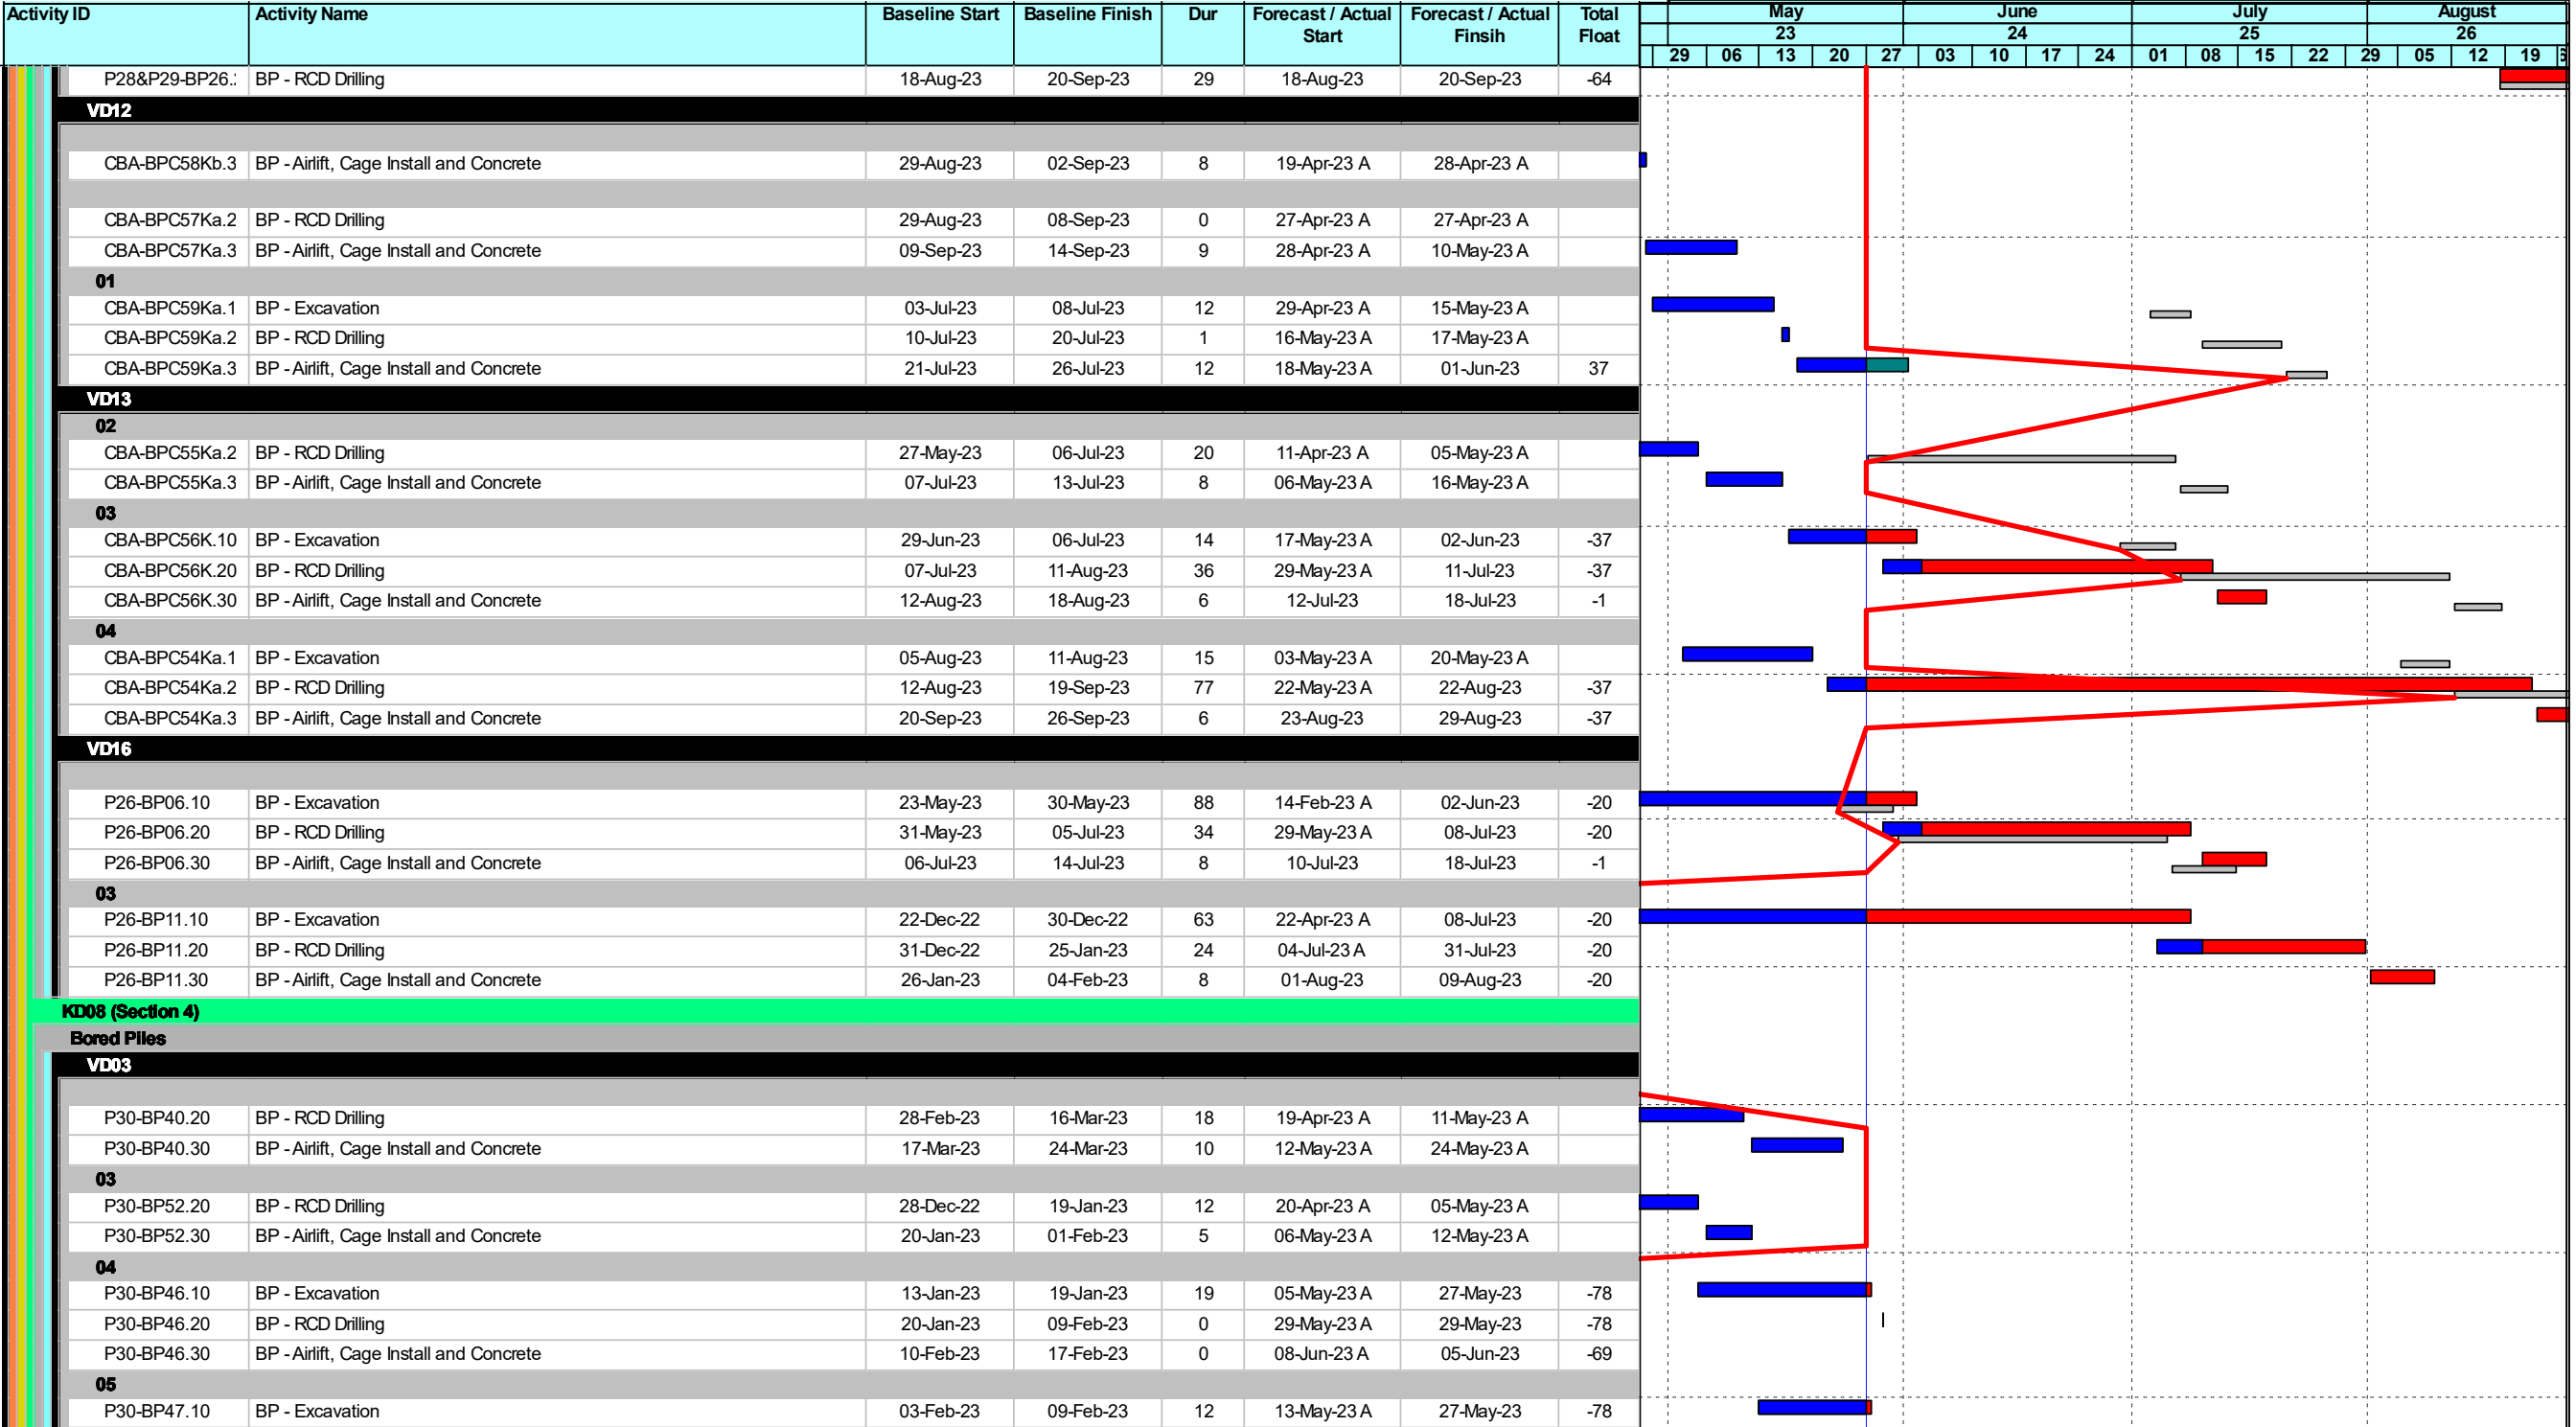Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	May 23				June 24				July 25				August 26							
								29	06	13	20	27	03	10	17	24	01	08	15	22	29	05	12	19			
P18-BP01.30	BP - Airlift, Cage Install and Concrete	17-Jan-23	27-Jan-23	6	23-May-23 A	30-May-23	-178																				
09																											
P18-BP07.10	BP IAR-S - Excavation	11-Mar-23	17-Mar-23	20	04-May-23 A	27-May-23	-194																				
P18-BP07.20	BP IAR-S - RCD Drilling	18-Mar-23	04-Apr-23	15	29-May-23 A	14-Jun-23	-194																				
P18-BP07.30	BP IAR-S - Airlift, Cage Install and Concrete	06-Apr-23	17-Apr-23	3	15-Jun-23 A	17-Jun-23	-194																				
TD09																											
CBA-BPC36Ka.1	BP IAR-N - Excavation	31-Mar-23	11-Apr-23	75	22-Feb-23 A	27-May-23	-190																				
CBA-BPC36Ka.2	BP IAR-N - RCD Drilling	12-Apr-23	22-Apr-23	15	20-May-23 A	07-Jun-23	-190																				
CBA-BPC36Ka.3	BP IAR-N - Airlift, Cage Install and Concrete	24-Apr-23	28-Apr-23	10	02-Jun-23 A	13-Jun-23	-190																				
KD06 (Section 2)																											
Bored Piles																											
VD14																											
05																											
P24&P27-BP15.	BP - Airlift, Cage Install and Concrete	28-Feb-23	08-Mar-23	6	26-Apr-23 A	04-May-23 A																					
08																											
P24&P27-BP21.	BP - Excavation	11-Apr-23	17-Apr-23	17	12-Apr-23 A	03-May-23 A																					
P24&P27-BP21.	BP - RCD Drilling	18-Apr-23	10-May-23	3	04-May-23 A	08-May-23 A																					
P24&P27-BP21.	BP - Airlift, Cage Install and Concrete	11-May-23	19-May-23	10	09-May-23 A	20-May-23 A																					
09																											
P24&P27-BP36.	BP - Excavation	04-May-23	10-May-23	11	08-May-23 A	20-May-23 A																					
P24&P27-BP36.	BP - RCD Drilling	11-May-23	02-Jun-23	25	22-May-23 A	20-Jun-23	-73																				
P24&P27-BP36.	BP - Airlift, Cage Install and Concrete	03-Jun-23	12-Jun-23	8	21-Jun-23	30-Jun-23	-73																				
VD15																											
06																											
P24&P27-BP03.	BP - RCD Drilling	22-Feb-23	27-Mar-23	10	15-Apr-23 A	27-Apr-23 A																					
P24&P27-BP03.	BP - Airlift, Cage Install and Concrete	28-Mar-23	06-Apr-23	6	28-Apr-23 A	06-May-23 A																					
07																											
P24&P27-BP10.	BP - Excavation	21-Mar-23	27-Mar-23	19	26-Apr-23 A	19-May-23 A																					
P24&P27-BP10.	BP - RCD Drilling	28-Mar-23	05-May-23	2	20-May-23 A	23-May-23 A																					
P24&P27-BP10.	BP - Airlift, Cage Install and Concrete	06-May-23	15-May-23	10	24-May-23 A	05-Jun-23	-52																				
CD01																											
P23-BP26.30	BP - Airlift, Cage Install and Concrete	28-Mar-23	06-Apr-23	9	26-Apr-23 A	08-May-23 A																					
02																											
P23-BP14.30	BP - Airlift, Cage Install and Concrete	05-Jan-23	13-Jan-23	13	27-Apr-23 A	13-May-23 A																					
08																											
P23-BP15.10	BP - Excavation	10-May-23	16-May-23	32	31-Mar-23 A	13-May-23 A																					
P23-BP15.20	BP - RCD Drilling	17-May-23	20-Jun-23	5	15-May-23 A	20-May-23 A																					
P23-BP15.30	BP - Airlift, Cage Install and Concrete	21-Jun-23	30-Jun-23	12	22-May-23 A	05-Jun-23	-52																				
CD03																											
02																											
P22&P19-BP13.	BP - RCD Drilling	28-Sep-22	11-Nov-22	203	28-Sep-22 A	07-Jun-23	-62																				
P22&P19-BP13.	BP - Airlift, Cage Install and Concrete	12-Nov-22	21-Nov-22	8	08-Jun-23	16-Jun-23	-62																				
KD07 (Section 3)																											
Bored Piles																											
VD01																											

- Planned
- Critical
- Actual
- Planned MS
- Critical MS
- Actual MS

Date	Revision	Checked	Approved
04-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C



	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS

Date	Revision	Checked	Approved
04-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C




Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	May 23				June 24				July 25				August 26				
								29	06	13	20	27	03	10	17	24	01	08	15	22	29	05	12	19
P30-BP47.20	BP - RCD Drilling	10-Feb-23	27-Feb-23	0	29-May-23 A	29-May-23	-78																	
P30-BP47.30	BP - Airlift, Cage Install and Concrete	28-Feb-23	07-Mar-23	0	08-Jun-23 A	05-Jun-23	-69																	
08																								
P30-BP49.10	BP - Excavation	28-Mar-23	03-Apr-23	1	27-May-23	27-May-23	-78																	
P30-BP49.20	BP - RCD Drilling	04-Apr-23	29-Apr-23	10	29-May-23	08-Jun-23	-78																	
P30-BP49.30	BP - Airlift, Cage Install and Concrete	02-May-23	10-May-23	6	09-Jun-23	15-Jun-23	-78																	
VD04																								
06																								
P30-BP31.20	BP - RCD Drilling	18-Feb-23	23-Mar-23	12	20-Apr-23 A	05-May-23 A																		
P30-BP31.30	BP - Airlift, Cage Install and Concrete	24-Mar-23	01-Apr-23	9	06-May-23 A	17-May-23 A																		
07																								
P30-BP35.10	BP - Excavation	17-Mar-23	23-Mar-23	25	17-Apr-23 A	17-May-23 A																		
P30-BP35.20	BP - RCD Drilling	24-Mar-23	14-Apr-23	5	18-May-23 A	24-May-23 A																		
P30-BP35.30	BP - Airlift, Cage Install and Concrete	15-Apr-23	22-Apr-23	8	25-May-23 A	03-Jun-23	-68																	
VD05																								
P30-BP50.10	BP - Excavation	03-Apr-23	13-Apr-23	20	20-Apr-23 A	15-May-23 A																		
P30-BP50.20	BP - RCD Drilling	14-Apr-23	06-May-23	10	16-May-23 A	27-May-23	-70																	
P30-BP50.30	BP - Airlift, Cage Install and Concrete	08-May-23	16-May-23	8	29-May-23	06-Jun-23	-70																	
05																								
P30-BP43.10	BP - Excavation	12-Jan-23	18-Jan-23	8	18-May-23 A	27-May-23	-70																	
P30-BP43.20	BP - RCD Drilling	19-Jan-23	13-Feb-23	0	29-May-23 A	29-May-23	-70																	
P30-BP43.30	BP - Airlift, Cage Install and Concrete	14-Feb-23	22-Feb-23	8	29-May-23	06-Jun-23	-70																	
TD09																								
P26-BP19.30	BP - Airlift, Cage Install and Concrete	16-Dec-22	22-Dec-22	8	21-Apr-23 A	02-May-23 A																		
P26-BP17.10	BP - Excavation	23-Feb-23	01-Mar-23	28	25-Mar-23 A	03-May-23 A																		
P26-BP17.20	BP - RCD Drilling	02-Mar-23	11-Apr-23	7	04-May-23 A	12-May-23 A																		
P26-BP17.30	BP - Airlift, Cage Install and Concrete	12-Apr-23	18-Apr-23	3	13-May-23 A	17-May-23 A																		
KD09 (Section 5)																								
Bored Piles																								
VD01																								
P23-BP34.30	BP - Airlift, Cage Install and Concrete	06-Jan-23	14-Jan-23	48	04-Apr-23 A	05-Jun-23	-52																	
CD01																								
03																								
P23-BP35.10	BP - Excavation	28-Dec-22	04-Jan-23	22	20-Apr-23 A	17-May-23 A																		
P23-BP35.20	BP - RCD Drilling	05-Jan-23	30-Jan-23	5	18-May-23 A	24-May-23 A																		
P23-BP35.30	BP - Airlift, Cage Install and Concrete	31-Jan-23	08-Feb-23	9	25-May-23 A	05-Jun-23	-52																	
CD02																								
09																								
P23-BP36.10	BP - Excavation	04-Apr-23	14-Apr-23	29	12-May-23 A	15-Jun-23	-98																	
P23-BP36.20	BP - RCD Drilling	15-Apr-23	19-May-23	45	29-May-23 A	21-Jul-23	-98																	
P23-BP36.30	BP - Airlift, Cage Install and Concrete	20-May-23	30-May-23	8	22-Jul-23	31-Jul-23	-98																	
TD01																								
02																								

	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 26 May 2023
Based on CMWP Rev.0 (3rd Draft)




Date	Revision	Checked	Approved
04-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C

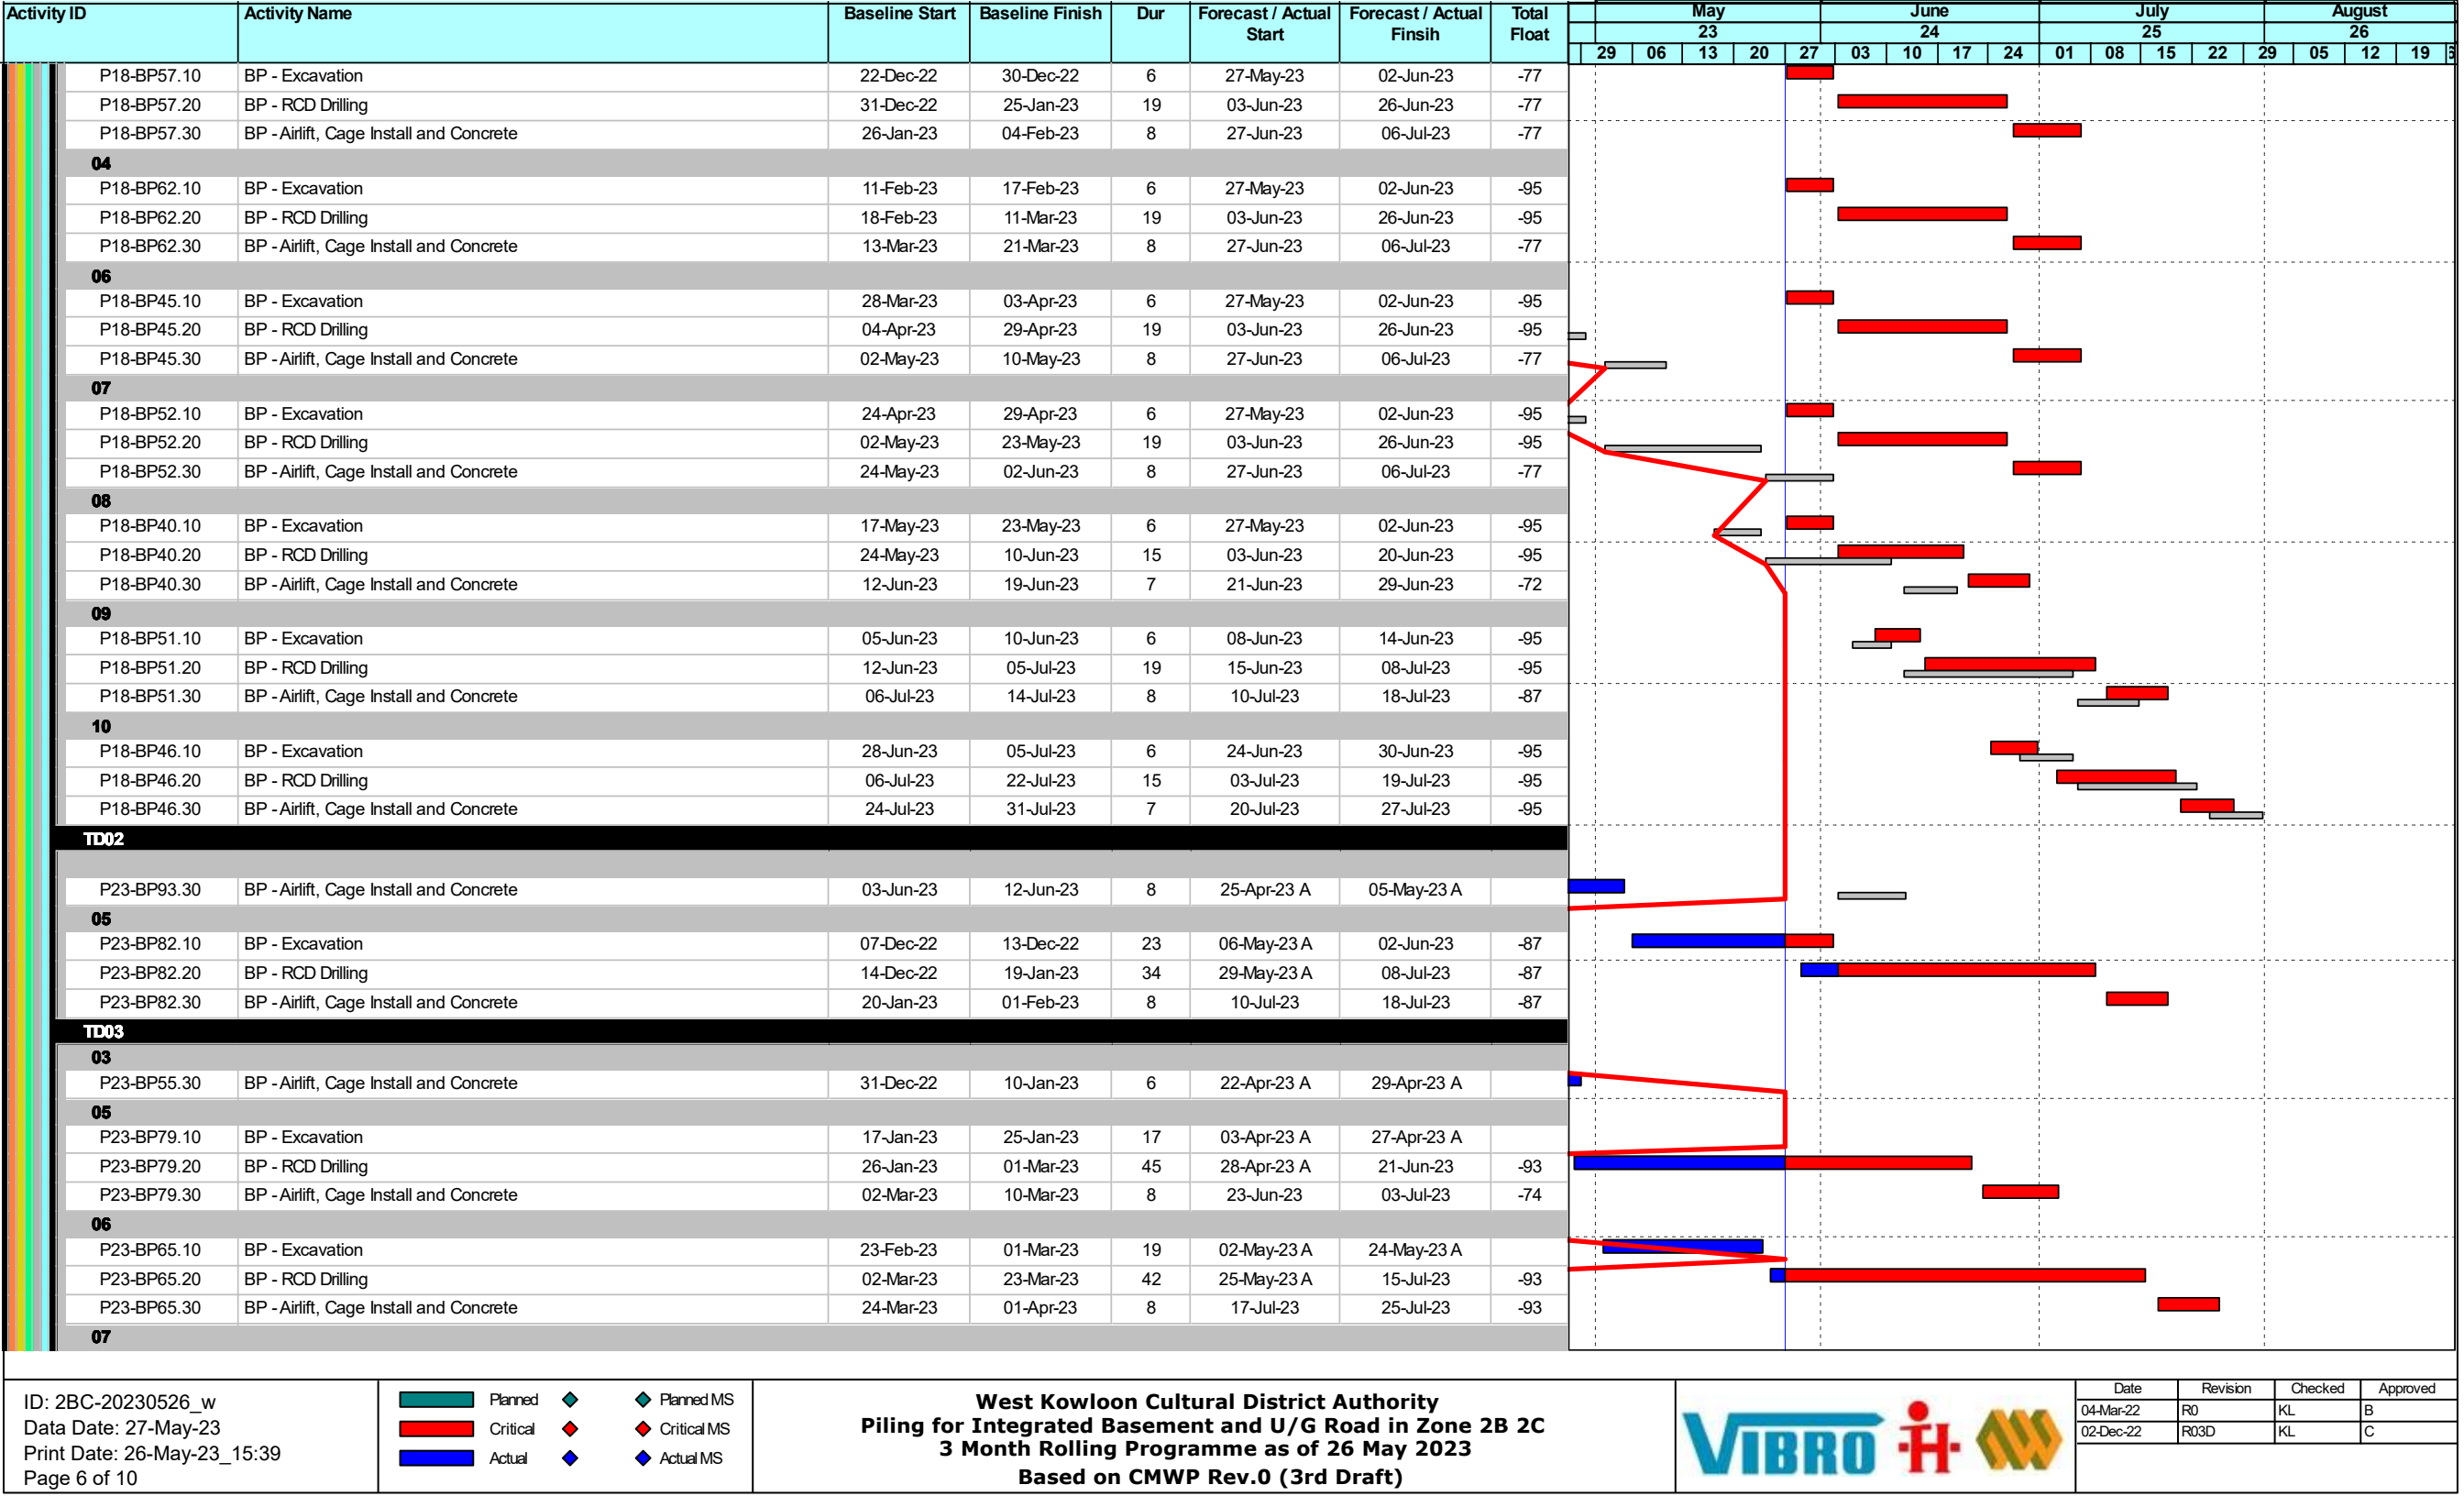

Planned	Planned MS
Critical	Critical MS
Actual	Actual MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 26 May 2023
Based on CMWP Rev.0 (3rd Draft)

	Date	Revision	Checked	Approved
	04-Mar-22	R0	KL	B
	02-Dec-22	R03D	KL	C

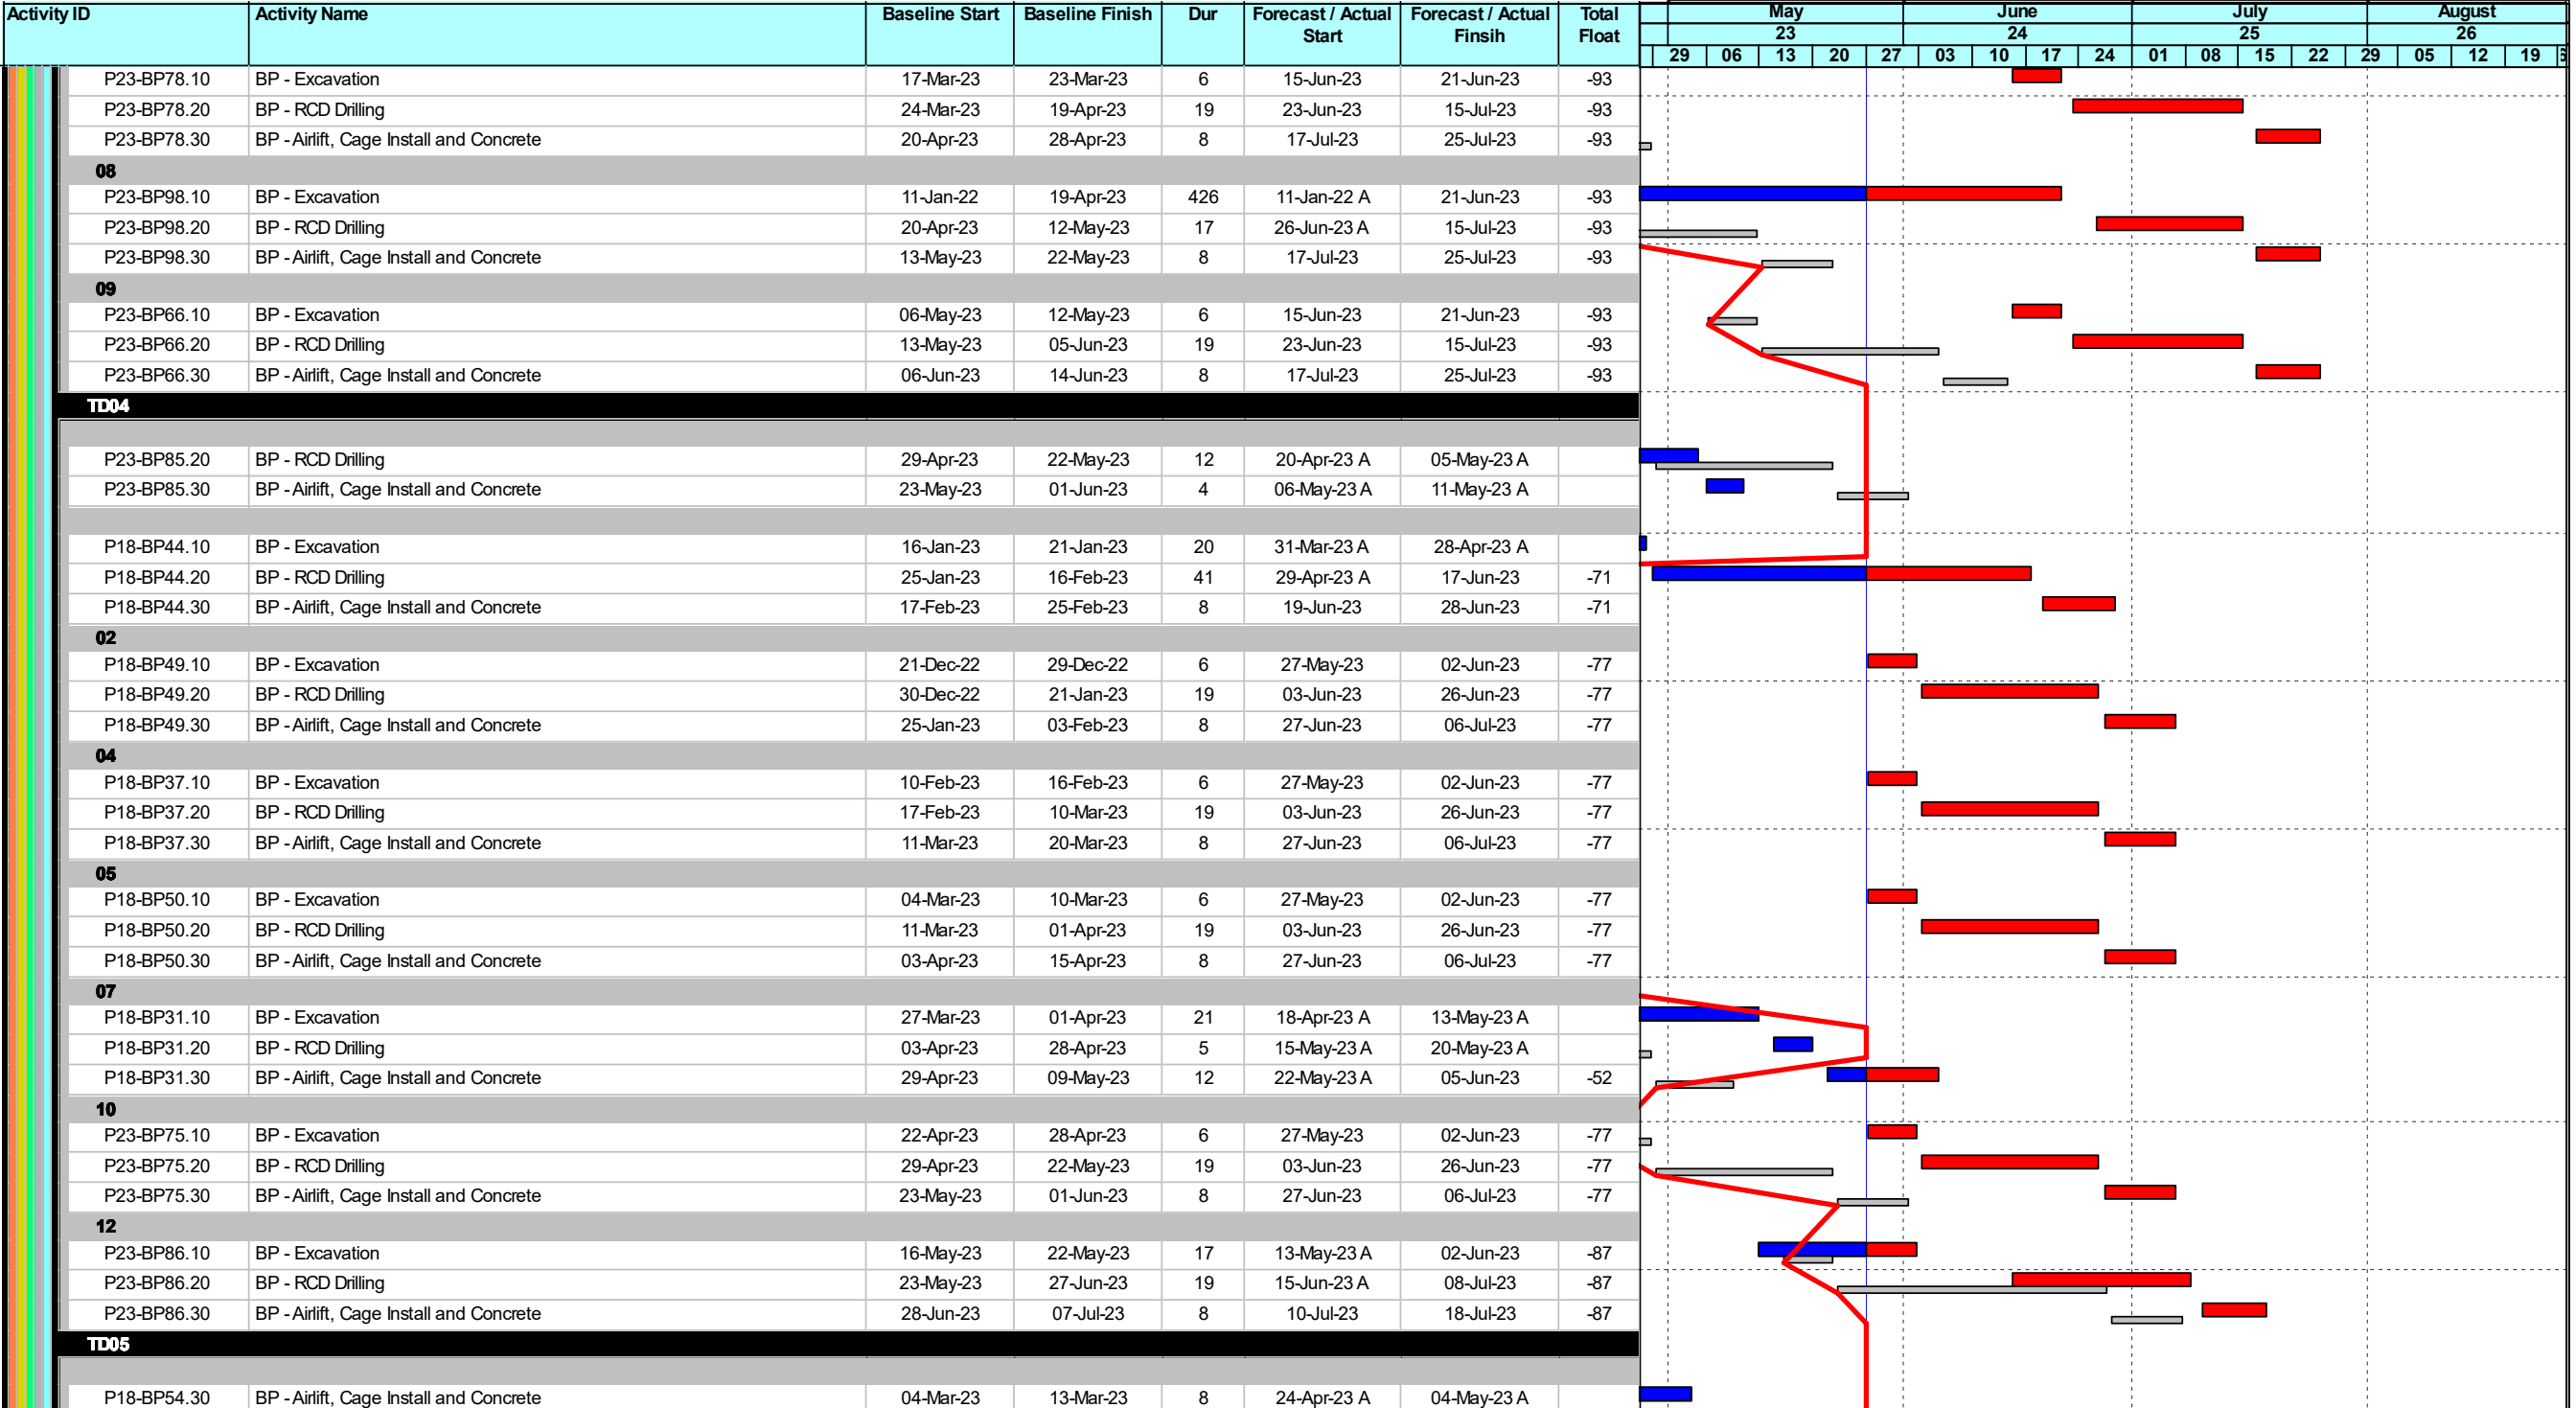


	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 26 May 2023
 Based on CMWP Rev.0 (3rd Draft)



Date	Revision	Checked	Approved
04-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C

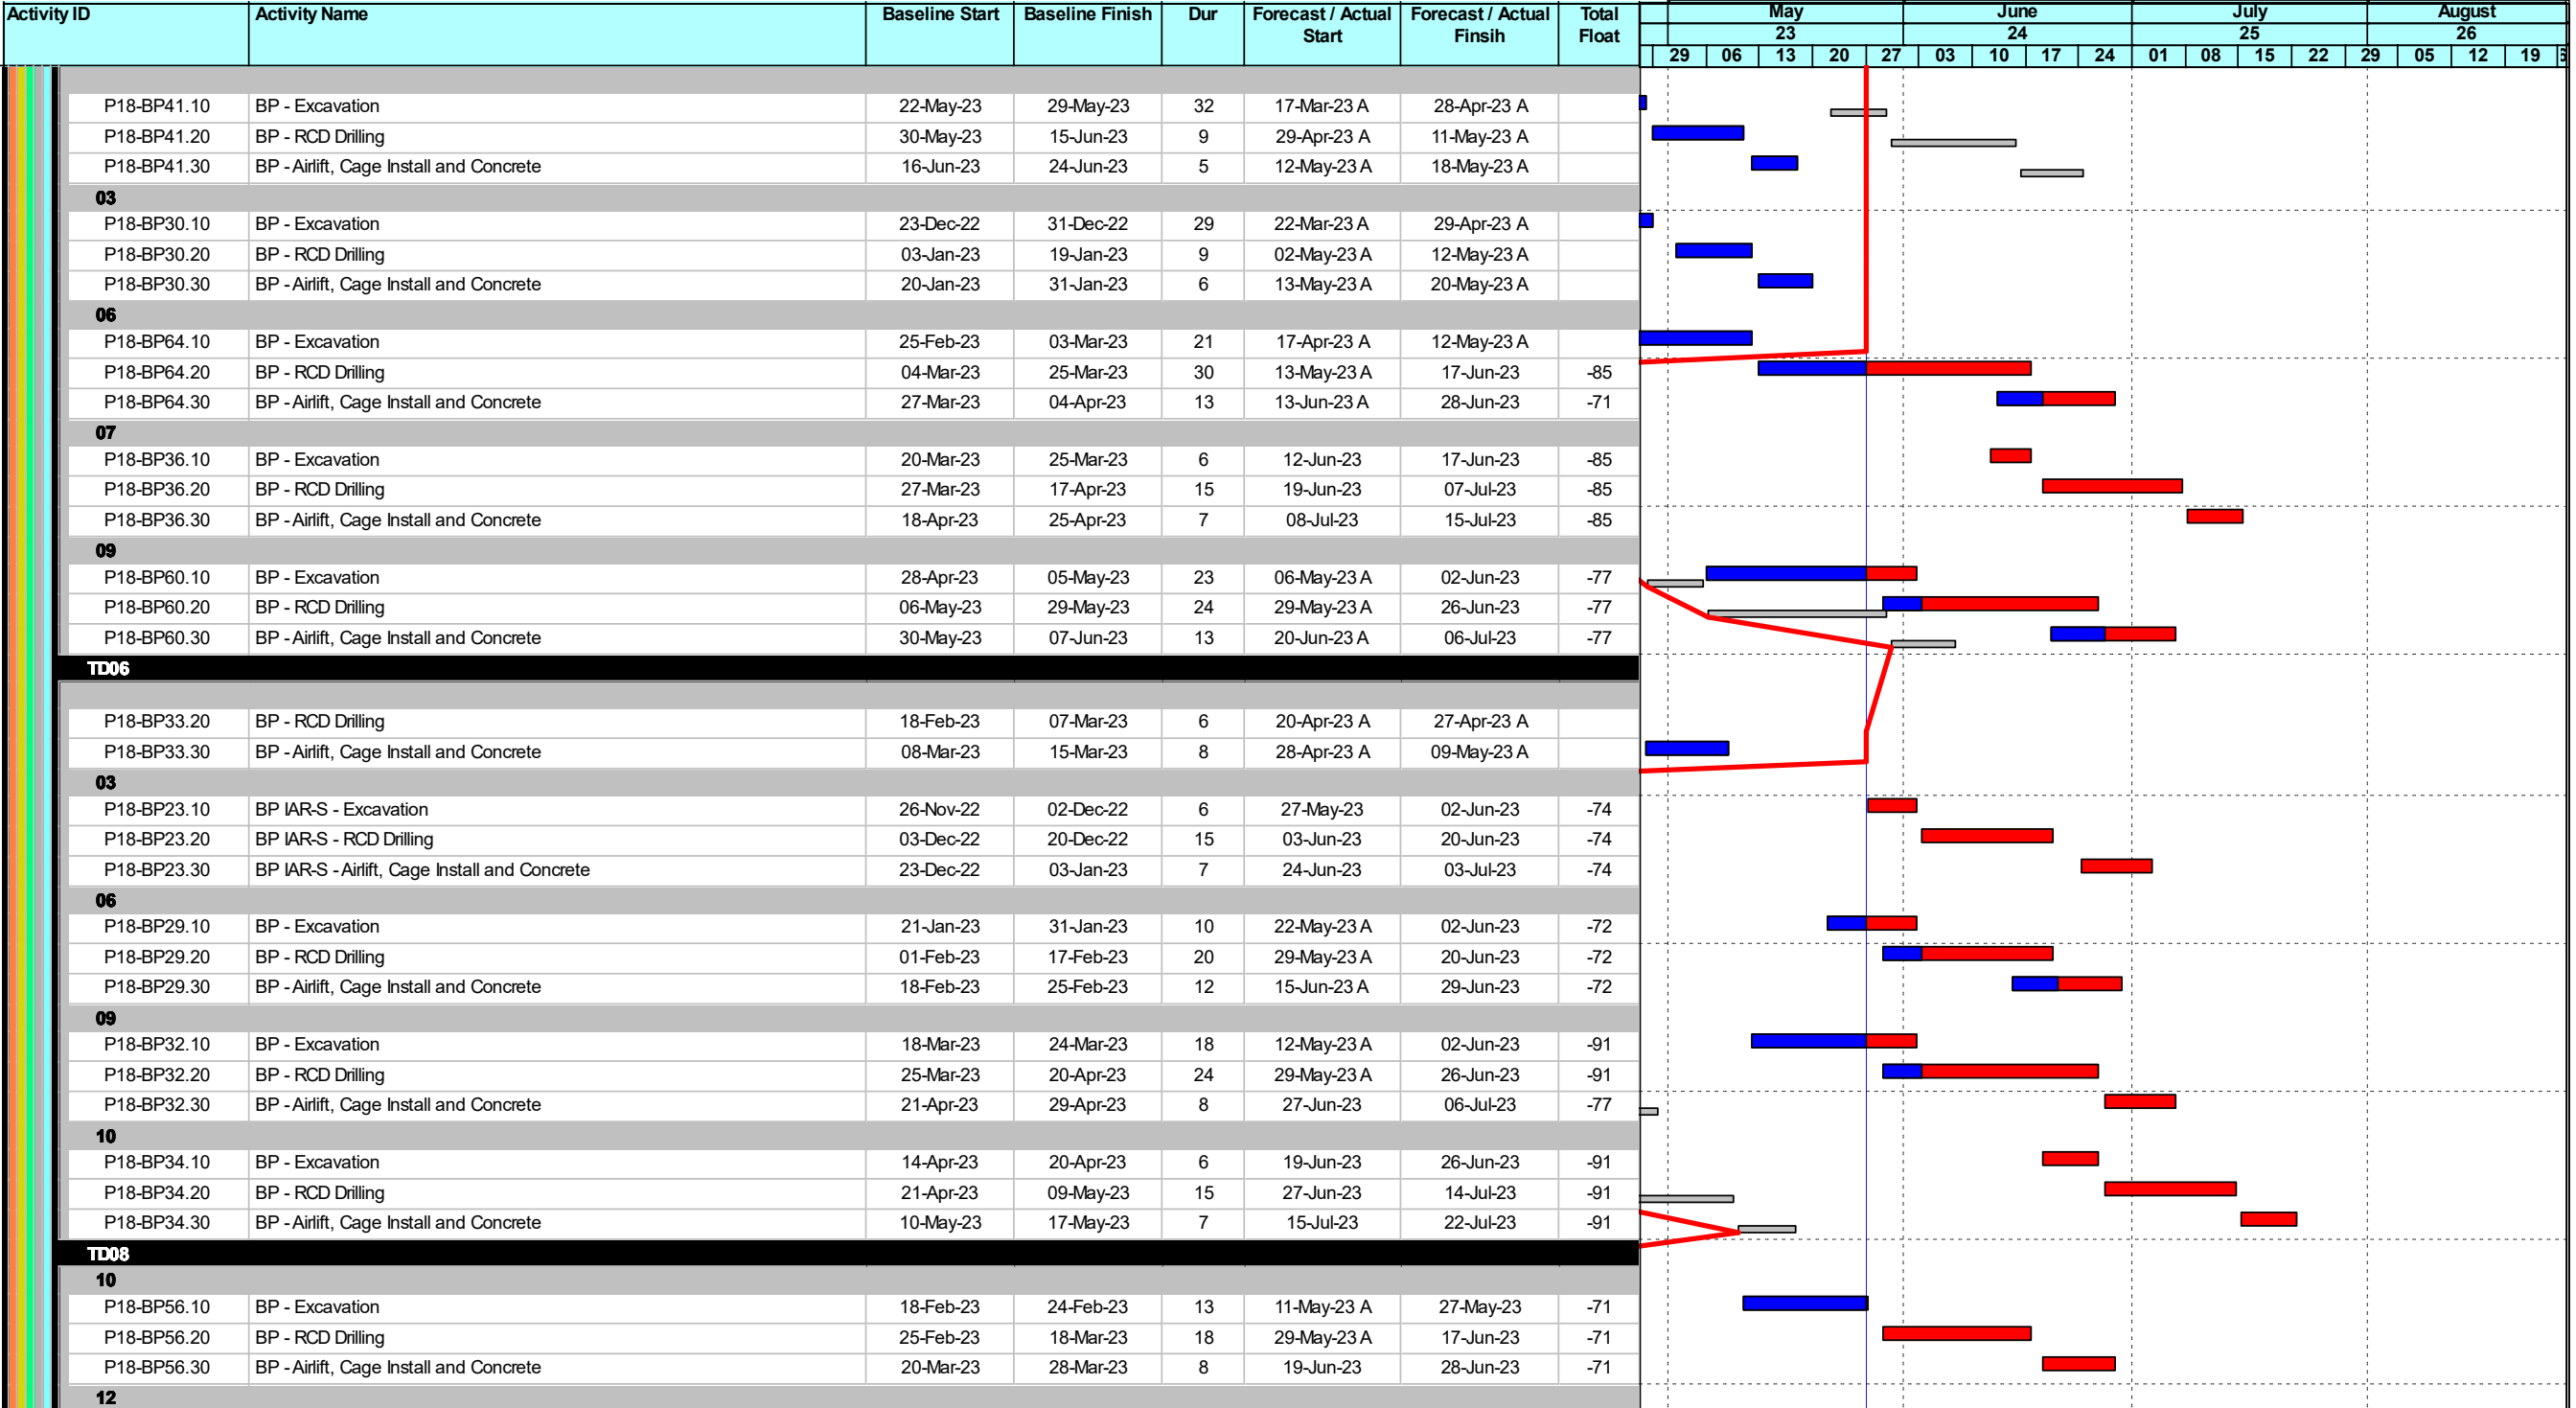








Planned	Planned MS
Critical	Critical MS
Actual	Actual MS

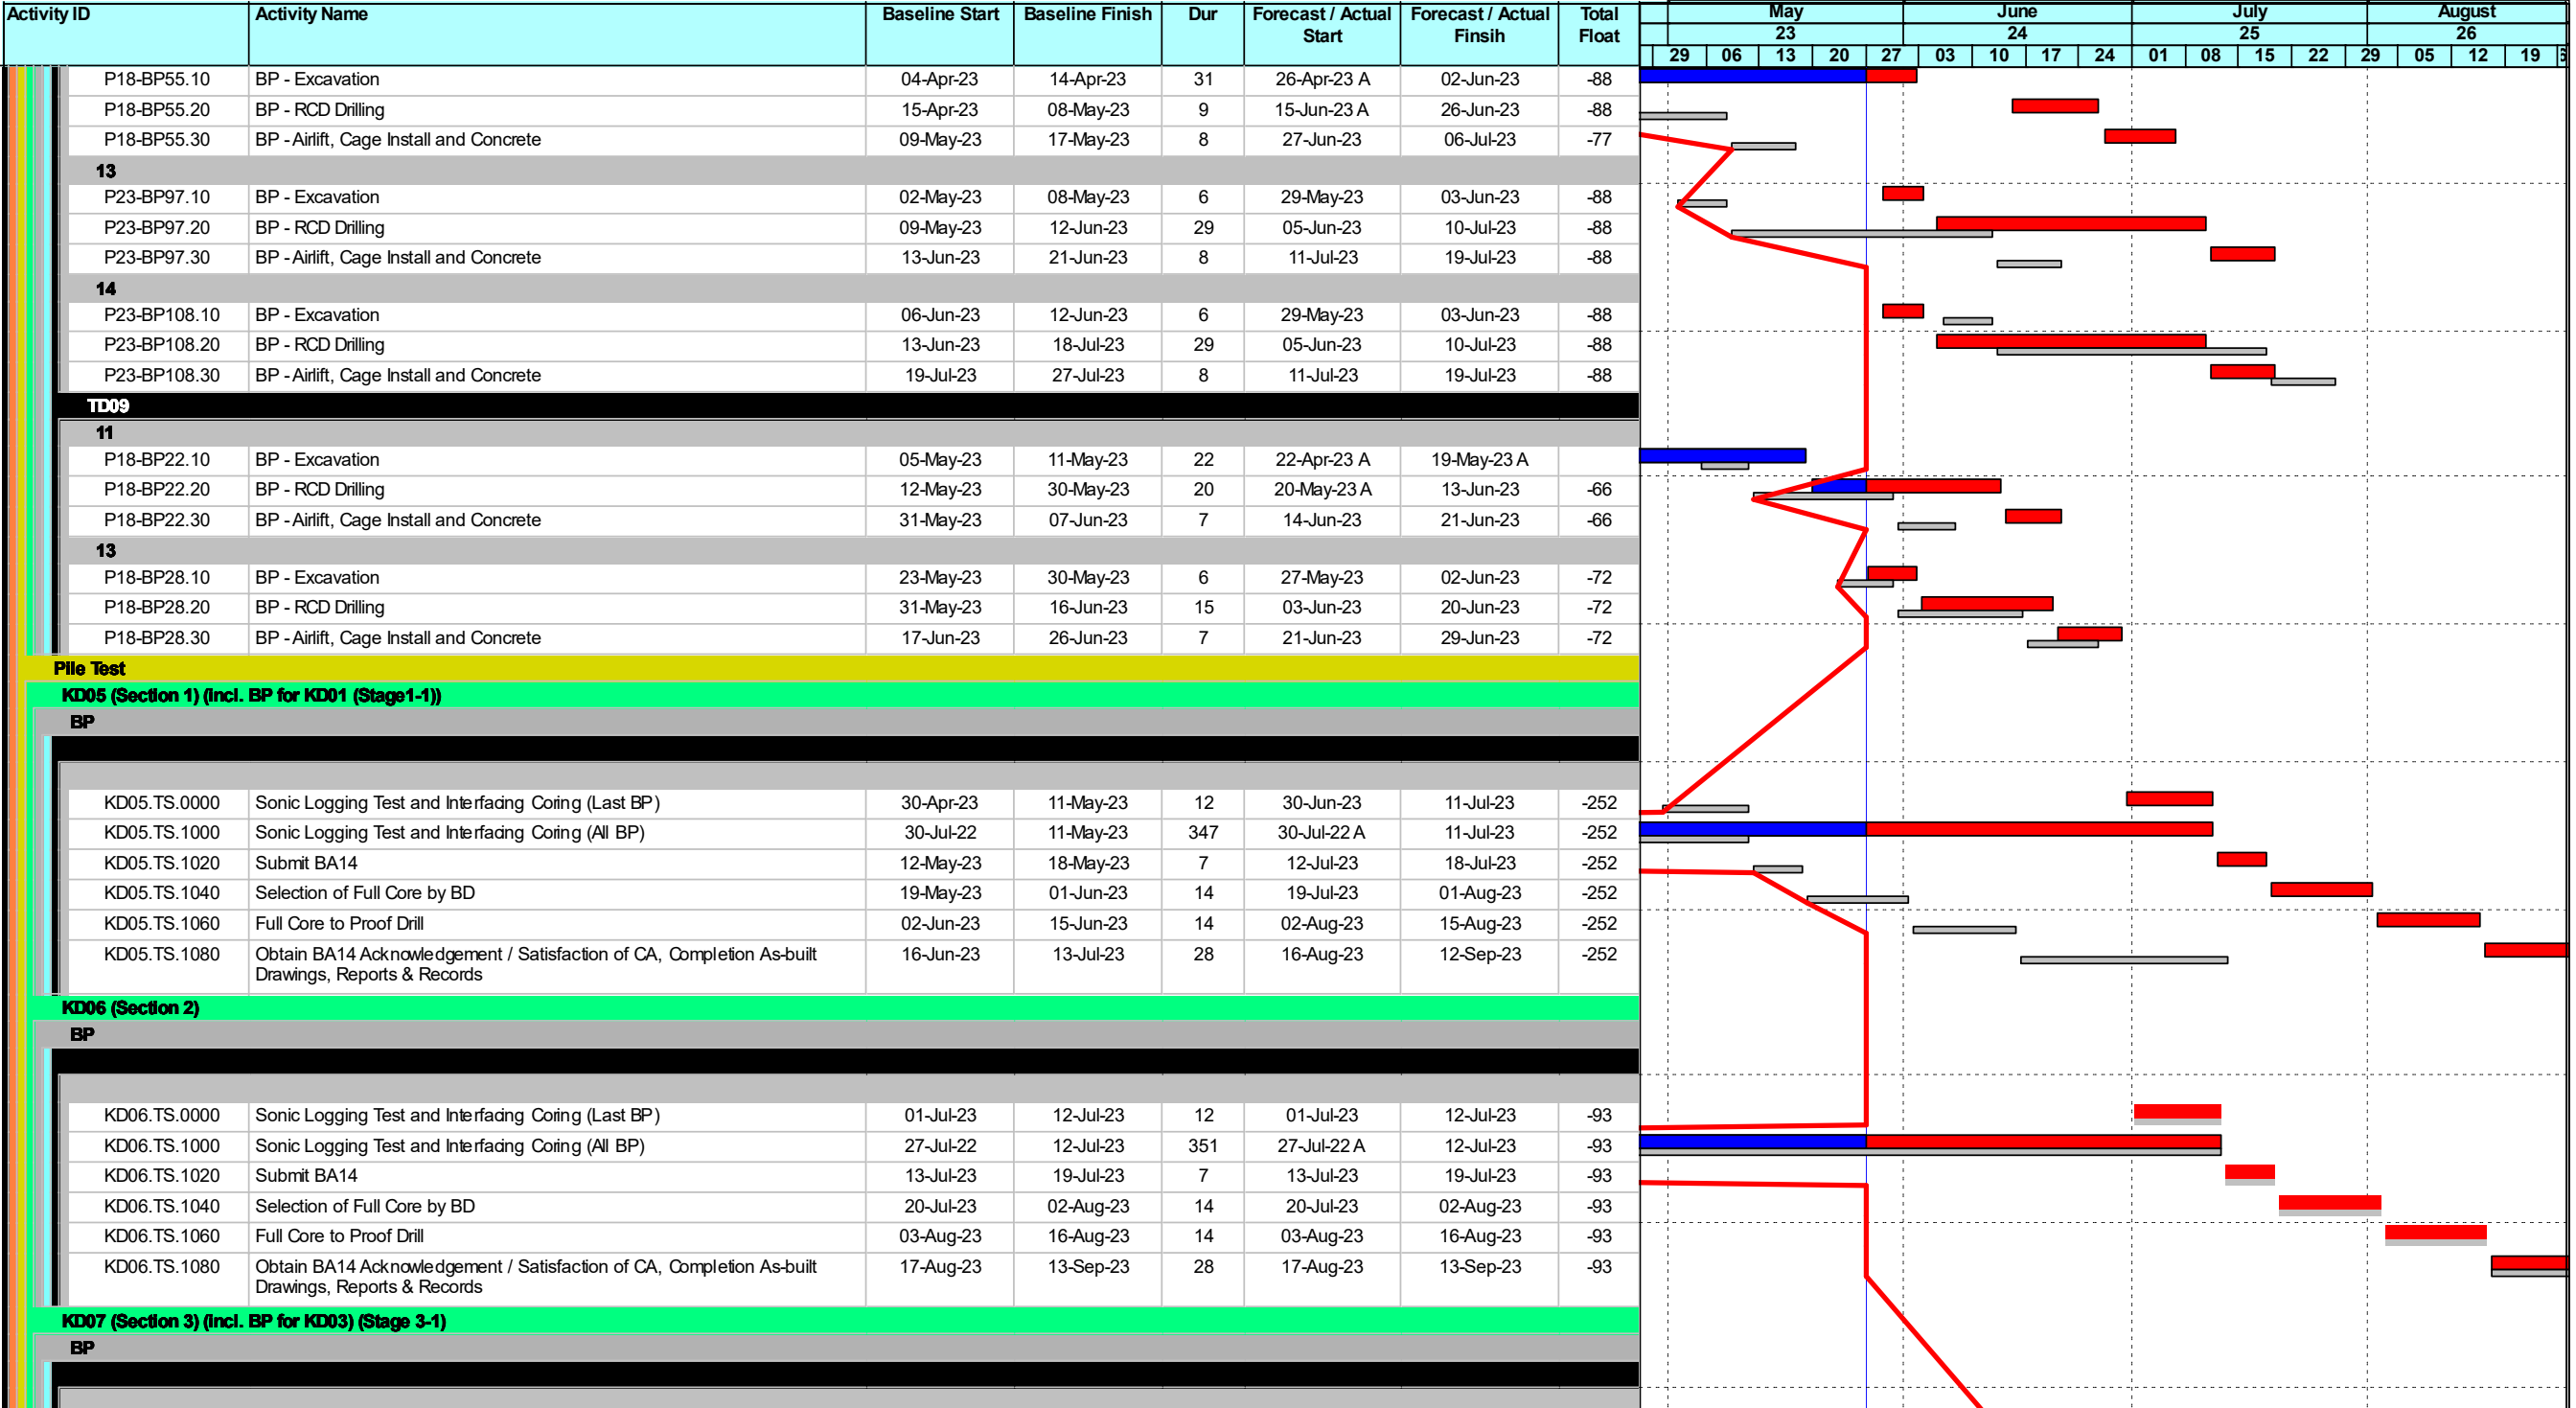West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 26 May 2023
 Based on CMWP Rev.0 (3rd Draft)



Date	Revision	Checked	Approved
04-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C



	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 26 May 2023
 Based on CMWP Rev.0 (3rd Draft)

	Date	Revision	Checked	Approved
	04-Mar-22	R0	KL	B
	02-Dec-22	R03D	KL	C

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	May 23				June 24				July 25				August 26				
								29	06	13	20	27	03	10	17	24	01	08	15	22	29	05	12	19
KD07.TS.1000	Sonic Logging Test and Interfacing Coring (All BP)	14-Jun-23	11-Oct-23	306	10-Dec-22 A	11-Oct-23	-74																	
KD08 (Section 4) (Incl. BP for KD04 (Stage 4-1) & SSHP in KD09 (Section 5))																								
BP																								
KD08.TS.0000	Sonic Logging Test and Interfacing Coring (Last BP)	31-May-23	11-Jun-23	12	16-Jun-23	27-Jun-23	-98																	
KD08.TS.1000	Sonic Logging Test and Interfacing Coring (All BP)	04-Jul-22	11-Jun-23	359	04-Jul-22 A	27-Jun-23	-98																	
KD08.TS.1020	Submit BA14	12-Jun-23	18-Jun-23	7	28-Jun-23	04-Jul-23	-98																	
KD08.TS.1040	Selection of Full Core by BD	19-Jun-23	02-Jul-23	14	05-Jul-23	18-Jul-23	-98																	
KD08.TS.1060	Full Core to Proof Drill	03-Jul-23	16-Jul-23	14	19-Jul-23	01-Aug-23	-98																	
KD08.TS.1080	Obtain BA14 Acknowledgement / Satisfaction of CA, Completion As-built Drawings, Reports & Records	17-Jul-23	13-Aug-23	28	02-Aug-23	29-Aug-23	-98																	
SSHP																								
KD08.TS.1120	Submit BA14	15-Nov-22	21-Nov-22	7	27-May-23	02-Jun-23	-67																	
KD08.TS.1140	Selection of Pile for Static Load Test	22-Nov-22	05-Dec-22	14	03-Jun-23	16-Jun-23	-67																	
KD08.TS.1160	Static Load Test of Selected Pile	06-Dec-22	19-Dec-22	14	17-Jun-23	30-Jun-23	-67																	
KD08.TS.1180	Obtain BA14 Acknowledgement / Satisfaction of CA, Completion As-built Drawings, Reports & Records	20-Dec-22	16-Jan-23	28	01-Jul-23	28-Jul-23	-67																	
KD09 (Section 5) (Incl. BP for KD02 (Stage 5-1))																								
BP																								
KD09.TS.0000	Sonic Logging Test and Interfacing Coring (Last BP)	01-Aug-23	12-Aug-23	12	01-Aug-23	12-Aug-23	-124																	
KD09.TS.1000	Sonic Logging Test and Interfacing Coring (All BP)	23-May-22	12-Aug-23	447	23-May-22 A	12-Aug-23	-124																	
KD09.TS.1020	Submit BA14	13-Aug-23	19-Aug-23	7	13-Aug-23	19-Aug-23	-124																	
KD09.TS.1040	Selection of Full Core by BD	20-Aug-23	02-Sep-23	14	20-Aug-23	02-Sep-23	-124																	
Attendance to Other Project Contractors (optional works item no. 2A to 2E)																								
S2.AT.0000	Attendance at Section 2 Area (optional works item no. 2B) (Duration TBC)	13-May-23	01-Jun-23	20	27-May-23	15-Jun-23	-3																	
S3.AT.0000	Attendance at Section 3 Area (optional works item no. 2C) (Duration TBC)	02-Jul-23	21-Jul-23	20	02-Jul-23	21-Jul-23	71																	

	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 26 May 2023
 Based on CMWP Rev.0 (3rd Draft)



Date	Revision	Checked	Approved
04-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	June				July				August				September			
								24				25				26				27			
								03	10	17	24	01	08	15	22	29	05	12	19	26	02	09	16

Piling for Integrated Basement and U/G Road in Zone 2B & 2C

Contract Dates

Key Dates

KD for Zone 2B

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float
KD05	KD05 (Section 1) - 03 Jan 2023		13-Jul-23	0		25-Sep-23*	-265
KD06	KD06 (Section 2) - 12 Jun 2023		13-Sep-23	0		09-Sep-23*	-89

KD for Zone 2C

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float
KD08	KD08 (Section 4) - 23 May 2023		13-Aug-23	0		10-Sep-23*	-110

Optional Works subjected to CA's Instruction

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float
CO2C	Last CAI date for Optional Works Item No.2C (330 Days to 710 Days after Commencement)	02-Jul-23		0	02-Jul-23		71

Construction Stage

Pile Construction

KD05 (Section 1)

Bored Piles - Drainage Diversion

CD08

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float
01							
P17-BP20.10	BP - Excavation	17-Feb-23	23-Feb-23	16	27-May-23 A	15-Jun-23 A	
P17-BP20.20	BP - RCD Drilling	24-Feb-23	13-Mar-23	9	16-Jun-23 A	28-Jun-23 A	
P17-BP20.30	BP - Airlift, Cage Install and Concrete	14-Mar-23	21-Mar-23	9	29-Jun-23 A	10-Jul-23	-211
03							
P17-BP18.10	BP IAR-N - Excavation	24-Mar-23	30-Mar-23	13	20-May-23 A	06-Jun-23 A	
P17-BP18.20	BP IAR-N - RCD Drilling	31-Mar-23	21-Apr-23	6	07-Jun-23 A	14-Jun-23 A	
P17-BP18.30	BP IAR-N - Airlift, Cage Install and Concrete	22-Apr-23	29-Apr-23	22	15-Jun-23 A	12-Jul-23	-213

Bored Piles - Gantry Gate A


CD07

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float
02							
P22&P19-BP26.:	BP - RCD Drilling	16-Jul-22	03-Dec-22	284	16-Jul-22 A	03-Jul-23	-212
P22&P19-BP26.:	BP - Airlift, Cage Install and Concrete	05-Dec-22	13-Dec-22	8	03-Jul-23	11-Jul-23	-212

Bored Piles

TD07

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float
04							
P18-BP01.30	BP - Airlift, Cage Install and Concrete	17-Jan-23	27-Jan-23	7	23-May-23 A	01-Jun-23 A	
09							
P18-BP07.20	BP IAR-S - RCD Drilling	18-Mar-23	04-Apr-23	10	31-May-23 A	12-Jun-23 A	
P18-BP07.30	BP IAR-S - Airlift, Cage Install and Concrete	06-Apr-23	17-Apr-23	5	24-Jun-23 A	30-Jun-23 A	

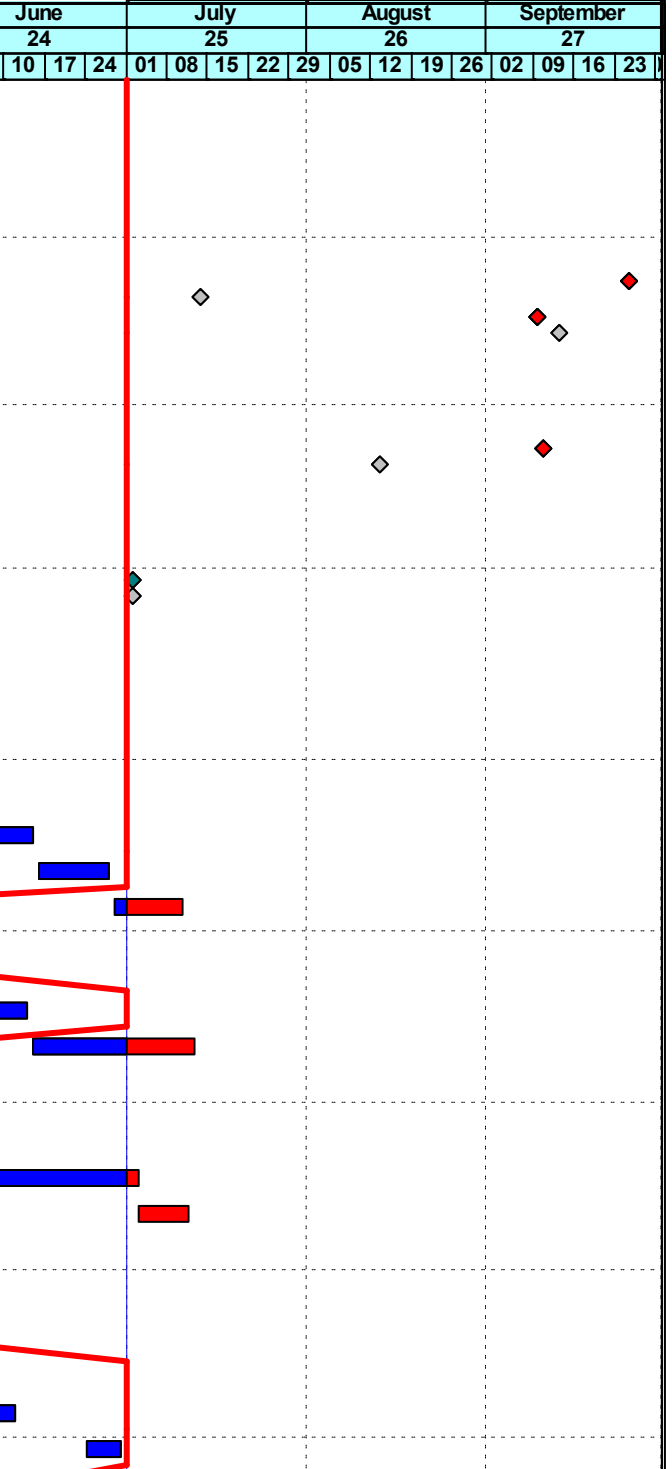

	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS

Date	Revision	Checked	Approved
04-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	June				July				August				September			
								24				25				26				27			
								03	10	17	24	01	08	15	22	29	05	12	19	26	02	09	16


TD09							
CBA-BPC36Ka.1	BP IAR-N - Excavation	31-Mar-23	11-Apr-23	104	22-Feb-23 A	03-Jul-23	-209
CBA-BPC36Ka.2	BP IAR-N - RCD Drilling	12-Apr-23	22-Apr-23	37	20-May-23 A	05-Jul-23	-209
CBA-BPC36Ka.3	BP IAR-N - Airlift, Cage Install and Concrete	24-Apr-23	28-Apr-23	29	02-Jun-23 A	07-Jul-23	-209

KD06 (Section 2)

Bored Piles							
VD14							
09							
P24&P27-BP36.:	BP - Airlift, Cage Install and Concrete	03-Jun-23	12-Jun-23	10	30-May-23 A	10-Jun-23 A	
VD15							
07							
P24&P27-BP10.:	BP - Airlift, Cage Install and Concrete	06-May-23	15-May-23	12	24-May-23 A	08-Jun-23 A	
CD01							
08							
P23-BP15.30	BP - Airlift, Cage Install and Concrete	21-Jun-23	30-Jun-23	19	22-May-23 A	14-Jun-23 A	
CD03							
02							
P22&P19-BP13.:	BP - RCD Drilling	28-Sep-22	11-Nov-22	200	28-Sep-22 A	05-Jun-23 A	
P22&P19-BP13.:	BP - Airlift, Cage Install and Concrete	12-Nov-22	21-Nov-22	16	06-Jun-23 A	26-Jun-23 A	


KD07 (Section 3)

Bored Piles							
VD01							
07							
P26-BP07.10	BP - Excavation	28-Apr-23	05-May-23	6	03-Jul-23	08-Jul-23	-30
P26-BP07.20	BP - RCD Drilling	06-May-23	09-Jun-23	29	10-Jul-23	11-Aug-23	-30
P26-BP07.30	BP - Airlift, Cage Install and Concrete	10-Jun-23	19-Jun-23	8	12-Aug-23	21-Aug-23	-30
08							
P26-BP05.10	BP - Excavation	03-Jun-23	09-Jun-23	6	03-Jul-23	08-Jul-23	-30
P26-BP05.20	BP - RCD Drilling	10-Jun-23	15-Jul-23	29	10-Jul-23	11-Aug-23	-30
P26-BP05.30	BP - Airlift, Cage Install and Concrete	17-Jul-23	25-Jul-23	8	12-Aug-23	21-Aug-23	-30
VD02							
02							
P30-BP71.30	BP - Airlift, Cage Install and Concrete	25-Feb-23	07-Mar-23	19	10-May-23 A	02-Jun-23 A	
04							
P30-BP75.10	BP - Excavation	24-Mar-23	30-Mar-23	17	17-Jun-23 A	08-Jul-23	-30
P30-BP75.20	BP - RCD Drilling	31-Mar-23	09-May-23	29	10-Jul-23	11-Aug-23	-30
P30-BP75.30	BP - Airlift, Cage Install and Concrete	10-May-23	18-May-23	8	12-Aug-23	21-Aug-23	-30
05							
P30-BP74.10	BP - Excavation	23-Jun-22	09-May-23	294	23-Jun-22 A	20-Jun-23 A	
P30-BP74.20	BP - RCD Drilling	10-May-23	01-Jun-23	33	21-Jun-23 A	31-Jul-23	-30
P30-BP74.30	BP - Airlift, Cage Install and Concrete	02-Jun-23	10-Jun-23	8	01-Aug-23	09-Aug-23	-20

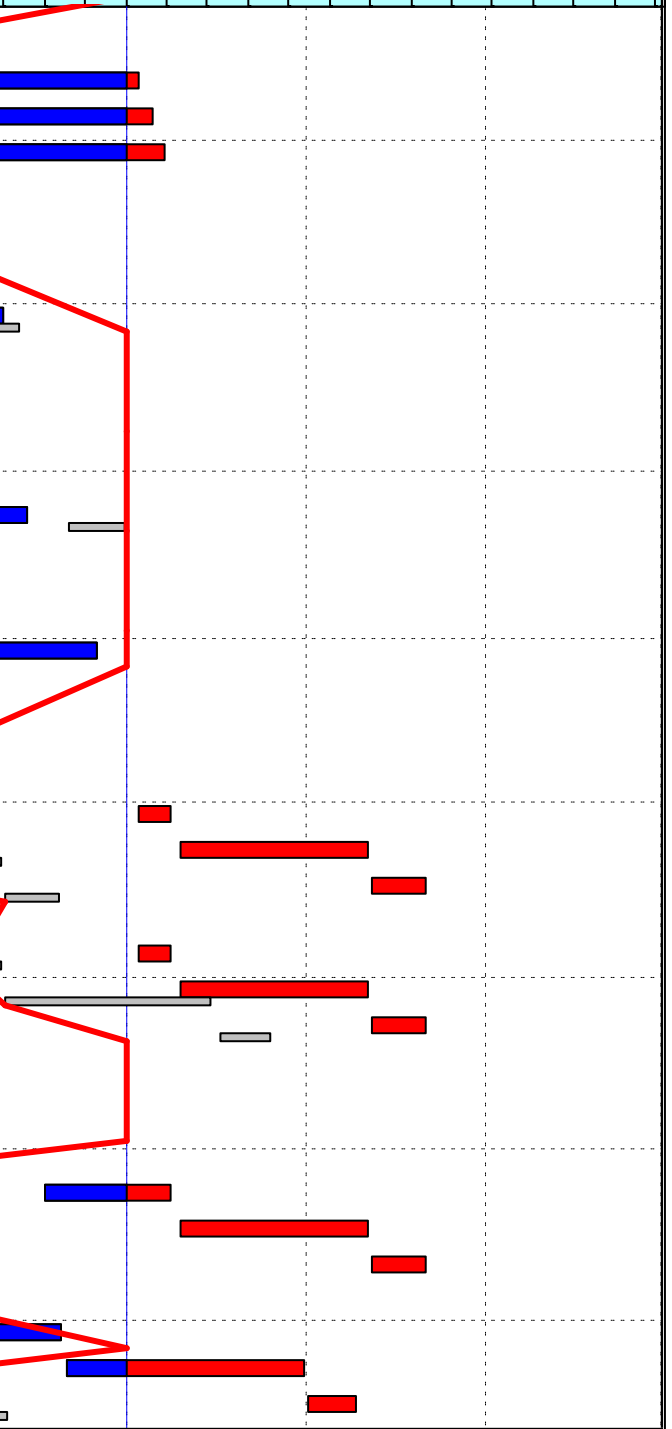

	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS

Date	Revision	Checked	Approved
04-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C

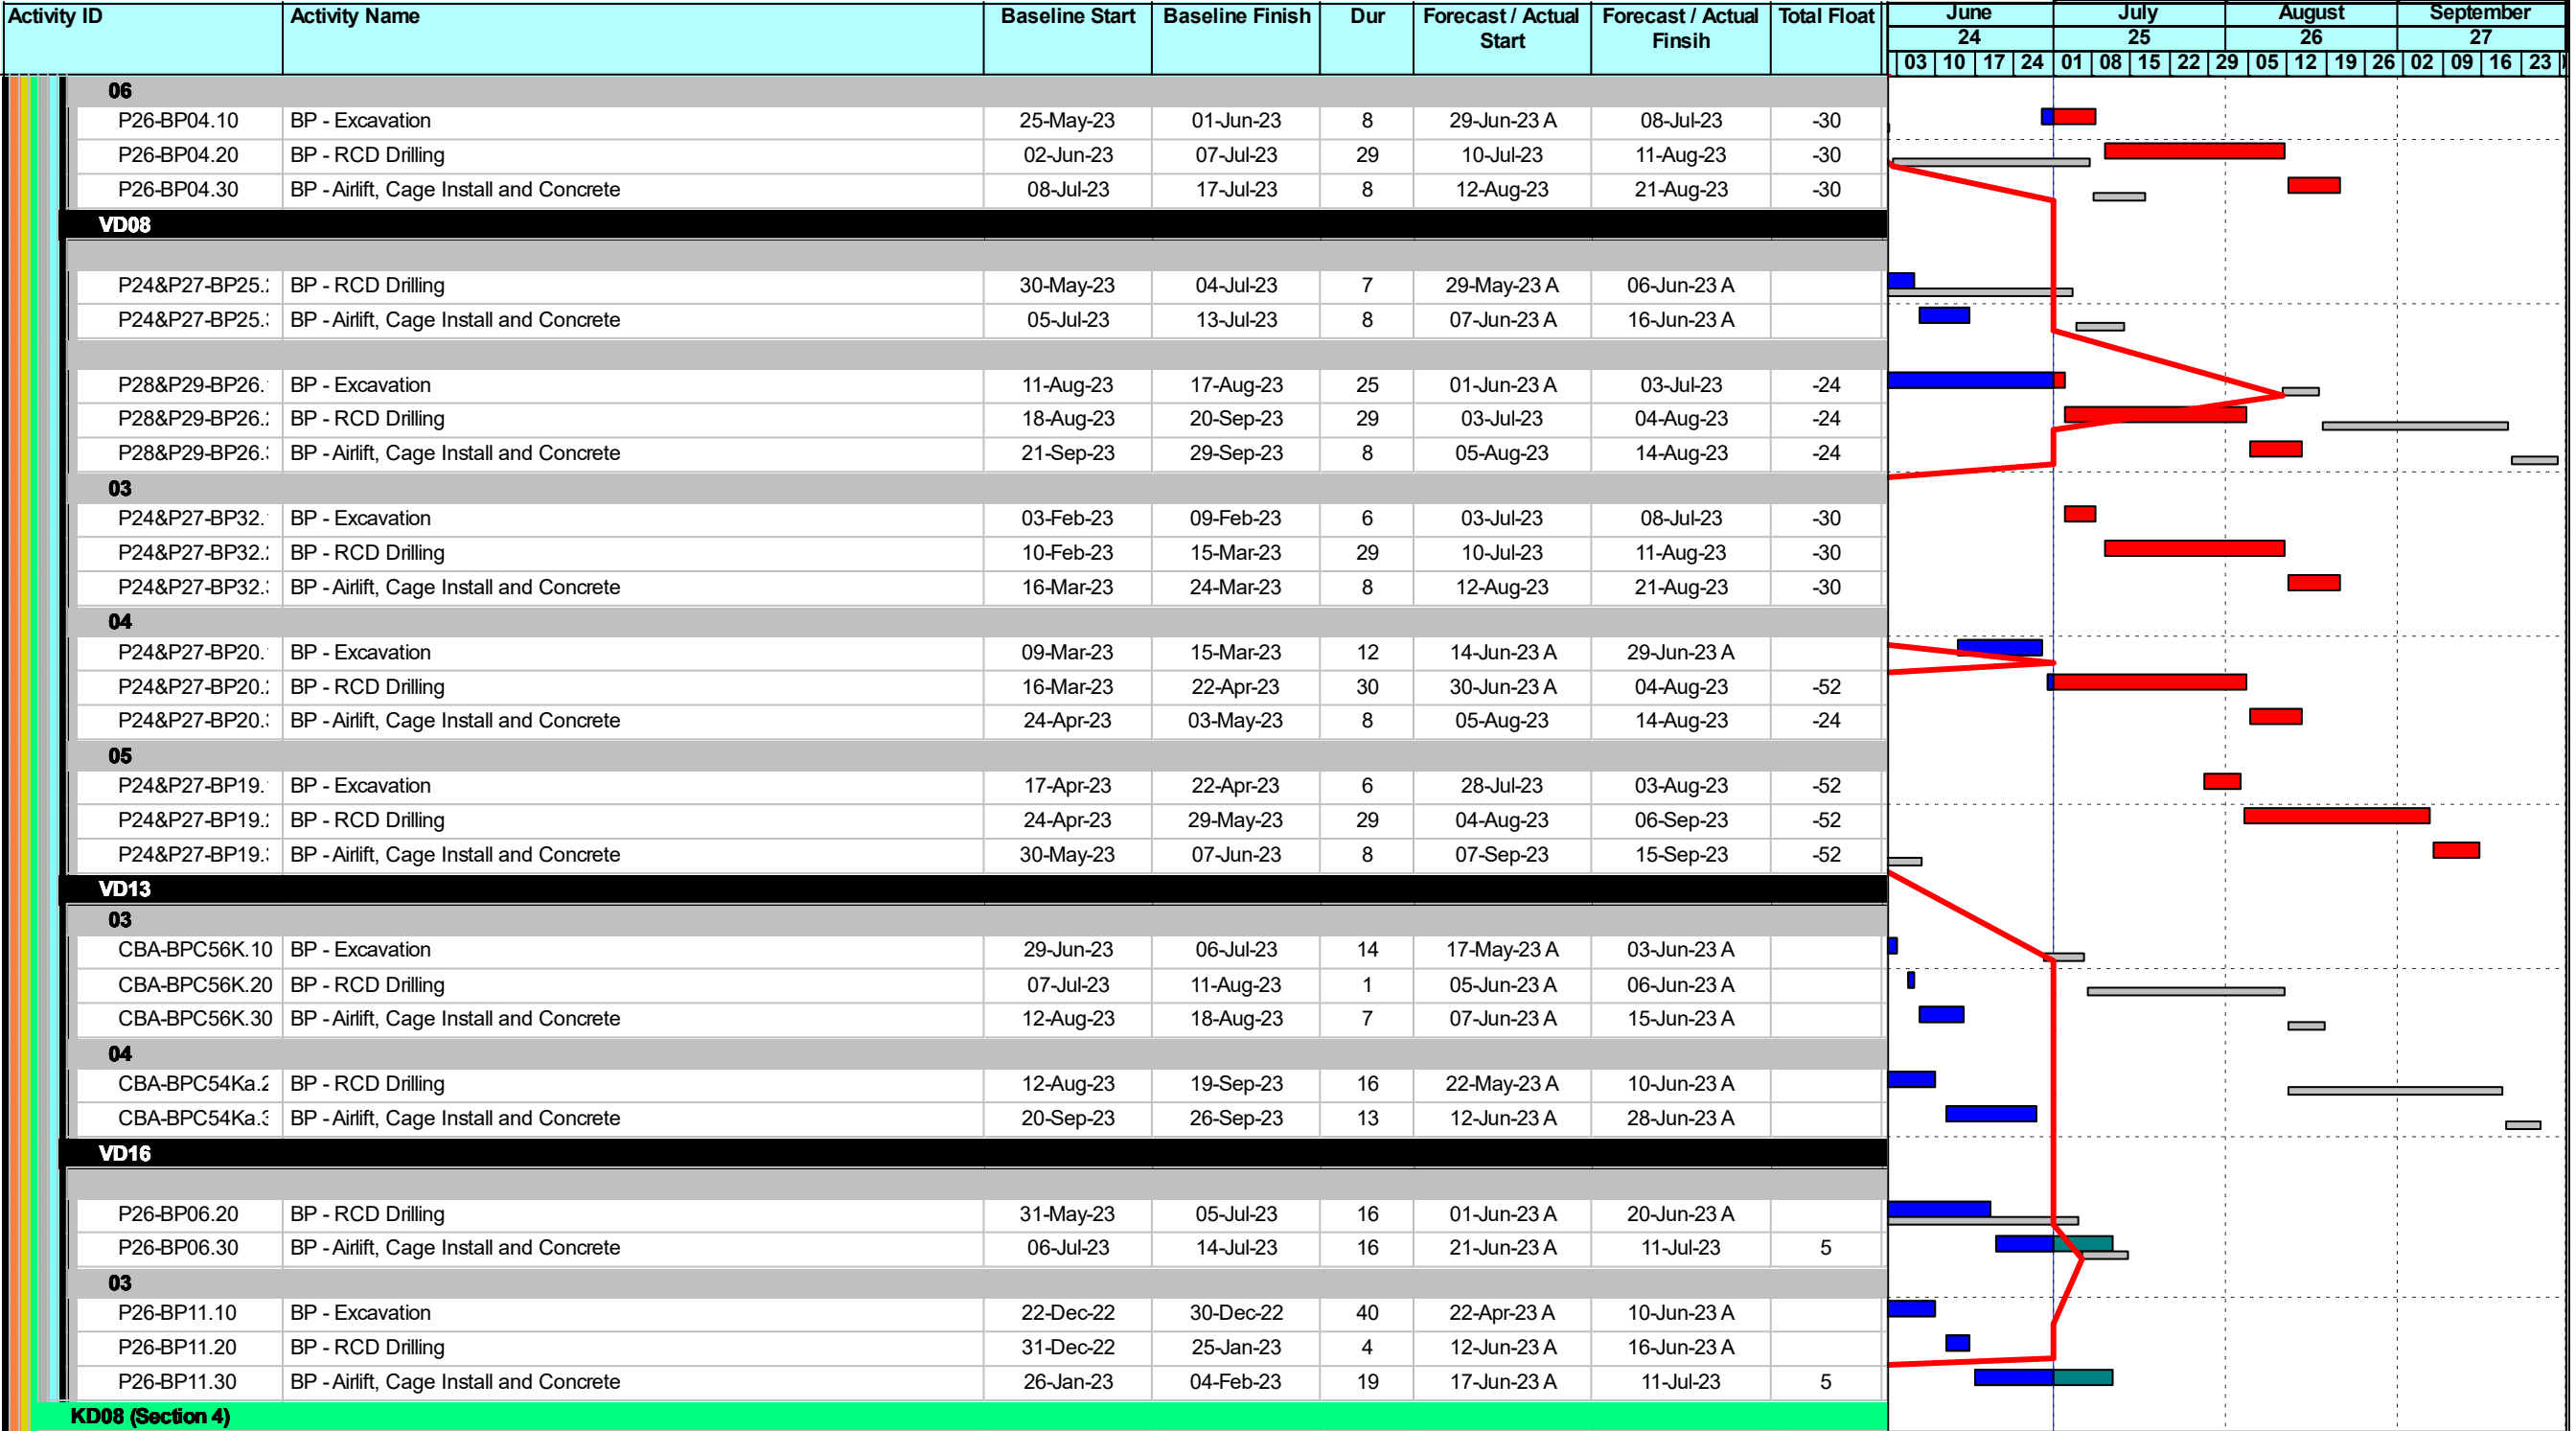

KD08 (Section 4)

	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS


	Date	Revision	Checked	Approved
	04-Mar-22	R0	KL	B
	02-Dec-22	R03D	KL	C

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	June				July				August				September			
								24				25				26				27			
								03	10	17	24	01	08	15	22	29	05	12	19	26	02	09	16

Bored Piles							
VD03							
04							
P30-BP46.10	BP - Excavation	13-Jan-23	19-Jan-23	22	05-May-23 A	01-Jun-23 A	
P30-BP46.20	BP - RCD Drilling	20-Jan-23	09-Feb-23	7	02-Jun-23 A	10-Jun-23 A	
P30-BP46.30	BP - Airlift, Cage Install and Concrete	10-Feb-23	17-Feb-23	6	12-Jun-23 A	19-Jun-23 A	
05							
P30-BP47.10	BP - Excavation	03-Feb-23	09-Feb-23	19	13-May-23 A	06-Jun-23 A	
P30-BP47.20	BP - RCD Drilling	10-Feb-23	27-Feb-23	4	07-Jun-23 A	12-Jun-23 A	
P30-BP47.30	BP - Airlift, Cage Install and Concrete	28-Feb-23	07-Mar-23	7	13-Jun-23 A	21-Jun-23 A	
08							
P30-BP49.10	BP - Excavation	28-Mar-23	03-Apr-23	11	27-May-23 A	09-Jun-23 A	
P30-BP49.20	BP - RCD Drilling	04-Apr-23	29-Apr-23	5	10-Jun-23 A	16-Jun-23 A	
P30-BP49.30	BP - Airlift, Cage Install and Concrete	02-May-23	10-May-23	7	17-Jun-23 A	27-Jun-23 A	
VD04							
07							
P30-BP35.30	BP - Airlift, Cage Install and Concrete	15-Apr-23	22-Apr-23	9	25-May-23 A	06-Jun-23 A	
VD05							
P30-BP50.30	BP - Airlift, Cage Install and Concrete	08-May-23	16-May-23	12	30-May-23 A	13-Jun-23 A	
05							
P30-BP43.10	BP - Excavation	12-Jan-23	18-Jan-23	18	18-May-23 A	09-Jun-23 A	
P30-BP43.20	BP - RCD Drilling	19-Jan-23	13-Feb-23	4	10-Jun-23 A	15-Jun-23 A	
P30-BP43.30	BP - Airlift, Cage Install and Concrete	14-Feb-23	22-Feb-23	6	16-Jun-23 A	24-Jun-23 A	

KD09 (Section 5)

Bored Piles							
CD01							
03							
P23-BP35.30	BP - Airlift, Cage Install and Concrete	31-Jan-23	08-Feb-23	12	25-May-23 A	09-Jun-23 A	
CD02							
09							
P23-BP36.10	BP - Excavation	04-Apr-23	14-Apr-23	21	12-May-23 A	07-Jun-23 A	
P23-BP36.20	BP - RCD Drilling	15-Apr-23	19-May-23	7	08-Jun-23 A	16-Jun-23 A	
P23-BP36.30	BP - Airlift, Cage Install and Concrete	20-May-23	30-May-23	19	17-Jun-23 A	11-Jul-23	-81
TD01							
02							
P18-BP57.10	BP - Excavation	22-Dec-22	30-Dec-22	6	03-Jul-23	08-Jul-23	-106
P18-BP57.20	BP - RCD Drilling	31-Dec-22	25-Jan-23	19	10-Jul-23	31-Jul-23	-106
P18-BP57.30	BP - Airlift, Cage Install and Concrete	26-Jan-23	04-Feb-23	8	01-Aug-23	09-Aug-23	-106
04							
P18-BP62.10	BP - Excavation	11-Feb-23	17-Feb-23	6	03-Jul-23	08-Jul-23	-116

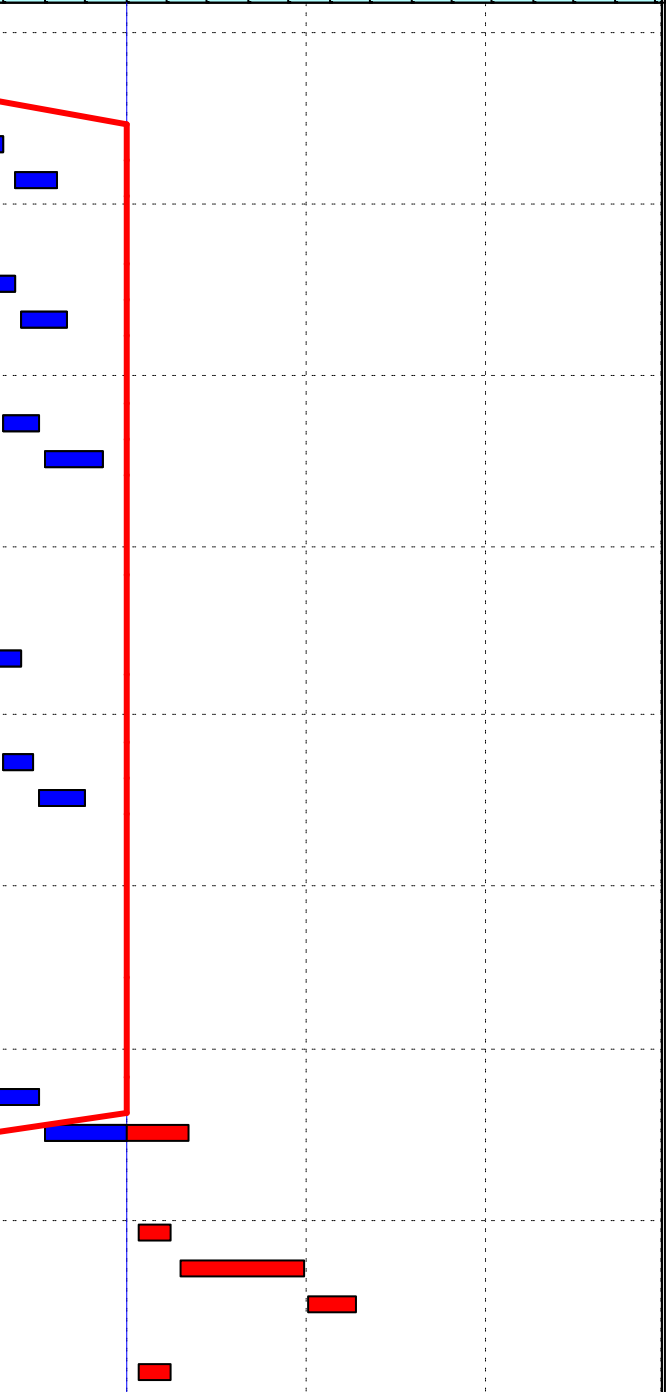

Planned	Planned MS
Critical	Critical MS
Actual	Actual MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 30 June 2023
 Based on CMWP Rev.0 (3rd Draft)

Date	Revision	Checked	Approved
04-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C


Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	June				July				August				September			
								24				25				26				27			
								03	10	17	24	01	08	15	22	29	05	12	19	26	02	09	16
P18-BP62.20	BP - RCD Drilling	18-Feb-23	11-Mar-23	19	10-Jul-23	31-Jul-23	-116																
P18-BP62.30	BP - Airlift, Cage Install and Concrete	13-Mar-23	21-Mar-23	8	01-Aug-23	09-Aug-23	-106																
06																							
P18-BP45.10	BP - Excavation	28-Mar-23	03-Apr-23	6	03-Jul-23	08-Jul-23	-116																
P18-BP45.20	BP - RCD Drilling	04-Apr-23	29-Apr-23	19	10-Jul-23	31-Jul-23	-116																
P18-BP45.30	BP - Airlift, Cage Install and Concrete	02-May-23	10-May-23	8	01-Aug-23	09-Aug-23	-106																
07																							
P18-BP52.10	BP - Excavation	24-Apr-23	29-Apr-23	12	30-May-23 A	13-Jun-23 A																	
P18-BP52.20	BP - RCD Drilling	02-May-23	23-May-23	8	14-Jun-23 A	24-Jun-23 A																	
P18-BP52.30	BP - Airlift, Cage Install and Concrete	24-May-23	02-Jun-23	19	26-Jun-23 A	18-Jul-23	-87																
08																							
P18-BP40.10	BP - Excavation	17-May-23	23-May-23	15	20-Jun-23 A	08-Jul-23	-116																
P18-BP40.20	BP - RCD Drilling	24-May-23	10-Jun-23	15	10-Jul-23	26-Jul-23	-116																
P18-BP40.30	BP - Airlift, Cage Install and Concrete	12-Jun-23	19-Jun-23	7	27-Jul-23	03-Aug-23	-101																
09																							
P18-BP51.10	BP - Excavation	05-Jun-23	10-Jun-23	20	06-Jun-23 A	30-Jun-23 A																	
P18-BP51.20	BP - RCD Drilling	12-Jun-23	05-Jul-23	19	03-Jul-23 A	24-Jul-23	-114																
P18-BP51.30	BP - Airlift, Cage Install and Concrete	06-Jul-23	14-Jul-23	8	25-Jul-23	02-Aug-23	-100																
10																							
P18-BP46.10	BP - Excavation	28-Jun-23	05-Jul-23	6	20-Jul-23	26-Jul-23	-116																
P18-BP46.20	BP - RCD Drilling	06-Jul-23	22-Jul-23	15	27-Jul-23	12-Aug-23	-116																
P18-BP46.30	BP - Airlift, Cage Install and Concrete	24-Jul-23	31-Jul-23	7	14-Aug-23	21-Aug-23	-116																
TD02																							
05																							
P23-BP82.10	BP - Excavation	07-Dec-22	13-Dec-22	52	06-May-23 A	08-Jul-23	-116																
P23-BP82.20	BP - RCD Drilling	14-Dec-22	19-Jan-23	63	29-May-23 A	11-Aug-23	-116																
P23-BP82.30	BP - Airlift, Cage Install and Concrete	20-Jan-23	01-Feb-23	8	12-Aug-23	21-Aug-23	-116																
TD03																							
05																							
P23-BP79.30	BP - Airlift, Cage Install and Concrete	02-Mar-23	10-Mar-23	5	29-May-23 A	03-Jun-23 A																	
06																							
P23-BP65.20	BP - RCD Drilling	02-Mar-23	23-Mar-23	5	25-May-23 A	01-Jun-23 A																	
P23-BP65.30	BP - Airlift, Cage Install and Concrete	24-Mar-23	01-Apr-23	8	02-Jun-23 A	12-Jun-23 A																	
07																							
P23-BP78.10	BP - Excavation	17-Mar-23	23-Mar-23	15	02-Jun-23 A	20-Jun-23 A																	
P23-BP78.20	BP - RCD Drilling	24-Mar-23	19-Apr-23	27	21-Jun-23 A	24-Jul-23	-100																
P23-BP78.30	BP - Airlift, Cage Install and Concrete	20-Apr-23	28-Apr-23	8	25-Jul-23	02-Aug-23	-100																
08																							
P23-BP98.20	BP - RCD Drilling	20-Apr-23	12-May-23	6	31-May-23 A	07-Jun-23 A																	
P23-BP98.30	BP - Airlift, Cage Install and Concrete	13-May-23	22-May-23	7	08-Jun-23 A	16-Jun-23 A																	
09																							







ID: 2BC-20230630_bw
 Data Date: 01-Jul-23
 Print Date: 03-Jul-23_14:17
 Page 5 of 9

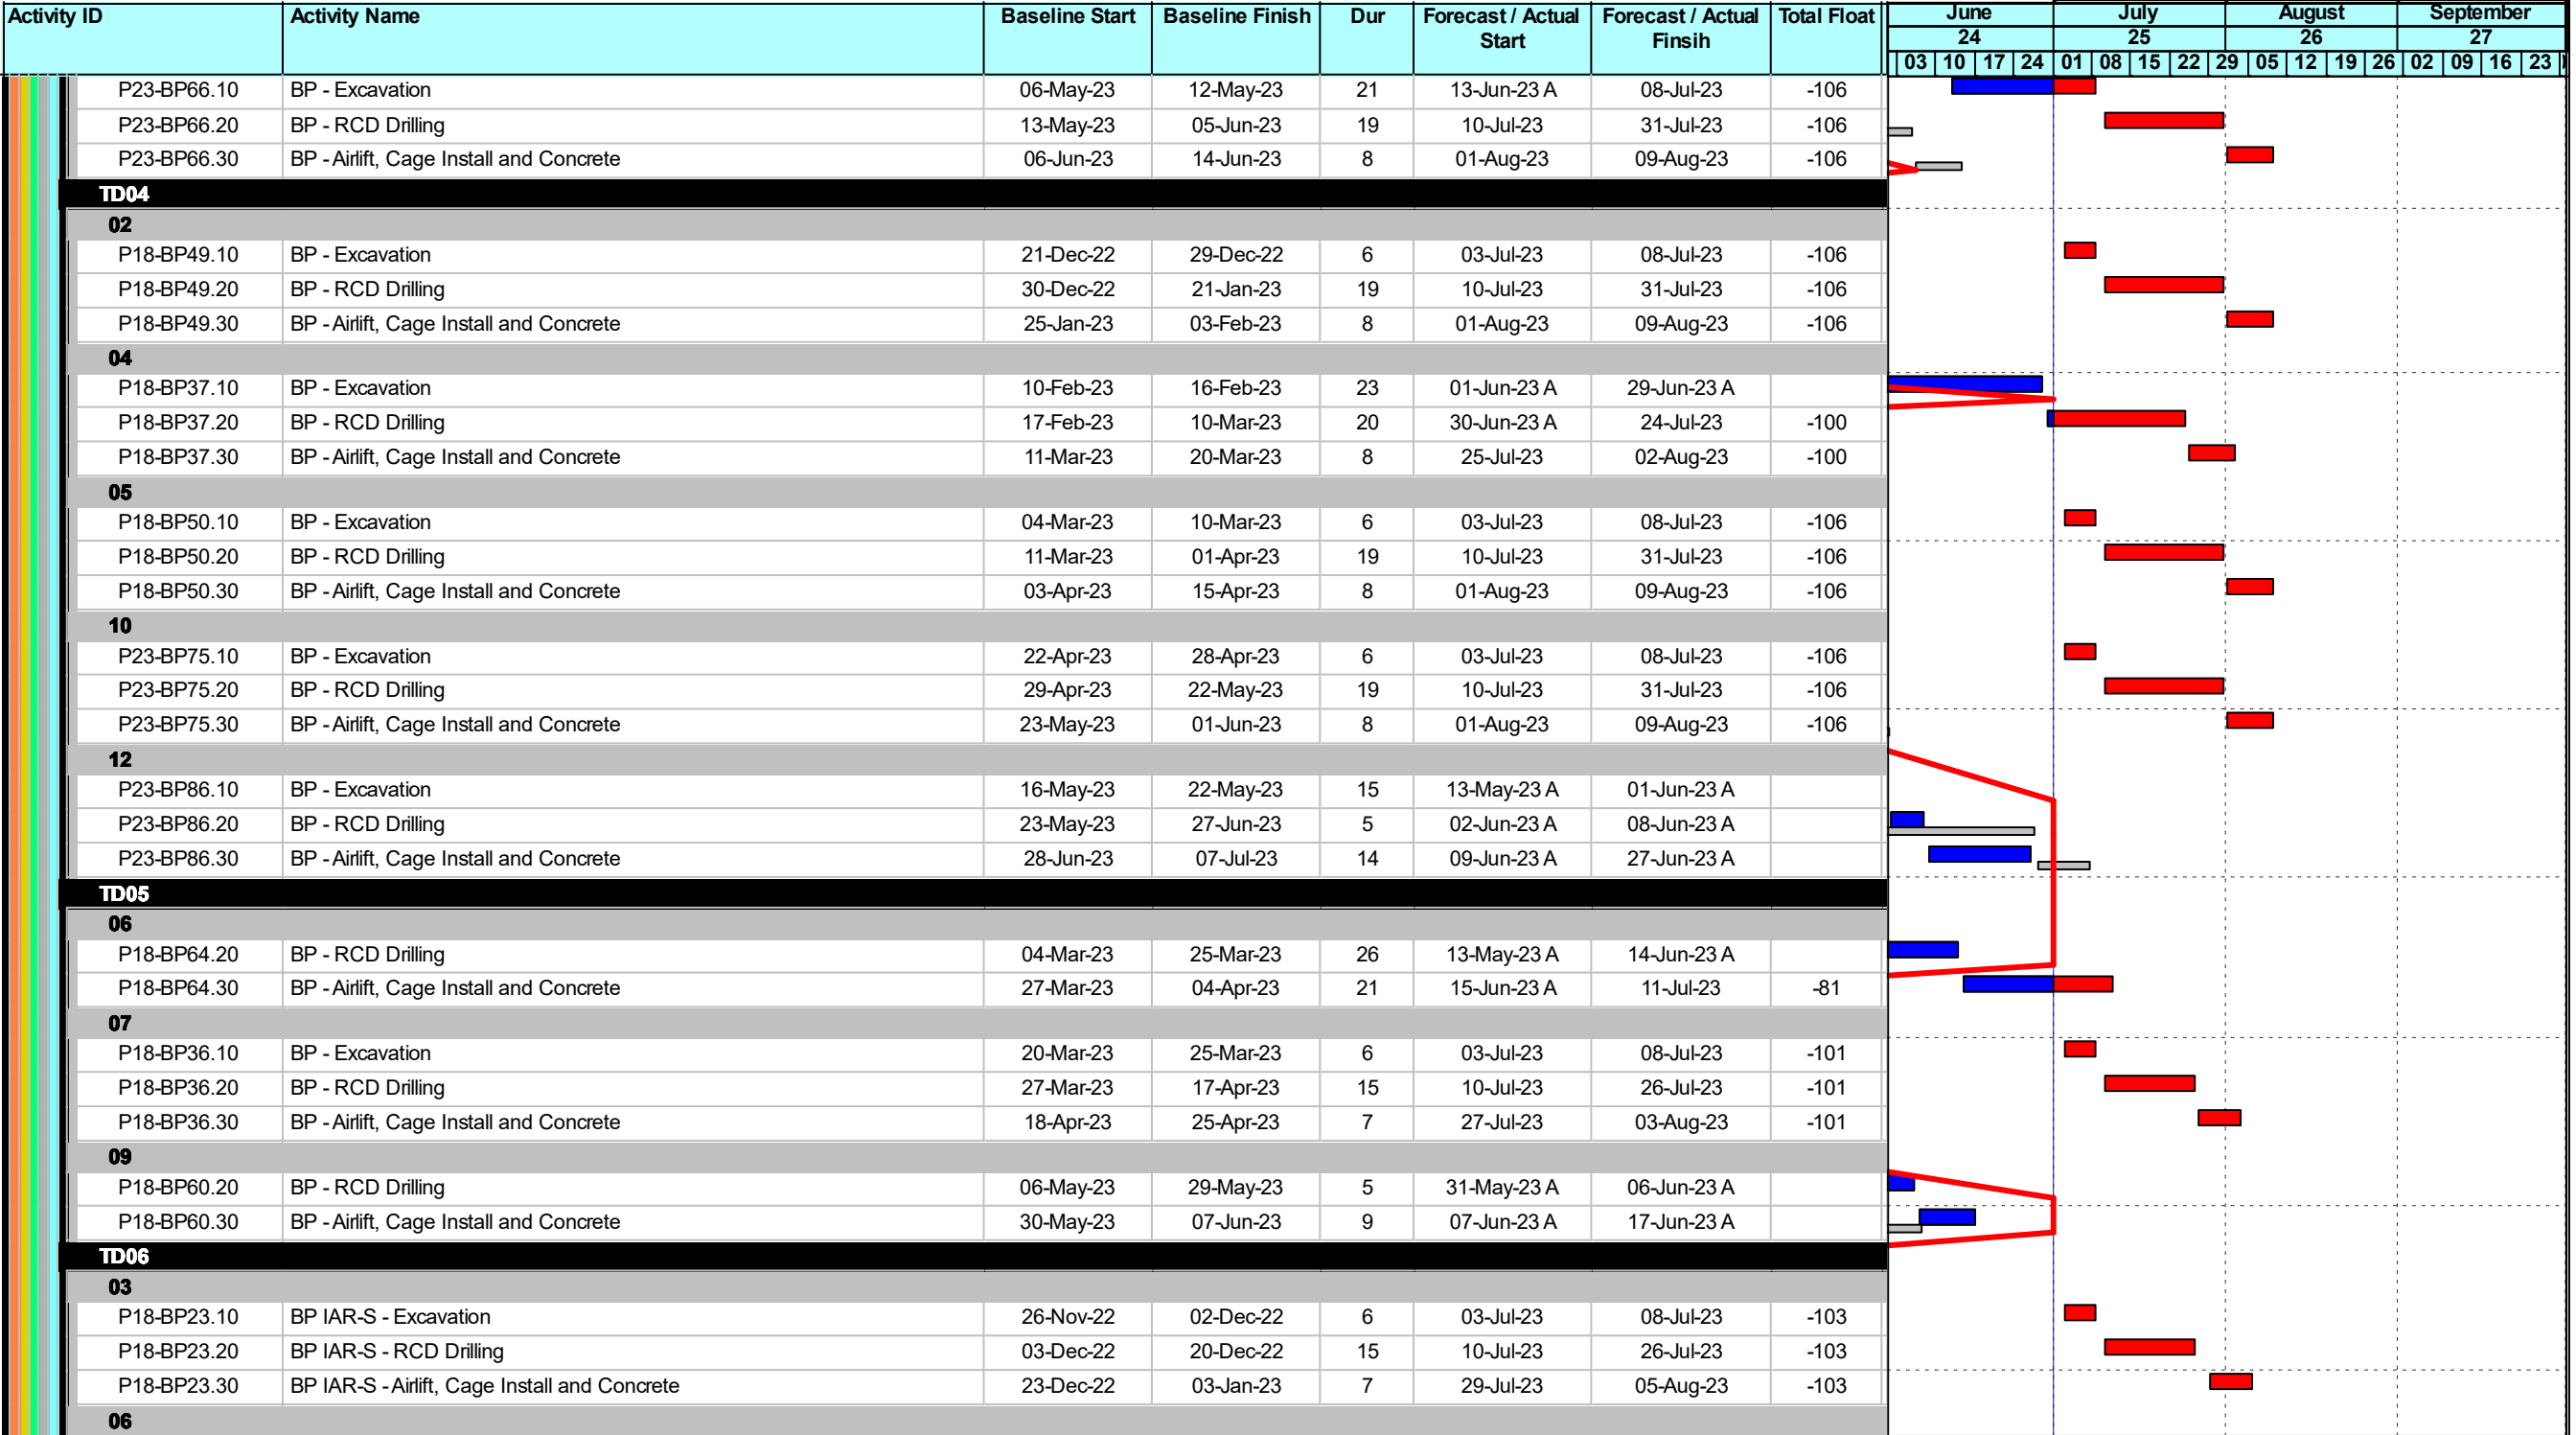 Planned	 Actual	 Planned MS	 Actual MS
 Critical		 Critical MS	


West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 30 June 2023
Based on CMWP Rev.0 (3rd Draft)


Date	Revision	Checked	Approved
04-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C



 Planned	 Planned MS
 Critical	 Critical MS
 Actual	 Actual MS


		Date	Revision	Checked	Approved
		04-Mar-22	R0	KL	B
		02-Dec-22	R03D	KL	C

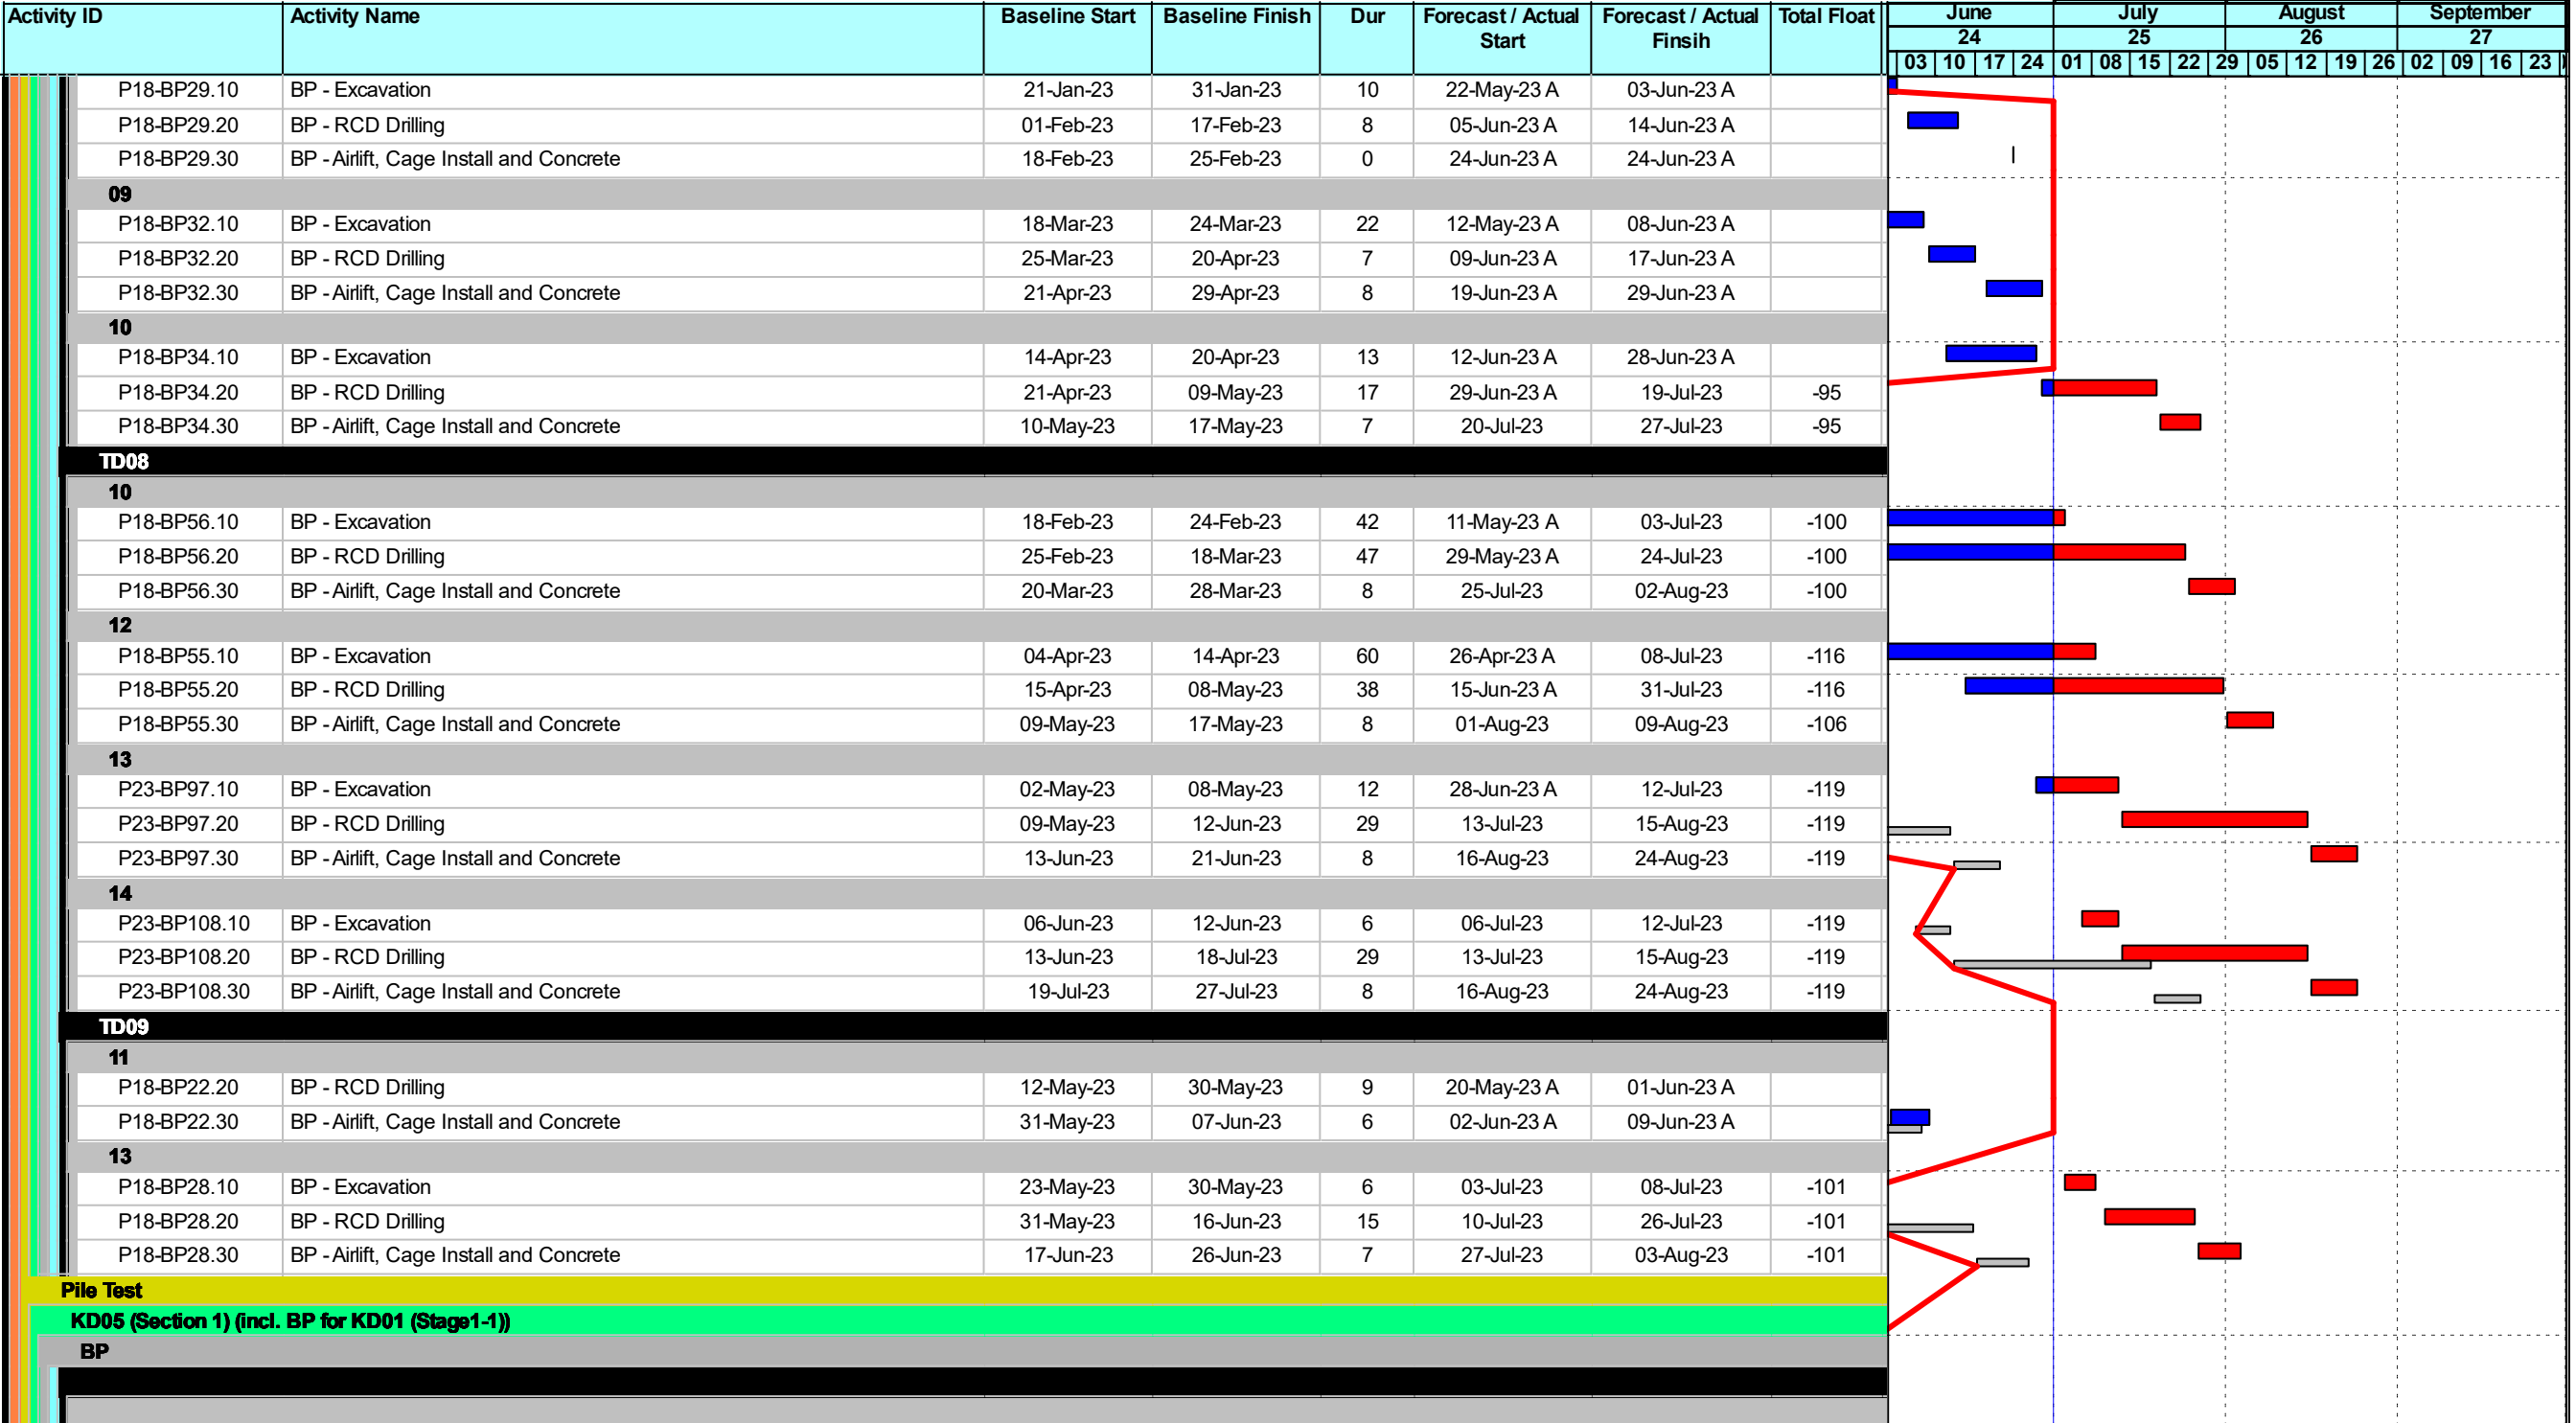

	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 30 June 2023
 Based on CMWP Rev.0 (3rd Draft)

	Date	Revision	Checked	Approved
	04-Mar-22	R0	KL	B
	02-Dec-22	R03D	KL	C

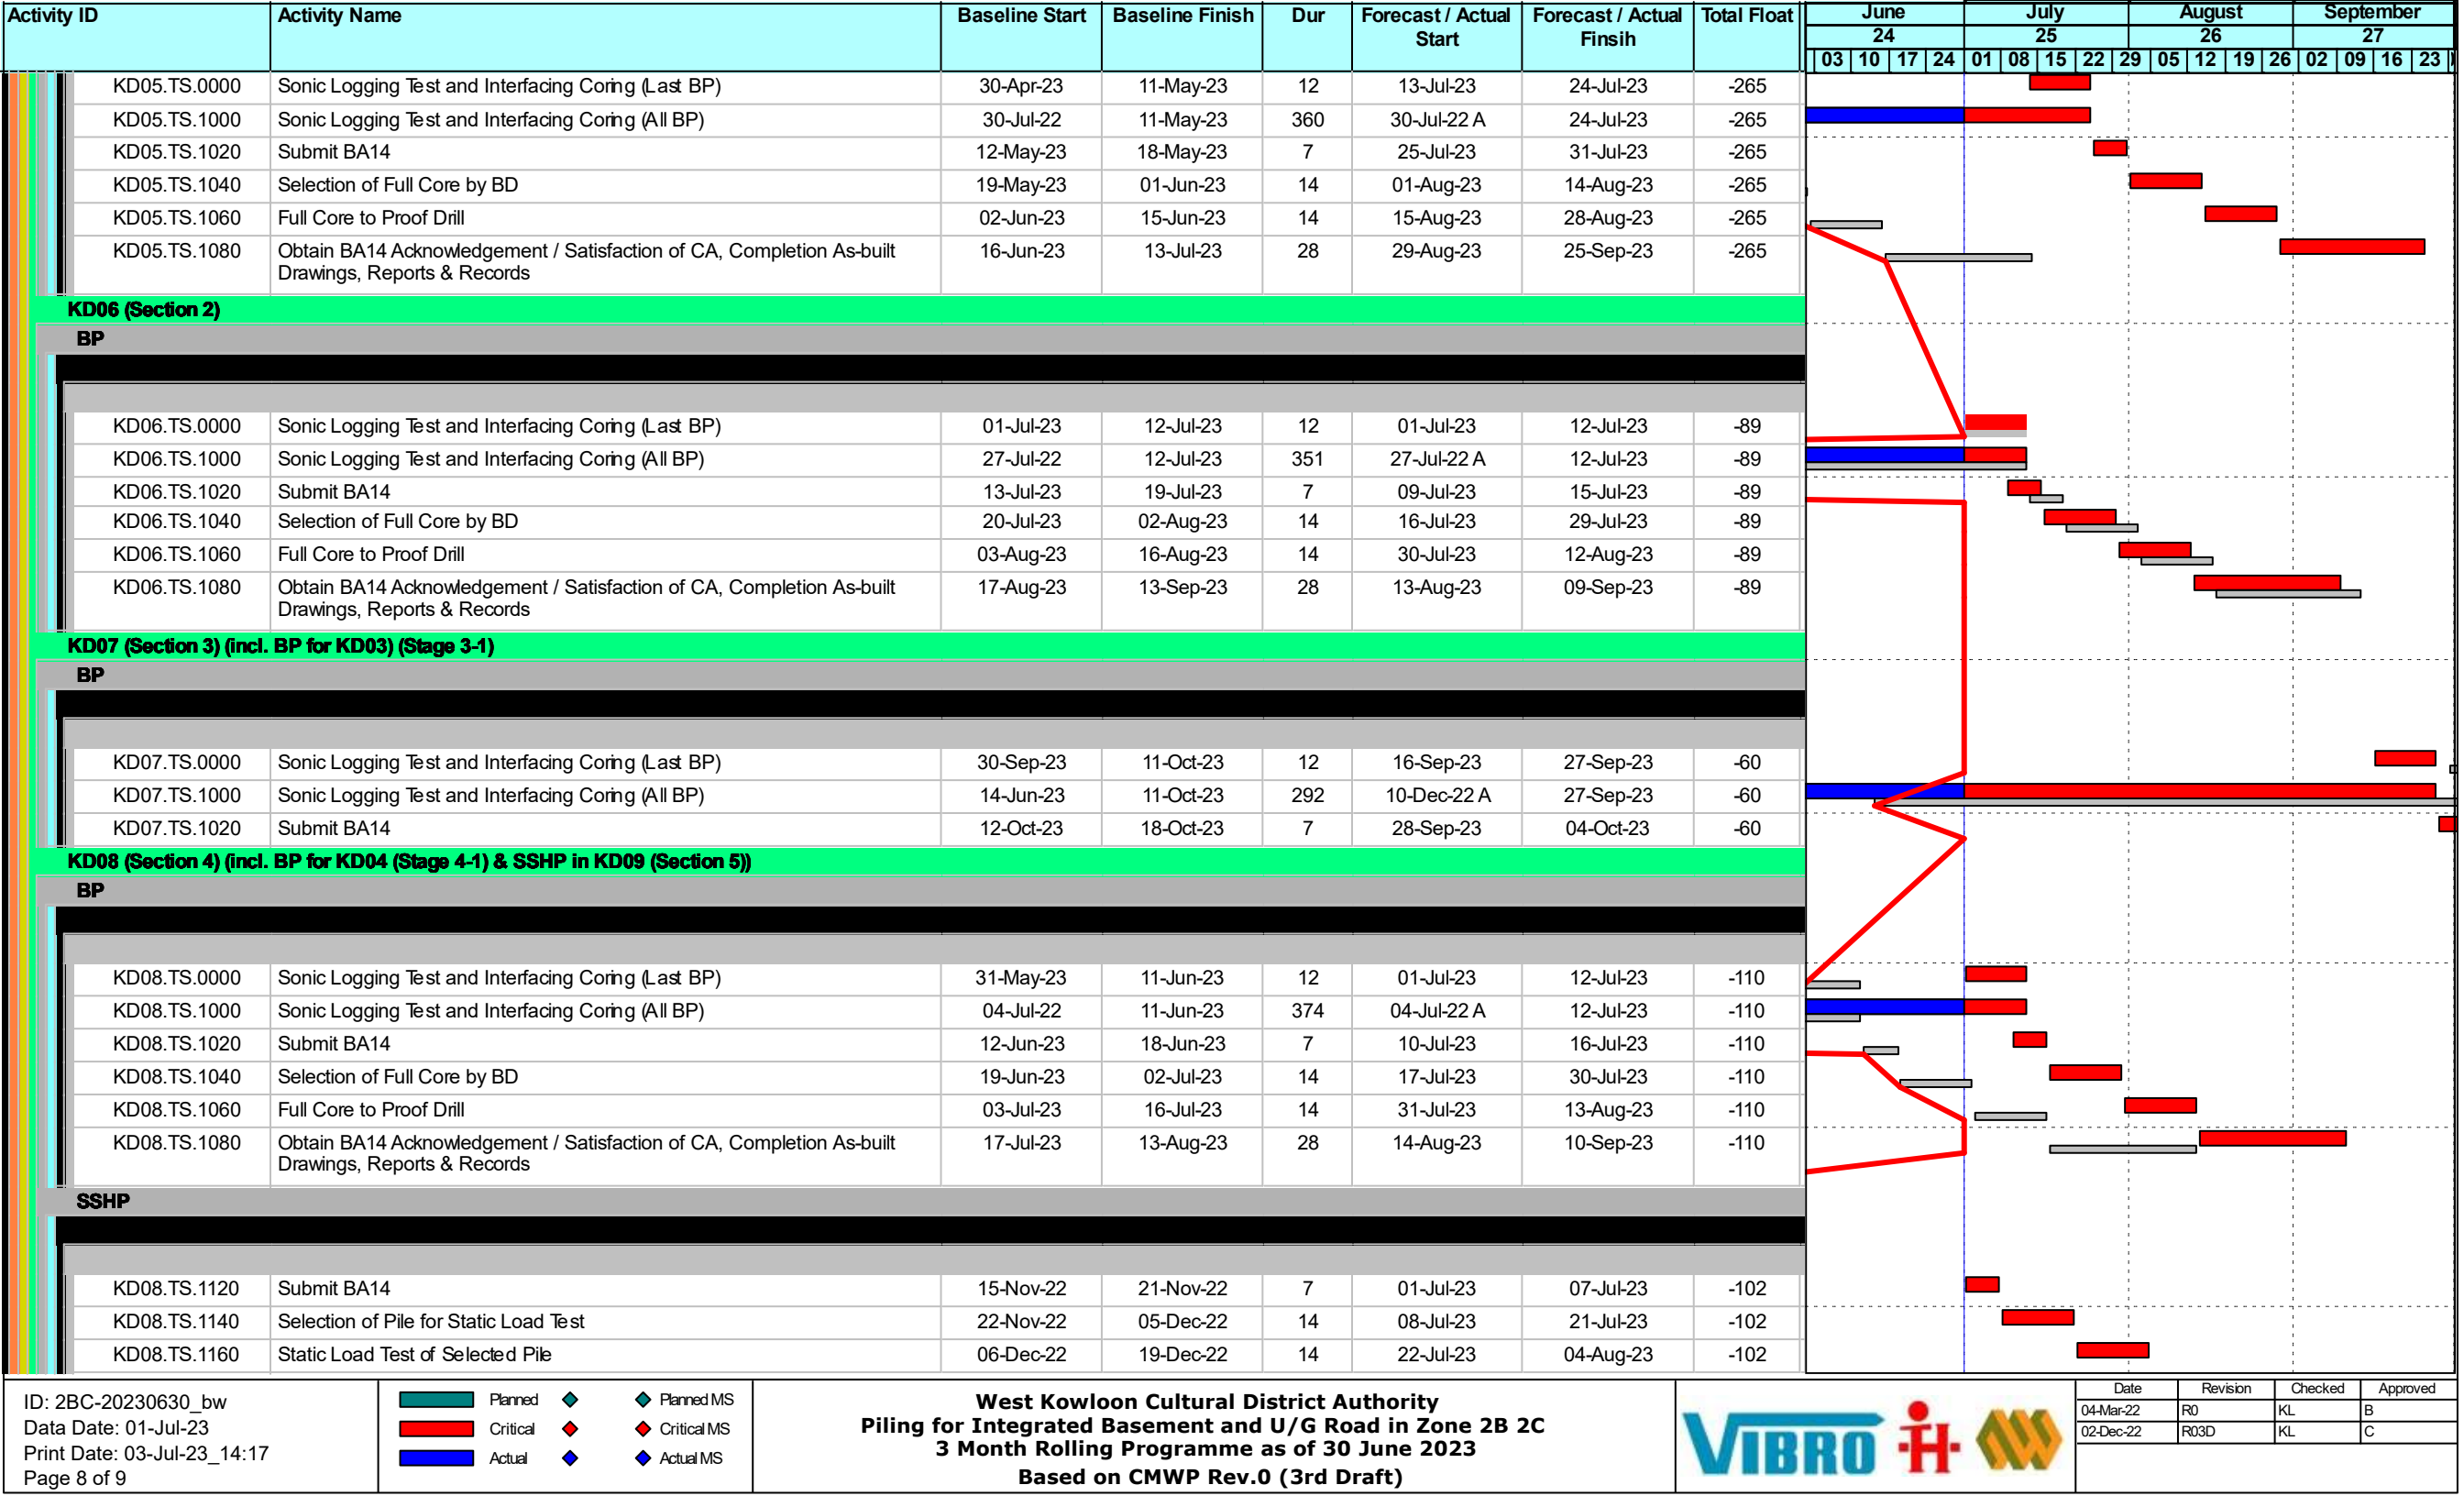

	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS


		Date	Revision	Checked	Approved
		04-Mar-22	R0	KL	B
		02-Dec-22	R03D	KL	C

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	June				July				August				September			
								24				25				26				27			
								03	10	17	24	01	08	15	22	29	05	12	19	26	02	09	16
KD08.TS.1180	Obtain BA14 Acknowledgement / Satisfaction of CA, Completion As-built Drawings, Reports & Records	20-Dec-22	16-Jan-23	28	05-Aug-23	01-Sep-23	-102																
KD09 (Section 5) (incl. BP for KD02 (Stage 5-1))																							
BP																							
KD09.TS.0000	Sonic Logging Test and Interfacing Coring (Last BP)	01-Aug-23	12-Aug-23	12	25-Aug-23	05-Sep-23	-148																
KD09.TS.1000	Sonic Logging Test and Interfacing Coring (All BP)	23-May-22	12-Aug-23	471	23-May-22 A	05-Sep-23	-148																
KD09.TS.1020	Submit BA14	13-Aug-23	19-Aug-23	7	06-Sep-23	12-Sep-23	-148																
KD09.TS.1040	Selection of Full Core by BD	20-Aug-23	02-Sep-23	14	13-Sep-23	26-Sep-23	-148																
KD09.TS.1060	Full Core to Proof Drill	03-Sep-23	16-Sep-23	14	27-Sep-23	10-Oct-23	-148																
Attendance to Other Project Contractors (optional works item no. 2A to 2E)																							
S2.AT.0000	Attendance at Section 2 Area (optional works item no. 2B) (Duration TBC)	13-May-23	01-Jun-23	20	01-Jul-23	20-Jul-23	-38																
S3.AT.0000	Attendance at Section 3 Area (optional works item no. 2C) (Duration TBC)	02-Jul-23	21-Jul-23	20	02-Jul-23	21-Jul-23	71																

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	July				August				September				October			
								25				26				27				28			
								01	08	15	22	29	05	12	19	26	02	09	16	23	30	07	14

Piling for Integrated Basement and U/G Road in Zone 2B & 2C


Contract Dates								
Key Dates								
KD for Zone 2B								
KD05	KD05 (Section 1) - 03 Jan 2023			13-Jul-23	0		25-Sep-23*	-265
KD06	KD06 (Section 2) - 12 Jun 2023			13-Sep-23	0		06-Sep-23*	-86
KD for Zone 2C								
KD08	KD08 (Section 4) - 23 May 2023			13-Aug-23	0		13-Sep-23*	-113
Optional Works subjected to CA's Instruction								
CO2C	Last CAI date for Optional Works Item No.2C (330 Days to 710 Days after Commencement)		02-Jul-23		0	02-Jul-23 A		
Construction Stage								
Pile Construction								
KD05 (Section 1)								
Bored Piles - Drainage Diversion								
CD08								
P17-BP18.30	BP IAR-N - Airlift, Cage Install and Concrete		22-Apr-23	29-Apr-23	0	10-Jul-23 A	10-Jul-23 A	
P17-BP20.30	BP - Airlift, Cage Install and Concrete (Rev. to P17-BP20A)		14-Mar-23	21-Mar-23	10	29-Jun-23 A	12-Jul-23 A	
Bored Piles								
TD07								
09								
P18-BP07.30	BP IAR-S - Airlift, Cage Install and Concrete		06-Apr-23	17-Apr-23	14	13-Jun-23 A	30-Jun-23 A	
KD07 (Section 3)								
Bored Piles								
VD01								
P26-BP07.10	BP - Excavation		28-Apr-23	05-May-23	20	06-Jul-23 A	29-Jul-23	-47
P26-BP07.20	BP - RCD Drilling		06-May-23	09-Jun-23	29	29-Jul-23	31-Aug-23	-47
P26-BP07.30	BP - Airlift, Cage Install and Concrete		10-Jun-23	19-Jun-23	8	01-Sep-23	09-Sep-23	-47
08								
P26-BP05.10	BP - Excavation		03-Jun-23	09-Jun-23	21	11-Jul-23 A	03-Aug-23	-52
P26-BP05.20	BP - RCD Drilling		10-Jun-23	15-Jul-23	29	04-Aug-23	06-Sep-23	-52
P26-BP05.30	BP - Airlift, Cage Install and Concrete		17-Jul-23	25-Jul-23	8	07-Sep-23	15-Sep-23	-52
VD02								

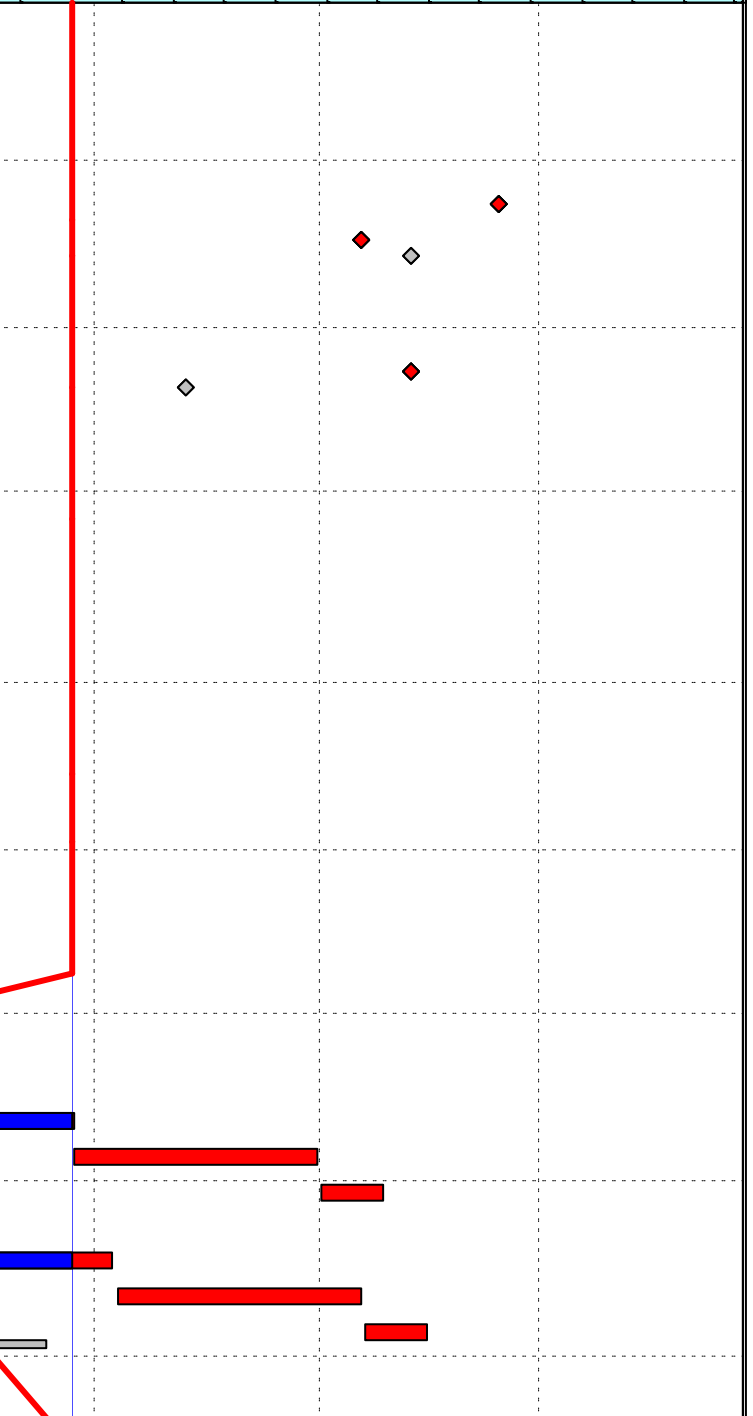





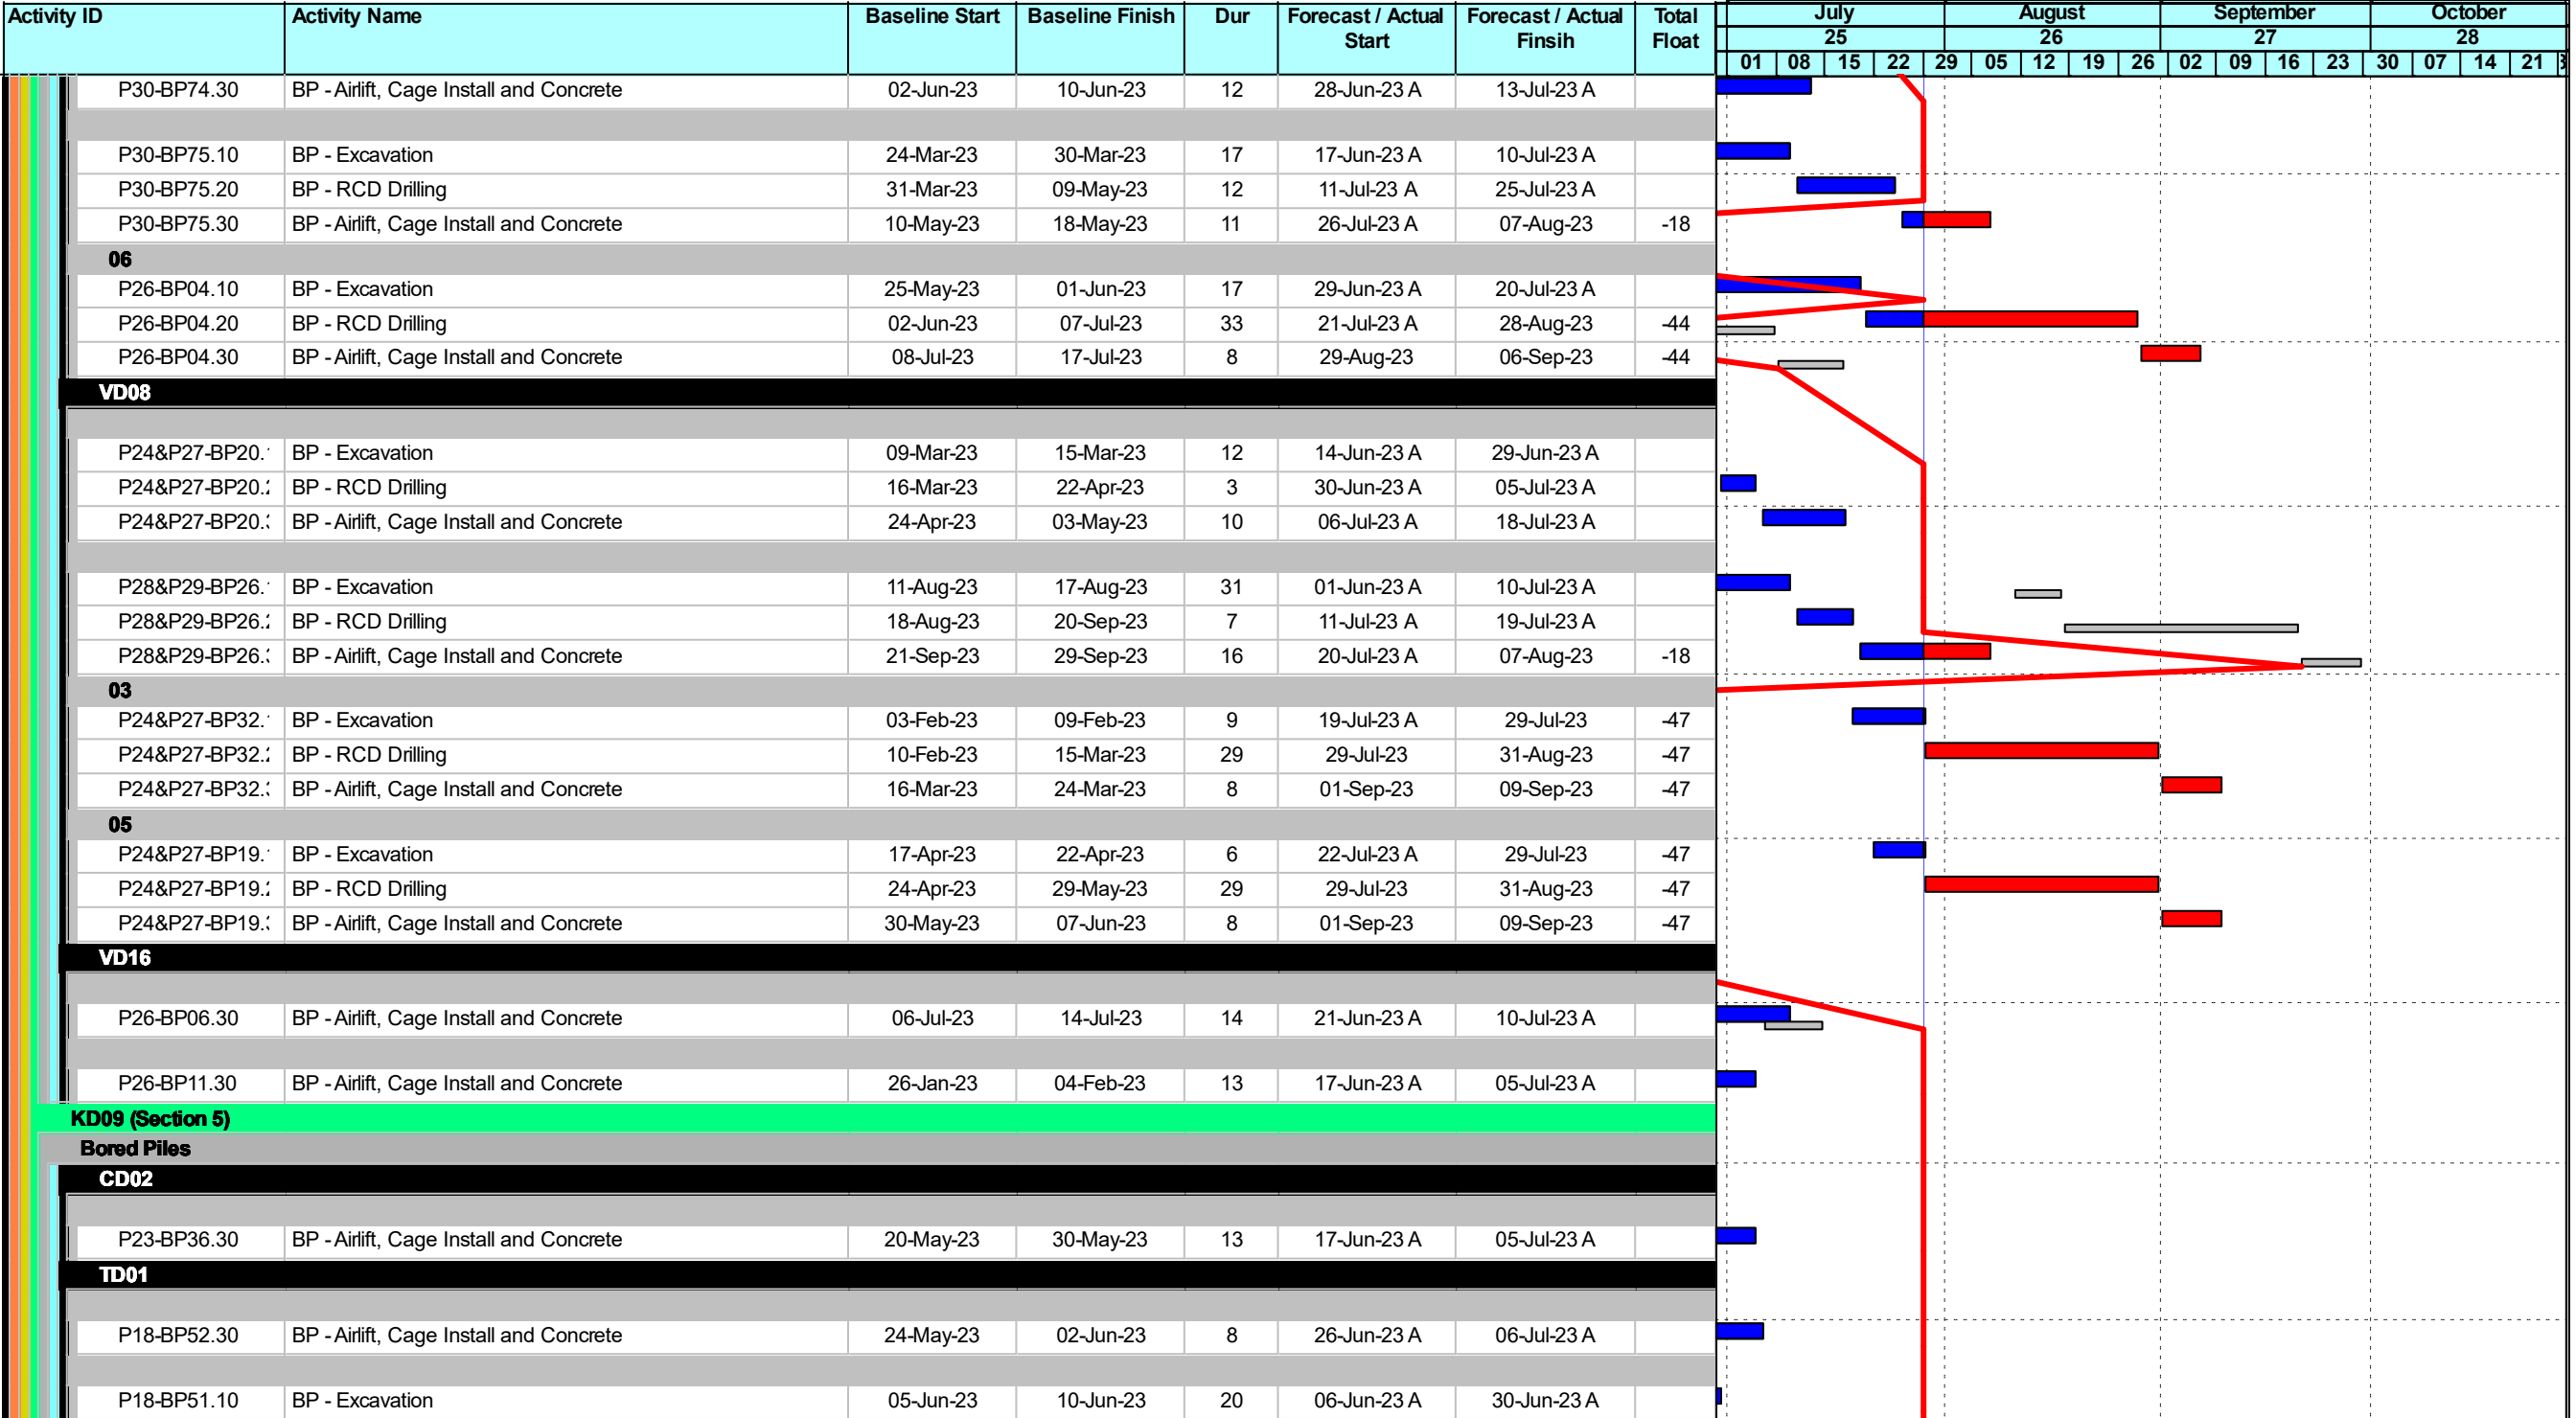

	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS



Date	Revision	Checked	Approved
04-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C










	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 28 July 2023
Based on CMWP Rev.0 (3rd Draft)

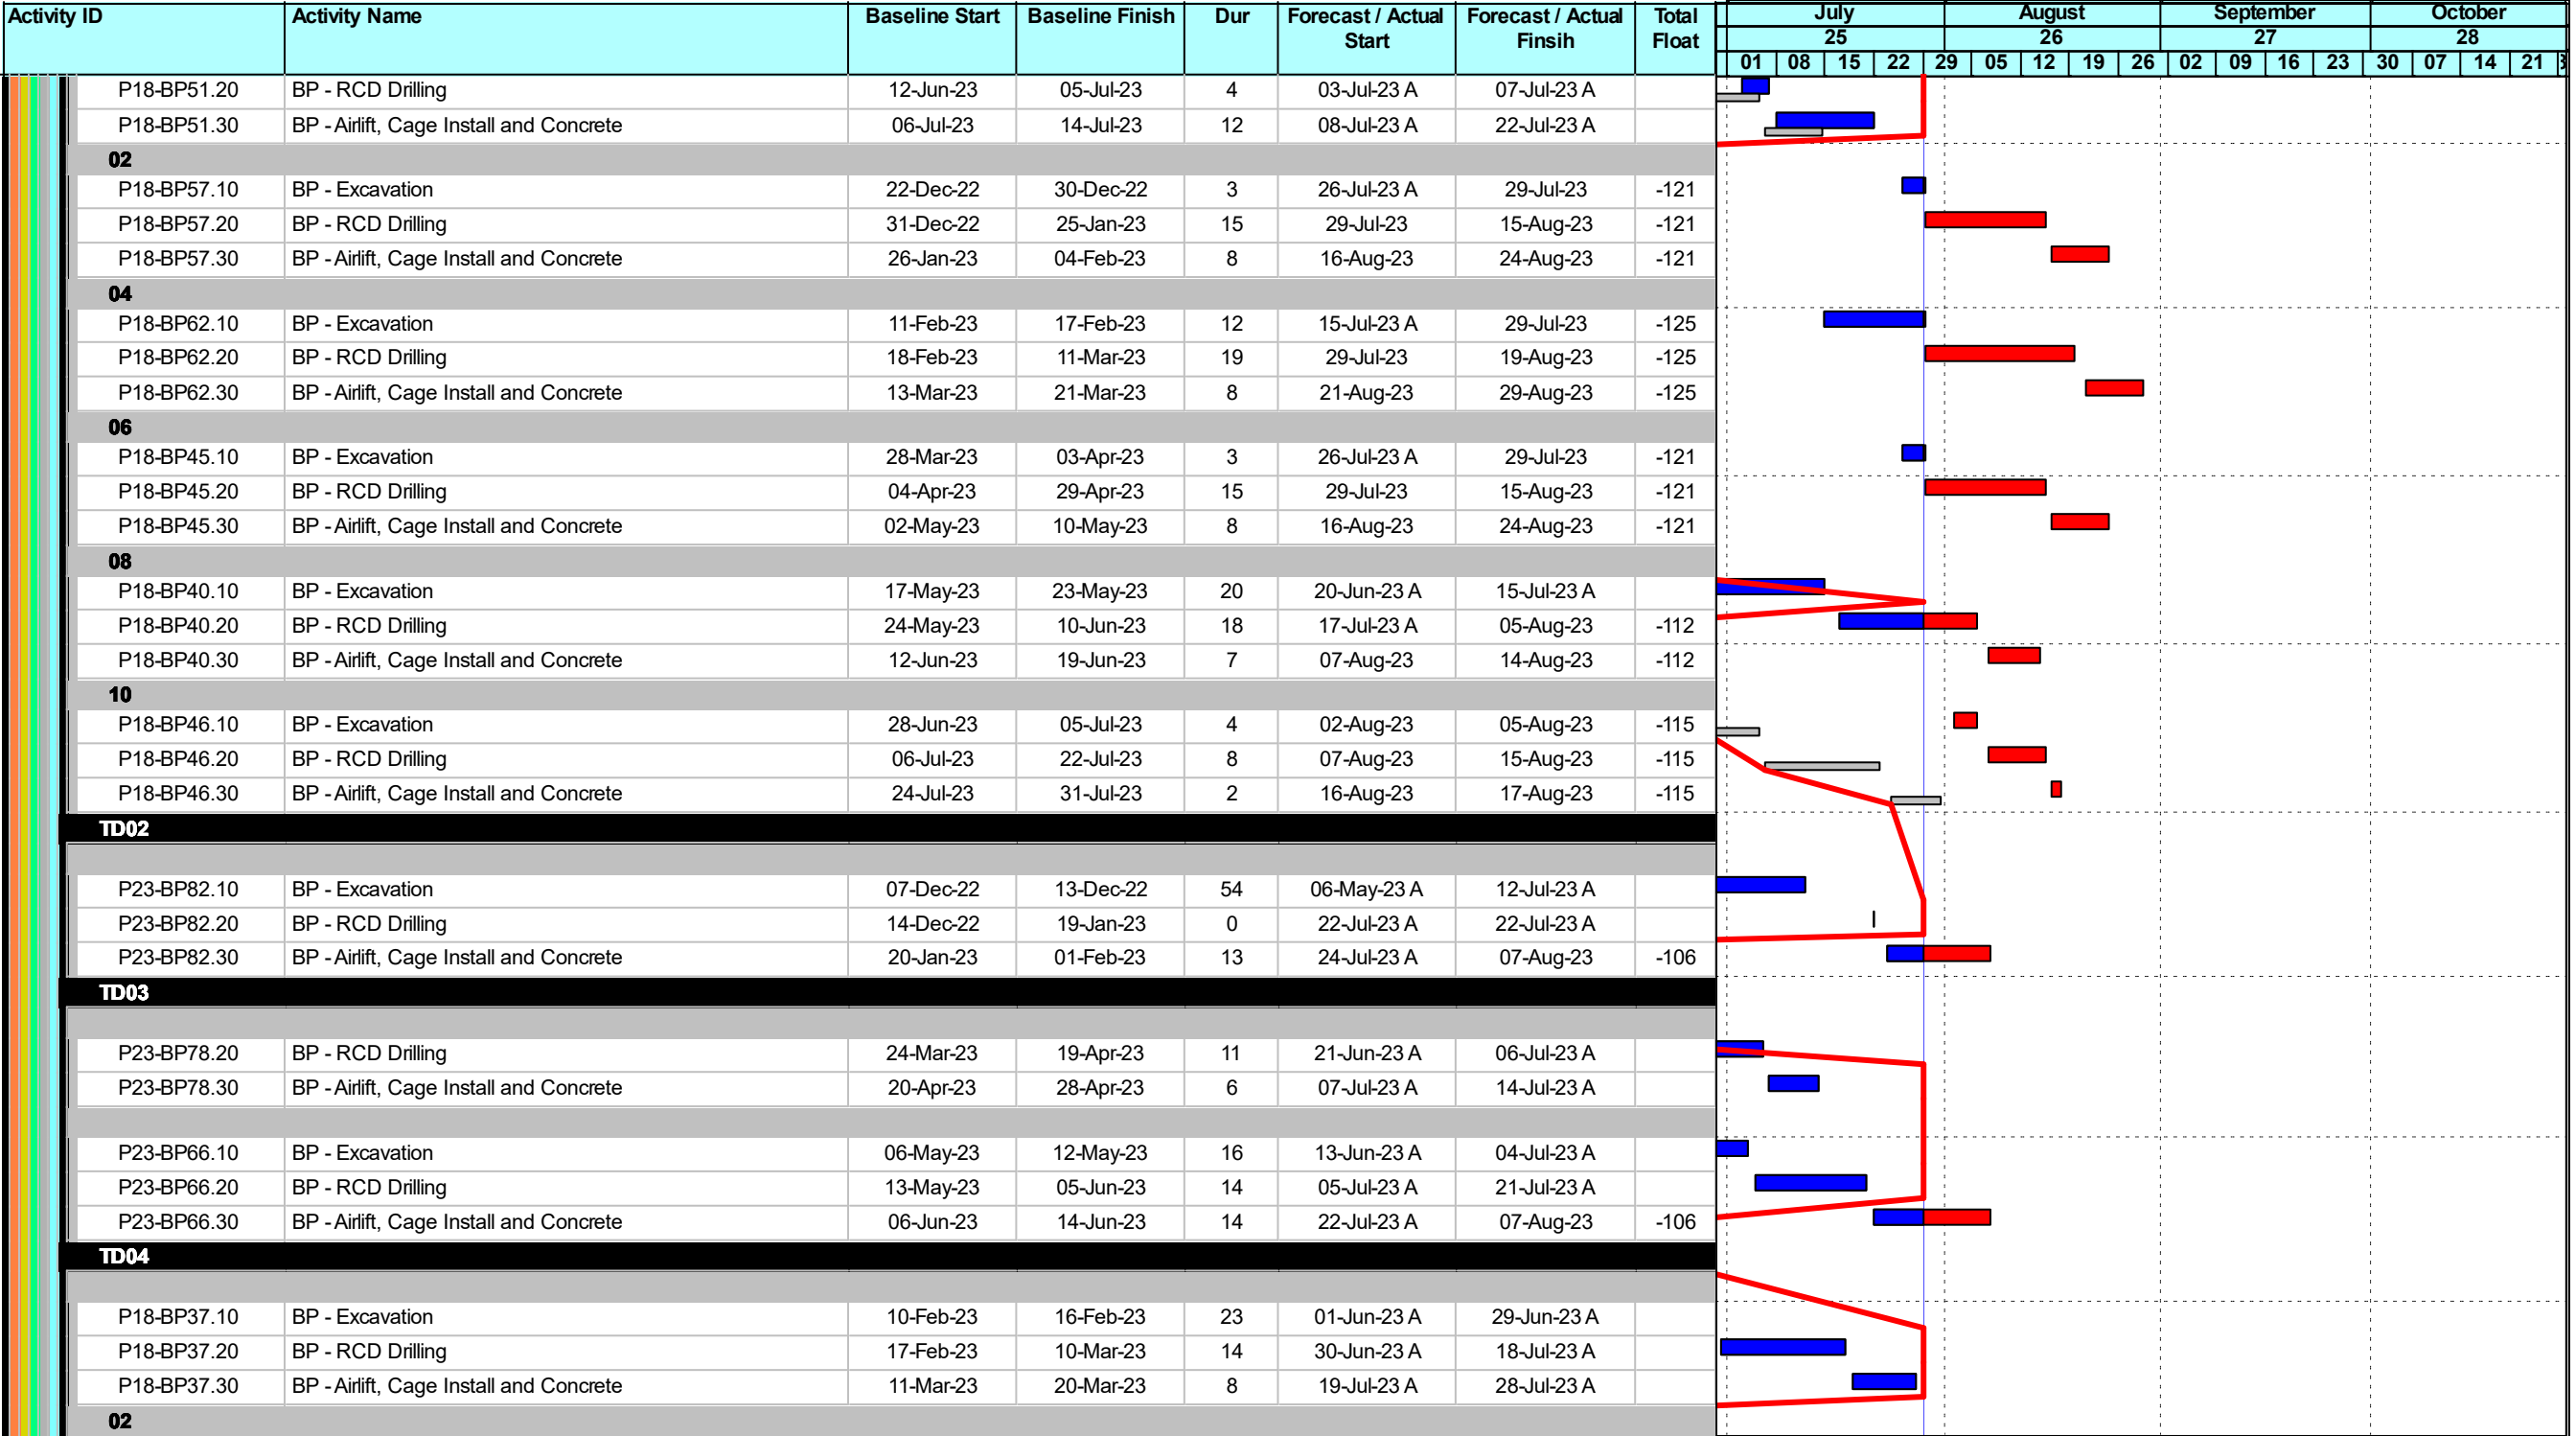

Date	Revision	Checked	Approved
04-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C



	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 28 July 2023
Based on CMWP Rev.0 (3rd Draft)



Date	Revision	Checked	Approved
04-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C


Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	July				August					September				October			
								25				26					27				28			
								01	08	15	22	29	05	12	19	26	02	09	16	23	30	07	14	21
P18-BP49.10	BP - Excavation	21-Dec-22	29-Dec-22	18	08-Jul-23 A	29-Jul-23	-123																	
P18-BP49.20	BP - RCD Drilling	30-Dec-22	21-Jan-23	17	29-Jul-23	17-Aug-23	-123																	
P18-BP49.30	BP - Airlift, Cage Install and Concrete	25-Jan-23	03-Feb-23	8	18-Aug-23	26-Aug-23	-123																	
05																								
P18-BP50.10	BP - Excavation	04-Mar-23	10-Mar-23	3	29-Jul-23	01-Aug-23	-123																	
P18-BP50.20	BP - RCD Drilling	11-Mar-23	01-Apr-23	14	02-Aug-23	17-Aug-23	-123																	
P18-BP50.30	BP - Airlift, Cage Install and Concrete	03-Apr-23	15-Apr-23	8	18-Aug-23	26-Aug-23	-123																	
10																								
P23-BP75.10	BP - Excavation	22-Apr-23	28-Apr-23	18	07-Jul-23 A	28-Jul-23 A																		
P23-BP75.20	BP - RCD Drilling	29-Apr-23	22-May-23	14	29-Jul-23 A	14-Aug-23	-120																	
P23-BP75.30	BP - Airlift, Cage Install and Concrete	23-May-23	01-Jun-23	8	15-Aug-23	23-Aug-23	-120																	
TD05																								
P18-BP64.30	BP - Airlift, Cage Install and Concrete	27-Mar-23	04-Apr-23	20	15-Jun-23 A	11-Jul-23 A																		
07																								
P18-BP36.10	BP - Excavation	20-Mar-23	25-Mar-23	19	07-Jul-23 A	29-Jul-23	-118																	
P18-BP36.20	BP - RCD Drilling	27-Mar-23	17-Apr-23	13	29-Jul-23	12-Aug-23	-118																	
P18-BP36.30	BP - Airlift, Cage Install and Concrete	18-Apr-23	25-Apr-23	7	14-Aug-23	21-Aug-23	-118																	
TD06																								
P18-BP32.30	BP - Airlift, Cage Install and Concrete	21-Apr-23	29-Apr-23	8	19-Jun-23 A	29-Jun-23 A																		
P18-BP34.20	BP - RCD Drilling	21-Apr-23	09-May-23	7	29-Jun-23 A	08-Jul-23 A																		
P18-BP34.30	BP - Airlift, Cage Install and Concrete	10-May-23	17-May-23	9	10-Jul-23 A	20-Jul-23 A																		
03																								
P18-BP23.10	BP IAR-S - Excavation	26-Nov-22	02-Dec-22	3	29-Jul-23	01-Aug-23	-124																	
P18-BP23.20	BP IAR-S - RCD Drilling	03-Dec-22	20-Dec-22	14	02-Aug-23	17-Aug-23	-124																	
P18-BP23.30	BP IAR-S - Airlift, Cage Install and Concrete	23-Dec-22	03-Jan-23	7	21-Aug-23	28-Aug-23	-124																	
TD08																								
10																								
P18-BP56.10	BP - Excavation	18-Feb-23	24-Feb-23	42	11-May-23 A	03-Jul-23 A																		
P18-BP56.20	BP - RCD Drilling	25-Feb-23	18-Mar-23	9	04-Jul-23 A	14-Jul-23 A																		
P18-BP56.30	BP - Airlift, Cage Install and Concrete	20-Mar-23	28-Mar-23	8	15-Jul-23 A	25-Jul-23 A																		
12																								
P18-BP55.10	BP - Excavation	04-Apr-23	14-Apr-23	77	26-Apr-23 A	29-Jul-23	-106																	
P18-BP55.20	BP - RCD Drilling	15-Apr-23	08-May-23	36	15-Jun-23 A	29-Jul-23	-106																	
P18-BP55.30	BP - Airlift, Cage Install and Concrete	09-May-23	17-May-23	8	29-Jul-23	07-Aug-23	-106																	
13																								
P23-BP97.10	BP - Excavation	02-May-23	08-May-23	14	28-Jun-23 A	15-Jul-23 A																		
P23-BP97.20	BP - RCD Drilling	09-May-23	12-Jun-23	7	17-Jul-23 A	25-Jul-23 A																		
P23-BP97.30	BP - Airlift, Cage Install and Concrete	13-Jun-23	21-Jun-23	11	26-Jul-23 A	07-Aug-23	-106																	





- Planned ◆ Planned MS
- Critical ◆ Critical MS
- Actual ◆ Actual MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 28 July 2023
Based on CMWP Rev.0 (3rd Draft)

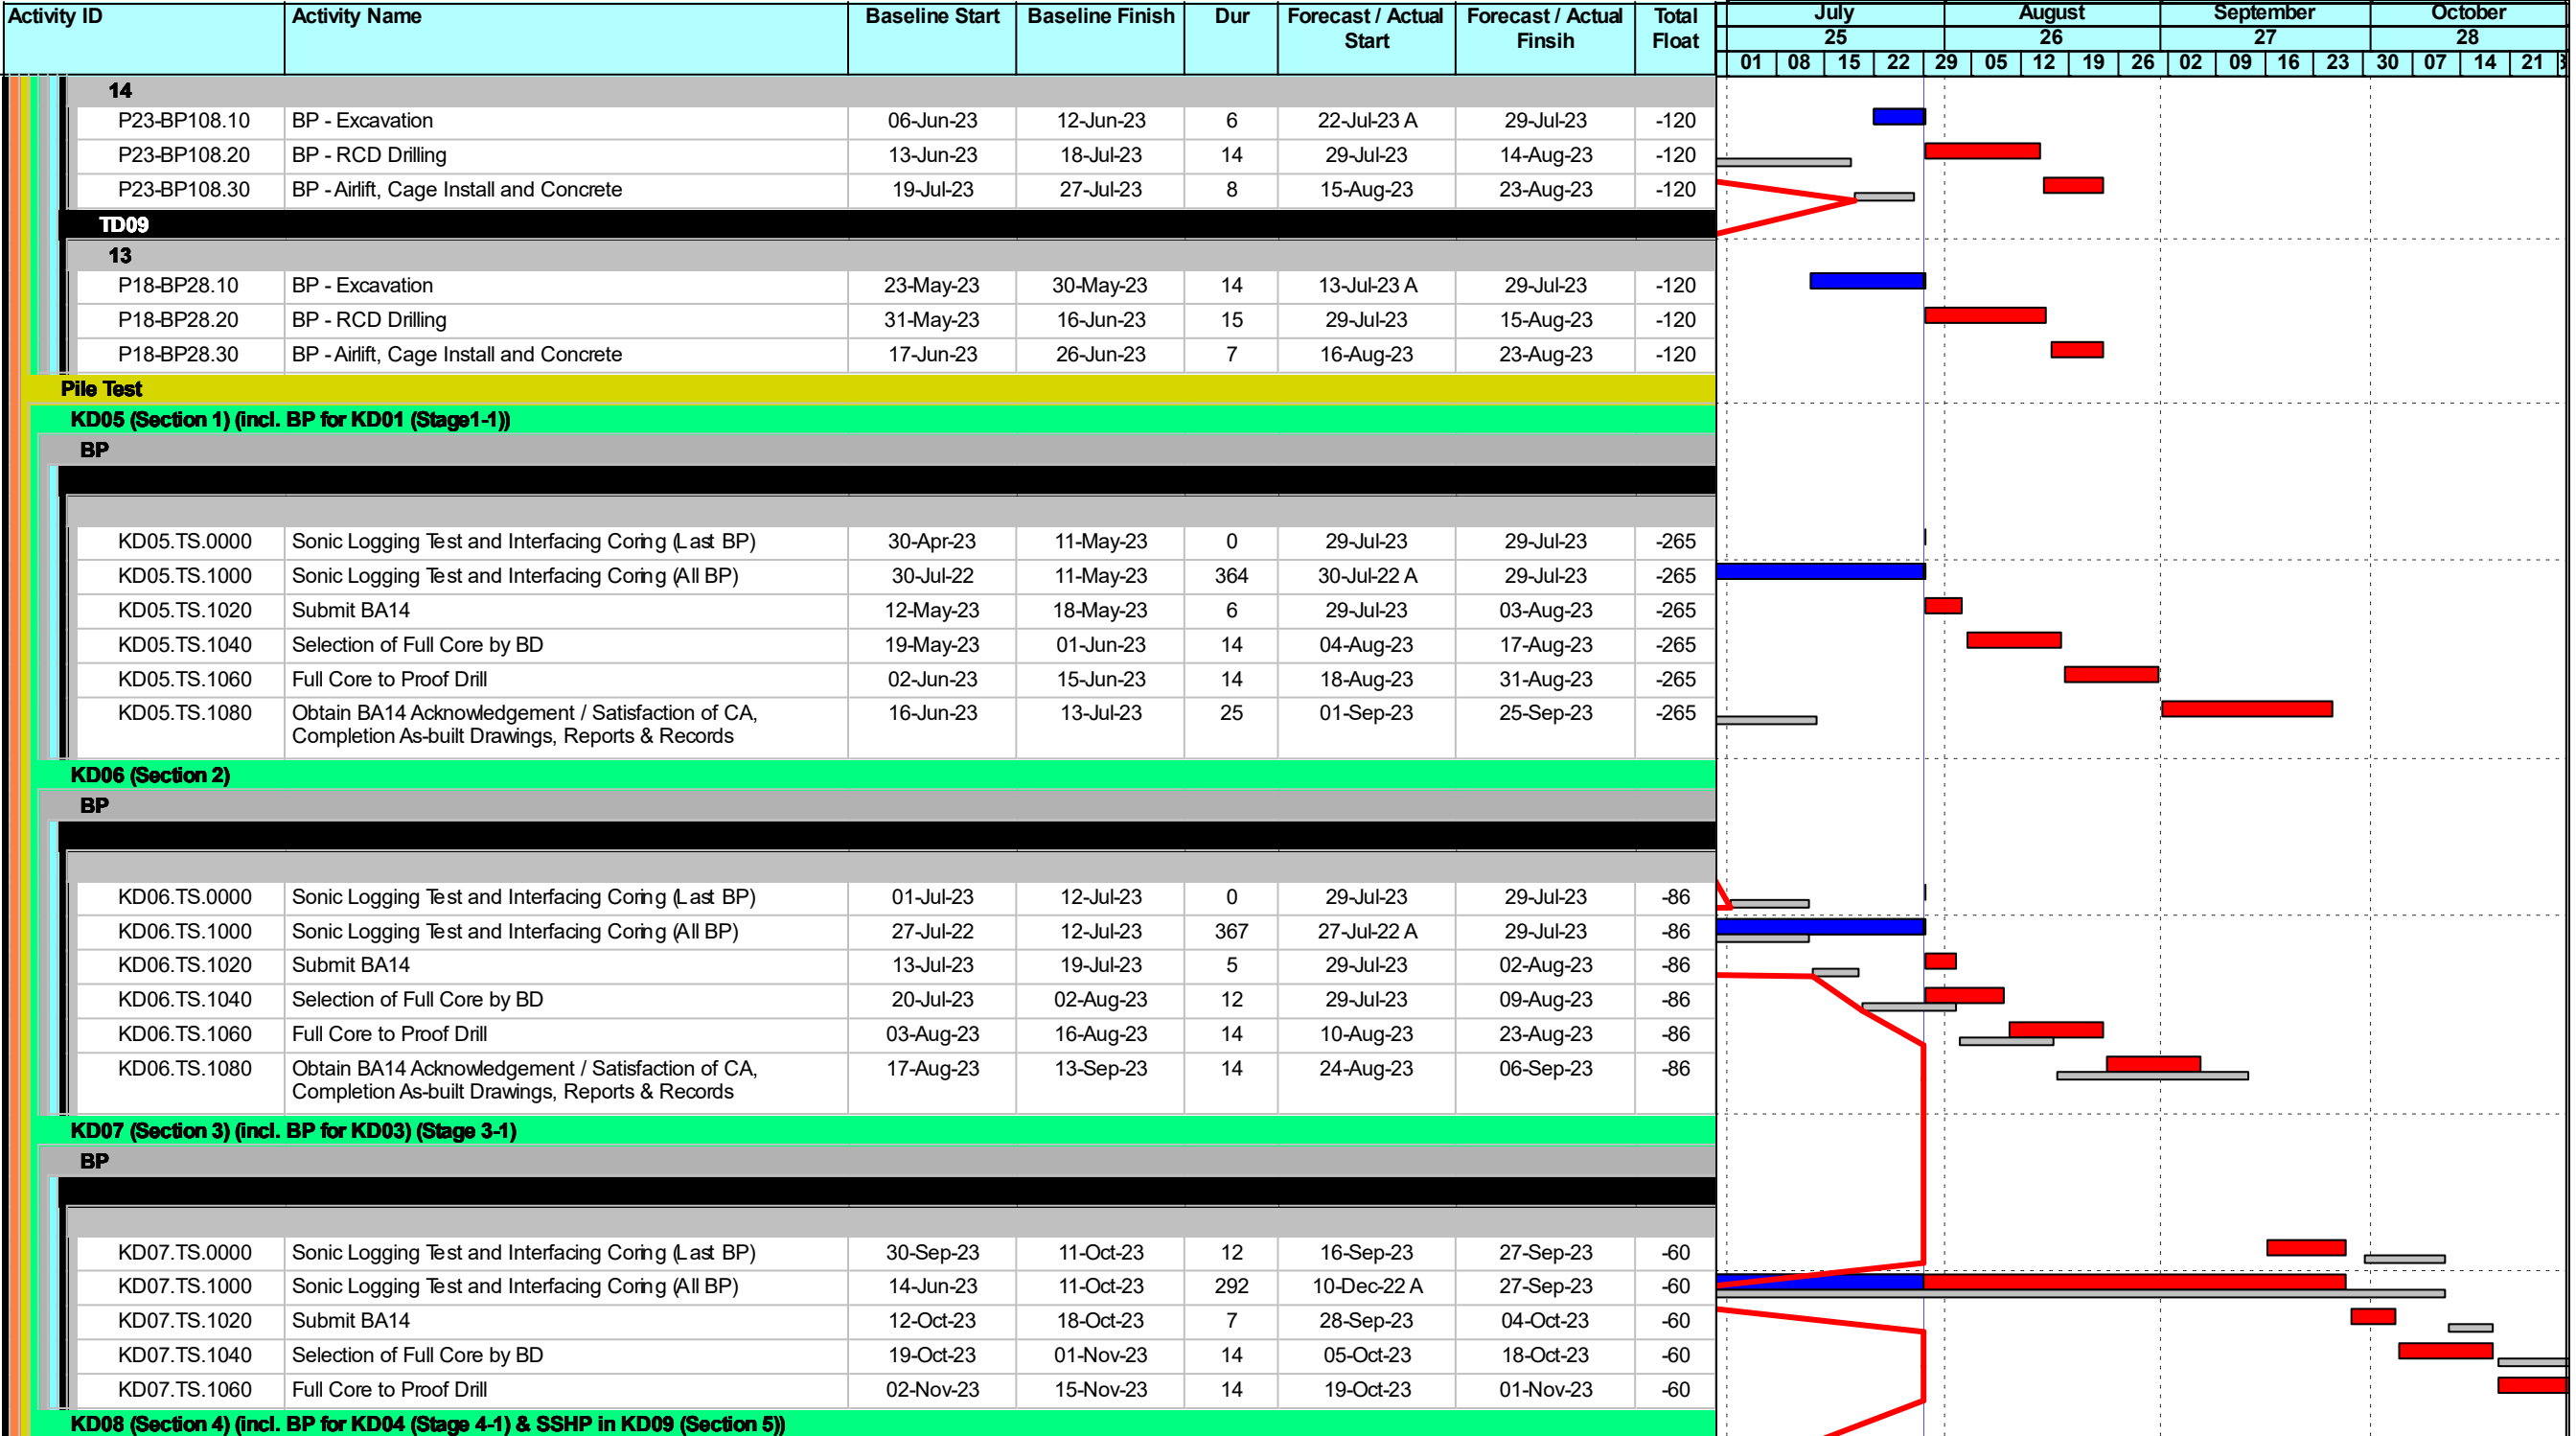

Date	Revision	Checked	Approved
04-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C









	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 28 July 2023
 Based on CMWP Rev.0 (3rd Draft)



Date	Revision	Checked	Approved
04-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	July				August				September				October			
								25				26				27				28			
								01	08	15	22	29	05	12	19	26	02	09	16	23	30	07	14
BP																							
KD08.TS.0000	Sonic Logging Test and Interfacing Coring (Last BP)	31-May-23	11-Jun-23	0	29-Jul-23	29-Jul-23	-113																
KD08.TS.1000	Sonic Logging Test and Interfacing Coring (All SSHP)	04-Jul-22	11-Jun-23	388	04-Jul-22 A	27-Jul-23 A		[Gantt bar: 04-Jul-22 to 27-Jul-23]															
KD08.TS.1020	Submit BA14	12-Jun-23	18-Jun-23	2	29-Jul-23	30-Jul-23	-113	[Gantt bar: 29-Jul-23 to 30-Jul-23]															
KD08.TS.1040	Selection of Full Core by BD	19-Jun-23	02-Jul-23	14	31-Jul-23	13-Aug-23	-113	[Gantt bar: 31-Jul-23 to 13-Aug-23]															
KD08.TS.1060	Full Core to Proof Drill	03-Jul-23	16-Jul-23	14	14-Aug-23	27-Aug-23	-113	[Gantt bar: 14-Aug-23 to 27-Aug-23]															
KD08.TS.1080	Obtain BA14 Acknowledgement / Satisfaction of CA, Completion As-built Drawings, Reports & Records	17-Jul-23	13-Aug-23	17	28-Aug-23	13-Sep-23	-113	[Gantt bar: 28-Aug-23 to 13-Sep-23]															
SSHP																							
KD08.TS.1160	Static Load Test of Selected Pile	06-Dec-22	19-Dec-22	3	21-Jul-23 A	24-Jul-23 A		[Gantt bar: 21-Jul-23 to 24-Jul-23]															
KD08.TS.1180	Obtain BA14 Acknowledgement / Satisfaction of CA, Completion As-built Drawings, Reports & Records	20-Dec-22	16-Jan-23	26	29-Jul-23	23-Aug-23	-93	[Gantt bar: 29-Jul-23 to 23-Aug-23]															
KD09 (Section 5) (incl. BP for KD02 (Stage 5-1))																							
BP																							
KD09.TS.0000	Sonic Logging Test and Interfacing Coring (Last BP)	01-Aug-23	12-Aug-23	14	30-Aug-23	12-Sep-23	-155	[Gantt bar: 30-Aug-23 to 12-Sep-23]															
KD09.TS.1000	Sonic Logging Test and Interfacing Coring (All BP)	23-May-22	12-Aug-23	478	23-May-22 A	12-Sep-23	-155	[Gantt bar: 23-May-22 to 12-Sep-23]															
KD09.TS.1020	Submit BA14	13-Aug-23	19-Aug-23	7	13-Sep-23	19-Sep-23	-155	[Gantt bar: 13-Sep-23 to 19-Sep-23]															
KD09.TS.1040	Selection of Full Core by BD	20-Aug-23	02-Sep-23	14	20-Sep-23	03-Oct-23	-155	[Gantt bar: 20-Sep-23 to 03-Oct-23]															
KD09.TS.1060	Full Core to Proof Drill	03-Sep-23	16-Sep-23	14	04-Oct-23	17-Oct-23	-155	[Gantt bar: 04-Oct-23 to 17-Oct-23]															
KD09.TS.1080	Obtain BA14 Acknowledgement / Satisfaction of CA, Completion As-built Drawings, Reports & Records	17-Sep-23	14-Oct-23	28	18-Oct-23	14-Nov-23	-155	[Gantt bar: 18-Oct-23 to 14-Nov-23]															

	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS



Date	Revision	Checked	Approved
04-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C
