

Zone 2B & 2C

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	August				September				October				November			
								26				27				28				29			
								29	05	12	19	26	02	09	16	23	30	07	14	21	28	04	11

Piling for Integrated Basement and U/G Road in Zone 2B & 2C

Contract Dates							
Key Dates							
KD for Zone 2B							
KD05	KD05 (Section 1) - 03 Jan 2023			13-Jul-23	0	25-Sep-23*	-265
KD06	KD06 (Section 2) - 12 Jun 2023			13-Sep-23	0	06-Sep-23*	-86

KD for Zone 2C							
KD08	KD08 (Section 4) - 23 May 2023			13-Aug-23	0	13-Sep-23*	-113

Construction Stage

Pile Construction

KD07 (Section 3)

Bored Piles

VD01

P26-BP07.10	BP - Excavation	28-Apr-23	05-May-23	25	06-Jul-23 A	04-Aug-23 A	
P26-BP07.20	BP - RCD Drilling	06-May-23	09-Jun-23	6	05-Aug-23 A	12-Aug-23 A	
P26-BP07.30	BP - Airlift, Cage Install and Concrete	10-Jun-23	19-Jun-23	8	14-Aug-23 A	23-Aug-23 A	

08

P26-BP05.10	BP - Excavation	03-Jun-23	09-Jun-23	17	11-Jul-23 A	31-Jul-23 A	
P26-BP05.20	BP - RCD Drilling	10-Jun-23	15-Jul-23	5	01-Aug-23 A	07-Aug-23 A	
P26-BP05.30	BP - Airlift, Cage Install and Concrete	17-Jul-23	25-Jul-23	6	08-Aug-23 A	15-Aug-23 A	

VD02

P30-BP75.30	BP - Airlift, Cage Install and Concrete	10-May-23	18-May-23	8	26-Jul-23 A	04-Aug-23 A	
-------------	---	-----------	-----------	---	-------------	-------------	--

06

P26-BP04.20	BP - RCD Drilling	02-Jun-23	07-Jul-23	13	21-Jul-23 A	05-Aug-23 A	
P26-BP04.30	BP - Airlift, Cage Install and Concrete	08-Jul-23	17-Jul-23	10	07-Aug-23 A	18-Aug-23 A	

VD08


P28&P29-BP26.:	BP - Airlift, Cage Install and Concrete	21-Sep-23	29-Sep-23	9	20-Jul-23 A	31-Jul-23 A	
----------------	---	-----------	-----------	---	-------------	-------------	--

03

P24&P27-BP32.:	BP - Excavation	03-Feb-23	09-Feb-23	14	19-Jul-23 A	04-Aug-23 A	
P24&P27-BP32.:	BP - RCD Drilling	10-Feb-23	15-Mar-23	9	05-Aug-23 A	16-Aug-23 A	
P24&P27-BP32.:	BP - Airlift, Cage Install and Concrete	16-Mar-23	24-Mar-23	13	17-Aug-23 A	31-Aug-23	-52

05

P24&P27-BP19.:	BP - Excavation	17-Apr-23	22-Apr-23	21	22-Jul-23 A	16-Aug-23 A	
P24&P27-BP19.:	BP - RCD Drilling	24-Apr-23	29-May-23	5	17-Aug-23 A	23-Aug-23 A	
P24&P27-BP19.:	BP - Airlift, Cage Install and Concrete	30-May-23	07-Jun-23	7	24-Aug-23 A	31-Aug-23	-51

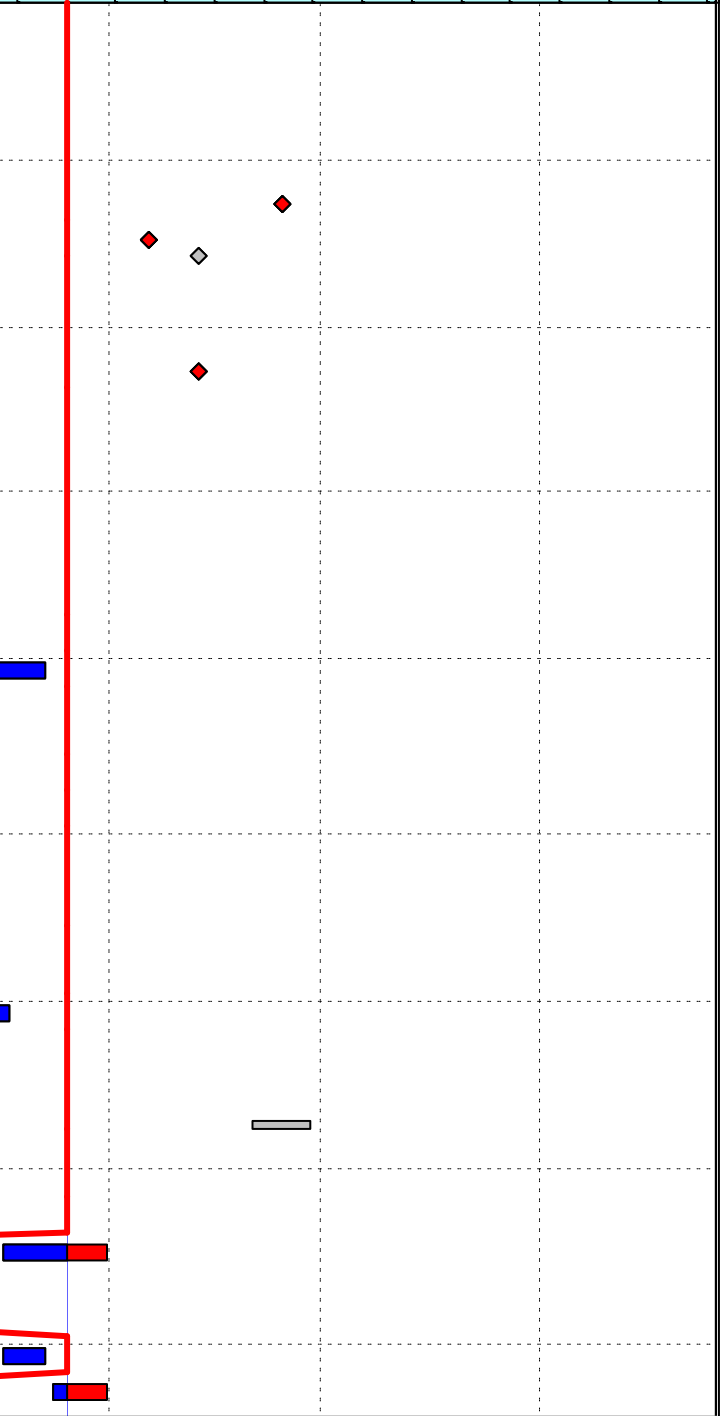

	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS

Date	Revision	Checked	Approved
04-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	August					September				October				November		
								26					27				28				29		
								29	05	12	19	26	02	09	16	23	30	07	14	21	28	04	11

KD09 (Section 5)

Bored Piles

TD01

P18-BP40.20	BP - RCD Drilling	24-May-23	10-Jun-23	17	17-Jul-23 A	05-Aug-23 A	
P18-BP40.30	BP - Airlift, Cage Install and Concrete	12-Jun-23	19-Jun-23	6	07-Aug-23 A	14-Aug-23 A	
P18-BP62.10	BP - Excavation	11-Feb-23	17-Feb-23	18	15-Jul-23 A	05-Aug-23 A	
P18-BP62.20	BP - RCD Drilling	18-Feb-23	11-Mar-23	5	07-Aug-23 A	12-Aug-23 A	
P18-BP62.30	BP - Airlift, Cage Install and Concrete	13-Mar-23	21-Mar-23	6	14-Aug-23 A	21-Aug-23 A	

02

P18-BP57.10	BP - Excavation	22-Dec-22	30-Dec-22	24	26-Jul-23 A	23-Aug-23 A	
P18-BP57.20	BP - RCD Drilling	31-Dec-22	25-Jan-23	7	24-Aug-23 A	31-Aug-23	-130
P18-BP57.30	BP - Airlift, Cage Install and Concrete	26-Jan-23	04-Feb-23	5	01-Sep-23	06-Sep-23	-130

06

P18-BP45.10	BP - Excavation	28-Mar-23	03-Apr-23	22	26-Jul-23 A	21-Aug-23 A	
P18-BP45.20	BP - RCD Drilling	04-Apr-23	29-Apr-23	14	22-Aug-23 A	06-Sep-23	-138
P18-BP45.30	BP - Airlift, Cage Install and Concrete	02-May-23	10-May-23	8	07-Sep-23	15-Sep-23	-138

10

P18-BP46.10	BP - Excavation	28-Jun-23	05-Jul-23	23	29-Jul-23 A	25-Aug-23 A	
P18-BP46.20	BP - RCD Drilling	06-Jul-23	22-Jul-23	9	26-Aug-23 A	05-Sep-23	-131
P18-BP46.30	BP - Airlift, Cage Install and Concrete	24-Jul-23	31-Jul-23	2	06-Sep-23	07-Sep-23	-131

TD02

P23-BP82.30	BP - Airlift, Cage Install and Concrete	20-Jan-23	01-Feb-23	7	24-Jul-23 A	01-Aug-23 A	
-------------	---	-----------	-----------	---	-------------	-------------	--

TD03

P23-BP66.30	BP - Airlift, Cage Install and Concrete	06-Jun-23	14-Jun-23	11	22-Jul-23 A	04-Aug-23 A	
-------------	---	-----------	-----------	----	-------------	-------------	--

TD04


P18-BP37.30	BP - Airlift, Cage Install and Concrete	11-Mar-23	20-Mar-23	8	19-Jul-23 A	28-Jul-23 A	
P23-BP75.10	BP - Excavation	22-Apr-23	28-Apr-23	18	07-Jul-23 A	28-Jul-23 A	
P23-BP75.20	BP - RCD Drilling	29-Apr-23	22-May-23	4	29-Jul-23 A	03-Aug-23 A	
P23-BP75.30	BP - Airlift, Cage Install and Concrete	23-May-23	01-Jun-23	6	04-Aug-23 A	11-Aug-23 A	

02

P18-BP49.10	BP - Excavation	21-Dec-22	29-Dec-22	29	08-Jul-23 A	11-Aug-23 A	
P18-BP49.20	BP - RCD Drilling	30-Dec-22	21-Jan-23	7	12-Aug-23 A	21-Aug-23 A	
P18-BP49.30	BP - Airlift, Cage Install and Concrete	25-Jan-23	03-Feb-23	12	22-Aug-23 A	04-Sep-23	-128

05

P18-BP50.10	BP - Excavation	04-Mar-23	10-Mar-23	21	31-Jul-23 A	24-Aug-23 A	
-------------	-----------------	-----------	-----------	----	-------------	-------------	--

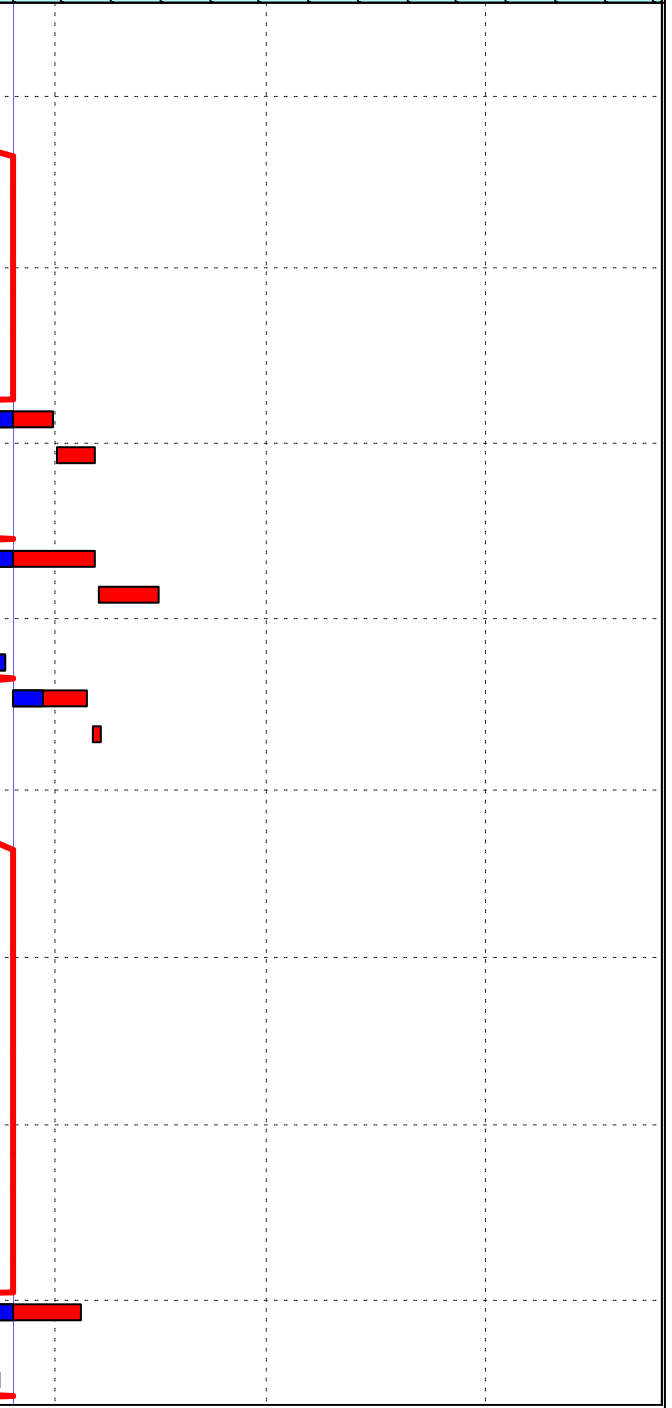

Planned	Planned MS
Critical	Critical MS
Actual	Actual MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 25 August 2023
Based on CMWP Rev.0 (3rd Draft)



Date	Revision	Checked	Approved
04-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	August				September				October				November		
								26				27				28				29		
								29	05	12	19	26	02	09	16	23	30	07	14	21	28	04
P18-BP50.20	BP - RCD Drilling	11-Mar-23	01-Apr-23	11	25-Aug-23 A	06-Sep-23	-138															
P18-BP50.30	BP - Airlift, Cage Install and Concrete	03-Apr-23	15-Apr-23	8	07-Sep-23	15-Sep-23	-138															
TD05																						
07																						
P18-BP36.10	BP - Excavation	20-Mar-23	25-Mar-23	31	07-Jul-23 A	12-Aug-23 A																
P18-BP36.20	BP - RCD Drilling	27-Mar-23	17-Apr-23	10	14-Aug-23 A	25-Aug-23 A																
P18-BP36.30	BP - Airlift, Cage Install and Concrete	18-Apr-23	25-Apr-23	7	26-Aug-23 A	02-Sep-23	-127															
TD06																						
03																						
P18-BP23.10	BP IAR-S - Excavation	26-Nov-22	02-Dec-22	15	12-Aug-23 A	29-Aug-23	-138															
P18-BP23.20	BP IAR-S - RCD Drilling	03-Dec-22	20-Dec-22	7	30-Aug-23	06-Sep-23	-138															
P18-BP23.30	BP IAR-S - Airlift, Cage Install and Concrete	23-Dec-22	03-Jan-23	6	09-Sep-23	15-Sep-23	-138															
TD08																						
P23-BP97.30	BP - Airlift, Cage Install and Concrete	13-Jun-23	21-Jun-23	11	26-Jul-23 A	08-Aug-23 A																
12																						
P18-BP55.10	BP - Excavation	04-Apr-23	14-Apr-23	101	26-Apr-23 A	26-Aug-23	-135															
P18-BP55.20	BP - RCD Drilling	15-Apr-23	08-May-23	10	26-Aug-23	06-Sep-23	-135															
P18-BP55.30	BP - Airlift, Cage Install and Concrete	09-May-23	17-May-23	5	07-Sep-23	12-Sep-23	-135															
14																						
P23-BP108.10	BP - Excavation	06-Jun-23	12-Jun-23	21	22-Jul-23 A	16-Aug-23 A																
P23-BP108.20	BP - RCD Drilling	13-Jun-23	18-Jul-23	3	17-Aug-23 A	21-Aug-23 A																
P23-BP108.30	BP - Airlift, Cage Install and Concrete	19-Jul-23	27-Jul-23	6	22-Aug-23 A	28-Aug-23	-122															
TD09																						
P18-BP28.10	BP - Excavation	23-May-23	30-May-23	40	13-Jul-23 A	28-Aug-23	-138															
P18-BP28.20	BP - RCD Drilling	31-May-23	16-Jun-23	9	29-Aug-23	07-Sep-23	-138															
P18-BP28.30	BP - Airlift, Cage Install and Concrete	17-Jun-23	26-Jun-23	7	08-Sep-23	15-Sep-23	-138															
Pile Test																						
KD05 (Section 1) (incl. BP for KD01 (Stage1-1))																						
BP																						
KD05.TS.0000	Sonic Logging Test and Interfacing Coring (Last BP)	30-Apr-23	11-May-23	7	29-Jul-23 A	05-Aug-23 A																
KD05.TS.1000	Sonic Logging Test and Interfacing Coring (All BP)	30-Jul-22	11-May-23	371	30-Jul-22 A	05-Aug-23 A																
KD05.TS.1020	Submit BA14	12-May-23	18-May-23	0	14-Aug-23 A	14-Aug-23 A																
KD05.TS.1040	Selection of Full Core by BD	19-May-23	01-Jun-23	7	26-Aug-23	01-Sep-23	-265															
KD05.TS.1060	Full Core to Proof Drill	02-Jun-23	15-Jun-23	7	02-Sep-23	08-Sep-23	-265															
KD05.TS.1080	Obtain BA14 Acknowledgement / Satisfaction of CA, Completion As-built Drawings, Reports & Records	16-Jun-23	13-Jul-23	17	09-Sep-23	25-Sep-23	-265															
KD06 (Section 2)																						

Planned	Planned MS
Critical	Critical MS
Actual	Actual MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 25 August 2023
Based on CMWP Rev.0 (3rd Draft)

		Date	Revision	Checked	Approved
		04-Mar-22	R0	KL	B
		02-Dec-22	R03D	KL	C

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	August				September				October				November		
								26				27				28				29		
								29	05	12	19	26	02	09	16	23	30	07	14	21	28	04

BP							
KD06.TS.1020	Submit BA14	13-Jul-23	19-Jul-23	29	28-Jul-23 A	26-Aug-23	-86
KD06.TS.1040	Selection of Full Core by BD	20-Jul-23	02-Aug-23	0	26-Aug-23	26-Aug-23	-86
KD06.TS.1060	Full Core to Proof Drill	03-Aug-23	16-Aug-23	5	26-Aug-23	30-Aug-23	-86
KD06.TS.1080	Obtain BA14 Acknowledgement / Satisfaction of CA, Completion As-built Drawings, Reports & Records	17-Aug-23	13-Sep-23	7	31-Aug-23	06-Sep-23	-86

KD07 (Section 3) (incl. BP for KD03) (Stage 3-1)

BP							
KD07.TS.0000	Sonic Logging Test and Interfacing Coring (Last BP)	30-Sep-23	11-Oct-23	12	02-Sep-23	13-Sep-23	-60
KD07.TS.1000	Sonic Logging Test and Interfacing Coring (All BP)	14-Jun-23	11-Oct-23	278	10-Dec-22 A	13-Sep-23	-60
KD07.TS.1020	Submit BA14	12-Oct-23	18-Oct-23	7	14-Sep-23	20-Sep-23	-60
KD07.TS.1040	Selection of Full Core by BD	19-Oct-23	01-Nov-23	14	21-Sep-23	04-Oct-23	-60
KD07.TS.1060	Full Core to Proof Drill	02-Nov-23	15-Nov-23	28	05-Oct-23	01-Nov-23	-60
KD07.TS.1080	Obtain BA14 Acknowledgement / Satisfaction of CA, Completion As-built Drawings, Reports & Records	16-Nov-23	13-Dec-23	28	02-Nov-23	29-Nov-23	-60


KD08 (Section 4) (incl. BP for KD04 (Stage 4-1) & SSHP in KD09 (Section 5))

BP							
KD08.TS.0000	Sonic Logging Test and Interfacing Coring (Last BP)	31-May-23	11-Jun-23	12	15-Jul-23 A	27-Jul-23 A	
KD08.TS.1000	Sonic Logging Test and Interfacing Coring (All BP)	04-Jul-22	11-Jun-23	388	04-Jul-22 A	27-Jul-23 A	
KD08.TS.1020	Submit BA14	12-Jun-23	18-Jun-23	0	17-Aug-23 A	17-Aug-23 A	
KD08.TS.1040	Selection of Full Core by BD	19-Jun-23	02-Jul-23	5	26-Aug-23	30-Aug-23	-113
KD08.TS.1060	Full Core to Proof Drill	03-Jul-23	16-Jul-23	7	31-Aug-23	06-Sep-23	-113
KD08.TS.1080	Obtain BA14 Acknowledgement / Satisfaction of CA, Completion As-built Drawings, Reports & Records	17-Jul-23	13-Aug-23	7	07-Sep-23	13-Sep-23	-113

SSHP							
KD08.TS.1180	Obtain BA14 Acknowledgement / Satisfaction of CA, Completion As-built Drawings, Reports & Records	20-Dec-22	16-Jan-23	7	26-Aug-23	01-Sep-23	-102

KD09 (Section 5) (incl. BP for KD02 (Stage 5-1))



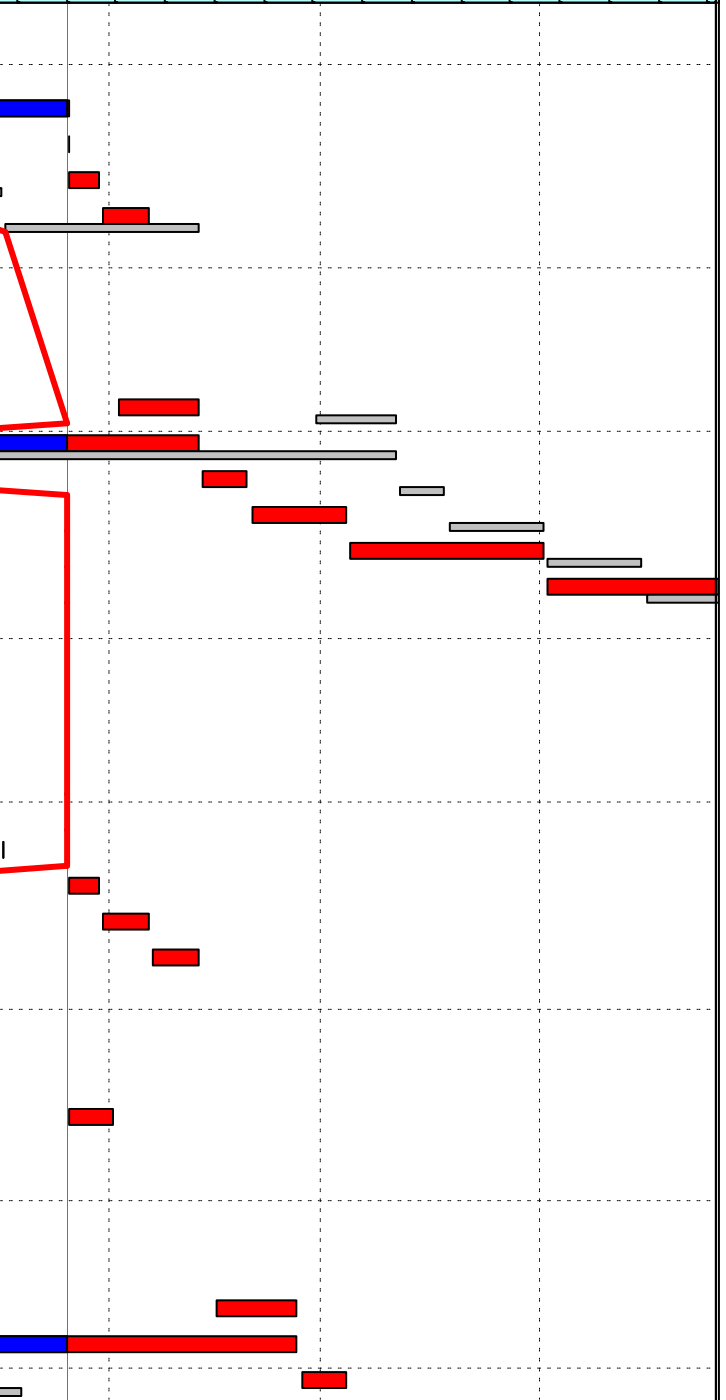



BP							
KD09.TS.0000	Sonic Logging Test and Interfacing Coring (Last BP)	01-Aug-23	12-Aug-23	12	16-Sep-23	27-Sep-23	-170
KD09.TS.1000	Sonic Logging Test and Interfacing Coring (All BP)	23-May-22	12-Aug-23	493	23-May-22 A	27-Sep-23	-170
KD09.TS.1020	Submit BA14	13-Aug-23	19-Aug-23	7	28-Sep-23	04-Oct-23	-170



Planned	Planned MS
Critical	Critical MS
Actual	Actual MS

Date	Revision	Checked	Approved
04-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	August				September				October				November					
								26				27				28				29					
								29	05	12	19	26	02	09	16	23	30	07	14	21	28	04	11	18	25
KD09.TS.1040	Selection of Full Core by BD	20-Aug-23	02-Sep-23	14	05-Oct-23	18-Oct-23	-170																		
KD09.TS.1060	Full Core to Proof Drill	03-Sep-23	16-Sep-23	14	19-Oct-23	01-Nov-23	-170																		
KD09.TS.1080	Obtain BA14 Acknowledgement / Satisfaction of CA, Completion As-built Drawings, Reports & Records	17-Sep-23	14-Oct-23	28	02-Nov-23	29-Nov-23	-170																		

	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 25 August 2023
Based on CMWP Rev.0 (3rd Draft)



Date	Revision	Checked	Approved
04-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	September				October				November				December			
								27				28				29				30			
								02	09	16	23	30	07	14	21	28	04	11	18	25	02	09	16

Piling for Integrated Basement and U/G Road in Zone 2B & 2C

Contract Dates

Key Dates

KD for Zone 2B

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float
KD05	KD05 (Section 1) - 03 Jan 2023		13-Jul-23	0		30-Sep-23*	-269
KD06	KD06 (Section 2) - 12 Jun 2023		13-Sep-23	0		30-Sep-23*	-109
KD07	KD07 (Section 3) - 30 Sep 2023		13-Dec-23	0		29-Nov-23*	-60

KD for Zone 2C

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float
KD08	KD08 (Section 4) - 23 May 2023		13-Aug-23	0		30-Sep-23*	-129
KD09	KD09 (Section 5) - 12 Jun 2023		14-Oct-23	0		29-Nov-23*	-170

Construction Stage

Pile Construction

KD07 (Section 3)

Bored Piles

VD01

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float
P26-BP07.30	BP - Airlift, Cage Install and Concrete	10-Jun-23	19-Jun-23	8	14-Aug-23 A	23-Aug-23 A	

VD08

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float
P24&P27-BP32.:	BP - Airlift, Cage Install and Concrete	16-Mar-23	24-Mar-23	9	17-Aug-23 A	28-Aug-23 A	

05

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float
P24&P27-BP19.:	BP - RCD Drilling	24-Apr-23	29-May-23	5	17-Aug-23 A	23-Aug-23 A	
P24&P27-BP19.:	BP - Airlift, Cage Install and Concrete	30-May-23	07-Jun-23	6	24-Aug-23 A	31-Aug-23 A	

KD09 (Section 5)

Bored Piles

TD01

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float
P18-BP57.10	BP - Excavation	22-Dec-22	30-Dec-22	24	26-Jul-23 A	23-Aug-23 A	
P18-BP57.20	BP - RCD Drilling	31-Dec-22	25-Jan-23	6	24-Aug-23 A	31-Aug-23 A	
P18-BP57.30	BP - Airlift, Cage Install and Concrete	26-Jan-23	04-Feb-23	7	01-Sep-23 A	09-Sep-23 A	


06

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float
P18-BP45.20	BP - RCD Drilling	04-Apr-23	29-Apr-23	12	22-Aug-23 A	05-Sep-23 A	
P18-BP45.30	BP - Airlift, Cage Install and Concrete	02-May-23	10-May-23	7	06-Sep-23 A	14-Sep-23 A	

10

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float
P18-BP46.10	BP - Excavation	28-Jun-23	05-Jul-23	23	29-Jul-23 A	25-Aug-23 A	
P18-BP46.20	BP - RCD Drilling	06-Jul-23	22-Jul-23	4	26-Aug-23 A	31-Aug-23 A	
P18-BP46.30	BP - Airlift, Cage Install and Concrete	24-Jul-23	31-Jul-23	9	01-Sep-23 A	12-Sep-23 A	

TD04

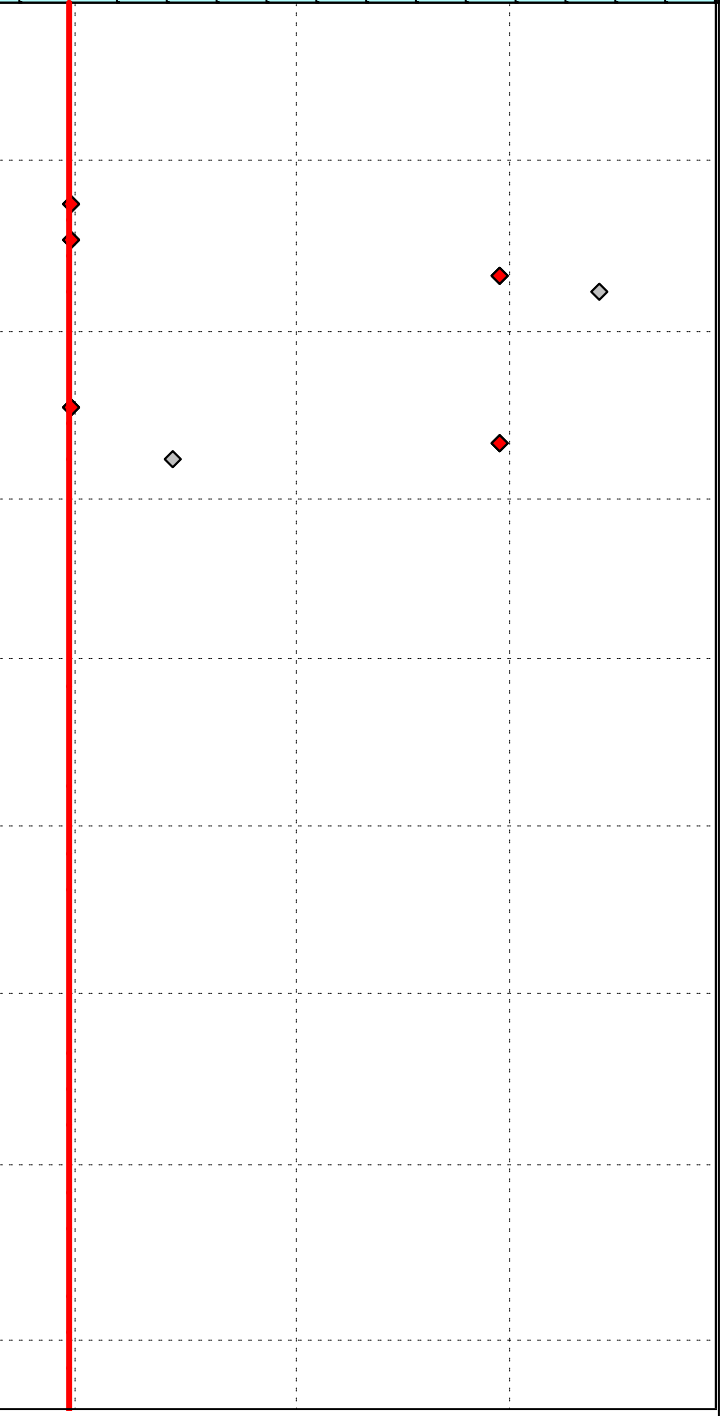

	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS



Date	Revision	Checked	Approved
04-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	September				October				November				December			
								27				28				29				30			
								02	09	16	23	30	07	14	21	28	04	11	18	25	02	09	16

02																										
P18-BP49.30	BP - Airlift, Cage Install and Concrete	25-Jan-23	03-Feb-23	13	22-Aug-23 A	06-Sep-23 A																				
05																										
P18-BP50.10	BP - Excavation	04-Mar-23	10-Mar-23	21	31-Jul-23 A	24-Aug-23 A																				
P18-BP50.20	BP - RCD Drilling	11-Mar-23	01-Apr-23	15	25-Aug-23 A	12-Sep-23 A																				
P18-BP50.30	BP - Airlift, Cage Install and Concrete	03-Apr-23	15-Apr-23	6	13-Sep-23 A	19-Sep-23 A																				
TD05																										
07																										
P18-BP36.20	BP - RCD Drilling	27-Mar-23	17-Apr-23	10	14-Aug-23 A	25-Aug-23 A																				
P18-BP36.30	BP - Airlift, Cage Install and Concrete	18-Apr-23	25-Apr-23	4	26-Aug-23 A	31-Aug-23 A																				
TD06																										
03																										
P18-BP23.30	BP IAR-S - Airlift, Cage Install and Concrete	23-Dec-22	03-Jan-23	5	19-Aug-23 A	25-Aug-23 A																				
TD08																										
P23-BP108.30	BP - Airlift, Cage Install and Concrete	19-Jul-23	27-Jul-23	5	22-Aug-23 A	28-Aug-23 A																				
12																										
P18-BP55.10	BP - Excavation	04-Apr-23	14-Apr-23	113	26-Apr-23 A	09-Sep-23 A																				
P18-BP55.20	BP - RCD Drilling	15-Apr-23	08-May-23	9	11-Sep-23 A	21-Sep-23 A																				
P18-BP55.30	BP - Airlift, Cage Install and Concrete	09-May-23	17-May-23	6	15-Sep-23 A	21-Sep-23 A																				
TD09																										
P18-BP28.10	BP - Excavation	23-May-23	30-May-23	40	13-Jul-23 A	29-Aug-23 A																				
P18-BP28.20	BP - RCD Drilling	31-May-23	16-Jun-23	10	30-Aug-23 A	11-Sep-23 A																				
P18-BP28.30	BP - Airlift, Cage Install and Concrete	17-Jun-23	26-Jun-23	5	12-Sep-23 A	16-Sep-23 A																				

Pile Test







KD05 (Section 1) (incl. BP for KD01 (Stage1-1))

BP							
KD05.TS.1040	Selection of Full Core by BD	19-May-23	01-Jun-23	0	30-Sep-23	30-Sep-23	-269
KD05.TS.1060	Full Core to Proof Drill	02-Jun-23	15-Jun-23	0	30-Sep-23	30-Sep-23	-269
KD05.TS.1080	Obtain BA14 Acknowledgement / Satisfaction of CA, Completion As-built Drawings, Reports & Records	16-Jun-23	13-Jul-23	0	30-Sep-23	30-Sep-23	-269

KD06 (Section 2)

BP							
KD06.TS.1040	Selection of Full Core by BD	20-Jul-23	02-Aug-23	0	30-Sep-23	30-Sep-23	-109
KD06.TS.1060	Full Core to Proof Drill	03-Aug-23	16-Aug-23	0	30-Sep-23	30-Sep-23	-109
KD06.TS.1080	Obtain BA14 Acknowledgement / Satisfaction of CA, Compli	17-Aug-23	13-Sep-23	0	30-Sep-23	30-Sep-23	-109

KD07 (Section 3) (incl. BP for KD03) (Stage 3-1)

	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 29 September 2023
Based on CMWP Rev.0 (3rd Draft)

		Date	Revision	Checked	Approved
		04-Mar-22	R0	KL	B
		02-Dec-22	R03D	KL	C

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	September				October				November				December								
								27				28				29				30								
								02	09	16	23	30	07	14	21	28	04	11	18	25	02	09	16	23				
BP																												
KD07.TS.0000	Sonic Logging Test and Interfacing Coring (Last BP)	30-Sep-23	11-Oct-23	0	30-Sep-23	30-Sep-23	-58																					
KD07.TS.1000	Sonic Logging Test and Interfacing Coring (All BP)	14-Jun-23	11-Oct-23	296	10-Dec-22 A	01-Oct-23	-60																					
KD07.TS.1020	Submit BA14	12-Oct-23	18-Oct-23	0	02-Oct-23	02-Oct-23	-60																					
KD07.TS.1040	Selection of Full Core by BD	19-Oct-23	01-Nov-23	3	02-Oct-23	04-Oct-23	-60																					
KD07.TS.1060	Full Core to Proof Drill	02-Nov-23	15-Nov-23	28	05-Oct-23	01-Nov-23	-60																					
KD07.TS.1080	Obtain BA14 Acknowledgement / Satisfaction of CA, Compli	16-Nov-23	13-Dec-23	28	02-Nov-23	29-Nov-23	-60																					
KD08 (Section 4) (incl. BP for KD04 (Stage 4-1) & SSHP in KD09 (Section 5))																												
BP																												
KD08.TS.1040	Selection of Full Core by BD	19-Jun-23	02-Jul-23	0	30-Sep-23	30-Sep-23	-129																					
KD08.TS.1060	Full Core to Proof Drill	03-Jul-23	16-Jul-23	0	30-Sep-23	30-Sep-23	-129																					
KD08.TS.1080	Obtain BA14 Acknowledgement / Satisfaction of CA, Compli	17-Jul-23	13-Aug-23	0	30-Sep-23	30-Sep-23	-129																					
SSHP																												
KD08.TS.1180	Obtain BA14 Acknowledgement / Satisfaction of CA, Compli	20-Dec-22	16-Jan-23	0	30-Sep-23	30-Sep-23	-130																					
KD09 (Section 5) (incl. BP for KD02 (Stage 5-1))																												
BP																												
KD09.TS.0000	Sonic Logging Test and Interfacing Coring (Last BP)	01-Aug-23	12-Aug-23	1	30-Sep-23	30-Sep-23	-170																					
KD09.TS.1000	Sonic Logging Test and Interfacing Coring (All BP)	23-May-22	12-Aug-23	496	23-May-22 A	01-Oct-23	-170																					
KD09.TS.1020	Submit BA14	13-Aug-23	19-Aug-23	4	01-Oct-23	04-Oct-23	-170																					
KD09.TS.1040	Selection of Full Core by BD	20-Aug-23	02-Sep-23	14	05-Oct-23	18-Oct-23	-170																					
KD09.TS.1060	Full Core to Proof Drill	03-Sep-23	16-Sep-23	14	19-Oct-23	01-Nov-23	-170																					
KD09.TS.1080	Obtain BA14 Acknowledgement / Satisfaction of CA, Compli	17-Sep-23	14-Oct-23	28	02-Nov-23	29-Nov-23	-170																					

	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS




Date	Revision	Checked	Approved
04-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	October					November					December				January											
								28	29	30	01	02	03	04	05	06	07	08	09	10	11	12	13	14	15	16	17	18	19	20	21	22	23

Piling for Integrated Basement and U/G Road in Zone 2B & 2C

Contract Dates							
Key Dates							
KD for Zone 2B							
KD05	KD05 (Section 1) - 03 Jan 2023			13-Jul-23	0	21-Oct-23*	-290
KD06	KD06 (Section 2) - 12 Jun 2023			13-Sep-23	0	21-Oct-23*	-130
KD07	KD07 (Section 3) - 30 Sep 2023			13-Dec-23	0	29-Nov-23*	-60
KD for Zone 2C							
KD08	KD08 (Section 4) - 23 May 2023			13-Aug-23	0	21-Oct-23*	-150
KD09	KD09 (Section 5) - 12 Jun 2023			14-Oct-23	0	29-Nov-23*	-170
KD for Zone 2B (Optional Items)							
KD10	KD10 (Section 6) (Tree felling at Austin Road West) (180 days after CA's Instruction) (Optional Works Item No.1A)			30-Jul-23	0	21-Oct-23*	-81
KD for Zone 2C (Optional Items)							
KD11	KD11 (Section 7) (Tree felling at Zone 2C) (180 days after CA's Instruction) (Optional Works Item No.1B)			30-Jul-23	0	21-Oct-23*	-81
Construction Stage							
Pile Construction							
KD09 (Section 5)							
Bored Piles							
TD01							
P18-BP45.30	BP - Airlift, Cage Install and Concrete			02-May-23	10-May-23	06-Sep-23 A	14-Sep-23 A
TD04							
05							
P18-BP50.30	BP - Airlift, Cage Install and Concrete			03-Apr-23	15-Apr-23	13-Sep-23 A	19-Sep-23 A
TD08							
P18-BP55.20	BP - RCD Drilling			15-Apr-23	08-May-23	11-Sep-23 A	21-Sep-23 A
P18-BP55.30	BP - Airlift, Cage Install and Concrete			09-May-23	17-May-23	15-Sep-23 A	21-Sep-23 A
TD09							
P18-BP28.30	BP - Airlift, Cage Install and Concrete			17-Jun-23	26-Jun-23	12-Sep-23 A	16-Sep-23 A
Pile Test							
KD05 (Section 1) (incl. BP for KD01 (Stage1-1))							

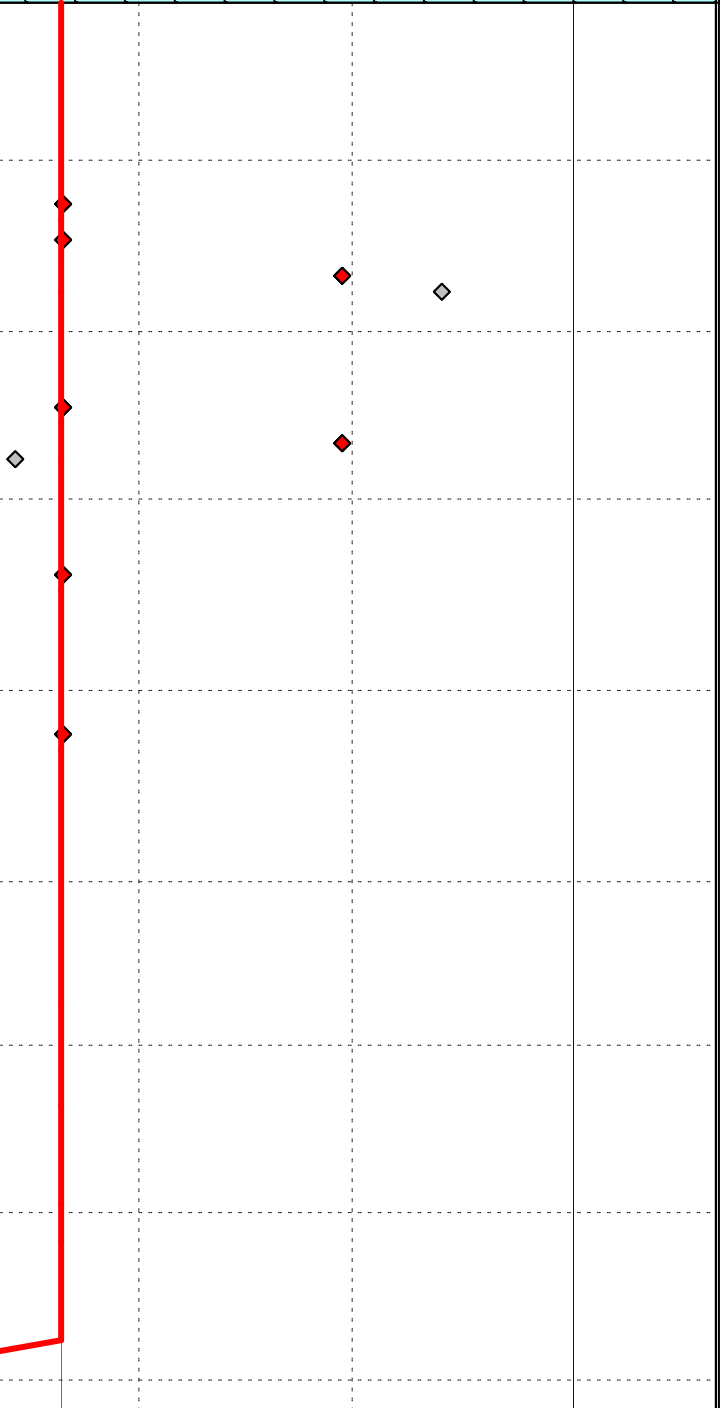

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	October					November					December				January		
								28					29					30				31		
								8	25	02	09	16	23	30	06	13	20	27	04	11	18	25	01	08

BP

KD05.TS.1040	Selection of Full Core by BD	19-May-23	01-Jun-23	0	21-Oct-23	21-Oct-23	-290
KD05.TS.1060	Full Core to Proof Drill	02-Jun-23	15-Jun-23	0	21-Oct-23	21-Oct-23	-290
KD05.TS.1080	Obtain BA14 Acknowledgement / Satisfaction of CA, Completion As-built Drawings, Reports & Records	16-Jun-23	13-Jul-23	0	21-Oct-23	21-Oct-23	-290

KD06 (Section 2)

BP

KD06.TS.1040	Selection of Full Core by BD	20-Jul-23	02-Aug-23	0	21-Oct-23	21-Oct-23	-130
KD06.TS.1060	Full Core to Proof Drill	03-Aug-23	16-Aug-23	0	21-Oct-23	21-Oct-23	-130
KD06.TS.1080	Obtain BA14 Acknowledgement / Satisfaction of CA, Completion As-built Drawings, Reports & Records	17-Aug-23	13-Sep-23	0	21-Oct-23	21-Oct-23	-130

KD07 (Section 3) (incl. BP for KD03) (Stage 3-1)

BP

KD07.TS.0000	Sonic Logging Test and Interfacing Coring (Last BP)	30-Sep-23	11-Oct-23	15	11-Sep-23 A	26-Sep-23 A	
KD07.TS.1000	Sonic Logging Test and Interfacing Coring (All BP)	14-Jun-23	11-Oct-23	291	10-Dec-22 A	26-Sep-23 A	
KD07.TS.1020	Submit BA14	12-Oct-23	18-Oct-23	1	21-Oct-23	21-Oct-23	-60
KD07.TS.1040	Selection of Full Core by BD	19-Oct-23	01-Nov-23	11	22-Oct-23	01-Nov-23	-60
KD07.TS.1060	Full Core to Proof Drill	02-Nov-23	15-Nov-23	14	02-Nov-23	15-Nov-23	-60
KD07.TS.1080	Obtain BA14 Acknowledgement / Satisfaction of CA, Completion As-built Drawings, Reports & Records	16-Nov-23	13-Dec-23	14	16-Nov-23	29-Nov-23	-60

KD08 (Section 4) (incl. BP for KD04 (Stage 4-1) & SSHP in KD09 (Section 5))

BP

KD08.TS.1040	Selection of Full Core by BD	19-Jun-23	02-Jul-23	0	21-Oct-23	21-Oct-23	-150
KD08.TS.1060	Full Core to Proof Drill	03-Jul-23	16-Jul-23	0	21-Oct-23	21-Oct-23	-150
KD08.TS.1080	Obtain BA14 Acknowledgement / Satisfaction of CA, Completion As-built Drawings, Reports & Records	17-Jul-23	13-Aug-23	0	21-Oct-23	21-Oct-23	-150


SSHP

KD08.TS.1180	Obtain BA14 Acknowledgement / Satisfaction of CA, Completion As-built Drawings, Reports & Records	20-Dec-22	16-Jan-23	0	21-Oct-23	21-Oct-23	-151
--------------	---	-----------	-----------	---	-----------	-----------	------





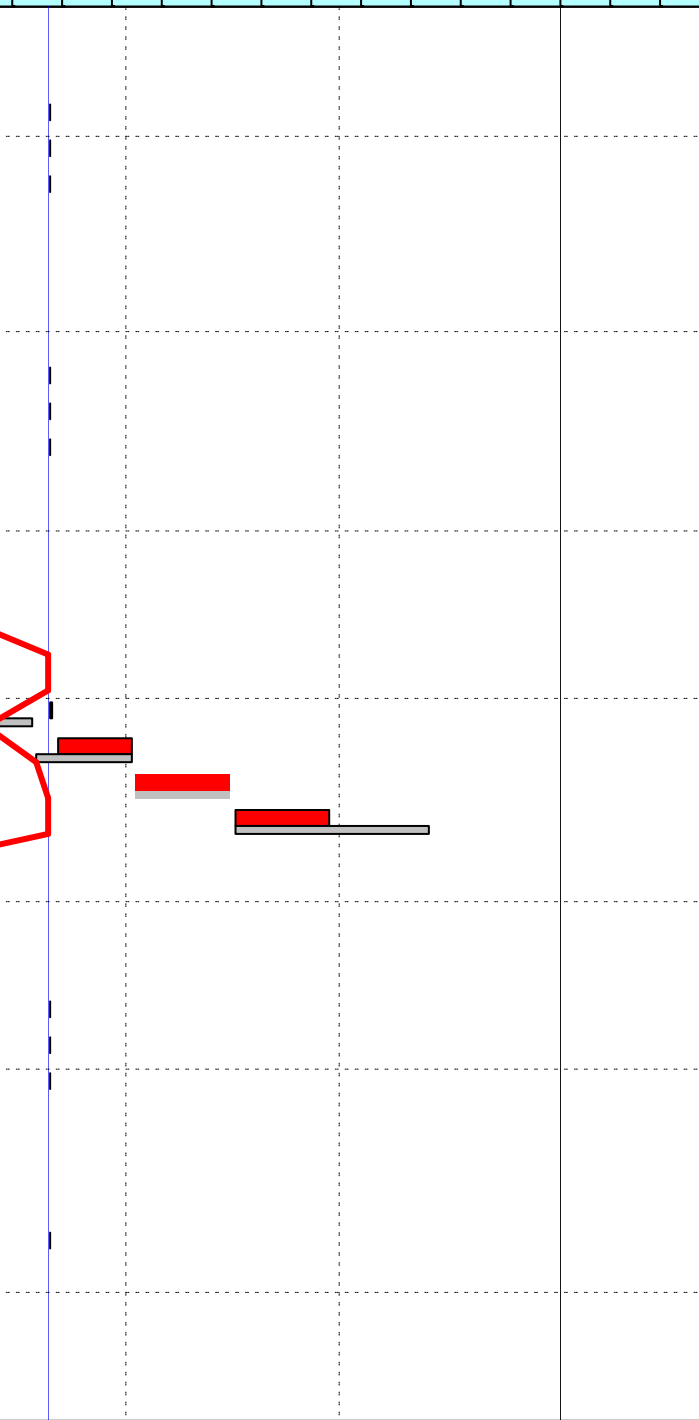

KD09 (Section 5) (incl. BP for KD02 (Stage 5-1))

BP

--	--	--	--	--	--	--	--



Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Gantt Chart															
								October				November				December				January			
								28	29	30	31	01	02	03	04	05	06	07	08	09	10	11	12
KD09.TS.0000	Sonic Logging Test and Interfacing Coring (Last BP)	01-Aug-23	12-Aug-23	149	18-May-23 A	13-Oct-23 A		[Gantt bar: 18-May-23 to 13-Oct-23]															
KD09.TS.1000	Sonic Logging Test and Interfacing Coring (All BP)	23-May-22	12-Aug-23	508	23-May-22 A	13-Oct-23 A		[Gantt bar: 23-May-22 to 13-Oct-23]															
KD09.TS.1020	Submit BA14	13-Aug-23	19-Aug-23	1	21-Oct-23	21-Oct-23	-170	[Gantt bar: 21-Oct-23 to 21-Oct-23]															
KD09.TS.1040	Selection of Full Core by BD	20-Aug-23	02-Sep-23	11	22-Oct-23	01-Nov-23	-170	[Gantt bar: 22-Oct-23 to 01-Nov-23]															
KD09.TS.1060	Full Core to Proof Drill	03-Sep-23	16-Sep-23	14	02-Nov-23	15-Nov-23	-170	[Gantt bar: 02-Nov-23 to 15-Nov-23]															
KD09.TS.1080	Obtain BA14 Acknowledgement / Satisfaction of CA, Completion As-built Drawings, Reports & Records	17-Sep-23	14-Oct-23	14	16-Nov-23	29-Nov-23	-170	[Gantt bar: 16-Nov-23 to 29-Nov-23]															

	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS

West Kowloon Cultural District Authority
Piling for Integrated Basement and U/G Road in Zone 2B 2C
3 Month Rolling Programme as of 20 October 2023
Based on CMWP Rev.0 (3rd Draft)

		Date	Revision	Checked	Approved
		04-Mar-22	R0	KL	B
		02-Dec-22	R03D	KL	C
