

**Zone 2B & 2C**

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	November					December				January				February			
								29					30				31				32			
								0	06	13	20	27	04	11	18	25	01	08	15	22	29	05	12	19

**Piling for Integrated Basement and U/G Road in Zone 2B & 2C**

**Contract Dates**

**Key Dates**

**KD for Zone 2B**

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float
KD05	KD05 (Section 1) - 03 Jan 2023		13-Jul-23	0		27-Dec-23*	-358
KD06	KD06 (Section 2) - 12 Jun 2023		13-Sep-23	0		27-Dec-23*	-198
KD07	KD07 (Section 3) - 30 Sep 2023		13-Dec-23	0		27-Dec-23*	-88

**KD for Zone 2C**

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float
KD08	KD08 (Section 4) - 23 May 2023		13-Aug-23	0		27-Dec-23*	-218
KD09	KD09 (Section 5) - 12 Jun 2023		14-Oct-23	0		28-Dec-23*	-199

**Construction Stage**

**Pile Test**

**KD05 (Section 1) (incl. BP for KD01 (Stage1-1))**

**BP**

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float
KD05.TS.1040	Selection of Full Core by BD	19-May-23	01-Jun-23	2	02-Dec-23	03-Dec-23	-358
KD05.TS.1060	Full Core to Proof Drill	02-Jun-23	15-Jun-23	10	04-Dec-23	13-Dec-23	-358
KD05.TS.1080	Obtain BA14 Acknowledgement / Satisfaction of CA, Completion As-built Drawings, Reports & Records	16-Jun-23	13-Jul-23	14	14-Dec-23	27-Dec-23	-358

**KD06 (Section 2)**

**BP**

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float
KD06.TS.1040	Selection of Full Core by BD	20-Jul-23	02-Aug-23	1	07-Nov-23 A	07-Nov-23 A	
KD06.TS.1060	Full Core to Proof Drill	03-Aug-23	16-Aug-23	19	25-Nov-23 A	13-Dec-23	-198
KD06.TS.1080	Obtain BA14 Acknowledgement / Satisfaction of CA, Completion As-built Drawings, Reports & Records	17-Aug-23	13-Sep-23	14	14-Dec-23	27-Dec-23	-198

**KD07 (Section 3) (incl. BP for KD03) (Stage 3-1)**


**BP**

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float
KD07.TS.1040	Selection of Full Core by BD	19-Oct-23	01-Nov-23	4	02-Dec-23	05-Dec-23	-88
KD07.TS.1060	Full Core to Proof Drill	02-Nov-23	15-Nov-23	8	06-Dec-23	13-Dec-23	-88
KD07.TS.1080	Obtain BA14 Acknowledgement / Satisfaction of CA, Completion As-built Drawings, Reports & Records	16-Nov-23	13-Dec-23	14	14-Dec-23	27-Dec-23	-88

**KD08 (Section 4) (incl. BP for KD04 (Stage 4-1) & SSHP in KD09 (Section 5))**

**BP**

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float

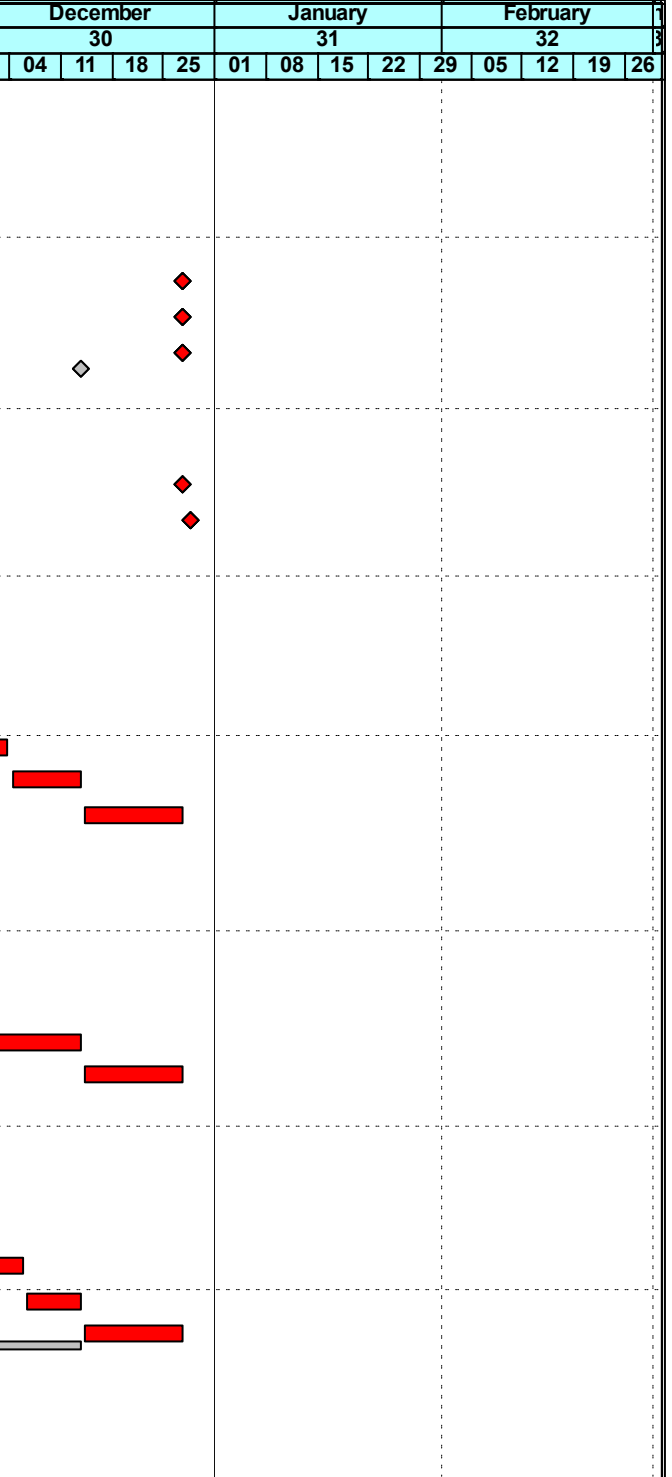



Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	December				January				February				March			
								30				31				32				33			
								0	27	04	11	18	25	01	08	15	22	29	05	12	19	26	04

**Piling for Integrated Basement and U/G Road in Zone 2B & 2C**

**Contract Dates**

**Key Dates**

**KD for Zone 2B**

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float
KD05	KD05 (Section 1) - 03 Jan 2023		13-Jul-23	0		27-Dec-23*	-358
KD06	KD06 (Section 2) - 12 Jun 2023		13-Sep-23	0		27-Dec-23*	-198
KD07	KD07 (Section 3) - 30 Sep 2023		13-Dec-23	0		27-Dec-23*	-88

**KD for Zone 2C**

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float
KD08	KD08 (Section 4) - 23 May 2023		13-Aug-23	0		27-Dec-23*	-218
KD09	KD09 (Section 5) - 12 Jun 2023		14-Oct-23	0		28-Dec-23*	-199

**Construction Stage**

**Pile Test**

**KD05 (Section 1) (incl. BP for KD01 (Stage1-1))**

**BP**

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float
KD05.TS.1040	Selection of Full Core by BD	19-May-23	01-Jun-23	0	23-Dec-23	23-Dec-23	-358
KD05.TS.1060	Full Core to Proof Drill	02-Jun-23	15-Jun-23	0	23-Dec-23	23-Dec-23	-358
KD05.TS.1080	Obtain BA14 Acknowledgement / Satisfaction of CA, Completion As-built Drawings, Reports & Records	16-Jun-23	13-Jul-23	5	23-Dec-23	27-Dec-23	-358

**KD06 (Section 2)**

**BP**

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float
KD06.TS.1060	Full Core to Proof Drill	03-Aug-23	16-Aug-23	30	25-Nov-23 A	24-Dec-23	-198
KD06.TS.1080	Obtain BA14 Acknowledgement / Satisfaction of CA, Completion As-built Drawings, Reports & Records	17-Aug-23	13-Sep-23	3	25-Dec-23	27-Dec-23	-198

**KD07 (Section 3) (incl. BP for KD03) (Stage 3-1)**


**BP**

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float
KD07.TS.1040	Selection of Full Core by BD	19-Oct-23	01-Nov-23	0	23-Dec-23	23-Dec-23	-88
KD07.TS.1060	Full Core to Proof Drill	02-Nov-23	15-Nov-23	0	23-Dec-23	23-Dec-23	-88
KD07.TS.1080	Obtain BA14 Acknowledgement / Satisfaction of CA, Completion As-built Drawings, Reports & Records	16-Nov-23	13-Dec-23	5	23-Dec-23	27-Dec-23	-88

**KD08 (Section 4) (incl. BP for KD04 (Stage 4-1) & SSHP in KD09 (Section 5))**

**BP**

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float
KD08.TS.1060	Full Core to Proof Drill	03-Jul-23	16-Jul-23	29	26-Nov-23 A	24-Dec-23	-218

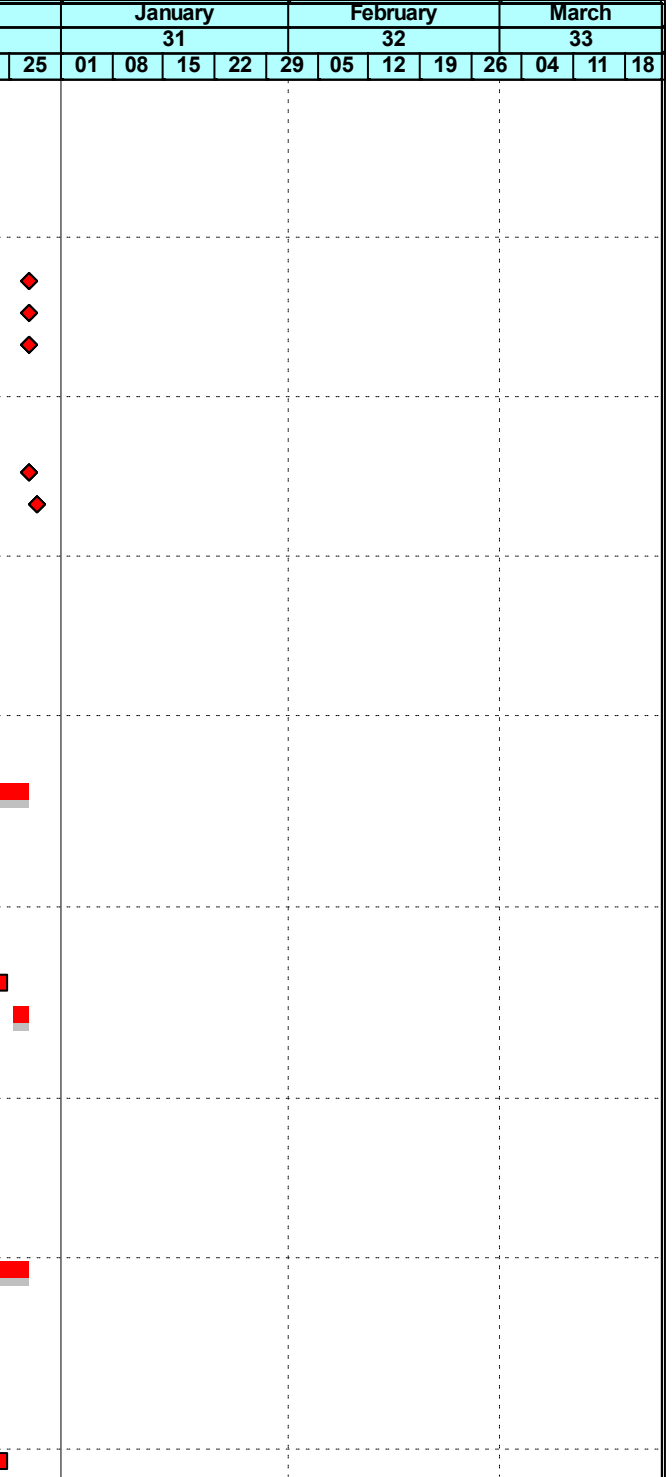




Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	December		January				February				March			April		
								28	25	31		32		33		34							
										01	08	15	22	29	05	12	19	26	04	11	18	25	01

**Piling for Integrated Basement and U/G Road in Zone 2B & 2C**

Contract Dates							
Key Dates							
KD for Zone 2B							
KD05	KD05 (Section 1) - 03 Jan 2023		13-Jul-23	0		02-Feb-24*	-395
KD06	KD06 (Section 2) - 12 Jun 2023		13-Sep-23	0		02-Feb-24*	-235
KD07	KD07 (Section 3) - 30 Sep 2023		13-Dec-23	0		23-Feb-24*	-146
KD for Zone 2C							
KD08	KD08 (Section 4) - 23 May 2023		13-Aug-23	0		02-Feb-24*	-255
KD09	KD09 (Section 5) - 12 Jun 2023		14-Oct-23	0		23-Feb-24*	-256
Construction Stage							
Pile Test							
KD05 (Section 1) (incl. BP for KD01 (Stage1-1))							
BP							
KD05.TS.1060	Full Core to Proof Drill	02-Jun-23	15-Jun-23	32	15-Dec-23 A	15-Jan-24 A	
KD05.TS.1080	Obtain BA14 Acknowledgement / Satisfaction of CA, Completion As-built Drawings, Reports & Records	16-Jun-23	13-Jul-23	14	20-Jan-24	02-Feb-24	-395
KD06 (Section 2)							
BP							
KD06.TS.1060	Full Core to Proof Drill	03-Aug-23	16-Aug-23	26	21-Dec-23 A	15-Jan-24 A	
KD06.TS.1080	Obtain BA14 Acknowledgement / Satisfaction of CA, Completion As-built Drawings, Reports & Records	17-Aug-23	13-Sep-23	14	20-Jan-24	02-Feb-24	-235
KD07 (Section 3) (incl. BP for KD03) (Stage 3-1)							
BP							
KD07.TS.1040	Selection of Full Core by BD	19-Oct-23	01-Nov-23	1	06-Jan-24 A	06-Jan-24 A	
KD07.TS.1060	Full Core to Proof Drill	02-Nov-23	15-Nov-23	12	22-Jan-24 A	02-Feb-24	-146
KD07.TS.1080	Obtain BA14 Acknowledgement / Satisfaction of CA, Completion As-built Drawings, Reports & Records	16-Nov-23	13-Dec-23	21	03-Feb-24	23-Feb-24	-146
KD08 (Section 4) (incl. BP for KD04 (Stage 4-1) & SSHP in KD09 (Section 5))							
BP							
KD08.TS.1060	Full Core to Proof Drill	03-Jul-23	16-Jul-23	58	24-Nov-23 A	20-Jan-24	-255
KD08.TS.1080	Obtain BA14 Acknowledgement / Satisfaction of CA, Completion As-built Drawings, Reports & Records	17-Jul-23	13-Aug-23	13	21-Jan-24	02-Feb-24	-255
SSHP							
KD08.TS.1180	Obtain BA14 Acknowledgement / Satisfaction of CA, Completion As-built Drawings, Reports & Records	20-Dec-22	16-Jan-23	0	20-Jan-24	20-Jan-24	-242
KD09 (Section 5) (incl. BP for KD02 (Stage 5-1))							
BP							
KD09.TS.1040	Selection of Full Core by BD	20-Aug-23	02-Sep-23	12	09-Jan-24 A	20-Jan-24	-256
KD09.TS.1060	Full Core to Proof Drill	03-Sep-23	16-Sep-23	24	10-Jan-24 A	02-Feb-24	-256
KD09.TS.1080	Obtain BA14 Acknowledgement / Satisfaction of CA, Completion As-built Drawings, Reports & Records	17-Sep-23	14-Oct-23	21	03-Feb-24	23-Feb-24	-256

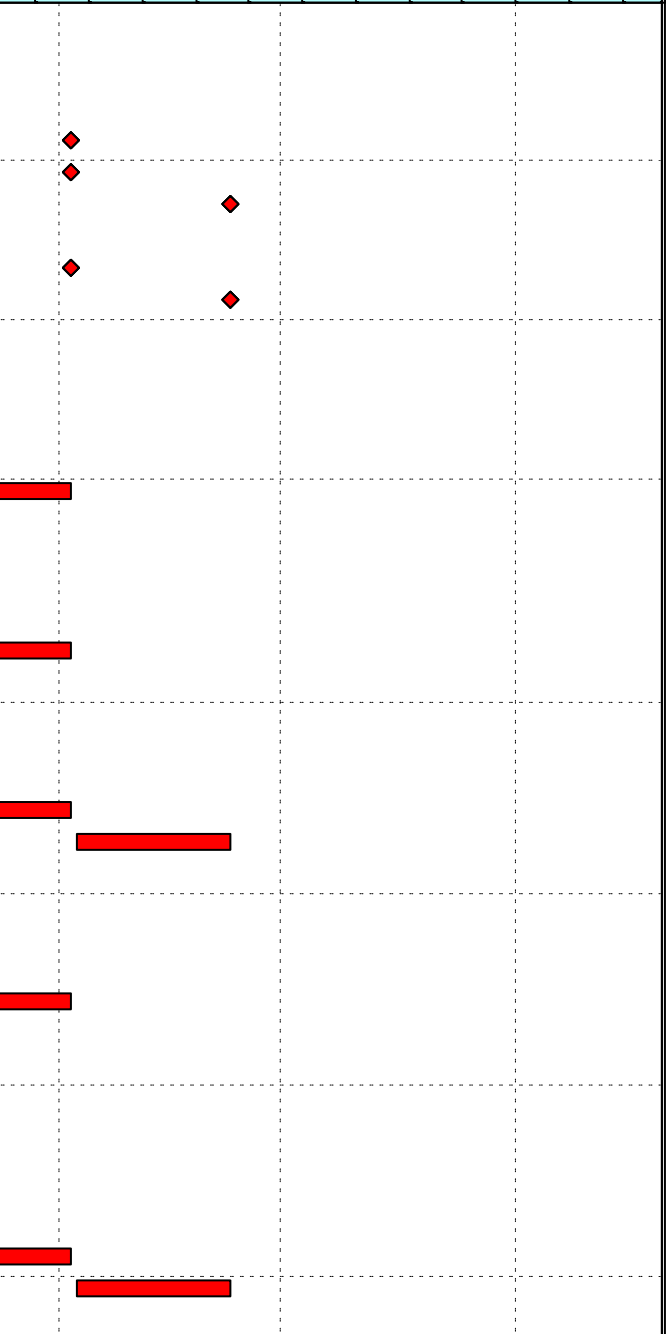

	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS



Date	Revision	Checked	Approved
04-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C
