


Zone 2B & 2C

Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	Activity % Complete	January	February	March	April	May
									5	12	19	26	03

Piling for Integrated Basement and U/G Road in Zone 2B & 2C


Contract Dates									
Key Dates									
KD for Zone 2B									
KD05	KD05 (Section 1) - 03 Jan 2023		13-Jul-23	0		06-Feb-24 A		100%	
KD06	KD06 (Section 2) - 12 Jun 2023		13-Sep-23	0		06-Feb-24 A		100%	
KD07	KD07 (Section 3) - 30 Sep 2023		13-Dec-23	0		30-Apr-24*	-213	0%	
KD for Zone 2C									
KD08	KD08 (Section 4) - 23 May 2023		13-Aug-23	0		30-Apr-24*	-343	0%	
KD09	KD09 (Section 5) - 12 Jun 2023		14-Oct-23	0		30-Apr-24*	-323	0%	

Construction Stage									
Pile Test									
KD05 (Section 1) (incl. BP for KD01 (Stage1-1))									
BP									
KD05.TS.1080	Obtain BA14 Acknowledgement (Excl. P22&P19-BP13, P23-BP01 and P23-BP08.)		16-Jun-23	13-Jul-23	1	06-Feb-24 A	06-Feb-24 A		100%
KD06 (Section 2)									
BP									
KD06.TS.1080	Obtain BA14 Acknowledgement / Satisfaction of CA, Completion As-built Drawings, Reports & Records		17-Aug-23	13-Sep-23	1	06-Feb-24 A	06-Feb-24 A		100%
KD07 (Section 3) (incl. BP for KD03) (Stage 3-1)									
BP									
KD07.TS.1060	Full Core to Proof Drill		02-Nov-23	15-Nov-23	72	22-Jan-24 A	02-Apr-24	-213	0%
KD07.TS.1080	Obtain BA14 Acknowledgement / Satisfaction of CA, Completion As-built Drawings, Reports & Records		16-Nov-23	13-Dec-23	28	03-Apr-24	30-Apr-24	-213	0%
KD08 (Section 4) (incl. BP for KD04 (Stage 4-1) & SSHP in KD09 (Section 5))									
BP									
KD08.TS.1060	Full Core to Proof Drill		03-Jul-23	16-Jul-23	131	24-Nov-23 A	02-Apr-24	-343	0%
KD08.TS.1080	Obtain BA14 Acknowledgement / Satisfaction of CA, Completion As-built Drawings, Reports & Records		17-Jul-23	13-Aug-23	28	03-Apr-24	30-Apr-24	-343	0%
SSHP									
KD08.TS.1180	Obtain BA14 Acknowledgement / Satisfaction of CA, Completion As-built Drawings, Reports & Records		20-Dec-22	16-Jan-23	1	06-Feb-24 A	06-Feb-24 A		100%
KD09 (Section 5) (incl. BP for KD02 (Stage 5-1))									
BP									
KD09.TS.1060	Full Core to Proof Drill		03-Sep-23	16-Sep-23	84	10-Jan-24 A	02-Apr-24	-323	0%
KD09.TS.1080	Obtain BA14 Acknowledgement / Satisfaction of CA, Completion As-built Drawings, Reports & Records		17-Sep-23	14-Oct-23	28	03-Apr-24	30-Apr-24	-323	0%

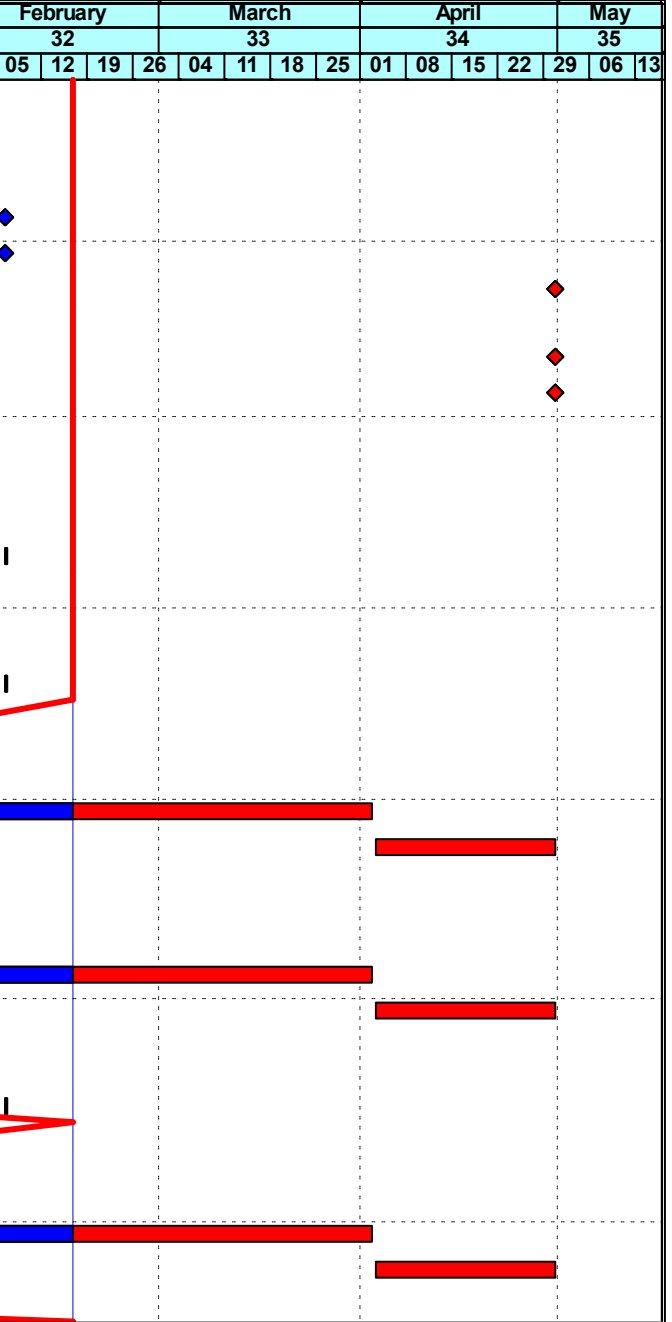







Planned	Planned MS
Critical	Critical MS
Actual	Actual MS

Date	Revision	Checked	Approved
04-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C



Activity ID	Activity Name	Baseline Start	Baseline Finish	Dur	Forecast / Actual Start	Forecast / Actual Finsih	Total Float	February		March			April				May			June					
								19	26	04	11	18	25	01	08	15	22	29	06	13	20	27	03	10	
Piling for Integrated Basement and U/G Road in Zone 2B & 2C																									
Contract Dates																									
Key Dates																									
KD for Zone 2B																									
KD07	KD07 (Section 3) - 30 Sep 2023		13-Dec-23	0		30-Apr-24*	-213																		
KD for Zone 2C																									
KD08	KD08 (Section 4) - 23 May 2023		13-Aug-23	0		30-Apr-24*	-343																		
KD09	KD09 (Section 5) - 12 Jun 2023		14-Oct-23	0		30-Apr-24*	-323																		
Construction Stage																									
Pile Test																									
KD07 (Section 3) (incl. BP for KD03) (Stage 3-1)																									
BP																									
KD07.TS.1060	Full Core to Proof Drill	02-Nov-23	15-Nov-23	72	22-Jan-24 A	02-Apr-24	-213																		
KD07.TS.1080	Obtain BA14 Acknowledgement / Satisfaction of CA, Completion As-built Drawings, Reports & Records	16-Nov-23	13-Dec-23	28	03-Apr-24	30-Apr-24	-213																		
KD08 (Section 4) (incl. BP for KD04 (Stage 4-1) & SSHP in KD09 (Section 5))																									
BP																									
KD08.TS.1060	Full Core to Proof Drill	03-Jul-23	16-Jul-23	106	24-Nov-23 A	08-Mar-24 A																			
KD08.TS.1080	Obtain BA14 Acknowledgement / Satisfaction of CA, Completion As-built Drawings, Reports & Records	17-Jul-23	13-Aug-23	46	16-Mar-24	30-Apr-24	-343																		
KD09 (Section 5) (incl. BP for KD02 (Stage 5-1))																									
BP																									
KD09.TS.1060	Full Core to Proof Drill	03-Sep-23	16-Sep-23	59	10-Jan-24 A	08-Mar-24 A																			
KD09.TS.1080	Obtain BA14 Acknowledgement / Satisfaction of CA, Completion As-built Drawings, Reports & Records	17-Sep-23	14-Oct-23	46	16-Mar-24	30-Apr-24	-323																		

	Planned		Planned MS
	Critical		Critical MS
	Actual		Actual MS



Date	Revision	Checked	Approved
04-Mar-22	R0	KL	B
02-Dec-22	R03D	KL	C
