



Development at West Kowloon Cultural District

Monthly Environmental Monitoring and Audit
(EM&A) Report for November 2016

December 2016

20/F AIA Kowloon Tower
Landmark East
100 How Ming Street
Kwun Tong
Kowloon
Hong Kong

T +852 2828 5757
F +852 2827 1823
mottmac.hk


Development at West Kowloon Cultural District

Monthly Environmental Monitoring and Audit
(EM&A) Report for November 2016

December 2016

This Monthly EM&A Report has been reviewed and certified by the Environmental Team Leader (ETL) and verified by the Independent Environmental Checker (IEC).

Certified by:




Brian Tam
Environmental Team Leader (ETL)
West Kowloon Cultural District Authority

Date

13 DEC 2016

Verified by:



Fredrick Leong
Independent Environmental Checker (IEC)
Meinhardt Infrastructure & Environment Ltd

Date

13 Dec 2016

Contents

Executive Summary	1
1 Introduction	3
1.1 Background	3
1.2 Project Organisation	3
1.3 Environmental Status in the Reporting Period	3
1.4 Summary of EM&A Requirements	4
2 Impact Monitoring Methodology	6
2.1 Introduction	6
2.2 Air Quality	6
2.2.1 Monitoring Parameters, Frequency and Duration	6
2.2.2 Monitoring Locations	6
2.2.3 Monitoring Equipment	6
2.2.4 Monitoring Methodology	7
2.3 Noise	8
2.3.1 Monitoring Parameters, Frequency and Duration	8
2.3.2 Monitoring Location	9
2.3.3 Monitoring Equipment	9
2.3.4 Monitoring Methodology	9
2.4 Landscape and Visual	10
2.4.1 Monitoring Program	10
3 Monitoring Results	11
3.1 Impact Monitoring	11
3.2 Air Quality Monitoring	11
3.2.1 1-hour TSP	11
3.2.2 24-hour TSP	11
3.3 Noise Monitoring	12
3.4 Landscape and Visual Impact	12
4 Environmental Site Inspection	13
4.1 Site Inspection	13
4.1.1 M+ Museum	13
4.1.2 Lyric Theatre Complex	15
4.2 Advice on the Solid and Liquid Waste Management Status	16
4.2.1 M+ Museum	16
4.2.2 Lyric Theatre Complex	16
4.3 Status of Environmental Licenses and Permits	17
4.3.1 M+ Museum	17

4.3.2	Lyric Theatre Complex	17
4.4	Recommended Mitigation Measures	17
4.4.1	M+ Museum	18
4.4.2	Lyric Theatre Complex	18
5	Compliance with Environmental Permit	19
6	Report in Non-compliance, Complaints, Notification of Summons and Successful Prosecutions	20
6.1	Record on Non-compliance of Action and Limit Levels	20
6.2	Record on Environmental Complaints Received	20
6.3	Record on Notifications of Summons and Successful Prosecution	20
7	Future Key Issues	21
7.1	Construction Works for the Coming Month(s)	21
7.1.1	M+ Museum	21
7.1.2	Lyric Theatre Complex	21
7.2	Key Issues for the Coming Month	21
7.2.1	M+ Museum	21
7.2.2	Lyric Theatre Complex	21
7.3	Monitoring Schedule for the Coming Month	22
8	Conclusions and Recommendations	23
8.1	Conclusions	23
8.2	Recommendations	23
Figure 1	Site Layout Plan and Monitoring Stations	24
Appendices		25
A.	Project Organisation	26
B.	Tentative Construction Programme	27
C.	Action and Limit Levels for Construction Phase	28
D.	Event and Action Plan for Air Quality, Noise, Landscape and Visual Impact	29
E.	Monitoring Schedule	30
F.	Calibration Certifications	31
G.	Graphical Plots of the Monitoring Results	32

H.	Meteorological Data Extracted from Hong Kong Observatory	33
I.	Waste Flow table	34
J.	Environmental Mitigation Measures – Implementation Status	35
K.	Cumulative Statistics on Complaints, Notifications of Summons and Successful Prosecutions	36

Executive Summary

Mott MacDonald Hong Kong Limited (MMHK) was commissioned to undertake the Environmental Team (ET) services (including environmental monitoring and audit (EM&A)) for the construction of M+ Museum Main Works (Contract No.: CC/2015/3A/022) and Lyric Theatre Complex Foundation Works (Contract No.: CC/2015/3A/014) at West Kowloon Cultural District (WKCD) (The Project) as part of the WKCD development. The Project Proponent is the West Kowloon Cultural District Authority (WKDA). The construction works and EM&A programme for M+ Museum and Lyric Theatre Complex commenced on 31 October 2015 and 1 March 2016 respectively.

The overall works for the WKCD fall under two separate categories of Designated Project (DP) of the Environmental Impact Assessment Ordinance (EIAO), namely an “engineering feasibility study of urban development projects with a study area covering more than 20 ha or involving a total population of more than 100 000” (Item 3 of Schedule 3) and “an underpass more than 100m in length under the built areas” (Item A.9, Part I, Schedule 2). An Environmental Permit No. EP-453/2013/B (EP) was issued with respect to the “Underpass Road and Austin Road Flyover Serving the West Kowloon Cultural District” which specifically includes the abovementioned category of DP under Item A.9, Part I, Schedule 2 of the EIAO.

This Monthly EM&A Report presents the monitoring works at both the main works of M+ Museum and foundation works of Lyric Theatre Complex conducted from 1 November to 30 November 2016.

Exceedance of Action and Limit Levels

There was no breach of Action or Limit levels for Air Quality (1-hour TSP and 24-hour TSP) and Noise in this reporting month.

Implementation of Mitigation Measures

Construction phase weekly site inspections were carried out on 3, 11, 17 and 24 November 2016 for M+ Museum and 2, 9, 18, 23 and 30 November 2016 for Lyric Theatre Complex to confirm the implementation measures undertaken by the Contractors in the reporting month. The outcomes are presented in Section 4 and the status of implementation of mitigation measures in the site is shown in **Appendix J**.

Landscape and visual impact inspections were conducted as part of the abovementioned weekly site inspections during the reporting month. No adverse comment on landscape and visual aspects was made during these inspections.

EPD site inspection with Contractor was conducted on 25 November 2016 at M+ Museum. No malpractice was observed.

EPD site inspection with Contractor was conducted on 3 November 2016 at Lyric Theatre Complex. No sampling, no issuance of notices nor prosecution was taken.

Record of Complaints

Two environmental complaints regarding muddy water at seafront of the Lyric Theatre Complex were recorded in the reporting month.

Record of Notification of Summons and Successful Prosecutions

No notification of summons and successful prosecution were recorded in the reporting month.

Future Key Issues

The major site works at M+ Museum scheduled to be commissioned in the coming month include:

- Excavation & ELS Works
- Basement works
- Mega truss 4 structure and mega trusses falsework
- Construction of slab
- Construction of columns & walls
- Construction of transformer room, LV switch room and water tank

The major site works at Lyric Theatre Complex scheduled to be commissioned in the coming month include:

- Pre-drilling
- Pre-grouting adjacent to Seawall
- Pipe Pile Construction
- Socket-H Pile Construction
- Bored Pile Construction

Potential environmental impacts due to the construction activities, including air quality, noise, water quality, waste, landscape and visual, will be monitored or reviewed. The recommended environmental mitigation measures shall be implemented on site and regular inspections as required will be carried out to ensure that the environmental conditions are acceptable.

1 Introduction

1.1 Background

Mott MacDonald Hong Kong Limited (MMHK) was commissioned to undertake the Environmental Team (ET) services (including environmental monitoring and audit (EM&A)) for the construction of M+ Museum Main Works (Contract No.: CC/2015/3A/022) and Lyric Theatre Complex Foundation Works (Contract No.: CC/2015/3A/014) at West Kowloon Cultural District (WKCD) (The Project) as part of the WKCD development. The Project Proponent is the West Kowloon Cultural District Authority (WKCDA). The construction works and EM&A programme for M+ Museum and Lyric Theatre Complex commenced on 31 October 2015 and 1 March 2016 respectively.

The overall works for the WKCD fall under two separate categories of Designated Project (DP) of the Environmental Impact Assessment Ordinance (EIAO), namely an “engineering feasibility study of urban development projects with a study area covering more than 20 ha or involving a total population of more than 100 000” (Item 3 of Schedule 3) and “an underpass more than 100m in length under the built areas” (Item A.9, Part I, Schedule 2). An Environmental Permit No. EP-453/2013/B (EP) was issued with respect to the “Underpass Road and Austin Road Flyover Serving the West Kowloon Cultural District” which specifically includes the abovementioned category of DP under Item A.9, Part I, Schedule 2 of the EIAO. The captioned projects include part of the abovementioned underpass road located within the site boundary also falls under this same category.

The M+ museum development aims to provide an iconic presence for the M+ museum, semi-transparent vertical plane, housing education facilities, a public restaurant and museum offices. At ground and lower levels, generous access will be provided to the park and other West Kowloon Cultural District facilities, alongside a public resource centre, theatres, retail and dining, and back-of-house functions.

The 1,200-seat Lyric Theatre Complex will be Hong Kong’s first world-class facility for dance performances, including ballet, contemporary and Chinese dance forms. In the run up to the opening of further major performing arts venues in the WKCD, it will also be used for a wide variety of performing arts events including drama, opera and musical performances. The Lyric Theatre Complex will act as a platform for Hong Kong’s leading arts organisations, and be a new major venue to show programmes from Asia and worldwide.

The Monthly EM&A Report is prepared in accordance with the Condition 3.4 of the Environmental Permit No. EP-453/2013/B. This Monthly EM&A Report presents the monitoring works at both the main works of M+ Museum and foundation works of Lyric Theatre Complex conducted from 1 November to 30 November 2016. The purpose of this report is to summarise the findings in the EM&A of the project over the reporting period.

1.2 Project Organisation

The organisation chart and lines of communication with respect to the on-site environmental management structure together with the contact information of the key personnel are shown in **Appendix A**.

1.3 Environmental Status in the Reporting Period

During the reporting period, construction works at M+ Museum undertaken include:

- Construction of slab

- Construction of columns & walls
- Construction of transformer room, LV switch room and water tank

During the reporting period, construction works at Lyric Theatre Complex undertaken include:

- Predrilling
- Pre-grouting adjacent to Seawall
- Pipe Pile Construction
- Socket-H Pile Construction
- Bored Pile Construction

The Construction Works Programmes of M+ Museum and Lyric Theatre Complex are provided in **Appendix B**. A layout plan of the Project is provided in **Figure 1**. Please refer to **Table 4.3** on the status of the environmental licenses.

1.4 Summary of EM&A Requirements

The EM&A programme requires environmental monitoring of air quality, noise, landscape and visual as specified in the approved EM&A Manual.

A summary of impact EM&A requirements is presented in **Table 1.1**.

Table 1.1: Summary of Impact EM&A Requirements

Parameters	Descriptions	Locations	Frequencies
Air Quality	24-Hour TSP	AM1 - International Commerce Centre	At least once every 6 days
	1-Hour TSP	AM1 - International Commerce Centre	At least 3 times every 6 days
	24-Hour TSP	AM2A – Austin Road West opposite to The Harbourside Tower 1	At least once every 6 days
	1-Hour TSP	AM2A – Austin Road West opposite to The Harbourside Tower 1	At least 3 times every 6 days
Noise	Leq, 30 minutes	NM1A- Podium level of The Harbourside Tower 1	Weekly
Landscape & Visual	Monitor implementation of proposed mitigation measures during the construction stage	As described in Table 9.1 and 9.2 of the EM&A Manual	Bi-weekly

Given that the Project covers only a small part of the whole WKCD area (i.e. M+ Museum, Lyric Theatre Complex and respective portions of underpass road), it was proposed that the EM&A programme for the Project should only require 1 noise monitoring station and 2 air quality monitoring stations located closest to the Project area. Currently, the works under the captioned project are confined in the western part of the WKCD site. Therefore, only the monitoring stations AM1, AM2 and NM1 were set up. Other monitoring locations are too far away (i.e. AM3 to AM5 and NM2 to NM5) are not included in this EM&A programme until the construction of the corresponding area commences.

The Harbourside management office formally rejected our proposal of setting up air quality and noise monitoring equipment on its premises at the podium level of Tower 1 (AM2/NM1) on 10 November 2015. Alternative noise monitoring location was identified at The Arch (NM2), however The Arch management office formally rejected our proposal of setting up noise monitoring equipment on its premises on 23 November 2015. Nevertheless, suitable air quality monitoring location at AM2 was identified on the ground floor in front of The Harbourside Tower 1, which is at the same location as that of baseline monitoring for consistency. No management approval is required at the ground floor for conducting the air monitoring. However, the electricity supply at AM2 was suspended from 31 August 2016 and was no longer available. In order to have a more secure electricity supply, an alternative air monitoring location (AM2A) was identified at Austin Road West opposite to The Harbourside Tower 1, which is close to Lyric Theatre Complex site entrance. This alternative air

monitoring location was approved by EPD on 28 September 2016. Noise monitoring at G/F of Harbourside will not be representative. Approval from the management office of the International Commerce Centre has been granted on 29 February 2016 for conducting noise monitoring at the alternative noise monitoring location identified at the podium floor (NM1A) which is free from screening to the construction activities. Therefore, 2 air quality monitoring stations and 1 noise impact monitoring station were confirmed for the impact monitoring.

The Environmental Quality Performance Limits for air quality and noise are shown in **Appendix C**.

The Event and Action Plan for air quality, construction noise, landscape and visual are shown in **Appendix D**.

The EM&A programme followed the recommended mitigation measures in the EM&A Manual. The EM&A requirements as well as the summary of implementation status of the environmental mitigation measures are provided in **Appendix J**.

2 Impact Monitoring Methodology

2.1 Introduction

For air quality and noise, the monitoring methodology, including the monitoring locations, monitoring equipment used, monitoring parameters, and frequency and duration etc., for air quality and noise are detailed in this Section. The environmental monitoring schedules for the reporting period and the tentative monitoring Schedule for the coming month are provided in **Appendix E**.

For landscape and audit impact, the relevant EM&A monitoring requirements and details are also presented in this Section.

2.2 Air Quality

2.2.1 Monitoring Parameters, Frequency and Duration

Table 2.1 summarizes the monitoring parameters, frequency and duration of the TSP monitoring.

Table 2.1: Air Quality Monitoring Parameters, Frequency and Duration

Parameter	Frequency	Duration
24-hour TSP	At least once in every six-days	24 hours
1-hour TSP	At least 3 times every six-days	60 minutes

2.2.2 Monitoring Locations

Currently, the works under the captioned project are confined in the western part of the WKCD site. Therefore, only the monitoring stations AM1 and AM2A were set up at the proposed locations in accordance with updated EM&A Manual. Location of the monitoring station is given in **Table 2.2** and shown in **Figure 1**.

Table 2.2: Air Quality Monitoring Station

Monitoring Station	Location
AM1	International Commerce Centre (ICC)
AM2A	Austin Road West opposite to The Harbourside Tower 1

2.2.3 Monitoring Equipment

Continuous 24-hour TSP air quality monitoring was conducted using High Volume Sampler (HVS) (Model: TE-5170) located at the designated monitoring station. The HVS meets all the requirements stated in of the EM&A Manual. Portable direct reading dust meter was used to carry out the 1-hour TSP monitoring. **Table 2.3** summarizes the equipment used in the impact air quality monitoring. Copies of the calibration certificates for the HVS, calibration kit and portable dust meters are attached in **Appendix F**.

Table 2.3: TSP Monitoring Equipment

Equipment	Model
24-hour TSP monitoring	
High Volume Sampler	TE-5170 (Serial No.: 0767 and 8919)
Calibrator	TE-5025A (Orifice I.D.: 2454)
1-hour TSP monitoring	
Portable direct reading dust meter	Sibata LD-5R (Serial No.: 620402)

Calibration of the HVS (five point calibration) using Calibration Kit was carried out every two months. The HVS calibration orifice will be calibrated annually. Calibration certificate of the TE-5025A Calibration Kit and the HVS are provided in **Appendix F**

The 1-hour TSP monitoring should be determined periodically (e.g. annually) by the HVS to check the validity and accuracy of the results measured by direct reading method.

2.2.4 Monitoring Methodology

24-hour TSP Monitoring

Installation

The HVS was installed at the site boundary. The following criteria were considered in the installation of the HVS.

- A horizontal platform with appropriate support to secure the sampler against gusty wind was provided.
- The distance between the HVS and any obstacles, such as buildings, was at least twice the height that the obstacle protrudes above the HVS.
- A minimum of 2 metres separation from walls, parapets and penthouse was required for rooftop sampler.
- A minimum of 2 metres separation from any supporting structure, measured horizontally was required.
- No furnace or incinerator flues or building vent were nearby.
- Airflow around the sampler was unrestricted.
- The sampler has been more than 20 metres from any drip line.
- Permission was obtained to set up the sampler and to obtain access to the monitoring station.
- A secured supply of electricity is needed to operate the sampler.

Preparation of Filter Papers

- Glass fibre filters were labelled and sufficient filters that were clean and without pinholes were selected.
- The filters used are specified to have a minimum collection efficiency of 99 percent for 0.3 µm (DOP) particles.
- All filters were equilibrated in the conditioning environment for 24 hours before weighing. The conditioning environment temperature was around 25 °C and not variable by more than ±3 °C with relative humidity (RH) < 50% and was not variable by more than ±5 %. A convenient working RH was 40%. All preparation of filters was done by Hong Kong Laboratory Accreditation Scheme (HOKLAS) accredited laboratory.

Field Monitoring Procedures

- The power supply was checked to ensure the HVS works properly.
- The filter holder and the area surrounding the filter were cleaned.
- The filter holder was removed by loosening the four bolts and a new filter, with stamped number upward, on a supporting screen was aligned carefully.
- The filter was properly aligned on the screen so that the gasket formed an airtight seal on the outer edges of the filter.
- The swing bolts were fastened to hold the filter holder down to the frame. The pressure applied should be sufficient to avoid air leakage at the edges.
- The shelter lid was closed and was secured with the aluminium strip.
- The HVS was warmed-up for about 5 minutes to establish run-temperature conditions.
- A new flow rate record sheet was set into the flow recorder.
- The flow rate of the HVS was checked and adjusted at around 1.3 m³/min. The range specified in the EM&A Manual was between 0.6-1.7 m³/min.

- The programmable timer was set for a sampling period of 24 hours, and the starting time, weather condition and the filter number were recorded.
- The initial elapsed time was recorded.
- At the end of sampling, the sampled filter was removed carefully and folded in half length so that only surfaces with collected particulate matter were in contact.
- It was then placed in a clean plastic envelope and sealed.
- All monitoring information was recorded on a standard data sheet.
- Filters were sent to a Hong Kong Laboratory Accreditation Scheme (HOKLAS) accredited laboratory for analysis.

Maintenance and Calibration

- The HVS and its accessories are maintained in good working condition, such as replacing motor brushes routinely and checking electrical wiring to ensure a continuous power supply.
- HVSs were calibrated upon installation and thereafter at bi-monthly intervals. The calibration kits were calibrated annually.
- Calibration records for HVS and calibration kit are shown in **Appendix F**.

1-hour TSP Monitoring

Field Monitoring

The measuring procedures of the 1-hour dust meter are in accordance with the Manufacturer's Instruction Manual as follows:

- Turn the power on.
- Close the air collecting opening cover.
- Push the "TIME SETTING" switch to [BG].
- Push "START/STOP" switch to perform background measurement for 6 seconds.
- Turn the knob at SENSI ADJ position to insert the light scattering plate.
- Leave the equipment for 1 minute upon "SPAN CHECK" is indicated in the display.
- Push "START/STOP" switch to perform automatic sensitivity adjustment. This measurement takes 1 minute.
- Pull out the knob and return it to MEASURE position.
- Setting time period of 1 hour for the 1-hour TSP measurement.
- Push "START/STOP" to start the 1-hour TSP measurement.
- Regular checking of the time period setting to ensure monitoring time of 1 hour.

Maintenance and Calibration

- The 1-hour dust meter would be checked at 3-month intervals and calibrated at 1-year intervals throughout all stages of the air quality monitoring.
- Calibration records for direct dust meters are shown in **Appendix F**.

Weather Condition

- Meteorological data extracted from Hong Kong Observatory for the reporting month is provided in **Appendix H**.

2.3 Noise

2.3.1 Monitoring Parameters, Frequency and Duration

Table 2.4 summarizes the monitoring parameters, frequency and duration of noise monitoring. The noise in A-weighted levels L_{eq} , L_{10} and L_{90} are recorded in a 30-minute interval between 0700 and 1900 hours.

Table 2.4: Noise Monitoring Parameters, Period and Frequency

Time Period	Parameters	Frequency
Daytime on normal weekdays (0700-1900 hours)	L_{eq} (30 min), L_{90} (30 min) & L_{10} (30 min)	Once every week

2.3.2 Monitoring Location

Currently, the works under the captioned project are confined in the western part of the WKCD site. Therefore, only the monitoring station NM1A was set up at the proposed location in accordance with updated EM&A Manual. Location of the monitoring station is given in **Table 2.5** and shown in **Figure 1**.

Table 2.5: Noise Monitoring Station

Monitoring Station	Location
NM1A	Podium floor of International Commerce Centre (ICC)

2.3.3 Monitoring Equipment

Integrating Sound Level Meter was used for noise monitoring. It was a Type 1 sound level meter capable of giving a continuous readout of the noise level readings including equivalent continuous sound pressure level (L_{Aeq}) and percentile sound pressure level (L_x). They comply with International Electrotechnical Commission Publications 651:1979 (Type 1) and 804:1985 (Type 1). **Table 2.6** summarizes the noise monitoring equipment model being used.

Table 2.6: Noise Monitoring Equipments

Monitoring Station	Equipment Model	
	Integrating Sound Level Meter	Calibrator
NM1A	Rion NL-18 (Serial No.00360030)	Rion NC-73 (Serial No.10997142)

2.3.4 Monitoring Methodology

Field Monitoring

- The microphone of the Sound Level Meter was set at least 1.2 m above the ground.
- Free Field measurement was made at the monitoring locations.
- The battery condition was checked to ensure the correct functioning of the meter.
- Parameters such as frequency weighting, the time weighting and the measurement time were set as follows:
 - frequency weighting: A
 - time weighting: Fast
 - time measurement: 30 minutes intervals (between 0700-1900 on normal weekdays)
- Prior to and after each noise measurement, the meter was calibrated using a Calibrator for 94 dB at 1 kHz. If the difference in the calibration level before and after measurement was more than 1 dB, the measurement would be considered invalid and has to be repeated after re-calibration or repair of the equipment.
- During the monitoring period, the L_{eq} , L_{10} and L_{90} were recorded. In addition, any site observations and noise sources were recorded on a standard record sheet.
- A correction of +3dB(A) was made to the free field measurements.

Maintenance and Calibration

- The microphone head of the sound level meter and calibrator is cleaned with soft cloth at quarterly intervals.

- The sound level meter and calibrator are sent to the supplier or HOKLAS laboratory to check and calibrate at yearly intervals.
- Calibration records are shown in **Appendix F**.

Weather Condition

- Meteorological data extracted from Hong Kong Observatory for the reporting month is provided in **Appendix H**.

2.4 Landscape and Visual

2.4.1 Monitoring Program

Table 2.7 details the monitoring program (as proposed in the WKCD EIA report) for landscape and visual impact during the construction phase.

Table 2.7: Monitoring Program for Landscape and Visual Impact during Construction Phase

Stage	Monitoring Task	Frequency	Report	Approval
Construction	Monitor implementation of proposed mitigation measures during the construction stage.	Bi-weekly	ET to report on Contractor's compliance	Counter-signed by IEC

During the landscape and visual impact monitoring, any changes in relation to the landscape and visual amenity should be monitored with reference to the baseline conditions of the site. In addition, mitigation measures were proposed in the WKCD EIA report to minimise the landscape and visual impacts during the construction phase. The proposed mitigation measures as shown in Table 9.1 and Table 9.2 of the EM&A Manual should be checked for proper implementation.

3 Monitoring Results

3.1 Impact Monitoring

Construction impact monitoring for air quality, noise and landscape and visual impact was undertaken in compliance with the EM&A Manual during the reporting month.

3.2 Air Quality Monitoring

3.2.1 1-hour TSP

Results of 1-hour TSP at the monitoring location AM1 and AM2A are summarised in **Table 3.1**. Graphical plots of the monitoring results are shown in **Appendix G**.

Table 3.1: Summary of 1-hour TSP monitoring results

Monitoring Station	Monitoring Date	Start Time	1-hour TSP ($\mu\text{g}/\text{m}^3$)			Range ($\mu\text{g}/\text{m}^3$)	Action Level ($\mu\text{g}/\text{m}^3$)	Limit Level ($\mu\text{g}/\text{m}^3$)
			1st Result	2nd Result	3rd Result			
AM1	2-Nov-16	10:40	80	88	97	49-97	273.7	500
	8-Nov-16	10:48	78	85	92			
	14-Nov-16	10:42	78	65	70			
	18-Nov-16	8:00	59	64	60			
	24-Nov-16	10:40	49	52	55			
	30-Nov-16	10:42	49	53	56			
AM2A	2-Nov-16	10:52	81	90	97	54-121	274.2	500
	8-Nov-16	11:00	80	88	96			
	14-Nov-16	10:54	109	111	121			
	18-Nov-16	8:14	69	71	77			
	24-Nov-16	10:52	63	54	58			
	30-Nov-16	10:54	60	58	59			

3.2.2 24-hour TSP

Results of 24-hour TSP at the monitoring location AM1 and AM2A are summarised in **Table 3.2**. Graphical plots of the monitoring results are shown in **Appendix G**.

Table 3.2: Summary of 24-hour TSP monitoring results

Monitoring Station	Monitoring Date	Start Time	Monitoring Results ($\mu\text{g}/\text{m}^3$)	Range ($\mu\text{g}/\text{m}^3$)	Action Level ($\mu\text{g}/\text{m}^3$)	Limit Level ($\mu\text{g}/\text{m}^3$)
AM1	2-Nov-16	10:42	44	44-52	143.6	260
	8-Nov-16	10:50	51			
	14-Nov-16	10:40	52			
	18-Nov-16	8:02	52			
	24-Nov-16	10:42	46			
	30-Nov-16	10:40	51			
AM2A	2-Nov-16	10:55	50	50-72	151.1	260
	8-Nov-16	11:02	58			
	14-Nov-16	10:52	69			

Monitoring Station	Monitoring Date	Start Time	Monitoring Results ($\mu\text{g}/\text{m}^3$)	Range ($\mu\text{g}/\text{m}^3$)	Action Level ($\mu\text{g}/\text{m}^3$)	Limit Level ($\mu\text{g}/\text{m}^3$)
	18-Nov-16	8:12	72			
	24-Nov-16	10:54	64			
	30-Nov-16	10:52	59			

No exceedance of 1-hour and 24-hour TSP (Action or Limit Level) was recorded in the reporting period.

3.3 Noise Monitoring

The construction noise monitoring results at the monitoring location NM1A are summarized in **Table 3.3**. Graphical plots of the monitoring data and the station set-up of a free-field measurement are shown in **Appendix G**.

Table 3.3: Summary of noise monitoring results during normal weekdays

Monitoring Date	Start Time	End Time	Leq (30 mins), dB(A)	Limit Level for Leq (dB(A))
2-Nov-16	14:00	14:30	69.5	
8-Nov-16	14:00	14:30	69.9	
14-Nov-16	14:00	14:30	68.4	75
24-Nov-16	14:00	14:30	68.5	
30-Nov-16	14:00	14:30	69.2	

Remarks:

+3dB (A) correction was applied to free-field measurement.

No exceedance (Action/Limit Level) of construction noise was recorded in the reporting period as no noise related environmental complaint was received during the reporting period and noise levels recorded during the monitoring period were below 75 dB(A).

Construction works were extended to holidays on 6, 13, 20 and 27 November 2016. In accordance with the EM&A Manual, additional monitoring was carried out during the restricted hours on 6, 13, 20 and 27 November 2016. The L_{eq} (5 mins) is in the range of 69.1 – 71.0 dB(A). Major noise source includes traffic. Construction Noise Permits for the works carried out during restricted hours were obtained and listed in **Table 4.3**.

3.4 Landscape and Visual Impact

Landscape and visual impact inspections were conducted as part of the weekly site inspections on 11 and 24 November 2016 for M+ Museum and 9 and 23 November 2016 for Lyric Theatre Complex during the reporting month. As reviewed by the registered Landscape Architect, no adverse comment on landscape and visual aspects was made during these inspections.

The landscape and visual mitigation measures were implemented during the reporting period. The summary of implementation status of the environmental mitigation measures are provided in **Appendix J**.

4 Environmental Site Inspection

4.1 Site Inspection

4.1.1 M+ Museum

Construction phase weekly site inspections were carried out on 3, 11, 17 and 24 November 2016. The joint site inspection with IEC, ET, ER and Contractor was held on 11 November 2016. EPD site inspection with Contractor was conducted on 25 November 2016. The discharge points, wastewater treatment facilities and the chemical waste store were inspected and no malpractice was observed. All observations have been recorded in the site inspection checklist and passed to the Contractor together with the appropriate recommended mitigation measures where necessary. The key observations from the site inspections and associated recommendations are summarized in **Table 4.1**.

Table 4.1: Summary of Site Inspections and Recommendations for M+ Museum

Inspection Date	Parameter	Observation / Recommendation	Contractor's Responses / Action(s) Undertaken	Close-out (Date)
28 Oct 2016	Waste management	Stagnant water/ mixture was found in the drip tray near wetsep no. 2. The contractor was reminded to remove the stagnant water in the drip tray.	The stagnant water in the drip tray near wetsep no. 2 was removed.	3 Nov 2016
28 Oct 2016	Water quality	Effluent quality at ICP discharge point and all wetseps at M+ was checked. They were visually clear when comparing with the standard solution except wetsep no. 6 and all were within acceptable pH range. The contractor was reminded to enhance the wastewater treatment. The pH meter at wetsep no. 2 was found not function properly and the contractor has called the supplier to replace the pH meter.	On 3 Nov 2016, the treated wastewater at wetsep no. 2 and 6 was found clear. The pH meter of wetsep no.2 was not functioning properly. On 11 Nov 2016, the pH meter of wetsep no. 2 was replaced and would function properly.	11 Nov 2016
28 Oct 2016	Waste management	Contaminated soil was found near Gate 1. The contractor was reminded to remove the contaminated soil and treat it as chemical waste.	The contaminated soil near gate 1 was removed.	3 Nov 2016
3 Nov 2016	Waste management	The drip tray near CSO and at wetsep no. 6 was filled with mixture of stagnant water and chemicals. The contractor was reminded to clear the mixture and treat as chemical waste.	On 11 Nov 2016, the contractor has cleared the drip tray at wetsep no. 6, while the drip tray near CSO was still observed with mixture of stagnant water. The contractor was reminded to clear the drip tray and treat it as chemical waste. On 23 Nov 2016, The contractor has cleaned up the drip tray of chemical drum near CSO.	23 Nov 2016
3 Nov 2016	Air quality	Area near gate 1 was observed dry. The contractor was reminded to increase water spraying frequency at that area.	The contractor has enhanced water spraying frequency at area near Gate 1.	11 Nov 2016
3 Nov 2016	Noise	Noise emission label was missing in a generator at area A10a. The contractor was reminded to place	The contractor has provided the QPME noise emission label for the generator at A10a.	24 Nov 2016

Inspection Date	Parameter	Observation / Recommendation	Contractor's Responses / Action(s) Undertaken	Close-out (Date)
		the label properly.		
3 Nov 2016	Waste management	Chemical containers were found without drip tray near CSO. The contractor was reminded to provide drip tray to all the chemicals.	The chemical containers previously observed without drip tray near CSO were removed/ provided with drip tray.	11 Nov 2016
3 Nov 2016	Water quality	Effluent quality at ICP discharge point and all wetseps at M+ was checked. They were visually clear when comparing with the standard solution.	N/A	N/A
11 Nov 2016	Waste management	Refuse was observed idled near wetsep no.5. The contractor was reminded to remove the refuse regularly.	The contractor has removed the refuse near wetsep no.5.	17 Nov 2016
11 Nov 2016	Waste management	Some chemical containers were observed without drip tray near DCS. The contractor was reminded to remove them off site or provide drip tray.	The contractor has removed the chemical containers previously observed without drip tray near DCS.	17 Nov 2016
11 Nov 2016	Waste management	Chemical store at ICP was observed without lock. The contractor was reminded to provide lock for chemical store.	The contractor has provided lock for the chemical store at ICP.	23 Nov 2016
11 Nov 2016	Water quality	Effluent quality at ICP sampling point and all wetseps at M+ was checked. They were all visually clear when comparing with the standard solution and in proper pH range.	N/A	N/A
17 Nov 2016	Air quality	The contractor was reminded to enhance water spraying near wetsep no.5 to reduce dust impact.	The contractor has enhanced water spraying at area near wetsep. no. 5 and the ground was observed wet.	24 Nov 2016
17 Nov 2016	Waste management	The contractor was reminded to improve the access to chemical store near CSO.	Follow-up status will be provided in the next reporting month	On-going
17 Nov 2016	Waste management	Chemical containers/ drums were observed without drip tray in some of the site areas. The contractor was reminded to provide drip tray or remove them off site.	The contractor has removed the chemical containers/ drum previously observed without drip tray.	23 Nov 2016
17 Nov 2016	Waste management	Chemical waste/ oil leakage and contaminated soil was observed in some of the site areas. The contractor was reminded to remove them and treat them as chemical waste.	The contractor has removed the chemical leakage and contaminated soil previously observed.	23 Nov 2016
17 Nov 2016	Air quality	Cement and base plaster at A10a was not covered. The contractor was reminded to well cover them to reduce dust impact.	The contractor has well covered the base plaster and removed the cement bags off site.	23 Nov 2016
17 Nov 2016	Water quality	Effluent quality at ICP sampling point and all wetseps at M+ was checked. They were all visually clear when compared to standard solution and within proper pH range.	N/A	N/A
24 Nov 2016	Waste management	Stagnant water/ mixture of chemical waste was observed in drip trays near CSO, DCS and wetsep no. 2. The contractor was reminded to clean the drip tray and treat it as chemical waste.	The contractor has cleared the drip trays.	30 Nov 2016
24 Nov 2016	Waste	Oil stain was found near B1	The contractor has removed the oil	30 Nov 2016

Inspection Date	Parameter	Observation / Recommendation	Contactor's Responses / Action(s) Undertaken	Close-out (Date)
	management	(workers resting area). The contractor was reminded to remove the oil stain and treat it as chemical waste.	stain on the ground near B1.	
24 Nov 2016	Waste management	Construction waste was found in B2. The contractor was reminded to remove the construction waste.	The contractor has removed the construction waste found in B2.	30 Nov 2016
24 Nov 2016	Water quality	Effluent quality at ICP sampling point and wetseps at M+ was checked. They were all visually clear when compared to standard solution and within proper pH range. The contractor was reminded to enhance maintenance and clean up at wetseps as very fine suspended particles were found in wetsep systems.	Follow-up status will be provided in the next reporting month	On-going

4.1.2 Lyric Theatre Complex

Construction phase weekly site inspections were carried out on 2, 9, 18, 23 and 30 November 2016. The joint site inspection with IEC, ET, ER and Contractor was held on 18 November 2016. EPD site inspection with Contractor was conducted on 3 November 2016. The sea-wall of the harbour was inspected and muddy water found during the inspection. All observations have been recorded in the site inspection checklist and passed to the Contractor together with the appropriate recommended mitigation measures where necessary. The key observations from the site inspections and associated recommendations are summarized in **Table 4.2**.

Table 4.2: Summary of Site Inspections and Recommendations for Lyric Theatre Complex

Inspection Date	Parameter	Observation / Recommendation	Contactor's Responses / Action(s) Undertaken	Close-out (Date)
2 Nov 2016	Waste management	The drip tray of an air compressor near area L07 was filled with mixture of chemical and algae. The contractor was reminded to clean the drip tray and treat as chemical waste.	The drip tray of an air compressor near area L07 was cleaned.	5 Nov 2016
2 Nov 2016	Air quality	Area L07 was observed dry. The contractor was reminded to increase water spraying frequency at that area.	Regular water spraying at area L07 was undertaken.	5 Nov 2016
2 Nov 2016	Waste management	An oil drum was found without drip tray near area L04. The contractor was reminded to provide drip tray to all the chemicals.	The oil drum has been removed.	5 Nov 2016
9 Nov 2016	Water quality	Turbid wastewater was observed at both wetseps on-site. The contractor was reminded to review the wastewater treatment process.	Wetseps were cleaned and treated wastewater was observed to be clear.	10 Nov 2016
9 Nov 2016	Noise	The panel of the power pack near site office was open. The contractor was reminded to always close the panel to reduce noise level.	Power pack was removed from the site area.	10 Nov 2016
18 Nov 2016	Water quality	The Contractor was reminded to continue monitoring the presence of surface runoff at site works near the seafront and to take the necessary mitigation measures to prevent potential overflow.	Necessary mitigation measures was taken to prevent potential overflow. Additional pumps was in placed and stagnant water was pumped away.	18 Nov 2016

Inspection Date	Parameter	Observation / Recommendation	Contractor's Responses / Action(s) Undertaken	Close-out (Date)
23 Nov 2016	Water quality	Turbid water was observed at the wetsep far from site entrance. The contractor was reminded to desludge more frequently to ensure good efficiency of wetsep.	De-sludge was arranged for the concerned treatment facility and treated effluent was observed clearer.	28 Nov 2016
23 Nov 2016	Noise	The panel of the enclosure of grout pump was found open. The contractor was reminded to close the panel of the enclosure.	The panel of the enclosure of grout pump was closed.	28 Nov 2016
23 Nov 2016	Waste management	Some chemical drums were found without drip tray. The contractor was reminded to provide drip tray or remove the chemical drums.	The chemical drums were removed to the chemical storage area.	28 Nov 2016
30 Nov 2016	Air quality	Haul road was observed a little bit dry at car park. The contractor was reminded to increase water spraying frequency.	Follow-up status will be provided in the next reporting month	On-going
30 Nov 2016	Waste management	The drip tray of air-compressor was observed full of mixture of water, oil and algae. The contractor was reminded to pump out the mixture and treat as chemical waste.	Follow-up status will be provided in the next reporting month	On-going

4.2 Advice on the Solid and Liquid Waste Management Status

The Contractors have been registered as a chemical waste producer for the Project. Construction and demolition (C&D) material sorting will be carried out on site. A sufficient number of receptacles were available for general refuse collection.

4.2.1 M+ Museum

As advised by the Contractor, 9.78 ton, 201.04 ton and 644.69 ton of inert C&D material were disposed of as public fill to Chai Wan Public Fill Barging Point, Tuen Mun Area 38 and Tseung Kwan O Area 137 Public Fill respectively, while 129.1 ton of general refuse was disposed of at SENT landfill. 88.4 ton of metals, 0.6 ton of paper/cardboard packaging, 0 ton of plastic and 63.0 ton of timber were collected by recycling contractors in the reporting month. 0 ton of inert C&D materials was reused on site. 2,384.0 ton of inert C&D materials were reused in other projects and 63.2 ton of inert C&D materials were disposed to sorting facility. 0 ton of chemical waste was collected by licensed contractors in the reporting period.

The actual amounts of different types of waste generated by the activities of construction works at M+ Museum in the reporting month are shown in **Appendix I**.

4.2.2 Lyric Theatre Complex

As advised by the Contractor, 4,415.34 ton and 8,009.37 ton of inert C&D material were disposed of as public fill to Tuen Mun Area 38 and Tseung Kwan O Area 137 respectively, while 10.2 ton of general refuse was disposed of at SENT landfill. 74.7 ton of metals, 0 ton of paper/cardboard packaging, 0 ton of plastic and 0 ton of timber were collected by recycling contractors in the reporting month. 0 ton of inert C&D materials was reused on site. 0 ton of inert C&D materials was reused in other projects. 1.4 ton of chemical wastes was collected by licensed contractors in the reporting period.

The actual amounts of different types of waste generated by the activities of construction works at Lyric Theatre Complex in the reporting month are shown in **Appendix I**.

4.3 Status of Environmental Licenses and Permits

The environmental permits, licenses, and/or notifications on environmental protection for this Project which were valid during the period are summarised in **Table 4.3** and **Table 4.4**.

4.3.1 M+ Museum

Table 4.3: Status of Environmental Submissions, Licenses and Permits for M+ Museum

Permit / License No. / Notification / Reference No.	Valid Period		Status	Remarks
	From	To		
Chemical Waste Producer Registration				
5213-217-H2913-45	05-Nov-15	--	Valid	--
Billing Account Construction Waste Disposal				
7023393	13-Oct-15	--	Account Active	--
Construction Noise Permit				
GW-RE0995-16	17-Oct-16	16-Apr-17	Cancelled on 4-Nov-16	--
GW-RE1058-16	4-Nov-16	3-May-17	Valid	--
Wastewater Discharge License				
WT00023633-2016	4-Mar-16	31-Mar-21	Valid	--
Notification under Air Pollution Control (Construction Dust) Regulation				
394083	7-Oct-15	--	Notified	--

4.3.2 Lyric Theatre Complex

Table 4.4: Status of Environmental Submissions, Licenses and Permits for Lyric Theatre Complex

Permit / License No. / Notification / Reference No.	Valid Period		Status	Remarks
	From	To		
Chemical Waste Producer Registration				
5213-217-G2347-39	17-Feb-16	--	Valid	--
Billing Account Construction Waste Disposal				
7024189	25-Jan-16	--	Account Active	--
Construction Noise Permit				
GW-RE0987-16	25-Oct-16	24-Apr-17	Cancelled on 23-Nov-16	--
GW-RE1113-16	23-Nov-16	20-May-17	Valid	--
Wastewater Discharge License				
WT00023648-2016	9-Mar-16	31-Mar-21	Valid	--
Notification under Air Pollution Control (Construction Dust) Regulation				
398075	18-Jan-16	--	Notified	--

4.4 Recommended Mitigation Measures

The EM&A programme followed the recommended mitigation measures in the EM&A Manual. The EM&A requirements as well as the summary of implementation status of the environmental mitigation measures are provided in **Appendix J**. In particular, the following mitigation measures were brought to attention during the site inspections:

4.4.1 M+ Museum

Chemical and Waste Management

- All chemical drum/ containers stored on site should be provided with drip trays.
- Chemical waste in drip trays should be frequently removed.
- All chemicals should be kept proper containers and clearly labelled.
- Good housekeeping of site should be maintained.
- Maintain access to the chemical store.
- Leakage of oil/ chemical waste on ground should be removed.

Air Quality

- Maintain high standard of housekeeping to prevent emission of fugitive dust.
- Dusty materials stored on site should be well covered to reduce dust impact.
- Enhance water spraying for haul roads to reduce dust impact.

Water Quality

- Wetsep units should be regularly checked to ensure proper function and adequate capacity of the system to treat wastewater or runoff before discharge.
- All wastewater or site runoff must be treated in wastewater treatment facilities before discharge.

Noise

- Noise labels should be provided for QPME/ PME.

4.4.2 Lyric Theatre Complex

Chemical and Waste Management

- Drip trays should be kept in good condition.
- Chemical waste in drip trays should be frequently removed and ensure no leakage of oil/ chemicals from machines.
- All chemical drums stored on site should be provided with drip trays.

Air Quality

- Enhance water spraying for haul roads to reduce dust impact.

Noise

- The panel of the power pack should be always closed.

Water Quality

- Wetsep units should be regularly checked to ensure proper function to treat wastewater or runoff before discharge.
- Mitigation measures should be provided to prevent potential site runoff flowing into the harbour.

5 Compliance with Environmental Permit

The status of the required submission under the EP during the reporting period is summarized in **Table 5.1**.

Table 5.1: Status of Submissions under the Environmental Permit

EP Condition	Submission	Submission Date
Condition 3.4	Monthly EM&A Report for August 2016	14 November 2016

6 Report in Non-compliance, Complaints, Notification of Summons and Successful Prosecutions

6.1 Record on Non-compliance of Action and Limit Levels

There was no breach of Action or Limit Levels for Air Quality and Noise monitoring in the reporting month.

6.2 Record on Environmental Complaints Received

Two environmental complaints regarding muddy water at seafront of the Lyric Theatre Complex were received this month. The complaint was handled in accordance with the EM&A Manual and relevant parties including the Engineer's Representative and IEC were informed of the complaint.

A complaint regarding muddy water appeared at seafront of Lyric Theatre in the afternoon of 3 November 2016 was referred from EPD on 4 November 2016. At 17:00 on 3 November 2016, EPD inspectors arrived at Lyric Theatre. No muddy water was found at the seafront and the nearest piling machine was not in operation. In the evening of 3 November 2016, the complainant reported muddy water was not observed at 5 p.m. but appeared again at 6 p.m. Investigation results revealed that the main construction activities carried out included construction of clutched pipe pile near seafront area. It is noticed that there are two concrete outfall structures locating near the seafront area, which might be the cause of the muddy water observed near the seafront. The piling works at the concerned area has ceased and the corresponding piling machine has been temporarily mobilized to other works front. The contractor has taken follow-up actions including carrying out additional pre-grouting which aimed to form a grout curtain screen to prevent any leaks to the harbour when carrying out piling works. The contractor has also deployed additional site staff to closely monitor the condition of the harbour.

A complaint regarding muddy water appeared at the seafront of Lyric Theatre was received on 14 November 2016. Investigation results revealed that the main construction activities carried out included construction of clutched pipe pile near the seafront area. At the concerned location, there is a small landing area with stairs. The suspected cause of the incident is leaks at the seawall. The contractor has stopped the piling works at the concerned area, mobilised the mini-piling rig for construction and installed additional pre-grout hole along the seawall area. Additional pre-grouting work at the concerned area have been carried out and frontline supervisor have been appointed to closely monitor the harbour.

The cumulative statistics on complaints were provided in **Appendix K**.

6.3 Record on Notifications of Summons and Successful Prosecution

No notifications of summons or successful prosecution were received this month. The cumulative statistics on notifications of summons and successful prosecutions were provided in **Appendix K**.

7 Future Key Issues

7.1 Construction Works for the Coming Month(s)

7.1.1 M+ Museum

The major site works scheduled to be commissioned in the coming month include:

- Excavation & ELS Works
- Basement works
- Mega truss 4 structure and mega trusses falsework
- Construction of slab
- Construction of columns & walls
- Construction of transformer room, LV switch room and water tank

7.1.2 Lyric Theatre Complex

The major site works scheduled to be commissioned in the coming month include:

- Predrilling
- Pre-grouting adjacent to Seawall
- Pipe Pile Construction
- Socket-H Pile Construction
- Bored Pile Construction

7.2 Key Issues for the Coming Month

7.2.1 M+ Museum

Key issues to be considered in the coming month include:

- Generation of dust from construction works;
- Noise impact from operating equipment and machinery on-site;
- Generation of site surface runoffs and wastewater from activities on-site;
- Management of stockpiles and slopes, particularly on rainy days;
- Sorting, recycling, storage and disposal of general refuse and construction waste; and
- Management of chemicals and avoidance of oil spillage on-site.

7.2.2 Lyric Theatre Complex

Key issues to be considered in the coming month include:

- Generation of dust from construction works;
- Noise impact from operating equipment and machinery on-site;
- Generation of site surface runoffs and wastewater from activities on-site;
- Management of stockpiles and slopes, particularly on rainy days;
- Sorting, recycling, storage and disposal of general refuse and construction waste; and
- Management of chemicals and avoidance of oil spillage on-site.

7.3 Monitoring Schedule for the Coming Month

The environmental site inspection and environmental monitoring will be continued in the coming month. Impact monitoring for air quality and noise in accordance with the approved EM&A Manual has commenced since 31 October 2015 and 5 March 2016 respectively. The tentative monitoring schedule for the coming month is shown in the **Appendix E**.

8 Conclusions and Recommendations

8.1 Conclusions

The EM&A programme as recommended in the EM&A Manual has been undertaken since the construction of M+ Museum main works commenced on 31 October 2015, and the construction of Lyric Theatre Complex foundation works commenced on 1 March 2016.

Monitoring of air quality and noise with respect to the Projects is underway. In particular, the 1-hour TSP, 24-hour TSP, noise level (as Leq, 30 minutes) under monitoring have been checked against established Action and Limit levels. There was no breach of Action and Limit Levels for 1-hour TSP, 24-hour TSP and noise in the reporting month.

Two environmental complaints regarding muddy water at seafront of the Lyric Theatre Complex and no notifications of summons or successful prosecution were received during the reporting month.

Weekly construction phase site inspections and bi-weekly landscape and visual impact inspections were conducted during the reporting month as required. It was observed that the Contractors had implemented all possible and feasible mitigation measures to mitigate the potential environmental impacts during construction phase works.

8.2 Recommendations

Potential environmental impacts due to the construction activities, including air quality, noise, water quality, waste, landscape and visual, will be monitored or reviewed. The recommended environmental mitigation measures shall be implemented on site and regular inspections as required will be carried out to ensure that the environmental conditions are acceptable.

Figure 1 Site Layout Plan and Monitoring Stations

Appendices

A.	Project Organisation	26
B.	Tentative Construction Programme	27
C.	Action and Limit Levels for Construction Phase	28
D.	Event and Action Plan for Air Quality, Noise, Landscape and Visual Impact	29
E.	Monitoring Schedule	30
F.	Calibration Certifications	31
G.	Graphical Plots of the Monitoring Results	32
H.	Meteorological Data Extracted from Hong Kong Observatory	33
I.	Waste Flow table	34
J.	Environmental Mitigation Measures – Implementation Status	35
K.	Cumulative Statistics on Complaints, Notifications of Summons and Successful Prosecutions	36

A. Project Organisation

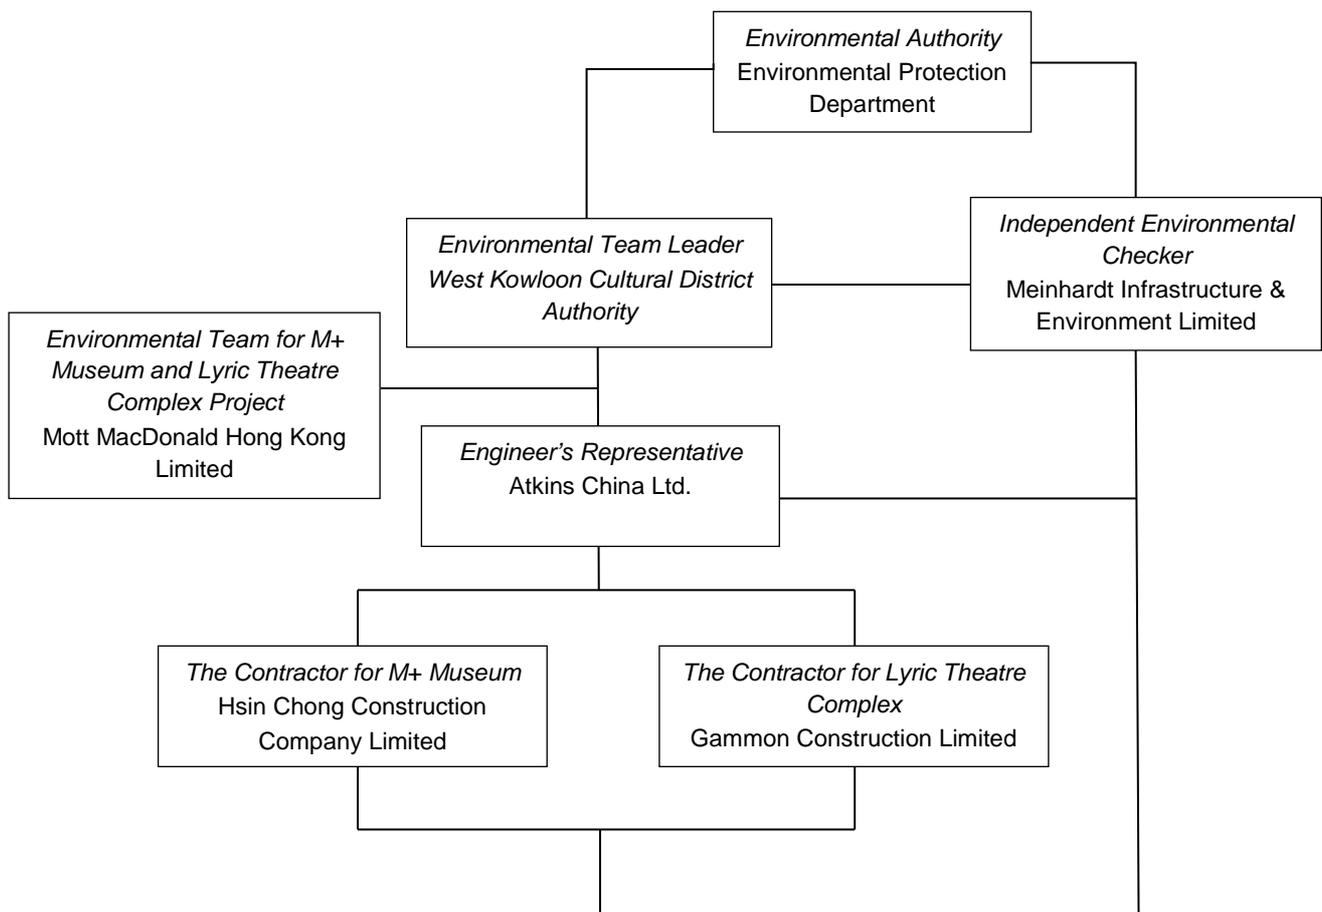


Table A-1: Contact information

Company Name	Role	Name	Telephone
Atkins China Ltd.	Senior Resident Engineer	Mr. Alfred Lee	5401 7289
Meinhardt Infrastructure & Environment Limited	IEC	Mr. Fredrick Leong	2859 1739
Hsin Chong Construction Company Limited	Environmental Manager	Mr. Leo Chow	9266 6855
Gammon Construction Limited	Environmental Manager	Ms. Michelle Tang	9267 8866
Mott MacDonald Hong Kong Ltd.	Contractor's Environmental Team Leader	Mr Brandon Wong	2828 5875
West kowloon Cultural District Authority	Senior Environmental Specialist	Mr. Brian Tam	2200 0059

B. Tentative Construction Programme

M+ Museum

(3MRP-13) Three Months Rolling Programme Status at 31 Oct 2016

Activity ID	Activity Name	Ori. Dur.	BaseLine Start	BaseLine Finish	Forecast / Actual Start	Forecast / Actual Finish	% Compl.	Finish Variance	Current Float	October 2016				November 2016				December 2016				January 2017				February 2017					
										02	09	16	23	30	06	13	20	27	04	11	18	25	01	08	15	22	29	05			
3MRP Three Months Rolling Programme Update (31 Oct 2016)																															
Contract Key Dates & Milestones																															
Contract Dates																															
CP02	Contract Period (1218 days)	1216	26-Sep-15	23-Jan-19	26-Sep-15 A	04-May-19	30%	-98	-98																						
Schedule of Milestones																															
Cost Centre A - Preliminaries and General Requirements																															
MSA.06	Compliance Review to the CA's satisfaction on Project Time & C	0		31-Oct-16		20-Oct-16 A	100%	-3		Compliance Review to the CA's satisfaction on Project Time & Construction PMg																					
MSA.07	Compliance Review to the CA's satisfaction on Project Time & C	0		31-Oct-16		20-Oct-16 A	100%	0		Compliance Review to the CA's satisfaction on Project Time & Construction PMg																					
MSA.08	Compliance Review to the CA's satisfaction on Project Time & C	0		31-Dec-16		31-Dec-16	0%	0	6	Compliance Review to the CA's																					
Cost Centre B - M+																															
MSB.03	Complete Excavation to 100% of Overall Volume of Bulk Excav.	0		21-Nov-16		21-Nov-16	0%	105	642	Complete Excavation to 100% of Overall Volume of Bulk Excav.																					
MSB.05	Complete all Columns, Structural Cores and other work necessa	0		30-Nov-16		30-Nov-16	0%	-51	634	Complete all Columns, Structural Cores and other work																					
Cost Centre C - Public Works and Tunnel Protection Works																															
MSC.02	First delivery of major Truss Steelwork elements to the Site for	0		31-Oct-16		28-Sep-16 A	100%	-3		First delivery of major Truss Steelwork elements to the Site for Trusses (t=M9)																					
MSC.04ii	Complete all Columns, Structural Cores and other work necessa	0		30-Nov-16		30-Nov-16	0%	-4	27	Complete all Columns, Structural Cores and other work																					
MSC.04i	Complete of all work necessary for commencement of erection	0		31-Dec-16		31-Dec-16	0%	-3	26	Complete of all work necessary																					
Interface Dates																															
Access Date																															
AD1380	M42 - Lyric Waterfront East of Barging Point	0	01-Oct-16		03-Oct-16 A		100%	-2		M42 - Lyric Waterfront East of Barging Point, M42 - Lyric Waterfront East of Barging Point, 03-Oct-16																					
AD1370	M41 - Lyric Waterfront at Barging Point (Part of MTR Area 3) (F	0	01-Oct-16		03-Oct-16 A		100%	-2		M41 - Lyric Waterfront at Barging Point (Part of MTR Area 3) (Following MTR Vacation of its Area 3), M																					
AD1420	M45 - At-grade Road Footpath along M+ Basement (from PIW)	0	31-Oct-16		31-Oct-16		0%	-152	194	M45 - At-grade Road Footpath along M+ Basement (from PIW) (01Jun2016), M																					
AD1530	M70 - Arts Pavilion Area on M+ side of M+ / Park Interface (t.b	0	31-Oct-16		31-Oct-16		0%	-124	817	M70 - Arts Pavilion Area on M+ side of M+ / Park Interface (t.b.a.), M70 - Arts																					
AD1410	M44 - At-grade Road Footpath at ICP / SPS Frontage (from PIW	0	31-Oct-16		31-Oct-16		0%	-152	310	M44 - At-grade Road Footpath at ICP / SPS Frontage (from PIW) (01Jun2016),																					
AD1110	M12 - Lyric Interface North (2nd access) (30Nov16)	0	09-Nov-16		09-Nov-16		0%	50	19	M12 - Lyric Interface North (2nd access) (30Nov16), M12 - Lyric Interfa																					
Vacation Date																															
VD1240	M22 - ICP/SPS Frontage within At-grade Road (H/O to PIW) (3C	0		31-Oct-16		31-Oct-16	0%	-335	-100	M22 - ICP/SPS Frontage within At-grade Road (H/O to PIW) (30Nov2015), M22																					
VD1070	M08 - Park Phase 3 Part at Waterfront (15Jun2016)	0		01-Dec-16		01-Dec-16	0%	-169	785	M08 - Park Phase 3 Part at Waterfront (15Jun2016), M																					
Interface Schedule (Refer to Interface Schedule - Appendix D1 20-Nov-2015)																															
Lyric Theatre Complex and Extended Basement (Lyric)																															
Along Interface North of AEL																															
IF1020	Complete excavation north of AEL for B2/F slab and vacate M12	0		31-Oct-16		31-Oct-16	0%	-37	28	Complete excavation north of AEL for B2/F slab and vacate M12, Complete exca																					
IF1060	Take possession of M12 for external wall construction	0	11-Jan-17		11-Jan-17		0%	-13	-44	Take possession of M12																					
Along Interface South of AEL																															
Grid 6 & 12 Area																															
IF1038	Complete Core Walls on PC96 to G/F Level	0		31-Oct-16		20-Oct-16 A	100%	-152		Complete Core Walls on PC96 to G/F Level, Complete Core Walls on PC96 to G/																					
IF1036	Complete PC109 & Basement Road Wall between PC109 & 116	0		18-Nov-16		18-Nov-16	0%	-178	798	Complete PC109 & Basement Road Wall between PC109 & 116 to																					
IF1039	Complete Basement Road Wall between PC96, 103 & 105 to G/	0		17-Dec-16		17-Dec-16	0%	-203	769	Complete Basement Road Wall between PC																					
IF1034	Complete External Wall from B1/F to G/F Level between Grid 6	0		12-Jan-17		12-Jan-17	0%	-199	743	Complete External Wa																					
PIW Phase 1																															

- ◆ Baseline Milestone
- ◆ Milestone
- ◆ Non-Critical
- Critical Bar
- Actual Work

West Kowloon Cultural District Authority
**(3MRP-13) Three Months Rolling Programme
 Status at 31 Oct 2016**



CMWP-12			
Date	Revision	Checked	Approved
14-Jul-16	(CMWP-09) Monthly Update Status at 30 June 2016	Jojo	Ricky Lau / Chris Chau
08-Aug-16	(CMWP-10) Monthly Update Status at 31 July 2016	Jojo	Ricky Lau / Chris Chau
08-Sep-16	(CMWP-11) Monthly Update Status at 31 Aug 2016	Jojo	Ricky Lau / Chris Chau
06-Oct-16	(CMWP-12) Monthly Update Status at 30 Sept 2016	Chris / Jojo	Ricky Lau / Chris Chau
08-Nov-16	(CMWP-13) Monthly Update Status at 31 Oct 2016	Chris / Jojo	Ricky Lau / Chris Chau

(3MRP-13) Three Months Rolling Programme Status at 31 Oct 2016

Activity ID	Activity Name	Ori. Dur.	BaseLine Start	BaseLine Finish	Forecast / Actual Start	Forecast / Actual Finish	% Compl.	Finish Variance	Current Float	October 2016				November 2016				December 2016				January 2017				February 2017	
										02	09	16	23	30	06	13	20	27	04	11	18	25	01	08	15	22	29
SUM.0040	Facade - BD Submission	180	15-Jul-16	22-Feb-17	05-Jun-16 A	18-Jul-17	15%		150																		
SUM.0070	Facade - Production Mock-Up	207	31-Oct-16	14-Jul-17	31-Oct-16	14-Jul-17	0%		6																		
SUM.0080	Facade - Performance Test Mock-Up	246	31-Oct-16	29-Aug-17	31-Oct-16	29-Aug-17	0%		80																		
SUM.0025	Facade Door - Shop Drawings	77	31-Oct-16	04-Feb-17	31-Oct-16	04-Feb-17	0%		-57																		
SUM.0090	Facade - Bulk Production & Fabrication	385	01-Dec-16	22-Mar-18	01-Dec-16	22-Mar-18	0%		-34																		
M+ RC Structure																											
M+ Podium																											
SUM.0100	Podium - B1/Floor Slab Structure	215	31-Mar-16	16-Dec-16	15-Mar-16 A	23-Jan-17	40%		591																		
SUM.0110	Podium - Grd/Flr Slab Structure	268	31-Oct-16	23-Sep-17	12-Oct-16 A	23-Sep-17	5%		33																		
SUM.0120	Podium - 1st/Flr Slab Structure	260	22-Nov-16	09-Oct-17	22-Nov-16	09-Oct-17	0%		382																		
SUM.0130	Podium - 1M/Flr Slab Structure	243	12-Dec-16	09-Oct-17	12-Dec-16	09-Oct-17	0%		-37																		
SUM.0140	Podium - 2nd/Flr Slab Structure	231	13-Jan-17	24-Oct-17	13-Jan-17	24-Oct-17	0%		18																		
Preliminaries																											
Pre-Construction - Design & Procurements																											
External Facade for M+ Podium (By Permasteelisa)																											
Facade Shop Drawing Submission																											
Tower Facade																											
DS.2004.08	Comment on 2nd Submission	11	02-Aug-16	13-Aug-16	01-Sep-16 A	19-Sep-16 A	100%																				
DS.2004.10	3rd Submission	10	31-Oct-16	10-Nov-16	31-Oct-16	10-Nov-16	0%		13																		
DS.2004.12	Approval	11	11-Nov-16	23-Nov-16	11-Nov-16	23-Nov-16	0%		13																		
Podium Facade																											
DS.2004.18	2nd Submission	6	31-Oct-16	05-Nov-16	31-Oct-16	05-Nov-16	0%		-66																		
DS.2004.20	Comment on 2nd Submission	11	07-Nov-16	18-Nov-16	07-Nov-16	18-Nov-16	0%		-66																		
DS.2004.22	3rd Submission	6	19-Nov-16	25-Nov-16	19-Nov-16	25-Nov-16	0%		-66																		
DS.2004.24	Approval	12	26-Nov-16	09-Dec-16	26-Nov-16	09-Dec-16	0%		-66																		
Glass Wall with T Mullion (Kinked & Straight B1/F & G/F),CW-01a to 03d																											
DS.2004.26	1st Submission	8	31-Oct-16	09-Nov-16	31-Oct-16	09-Nov-16	0%		-78																		
DS.2004.28	Comment on 1st Submission	10	10-Nov-16	22-Nov-16	10-Nov-16	22-Nov-16	0%		-78																		
DS.2004.30	2nd Submission	5	22-Nov-16	28-Nov-16	22-Nov-16	28-Nov-16	0%		-78																		
DS.2004.32	Comment on 2nd Submission	10	29-Nov-16	10-Dec-16	29-Nov-16	10-Dec-16	0%		-78																		
DS.2004.34	3rd Submission	7	10-Dec-16	19-Dec-16	10-Dec-16	19-Dec-16	0%		-78																		
DS.2004.36	Approval	12	19-Dec-16	05-Jan-17	19-Dec-16	05-Jan-17	0%		-78																		
Glass Wall with Precast Mullion & Ceramic Mullion,CW-04-05d and 07																											
DS.2004.38	1st Submission	10	31-Oct-16	10-Nov-16	31-Oct-16	10-Nov-16	0%		-57																		
DS.2004.40	Comment on 1st Submission	10	11-Nov-16	22-Nov-16	11-Nov-16	22-Nov-16	0%		-57																		
DS.2004.42	2nd Submission	6	23-Nov-16	29-Nov-16	23-Nov-16	29-Nov-16	0%		-57																		
DS.2004.44	Comment on 2nd Submission	11	01-Dec-16	13-Dec-16	01-Dec-16	13-Dec-16	0%		-57																		
DS.2004.46	3rd Submission	6	14-Dec-16	20-Dec-16	14-Dec-16	20-Dec-16	0%		-57																		
DS.2004.48	Approval	12	22-Dec-16	06-Jan-17	22-Dec-16	06-Jan-17	0%		-57																		
Podium Ceramic Concrete Tubes & with Perforated Cladding, FAC-CW-07																											
DS.2004.50	1st Submission	10	31-May-16	11-Jun-16	27-May-16 A	05-Nov-16	30%		-46																		
DS.2004.52	Comment on 1st Submission	10	08-Nov-16	18-Nov-16	08-Nov-16	18-Nov-16	0%		-46																		
DS.2004.54	2nd Submission	6	19-Nov-16	25-Nov-16	19-Nov-16	25-Nov-16	0%		-46																		

(3MRP-13) Three Months Rolling Programme Status at 31 Oct 2016

Activity ID	Activity Name	Ori. Dur.	BaseLine Start	BaseLine Finish	Forecast / Actual Start	Forecast / Actual Finish	% Compl.	Finish Variance	Current Float	October 2016					November 2016					December 2016					January 2017					February 2017									
										02	09	16	23	30	06	13	20	27	04	11	18	25	01	08	15	22	29	05											
DS.2004.656	Facade Door Package # 9 - Comment on 1st Submission	12	14-Nov-16	28-Nov-16	14-Nov-16	28-Nov-16	0%		-44																														
DS.2004.666	Facade Door Package # 9 - 2nd Submission	12	28-Nov-16	12-Dec-16	28-Nov-16	12-Dec-16	0%		-44																														
DS.2004.676	Facade Door Package # 9 - Comment on 2nd Submission	11	12-Dec-16	27-Dec-16	12-Dec-16	27-Dec-16	0%		-44																														
DS.2004.686	Facade Door Package # 9 - 3rd Submission	6	27-Dec-16	04-Jan-17	27-Dec-16	04-Jan-17	0%		-44																														
DS.2004.696	Facade Door Package # 9 - Approval	11	04-Jan-17	17-Jan-17	04-Jan-17	17-Jan-17	0%		-44																														
Facade Door Package # 10: B1/F Carriageway Access Panel / Doors (Total = 24 nos)																																							
DS.2004.706	Facade Door Package # 10 - 1st Submission	12	31-Oct-16	12-Nov-16	31-Oct-16*	12-Nov-16	0%		-57																														
DS.2004.716	Facade Door Package # 10 - Comment on 1st Submission	11	14-Nov-16	26-Nov-16	14-Nov-16	26-Nov-16	0%		-57																														
DS.2004.726	Facade Door Package # 10 - 2nd Submission	18	26-Nov-16	17-Dec-16	26-Nov-16	17-Dec-16	0%		-57																														
DS.2004.736	Facade Door Package # 10 - Comment on 2nd Submission	12	17-Dec-16	04-Jan-17	17-Dec-16	04-Jan-17	0%		-57																														
DS.2004.746	Facade Door Package # 10 - 3rd Submission	12	04-Jan-17	18-Jan-17	04-Jan-17	18-Jan-17	0%		-57																														
DS.2004.756	Facade Door Package # 10 - Approval	12	18-Jan-17	04-Feb-17	18-Jan-17	04-Feb-17	0%		-57																														
Facade Door Package # 11: CSF Bldg (Total = 2 nos)																																							
DS.2004.766	Facade Door Package # 11 - 1st Submission	12	31-Oct-16	14-Nov-16	31-Oct-16*	14-Nov-16	0%		-43																														
DS.2004.776	Facade Door Package # 11 - Comment on 1st Submission	12	14-Nov-16	28-Nov-16	14-Nov-16	28-Nov-16	0%		-43																														
DS.2004.786	Facade Door Package # 11 - 2nd Submission	11	28-Nov-16	10-Dec-16	28-Nov-16	10-Dec-16	0%		-43																														
DS.2004.796	Facade Door Package # 11 - Comment on 2nd Submission	10	10-Dec-16	23-Dec-16	10-Dec-16	23-Dec-16	0%		-43																														
DS.2004.806	Facade Door Package # 11 - 3rd Submission	6	23-Dec-16	31-Dec-16	23-Dec-16	31-Dec-16	0%		-43																														
DS.2004.816	Facade Door Package # 11 - Approval	12	31-Dec-16	16-Jan-17	31-Dec-16	16-Jan-17	0%		-43																														
Facade Door Package # 12: B1/F Smoke Vent Panel (Total = 1 no)																																							
DS.2004.826	Facade Door Package # 12 - 1st Submission	12	31-Oct-16	14-Nov-16	31-Oct-16*	14-Nov-16	0%		-45																														
DS.2004.836	Facade Door Package # 12 - Comment on 1st Submission	11	14-Nov-16	26-Nov-16	14-Nov-16	26-Nov-16	0%		-45																														
DS.2004.846	Facade Door Package # 12 - 2nd Submission	12	26-Nov-16	10-Dec-16	26-Nov-16	10-Dec-16	0%		-45																														
DS.2004.856	Facade Door Package # 12 - Comment on 2nd Submission	12	10-Dec-16	27-Dec-16	10-Dec-16	27-Dec-16	0%		-45																														
DS.2004.866	Facade Door Package # 12 - 3rd Submission	6	27-Dec-16	04-Jan-17	27-Dec-16	04-Jan-17	0%		-45																														
DS.2004.876	Facade Door Package # 12 - Approval	12	04-Jan-17	18-Jan-17	04-Jan-17	18-Jan-17	0%		-45																														
Embed BD Submission																																							
M+ Podium																																							
M+ Podium (B1/F) - Embed Submission																																							
DS.2005.10	BD Submission & Approval	60	11-Aug-16	22-Oct-16	01-Sep-16 A	15-Sep-16 A	100%																																
DS.2005.12	Preparation of BD Consent Application	5	31-Oct-16	04-Nov-16	31-Oct-16	04-Nov-16	0%		19																														
DS.2005.14	BD Consent Application	30	05-Nov-16	09-Dec-16	05-Nov-16	09-Dec-16	0%		19																														
M+ Podium (G/F to 3/F) - Embed Submission																																							
DS.2005.24	3rd Submission to RSE	3	05-Oct-16	07-Oct-16	01-Sep-16 A	15-Sep-16 A	100%																																
DS.2005.26	Preparation of BD Consent Application	6	31-Oct-16	05-Nov-16	31-Oct-16	05-Nov-16	0%		-20																														
DS.2005.28	BD Consent Application	30	07-Nov-16	10-Dec-16	07-Nov-16	10-Dec-16	0%		-20																														
M+ Tower																																							
M+ Tower (4/F to RF/F) - Embed Submission																																							
DS.2006.02	1st embed BD submission to Consultants	11	31-Oct-16	11-Nov-16	31-Oct-16	11-Nov-16	0%		-49																														
DS.2006.04	1st embed BD submission Comments	11	12-Nov-16	24-Nov-16	12-Nov-16	24-Nov-16	0%		-49																														
DS.2006.06	2nd embed BD submission to Consultants	6	25-Nov-16	01-Dec-16	25-Nov-16	01-Dec-16	0%		-49																														
DS.2006.08	RSC Submitted to BD	3	02-Dec-16	06-Dec-16	02-Dec-16	06-Dec-16	0%		-49																														
DS.2006.10	BD Submission & Approval	60	06-Dec-16	21-Feb-17	06-Dec-16	21-Feb-17	0%		-49																														
BD Submission, Consent & Approval																																							

(3MRP-13) Three Months Rolling Programme Status at 31 Oct 2016

Activity ID	Activity Name	Ori. Dur.	BaseLine Start	BaseLine Finish	Forecast / Actual Start	Forecast / Actual Finish	% Compl.	Finish Variance	Current Float	October 2016					November 2016				December 2016				January 2017				February 2017	
										02	09	16	23	30	06	13	20	27	04	11	18	25	01	08	15	22	29	05
Tower Precast Unitized Facade																												
DS.2016.12	1st BD Submission to Consultant	10	15-Jul-16	27-Jul-16	05-Jun-16 A	11-Nov-16	60%		-49	DS.2016.12, 1st BD Submission to Consultant, 1st BD Submission to																		
DS.2016.14	Comment on 1st Submission	11	12-Nov-16	24-Nov-16	12-Nov-16	24-Nov-16	0%		-49	DS.2016.14, Comment on 1st Submission																		
DS.2016.16	2nd Submission	10	25-Nov-16	06-Dec-16	25-Nov-16	06-Dec-16	0%		-49	DS.2016.16, 2nd Submission																		
DS.2016.18	Comment on 2nd Submission	11	07-Dec-16	20-Dec-16	07-Dec-16	20-Dec-16	0%		-49	DS.2016.18, Comment on 2nd Submiss																		
DS.2016.20	3rd Submission	10	20-Dec-16	03-Jan-17	20-Dec-16	03-Jan-17	0%		-49	DS.2016.20, 3rd Submission																		
DS.2016.22	Comment on 3rd Submission	12	04-Jan-17	17-Jan-17	04-Jan-17	17-Jan-17	0%		-49	DS.2016.22, Comm																		
DS.2016.24	RSE Submitted to BD	4	18-Jan-17	21-Jan-17	18-Jan-17	21-Jan-17	0%		-49	DS.2016.24, R																		
DS.2016.26	BD Submission & Approval	60	23-Jan-17	06-Apr-17	23-Jan-17	06-Apr-17	0%		-49																			
Podium Precast Unitized Facade																												
DS.2016.32	1st BD Submission to Consultant	9	31-Oct-16	09-Nov-16	31-Oct-16*	09-Nov-16	0%		4	DS.2016.32, 1st BD Submission to Consultant																		
DS.2016.34	Comment on 1st Submission	12	10-Nov-16	23-Nov-16	10-Nov-16	23-Nov-16	0%		4	DS.2016.34, Comment on 1st Submission																		
DS.2016.36	2nd Submission	9	24-Nov-16	03-Dec-16	24-Nov-16	03-Dec-16	0%		4	DS.2016.36, 2nd Submission																		
DS.2016.38	Comment on 2nd Submission	11	05-Dec-16	16-Dec-16	05-Dec-16	16-Dec-16	0%		4	DS.2016.38, Comment on 2nd Submission																		
DS.2016.40	3rd Submission	11	17-Dec-16	31-Dec-16	17-Dec-16	31-Dec-16	0%		4	DS.2016.40, 3rd Submission																		
DS.2016.42	Comment on 3rd Submission	11	03-Jan-17	14-Jan-17	03-Jan-17	14-Jan-17	0%		4	DS.2016.42, Comm																		
DS.2016.44	RSE Submitted to BD	3	16-Jan-17	19-Jan-17	16-Jan-17	19-Jan-17	0%		4	DS.2016.44, RS																		
DS.2016.46	BD Submission & Approval	60	19-Jan-17	03-Apr-17	19-Jan-17	03-Apr-17	0%		4																			
Glass Wall with T Mullion (Kinked & Straight B1/F & G/F),CW-01a-03d																												
DS.2016.52	1st BD Submission to Consultant	10	28-Dec-16	10-Jan-17	28-Dec-16	10-Jan-17	0%		-15	DS.2016.52, 1st BD Su																		
DS.2016.54	Comment on 1st Submission	11	10-Jan-17	23-Jan-17	10-Jan-17	23-Jan-17	0%		-15	DS.2016.54,																		
DS.2016.56	2nd Submission	10	23-Jan-17	07-Feb-17	23-Jan-17	07-Feb-17	0%		-15	D																		
Glass Wall with Precast Mullion & Ceramic Mullion,CW-04 to 05d and 07																												
DS.2016.72	1st BD Submission to Consultant	10	31-Oct-16	10-Nov-16	31-Oct-16*	10-Nov-16	0%		23	DS.2016.72, 1st BD Submission to Consultant																		
DS.2016.74	Comment on 1st Submission	11	11-Nov-16	24-Nov-16	11-Nov-16	24-Nov-16	0%		23	DS.2016.74, Comment on 1st Submission																		
DS.2016.76	2nd Submission	11	25-Nov-16	07-Dec-16	25-Nov-16	07-Dec-16	0%		23	DS.2016.76, 2nd Submission																		
DS.2016.78	Comment on 2nd Submission	12	08-Dec-16	22-Dec-16	08-Dec-16	22-Dec-16	0%		23	DS.2016.78, Comment on 2nd Submi																		
DS.2016.80	3rd Submission	9	23-Dec-16	04-Jan-17	23-Dec-16	04-Jan-17	0%		23	DS.2016.80, 3rd Submissio																		
DS.2016.82	Comment on 3rd Submission	11	05-Jan-17	17-Jan-17	05-Jan-17	17-Jan-17	0%		23	DS.2016.82, Comm																		
DS.2016.84	RSE Submitted to BD	3	18-Jan-17	20-Jan-17	18-Jan-17	20-Jan-17	0%		23	DS.2016.84, RS																		
DS.2016.86	BD Submission & Approval	60	21-Jan-17	04-Apr-17	21-Jan-17	04-Apr-17	0%		23																			
Podium Ceramic Concrete Tubes & with Perforated Cladding,CE01a,01b,02a																												
DS.2016.092	1st BD Submission to Consultant	9	09-Dec-16	20-Dec-16	09-Dec-16*	20-Dec-16	0%		6	DS.2016.092, 1st:BD Submission to Co																		
DS.2016.094	Comment on 1st Submission	12	20-Dec-16	06-Jan-17	20-Dec-16	06-Jan-17	0%		6	DS.2016.094, Comment o																		
DS.2016.096	2nd Submission	10	06-Jan-17	18-Jan-17	06-Jan-17	18-Jan-17	0%		6	DS.2016.096, 2r																		
DS.2016.098	Comment on 2nd Submission	12	18-Jan-17	04-Feb-17	18-Jan-17	04-Feb-17	0%		6	DS.																		
Garden Gallery Ceramic Cladding & Ceiling,CE-3a,3b,3c																												
DS.2016.112	1st BD Submission to Consultant	9	15-Dec-16	28-Dec-16	15-Dec-16*	28-Dec-16	0%		84	DS.2016.112, 1st BD Submission																		
DS.2016.114	Comment on 1st Submission	11	28-Dec-16	11-Jan-17	28-Dec-16	11-Jan-17	0%		84	DS.2016.114, Comme																		
DS.2016.116	2nd Submission	11	11-Jan-17	24-Jan-17	11-Jan-17	24-Jan-17	0%		84	DS.2016.116																		
DS.2016.118	Comment on 2nd Submission	11	24-Jan-17	09-Feb-17	24-Jan-17	09-Feb-17	0%		84																			
L3 Storefront,CW-08a,08b																												
DS.2016.132	1st BD Submission to Consultant	10	12-Nov-16	23-Nov-16	12-Nov-16	23-Nov-16	0%		185	DS.2016.132, 1st BD Submission to Consultant																		
DS.2016.134	Comment on 1st Submission	12	23-Nov-16	07-Dec-16	23-Nov-16	07-Dec-16	0%		185	DS.2016.134, Comment on 1st Submission																		

(3MRP-13) Three Months Rolling Programme Status at 31 Oct 2016

Activity ID	Activity Name	Ori. Dur.	BaseLine Start	BaseLine Finish	Forecast / Actual Start	Forecast / Actual Finish	% Compl.	Finish Variance	Current Float	October 2016					November 2016					December 2016					January 2017					February 2017				
										02	09	16	23	30	06	13	20	27	04	11	18	25	01	08	15	22	29	05						
DS.2022.48	Die Making	48	10-Dec-16	10-Feb-17	10-Dec-16	10-Feb-17	0%		-25																									
DS.2022.46	PVF2 Paint Ordering	12	10-Dec-16	24-Dec-16	10-Dec-16	24-Dec-16	0%		23																									
Podium Facade - Terracotta																																		
DS.2022.58	Ordering of Terracotta	10	10-Dec-16	22-Dec-16	10-Dec-16	22-Dec-16	0%		-66																									
DS.2022.60	Die Making of Terracotta	45	23-Dec-16	18-Feb-17	23-Dec-16	18-Feb-17	0%		-66																									
Podium Facade - Precast Concrete Facade																																		
Podium Facade - Percast Facade Die Making																																		
DS.2022.64	Percast Concrete Mould Making	45	10-Dec-16	07-Feb-17	10-Dec-16	07-Feb-17	0%		-8																									
Kinked Glass Wall with T Mullion and reflective Glass at B1,CW-02b																																		
Kinked Glass Wall with T Mullion - Ordering & Production of Material																																		
Kinked Glass Wall with T Mullion - Glass Production & Fabrication																																		
DS.2022.78	Coated Glass Production	48	31-Oct-16	27-Dec-16	31-Oct-16	27-Dec-16	0%		-19																									
DS.2022.80	Fabrication of Insulated Glass Panel	12	28-Dec-16	11-Jan-17	28-Dec-16	11-Jan-17	0%		-19																									
DS.2022.76	Sealant Ordering (Typical two weeks time, tailor made need th	12	05-Jan-17	19-Jan-17	05-Jan-17*	19-Jan-17	0%		-25																									
Kinked Glass Wall with T Mullion - Curtain Wall glazed panel production and Fabrication																																		
DS.2022.84	PVF2 Paint Ordering	12	31-Oct-16	12-Nov-16	31-Oct-16	12-Nov-16	0%		24																									
DS.2022.86	Order of Paint	24	31-Oct-16	26-Nov-16	31-Oct-16	26-Nov-16	0%		12																									
DS.2022.90	Fabrication of T Steel Mullions	17	28-Nov-16	16-Dec-16	28-Nov-16	16-Dec-16	0%		12																									
DS.2022.93	Painting of Steel Mullion	6	16-Dec-16	24-Dec-16	16-Dec-16	24-Dec-16	0%		12																									
DS.2022.82	Die Making	48	05-Jan-17	06-Mar-17	05-Jan-17	06-Mar-17	0%		-78																									
Glass Wall with Percast Concrete Mullion,CW-07																																		
Glass Wall with PC Mullion - Ordering & Production of Material																																		
Glass Production & Fabrication																																		
DS.2022.104	Sealant Ordering (Typical two weeks time, tailor made need th	12	31-Oct-16	12-Nov-16	31-Oct-16*	12-Nov-16	0%		158																									
DS.2022.106	Coated Glass Production	48	31-Oct-16	27-Dec-16	31-Oct-16*	27-Dec-16	0%		110																									
DS.2022.108	Fabrication of Insulated Glass Panel	12	07-Jan-17	20-Jan-17	07-Jan-17	20-Jan-17	0%		102																									
Glass Wall glazed panel production and Fabrication																																		
DS.2022.110	PVF2 Paint Ordering	12	31-Oct-16	12-Nov-16	31-Oct-16*	12-Nov-16	0%		152																									
DS.2022.112	Die Making	48	07-Jan-17	07-Mar-17	07-Jan-17*	07-Mar-17	0%		48																									
Precast Concrete Mullion																																		
DS.2022.120	Production Precast Concrete Moulding	24	07-Jan-17	07-Feb-17	07-Jan-17*	07-Feb-17	0%		69																									
L3 Storefront,CW-08																																		
L3 Storefront - Ordering & Production of Material																																		
Glass Production & Fabrication																																		
DS.2022.130	Sealant Ordering (Typical two weeks time, tailor made need th	12	16-Dec-16	31-Dec-16	16-Dec-16	31-Dec-16	0%		132																									
DS.2022.132	Coated Glass Production	48	16-Dec-16	16-Feb-17	16-Dec-16	16-Feb-17	0%		84																									
Glass Wall glazed panel production and Fabrication																																		
DS.2022.138	Die Making	48	16-Dec-16	16-Feb-17	16-Dec-16	16-Feb-17	0%		79																									
DS.2022.136	PVF2 Paint Ordering	12	16-Dec-16	31-Dec-16	16-Dec-16	31-Dec-16	0%		127																									
G/F Facade - Precast Concrete Tubes , Ceramic Rows Rainscreen Cladding, Ceramic Precast Mull																																		
G/F Facade - Ordering & Production of Material																																		
DS.2022.152	Sealant Ordering (Typical two weeks time, tailor made need th	12	07-Jan-17	20-Jan-17	07-Jan-17*	20-Jan-17	0%		1																									
G/F Facade - Glass Production & Fabrication																																		
DS.2022.154	Coated Glass production	48	07-Jan-17	07-Mar-17	07-Jan-17	07-Mar-17	0%		-35																									

(3MRP-13) Three Months Rolling Programme Status at 31 Oct 2016

Activity ID	Activity Name	Ori. Dur.	BaseLine Start	BaseLine Finish	Forecast / Actual Start	Forecast / Actual Finish	% Compl.	Finish Variance	Current Float	October 2016					November 2016					December 2016					January 2017					February 2017									
										02	09	16	23	30	06	13	20	27	04	11	18	25	01	08	15	22	29	05	12	19	26	01	08	15	22	29			
DS.2260.60	1st Shop Drawing Comment	11	07-Jan-17	20-Jan-17	07-Jan-17	20-Jan-17	0%		82																														
DS.2260.62	2nd Shop Drawing Submission	11	20-Jan-17	06-Feb-17	20-Jan-17	06-Feb-17	0%		82																														
Ordering & Production of Material																																							
Glass Production & Fabrication																																							
DS.2260.66	Coated Glass Production	48	15-Dec-16	16-Feb-17	15-Dec-16*	16-Feb-17	0%		85																														
Curtain Wall glazed panel production and Fabrication																																							
DS.2260.70	Die Making	48	12-Nov-16	10-Jan-17	12-Nov-16*	10-Jan-17	0%		107																														
DS.2260.72	PVF2 Paint Ordering	49	12-Nov-16	11-Jan-17	12-Nov-16*	11-Jan-17	0%		123																														
DS.2260.74	Aluminium Extrusion Production	17	11-Jan-17	02-Feb-17	11-Jan-17	02-Feb-17	0%		107																														
Bulk Ordering & Production of Material																																							
Curtain Wall glazed panel production and Fabrication																																							
DS.2260.92	Die Making	48	12-Nov-16	10-Jan-17	12-Nov-16*	10-Jan-17	0%		150																														
DS.2260.94	PVF2 Paint Ordering	49	12-Nov-16	11-Jan-17	12-Nov-16	11-Jan-17	0%		166																														
DS.2260.96	Aluminium Extrusion Production	17	11-Jan-17	02-Feb-17	11-Jan-17	02-Feb-17	0%		150																														
Glass Production & Fabrication																																							
DS.2260.102	Coated Glass Production	48	15-Dec-16	16-Feb-17	15-Dec-16*	16-Feb-17	0%		128																														
(Redland) Precast Facade for M+ Podium & CSF Bldg																																							
(Redland) General Submission																																							
(Redland) Project Quality Plan																																							
DS.3240	PQP - 2nd Submission and Approval	12	31-Oct-16	12-Nov-16	31-Oct-16	12-Nov-16	0%		-8																														
DS.3250	PQP - Approval of Project Quality Plan	0		12-Nov-16		12-Nov-16	0%		-9																														
(Redland) Production Method Statement																																							
DS.3290	PMS - 2nd Submission and Approval	12	31-Oct-16	12-Nov-16	31-Oct-16	12-Nov-16	0%		-8																														
DS.3300	PMS - Approval of Production Method Statement	0		12-Nov-16		12-Nov-16	0%		-9																														
(Redland) Drawing Submission and Approval																																							
DS.3340	2nd Submission and Approval	12	31-Oct-16	12-Nov-16	31-Oct-16	12-Nov-16	0%		-8																														
DS.3350	Approval of Schematic Design Drawings	0		12-Nov-16		12-Nov-16	0%		-9																														
(Redland) BD Submission and Approval																																							
(Redland) BD Submission																																							
DS.3420	BD Comments and review	36	31-Oct-16	10-Dec-16	31-Oct-16	10-Dec-16	0%		-32																														
DS.3410	BD Submission	0	31-Oct-16		31-Oct-16		0%		-40																														
DS.3430	Approval of BD Submission	0		10-Dec-16		10-Dec-16	0%		-37																														
(Redland) Fixing Layout for ARUP's Onward Submission to BD																																							
DS.3450	BD Comments and review	36	31-Oct-16	10-Dec-16	31-Oct-16	10-Dec-16	0%		-32																														
DS.3440	BD Submission	0	31-Oct-16		31-Oct-16		0%		-40																														
DS.3460	Approval of BD Submission	0		10-Dec-16		10-Dec-16	0%		-37																														
(Redland) Shop Drawings																																							
DS.3500	2nd Submission and Approval	12	12-Dec-16	27-Dec-16	12-Dec-16	27-Dec-16	0%		-32																														
DS.3510	Approval of Shop Drawings	0		27-Dec-16		27-Dec-16	0%		-40																														
(Redland) Bulk Production, Fabrication and Delivery																																							
DS.3520	Procurements of Materials	90	28-Dec-16	20-Apr-17	28-Dec-16	20-Apr-17	0%		-32																														
Structural Steel Trusses																																							
DS.1130	Steel Tuss - Procurement, Fabrication & Delivery	150	14-Jun-16	10-Dec-16	29-Jan-16 A	28-Nov-16	75%		-56																														
Design, Shop Dwgs, Materials, Method Statement & Welding																																							

(3MRP-13) Three Months Rolling Programme Status at 31 Oct 2016

Activity ID	Activity Name	Ori. Dur.	BaseLine Start	BaseLine Finish	Forecast / Actual Start	Forecast / Actual Finish	% Compl.	Finish Variance	Current Float	October 2016					November 2016				December 2016				January 2017				February 2017	
										02	09	16	23	30	06	13	20	27	04	11	18	25	01	08	15	22	29	05
Shop Drawings																												
DS.1030.41	Shop Drawing submission and approval of Steelwork for Shear I	117	21-Dec-15	19-May-16	21-Dec-15 A	28-Nov-16	80%		-44	DS.1030.41, Shop Drawing submission and approval of S																		
Statutory Approval Status e.g. (BD & MTRC Approval)-1																												
DS.7060b11	BD issue endorsement to ARUP	14	30-Sep-16	18-Oct-16	26-Aug-16 A	28-Nov-16	90%		-58	DS.7060b11, BD issue endorsement to ARUP, BD issue e																		
Materials Procurements																												
DS.1040	Steel Tuss - Procurement, Fabrication & Delivery	150	23-May-16	19-Nov-16	01-Oct-15 A	28-Nov-16	80%	-115	-56	DS.1040, Steel Tuss - Procurement, Fabrication & Delive																		
Fabrication & Delivery To Site																												
DS.1050	Steel Tuss - First Batch Arrival on Site (Contract Requirement -	0	31-Oct-16		31-Oct-16		0%	-152	-69	Steel Tuss - First Batch Arrival on Site (Contract Requirement - MSC.02 on 31M																		
Temporary Support System for Trusses - Proprietary & Non Proprietary System																												
DS.1040.68	Fabrication & Delivery of non-proprietary system	50	30-Jun-16	29-Aug-16	11-Jun-16 A	18-Nov-16	20%		-67	DS.1040.68, Fabrication & Delivery of non-proprietary system, F																		
Hanger Column																												
DS.1040.85	Fabrication of Hanger Column Suspended from RC	43	11-Nov-16	03-Jan-17	11-Nov-16	03-Jan-17	0%		-44	DS.1040.85, Fabrication of																		
DS.1040.80	Fabrication of Hanger Column Suspended from mega Truss	43	11-Nov-16	03-Jan-17	11-Nov-16	03-Jan-17	0%		-1	DS.1040.80, Fabrication of																		
DS.1040.86	Delivery of hanger column	0	04-Jan-17		04-Jan-17		0%		-55	Delivery of hanger column, I																		
Composite Column																												
DS.1040.91	Composite Column Fabrication	34	02-Jan-16	13-Feb-16	02-Jan-16 A	15-Nov-16	96%		-70	DS.1040.91, Composite Column Fabrication, Composite Column Fa																		
Steel Truss Support Fabrication																												
DS.1090	Steel Truss Support Fabrication for Truss 4 (*C94 & *C96)	21	15-Sep-16	12-Oct-16	19-Aug-16 A	09-Nov-16	85%		6	DS.1090, Steel Truss Support Fabrication for Truss 4 (*C94 & *C96), S																		
DS.1056	Steel Truss Support Fabrication for Truss 3 (*C85 & C86)	21	25-Aug-16	19-Sep-16	19-Aug-16 A	04-Nov-16	90%		10	DS.1056, Steel Truss Support Fabrication for Truss 3 (*C85 & C86), Steel T																		
Steel Truss Support Delivery to Site																												
DS.1050.10	Steel Truss Support @ East Core Wall for Trusses # 1, 2 & 5	0	03-Oct-16		30-Sep-16 A		100%			Steel Truss Support @ East Core Wall for Trusses # 1, 2 & 5, Steel Truss Support @ East Core Wall fo																		
DS.1130.10	Steel Truss Support for Truss # 5 (*C25)	0	31-Oct-16		24-Oct-16 A		100%			Steel Truss Support for Truss # 5 (*C25), Steel Truss Support for Truss # 5 (*C																		
DS.1055.10	Steel Truss Support for Truss # 1 & 2(Column 68 & Column 71)	0	31-Oct-16		28-Oct-16 A		100%			Steel Truss Support for Truss # 1 & 2(Column 68 & Column 71), Steel Truss Su																		
DS.1090.10	Steel Truss Support for Truss # 3 (*C85 & C86)	0	09-Nov-16		09-Nov-16		0%		8	Steel Truss Support for Truss # 3 (*C85 & C86), Steel Truss Support for																		
DS.1110.10	Steel Truss Support for Truss # 4 (*C94 & *C96)	0	15-Nov-16		15-Nov-16		0%		2	Steel Truss Support for Truss # 4 (*C94 & *C96), Steel Truss Supp																		
Steel Truss Members Fabrication																												
DS.1080	Steel Truss Fabrication for Truss # 3	69	05-May-16	28-Jul-16	23-Apr-16 A	12-Nov-16	87%		-53	DS.1080, Steel Truss Fabrication for Truss # 3, Steel Truss Fabricatio																		
DS.1070	Steel Truss Fabrication for Truss # 2	69	03-May-16	26-Jul-16	23-Apr-16 A	11-Nov-16	99%		-43	DS.1070, Steel Truss Fabrication for Truss # 2, Steel Truss Fabrication																		
DS.1060.1	Steel Truss Fabrication for Truss # 1	69	30-Apr-16	25-Jul-16	23-Apr-16 A	11-Nov-16	99%		-75	DS.1060.1, Steel Truss Fabrication for Truss # 1, Steel Truss Fabricat																		
DS.1120	Steel Truss Fabrication for Truss # 5	69	30-Apr-16	25-Jul-16	23-Apr-16 A	09-Nov-16	98%		-53	DS.1120, Steel Truss Fabrication for Truss # 5, Steel Truss Fabrication																		
DS.1100	Steel Truss Fabrication for Truss # 4	69	13-May-16	05-Aug-16	09-May-16 A	15-Nov-16	78%		10	DS.1100, Steel Truss Fabrication for Truss # 4, Steel Truss Fabrica																		
Steel Truss Members Delivery to Site																												
DS.1140.10	Steel Truss Members for Truss # 5	0	07-Oct-16		07-Oct-16 A		100%			Steel Truss Members for Truss # 5, Steel Truss Members for Truss # 5, 07-Oct-16 A, Steel Truss																		
DS.1080.10	Steel Truss Members for Truss # 2	0	27-Oct-16		28-Oct-16 A		100%			Steel Truss Members for Truss # 2, Steel Truss Members for Truss # 2, 28-Oct-16																		
DS.1070.10	Steel Truss Members for Truss # 1	0	30-Oct-16		31-Oct-16 A		100%			Steel Truss Members for Truss # 1, Steel Truss Members for Truss # 1, 31-Oct-																		
DS.1100.10	Steel Truss Members for Truss # 3	0	13-Nov-16		13-Nov-16		0%		3	Steel Truss Members for Truss # 3, Steel Truss Members for Truss #																		
DS.1120.10	Steel Truss Members for Truss # 4	0	16-Nov-16		16-Nov-16		0%		12	Steel Truss Members for Truss # 4, Steel Truss Members for Truss																		
Building Services																												
MVAC																												
DS.3070	MVAC - Shop Drawings, Materials & Method Statements Submi:	120	01-Dec-15	30-Apr-16	01-Dec-15 A	18-Nov-16	44%	-192	-18	DS.3070, MVAC - Shop Drawings, Materials & Method Statement																		
DS.3080	MVAC - CA Review & Comments	30	23-Aug-16	27-Sep-16	01-Apr-16 A	25-Nov-16	37%	-173	-18	DS.3080, MVAC - CA Review & Comments, MVAC - CA Revi																		
DS.3090	MVAC - Incorporate Comments & Resubmit	30	15-Sep-16	22-Oct-16	15-Apr-16 A	12-Dec-16	17%	-163	-18	DS.3090, MVAC - Incorporate Comments & Re																		
DS.3100	MVAC - CA Review & Approval	30	13-Oct-16	16-Nov-16	02-May-16 A	30-Dec-16	19%	-153	-18	DS.3100, MVAC - CA Review & A																		
DS.3110	MVAC - Procurement and Delivery	180	27-Oct-16	24-Apr-17	01-Sep-16 A	21-Apr-17	6%	-118	-22																			

(3MRP-13) Three Months Rolling Programme Status at 31 Oct 2016

Activity ID	Activity Name	Ori. Dur.	BaseLine Start	BaseLine Finish	Forecast / Actual Start	Forecast / Actual Finish	% Compl.	Finish Variance	Current Float	October 2016					November 2016				December 2016				January 2017				February 2017	
										02	09	16	23	30	06	13	20	27	04	11	18	25	01	08	15	22	29	05
Electrical and ELV Systems																												
DS.4120	Elect & ELV Systems - Shop Drawings and Materials Submissior	120	29-Feb-16	27-Jul-16	01-Dec-15 A	12-Nov-16	50%	-187	-52	DS.4120, Elect & ELV Systems - Shop Drawings and Materials Submi																		
DS.4130	Elect & ELV Systems - CA Review & Comments	30	01-Aug-16	03-Sep-16	01-Apr-16 A	28-Nov-16	37%	-175	-52	DS.4130, Elect & ELV Systems - CA Review & Comments																		
DS.4140	Elect & ELV Systems - Incorporate Comments & Resubmit	30	31-Aug-16	06-Oct-16	15-Apr-16 A	14-Dec-16	18%	-165	-52	DS.4140, Elect & ELV Systems - Incorporate																		
DS.4150	Elect & ELV Systems - CA Review & Approval	30	30-Sep-16	05-Nov-16	16-May-16	03-Jan-17	19%	-155	-52	DS.4150, Elect & ELV Syster																		
DS.4160	Elect & ELV Systems - Procurement and Delivery	150	04-Jan-17	02-Jun-17	04-Jan-17	02-Jun-17	0%	-190	-64																			
Fire Services																												
DS.4010	FS - Shop Drawings and Materials Submission and Approval	120	01-Dec-15	30-Apr-16	01-Dec-15 A	12-Nov-16	90%	-187	-29	DS.4010, FS - Shop Drawings and Materials Submission and Approva																		
DS.4020	FS - CA Review & Comments	30	01-Jun-16	07-Jul-16	15-Apr-16 A	28-Nov-16	85%	-175	-36	DS.4020, FS - CA Review & Comments, FS - CA Review &																		
DS.4030	FS - Incorporate Comments & Resubmit	30	02-Jul-16	06-Aug-16	22-Apr-16 A	05-Dec-16	80%	-157	-36	DS.4030, FS - Incorporate Comments & Resubmit,																		
DS.4040	FS - CA Review & Approval	30	01-Aug-16	03-Sep-16	16-May-16	12-Dec-16	75%	-139	-36	DS.4040, FS - CA Review & Approval, FS - CA																		
DS.4050	FS - Procurement and Delivery	150	13-Dec-16	11-May-17	13-Dec-16	11-May-17	0%	-118	-42																			
Plumbing and Drainage																												
DS.3010	Plumbing & Drainage - Shop Drawings, Materials & Method Stal	90	30-Dec-15	21-Apr-16	30-Dec-15 A	12-Nov-16	90%	-187	-52	DS.3010, Plumbing & Drainage - Shop Drawings, Materials & Method																		
DS.3020	Plumbing & Drainage - CA Review & Comments	30	01-Aug-16	03-Sep-16	01-Apr-16 A	28-Nov-16	85%	-175	-52	DS.3020, Plumbing & Drainage - CA Review & Comments																		
DS.3030	Plumbing & Drainage - Incorporate Comments & Resubmit	30	31-Aug-16	06-Oct-16	14-Apr-16 A	14-Dec-16	80%	-165	-52	DS.3030, Plumbing & Drainage - Incorporate																		
DS.3040	Plumbing & Drainage - CA Review & Approval	30	30-Sep-16	05-Nov-16	02-May-16	03-Jan-17	75%	-155	-52	DS.3040, Plumbing & Draina																		
DS.3050	Plumbing & Drainage - Procurement and Delivery	150	04-Jan-17	02-Jun-17	04-Jan-17	02-Jun-17	0%	-190	-64																			
Mechanical and Lifting Platform																												
DS.5210	Lifting Platform - Shop Drawings, Materials & Method Statemen	90	31-May-16	15-Sep-16	01-Dec-15 A	12-Nov-16	70%	-210	-13	DS.5210, Lifting Platform - Shop Drawings, Materials & Method State																		
DS.5220	Lifting Platform - CA Review & Comments	30	30-Sep-16	05-Nov-16	15-Apr-16 A	26-Nov-16	30%	-199	-13	DS.5220, Lifting Platform - CA Review & Comments, Lifting																		
DS.5230	Lifting Platform - Incorporate Comments & Resubmit	30	30-Sep-16	05-Nov-16	30-Apr-16 A	13-Dec-16	30%	-188	-13	DS.5230, Lifting Platform - Incorporate Comr																		
DS.5240	Lifting Platform - CA Review & Approval	30	12-Oct-16	15-Nov-16	16-May-16	31-Dec-16	3%	-178	-13	DS.5240, Lifting Platform - CA																		
DS.5250	Lifting Platform - Procurement and Delivery	300	01-Jan-17	27-Oct-17	01-Jan-17	27-Oct-17	0%	-217	-17																			
Lifts and Escalator																												
DS.5110	Lift & Escalator - Shop Drawings, Materials & Method Statemen	90	01-Dec-15	22-Mar-16	01-Dec-15 A	12-Nov-16	55%	-210	-56	DS.5110, Lift & Escalator - Shop Drawings, Materials & Method State																		
DS.5120	Lift & Escalator - CA Review & Comments	30	01-Aug-16	03-Sep-16	15-Apr-16 A	28-Nov-16	48%	-200	-56	DS.5120, Lift & Escalator - CA Review & Comments, Lift																		
DS.5130	Lift & Escalator - Incorporate Comments & Resubmit	30	31-Aug-16	06-Oct-16	30-Apr-16 A	14-Dec-16	45%	-189	-56	DS.5130, Lift & Escalator - Incorporate Com																		
DS.5140	Lift & Escalator- CA Review & Approval	30	30-Sep-16	05-Nov-16	16-May-16	03-Jan-17	3%	-179	-56	DS.5140, Lift & Escalator- CA																		
DS.5150	Lift & Escalator - Procurement and Delivery	300	04-Jan-17	30-Oct-17	04-Jan-17	30-Oct-17	0%	-220	-69																			
Art Lift (LT-11 & LT-13)																												
DS.5020	Art Lift - Shop Drawings, Materials & Method Statements Subm	90	01-Dec-15	22-Mar-16	01-Dec-15 A	05-Nov-16	70%	-204	-6	DS.5020, Art Lift - Shop Drawings, Materials & Method Statements Submis																		
DS.5025	Art Lift - CA Review & Comments	30	01-Aug-16	03-Sep-16	15-Apr-16 A	11-Nov-16	70%	-186	-6	DS.5025, Art Lift - CA Review & Comments, Art Lift - CA Review & Con																		
DS.5030	Art Lift - Incorporate Comments & Resubmit	54	12-Nov-16	17-Jan-17	03-Oct-16 A	31-Dec-16	70%	-202	-6	DS.5030, Art Lift																		
DS.5040	Art Lift - CA Review & Approval	30	03-Jan-17	09-Feb-17	03-Jan-17	09-Feb-17	0%	-208	-6																			
ABWF and Fitout																												
Ceramic Tile																												
DS.6010	Ceramic Tile - Shop Drawings, Materials Sample Submission	90	30-Nov-15	21-Mar-16	30-Nov-15 A	09-Nov-16	90%	-207	16	DS.6010, Ceramic Tile - Shop Drawings, Materials Sample Submission,																		
DS.6020	Ceramic Tile - CA Review & Comments	30	10-Nov-16	14-Dec-16	10-Nov-16	14-Dec-16	0%	-215	16	DS.6020, Ceramic Tile - CA Review & Comm																		
DS.6030	Ceramic Tile - Incorporate Comments & Resubmit	30	15-Dec-16	21-Jan-17	15-Dec-16	21-Jan-17	0%	-220	16	DS.6030, Cera																		
DS.6040	Ceramic Tile - CA Review & Approval	30	23-Jan-17	01-Mar-17	23-Jan-17	01-Mar-17	0%	-226	16																			
Soft and Hard Landscaping																												
DS.7010	Landscaping - Shop Drawings, Materials & Method Statements	90	31-Oct-16	18-Feb-17	31-Oct-16	18-Feb-17	0%	-177	34																			
DS.7000	Landscaping - Award Specialist Subcontractor	0	31-Oct-16		31-Oct-16		0%	-196	39	Landscaping - Award Specialist Subcontractor, Landscaping - Award Specialist S																		

(3MRP-13) Three Months Rolling Programme Status at 31 Oct 2016

Activity ID	Activity Name	Ori. Dur.	BaseLine Start	BaseLine Finish	Forecast / Actual Start	Forecast / Actual Finish	% Compl.	Finish Variance	Current Float	October 2016					November 2016					December 2016				January 2017				February 2017	
										02	09	16	23	30	06	13	20	27	04	11	18	25	01	08	15	22	29	05	
Design Detailing / Buildability Co-ordination																													
Spatial Coordination for BIM / CSD / CBWD																													
Basement																													
B00.0010	Preparation and submission for BIM / CSD / CBWD at B1/F (Tea	60	02-Oct-15	11-Dec-15	01-Oct-15 A	16-Nov-16	85%	-284	-37	B00.0010, Preparation and submission for BIM / CSD / CBWD at B1/F (Tea)																			
B00.0030	Review, resubmission and approval for BIM / CSD / CBWD at B1	30	30-Nov-15	07-Jan-16	30-Nov-15 A	02-Dec-16	20%	-275	-37	B00.0030, Review, resubmission and approval for BIM / CSD / CBWD at B1																			
M+ Podium																													
B00.0040	Preparation and submission for BIM / CSD / CBWD at G/F (Tea	60	30-Nov-15	15-Feb-16	30-Nov-15 A	03-Dec-16	70%	-251	-48	B00.0040, Preparation and submission for BIM / CSD / CBWD at G/F (Tea)																			
B00.0080	Preparation and submission for BIM / CSD / CBWD at 1M/F (Tea	60	05-Sep-16	16-Nov-16	30-Jul-16 A	28-Nov-16	80%	-201	-48	B00.0080, Preparation and submission for BIM / CSD / CBWD at 1M/F (Tea)																			
B00.0050	Preparation and submission for BIM / CSD / CBWD at 1/F (Tea	60	30-Sep-16	10-Dec-16	15-Aug-16 A	28-Nov-16	20%	-246	-25	B00.0050, Preparation and submission for BIM / CSD / CBWD at 1/F (Tea)																			
B00.0100	Review, resubmission and approval for BIM / CSD / CBWD at 1F	30	15-Oct-16	18-Nov-16	15-Aug-16 A	28-Nov-16	20%	-176	1	B00.0100, Review, resubmission and approval for BIM / CSD / CBWD at 1F																			
B00.0060	Review, resubmission and approval for BIM / CSD / CBWD at G,	30	31-Oct-16	03-Dec-16	31-Oct-16	03-Dec-16	0%	-228	12	B00.0060, Review, resubmission and approval for BIM / CSD / CBWD at G,																			
B00.0090	Preparation and submission for BIM / CSD / CBWD at 2/F (Tea	60	31-Oct-16	11-Jan-17	31-Oct-16	11-Jan-17	0%	-236	-25	B00.0090, Preparation and submission for BIM / CSD / CBWD at 2/F (Tea)																			
B00.0120	Preparation and submission for BIM / CSD / CBWD at 3/F (Tea	60	31-Oct-16	11-Jan-17	31-Oct-16	11-Jan-17	0%	-187	-48	B00.0120, Preparation and submission for BIM / CSD / CBWD at 3/F (Tea)																			
B00.0110	Review, resubmission and approval for BIM / CSD / CBWD at 2/	30	14-Nov-16	17-Dec-16	14-Nov-16	17-Dec-16	0%	-193	-12	B00.0110, Review, resubmission and approval for BIM / CSD / CBWD at 2/																			
B00.0070	Review, resubmission and approval for BIM / CSD / CBWD at 1/	30	17-Nov-16	22-Dec-16	17-Nov-16	22-Dec-16	0%	-243	-37	B00.0070, Review, resubmission and approval for BIM / CSD / CBWD at 1/																			
B00.0130	Review, resubmission and approval for BIM / CSD / CBWD at 3/	30	12-Jan-17	18-Feb-17	12-Jan-17	18-Feb-17	0%	-193	-42	B00.0130, Review, resubmission and approval for BIM / CSD / CBWD at 3/																			
M+ Tower																													
B6B.0000	Preparation and submission for BIM / CSD / CBWD at 4/F (Tea	45	31-Oct-16	22-Dec-16	31-Oct-16	22-Dec-16	0%	-184	-25	B6B.0000, Preparation and submission for BIM / CSD / CBWD at 4/F (Tea)																			
B6B.0030	Preparation and submission for BIM / CSD / CBWD at 5/F (Tea	45	31-Oct-16	22-Dec-16	31-Oct-16	22-Dec-16	0%	-136	-48	B6B.0030, Preparation and submission for BIM / CSD / CBWD at 5/F (Tea)																			
B6B.0070	Preparation and submission for BIM / CSD / CBWD at 6/F (Tea	45	06-Dec-16	02-Feb-17	06-Dec-16	02-Feb-17	0%	-129	-48	B6B.0070, Preparation and submission for BIM / CSD / CBWD at 6/F (Tea)																			
B6B.0020	Preparation and submission for BIM / CSD / CBWD at 10/F (Tea	45	06-Dec-16	02-Feb-17	06-Dec-16	02-Feb-17	0%	-179	-25	B6B.0020, Preparation and submission for BIM / CSD / CBWD at 10/F (Tea)																			
B6B.0010	Review, resubmission and approval for BIM / CSD / CBWD at 4/	20	23-Dec-16	17-Jan-17	23-Dec-16	17-Jan-17	0%	-188	16	B6B.0010, Review, resubmission and approval for BIM / CSD / CBWD at 4/																			
B6B.0060	Review, resubmission and approval for BIM / CSD / CBWD at 5/	20	23-Dec-16	17-Jan-17	23-Dec-16	17-Jan-17	0%	-140	28	B6B.0060, Review, resubmission and approval for BIM / CSD / CBWD at 5/																			
B6B.0110	Preparation and submission for BIM / CSD / CBWD at 7/F (Tea	45	14-Jan-17	10-Mar-17	14-Jan-17	10-Mar-17	0%	-124	-48	B6B.0110, Preparation and submission for BIM / CSD / CBWD at 7/F (Tea)																			
B6B.0050	Preparation and submission for BIM / CSD / CBWD at 11/F (Tea	45	14-Jan-17	10-Mar-17	14-Jan-17	10-Mar-17	0%	-173	-25	B6B.0050, Preparation and submission for BIM / CSD / CBWD at 11/F (Tea)																			
CSF Block																													
B20.0280	Preparation and submission for BIM / CSD / CBWD at G/F (Tea	45	30-Sep-16	23-Nov-16	15-Aug-16 A	13-Dec-16	10%	-214	10	B20.0280, Preparation and submission for BIM / CSD / CBWD at G/F (Tea)																			
B20.0300	Preparation and submission for BIM / CSD / CBWD at 1-5/F (Tea	60	31-Oct-16	11-Jan-17	31-Oct-16	11-Jan-17	0%	-187	10	B20.0300, Preparation and submission for BIM / CSD / CBWD at 1-5/F (Tea)																			
B20.0290	Review, resubmission and approval for BIM / CSD / CBWD at G,	20	14-Dec-16	09-Jan-17	14-Dec-16	09-Jan-17	0%	-218	101	B20.0290, Review, resubmission and approval for BIM / CSD / CBWD at G,																			
B20.0320	Preparation and submission for BIM / CSD / CBWD at 6/F (Tea	45	24-Dec-16	20-Feb-17	24-Dec-16	20-Feb-17	0%	-182	10	B20.0320, Preparation and submission for BIM / CSD / CBWD at 6/F (Tea)																			
B20.0310	Review, resubmission and approval for BIM / CSD / CBWD at 1	30	12-Jan-17	18-Feb-17	12-Jan-17	18-Feb-17	0%	-193	69	B20.0310, Review, resubmission and approval for BIM / CSD / CBWD at 1																			
Interfacing Car Park and Sewage Pumping Station (SPS)																													
D02.0010	Review, resubmission and approval for BIM / CSD / CBWD at IC	15	18-Jul-16	03-Aug-16	16-Jun-16 A	16-Nov-16	50%	-284	-30	D02.0010, Review, resubmission and approval for BIM / CSD / CBWD at IC																			
D01.0010	Review, resubmission and approval for BIM / CSD / CBWD at SF	15	18-Jul-16	03-Aug-16	16-Jun-16 A	12-Nov-16	50%	-210	-43	D01.0010, Review, resubmission and approval for BIM / CSD / CBWD at SF																			
D02.0020	Preparation and submission for BIM / CSD / CBWD at ICP G/F (45	31-Oct-16	22-Dec-16	31-Oct-16	22-Dec-16	0%	-291	101	D02.0020, Preparation and submission for BIM / CSD / CBWD at ICP G/F (
D02.0030	Review, resubmission and approval for BIM / CSD / CBWD at IC	30	06-Dec-16	12-Jan-17	06-Dec-16	12-Jan-17	0%	-282	101	D02.0030, Review, resubmission and approval for BIM / CSD / CBWD at IC																			
4D Time Management (1st Draft)																													
B00.0160	Facade works	75	31-Oct-16	01-Feb-17	31-Oct-16	01-Feb-17	0%	-251	192	B00.0160, Facade works																			
Visual Mock-Up (VMU)																													
VMU Preliminary																													
A00.3610	VMU Works Period (Contract requirement of 200 calendar days	169	02-Oct-15	29-Apr-16	01-Oct-15 A	24-Nov-16	80%	-182	76	VMU Works Period (Contract requirement of 200 calendar days)																			
VMU Construction																													
Step 2.0 - Existing Concrete Shell																													
VMU Facade Works																													

(3MRP-13) Three Months Rolling Programme Status at 31 Oct 2016

Activity ID	Activity Name	Ori. Dur.	BaseLine Start	BaseLine Finish	Forecast / Actual Start	Forecast / Actual Finish	% Compl.	Finish Variance	Current Float	October 2016				November 2016				December 2016				January 2017				February 2017	
										02	09	16	23	30	06	13	20	27	04	11	18	25	01	08	15	22	29
B10.3220	ICP - Pile Cap Construction of Area A	25	30-Jul-16	05-Sep-16	16-Jul-16 A	22-Nov-16	80%	-107	-40	B10.3220, ICP - Pile Cap Construction of Area A, ICP - Pile Ca																	
B10.3230	ICP - Pile Cap Construction of Area B	25	14-Oct-16	14-Nov-16	27-Aug-16 A	22-Nov-16	30%	-82	-33	B10.3230, ICP - Pile Cap Construction of Area B, ICP - Pile Ca																	
B10.3250	ICP - Complete Excavation & Lateral Support	0		30-Nov-16		30-Nov-16	0%	-127	-50	ICP - Complete Excavation & Lateral Support, ICP - Com																	
Structures																											
Basement Structures / Sub-Structure																											
Pilecaps																											
AEL North																											
Stage 3 - Pilecap (A4,A5,B4,B5)																											
Pilecap (A4 & A5)																											
B10.2060p	AEL North - ELS Stage 4 - Extend 1st height of basement wall	10	05-Aug-16	18-Aug-16	28-Jul-16 A	11-Nov-16	90%		-55	B10.2060p, AEL North - ELS Stage 4 - Extend 1st height of basement																	
Pilecap (B4 & B5)																											
B10.2070m	AEL North - ELS Stage 4 - Extend 1st height of basement wall	12	15-Aug-16	30-Aug-16	08-Aug-16 A	08-Nov-16	90%		-47	B10.2070m, AEL North - ELS Stage 4 - Extend 1st height of basement w																	
Stage 4 to 7: ELS & Excavation (A6, A7, A8, A9, A10, A11, A12 & B6, B7, B8, B9)																											
Pilecaps - Portion (A10a, A10b, A11 & A12)																											
Pile Cap Portion A11																											
B10.3710	AEL North - BD Stage 6 - Pile Cap Construction (Portion A11)	6	31-Oct-16	05-Nov-16	12-Sep-16 A	11-Oct-16 A	100%			B10.3710, AEL North - BD Stage 6 - Pile Cap Construction (Portion A11), A																	
B10.3720	AEL North - BD Stage 6 - Underground Drainage (Portion A11)	6	31-Oct-16	05-Nov-16	19-Sep-16 A	08-Oct-16 A	100%			B10.3720, AEL North - BD Stage 6 - Underground Drainage (Portion A11),																	
Pile Cap Portion A12																											
B10.3730	AEL North - BD Stage 6 - Pile Cap Construction (Portion A12)	6	31-Oct-16	05-Nov-16	15-Sep-16 A	21-Oct-16 A	100%			B10.3730, AEL North - BD Stage 6 - Pile Cap Construction (Portion A12), A																	
B10.3740	AEL North - BD Stage 6 - Underground Drainage (Portion A12)	6	31-Oct-16	05-Nov-16	19-Sep-16 A	08-Oct-16 A	100%			B10.3740, AEL North - BD Stage 6 - Underground Drainage (Portion A12),																	
Pilecaps - Portion B6 & B7																											
B10.3610	AEL North - BD Stage 4 - Pile Cap Construction (Portion A8, B6)	30	05-Sep-16	21-Oct-16	08-Sep-16 A	22-Sep-16 A	100%	-1		B10.3610, AEL North - BD Stage 4 - Pile Cap Construction (Portion A8, B6), AEL North																	
B10.3620	AEL North - BD Stage 5 - Underground Drainage (Portion B6)	12	30-Sep-16	20-Oct-16	12-Sep-16 A	20-Sep-16 A	100%	-17		B10.3620, AEL North - BD Stage 5 - Underground Drainage (Portion B6), AEL North - B																	
B10.3630	AEL North - BD Stage 6 - Pile Cap Construction (Portion B7)	9	14-Nov-16	23-Nov-16	14-Nov-16*	23-Nov-16	0%	-52	-20	B10.3630, AEL North - BD Stage 6 - Pile Cap Construction (P																	
B10.3640	AEL North - BD Stage 6 - Underground Drainage (Portion B7)	9	14-Nov-16	23-Nov-16	14-Nov-16	23-Nov-16	0%	-69	-14	B10.3640, AEL North - BD Stage 6 - Underground Drainage																	
RC Structure for Water Tank																											
B10.3355	AEL North - Construct Water Tank Part 2 (West of Portion B1)	35	03-Oct-16	18-Nov-16	10-Oct-16 A	16-Nov-16	85%	-29	582	B10.3355, AEL North - Construct Water Tank Part 2 (West of Por																	
B2/F Slabs																											
B2 Slab - Portion (B8 & A9)																											
B10.3530	AEL North - B2 Slab - Stage 7 (Portion B8)	9	03-Oct-16	17-Oct-16	19-Sep-16 A	26-Sep-16 A	100%			B10.3530, AEL North - B2 Slab - Stage 7 (Portion B8), AEL North - B2 Slab - Stage 7 (Por																	
B10.3490	AEL North - B2 Slab - Stage 7 (Portion A9)	11	30-Sep-16	18-Oct-16	27-Sep-16 A	14-Oct-16 A	100%	-37		B10.3490, AEL North - B2 Slab - Stage 7 (Portion A9), AEL North - B2 Slab - Stage 7 (Po																	
B2 Slab - Portion (B9)																											
B10.3500	AEL North - B2 Slab - Stage 7 (Portion B9)	9	03-Oct-16	17-Oct-16	22-Sep-16 A	11-Oct-16 A	100%	-55		B10.3500, AEL North - B2 Slab - Stage 7 (Portion B9), AEL North - B2 Slab - Stage 7 (Por																	
B2 Slab - Portion (A10a, A10b, A11 & A12)																											
B10.3075	AEL North - B2 Slab - Stage 7 (Portion A11)	6	31-Oct-16	05-Nov-16	12-Oct-16 A	29-Oct-16 A	100%			B10.3075, AEL North - B2 Slab - Stage 7 (Portion A11), AEL North - B2 Sla																	
B10.3005	AEL North - B2 Slab - Stage 7 (Portion A10, A11, A12)	14	31-Oct-16	15-Nov-16	12-Oct-16 A	15-Nov-16	85%	-42	-40	B10.3005, AEL North - B2 Slab - Stage 7 (Portion A10, A11, A12),																	
B10.3045	AEL North - B2 Slab - Stage 7 (Portion A10a)	10	03-Nov-16	15-Nov-16	18-Oct-16 A	04-Nov-16	90%	-37		B10.3045, AEL North - B2 Slab - Stage 7 (Portion A10a), AEL North																	
B10.3035	AEL North - B2 Slab - Stage 7 (Portion A10b)	10	03-Nov-16	15-Nov-16	25-Oct-16 A	08-Nov-16*	90%	-40		B10.3035, AEL North - B2 Slab - Stage 7 (Portion A10b), AEL North																	
B10.3085	AEL North - B2 Slab - Stage 7 (Portion A12)	6	09-Nov-16	15-Nov-16	09-Nov-16	15-Nov-16*	0%	-40		B10.3085, AEL North - B2 Slab - Stage 7 (Portion A12)																	
B2 Slab - Portion (B6 & B7)																											
B10.3022	AEL North - B2 Slab - Stage 5 (Portion B6)	7	31-Oct-16	07-Nov-16	08-Sep-16 A	29-Oct-16 A	100%	-13		B10.3022, AEL North - B2 Slab - Stage 5 (Portion B6), AEL North - B2 Sl																	
B10.3023	AEL North - B2 Slab - Stage 7 (Portion B7)	11	24-Nov-16	06-Dec-16	24-Nov-16	06-Dec-16	0%	-36	-20	B10.3023, AEL North - B2 Slab - Stage 7 (Portion B7)																	
B10.3024	Complete B2 Slab (exclude AEL Zone)	0		06-Dec-16		06-Dec-16	0%	-36	-20	Complete B2 Slab (exclude AEL Zone), Complete B																	

(3MRP-13) Three Months Rolling Programme Status at 31 Oct 2016

Activity ID	Activity Name	Ori. Dur.	BaseLine Start	BaseLine Finish	Forecast / Actual Start	Forecast / Actual Finish	% Compl.	Finish Variance	Current Float	October 2016					November 2016					December 2016					January 2017					February 2017					
										02	09	16	23	30	06	13	20	27	04	11	18	25	01	08	15	22	29	05							
B1/F Slab - Walls, Columns & B1/F Slabs																																			
AEL North - B1/F Slab other than AEL Zone																																			
B10.3690	AEL North - Wall, Column & B1 Slab (Portion B1R)	20	31-Oct-16	22-Nov-16	12-Oct-16 A	21-Nov-16	50%	-68	-24	B10.3690, AEL North - Wall, Column & B1 Slab (Portion B1R)																									
B10.3560	AEL North - Wall, Column & B1 Slab (Portion B1G) (Portion A6,	14	31-Oct-16	15-Nov-16	17-Oct-16 A	15-Nov-16	20%	-28	-26	B10.3560, AEL North - Wall, Column & B1 Slab (Portion B1G) (Portion A6,																									
B10.3550	AEL North - Wall, Column & B1 Slab (Portion B1J) (Portion B6)	12	31-Oct-16	12-Nov-16	31-Oct-16	12-Nov-16	0%	-16	24	B10.3550, AEL North - Wall, Column & B1 Slab (Portion B1J) (Portion B6)																									
B10.3680	AEL North - Wall, Column & B1 Slab (Portion B1L) (Access Ram	26	22-Dec-16	23-Jan-17	22-Dec-16	23-Jan-17	0%	-36	527	B10.3680, AEL North - Wall, Column & B1 Slab (Portion B1L) (Access Ram																									
AEL North - B1/F Slab for Truss T1, T2 & T5 Erection																																			
C10.0120	AEL North - Construct Found Space Basement Wall and Cols to	15	12-Nov-16	29-Nov-16	12-Nov-16	29-Nov-16	0%	-49	539	C10.0120, AEL North - Construct Found Space Basement Wall and Cols to																									
AEL North - B1/F Slab for CSF & RDE (North of GL 1)																																			
B10.3150	AEL North - Wall, Column & B1 Slab (Portion B1H) (Portion A10	45	16-Nov-16	10-Jan-17	16-Nov-16	10-Jan-17	0%	-28	-47	B10.3150, AEL North - Wall, Column & B1 Slab (Portion B1H) (Portion A10																									
B10.3170	AEL North - Wall, Column & B1 Slab (Portion B1K) (Portion A12	12	07-Dec-16	20-Dec-16	07-Dec-16	20-Dec-16	0%	-36	-20	B10.3170, AEL North - Wall, Column & B1 Slab (Portion B1K) (Portion A12																									
B10.3260	Complete Wall, Column & B1 Slab (exclude AEL Zone & East of	0		10-Jan-17		10-Jan-17	0%	-36	-44	Complete Wall, Column & B1 Slab (exclude AEL Zone & East of																									
C10.0385	AEL North - External Wall & B1 Slab GL 1'-7'/J' within M12 (Del	16	11-Jan-17	01-Feb-17	11-Jan-17	01-Feb-17	0%	-10	-35	C10.0385, AEL North - External Wall & B1 Slab GL 1'-7'/J' within M12 (Del																									
AEL South - B1/F Slab for DCS to facilitate Truss Erection																																			
B10.2115	AEL South (DCS) - Remove 2nd Layer Struts at 0.0mPD of DCS	8	31-Oct-16	08-Nov-16	31-Oct-16	08-Nov-16	0%	-118	-33	B10.2115, AEL South (DCS) - Remove 2nd Layer Struts at 0.0mPD of DCS																									
AEL South - RC Structures Prior to Area M14 H/O																																			
B10.1040	AEL South - Construct Core Wall on PC96 from 1/F to 1M/F Lev	5	30-Sep-16	08-Oct-16	25-Sep-16 A	20-Oct-16 A	100%	-97		B10.1040, AEL South - Construct Core Wall on PC96 from 1/F to 1M/F Level, AEL South																									
B10.3310	AEL South - Construct Basement Road Wall between PC 109 &	17	31-Oct-16	18-Nov-16	31-Oct-16	18-Nov-16	0%	-119	119	B10.3310, AEL South - Construct Basement Road Wall between PC 109 &																									
B10.3290	AEL South - Construct Basement Road Wall between PC 96 & P	17	31-Oct-16	18-Nov-16	31-Oct-16	18-Nov-16	0%	-106	119	B10.3290, AEL South - Construct Basement Road Wall between PC 96 & P																									
B10.3300	AEL South - Construct External Wall between PC 96 & PC105 tc	25	19-Nov-16	17-Dec-16	19-Nov-16	17-Dec-16	0%	-141	119	B10.3300, AEL South - Construct External Wall between PC 96 & PC105 tc																									
B10.3315	AEL South - Construct Walls, Column & Staircases to G/F Level	27	28-Nov-16	30-Dec-16	28-Nov-16	30-Dec-16	0%	-141	119	B10.3315, AEL South - Construct Walls, Column & Staircases to G/F Level																									
B10.3320	AEL South - Construct G/F slab between PC 105, 109 & 116	16	23-Dec-16	12-Jan-17	23-Dec-16	12-Jan-17	0%	-141	119	B10.3320, AEL South - Construct G/F slab between PC 105, 109 & 116																									
Podium Super-Structures																																			
Trusses																																			
AEL Tunnel Zone -Trusses 1																																			
C10.0150	AEL Tunnel Zone - Erection of Temp Working Platform and Fals	50	13-Oct-16	09-Dec-16	12-Jul-16 A	29-Nov-16	60%	-80	-76	C10.0150, AEL Tunnel Zone - Erection of Temp Working Platform and Fals																									
C10.0145	AEL Tunnel Zone - Construct RC Column for Steel Trusses T1	21	22-Aug-16	15-Sep-16	22-Aug-16 A	07-Nov-16	90%	-91	-76	C10.0145, AEL Tunnel Zone - Construct RC Column for Steel Trusses T1,																									
C10.0155	AEL Tunnel Zone - Truss 1 Construction Summary	117	30-Nov-16	26-Apr-17	30-Nov-16	26-Apr-17	0%	-69	-74	C10.0155, AEL Tunnel Zone - Truss 1 Construction Summary																									
C10.0160	AEL Tunnel Zone - Truss 1 Concreting of 1st pour of bottom ch	12	30-Nov-16	13-Dec-16	30-Nov-16	13-Dec-16	0%	-77	-76	C10.0160, AEL Tunnel Zone - Truss 1 Concreting of 1st pour of bottom ch																									
C10.0185	AEL Tunnel Zone - Truss 1 install bottom steel plates	24	14-Dec-16	13-Jan-17	14-Dec-16	13-Jan-17	0%	-70	-74	C10.0185, AEL Tunnel Zone - Truss 1 install bottom steel plates																									
C10.0190	AEL Tunnel Zone - Truss 1 install temp platform, top nodes & ir	24	14-Jan-17	14-Feb-17	14-Jan-17	14-Feb-17	0%	-69	-74	C10.0190, AEL Tunnel Zone - Truss 1 install temp platform, top nodes & ir																									
C10.0195	AEL Tunnel Zone - Truss 1 Concreting of 2nd pour of bottom ch	15	25-Jan-17	14-Feb-17	25-Jan-17	14-Feb-17	0%	-69	-74	C10.0195, AEL Tunnel Zone - Truss 1 Concreting of 2nd pour of bottom ch																									
AEL Tunnel Zone -Trusses 2																																			
C10.0162	AEL Tunnel Zone - Erection of Temp Working Platform and Fals	50	29-Oct-16	28-Dec-16	12-Jul-16 A	30-Nov-16	50%	-67	-65	C10.0162, AEL Tunnel Zone - Erection of Temp Working Platform and Fals																									
C10.0161	AEL Tunnel Zone - Construct RC Column for Steel Trusses T2	22	22-Aug-16	15-Sep-16	22-Aug-16 A	08-Nov-16	90%		-65	C10.0161, AEL Tunnel Zone - Construct RC Column for Steel Trusses T2																									
C10.0170	AEL Tunnel Zone - Truss 2 Concreting of 1st pour of bottom ch	12	07-Dec-16	20-Dec-16	07-Dec-16	20-Dec-16	0%	-71	-76	C10.0170, AEL Tunnel Zone - Truss 2 Concreting of 1st pour of bottom ch																									
C10.0165	AEL Tunnel Zone - Truss 2 Construction Summary	125	07-Dec-16	15-May-17	07-Dec-16	15-May-17	0%	-65	-76	C10.0165, AEL Tunnel Zone - Truss 2 Construction Summary																									
C10.0198	AEL Tunnel Zone - Truss 2 install bottom steel plates	24	22-Dec-16	20-Jan-17	22-Dec-16	20-Jan-17	0%	-65	-76	C10.0198, AEL Tunnel Zone - Truss 2 install bottom steel plates																									
C10.0200	AEL Tunnel Zone - Truss 2 install temp. platform, top nodes & i	24	21-Jan-17	21-Feb-17	21-Jan-17	21-Feb-17	0%	-65	-76	C10.0200, AEL Tunnel Zone - Truss 2 install temp. platform, top nodes & i																									
AEL Tunnel Zone -Trusses 5																																			
C10.0172	AEL Tunnel Zone - Erection of Temp Working Platform and Fals	50	29-Oct-16	28-Dec-16	12-Jul-16 A	18-Nov-16	90%	-57	-73	C10.0172, AEL Tunnel Zone - Erection of Temp Working Platform and Fals																									
C10.0180	AEL Tunnel Zone - Truss 5 Concreting of 1st pour of bottom ch	12	19-Nov-16	02-Dec-16	19-Nov-16	02-Dec-16	0%	-47	-73	C10.0180, AEL Tunnel Zone - Truss 5 Concreting of 1st pour of bottom ch																									
C10.0175	AEL Tunnel Zone - Truss 5 Construction Summary	105	19-Nov-16	28-Mar-17	19-Nov-16	28-Mar-17	0%	-44	-58	C10.0175, AEL Tunnel Zone - Truss 5 Construction Summary																									
C10.0215	AEL Tunnel Zone - Truss 5 install bottom steel plates	24	03-Dec-16	03-Jan-17	03-Dec-16	03-Jan-17	0%	-44	-58	C10.0215, AEL Tunnel Zone - Truss 5 install bottom steel plates																									

(3MRP-13) Three Months Rolling Programme Status at 31 Oct 2016

Activity ID	Activity Name	Ori. Dur.	BaseLine Start	BaseLine Finish	Forecast / Actual Start	Forecast / Actual Finish	% Compl.	Finish Variance	Current Float	October 2016				November 2016				December 2016				January 2017				February 2017	
										02	09	16	23	30	06	13	20	27	04	11	18	25	01	08	15	22	29
B2/F MEP																											
First Fix																											
B40.8985	Early Access for Building Services (1st Fix)	0	18-Dec-16		18-Dec-16		0%	-74	157																		
B40.8995	B2/F - Building Services - 1st Fix - Summary	157	19-Dec-16	04-Jul-17	19-Dec-16	04-Jul-17	0%	16	36																		
B40.8990	B2/F - Building Services - Zone A - 1st Fix	60	19-Dec-16	04-Mar-17	19-Dec-16	04-Mar-17	0%	-63	122																		
B40.9030	B2/F - Building Services - Zone C - 1st Fix	40	07-Jan-17	25-Feb-17	07-Jan-17	25-Feb-17	0%	-25	114																		
B40.9060	B2/F - Building Services - Zone D - 1st Fix	40	27-Jan-17	17-Mar-17	27-Jan-17	17-Mar-17	0%	-14	-47																		
B1/F MEP																											
First Fix																											
B40.9330	Early Access for Building Services (1st Fix)	0	08-Dec-16		08-Dec-16		0%	19	223																		
B40.9335	B1/F - Building Services - Zone A - 1st Fix	60	08-Dec-16	22-Feb-17	08-Dec-16	22-Feb-17	0%	14	177																		
SPS MEP																											
D01.3020	SPS - Installation of Sewage/Drainage Pipes and Manholes	70	03-Jan-17	28-Mar-17	03-Jan-17	28-Mar-17	0%	-104	-83																		
ABWF																											
M+ Basement ABWF																											
B2/F ABWF																											
B30.0006	B2/F Zone A - Builder's Work	42	31-Oct-16	17-Dec-16	31-Oct-16	17-Dec-16	0%	-63	89																		
B30.0004	Early Access date for Builders Works at B2/F M+ Basement	0	31-Oct-16		31-Oct-16		0%	-77	110																		
B30.0020	B2/F Zone C - Builder's Work	42	16-Nov-16	06-Jan-17	16-Nov-16	06-Jan-17	0%	-31	59																		
B30.0040	B2/F Zone E - Builder's Work	42	08-Dec-16	01-Feb-17	08-Dec-16	01-Feb-17	0%	-60	75																		
B30.0010	B2/F Zone B - Builder's Work	42	16-Dec-16	09-Feb-17	16-Dec-16	09-Feb-17	0%	-16	68																		
B30.0050	B2/F Zone F - Builder's Work	42	22-Dec-16	14-Feb-17	22-Dec-16	14-Feb-17	0%	-36	52																		
B1/F ABWF																											
B30.1002	Early Access date for Builders Works at B1/F M+ Basement	0	08-Dec-16		08-Dec-16		0%	-10	187																		
B30.1004	B1/F Zone A - Builder's Work	42	08-Dec-16	01-Feb-17	08-Dec-16	01-Feb-17	0%	-9	148																		
SPS ABWF																											
D01.3030	SPS - ABWF	70	03-Jan-17	28-Mar-17	03-Jan-17	28-Mar-17	0%	-34	-83																		
External Works																											
M+ External Works																											
Utilities																											
Drainage																											
EW1045	Construct M+ manholes S1.1, S3.2, S3.3, S3.4 (terminal)	91	31-Oct-16	20-Feb-17	31-Oct-16	20-Feb-17	0%	-250	444																		
EW1010	Construct the DN375 and DN600 storm drains within the At-gr.	75	31-Oct-16	01-Feb-17	31-Oct-16	01-Feb-17	0%	-230	55																		
Storm Drain DN600 at Portion M45																											
Storm Drain along Gridline D'-E'/1'-2'																											
EW1700	Fence off work area for DN600 storm drain excavation	1	31-Oct-16	31-Oct-16	31-Oct-16	31-Oct-16	0%		225																		
EW1695	PIW handover of WHC6_1c for M+ connection	0	31-Oct-16		31-Oct-16*		0%	-123																			
EW1705	Excavate trial trench for existing Underground Utilities	14	31-Oct-16	15-Nov-16	31-Oct-16	15-Nov-16	0%		225																		
EW1708	Intall support to exisiting Underground Utilities	7	16-Nov-16	23-Nov-16	16-Nov-16	23-Nov-16	0%		225																		
EW1710	Excavate trench for DN600 and install shoring	10	24-Nov-16	05-Dec-16	24-Nov-16	05-Dec-16	0%		225																		
EW1730	Lay down DN600 pipe between WHC6_1c & MHS3.4	7	06-Dec-16	13-Dec-16	06-Dec-16	13-Dec-16	0%		225																		
EW1740	Backfill and reinstate pavement	2	14-Dec-16	15-Dec-16	14-Dec-16	15-Dec-16*	0%		225																		
Storm Drain along Gridline E'-G' / 1'-2'																											

(3MRP-13) Three Months Rolling Programme Status at 31 Oct 2016

Activity ID	Activity Name	Ori. Dur.	BaseLine Start	BaseLine Finish	Forecast / Actual Start	Forecast / Actual Finish	% Compl.	Finish Variance	Current Float	October 2016					November 2016					December 2016					January 2017					February 2017				
										02	09	16	23	30	06	13	20	27	04	11	18	25	01	08	15	22	29	05						
EW1765	Complete B2 Slab, Columns & Walls at A6 & A7	0	06-Nov-16		06-Nov-16*		0%		360						Complete B2 Slab, Columns & Walls at A6 & A7, Complete B2 Slab, Columns & Walls at A6 & A7																			
EW1755	Excavate Trial trench for existing Underground Utilities	14	16-Dec-16	04-Jan-17	16-Dec-16	04-Jan-17	0%		225																									
EW1758	Install support to existing Underground Utilities	7	05-Jan-17	12-Jan-17	05-Jan-17	12-Jan-17	0%		225																									
EW1760	Excavate trench for DN600 at gridline E'-G' / 1' and install shoring	10	13-Jan-17	24-Jan-17	13-Jan-17	24-Jan-17	0%		225																									
EW1780	Lay down DN600 at gridline E'-G'/1'	7	25-Jan-17	04-Feb-17	25-Jan-17	04-Feb-17	0%		225																									
Storm Drain DN375 at Portion M45																																		
Storm Drain along Gridline A-K' / 5'																																		
EW6110	Fence off Work area for DN375 storm drain excavation	1	31-Oct-16	31-Oct-16	31-Oct-16	31-Oct-16	0%		284																									
EW1640	PIW handover of WHC6_1e for M+ connection	0		31-Oct-16		31-Oct-16*	0%		-90																									
EW1615	Excavate Trial Trench for existing Underground Utilities	14	31-Oct-16	15-Nov-16	31-Oct-16	15-Nov-16	0%		284																									
EW1618	Install support to existing underground Utilities	14	16-Nov-16	01-Dec-16	16-Nov-16	01-Dec-16	0%		284																									
EW6120	Excavate trench for DN375 and install shoring	15	02-Dec-16	19-Dec-16	02-Dec-16	19-Dec-16	0%		284																									
EW6140	Lay down DN375 pipe between WHC6_1e	12	20-Dec-16	05-Jan-17	20-Dec-16	05-Jan-17	0%		284																									
EW6150	Backfill and reinstate pavement	4	06-Jan-17	10-Jan-17	06-Jan-17	10-Jan-17*	0%		284																									
Storm Drain DN150 at Portion M45																																		
Storm Drain along Gridline A / 5' - 6'																																		
EW1900	PIW handover of WHC6_1f for M+ connection	0		31-Oct-16		31-Oct-16*	0%		-81																									
EW1910	Fence off work area for DN150 storm drain excavation	1	31-Oct-16	31-Oct-16	31-Oct-16	31-Oct-16	0%		302																									
EW1915	Excavate Trial Trench for existing Underground Utilities	14	01-Nov-16	16-Nov-16	01-Nov-16	16-Nov-16	0%		302																									
EW1930	Install support to existing Underground Utilities	8	17-Nov-16	25-Nov-16	17-Nov-16	25-Nov-16	0%		302																									
EW1920	Excavate trench for DN150 and install shoring	6	26-Nov-16	02-Dec-16	26-Nov-16	02-Dec-16	0%		302																									
EW1940	Lay down DN150 and connect to WHC6_1f	9	03-Dec-16	13-Dec-16	03-Dec-16	13-Dec-16	0%		302																									
EW1950	Backfill and reinstate pavement	3	14-Dec-16	16-Dec-16	14-Dec-16	16-Dec-16*	0%		302																									
Storm Drain DN300 along Gridline G-M/14																																		
EW1945	DCS Plant Room RC Structure complete (including deferred pile caps & sump pits)	0		31-Oct-16		31-Oct-16	0%		372																									
EW1955	Prepare / Submit Temp Works ELS with ICE Cert	14	31-Oct-16	15-Nov-16	31-Oct-16	15-Nov-16	0%		270																									
EW1960	Excavate Trial Trench for existing underground utilities	14	05-Nov-16	21-Nov-16	05-Nov-16	21-Nov-16	0%		270																									
EW1970	Install support on existing underground utilities	14	22-Nov-16	07-Dec-16	22-Nov-16	07-Dec-16	0%		270																									
EW1980	Excavate to formation level & install laterla support	14	08-Dec-16	24-Dec-16	08-Dec-16	24-Dec-16	0%		270																									
EW1990	Construct Manhole S2.12 & S2.13	14	27-Dec-16	12-Jan-17	27-Dec-16	12-Jan-17	0%		270																									
EW2040	Install DN300 pipe and connect to Manholes S2.12 & S2.13	7	13-Jan-17	20-Jan-17	13-Jan-17	20-Jan-17	0%		270																									
EW2050	Backfill to existing ground level	5	21-Jan-17	26-Jan-17	21-Jan-17	26-Jan-17*	0%		270																									
Storm Drain DN600 along Gridline B-G/14																																		
EW8610	Excavate Trial Trench for existing underground utilities	14	31-Oct-16	15-Nov-16	31-Oct-16	15-Nov-16	0%		163																									
EW8605	Completion of B1 Slab (Portion B1E)	0		31-Oct-16		31-Oct-16	0%		208																									
EW8620	Install support on existing underground utilities	14	16-Nov-16	01-Dec-16	16-Nov-16	01-Dec-16	0%		163																									
EW8630	Excavate to formation level & install laterla support	14	02-Dec-16	17-Dec-16	02-Dec-16	17-Dec-16	0%		275																									
EW8640	Construct Manhole S2.12 & S2.13	14	19-Dec-16	06-Jan-17	19-Dec-16	06-Jan-17	0%		275																									
EW8650	Install DN300 pipe and connect to Manholes S2.12 & S2.13	7	07-Jan-17	14-Jan-17	07-Jan-17	14-Jan-17	0%		275																									
EW8660	Backfill to existing ground level	5	16-Jan-17	20-Jan-17	16-Jan-17	20-Jan-17*	0%		275																									
Storm Drain DN750 along Gridline A-B/14																																		
EW8670	Excavate Trial Trench for existing underground utilities	14	02-Dec-16	17-Dec-16	02-Dec-16	17-Dec-16	0%		163																									
EW8680	Install support on existing underground utilities	14	19-Dec-16	06-Jan-17	19-Dec-16	06-Jan-17	0%		163																									
EW8690	Excavate to formation level & install laterla support	14	07-Jan-17	23-Jan-17	07-Jan-17	23-Jan-17	0%		247																									

Lyric Theatre Complex

C. Action and Limit Levels for Construction Phase

Air Quality

The Action and Limit Levels for 1-hour and 24-hour TSP for the monitoring station are presented in following tables:

Table C-1: Action and Limit Levels for 1-hour TSP

Monitoring Station	Action Level (mg/m ³)	Limit Level (mg/m ³)
AM1	273.7	500
AM2A	274.2	500

Table C-2: Action and Limit Levels for 24-hour TSP

Monitoring Station	Action Level (µg/m ³)	Limit Level (µg/m ³)
AM1	143.6	260
AM2A	151.1	260

Noise

The Action and Limit Levels for Noise for the monitoring stations are presented in following table:

Table C-3: Action and Limit Levels for Construction Noise

Time Period & Monitoring Locations	Action Level	Limit Level
NM1A		
0700-1900 hours on normal weekdays	When one documented complaint is received from any one of the sensitive receivers	75 dB(A)

D. Event and Action Plan for Air Quality, Noise, Landscape and Visual Impact

Air Quality

In case the Action and Limit Levels are not complied during construction stage, the following Event and Action Plan should be followed:

Table D-1: Event and Action Plan for Air Quality

Event	Action			
	ET	IEC	WKCD A	Contractor
Action Level				
1. Exceedance for one sample	<ol style="list-style-type: none"> 1. Identify source, investigate the causes of exceedance and propose remedial measures; 2. Inform IEC and WKCD A; 3. Repeat measurement to confirm finding; 4. Increase monitoring frequency to daily. 	<ol style="list-style-type: none"> 1. Check monitoring data submitted by ET; 2. Check Contractor's working method. 	<ol style="list-style-type: none"> 1. Notify Contractor 	<ol style="list-style-type: none"> 1. Rectify any unacceptable practice; 2. Amend working methods if appropriate.
2. Exceedance for two or more consecutive samples	<ol style="list-style-type: none"> 1. Identify source; 2. Inform IEC and WKCD A; 3. Advise the WKCD A on the effectiveness of the proposed remedial measures; 4. Repeat measurements to confirm findings; 5. Increase monitoring frequency to daily; 6. Discuss with IEC and Contractor on remedial actions required; 7. If exceedance continues, arrange meeting with IEC and WKCD A; 8. If exceedance stops, cease additional monitoring. 	<ol style="list-style-type: none"> 1. Check monitoring data submitted by ET; 2. Check Contractor's working method; 3. Discuss with ET and Contractor on possible remedial measures; 4. Advise the ET on the effectiveness of the proposed remedial measures; 5. Monitor the implementation of remedial measures. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. Ensure remedial measures properly implemented. 	<ol style="list-style-type: none"> 1. Submit proposals for remedial to WKCD A within three working days of notification; 2. Implement the agreed proposals; 3. Amend proposal if appropriate.
Limit Level				
1. Exceedance for one sample	<ol style="list-style-type: none"> 1. Identify source, investigate the causes of exceedance and propose remedial measures; 2. Inform WKCD A, Contractor and EPD; 3. Repeat measurement to confirm finding; 4. Increase monitoring frequency to daily; 5. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and WKCD A informed of the results. 	<ol style="list-style-type: none"> 1. Check monitoring data submitted by ET; 2. Check Contractor's working method; 3. Discuss with ET and Contractor on possible remedial measures; 4. Advise the WKCD A on the effectiveness of the proposed remedial measures; 5. Monitor the implementation of remedial measures. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. Ensure remedial measures properly implemented. 	<ol style="list-style-type: none"> 1. Take immediate action to avoid further exceedance; 2. Submit proposals for remedial actions to IEC within three working days of notification; 3. Implement the agreed proposals; 4. Amend proposal if appropriate.

Event**Action**

2. Exceedance for two or more consecutive samples	<ol style="list-style-type: none">1. Notify IEC, WKCDA, Contractor and EPD;2. Identify source;3. Repeat measurement to confirm findings;4. Increase monitoring frequency to daily;5. Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented;6. Arrange meeting with IEC and WKCDA to discuss the remedial actions to be taken;7. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and WKCDA informed of the results;8. If exceedance stops, cease additional monitoring.	<ol style="list-style-type: none">1. Check monitoring data submitted by ET;2. Check Contractor's working method;3. Discuss amongst WKCDA, ET, and Contractor on the potential remedial actions;4. Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the WKCDA accordingly;5. Monitor the implementation of remedial measures.	<ol style="list-style-type: none">1. Confirm receipt of notification of failure in writing;2. Notify Contractor;3. In consolidation with the IEC, agree on the remedial measures to be implemented;4. Ensure remedial measures properly implemented;5. If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated.	<ol style="list-style-type: none">1. Take immediate action to avoid further exceedance;2. Submit proposals for remedial actions to IEC within three working days of notification;3. Implement the agreed proposals;4. Resubmit proposals if problem still not under control;5. Stop the relevant portion of works as determined by the WKCDA until the exceedance is abated.
---	--	--	---	--

Construction Noise

In case the Action and Limit Levels are not complied during construction stage, the following Event and Action Plan should be followed:

Table D-2: Event and Action Plan for Construction Noise

Event	Action			
	ET	IEC	WKCD	Contractor
Action Level	<ol style="list-style-type: none"> 1. Notify WKCD, IEC and Contractor; 2. Carry out investigation; 3. Report the results of investigation to the IEC, WKCD and Contractor; 4. Discuss with the IEC and Contractor on remedial measures required; 5. Increase monitoring frequency to check mitigation effectiveness. 	<ol style="list-style-type: none"> 1. Review the investigation results submitted by the ET; 2. Review the proposed remedial measures by the Contractor and advise the WKCD accordingly; 3. Advise the WKCD on the effectiveness of the proposed remedial measures. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. In consolidation with the IEC, agree with the Contractor on the remedial measures to be implemented; 4. Supervise the implementation of remedial measures. 	<ol style="list-style-type: none"> 1. Submit noise mitigation proposals to IEC and WKCD; 2. Implement noise mitigation proposals.
Limit Level	<ol style="list-style-type: none"> 1. Inform IEC, WKCD, Contractor and EPD; 2. Repeat measurements to confirm findings; 3. Increase monitoring frequency; 4. Identify source and investigate the cause of exceedance; 5. Carry out analysis of Contractor's working procedures; 6. Discuss with the IEC, Contractor and WKCD on remedial measures required; 7. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and WKCD informed of the results; 8. If exceedance stops, cease additional monitoring. 	<ol style="list-style-type: none"> 1. Discuss amongst WKCD, ET, and Contractor on the potential remedial actions; 2. Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the WKCD accordingly. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. In consolidation with the IEC, agree with the Contractor on the remedial measures to be implemented; 4. Supervise the implementation of remedial measures; 5. If exceedance continues, consider stopping the Contractor to continue working on that portion of work which causes the exceedance until the exceedance is abated. 	<ol style="list-style-type: none"> 1. Take immediate action to avoid further exceedance; 2. Submit proposals for remedial actions to IEC and WKCD within 3 working days of notification; 3. Implement the agreed proposals; 4. Submit further proposal if problem still not under control; 5. Stop the relevant portion of works as instructed by the WKCD until the exceedance is abated.

Landscape and Visual Impact

In case of non-compliance of landscape and visual impacts, procedures in accordance with the Event and Action Plan should be followed:

Table D-3: Event and Action Plan for Landscape and Visual Impact

Event	Action			
	ET	IEC	WKCDA	Contractor
Design Check	<ol style="list-style-type: none"> 1. Design check to make sure the design complies with all the proposed mitigation measures in the EIA report; 2. Prepare and submit report. 	<ol style="list-style-type: none"> 1. Check report submitted by ET; 2. Recommend remedial design if necessary. 	<ol style="list-style-type: none"> 1. Undertake remedial design if necessary. 	-
Non-conformity on one occasion	<ol style="list-style-type: none"> 1. Identify source of non-conformity; 2. Report to IEC and WKCDA; 3. Discuss remedial actions with IEC, WKCDA and Contractor; 4. Monitor remedial actions until rectification has been completed. 	<ol style="list-style-type: none"> 1. Check and verify source of non-conformity; 2. Discuss remedial actions with ET and Contractor; 3. Advise WKCDA on effectiveness of proposed remedial actions; 4. Check implementation of remedial actions. 	<ol style="list-style-type: none"> 1. Notify Contractor; 2. Ensure remedial actions are properly implemented. 	<ol style="list-style-type: none"> 1. Amend working method as necessary; 2. Rectify damage and undertake necessary replacement and remedial actions.
Repeated conformity	<ol style="list-style-type: none"> 1. Identify source of non-conformity; 2. Report to IEC and WKCDA; 3. Increase monitoring frequency; 4. Discuss remedial actions with IEC, WKCDA and Contractor; 5. Monitor remedial actions until rectification has been completed; 6. If non-conformity rectified, reduce monitoring frequency back to normal. 	<ol style="list-style-type: none"> 1. Check and verify source of non-conformity; 2. Check Contractor's working method; 3. Discuss remedial actions with ET and Contractor; 4. Advise WKCDA on effectiveness of proposed remedial actions; 5. Supervise implementation of remedial actions. 	<ol style="list-style-type: none"> 1. Notify Contractor; 2. Ensure remedial actions are properly implemented. 	<ol style="list-style-type: none"> 1. Amend working method as necessary; 2. Rectify damage and undertake necessary replacement and remedial actions.

E. Monitoring Schedule

NOVEMBER 2016

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
		1	2 AM1, AM2A - 24hrTSP, 1hr TSP x3 NM1A - Noise Impact Monitoring	3	4	5
6	7	8 AM1, AM2A - 24hrTSP, 1hr TSP x3 NM1A - Noise Impact Monitoring	9	10	11	12
13	14 AM1, AM2A - 24hrTSP, 1hr TSP x3 NM1A - Noise Impact Monitoring	15	16	17	18 AM1, AM2A - 24hrTSP, 1hr TSP x3	19
20	21	22	23	24 AM1, AM2A - 24hrTSP, 1hr TSP x3 NM1A - Noise Impact Monitoring	25	26
27	28	29	30 AM1, AM2A - 24hrTSP, 1hr TSP x3 NM1A - Noise Impact Monitoring			
		Notes: AM1 - International Commerce Centre (ICC) AM2A - Austin Road West (Opposite to The Harbourside) NM1A - International Commerce Centre (ICC)				

DECEMBER 2016

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
				1	2	3
4	5	6 AM1, AM2A - 24hrTSP, 1hr TSP x3 NM1A - Noise Impact Monitoring	7	8	9	10
11	12 AM1, AM2A - 24hrTSP, 1hr TSP x3 NM1A - Noise Impact Monitoring	13	14	15	16 AM1, AM2A - 24hrTSP, 1hr TSP x3	17
18	19	20	21	22 AM1, AM2A - 24hrTSP, 1hr TSP x3 NM1A - Noise Impact Monitoring	23	24
25	26	27	28 AM1, AM2A - 24hrTSP, 1hr TSP x3 NM1A - Noise Impact Monitoring	29	30	31
		Notes: AM1 - International Commerce Centre (ICC) AM2A - Austin Road West (Opposite to The Harbourside) NM1A - International Commerce Centre (ICC)				

F. Calibration Certifications

High-Volume TSP Sampler
5-Point Calibration Record

Location : AM1(ICC)
 Calibrated by : K.T.Ho
 Date : 16/10/2016

Sampler

Model : TE-5170
 Serial Number : S/N 0767

Calibration Orifice and Standard Calibration Relationship

Serial Number : 2454
 Service Date : 14 Mar 2016
 Slope (m) : 2.09532
 Intercept (b) : -0.03812
 Correlation Coefficient(r) : 0.99994

Standard Condition

Pstd (hpa) : 1013
 Tstd (K) : 298.18

Calibration Condition

Pa (hpa) : 1013
 Ta(K) : 301

Resistance Plate	dH [green liquid] (inch water)	Z	X=Qstd (cubic meter/min)	IC (chart)	Y (corrected)
1 18 holes	10.2	3.178	1.543	60	59.70
2 13 holes	8.4	2.884	1.403	52	51.74
3 10 holes	6.2	2.478	1.210	44	43.78
4 7 holes	4.4	2.087	1.024	34	33.83
5 5 holes	2.6	1.604	0.795	22	21.89

Notes: $Z = \sqrt{dH(Pa/Pstd)(Tstd/Ta)}$, $X = Z/m - b$, $Y(\text{Corrected Flow}) = IC * \{\sqrt{Pa/Pstd}(Tstd/Ta)\}$

Sampler Calibration Relationship

Slope(m): 49.892 Intercept(b): -17.425 Correlation Coefficient(r): 0.9991

Checked by: 
 Magnum Fan

Date: 23/10/2016

High-Volume TSP Sampler
5-Point Calibration Record

Location : AM2A (Harbourside)
 Calibrated by : K.T.Ho
 Date : 16/10/2016

Sampler

Model : TE-5170
 Serial Number : S/N 8919

Calibration Orifice and Standard Calibration Relationship

Serial Number : 2454
 Service Date : 14 Mar 2016
 Slope (m) : 2.10326
 Intercept (b) : -0.06696
 Correlation Coefficient(r) : 0.99989

Standard Condition

Pstd (hpa) : 1013
 Tstd (K) : 298.18

Calibration Condition

Pa (hpa) : 1013
 Ta(K) : 301

Resistance Plate	dH [green liquid] (inch water)	Z	X=Qstd (cubic meter/min)	IC (chart)	Y (corrected)
1 18 holes	12.2	3.475	1.684	60	59.70
2 13 holes	9.2	3.018	1.467	51	50.75
3 10 holes	7.2	2.670	1.301	44	43.78
4 7 holes	4.6	2.134	1.046	34	33.83
5 5 holes	2.6	1.604	0.794	24	23.880

Notes: $Z = \sqrt{dH(Pa/Pstd)(Tstd/Ta)}$, $X = Z/m - b$, $Y(\text{Corrected Flow}) = IC * \{\sqrt{Pa/Pstd}(Tstd/Ta)\}$

Sampler Calibration Relationship

Slope(m): 40.221 Intercept(b): -8.238 Correlation Coefficient(r): 0.9999

Checked by: 
 Magnum Fan

Date: 23/10/2016



TISCH ENVIRONMENTAL, INC.
 145 SOUTH MIAMI AVE
 VILLAGE OF CLEVELAND, OH
 45002
 513.467.9000
 877.263.7610 TOLL FREE
 513.467.9009 FAX

ORIFICE TRANSFER STANDARD CERTIFICATION WORKSHEET TE-5025A

Date - Mar 14, 2016 Rootsmeter S/N 0438320 Ta (K) - 295
 Operator Tisch Orifice I.D. - 2454 Pa (mm) - 745.49

PLATE OR Run #	VOLUME START (m3)	VOLUME STOP (m3)	DIFF VOLUME (m3)	DIFF TIME (min)	METER DIFF Hg (mm)	ORFICE DIFF H2O (in.)
1	NA	NA	1.00	1.4020	3.2	2.00
2	NA	NA	1.00	1.0060	6.4	4.00
3	NA	NA	1.00	0.9010	7.9	5.00
4	NA	NA	1.00	0.8590	8.8	5.50
5	NA	NA	1.00	0.7090	12.8	8.00

DATA TABULATION

Vstd	(x axis) Qstd	(y axis)	Va	(x axis) Qa	(y axis)
0.9866	0.7037	1.4078	0.9957	0.7102	0.8896
0.9824	0.9765	1.9909	0.9914	0.9855	1.2581
0.9803	1.0880	2.2259	0.9893	1.0980	1.4066
0.9792	1.1399	2.3345	0.9882	1.1504	1.4753
0.9738	1.3735	2.8155	0.9828	1.3862	1.7792
Qstd slope (m) = 2.10326			Qa slope (m) = 1.31703		
intercept (b) = -0.06696			intercept (b) = -0.04232		
coefficient (r) = 0.99989			coefficient (r) = 0.99989		
y axis = SQRT[H2O(Pa/760) (298/Ta)]			y axis = SQRT[H2O(Ta/Pa)]		

CALCULATIONS

Vstd = Diff. Vol [(Pa-Diff. Hg)/760] (298/Ta)
 Qstd = Vstd/Time

Va = Diff Vol [(Pa-Diff Hg)/Pa]
 Qa = Va/Time

For subsequent flow rate calculations:

Qstd = 1/m{ [SQRT(H2O(Pa/760) (298/Ta))] - b}
 Qa = 1/m{ [SQRT H2O(Ta/Pa)] - b}

CALIBRATION CERTIFICATE

Date: February 17, 2016

Equipment Name	:	Digital Dust Indicator, Model LD-5R
Code No.	:	080000-72
Quantity	:	1 unit
Serial No.	:	620402
Sensitivity	:	0.001 mg/m ³
Sensitivity Adjustment	:	783CPM
Scale Setting	:	February 8, 2016

We hereby certify that the above mentioned instrument has been calibrated satisfactory.

Sincerely

SIBATA SCIENTIFIC TECHNOLOGY LTD.

Shintaro Okamura

Shintaro Okamura

Overseas Sales Division


REPORT OF EQUIPMENT PERFORMANCE CHECK / CALIBRATION

REPORT NO. : HK1610285
 PROJECT NAME : PERFORMANCE CHECK / CALIBRATION OF DUST METER
 DATE OF ISSUE : 15/6/2016

CUSTOMER : ENVIROTECH SERVICES COMPANY
 ADDRESS : RM. 113, 1/F, MY LOFT, 9 HOI WING ROAD, TUEN MUN, N.T.


REPORT NO. : HK1610285
 PROJECT ITEM NO. : HK1610285-01
PERFORMANCE CHECK / CALIBRATED EQUIPMENT
 TYPE : LASER DUST MONITOR
 MANUFACTURER : SIBATA
 MODEL NO. : LD-5R
 SERIAL NO. : 620402
 EQUIPMENT NO. : ---
 RECEIPT DATE : 3/6/2016
 PERFORMANCE CHECK / CALIBRATION DATE : 7/6/2016

PERFORMANCE CHECK / CALIBRATION Information

CODE	Calibration Parameter	Method Procedure	Reference Method
Dust PC/CAL	Performance Check / Calibration of Dust Meter	CAL003	General Technical Requirements of Environmental Monitoring, Environmental Monitoring & Audit Guidelines for Development Projects in HK

- Notes : 1. This report shall not be reproduced, except in full, without prior approval from Pilot Testing Limited.
 2. Performance Check / Calibration result relates to performance check / calibration item(s) as received.

Approved Signatory :



 Wong Po Yan Pauline
 (Testing Engineer)

Issue Date: 15/6/2016



REPORT OF PERFORMANCE CHECK / CALIBRATION

PROJECT NAME : PERFORMANCE CHECK / CALIBRATION OF DUST METER
 DATE OF ISSUE : 15/6/2016
 REPORT NO. : HK1610285

PERFORMANCE CHECK / CALIBRATED EQUIPMENT

TYPE : LASER DUST MONITOR
 MANUFACTURER : SIBATA
 MODEL NO. : LD-5R
 SERIAL NO. : 620402
 EQUIPMENT NO. : ---
 SENSITIVITY ADJUSTMENT : 783 CPM
 SETTING :
 PERFORMANCE CHECK / CALIBRATION DATE : 7/6/2016

STANDARD EQUIPMENT

TYPE : HIGH VOLUME AIR SAMPLER
 MANUFACTURER : TISCH
 MODEL NO. : TE-5170
 EQUIPMENT REF NO. : PTL_HV002
 LAST CALIBRATION DATE : 30/5/2016


EQUIPMENT PERFORMANCE CHECK / CALIBRATION RESULTS:

Sensitivity Adjustment Scale Setting (Before Performance check / Calibration): 783 CPM
 Sensitivity Adjustment Scale Setting (After Performance check / Calibration): 783 CPM


Trial no. in 1-hr period	Time	Mean Temp (°C)	Mean Pressure (hPa)	Concentration in ug/m ³ (Standard equipment) (Y - Axis)	Total Count ² (Performance Check / Calibrated equipment)	Concentration in Count/Minute ³ (Performance Check / Calibrated equipment) (X - Axis)
Zero Check ¹	7/6/2016, 08:00	28.1	1008	0.0	0	0.0
1	7/6/2016, 09:10 - 10:10	28.1	1008	21.8	631	10.5
2	7/6/2016, 12:59 - 13:59	28.1	1008	23.3	670	11.2
3	7/6/2016, 14:17 - 15:17	28.1	1008	20.4	509	8.5


Linear Regression of Y on X

Slope (K- factor) : 2.1
 Correlation Coefficient : 0.9924
 Validity of Performance Check / Calibration Record : 7/6/2017

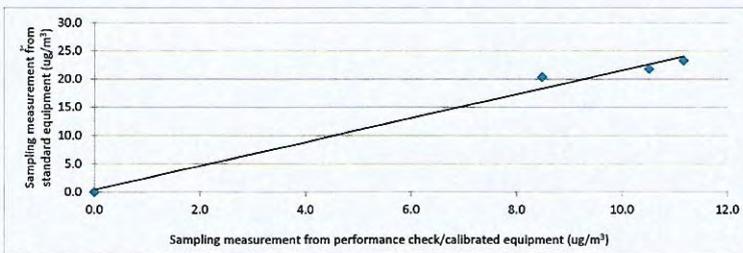

- Notes : 1. Zero check conducted as per CAL003 SOP and manufacturer's manual as appropriate.
 2. Total Count was measured by laser dust monitor.
 3. Count/minute was calculated by (Total Count/60).
 4. This report shall not be reproduced, except in full, without prior approval from Pilot Testing Limited.
 5. Performance Check / Calibration result relates to performance check / calibration item(s) as received.

Operator: Kong Wing Yan, Emily Signature:  Date: 7/6/2016

Checked by: Wong Po Yan, Pauline Signature:  Date: 15/6/2016



輝創工程有限公司

Sun Creation Engineering Limited

Calibration and Testing Laboratory

Certificate of Calibration

校正證書

Certificate No. : C164166
證書編號

ITEM TESTED / 送檢項目 (Job No. / 序引編號 : IC16-1465) Date of Receipt / 收件日期 : 20 July 2016

Description / 儀器名稱 : Precision Integrating Sound Level Meter
Manufacturer / 製造商 : Rion
Model No. / 型號 : NL-18
Serial No. / 編號 : 00360030
Supplied By / 委託者 : Envirotech Services Co.
Room 113, 1/F, My Loft, 9 Hoi Wing Road, Tuen Mun,
New Territories, Hong Kong

TEST CONDITIONS / 測試條件

Temperature / 溫度 : $(23 \pm 2)^{\circ}\text{C}$ Relative Humidity / 相對濕度 : $(55 \pm 20)\%$
Line Voltage / 電壓 : ---

TEST SPECIFICATIONS / 測試規範

Calibration check


DATE OF TEST / 測試日期 : 29 July 2016

TEST RESULTS / 測試結果

The results apply to the particular unit-under-test only.
The results do not exceed manufacturer's specification.
The results are detailed in the subsequent page(s).

The test equipment used for calibration are traceable to National Standards via :

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- Agilent Technologies / Keysight Technologies
- Rohde & Schwarz Laboratory, Germany
- Fluke Everett Service Center, USA

Tested By : 
測試 : H T Wong
Technical Officer

Certified By : 
核證 : K C Lee
Project Engineer

Date of Issue : 1 August 2016
簽發日期

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室書面批准。

Sun Creation Engineering Limited – Calibration & Testing Laboratory

c/o 4/F, Tsing Shan Wan Exchange Building, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong

輝創工程有限公司 – 校正及檢測實驗室

c/o 香港新界屯門興安里一號青山灣機樓四樓

Tel/電話: 2927 2606

Fax/傳真: 2744 8986

E-mail/電郵: callab@suncreation.com

Website/網址: www.suncreation.com

Page 1 of 4

Certificate of Calibration

校正證書

Certificate No. : C164166
證書編號

- The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours, and switched on to warm up for over 10 minutes before the commencement of the test.
- Self-calibration was performed before the test.
- The results presented are the mean of 3 measurements at each calibration point.
- Test equipment :

Equipment ID	Description	Certificate No.
CL280	40 MHz Arbitrary Waveform Generator	C160077
CL281	Multifunction Acoustic Calibrator	PA160023

- Test procedure : MA101N.

- Results :

- 6.1 Sound Pressure Level

- 6.1.1 Reference Sound Pressure Level

UUT Setting				Applied Value		UUT Reading (dB)	IEC 60651 Type 1 Spec. (dB)
Range (dB)	Mode	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)		
50 - 110	LA	A	Fast	94.00	1	94.4	± 0.7

- 6.1.2 Linearity

UUT Setting				Applied Value		UUT Reading (dB)
Range (dB)	Mode	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)	
60 - 120	LA	A	Fast	94.00	1	94.4 (Ref.)
				104.00		104.4
				114.00		114.4

IEC 60651 Type 1 Spec. : ± 0.4 dB per 10 dB step and ± 0.7 dB for overall different.

- 6.2 Time Weighting

- 6.2.1 Continuous Signal

UUT Setting				Applied Value		UUT Reading (dB)	IEC 60651 Type 1 Spec. (dB)
Range (dB)	Mode	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)		
50 - 110	LA	A	Fast	94.00	1	94.4	Ref.
			Slow			94.4	± 0.1

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室書面批准。

Certificate of Calibration

校正證書

Certificate No. : C164166
證書編號

6.2.2 Tone Burst Signal (2 kHz)

UUT Setting				Applied Value		UUT Reading (dB)	IEC 60651 Type 1 Spec. (dB)
Range (dB)	Mode	Frequency Weighting	Time Weighting	Level (dB)	Burst Duration		
50 -110	LA	A	Fast	106.00	Continuous	106.0	Ref.
	LAmx				200 ms	105.1	-1.0 ± 1.0
	LA	Slow	Continuous		106.0	Ref.	
	LAmx		500 ms		102.4	-4.1 ± 1.0	

6.3 Frequency Weighting

6.3.1 A-Weighting

UUT Setting				Applied Value		UUT Reading (dB)	IEC 60651 Type 1 Spec. (dB)
Range (dB)	Mode	Frequency Weighting	Time Weighting	Level (dB)	Freq.		
50 - 110	LA	A	Fast	94.00	31.5 Hz	54.7	-39.4 ± 1.5
					63 Hz	68.0	-26.2 ± 1.5
					125 Hz	78.0	-16.1 ± 1.0
					250 Hz	85.6	-8.6 ± 1.0
					500 Hz	91.1	-3.2 ± 1.0
					1 kHz	94.4	Ref.
					2 kHz	95.7	+1.2 ± 1.0
					4 kHz	95.5	+1.0 ± 1.0
					8 kHz	93.3	-1.1 (+1.5 ; -3.0)
					12.5 kHz	90.1	-4.3 (+3.0 ; -6.0)

6.3.2 C-Weighting

UUT Setting				Applied Value		UUT Reading (dB)	IEC 60651 Type 1 Spec. (dB)
Range (dB)	Mode	Frequency Weighting	Time Weighting	Level (dB)	Freq.		
50 - 110	LC	C	Fast	94.00	31.5 Hz	91.3	-3.0 ± 1.5
					63 Hz	93.5	-0.8 ± 1.5
					125 Hz	94.2	-0.2 ± 1.0
					250 Hz	94.4	0.0 ± 1.0
					500 Hz	94.5	0.0 ± 1.0
					1 kHz	94.4	Ref.
					2 kHz	94.3	-0.2 ± 1.0
					4 kHz	93.6	-0.8 ± 1.0
					8 kHz	91.4	-3.0 (+1.5 ; -3.0)
					12.5 kHz	88.1	-6.2 (+3.0 ; -6.0)

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。

Certificate of Calibration

校正證書

Certificate No. : C164166

證書編號

6.4 Time Averaging

UUT Setting				Applied Value					UUT	IEC 60804
Range (dB)	Mode	Frequency Weighting	Integrating Time	Freq. (kHz)	Burst Duration (ms)	Burst Duty Factor	Burst Level (dB)	Equivalent Level (dB)	Reading (dB)	Type 1 Spec. (dB)
50 - 110	LAeq	A	10 sec.	4	1		110	100	100.1	± 0.5
			60 sec.					90	89.9	± 0.5
			5 min.					80	79.6	± 1.0
								70	69.7	± 1.0

Remarks : - UUT Microphone Model No. : UC-53A & S/N : 307435

- Mfr's Spec. : IEC 60651 Type 1 & IEC 60804 Type 1

- Uncertainties of Applied Value :

94 dB	31.5 Hz - 125 Hz	: ± 0.35 dB
	250 Hz - 500 Hz	: ± 0.30 dB
	1 kHz	: ± 0.20 dB
	2 kHz - 4 kHz	: ± 0.35 dB
	8 kHz	: ± 0.45 dB
	12.5 kHz	: ± 0.70 dB
104 dB	: 1 kHz	: ± 0.10 dB (Ref. 94 dB)
114 dB	: 1 kHz	: ± 0.10 dB (Ref. 94 dB)
	Burst equivalent level	: ± 0.2 dB (Ref. 110 dB continuous sound level)

- The uncertainties are for a confidence probability of not less than 95 %.

Note :

The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.



輝創工程有限公司

Sun Creation Engineering Limited

Calibration and Testing Laboratory

Certificate of Calibration

校正證書

Certificate No. : C163248
證書編號

ITEM TESTED / 送檢項目 (Job No. / 序引編號 : IC16-1307) Date of Receipt / 收件日期 : 10 June 2016

Description / 儀器名稱 : Sound Level Calibrator
Manufacturer / 製造商 : Rion
Model No. / 型號 : NC-73
Serial No. / 編號 : 10997142
Supplied By / 委託者 : Envirotech Services Co.
Room 113, 1/F, My Loft, 9 Hoi Wing Road, Tuen Mun,
New Territories, Hong Kong

TEST CONDITIONS / 測試條件

Temperature / 溫度 : $(23 \pm 2)^{\circ}\text{C}$ Relative Humidity / 相對濕度 : $(55 \pm 20)\%$
Line Voltage / 電壓 : ---

TEST SPECIFICATIONS / 測試規範

Calibration check


DATE OF TEST / 測試日期 : 15 June 2016


TEST RESULTS / 測試結果

The results apply to the particular unit-under-test only.
The results do not exceed manufacturer's specification.
The results are detailed in the subsequent page(s).

The test equipment used for calibration are traceable to National Standards via :

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- Agilent Technologies / Keysight Technologies
- Rohde & Schwarz Laboratory, Germany
- Fluke Everett Service Center, USA

Tested By : 
測試 : H T Wong
Technical Officer

Certified By : 
核證 : K C Lee
Project Engineer

Date of Issue : 17 June 2016
簽發日期

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室書面批准。

Certificate of Calibration

校正證書

Certificate No. : C163248
證書編號

- The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours before the commencement of the test.
- The results presented are the mean of 3 measurements at each calibration point.
- Test equipment :

Equipment ID	Description	Certificate No.
CL130	Universal Counter	C153519
CL281	Multifunction Acoustic Calibrator	PA160023
TST150A	Measuring Amplifier	C161175

- Test procedure : MA100N.

- Results :

5.1 Sound Level Accuracy

UUT Nominal Value	Measured Value (dB)	Mfr's Spec. (dB)	Uncertainty of Measured Value (dB)
94 dB, 1 kHz	93.7	± 0.5	± 0.2

5.2 Frequency Accuracy

UUT Nominal Value (kHz)	Measured Value (kHz)	Mfr's Spec.	Uncertainty of Measured Value (Hz)
1	0.985	1 kHz $\pm 2\%$	± 1

Remark : The uncertainties are for a confidence probability of not less than 95 %.

Note :


The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.

G. Graphical Plots of the Monitoring Results

Air Quality Monitoring Result at Station AM1 (1-hour TSP)

Date	Weather Condition	Time	Conc. ($\mu\text{g}/\text{m}^3$)			Action Level ($\mu\text{g}/\text{m}^3$)	Limit Level ($\mu\text{g}/\text{m}^3$)
			1 st Hour	2 nd Hour	3 rd Hour		
02-Nov-16	Sunny	10:40 - 16:00	80	88	97	273.7	500
08-Nov-16	Sunny	10:48 - 16:00	78	85	92	273.7	500
14-Nov-16	Sunny	10:42 - 16:00	78	65	70	273.7	500
18-Nov-16	Cloudy	8:00 - 11:00	59	64	60	273.7	500
24-Nov-16	Cloudy	10:40 - 16:00	49	52	55	273.7	500
30-Nov-16	Sunny	10:42 - 16:00	49	53	56	273.7	500


Graphical Presentation of Air Quality Monitoring Result at Station AM1 (1-hour TSP)

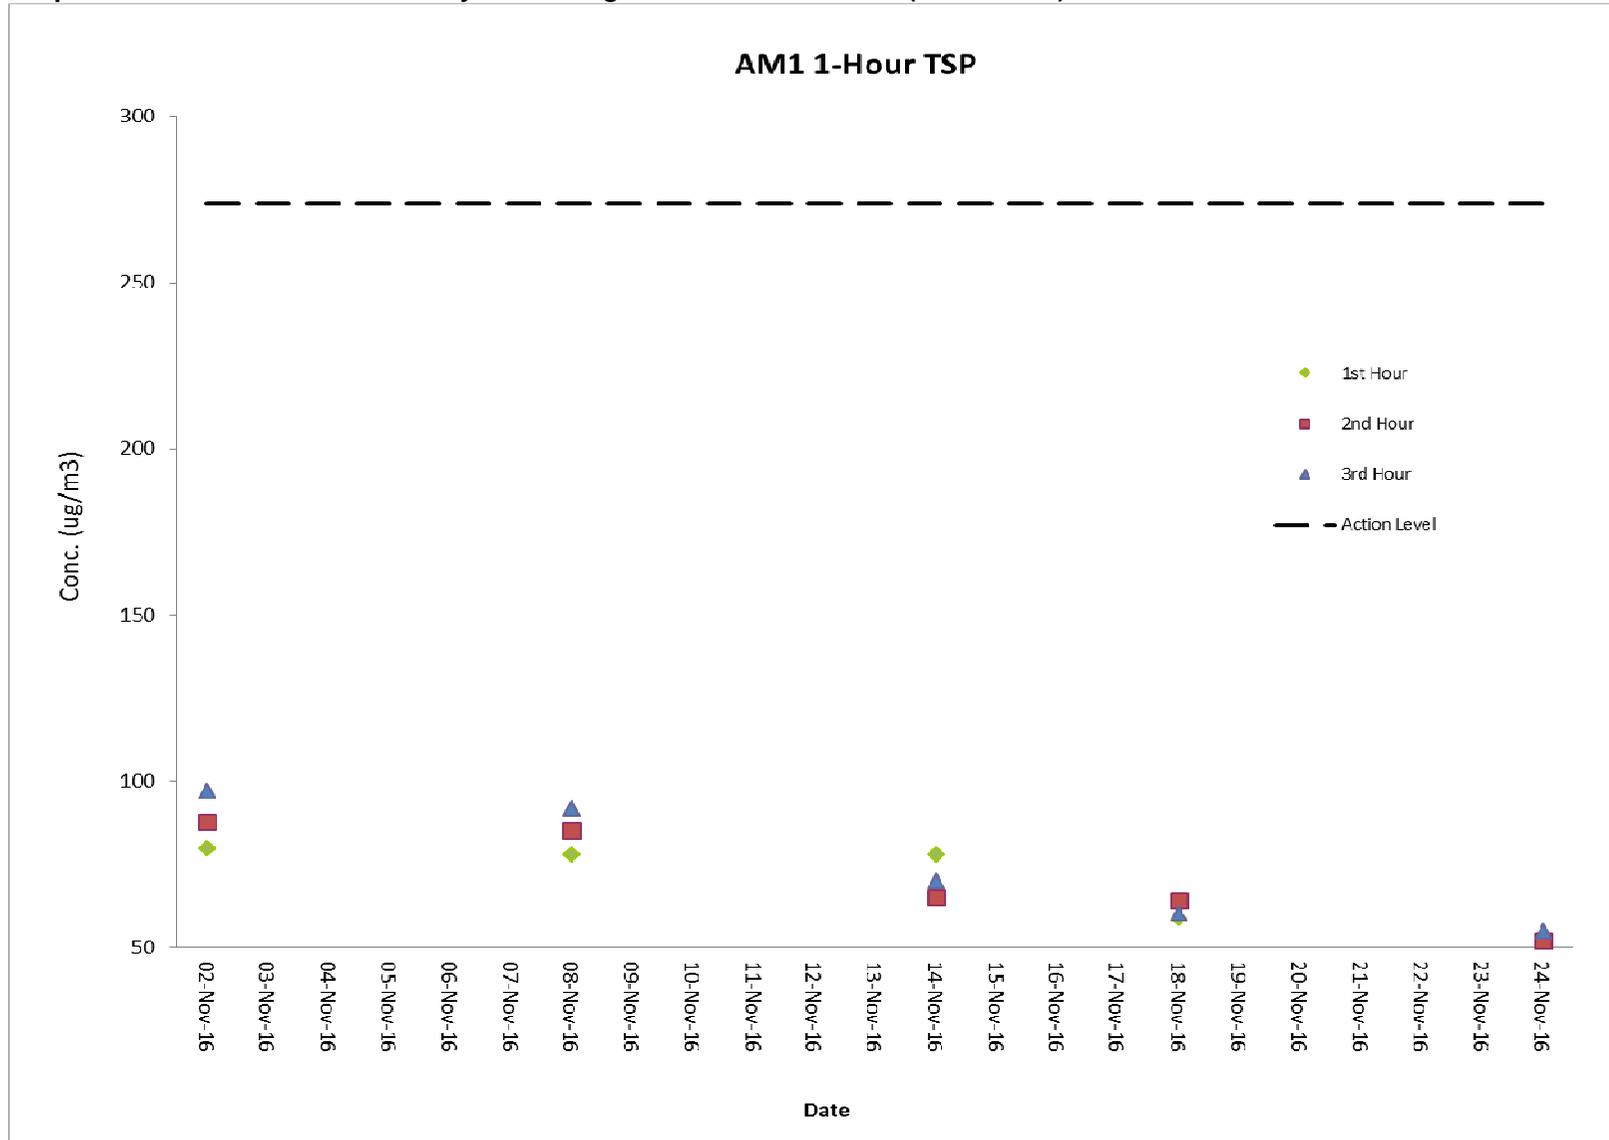

Air Quality Monitoring Result at Station AM2A (1-hour TSP)

Date	Weather Condition	Time	Conc. ($\mu\text{g}/\text{m}^3$)			Action Level ($\mu\text{g}/\text{m}^3$)	Limit Level ($\mu\text{g}/\text{m}^3$)
			1 st Hour	2 nd Hour	3 rd Hour		
02-Nov-16	Sunny	10:52 - 16:10	81	90	97	274.2	500
08-Nov-16	Sunny	11:00 - 16:10	80	88	96	274.2	500
14-Nov-16	Sunny	10:54 - 16:10	109	111	121	274.2	500
18-Nov-16	Cloudy	8:14 - 11:14	69	71	77	274.2	500
24-Nov-16	Cloudy	10:52 - 16:10	63	54	58	274.2	500
30-Nov-16	Sunny	10:54 - 16:10	60	58	59	274.2	500


Graphical Presentation of Air Quality Monitoring Result at Station AM2A (1-hour TSP)

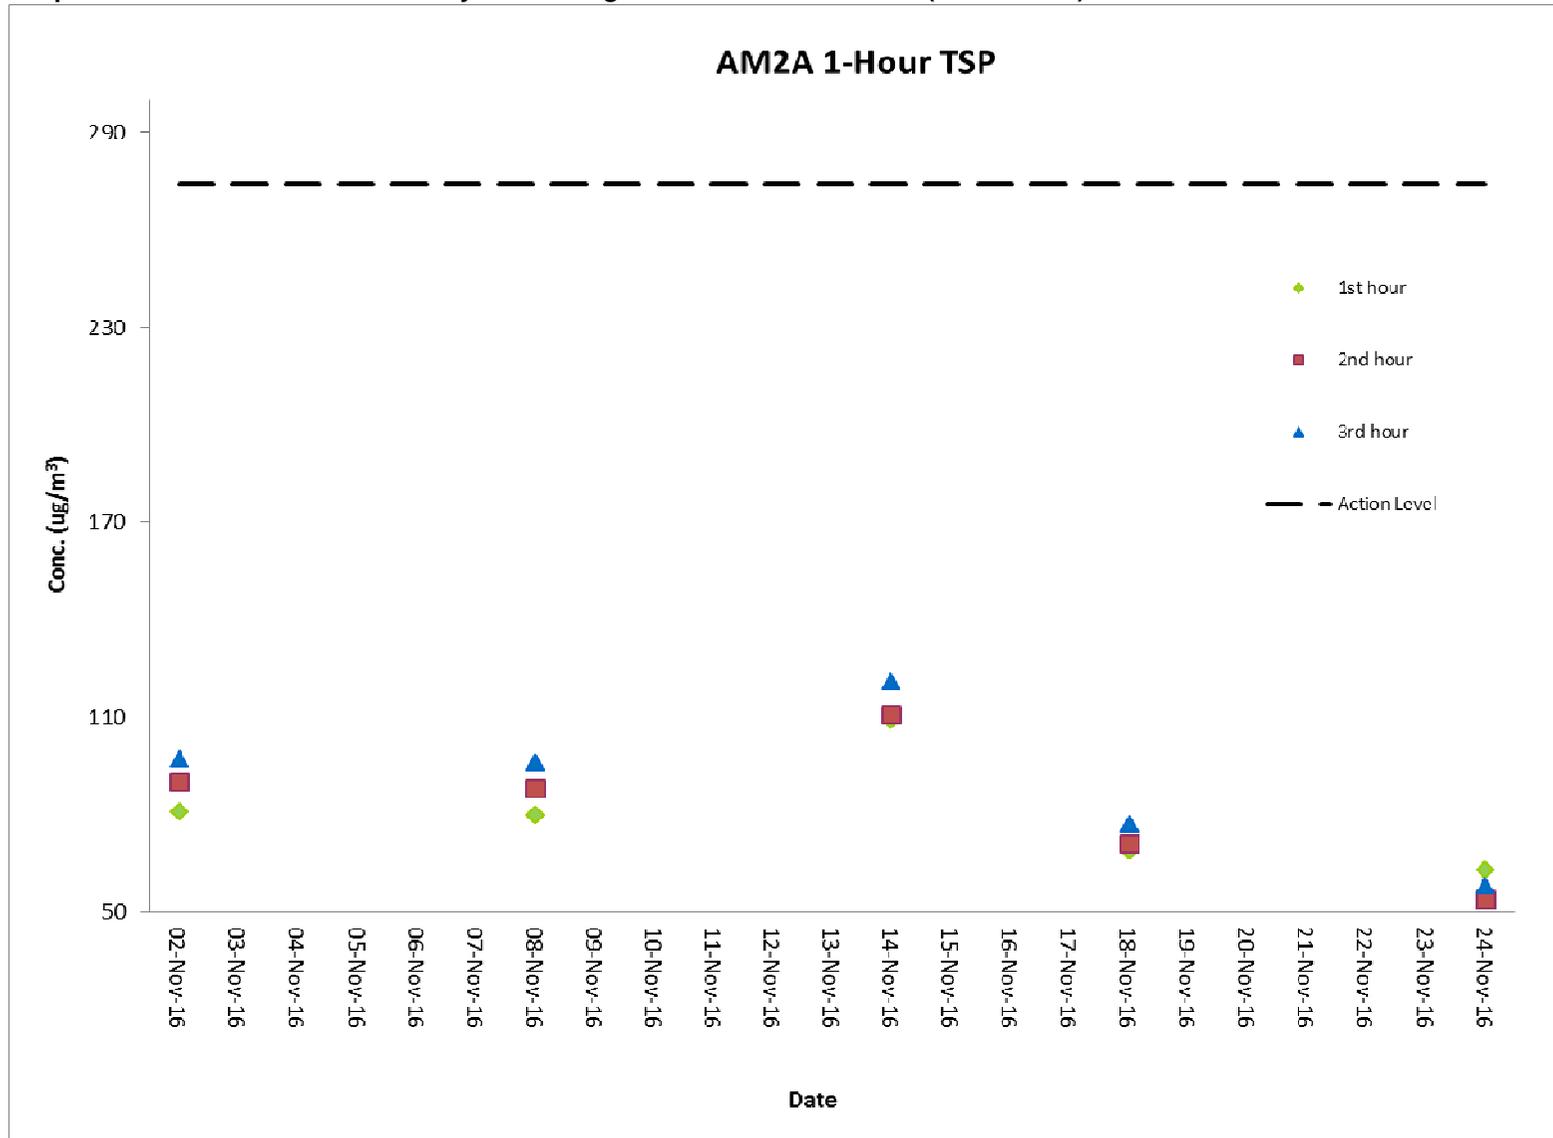

Air Quality Monitoring Result at Station AM1 (24-hour TSP)

Start		Finish		Filter Weight (g)		Elapsed Time Reading		Sampling Time (hrs)	Flow Rate (m ³ /min)			Conc. (µg/m ³)	Weather Condition	Action Level	Limit Level
Date	Time	Date	Time	Initial	Final	Initial	Final		Initial	Final	Average				
02-Nov-16	10:42	03-Nov-16	10:42	2.7984	2.877	20208.38	20232.38	24	1.23	1.23	1.23	44	Sunny	143.6	260
08-Nov-16	10:50	09-Nov-16	10:50	2.7901	2.88	20232.38	20256.38	24	1.23	1.23	1.23	51	Sunny	143.6	260
14-Nov-16	10:40	15-Nov-16	10:40	2.7656	2.8575	20256.38	20280.38	24	1.23	1.23	1.23	52	Sunny	143.6	260
18-Nov-16	08:02	19-Nov-16	08:02	2.7589	2.8506	20280.38	20304.38	24	1.23	1.23	1.23	52	Cloudy	143.6	260
24-Nov-16	10:42	25-Nov-16	10:42	2.748	2.8295	20304.38	20328.38	24	1.23	1.23	1.23	46	Cloudy	143.6	260
30-Nov-16	10:40	01-Dec-16	10:40	2.75	2.84	20328.38	20352.38	24	1.23	1.23	1.23	51	Sunny	143.6	260


Graphical Presentation of Air Quality Monitoring Result at Station AM1 (24-hour TSP)

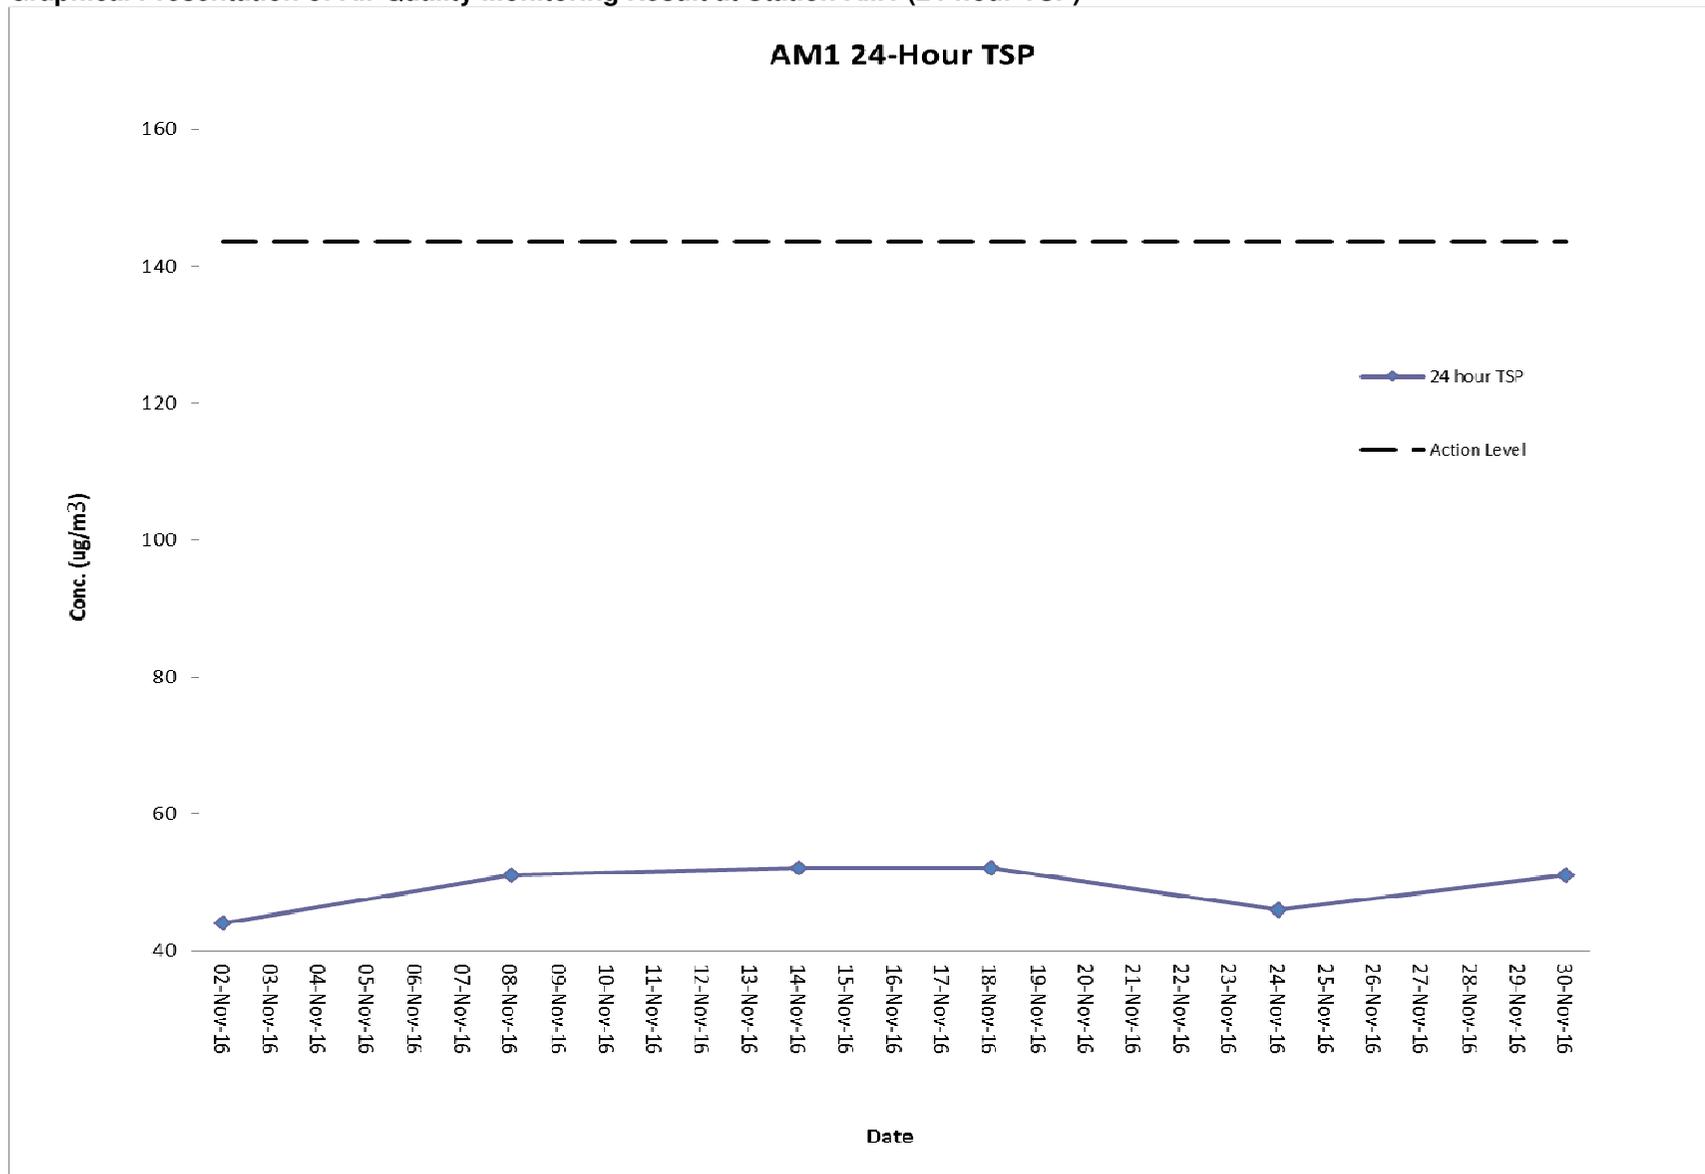

Air Quality Monitoring Result at Station AM2A (24-hour TSP)

Start		Finish		Filter Weight (g)		Elapsed Time Reading		Sampling Time (hrs)	Flow Rate (m ³ /min)			Conc. (µg/m ³)	Weather Condition	Action Level	Limit Level
Date	Time	Date	Time	Initial	Final	Initial	Final		Initial	Final	Average				
02-Nov-16	10:55	03-Nov-16	10:55	2.7816	2.8722	15863.59	15887.59	24	1.25	1.25	1.25	50	Sunny	151.1	260
08-Nov-16	11:02	09-Nov-16	11:02	2.7846	2.8882	15887.59	15911.59	24	1.25	1.25	1.25	58	Sunny	151.1	260
14-Nov-16	10:52	15-Nov-16	10:52	2.7633	2.8866	15911.59	15935.59	24	1.25	1.25	1.25	69	Sunny	151.1	260
18-Nov-16	08:12	19-Nov-16	08:12	2.7714	2.9009	15935.59	15959.59	24	1.25	1.25	1.25	72	Cloudy	151.1	260
24-Nov-16	10:54	25-Nov-16	10:54	2.7421	2.8575	15959.59	15983.59	24	1.25	1.25	1.25	64	Cloudy	151.1	260
30-Nov-16	10:52	01-Dec-16	10:52	2.7452	2.8511	15983.59	16007.59	24	1.25	1.25	1.25	59	Sunny	151.1	260

Graphical Presentation of Air Quality Monitoring Result at Station AM2A (24-hour TSP)

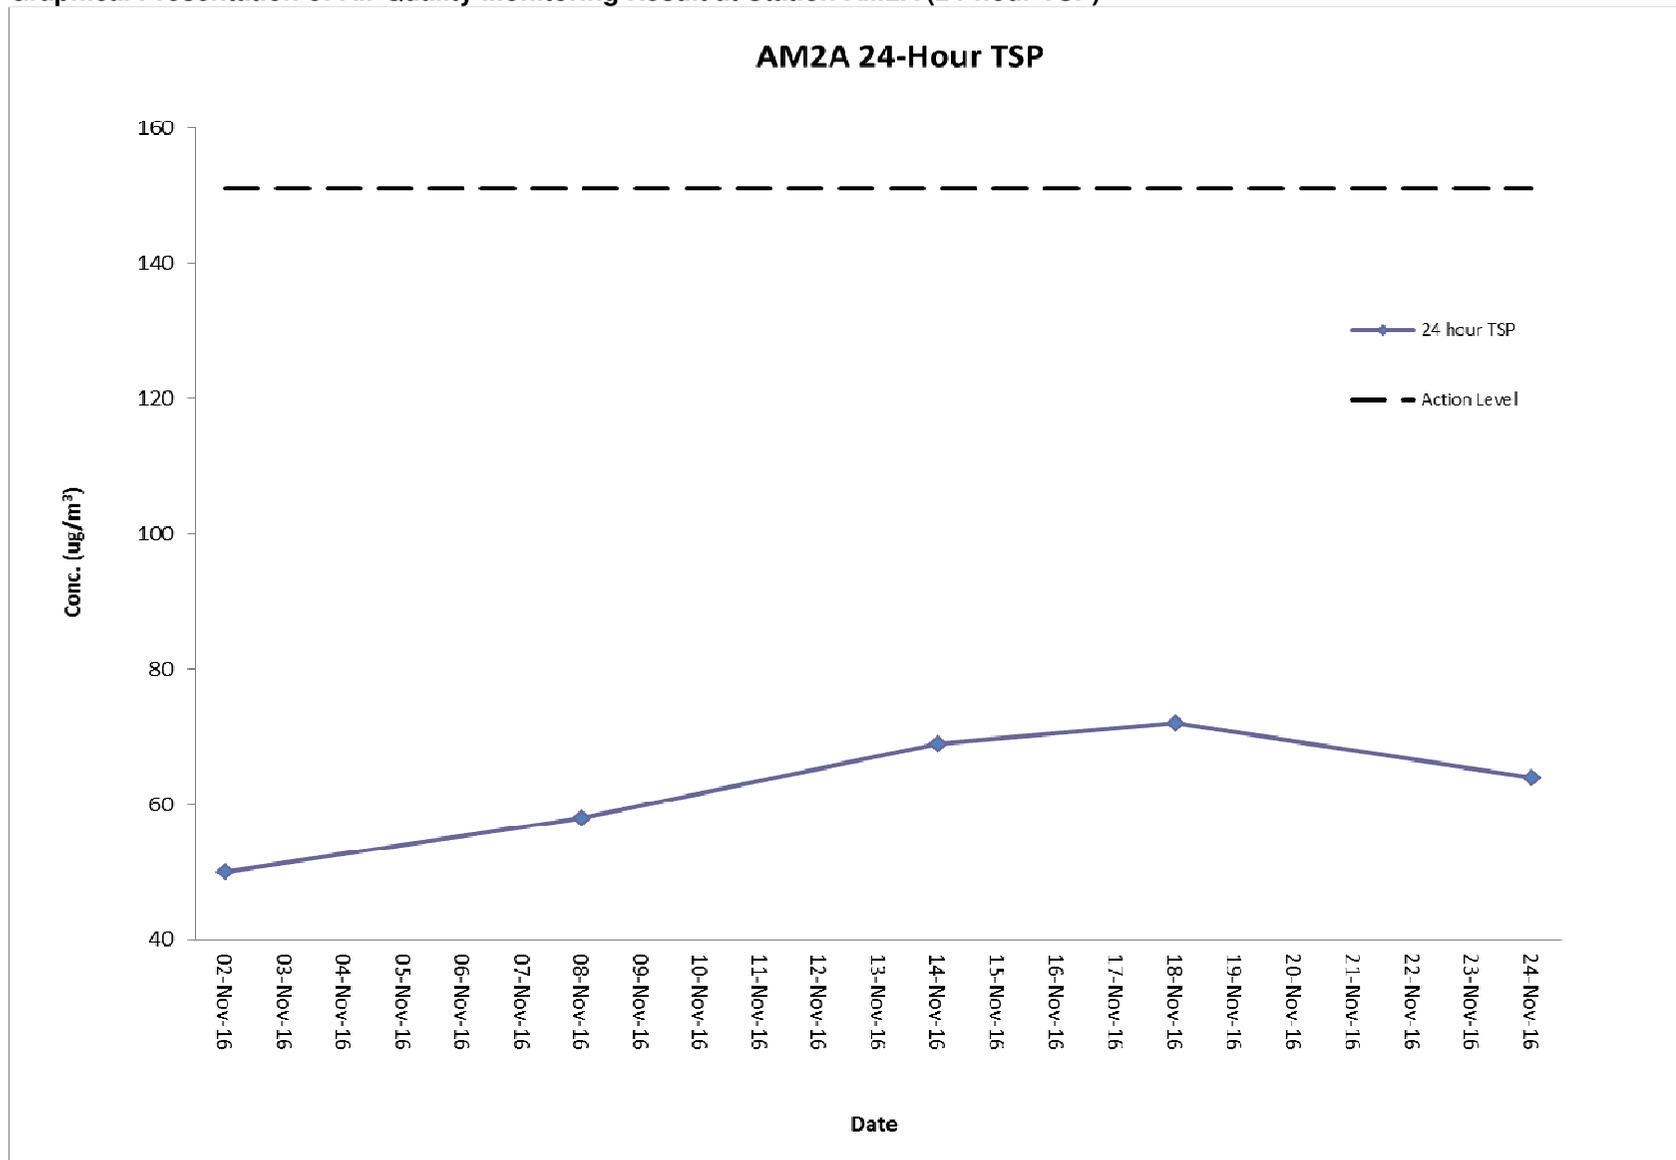

Noise Monitoring Result at Station NM1A

Date	Time	Measured L ₁₀ dB(A)	Measured L ₉₀ dB(A)	L _{eq} (30 min.) dB(A)
2-Nov-16	14:00	68.0	63.9	69.5
2-Nov-16	14:05	67.9	63.7	
2-Nov-16	14:10	69.0	64.0	
2-Nov-16	14:15	69.4	64.1	
2-Nov-16	14:20	67.9	63.8	
2-Nov-16	14:25	68.4	64.2	
8-Nov-16	14:00	68.0	63.7	69.9
8-Nov-16	14:05	67.9	62.7	
8-Nov-16	14:10	69.0	64.1	
8-Nov-16	14:15	70.0	63.9	
8-Nov-16	14:20	68.2	62.8	
8-Nov-16	14:25	70.2	63.8	
14-Nov-16	14:00	66.7	62.7	68.4
14-Nov-16	14:05	67.0	63.1	
14-Nov-16	14:10	67.9	63.4	
14-Nov-16	14:15	66.8	62.7	
14-Nov-16	14:20	67.7	63.7	
14-Nov-16	14:25	68.4	64.0	
24-Nov-16	14:00	67.1	63.2	68.5
24-Nov-16	14:05	66.8	62.4	
24-Nov-16	14:10	68.0	64.0	
24-Nov-16	14:15	67.8	63.7	
24-Nov-16	14:20	66.9	62.9	
24-Nov-16	14:25	68.8	64.1	
30-Nov-16	14:00	67.7	63.1	69.2
30-Nov-16	14:05	68.4	64.2	
30-Nov-16	14:10	68.8	64.1	
30-Nov-16	14:15	66.7	63.9	
30-Nov-16	14:20	68.7	64.1	
30-Nov-16	14:25	68.9	64.5	


Remarks:

+3dB (A) correction was applied to free-field measurement.



The station set-up of a free-field measurement at Station NM1A.


Graphical Presentation Noise Monitoring Result at Station NM1A

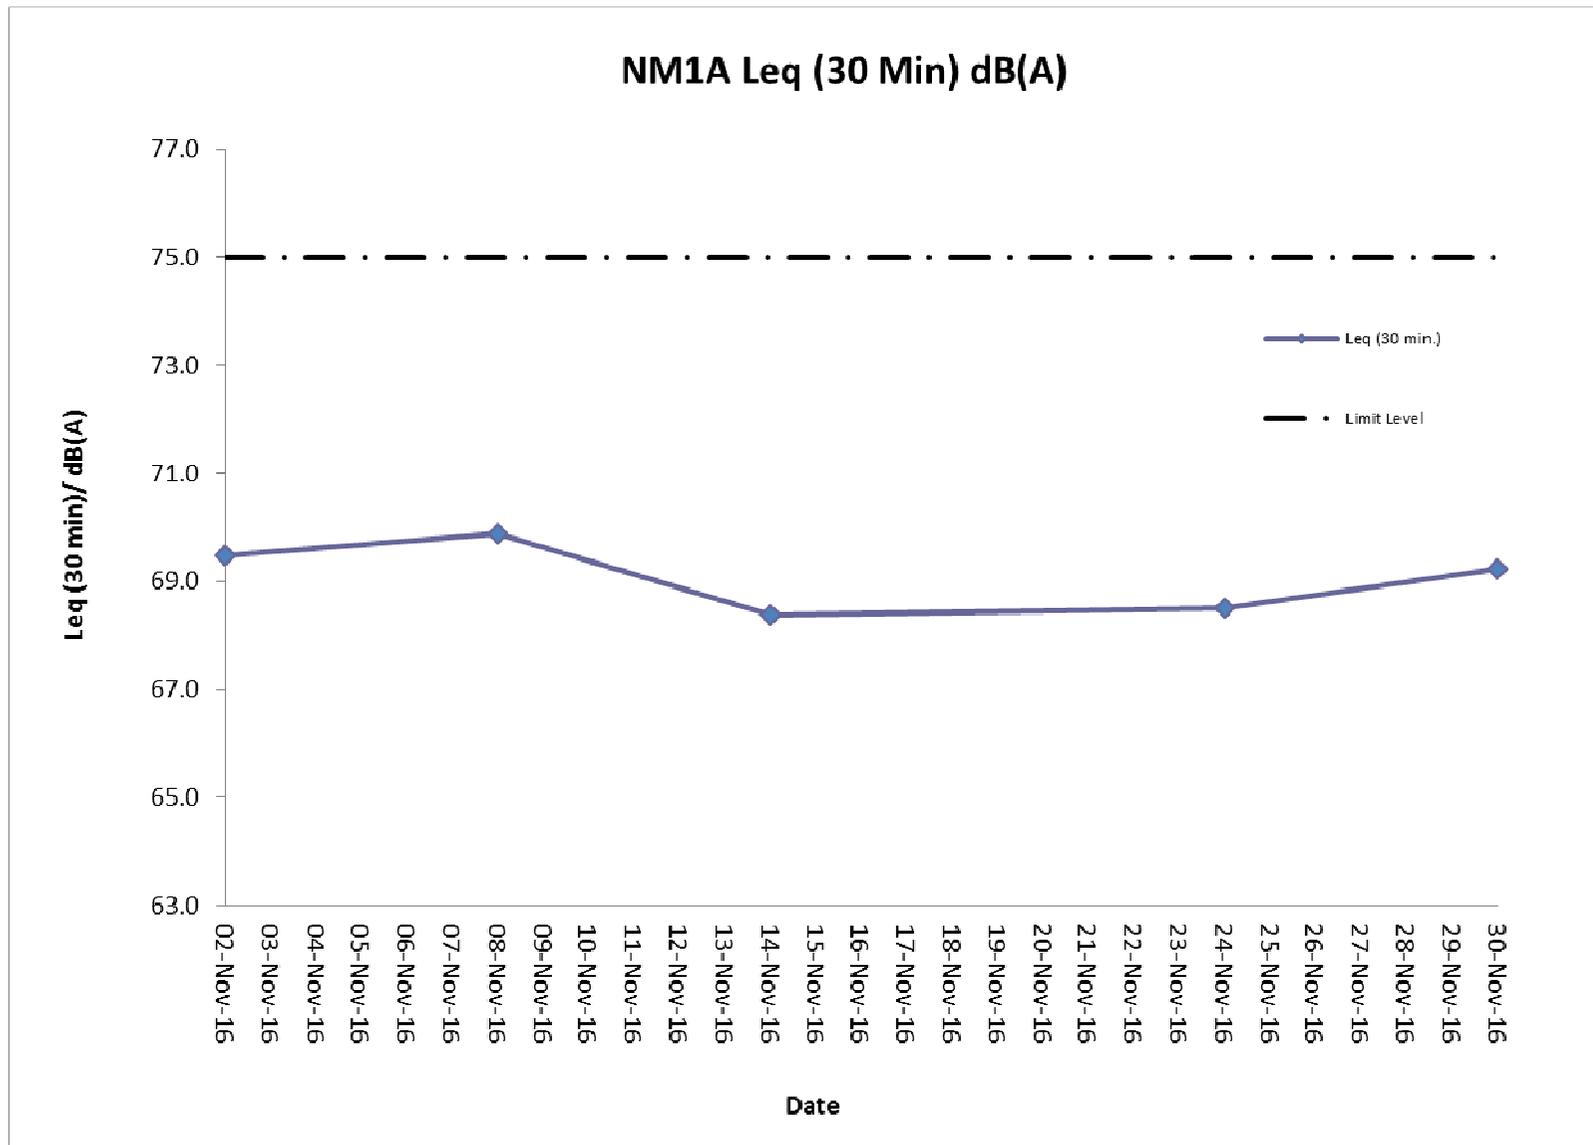

H. Meteorological Data Extracted from Hong Kong Observatory

Extract of Meteorological Observations for King's Park Automatic Weather Station, November 2016


Temperature Humidity:

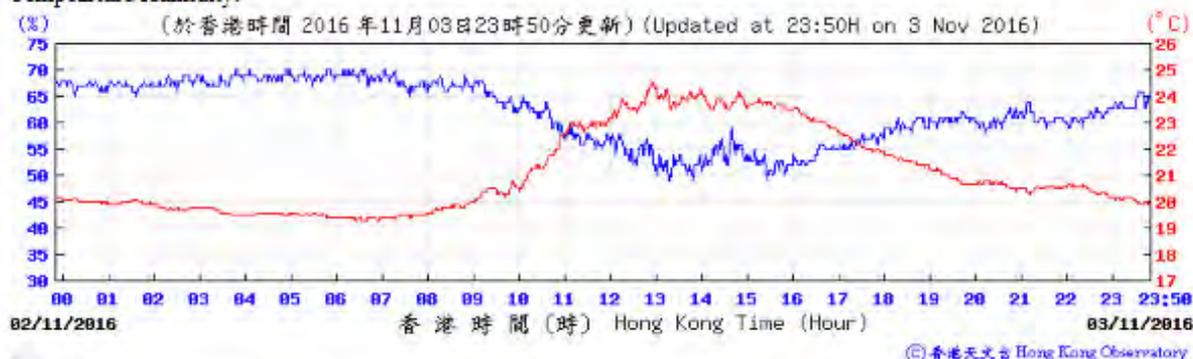


Pressure:




Wind Direction:

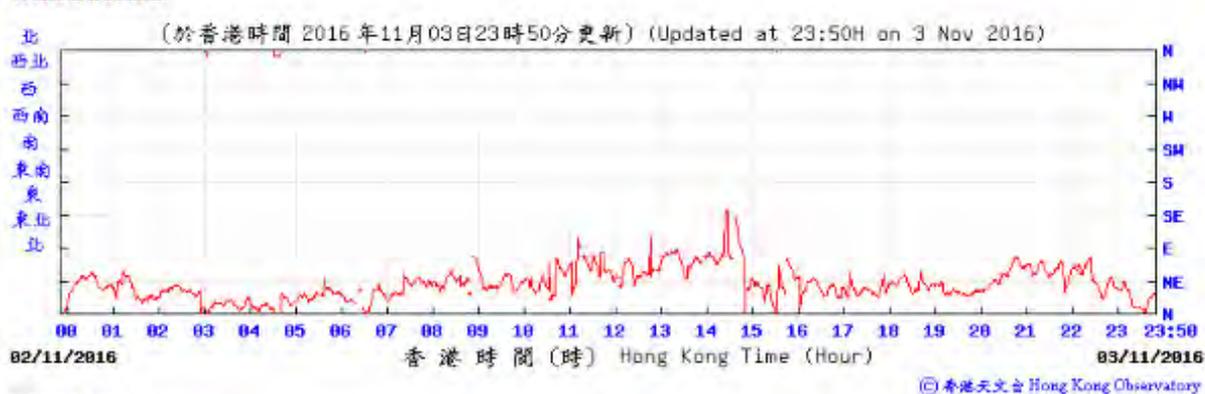


Wind Speed:

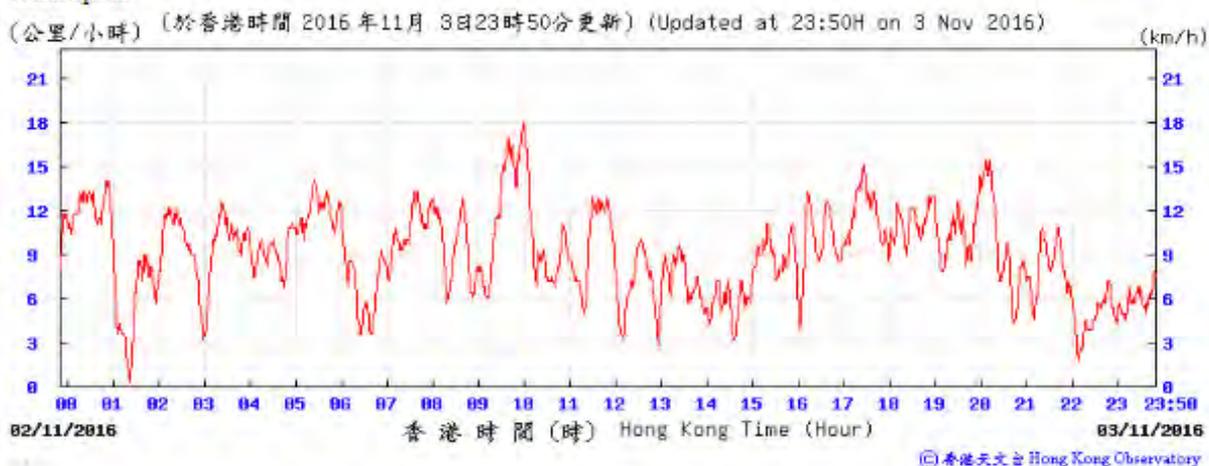


Temperature/Humidity:

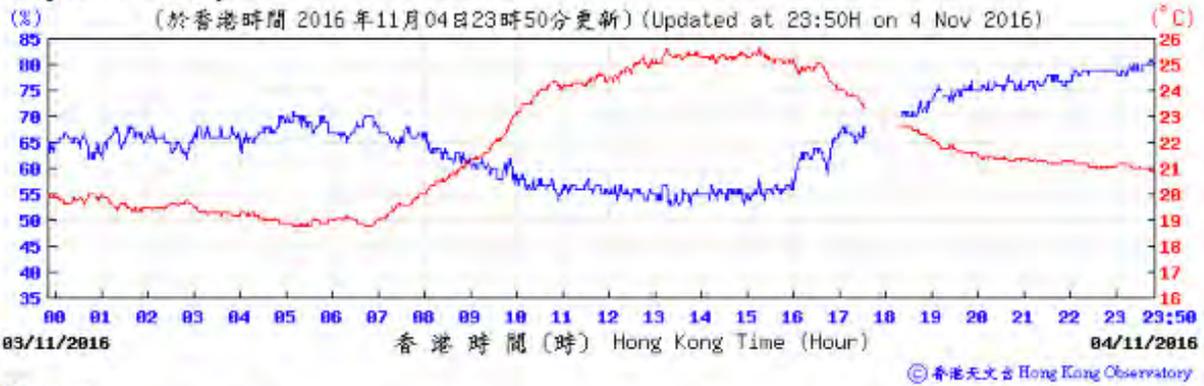


Pressure:

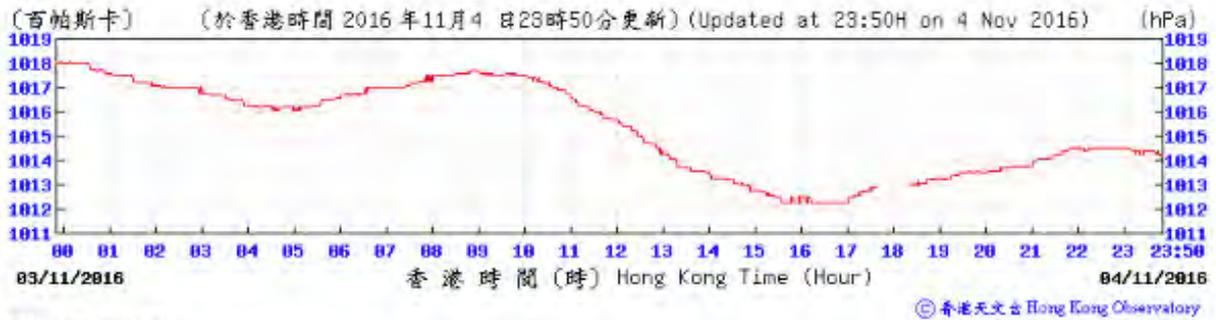


Wind Direction:

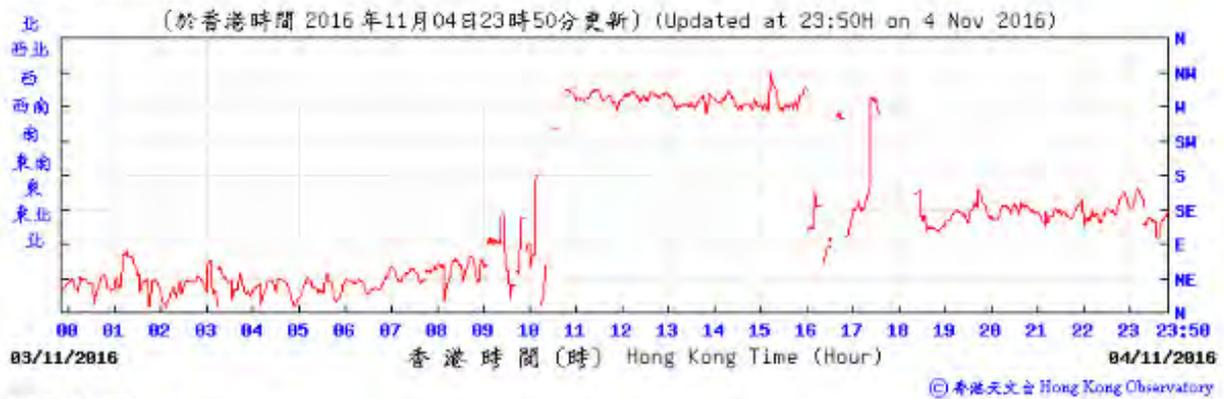

Wind Speed:

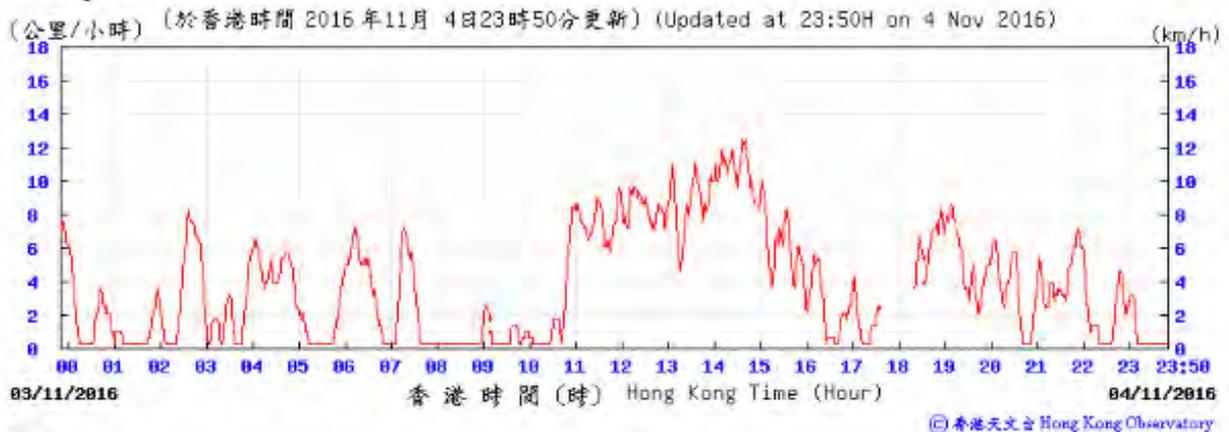


Temperature Humidity:

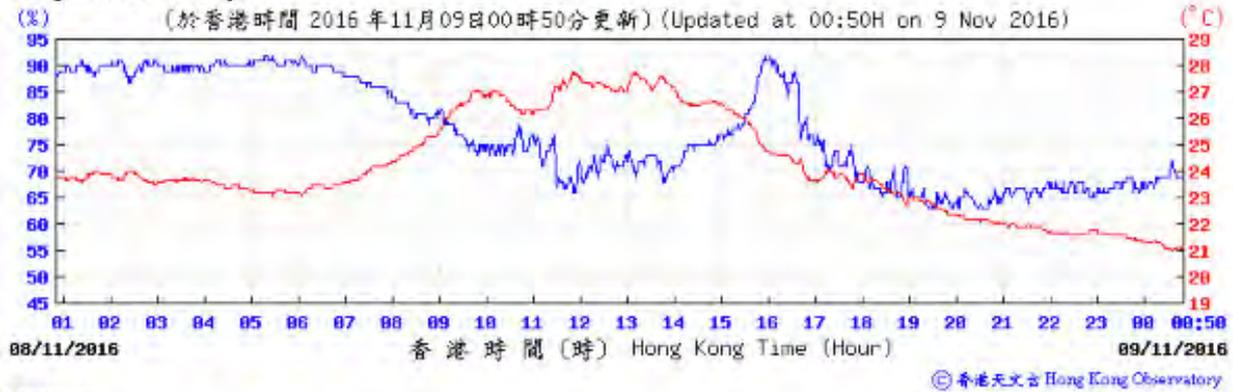

Pressure:




Wind Direction:

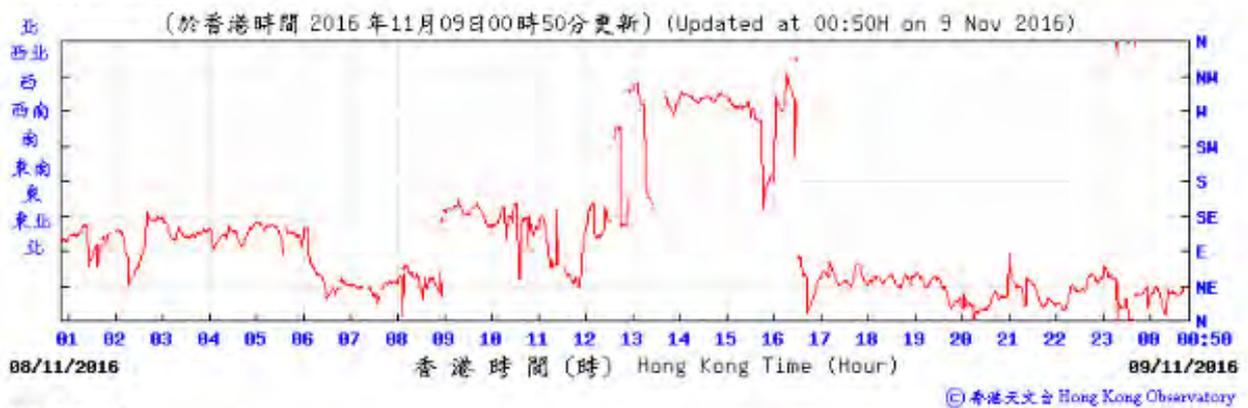


Wind Speed:




Temperature Humidity:

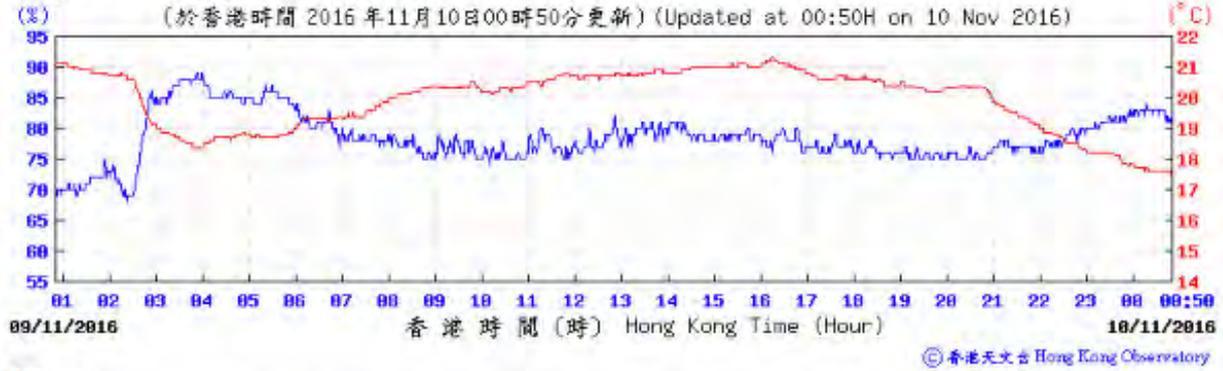


Pressure:

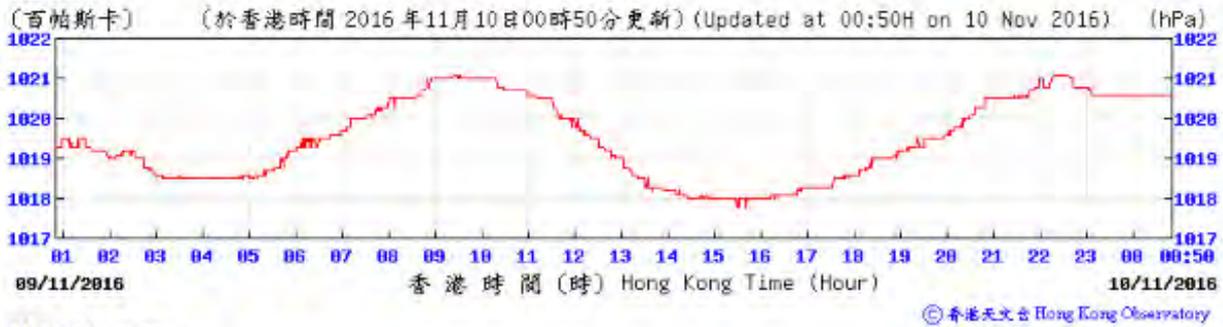


Wind Direction:

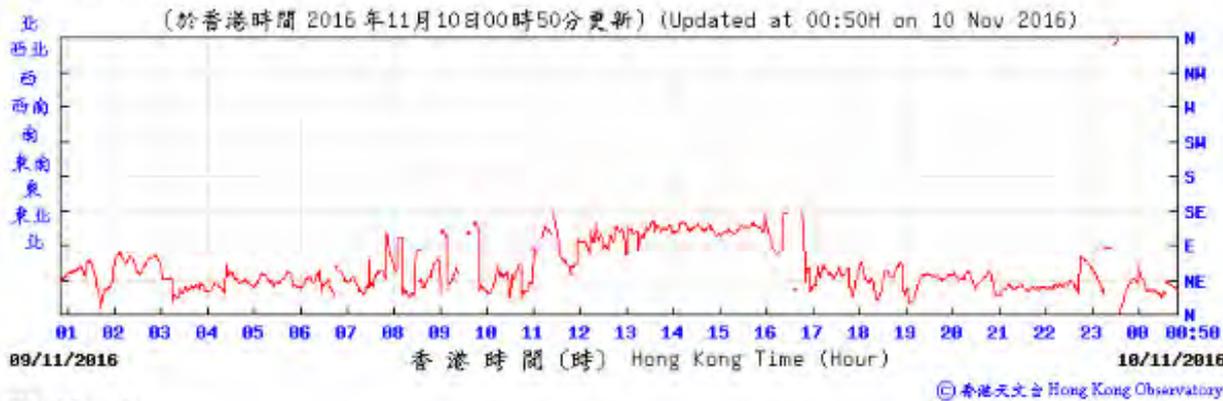


Wind Speed:

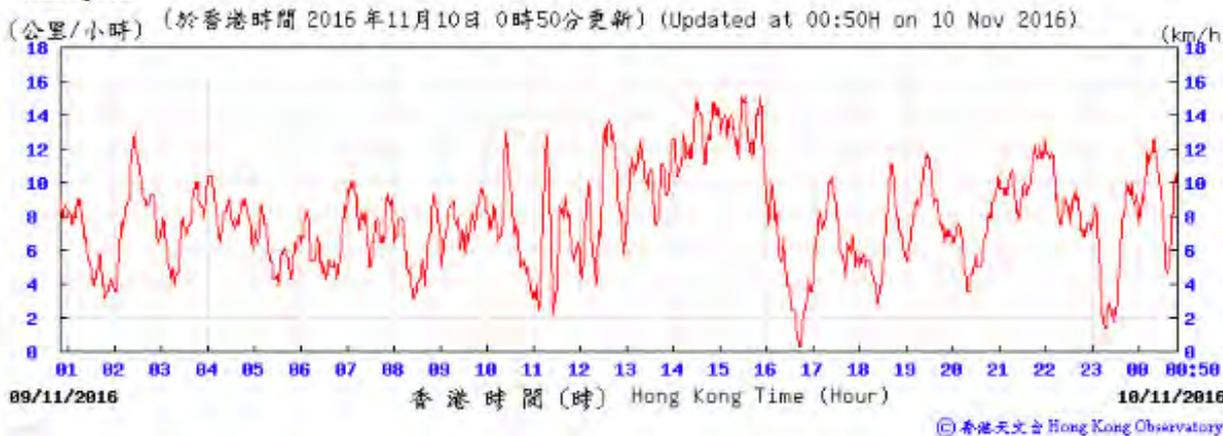


Temperature/Humidity:

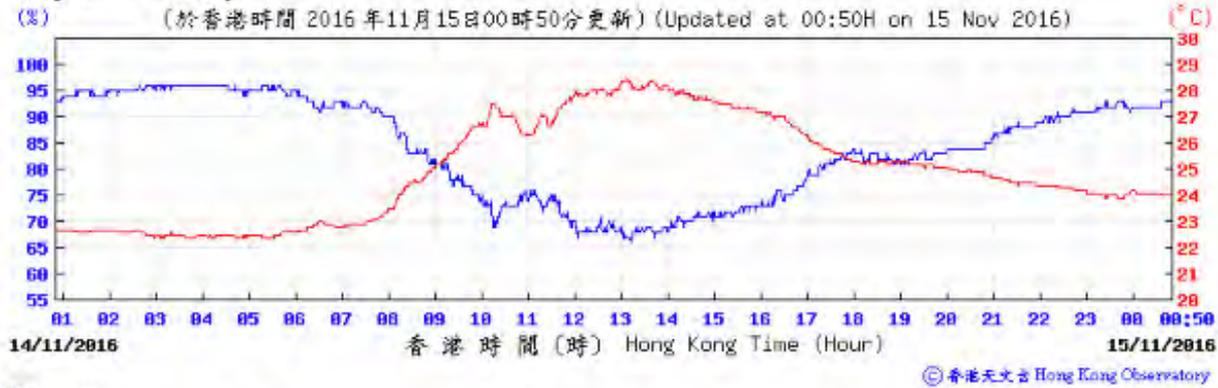


Pressure:

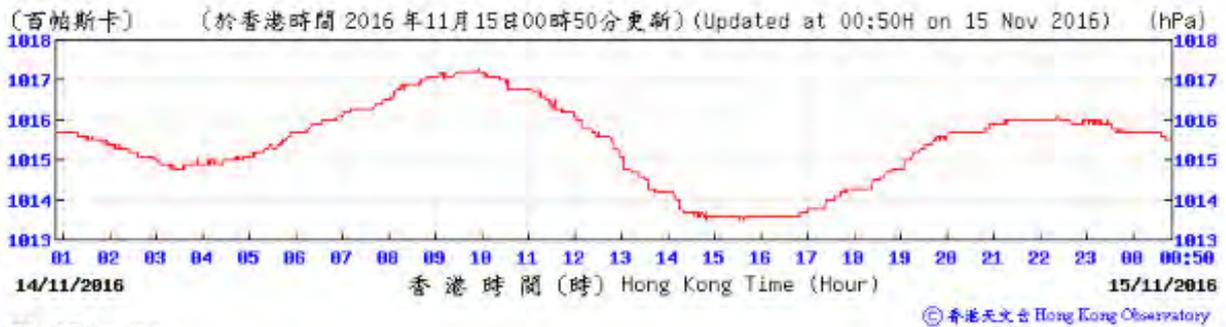


Wind Direction:

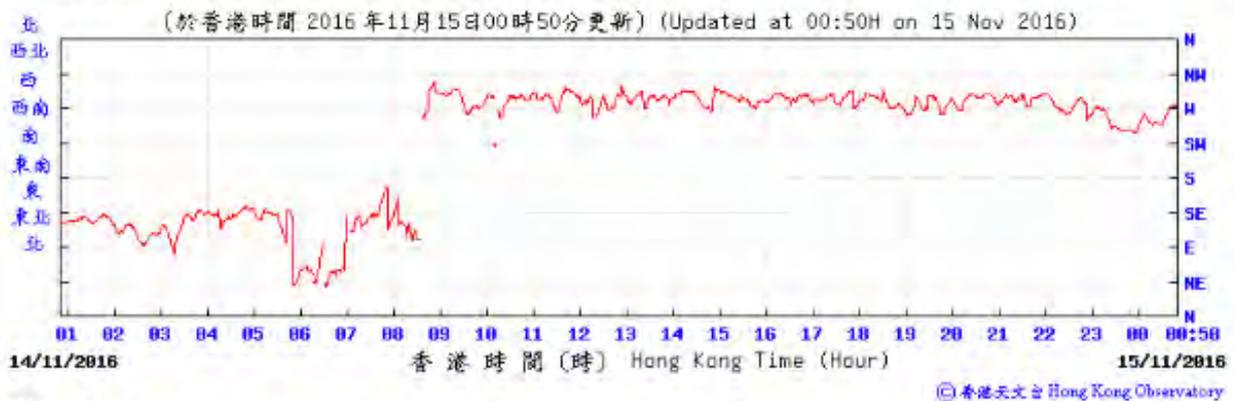

Wind Speed:

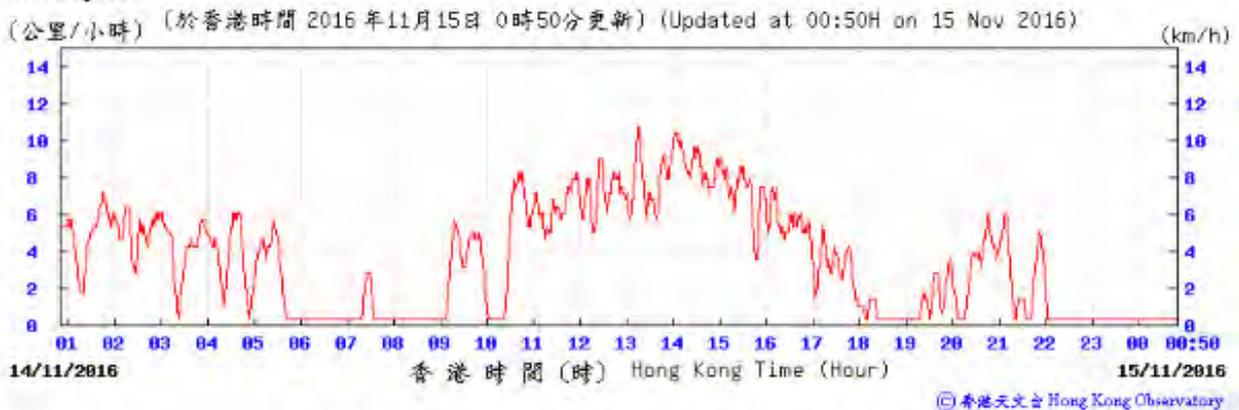


Temperature/Humidity:

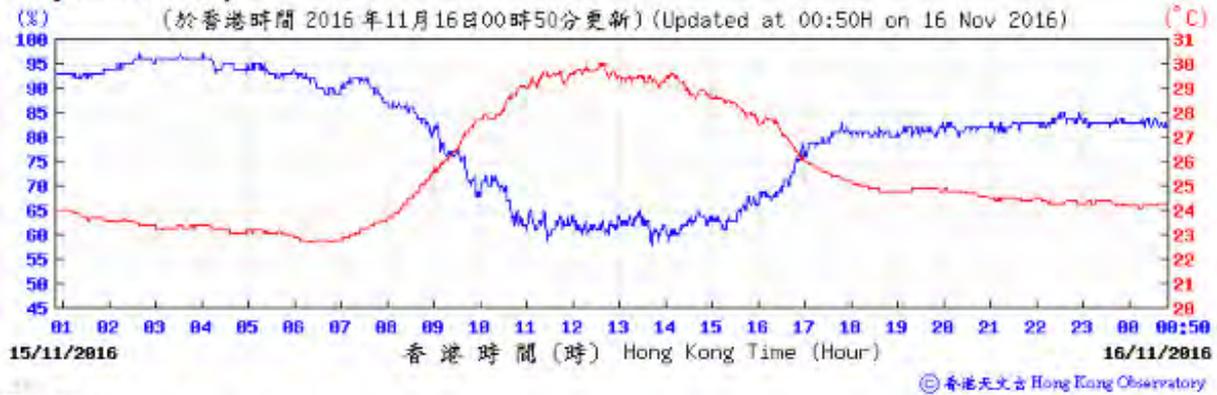


Pressure:




Wind Direction:

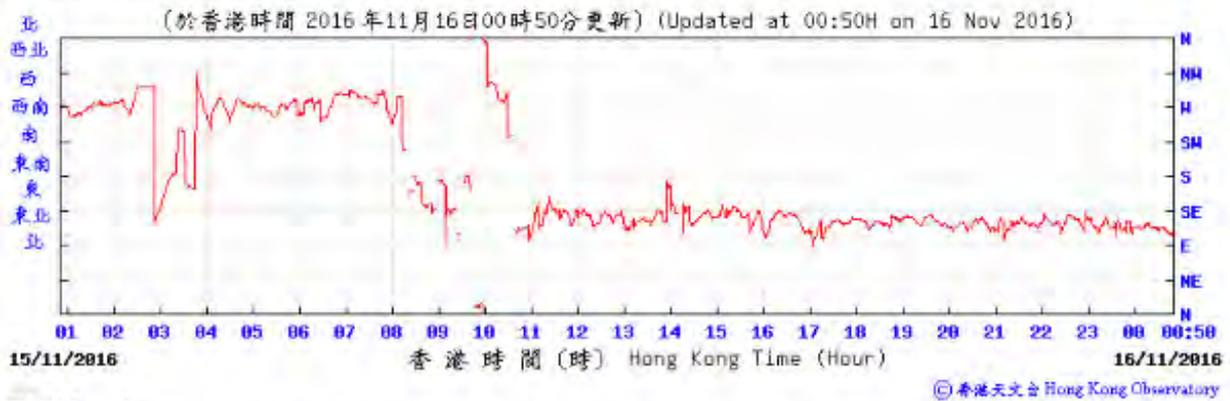


Wind Speed:

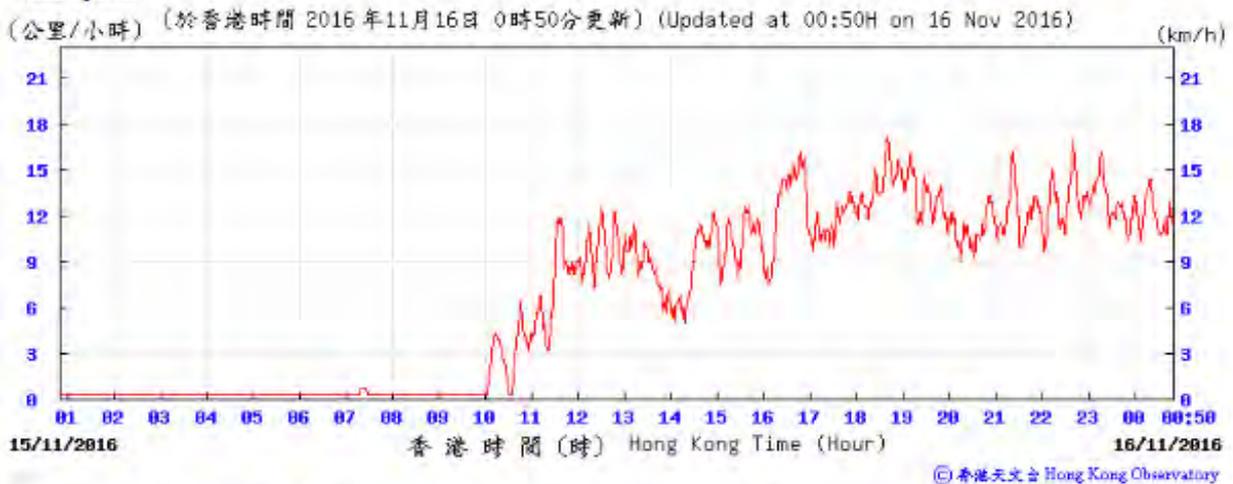


Temperature Humidity:

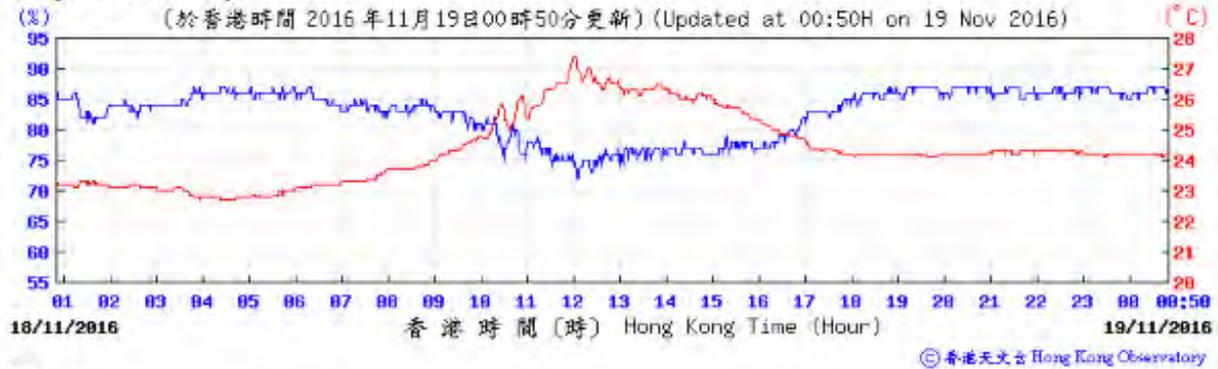


Pressure:

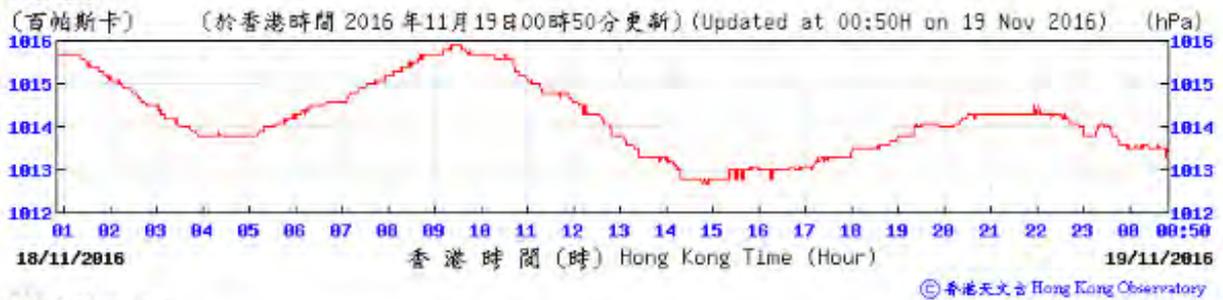


Wind Direction:

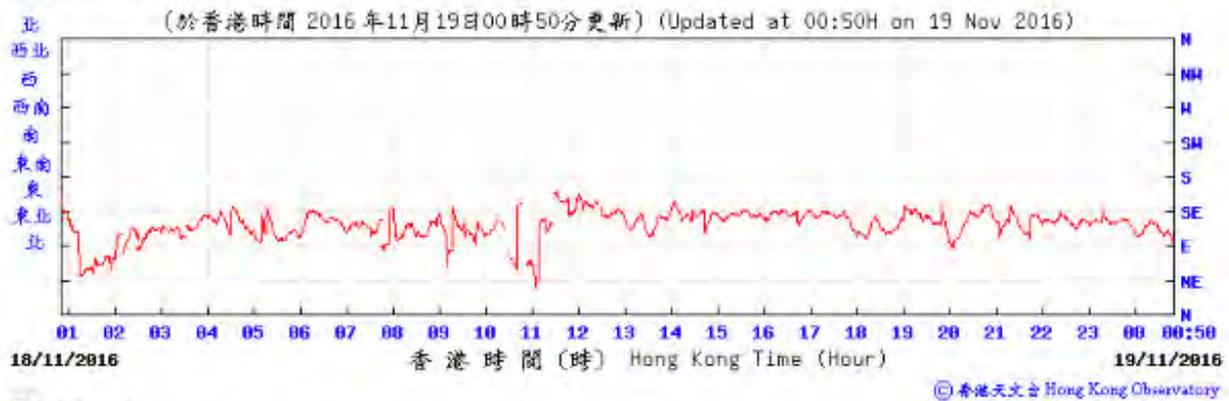

Wind Speed:

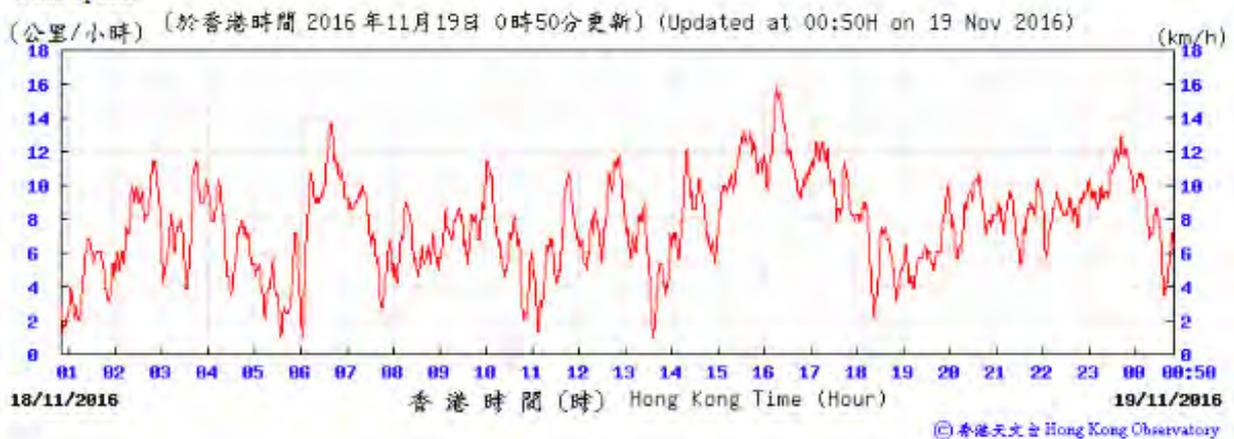


Temperature/Humidity:

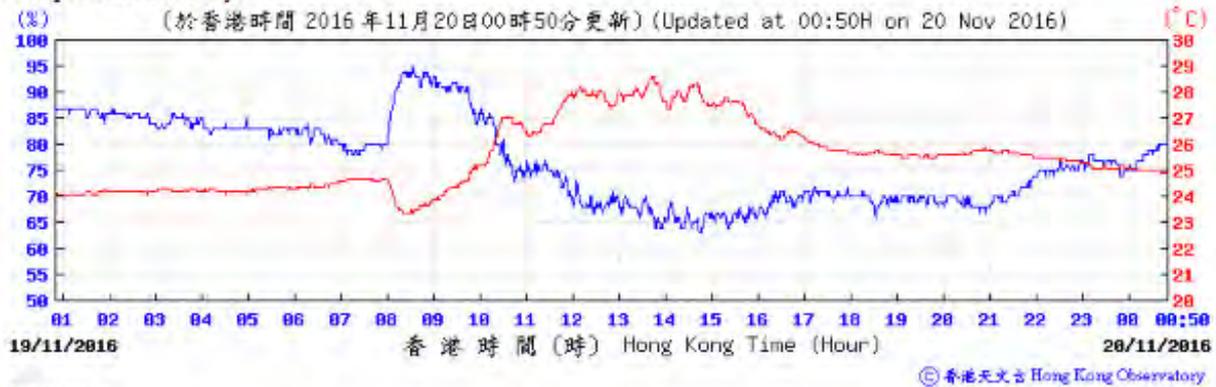


Pressure:




Wind Direction:

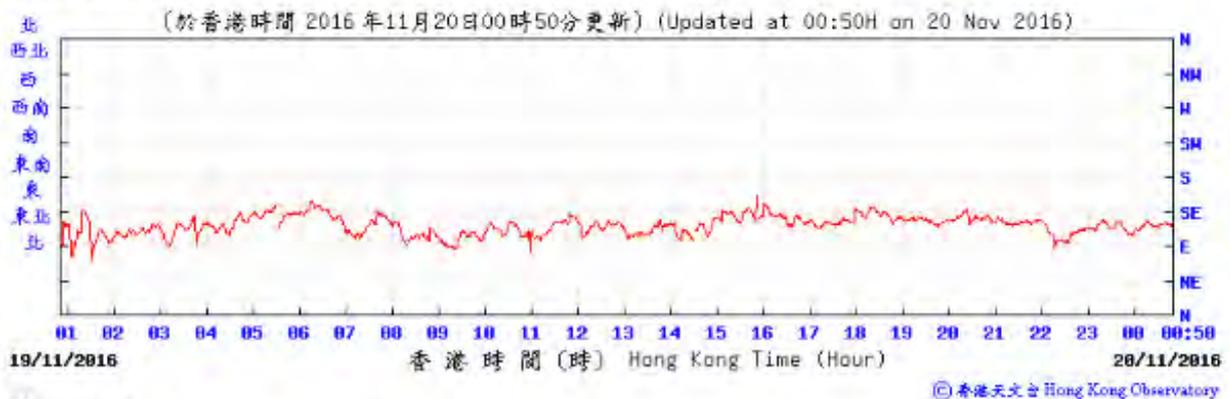

Wind Speed:

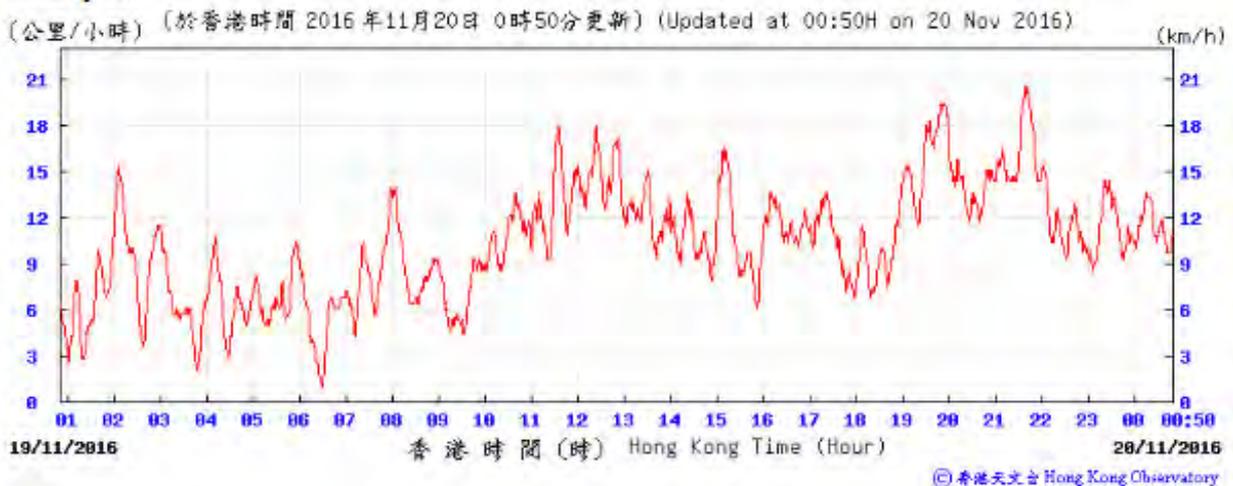


Temperature Humidity:

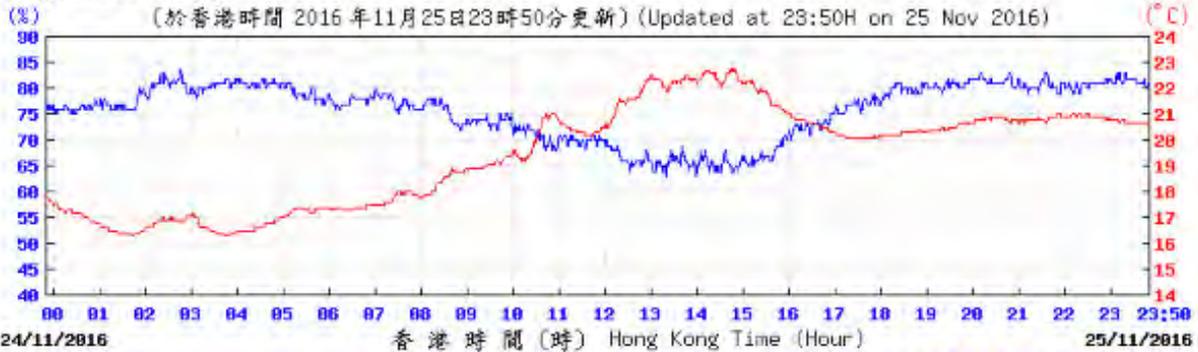


Pressure:




Wind Direction:

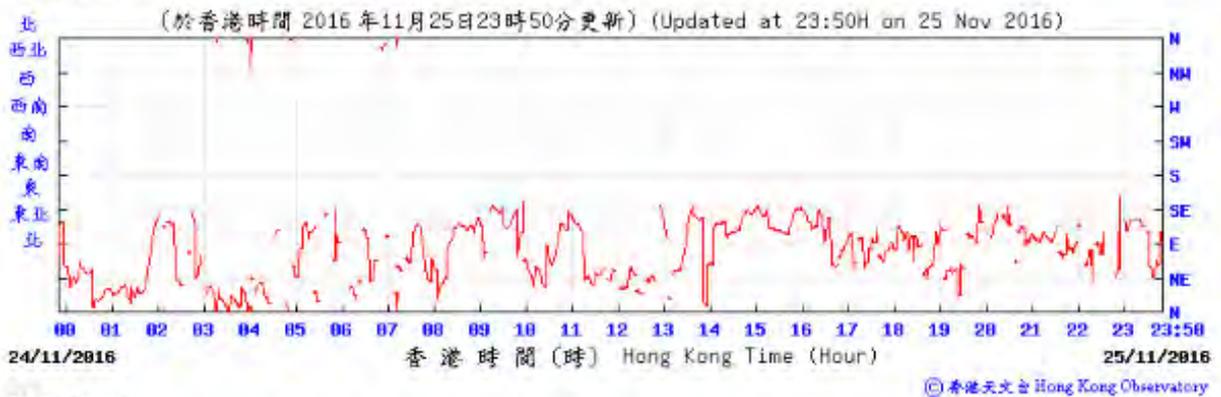


Wind Speed:

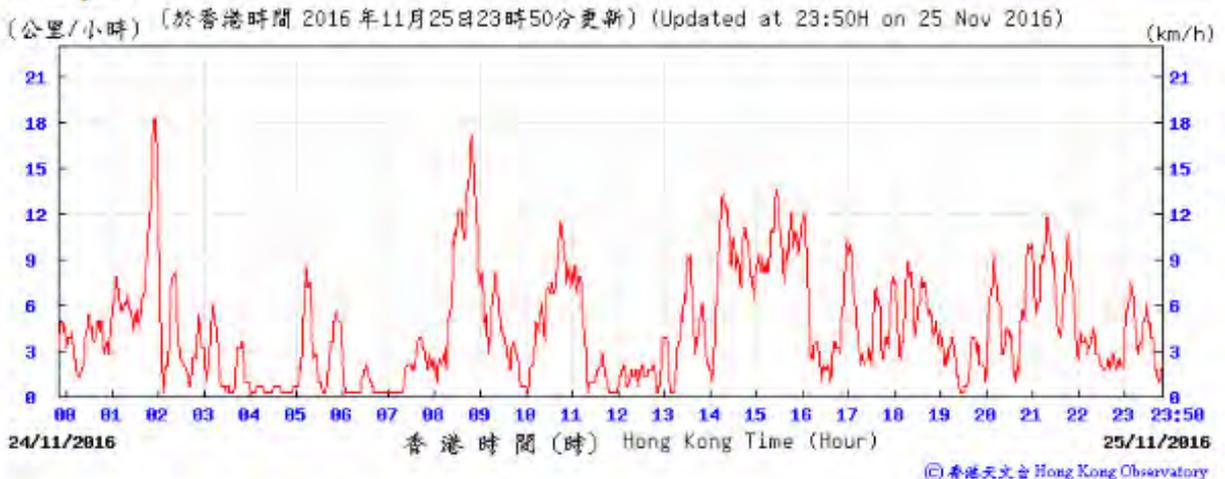


Temperature/Humidity:

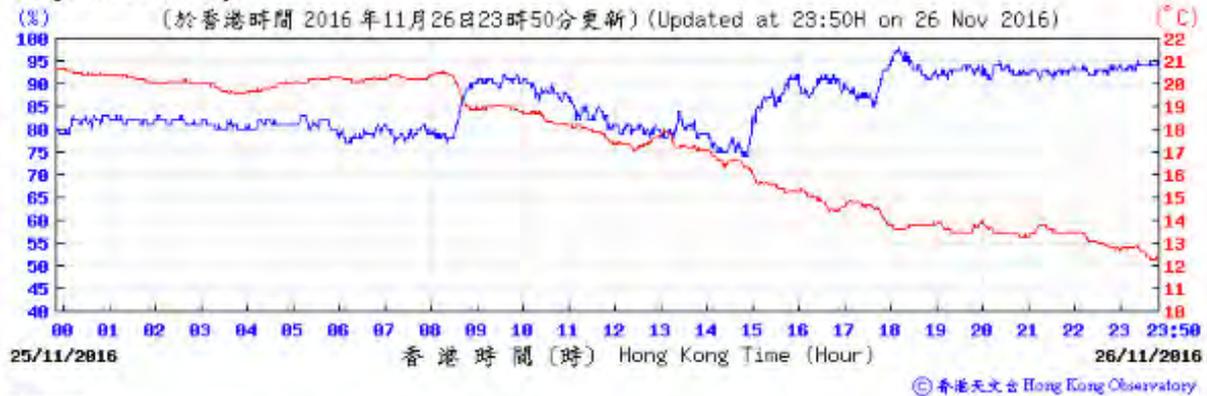


Pressure:

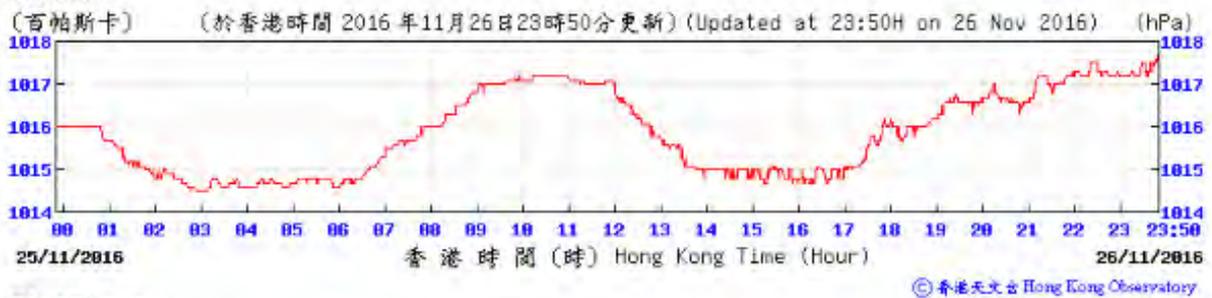


Wind Direction:

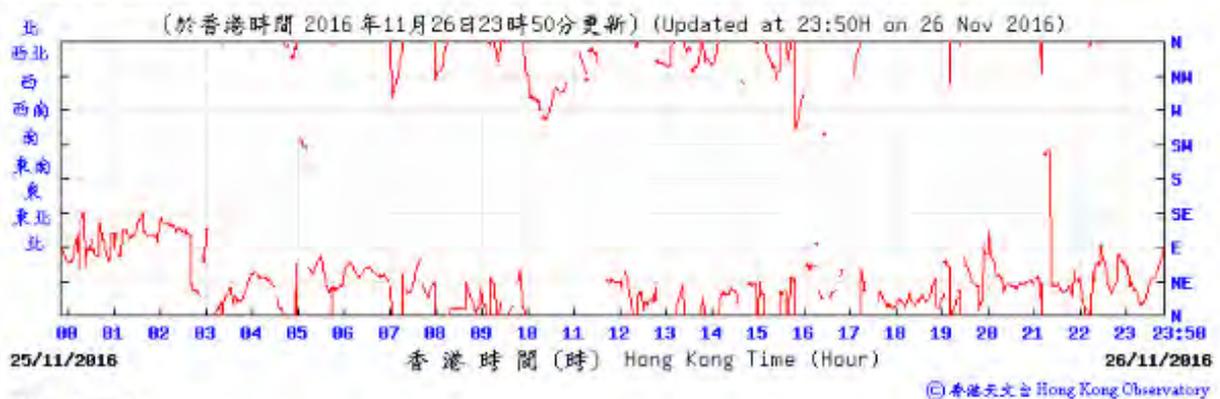

Wind Speed:

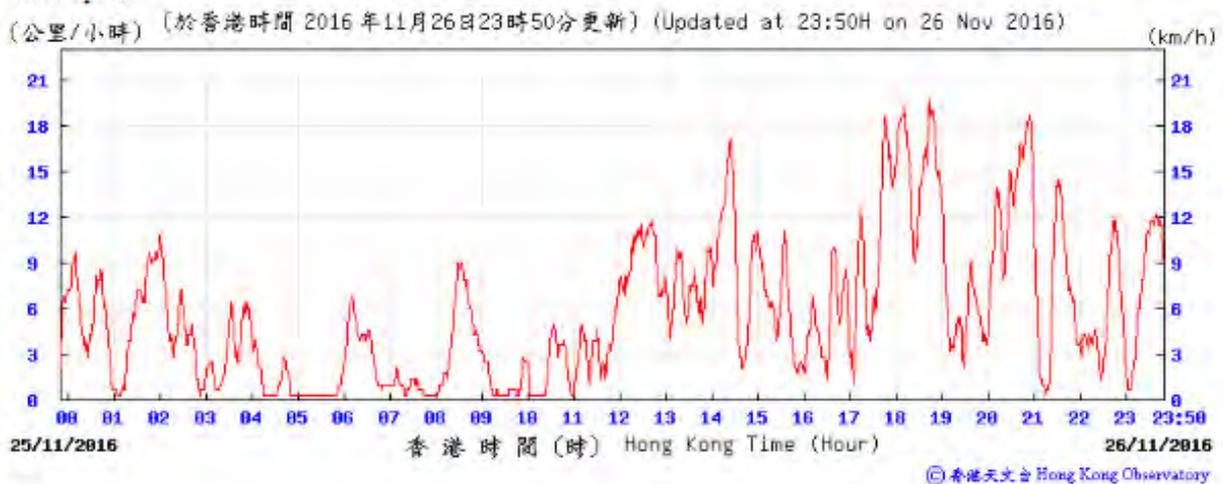


Temperature/Humidity:

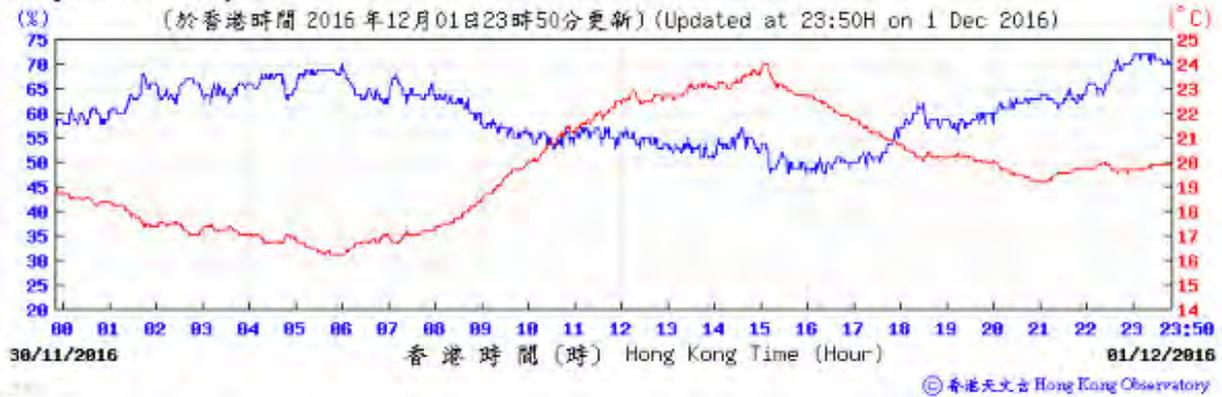


Pressure:




Wind Direction:

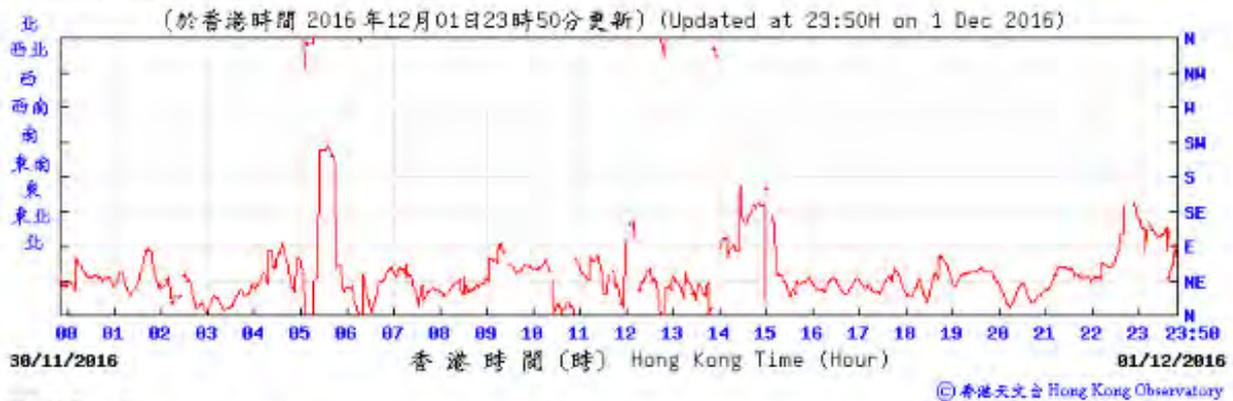

Wind Speed:

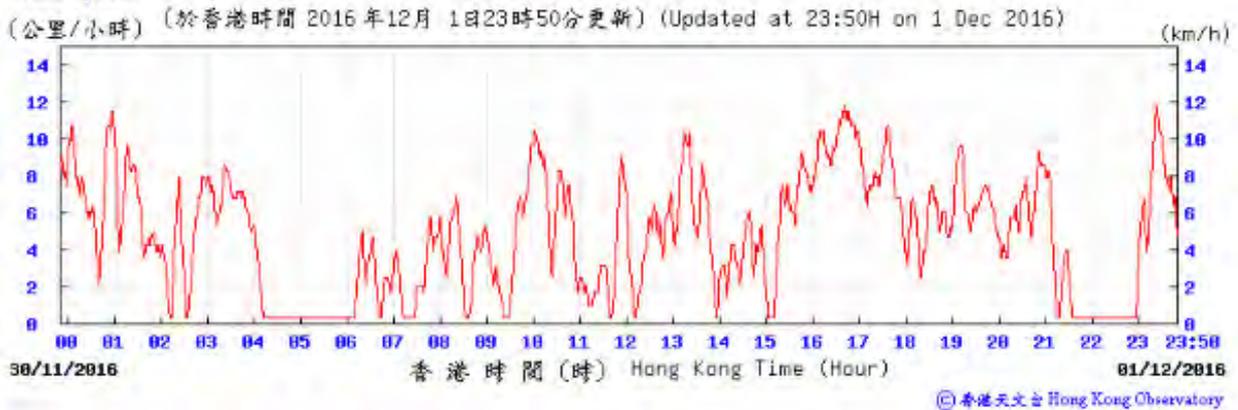


Temperature/Humidity:

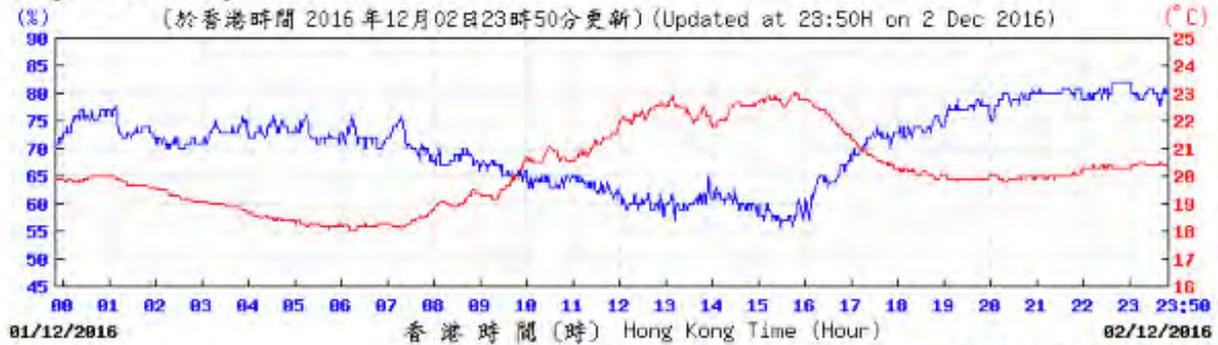


Pressure:



Wind Direction:

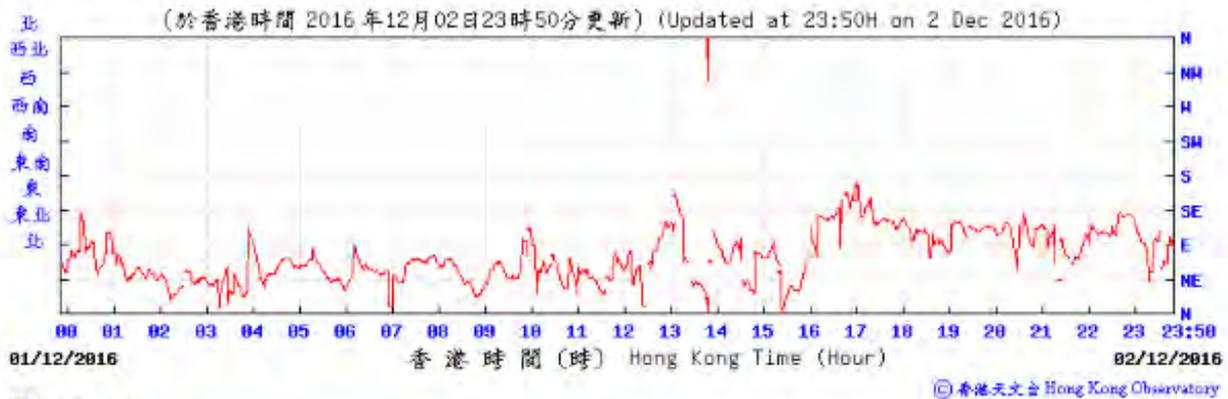

Wind Speed:

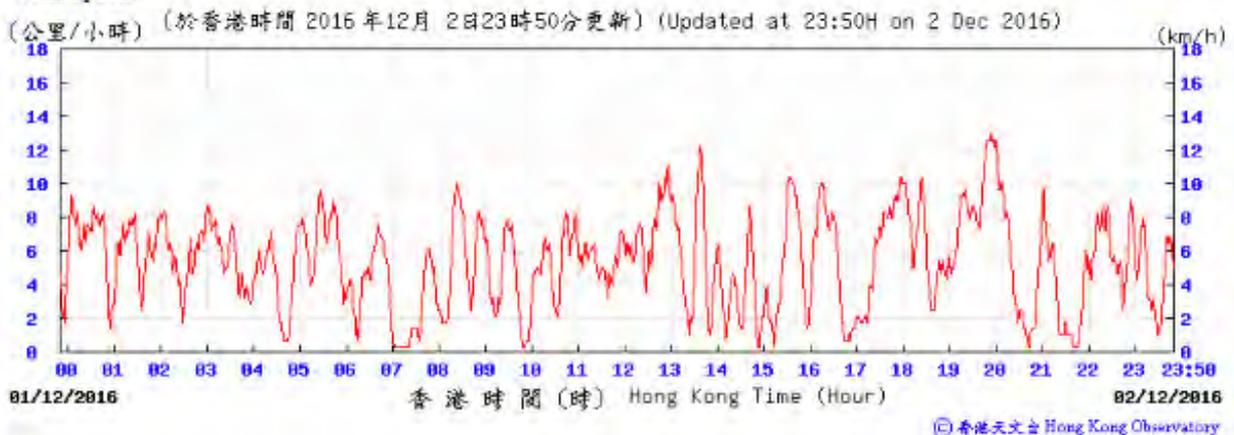

I. Waste Flow table

M+ Museum

Table I-1: Monthly Waste Flow Table for M+ Museum

Month	Actual Quantities of Inert C&D Materials Generated Monthly							Actual Quantities of C&D Wastes Generated Monthly					
	Total Quantity Generated	Hard Rocks and Large Broken Concrete	Reused in the Contract	Reused in other Projects	Disposed as Public Fill	Disposed to Sorting Facility	Imported Fill	Metals	Paper/ Cardboard Packaging	Plastics	Wood/ Timber	Chemical Waste	Others, e.g. General Refuse
	(in ton)	(in ton)	(in ton)	(in ton)	(in ton)	(in ton)	(in ton)	(in ton)	(in ton)	(in ton)	(in ton)	(in ton)	(in ton)
2015													
Nov	46607.4	0.0	0.0	8240.0	38367.4	0.0	0.0	76.2	0.0	0.0	0.0	0.0	67.6
Dec	29652.9	0.0	0.0	29621.4	31.5	0.0	0.0	26.3	0.0	0.0	0.0	1.0	66.0
Sub-total (2015)	76260.3	0.0	0.0	37861.4	38398.9	0.0	0.0	102.5	0.0	0.0	0.0	1.0	133.6
2016													
Jan	21077.4	0.0	6352.0	14576.0	149.4	0.0	0.0	18.8	0.0	0.0	0.0	0.0	23.2
Feb	7626.2	0.0	3424.0	4048.0	154.2	0.0	0.0	59.8	0.0	0.0	0.0	0.0	20.5
Mar	10442.5	0.0	1600.0	7888.0	954.5	0.0	0.0	29.7	0.0	0.0	0.0	0.0	46.3
Apr	30413.2	0.0	6352.0	23408.0	653.2	0.0	0.0	25.8	0.1	0.0	27.8	0.0	34.5
May	24083.5	0.0	112.0	23216.0	755.5	0.0	0.0	61.5	0.4	0.0	33.6	0.0	62.3
Jun	7880.1	0.0	4736.0	2384.0	760.1	0.0	0.0	106.6	0.1	0.0	14.6	0.0	52.8
Jul	5893.1	0.0	2656.0	2240.0	997.1	0.0	0.0	77.6	0.0	0.0	33.6	0.0	83.1
Aug	13709.6	0.0	0.0	12432.0	1277.6	0.0	0.0	111.3	0.3	0.0	38.5	0.0	104.9
Sep	6702.0	0.0	0.0	5648.0	1000.1	53.9	0.0	104.2	0.0	0.0	45.5	0.2	107.9
Oct	2103.6	0.0	0.0	496.0	1595.4	12.2	0.0	83.0	0.4	0.0	73.5	0.0	108.2
Nov	3302.7	0.0	0.0	2384.0	855.5	63.2	0.0	88.4	0.6	0.0	63.0	0.0	129.1
Dec													
Sub-total (2016)	133233.8	0.0	25232.0	98720.0	9152.5	129.3	0.0	766.6	1.9	0.0	330.1	0.2	772.9
Total	209494.1	0.0	25232.0	136581.4	47551.4	129.3	0.0	869.1	1.9	0.0	330.1	1.2	906.5

Note:
 -9.78 ton, 201.04 ton and 644.69 ton of inert C&D material were disposed of as public fill to Chai Wan Public Fill Barging Point, Tuen Mun Area 38 and Tseung Kwan O Area 137 Public Fill respectively in the reporting month.
 -For inert C&D materials reused in other projects, the projects refer to (1) Green Valley; (2) Advance Works for Shek Wu Hui Sewage Treatment Works (3) Design and Construction of Kai Tak Cable Tunnel, CLP; (4) MTR Contract 1002 Whampoa Station and Overrun Tunnel; (5) CEDD Tuen Mun Area 54 Contract No. CV/2015/03; (6) Union Construction Ltd.'s site; (7) Foundation Works at Marriot Hotel at Ocean Park.

Lyric Theatre Complex

Table I-2: Monthly Waste Flow Table for Lyric Theatre Complex

Month	Actual Quantities of Inert C&D Materials Generated Monthly							Actual Quantities of C&D Wastes Generated Monthly					
	Total Quantity Generated	Hard Rocks and Large Broken Concrete	Reused in the Contract	Reused in other Projects	Disposed as Public Fill	Disposed to Sorting Facility	Imported Fill	Metals	Paper/ Cardboard Packaging	Plastics	Wood/ Timber	Chemical Waste	Others, e.g. General Refuse
	(in ton)	(in ton)	(in ton)	(in ton)	(in ton)	(in ton)	(in ton)	(in ton)	(in ton)	(in ton)	(in ton)	(in ton)	(in ton)
2016													
Mar	2702.1	0.0	0.0	0.0	2702.1	0.0	0.0	4.5	0.1	0.0	0.0	0.0	30.6
Apr	8631.5	0.0	0.0	0.0	8631.5	0.0	0.0	16.0	0.0	0.0	0.0	0.0	19.2
May	12487.8	0.0	0.0	0.0	12487.8	0.0	0.0	34.0	0.0	0.0	0.0	0.7	60.5
Jun	8600.8	0.0	0.0	0.0	8600.8	0.0	0.0	31.4	0.2	0.0	0.0	0.5	13.5
Jul	12624.2	0.0	0.0	0.0	12624.2	0.0	0.0	19.6	0.0	0.0	0.0	2.0	9.9
Aug	14419.9	0.0	0.0	0.0	14419.9	0.0	0.0	43.9	0.0	0.0	0.0	0.0	11.1
Sep	13671.3	0.0	0.0	0.0	13671.3	0.0	0.0	59.8	0.0	0.0	0.0	1.6	12.4
Oct	13088.9	0.0	0.0	0.0	13088.9	0.0	0.0	37.1	0.2	1.5	0.0	0.0	15.2
Nov	12424.7	0.0	0.0	0.0	12424.7	0.0	0.0	74.7	0.0	0.0	0.0	1.4	10.2
Dec	0.0												
Sub-total (2016)	98651.2	0.0	0.0	0.0	98651.2	0.0	0.0	320.9	0.4	1.5	0.0	6.3	182.6
2017													
Jan	0.0												
Feb	0.0												
Mar	0.0												
Apr	0.0												
May	0.0												
Jun	0.0												
Sub-total (2017)	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
Total	98651.2	0.0	0.0	0.0	98651.2	0.0	0.0	320.9	0.4	1.5	0.0	6.3	182.6

Note:
 -4415.34 ton and 8009.37 ton of inert C&D material were disposed of as public fill to Tuen Mun Area 38 and Tseung Kwan O Area 137 respectively in the reporting month.

J. Environmental Mitigation Measures – Implementation Status

Table J-1: Environmental Mitigation Measures Implementation Status

EM&A Ref.	Recommendation Measures	Implementation Stage	
		M+ Museum	Lyric Theatre Complex
Air Quality Impact (Construction)			
2.1 & 10.3.1	<p>General Dust Control Measures</p> <p>Frequent water spraying for active construction areas (12 times a day or once every one hour), including Heavy construction activities such as construction of buildings or roads, drilling, ground excavation, cut and fill operations (i.e., earth moving)</p>	Obs/Rem	Obs
2.1 & 10.3.1	<p>Best Practice For Dust Control</p> <p>The relevant best practices for dust control as stipulated in the Air Pollution Control (construction Dust) Regulation should be adopted to further reduce the construction dust impacts from the Project. These best practices include:</p> <p><i>Good Site Management</i></p> <ul style="list-style-type: none"> • Good site management is important to help reducing potential air quality impact down to an acceptable level. As a general guide, the Contractor should maintain high standard of housekeeping to prevent emission of fugitive dust. Loading, unloading, handling and storage of raw materials, wastes or by-products should be carried out in a manner so as to minimise the release of visible dust emission. Any piles of materials accumulated on or around the work areas should be cleaned up regularly. Cleaning, repair and maintenance of all plant facilities within the work areas should be carried out in a manner minimising generation of fugitive dust emissions. The material should be handled properly to prevent fugitive dust emission before cleaning. <p><i>Disturbed Parts of the Roads</i></p> <ul style="list-style-type: none"> • Each and every main temporary access should be paved with concrete, bituminous hardcore materials or metal plates and kept clear of dusty materials; or • Unpaved parts of the road should be sprayed with water or a dust suppression chemical so as to keep the entire road surface wet. <p><i>Exposed Earth</i></p> <ul style="list-style-type: none"> • Exposed earth should be properly treated by compaction, hydroseeding, vegetation planting or seating with latex, vinyl, bitumen within six months after the last construction activity on the site or part of the site where the exposed earth lies. <p><i>Loading, Unloading or Transfer of Dusty Materials</i></p> <ul style="list-style-type: none"> • All dusty materials should be sprayed with water immediately prior to any loading or transfer operation 	Obs	✓
		✓	✓
		✓	✓
		N/A	N/A
		✓	✓

EM&A Ref.	Recommendation Measures	Implementation Stage	
		M+ Museum	Lyric Theatre Complex
	so as to keep the dusty material wet.		
	<i>Debris Handling</i>		
	<ul style="list-style-type: none"> Any debris should be covered entirely by impervious sheeting or stored in a debris collection area sheltered on the top and the three sides. 	✓	✓
	<ul style="list-style-type: none"> Before debris is dumped into a chute, water should be sprayed so that it remains wet when it is dumped. 	✓	✓
	<i>Transport of Dusty Materials</i>		
	<ul style="list-style-type: none"> Vehicle used for transporting dusty materials/spoils should be covered with tarpaulin or similar material. The cover should extend over the edges of the sides and tailboards. 	✓	✓
	<i>Wheel washing</i>		
	<ul style="list-style-type: none"> Vehicle wheel washing facilities should be provided at each construction site exit. Immediately before leaving the construction site, every vehicle should be washed to remove any dusty materials from its body and wheels. 	✓	✓
	<i>Use of vehicles</i>		
	<ul style="list-style-type: none"> The speed of the trucks within the site should be controlled to about 10km/hour in order to reduce adverse dust impacts and secure the safe movement around the site. 	✓	✓
	<ul style="list-style-type: none"> Immediately before leaving the construction site, every vehicle should be washed to remove any dusty materials from its body and wheels. 	✓	✓
	<ul style="list-style-type: none"> Where a vehicle leaving the construction site is carrying a load of dusty materials, the load should be covered entirely by clean impervious sheeting to ensure that the dusty materials do not leak from the vehicle. 	✓	✓
	<i>Site hoarding</i>		
	<ul style="list-style-type: none"> Where a site boundary adjoins a road, street, service lane or other area accessible to the public, hoarding of not less than 2.4m high from ground level should be provided along the entire length of that portion of the site boundary except for a site entrance or exit. 	✓	✓
2.1 & 10.3.1	<p>Best Practicable Means for Cement Works (Concrete Batching Plant)</p> <p>The relevant best practices for dust control as stipulated in the Guidance Note on the Best Practicable Means for Cement Works (Concrete Batching Plant) BPM 3/2(93) should be followed and implemented to further reduce the construction dust impacts of the Project. These best practices include:</p> <p>Exhaust from Dust Arrestment Plant</p>		

EM&A Ref.	Recommendation Measures	Implementation Stage	
		M+ Museum	Lyric Theatre Complex
	<ul style="list-style-type: none"> Wherever possible the final discharge point from particulate matter arrestment plant, where is not necessary to achieve dispersion from residual pollutants, should be at low level to minimise the effect on the local community in the case of abnormal emissions and to facilitate maintenance and inspection 	✓	✓
	Emission Limits		
	<ul style="list-style-type: none"> All emissions to air, other than steam or water vapour, shall be colourless and free from persistent mist or smoke 	✓	✓
	Engineering Design/Technical Requirements		
	<ul style="list-style-type: none"> As a general guidance, the loading, unloading, handling and storage of fuel, raw materials, products, wastes or by-products should be carried out in a manner so as to prevent the release of visible dust and/or other noxious or offensive emissions 	✓	✓
-	<p>Non-Road Mobile Machinery (NRMM):</p> <p>All NRMMs operating on-site which are subject to emission control of Air Pollution Control (Non-road Mobile Machinery) (Emission) Regulation are approved/exempted (as the case may be) and affixed with the requisite approval/exemption labels.</p>	✓	✓
Noise Impact (Construction)			
3.1 & 10.4.1	<p>Good Site Practice</p> <p>Good site practice and noise management can significantly reduce the impact of construction site activities on nearby NSRs. The following package of measures should be followed during each phase of construction:</p> <ul style="list-style-type: none"> only well-maintained plant to be operated on-site and plant should be serviced regularly during the construction works; machines and plant that may be in intermittent use to be shut down between work periods or should be throttled down to a minimum; plant known to emit noise strongly in one direction, should, where possible, be orientated to direct noise away from the NSRs; mobile plant should be sited as far away from NSRs as possible; and material stockpiles and other structures to be effectively utilised, where practicable, to screen noise from on-site construction activities. 	✓	Obs
		✓	✓
		✓	✓
		✓	✓
		✓	✓
3.1 & 10.4.1	<p>Adoption of Quieter PME</p> <p>The recommended quieter PME adopted in the assessment were taken from the EPD's QPME Inventory and "Sound Power Levels of Other Commonly Used PME" are presented in Table 4.26 in the EIA report. It should be noted that the silenced PME selected for assessment can be found in Hong Kong.</p>	N/A	N/A

EM&A Ref.	Recommendation Measures	Implementation Stage	
		M+ Museum	Lyric Theatre Complex
3.1 & 10.4.1	Use of Movable Noise Barriers Movable noise barriers can be very effective in screening noise from particular items of plant when constructing the Project. Noise barriers located along the active works area close to the noise generating component of a PME could produce at least 10 dB(A) screening for stationary plant and 5 dB(A) for mobile plant provided the direct line of sight between the PME and the NSRs is blocked.	✓	✓
3.1 & 10.4.1	Use of Noise Enclosure/ Acoustic Shed The use of noise enclosure or acoustic shed is to cover stationary PME such as air compressor and concrete pump. With the adoption of the noise enclosure, the PME could be completely screened, and noise reduction of 15 dB(A) can be achieved according to the EIAO Guidance Note No.9/2010.	N/A	N/A
3.1 & 10.4.1	Use of Noise Insulating Fabric Noise insulating fabric can also be adopted for certain PME (e.g. drill rig, pilling machine etc). The fabric should be lapped such that there are no openings or gaps on the joints. According to the approved Tsim Sha Tsui Station Northern Subway EIA report (AEIAR-127/2008), a noise reduction of 10 dB(A) can be achieved for the PME lapped with the noise insulating fabric.	✓	✓
3.1 & 10.4.1	Scheduling of Construction Works outside School Examination Periods During construction phase, the contractor should liaise with the educational institutions (including NSRs LCS and CRGPS) to obtain the examination schedule and avoid the noisy construction activities during school examination periods.	N/A	N/A
Water Quality Impact (Construction)			
4.1 & 10.5.1	Construction site runoff and drainage The site practices outlined in ProPECC Note PN 1/94 should be followed as far as practicable in order to minimise surface runoff and the chance of erosion. The following measures are recommended to protect water quality and sensitive uses of the coastal area, and when properly implemented should be sufficient to adequately control site discharges so as to avoid water quality impacts: <ul style="list-style-type: none"> At the start of site establishment, perimeter cut-off drains to direct off-site water around the site should be constructed with internal drainage works and erosion and sedimentation control facilities implemented. Channels, earth bunds or sand bag barriers should be provided on site to direct storm water to silt removal facilities. The design of the temporary on-site drainage system should be undertaken by the WKCDA's Contractor prior to the commencement of construction; Sand/silt removal facilities such as sand/silt traps and sediment basins should be provided to remove sand/silt particles from runoff to meet the requirements of the TM standards under the WPCO. The design of efficient silt removal facilities should be based on the guidelines in Appendix A1 of ProPECC Note PN 1/94. Sizes may vary depending upon the flow rate. The detailed design of the sand/silt traps should be undertaken by the WKCDA's Contractor prior to the commencement of construction. All drainage facilities and erosion and sediment control structures should be regularly inspected and 	✓	Rem
		✓	✓
		Obs	Obs

EM&A Ref.	Recommendation Measures	Implementation Stage	
		M+ Museum	Lyric Theatre Complex
	maintained to ensure proper and efficient operation at all times and particularly during rainstorms. Deposited silt and grit should be regularly removed, at the onset of and after each rainstorm to ensure that these facilities are functioning properly at all times.		
	<ul style="list-style-type: none"> Measures should be taken to minimize the ingress of site drainage into excavations. If excavation of trenches in wet periods is necessary, they should be dug and backfilled in short sections wherever practicable. Water pumped out from foundation excavations should be discharged into storm drains via silt removal facilities. 	✓	✓
	<ul style="list-style-type: none"> All vehicles and plant should be cleaned before leaving a construction site to ensure no earth, mud, debris and the like is deposited by them on roads. An adequately designed and sited wheel washing facility should be provided at construction site exit where practicable. Wash-water should have sand and silt settled out and removed regularly to ensure the continued efficiency of the process. The section of access road leading to, and exiting from, the wheel-wash bay to the public road should be paved with sufficient backfall toward the wheel-wash bay to prevent vehicle tracking of soil and silty water to public roads and drains. 	✓	✓
	<ul style="list-style-type: none"> Open stockpiles of construction materials or construction wastes on-site should be covered with tarpaulin or similar fabric during rainstorms. Measures should be taken to prevent the washing away of construction materials, soil, silt or debris into any drainage system. 	✓	✓
	<ul style="list-style-type: none"> Manholes (including newly constructed ones) should be adequately covered and temporarily sealed so as to prevent silt, construction materials or debris being washed into the drainage system and stormwater runoff being directed into foul sewers. 	✓	✓
	<ul style="list-style-type: none"> Precautions should be taken at any time of the year when rainstorms are likely. Actions should be taken when a rainstorm is imminent or forecasted and actions to be taken during or after rainstorms are summarized in Appendix A2 of ProPECC Note PN 1/94. Particular attention should be paid to the control of silty surface runoff during storm events, especially for areas located near steep slopes. 	✓	✓
	<ul style="list-style-type: none"> Bentonite slurries used in piling or slurry walling should be reconditioned and reused wherever practicable. Temporary enclosed storage locations should be provided on-site for any unused bentonite that needs to be transported away after all the related construction activities are completed. The requirements in ProPECC Note PN 1/94 should be adhered to in the handling and disposal of bentonite slurries. 	N/A	N/A
	Barging facilities and activities		
	Recommendations for good site practices during operation of the proposed barging point include:		
	<ul style="list-style-type: none"> All vessels should be sized so that adequate clearance is maintained between vessels and the seabed in all tide conditions, to ensure that undue turbidity is not generated by turbulence from vessel movement or propeller wash; 	N/A	N/A
	<ul style="list-style-type: none"> Loading of barges and hoppers should be controlled to prevent splashing of material into the surrounding water. Barges or hoppers should not be filled to a level that will cause the overflow of 	N/A	N/A

EM&A Ref.	Recommendation Measures	Implementation Stage	
		M+ Museum	Lyric Theatre Complex
	materials or polluted water during loading or transportation;		
	<ul style="list-style-type: none"> All hopper barges should be fitted with tight fitting seals to their bottom openings to prevent leakage of material; and Construction activities should not cause foam, oil, grease, scum, litter or other objectionable matter to be present on the water within the site. 	N/A	N/A
		N/A	N/A
4.1 & 10.5.1	Sewage effluent from construction workforce Temporary sanitary facilities, such as portable chemical toilets, should be employed on-site where necessary to handle sewage from the workforce. A licensed contractor should be employed to provide appropriate and adequate portable toilets and be responsible for appropriate disposal and maintenance.	✓	✓
4.1 & 10.5.1	General construction activities <ul style="list-style-type: none"> Construction solid waste, debris and refuse generated on-site should be collected, handled and disposed of properly to avoid entering any nearby storm water drain. Stockpiles of cement and other construction materials should be kept covered when not being used. Oils and fuels should only be stored in designated areas which have pollution prevention facilities. To prevent spillage of fuels and solvents to any nearby storm water drain, all fuel tanks and storage areas should be provided with locks and be sited on sealed areas, within bunds of a capacity equal to 110% of the storage capacity of the largest tank. The bund should be drained of rainwater after a rain event. 	Obs	✓
		Obs	Obs
Waste Management Implications (Construction)			
6.1 & 10.7.1	Good Site Practices Recommendations for good site practices during the construction activities include:		
	<ul style="list-style-type: none"> Nomination of an approved person, such as a site manager, to be responsible for good site practices, arrangements for collection and effective disposal to an appropriate facility, of all wastes generated at the site Training of site personnel in proper waste management and chemical handling procedures Provision of sufficient waste disposal points and regular collection of waste Appropriate measures to minimise windblown litter and dust/odour during transportation of waste by either covering trucks or by transporting wastes in enclosed containers Provision of wheel washing facilities before the trucks leaving the works area so as to minimise dust introduction to public roads Well planned delivery programme for offsite disposal such that adverse environmental impact from transporting the inert or non-inert C&D materials is not anticipated 	✓	✓
		✓	✓
		Obs	✓
		✓	✓
		✓	✓
		✓	✓

EM&A Ref.	Recommendation Measures	Implementation Stage	
		M+ Museum	Lyric Theatre Complex
6.1 & 10.7.1	<p>Waste Reduction Measures</p> <p>Recommendations to achieve waste reduction include:</p> <ul style="list-style-type: none"> Sort inert C&D material to recover any recyclable portions such as metals Segregation and storage of different types of waste in different containers or skips to enhance reuse or recycling of materials and their proper disposal Encourage collection of recyclable waste such as waste paper and aluminium cans by providing separate labelled bins to enable such waste to be segregated from other general refuse generated by the work force Proper site practices to minimise the potential for damage or contamination of inert C&D materials Plan the use of construction materials carefully to minimise amount of waste generated and avoid unnecessary generation of waste 	<p>✓</p> <p>✓</p> <p>✓</p> <p>✓</p> <p>✓</p>	<p>✓</p> <p>✓</p> <p>✓</p> <p>✓</p> <p>✓</p>
6.1 & 10.7.1	<p>Inert and Non-inert C&D Materials</p> <p>In order to minimise impacts resulting from collection and transportation of inert C&D material for off-site disposal, the excavated materials should be reused on-site as fill material as far as practicable. In addition, inert C&D material generated from excavation works could be reused as fill materials in local projects that require public fill for reclamation.</p> <ul style="list-style-type: none"> The surplus inert C&D material will be disposed of at the Government's PFRFs for beneficial use by other projects in Hong Kong. Liaison with the CEDD Public Fill Committee (PFC) on the allocation of space for disposal of the inert C&D materials at PFRF is underway. No construction work is allowed to proceed until all issues on management of inert C&D materials have been resolved and all relevant arrangements have been endorsed by the relevant authorities including PFC and EPD. The C&D materials generated from general site clearance should be sorted on site to segregate any inert materials for reuse or disposal of at PFRFs whereas the non-inert materials will be disposed of at the designated landfill site. In order to monitor the disposal of inert and non-inert C&D materials at respectively PFRFs and the designated landfill site, and to control fly-tipping, it is recommended that the Contractor should follow the Technical Circular (Works) No.6/2010 for Trip Ticket System for Disposal of Construction & Demolition Materials issued by Development Bureau. In addition, it is also recommended that the Contractor should prepare and implement a Waste Management Plan detailing their various waste arising and waste management practices in accordance with the relevant requirements of the Technical Circular (Works) No. 19/2005 Environmental Management on Construction Site. 	<p>✓</p> <p>✓</p> <p>✓</p> <p>✓</p> <p>✓</p>	<p>✓</p> <p>✓</p> <p>✓</p> <p>✓</p>

EM&A Ref.	Recommendation Measures	Implementation Stage	
		M+ Museum	Lyric Theatre Complex
6.1 & 10.7.1	<p>Chemical Waste</p> <ul style="list-style-type: none"> If chemical wastes are produced at the construction site, the Contractor will be required to register with the EPD as a chemical waste producer and to follow the guidelines stated in the “Code of Practice on the Packaging Labelling and Storage of Chemical Wastes”. Good quality containers compatible with the chemical wastes should be used, and incompatible chemicals should be stored separately. Appropriate labels should be securely attached on each chemical waste container indicating the corresponding chemical characteristics of the chemical waste, such as explosive, flammable, oxidizing, irritant, toxic, harmful, corrosive, etc. The Contractor should use a licensed collector to transport and dispose of the chemical wastes at the approved Chemical Waste Treatment Centre or other licensed recycling facilities, in accordance with the Waste Disposal (Chemical Waste) (General) Regulation. Potential environmental impacts arising from the handling activities (including storage, collection, transportation and disposal of chemical waste) are expected to be minimal with the implementation of appropriate mitigation measures as recommended. 	Obs/ Rem	Obs
6.1 & 10.7.1	<p>General Refuse</p> <p>General refuse should be stored in enclosed bins or compaction units separated from inert C&D materials. A reputable waste collector should be employed by the Contractor to remove general refuse from the site, separately from inert C&D materials. Preferably an enclosed and covered area should be provided to reduce the occurrence of 'wind blown' light material.</p>	✓	✓
Land Contamination (Construction)			
7.1 & 10.8.1	<p>The potential for land contamination issues at the TST Fire Station due to its future relocation will be confirmed by site investigation after land acquisition. Where necessary, mitigation measures for minimising potential exposure to contaminated materials (if any) or remediation measures will be identified. If contaminated land is identified (e.g., during decommissioning of fuel oil storage tanks) after the commencement of works, mitigation measures are proposed in order to minimise the potentially adverse effects on the health and safety of construction workers and impacts arising from the disposal of potentially contaminated materials.</p> <p>The following measures are proposed for excavation and transportation of contaminated material:</p> <ul style="list-style-type: none"> To minimize the chance for construction workers to come into contact with any contaminated materials, bulk earth-moving excavation equipment should be employed; Contact with contaminated materials can be minimised by wearing appropriate clothing and personal protective equipment such as gloves and masks (especially when interacting directly with contaminated material), provision of washing facilities and prohibition of smoking and eating on site; Stockpiling of contaminated excavated materials on site should be avoided as far as possible; 	N/A	N/A
		N/A	N/A
		N/A	N/A

EM&A Ref.	Recommendation Measures	Implementation Stage	
		M+ Museum	Lyric Theatre Complex
	<ul style="list-style-type: none"> The use of contaminated soil for landscaping purpose should be avoided unless pre-treatment was carried out; Vehicles containing any contaminated excavated materials should be suitably covered to reduce dust emissions and/or release of contaminated wastewater; Truck bodies and tailgates should be sealed to stop any discharge; Only licensed waste haulers should be used to collect and transport contaminated material to treatment/disposal site and should be equipped with tracking system to avoid fly tipping; Speed control for trucks carrying contaminated materials should be exercised; Observe all relevant regulations in relation to waste handling, such as Waste Disposal Ordinance (Cap 354), Waste Disposal (Chemical Waste) (General) Regulation (Cap 354) and obtain all necessary permits where required; and Maintain records of waste generation and disposal quantities and disposal arrangements. 	N/A	N/A
Ecological Impact (Construction)			
No mitigation measure is required.			
Landscape and Visual Impact (Construction)			
Table 9.1 & 10.8 (CM1)	Trees should be retained in situ on site as far as possible. Should tree removal be unavoidable due to construction impacts, trees will be transplanted or felled with reference to the stated criteria in the Tree Removal Applications to be submitted to relevant government departments for approval in accordance to ETWB TCW No. 29/2004 and 3/2006.	✓	N/A
Table 9.1 & 10.8 (CM2)	Compensatory tree planting shall be incorporated to the proposed project and maximize the new tree, shrubs and other vegetation planting to compensate tree felled and vegetation removed. Also, implementation of compensatory planting should be of a ratio not less than 1:1 in terms of quality and quantity within the site.	N/A	N/A
Table 9.1 & 10.8 (CM3)	Buffer trees for screening purposes to soften the hard architectural and engineering structures and facilities.	N/A	N/A
Table 9.1 & 10.8 (CM4)	Softscape treatments such as vertical green wall panel /planting of climbing and/or weeping plants, etc, to maximize the green coverage and soften the hard architectural and engineering structures and facilities.	N/A	N/A
Table 9.1 & 10.8 (CM5)	Roof greening by means of intensive and extensive green roof to maximize the green coverage and improve aesthetic appeal and visual quality of the building/structure.	N/A	N/A
Table 9.1 & 10.8 (CM6)	Sensitive streetscape design should be incorporated along all new roads and streets.	N/A	N/A

EM&A Ref.	Recommendation Measures	Implementation Stage	
		M+ Museum	Lyric Theatre Complex
Table 9.1 & 10.8 (CM7)	Structure, ornamental planting shall be provided along amenity strips to enhance the landscape quality.	N/A	N/A
Table 9.1 & 10.8 (CM8)	Landscape design shall be incorporated to architectural and engineering structures in order to provide aesthetically pleasing designs.	N/A	N/A
Table 9.1 (CM9)	Minimize the structure of marine facilities to built on the seabed and foreshore in order to minimize the affected extent to the waterbody	N/A	N/A
Table 9.2 & 10.9 (MCP1)	Use of decorative screen hoarding/boards	✓	✓
Table 9.2 & 10.9 (MCP2)	Early introduction of landscape treatments	N/A	N/A
Table 9.2 & 10.9 (MCP3)	Adoption of light colour for the temporary ventilation shafts for the basement during the transition period.	N/A	N/A
Table 9.2 & 10.9 (MCP4)	Control of night time lighting	✓	✓
Table 9.2 & 10.9 (MCP5)	Use of greenery such as grass cover for the temporary open areas will help achieve the visual balance and soften the hard edges of the structures.	N/A	N/A

N/A - Not Applicable

✓ - Implemented

Obs - Observed

Rem - Reminder

K. Cumulative Statistics on Complaints, Notifications of Summons and Successful Prosecutions

Cumulative statistics for complaints, notifications of summons and successful prosecutions for the Project account for period starting from the date of commencement of construction works (i.e. 31 October 2015 for M+ Museum main works and 1 March 2016 for Lyric Theatre Complex foundation works) to the end of the reporting month and are summarized in the **Table K-1** and **Table K-2** below respectively.

Table K-1: Statistics for complaints, notifications of summons and successful prosecutions for M+ Museum Main Works

Reporting Period	Cumulative Statistics		
	Complaints	Notifications of summons	Successful prosecutions
This reporting month	0	0	0
From 31 October 2015 to end of the reporting month	3	0	0

Table K-2: Statistics for complaints, notifications of summons and successful prosecutions for Lyric Theatre Complex Foundation Works

Reporting Period	Cumulative Statistics		
	Complaints	Notifications of summons	Successful prosecutions
This reporting month	2	0	0
From 1 March 2016 to end of the reporting month	4	0	0
