Project Name: Foundation and ELS Works for Integrated Basement and Underground Road in Zone 2A of the West Kowloon Cultural District

3-Month Rolling Programme

Activity ID	Activity Description	Duration (Cal. Day)	Start Date	Finish Date
	Preliminaries Works			
PRE. 10010	Water, Power and Discharge Point Installation	174	8-May-20	28-Oct-20
	Grouting Works (Trial 1 & Trial 2)			
	Pipe Pile Construction (Trial 1 and 2) (40/40 Nos Completed)	36	7-Oct-20	11-Nov-20
	Trial Grouting (Trial 1 and 2) - Stage 2 grouting (24/48 Nos Completed)	31	19-Dec-20	18-Jan-21
	ELS (Stage 1) - Grouting / Pipe Pile Works			
2A1. 10290	King Post (0/65 Nos Completed)	112	2-Jan-21	23-Apr-21
	Bored Pile Works			
	Bored Pile Works (Predrilling)			
2A1. 10020	Predrill (42/42 Nos Completed)	162	3-Oct-20	7-Dec-20
	Bored Pile Construction (Total 32 Nos. 2~4 Workfront)			
2A1. 10040 & 2A1. 10050	BP31L, BP33L, BP34I1, BP34G, BP31P (2 Nos. Cast; 1 Nos. completed RCD; 2 Nos. RCD in progress)	185	9-Nov-20	12-May-21
	ELS (Stage 1) - Grouting / Pipe Pile Works			
2A2. 10210	Stage 1a & 1b grouting (155/1054 Nos Completed)	161	22-Oct-20	31-Mar-21
2A2. 10180	Pipe Pile Construction (1/523 Nos Completed)	201	17-Nov-20	5-Jun-21

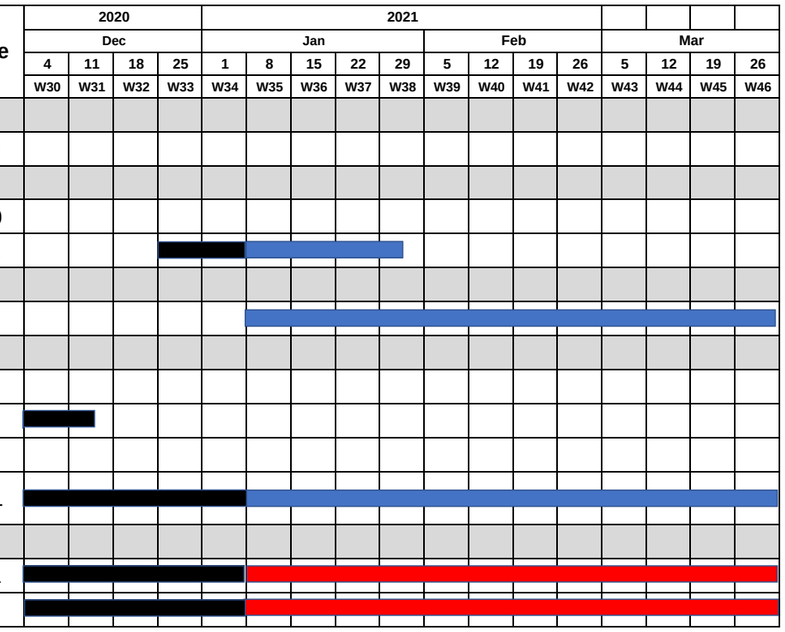

- Actual
- Remaining Works
- Critical Remaining Works
