TASK filter: Rev_2 Level 1 Summ with R_0 and R_1 KDs.

ID	Activity	RD	BL_Rev_00 Start	BL_Rev_00 Finish	BL_Rev_01 Start	BL_Rev_01 Finish	Start	Finish	LoE SUMM TF (approx, not for use)
*L2 CMWP_R02_00_01 2nd DRAFT IFA on 27Apr22 (18th UPD; DD = 31Mar2022) [*after compression]*									
GENERAL & PRELIMINARIES									
Contract Significant Dates									
Commencement & Completion Dates - CMWP_Rev_01									
Section Keydates									
KD05A	Complete Required Pedestrian Access Corridor and Floor Finishes at AURW	0		28-Feb-21		12-Nov-21		12-Nov-21 A	
KD05B	Complete Required Pedestrian Access Corridor & associated top slab at Avenue Level [if instructed]	0		14-Feb-21		12-Nov-21		12-Nov-21 A	
KD05C	PC for HO of Landscape Area at Avenue & Pedestrian level between P31 & P34 [if instructed]	0		28-Feb-21		05-Oct-22		25-Nov-22*	-51
KD05	PC for HO of the Remaining Works for M+ Promenade South	0		24-Aug-20		13-Jan-23		13-Jan-23*	0
KD08	PC for HO Loc ICT/Risers Rms to APC for ICT Sys Instn Wrks	0		10-Feb-23		10-Sep-24		08-Nov-24*	-59
KD10	PC for HO of ASDA, Lyric Theatre Promenade South to Authority	0		10-Feb-23		10-Sep-24		08-Nov-24*	-59
KD09	PC for HO of RDE areas for Tenancy Fit-out Wrks	0		10-Feb-23		10-Sep-24		08-Nov-24*	-59
KD11	PC for HO of Extended Basement for HO to Authority & HO of Carriageway to Relevant Govt Authority	0		10-Feb-23		12-Nov-24		10-Jan-25*	-59
KD07	PRACTICAL COMPLETION for C'Way 3A (M+ Day 2 Works)	0		10-Feb-23		09-Dec-24		11-Feb-25*	-32
KD13	PRACTICAL COMPLETION for Lyric Theatre, Extended Basement & C'Way 3B (Excl. PPE License)	0		08-Sep-23		10-Jan-25		12-Mar-25*	-61
Stage Keydates									
KD01	Compl Dsgn Coor/Subm and obtn NNO for L1 Contr Bsmt constn wrks	0		20-Jul-19		20-Jul-19		20-Jul-19 A	
KD06	PC for Fountain Related Plantroom(s) (allow access to Project Contractor)	0		01-Apr-21		07-Jun-22		13-Jun-22*	-6
KD03	OBTAIN OP for Lyric Theatre & Extended Basement	0		12-Dec-22		10-Sep-24		08-Nov-24*	-59
KD14	Complete U/G road and the associated plantrooms at Zone 3A&3B Integrated Basement	0		04-Aug-22		26-Sep-24		23-Nov-24*	-58
KD02	Obtain BA14 Acknowledge from BD for M+ Day2 A&A Works	0		12-Dec-22		08-Nov-24		07-Jan-25*	-60
CMWP - Summary Program - Level 1									
SUM10	[LoE] CC_B Lyric Theatre - Substructure RC Structural Concrete	0			06-May-20	22-Jan-22	06-May-20 A	22-Jan-22 A	
SUM30	[LoE] CC_H - Vibration Isolation Spring System Remaining as of 30Apr2020 (AS=30Sep19)	0			09-May-20	10-Feb-21	09-May-20 A	10-Feb-21 A	
SUM25	[LoE] CC_E - DCS Cofferdam A Works & Obtain BA14	320			23-Jun-20	23-May-23	23-Jun-20 A	10-Jun-23	23
SUM24	[LoE] CC_D - Remaining Works for M+ Promenade South	212			18-Feb-21	13-Jan-23	18-Feb-21 A	13-Jan-23	0
SUM21	[LoE] CC_C - LT EVA1 & EVA2	679			12-Apr-21	09-Sep-24	12-Apr-21 A	12-Oct-24	121
SUM27	[LoE] CC_G Extended Basement - ABWF Works (Incl. Deferred Areas Under Deck)	560			15-May-21	02-Feb-24	15-May-21 A	28-Feb-24	198
SUM28	[LoE] CC_G Extended Basement - MEP 1st Fix to Final Fix (Incl. Deferred Areas Under Deck)	542			17-May-21	12-Jan-24	17-May-21 A	31-Jan-24	25
SUM14	[LoE] CC_B Lyric Theatre - ABWF Work Including Theatres (Exd. Punch List Works)	793			28-May-21	14-Oct-24	28-May-21 A	09-Dec-24	25
SUM35	[LoE] CC_J - M+ Day 2 Works (excl. connections to M+ and SZ_1 FS Changeover)	677			03-Jun-21	25-Jun-24	03-Jun-21 A	23-Jul-24	-2
SUM23	[LoE] CC_C - Artist SQ. Bridge (ASB_1/2/3; ASB_3; P31_2; P34_2; AS_1/2; ASB-6/P31 EVA)	595			21-Jun-21	22-May-24	21-Jun-21 A	14-Jun-24	205
SUM15	[LoE] CC_B Lyric Theatre - MEP 1st to Final Fix (Excl. TH SYS done by SVE)	811			22-Jun-21	04-Nov-24	22-Jun-21 A	02-Jan-25	-11
SUM11	[LoE] CC_B Lyric Theatre - Superstructure RC Structural Concrete	385			02-Jul-21	22-Jul-23	02-Jul-21 A	08-Sep-23	11
SUM22	[LoE] CC_C - HoR Development (P32-1, P29-1, P31-EVA)	570			03-Aug-21	17-Apr-24	03-Aug-21 A	09-May-24	88
SUM31	[LoE] CC_I Carriageway 3B - ABWF Works	340			12-Aug-21	01-Apr-23	12-Aug-21 A	31-May-23	392
SUM42	[LoE] CC_E - DCS Outside of Cofferdam A Works (Connect DIA1,600 & Remove Temp O'fall)	438			08-Sep-21	29-Sep-23	08-Sep-21 A	18-Nov-23	-20
SUM32	[LoE] CC_I Carriageway 3B - MEP Works (1st Fix to Final Fix)	321			22-Mar-22	13-Feb-23	15-Sep-21 A	08-May-23	210
SUM40	[LoE] CC_N Lifts & Escalators	563			14-Dec-21	02-Feb-24	14-Dec-21 A	02-Mar-24	70
SUM41	[LoE] CC_B Lyric Theatre - Structural Steel by CSD	439			04-Mar-22	20-Oct-23	11-Mar-22 A	20-Nov-23	-7
SUM26	[LoE] CC_F - Mods to Existing Pump Cell Civil & MEP Works (Excl. Options 2 Add. Pumps)	158			01-Mar-22	26-Sep-22	01-Jun-22	28-Dec-22	142
SUM12	[LoE] CC_B Lyric Theatre - EWS Weather Tight Type	318			25-Jun-22	09-Sep-23	04-Aug-22	09-Oct-23	50
SUM20	[LoE] CC_C - LT Promenade & Pocket Square Bridge	574			04-Aug-22	31-Jul-24	12-Aug-22	23-Sep-24	-8
SUM17	[LoE] CC_B Lyric Theatre - TH Systems (by SVE) Incl. T&C, Precom. & Commissioning	708			30-Aug-22	25-Nov-24	30-Aug-22	23-Jan-25	-11
SUM29	[LoE] CC_G Extended Basement - T&C	308			03-Jan-23	02-Feb-24	11-Feb-23	28-Feb-24	25
SUM13	[LoE] CC_B Lyric Theatre - EWS Non-Weather Tight Type 4.1 & 4.3	291			23-Mar-23	25-Mar-24	29-Mar-23	25-Apr-24	71
SUM33	[LoE] CC_I Underpass 3B & Associated Area - T&C	184			13-Apr-23	25-Oct-23	06-May-23	13-Dec-23	82
SUM39	[LoE] CC_K - Water Main at Promenade	196			24-May-23	08-Jan-24	12-Jun-23	28-Feb-24	-20
SUM16	[LoE] CC_B Lyric Theatre - T&C (Excluding Non-FSD ELV & Electrical)	131			12-Dec-23	11-Jun-24	01-Feb-24	18-Jul-24	33
SUM18	[LoE] CC_B Lyric Theatre, EB, C'Way 3B - Stat. Insp. & Approval (from Form 314/501 to BD OP)	98			17-May-24	10-Sep-24	15-Jul-24	08-Nov-24	-48
SUM38	[LoE] CC_J - M+ Day 2 FS Changeover in 3A SZ_1, Connections to M+, Integrated T&C	51			29-Jul-24	26-Sep-24	24-Sep-24	23-Nov-24	-48
SUM34	[LoE] CC_J Carriageway 3A - Stat. Insp. & Approvals (from Form 314A to BA14)	56			02-Sep-24	08-Nov-24	31-Oct-24	07-Jan-25	-48

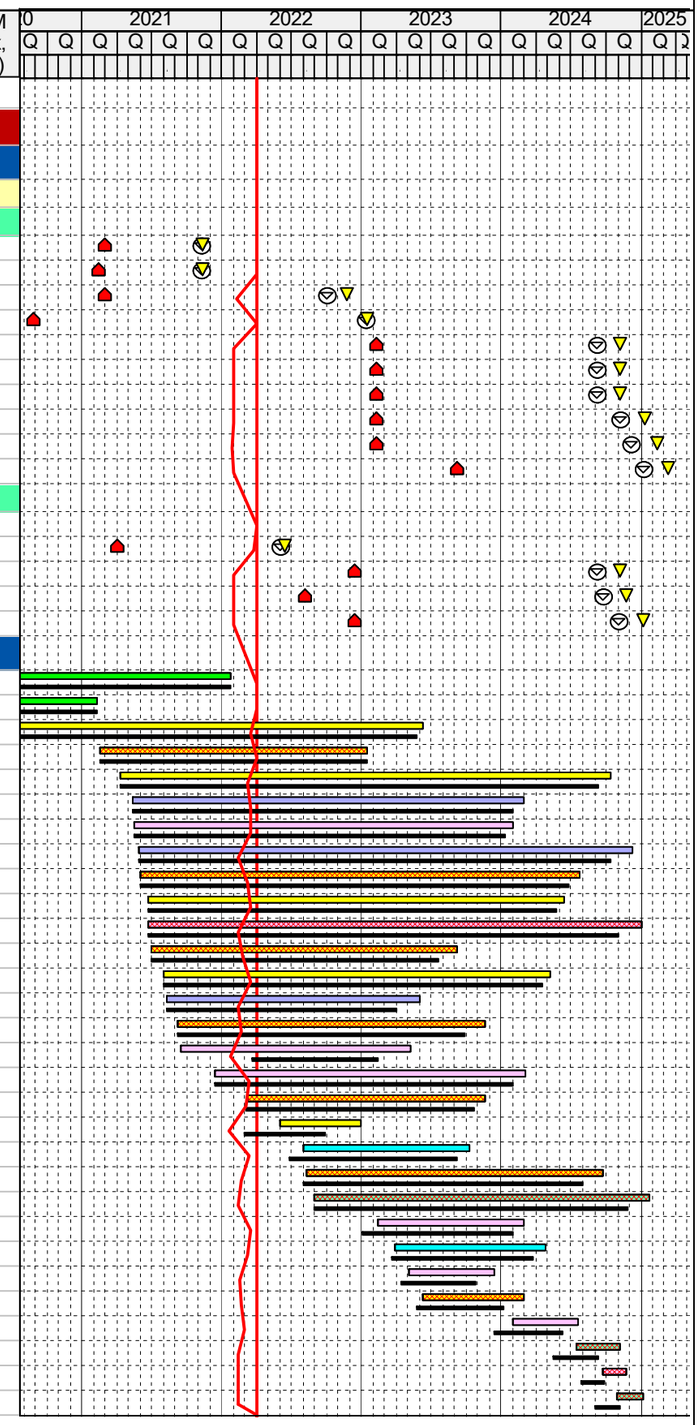

Gammon

Base Line ACT
Rev_0 KD
Base Line MS
Milestone
Current - Other Works
Current - Struct Works
Current - MEP Works
Current - ABWF Works
Current - Facade Works
Critical Works

L2 CMWP_R02_00_01 2nd DRAFT IFA on 27Apr22 (18th UPD; DD = 31Mar2022) [*after compression]

Date	Revision	Checked	Approved
10-May-22	CMWP Rev_2_01 - 2nd DRAFT 18th Update DD ...	NS	IH
