TASK filter: L2 UPD: Level 1 Prg [before compression].

ID	Activity	RD	BL_Rev_00 Start	BL_Rev_00 Finish	BL_Rev_02 Start	BL_Rev_02 Finish	Start	Finish	LoE SUMM TF (approx)	BL_R2 VAR	LM VAR
*L2 CMWP_R02_07 - IFA on 27Apr22 - ***LIVE*** (24th UPD; DD = 30Sep2022)*											
GENERAL & PRELIMINARIES											
Contract Significant Dates											
Commencement & Completion Dates - CMWP_Rev_01											
Section Keydates											
KD05A	Complete Required Pedestrian Access Corridor and Floor Finishes at AURW	0		28-Feb-21		12-Nov-21		12-Nov-21 A		0	0
KD05B	Complete Required Pedestrian Access Corridor & associated top slab at Avenue Level [if instructed]	0		14-Feb-21		12-Nov-21		12-Nov-21 A		0	0
KD05	PC for HO of the Remaining Works for M+ Promenade South	0		24-Aug-20		13-Jan-23		12-May-23*	-119	-119	-9
KD08	PC for HO Loc ICT/Risers Rms to APC for ICT Sys Instn Wrks	0		10-Feb-23		10-Sep-24		24-Jan-25*	-136	-136	-8
KD10	PC for HO of ASDA, Lyric Theatre Promenade South to Authority	0		10-Feb-23		10-Sep-24		24-Jan-25*	-136	-136	-8
KD09	PC for HO of RDE areas for Tenancy Fit-out Wrks	0		10-Feb-23		10-Sep-24		24-Jan-25*	-136	-136	-8
KD11	PC for HO of Extended Basement for HO to Authority & HO of Carriageway to Relevant Govt Authority	0		10-Feb-23		12-Nov-24		29-Mar-25*	-137	-137	-8
KD07	PRACTICAL COMPLETION for C'Way 3A (M+ Day 2 Works)	0		10-Feb-23		09-Dec-24		30-Apr-25*	-110	-142	-8
KD13	PRACTICAL COMPLETION for Lyric Theatre, EB & C'Way 3B (Incl. Provisional PPE License)	0		08-Sep-23		10-Jan-25		02-Jun-25*	-143	-143	-10
Stage Keydates											
KD01	Compl Dsgn Coor/Subm and obtn NNO for L1 Contr Bsmt constn wrks	0		20-Jul-19		20-Jul-19		20-Jul-19 A		0	0
KD06	PC for Fountain Related Plantroom(s) (allow access to Project Contractor)	0		01-Apr-21		07-Jun-22		31-Oct-22*	-146	-146	-33
KD03	OBTAIN OP for Lyric Theatre & Extended Basement	0		12-Dec-22		10-Sep-24		24-Jan-25*	-136	-136	-8
KD14	Complete U/G road and the associated plantrooms at Zone 3A&3B Integrated Basement	0		04-Aug-22		26-Sep-24		13-Feb-25*	-140	-140	-8
KD02	Obtain BA14 Acknowledge from BD for M+ Day2 A&A Works	0		12-Dec-22		08-Nov-24		26-Mar-25*	-138	-138	-8
CMWP - Summary Program - Level 1											
SUM10	[LoE] CC_B Lyric Theatre - Substructure RC Structural Concrete	0			06-May-20	22-Jan-22	06-May-20 A	22-Jan-22 A		0	0
SUM30	[LoE] CC_H - Vibration Isolation Spring System Remaining as of 30Apr2020 (AS=30Sep19)	0			09-May-20	10-Feb-21	09-May-20 A	10-Feb-21 A		0	0
SUM25	[LoE] CC_E - DCS Cofferdam A Works & Obtain BA14	289			23-Jun-20	23-May-23	23-Jun-20 A	26-Oct-23	-75	-111	-22
SUM24	[LoE] CC_D - Remaining Works for M+ Promenade South	170			18-Feb-21	13-Jan-23	18-Feb-21 A	12-May-23	-87	-87	-6
SUM21	[LoE] CC_C - LT EVA1 & EVA2	605			12-Apr-21	09-Sep-24	12-Apr-21 A	17-Dec-24	129	-77	-7
SUM27	[LoE] CC_G Extended Basement - ABWF Works (Incl. Deferred Areas Under Deck)	453			15-May-21	02-Feb-24	15-May-21 A	22-Apr-24	156	-58	0
SUM28	[LoE] CC_G Extended Basement - MEP 1st Fix to Final Fix (Incl. Deferred Areas Under Deck)	435			17-May-21	12-Jan-24	17-May-21 A	27-Mar-24	-17	-58	0
SUM14	[LoE] CC_B Lyric Theatre - ABWF Work Including Theatres (Exd. Punch List Works)	707			28-May-21	14-Oct-24	28-May-21 A	28-Feb-25	-38	-111	-7
SUM35	[LoE] CC_J - M+ Day 2 Works (excl. connections to M+ and SZ_1 FS Changeover)	592			03-Jun-21	25-Jun-24	03-Jun-21 A	08-Oct-24	-66	-87	-9
SUM23	[LoE] CC_C - Artist SQ. Bridge (ASB_1/2/3; ASB_3; P31_2; P34_2; AS_1/2; ASB-6/P31 EVA)	483			21-Jun-21	22-May-24	21-Jun-21 A	09-Jul-24	46	-33	0
SUM15	[LoE] CC_B Lyric Theatre - MEP 1st to Final Fix (Excl. TH SYS done by SVE)	725			22-Jun-21	04-Nov-24	22-Jun-21 A	21-Mar-25	-74	-111	-7
SUM11	[LoE] CC_B Lyric Theatre - Superstructure RC Structural Concrete	308			02-Jul-21	22-Jul-23	02-Jul-21 A	17-Nov-23	-41	-87	-7
SUM22	[LoE] CC_C - HoR Development (P32-1, P29-1, P31-EVA)	483			03-Aug-21	17-Apr-24	03-Aug-21 A	09-Jul-24	46	-58	0
SUM31	[LoE] CC_I Carriageway 3B - ABWF Works	240			12-Aug-21	01-Apr-23	12-Aug-21 A	29-Jul-23	343	-94	0
SUM42	[LoE] CC_E - DCS Outside of Cofferdam A Works (Connect DIA1,600 & Remove Temp O'fall)	331			08-Sep-21	29-Sep-23	08-Sep-21 A	14-Dec-23	-42	-60	-5
SUM32	[LoE] CC_I Carriageway 3B - MEP Works (1st Fix to Final Fix)	209			22-Mar-22	13-Feb-23	15-Sep-21 A	21-Jun-23	173	-104	-5
SUM40	[LoE] CC_N Lifts & Escalators	457			14-Dec-21	02-Feb-24	14-Dec-21 A	26-Apr-24	27	-62	0
SUM41	[LoE] CC_B Lyric Theatre - Structural Steel by CSD	371			04-Mar-22	20-Oct-23	11-Mar-22 A	02-Feb-24	-68	-86	-8
SUM17	[LoE] CC_B Lyric Theatre - TH Systems (by SVE) Incl. T&C, Precom. & Commissioning	732			30-Aug-22	25-Nov-24	17-Oct-22	16-Apr-25	-74	-111	-7
SUM26	[LoE] CC_F - Mods to Existing Pump Cell Civil & MEP Works (Excl. Options 2 Add. Pumps)	150			01-Mar-22	26-Sep-22	17-Oct-22	25-Apr-23	53	-162	-14
SUM12	[LoE] CC_B Lyric Theatre - EWS Weather Tight Type	269			25-Jun-22	09-Sep-23	05-Dec-22	01-Dec-23	6	-63	0
SUM20	[LoE] CC_C - LT Promenade & Pocket Square Bridge	520			04-Aug-22	31-Jul-24	31-Dec-22	02-Dec-24	-63	-93	-22
SUM13	[LoE] CC_B Lyric Theatre - EWS Non-Weather Tight Type 4.1 & 4.3	293			23-Mar-23	25-Mar-24	14-Jun-23	13-Jul-24	16	-77	-7
SUM29	[LoE] CC_G Extended Basement - T&C	243			03-Jan-23	02-Feb-24	24-Jun-23	22-Apr-24	-17	-58	0
SUM33	[LoE] CC_I Underpass 3B & Associated Area - T&C	171			13-Apr-23	25-Oct-23	02-Aug-23	01-Mar-24	23	-101	-7
SUM39	[LoE] CC_K - Water Main at Promenade	143			24-May-23	08-Jan-24	27-Oct-23	27-Apr-24	-65	-83	-22
SUM16	[LoE] CC_B Lyric Theatre - T&C (Excluding Non-FSD ELV & Electrical)	136			12-Dec-23	11-Jun-24	16-Apr-24	26-Sep-24	-29	-90	-7
SUM18	[LoE] CC_B Lyric Theatre, EB, C'Way 3B - Stat. Insp. & Approval (from Form 314/501 to BD OP)	98			17-May-24	10-Sep-24	27-Sep-24	24-Jan-25	-111	-111	-7
SUM38	[LoE] CC_J - M+ Day 2 FS Changeover in 3A SZ_1, Connections to M+, Integrated T&C	51			29-Jul-24	26-Sep-24	09-Dec-24	13-Feb-25	-111	-111	-7
SUM34	[LoE] CC_J Carriageway 3A - Stat. Insp. & Approvals (from Form 314A to BA14)	56			02-Sep-24	08-Nov-24	16-Jan-25	26-Mar-25	-111	-111	-7

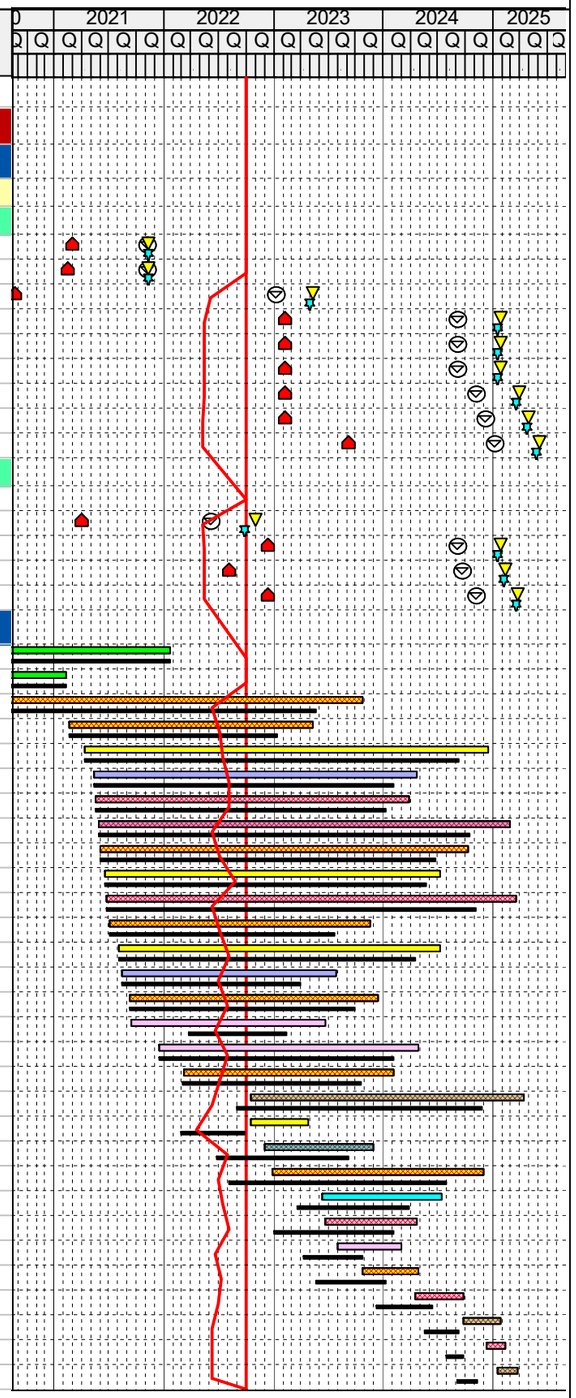

Gammon

Base Line ACT
Rev_0 KD
Base Line MS
Milestone
Current - Other Works
Current - Struct Works
Current - MEP Works
Current - ABWF Works
Current - Facade Works
Critical Works

L2 CMWP_R02_07 - IFA on 27Apr22 - ***LIVE*
(24th UPD; DD = 30Sep2022)**

Date	Revision	Checked	Approved
11-Oct-22	CMWP Rev_2_07 - 24th Update DD 30Sep22	NS	IH

TASK filter: L2 UPD: Level 1 Prg [after compression].

ID	Activity	RD	BL_Rev_00 Start	BL_Rev_00 Finish	BL_Rev_02 Start	BL_Rev_02 Finish	Start	Finish	LoE SUMM TF (approx)	BL_R2 VAR	LM VAR
*L2 CMWP_R02_07 - IFA on 27Apr22 - ***LIVE*** (24th UPD; DD = 30Sep2022)*											
GENERAL & PRELIMINARIES											
Contract Significant Dates											
Commencement & Completion Dates - CMWP_Rev_01											
Section Keydates											
KD05A	Complete Required Pedestrian Access Corridor and Floor Finishes at AURW	0		28-Feb-21		12-Nov-21		12-Nov-21 A		0	0
KD05B	Complete Required Pedestrian Access Corridor & associated top slab at Avenue Level [if instructed]	0		14-Feb-21		12-Nov-21		12-Nov-21 A		0	0
KD05	PC for HO of the Remaining Works for M+ Promenade South	0		24-Aug-20		13-Jan-23		12-May-23*	-119	-119	-9
KD08	PC for HO Loc ICT/Risers Rms to APC for ICT Sys Instn Wrks	0		10-Feb-23		10-Sep-24		16-Jan-25*	-128	-128	0
KD10	PC for HO of ASDA, Lyric Theatre Promenade South to Authority	0		10-Feb-23		10-Sep-24		16-Jan-25*	-128	-128	0
KD09	PC for HO of RDE areas for Tenancy Fit-out Wrks	0		10-Feb-23		10-Sep-24		16-Jan-25*	-128	-128	0
KD11	PC for HO of Extended Basement for HO to Authority & HO of Carriageway to Relevant Govt Authority	0		10-Feb-23		12-Nov-24		21-Mar-25*	-129	-129	0
KD07	PRACTICAL COMPLETION for C'Way 3A (M+ Day 2 Works)	0		10-Feb-23		09-Dec-24		22-Apr-25*	-102	-134	0
KD13	PRACTICAL COMPLETION for Lyric Theatre, EB & C'Way 3B (Incl. Provisional PPE License)	0		08-Sep-23		10-Jan-25		23-May-25*	-133	-133	0
Stage Keydates											
KD01	Compl Dsgn Coor/Subm and obtn NNO for L1 Contr Bsmt constn wrks	0		20-Jul-19		20-Jul-19		20-Jul-19 A		0	0
KD06	PC for Fountain Related Plantroom(s) (allow access to Project Contractor)	0		01-Apr-21		07-Jun-22		31-Oct-22*	-146	-146	-33
KD03	OBTAIN OP for Lyric Theatre & Extended Basement	0		12-Dec-22		10-Sep-24		16-Jan-25*	-128	-128	0
KD14	Complete U/G road and the associated plantrooms at Zone 3A&3B Integrated Basement	0		04-Aug-22		26-Sep-24		05-Feb-25*	-132	-132	0
KD02	Obtain BA14 Acknowledge from BD for M+ Day2 A&A Works	0		12-Dec-22		08-Nov-24		18-Mar-25*	-130	-130	0
CMWP - Summary Program - Level 1											
SUM10	[LoE] CC_B Lyric Theatre - Substructure RC Structural Concrete	0			06-May-20	22-Jan-22	06-May-20 A	22-Jan-22 A		0	0
SUM30	[LoE] CC_H - Vibration Isolation Spring System Remaining as of 30Apr2020 (AS=30Sep19)	0			09-May-20	10-Feb-21	09-May-20 A	10-Feb-21 A		0	0
SUM25	[LoE] CC_E - DCS Cofferdam A Works & Obtain BA14	289			23-Jun-20	23-May-23	23-Jun-20 A	26-Oct-23	-75	-111	-22
SUM24	[LoE] CC_D - Remaining Works for M+ Promenade South	170			18-Feb-21	13-Jan-23	18-Feb-21 A	12-May-23	-87	-87	-6
SUM21	[LoE] CC_C - LT EVA1 & EVA2	598			12-Apr-21	09-Sep-24	12-Apr-21 A	09-Dec-24	129	-70	0
SUM27	[LoE] CC_G Extended Basement - ABWF Works (Incl. Deferred Areas Under Deck)	453			15-May-21	02-Feb-24	15-May-21 A	22-Apr-24	156	-58	0
SUM28	[LoE] CC_G Extended Basement - MEP 1st Fix to Final Fix (Incl. Deferred Areas Under Deck)	435			17-May-21	12-Jan-24	17-May-21 A	27-Mar-24	-17	-58	0
SUM14	[LoE] CC_B Lyric Theatre - ABWF Work Including Theatres (Exd. Punch List Works)	700			28-May-21	14-Oct-24	28-May-21 A	20-Feb-25	-31	-104	0
SUM35	[LoE] CC_J - M+ Day 2 Works (excl. connections to M+ and SZ_1 FS Changeover)	583			03-Jun-21	25-Jun-24	03-Jun-21 A	26-Sep-24	-57	-78	0
SUM23	[LoE] CC_C - Artist SQ. Bridge (ASB_1/2/3; ASB_3; P31_2; P34_2; AS_1/2; ASB-6/P31 EVA)	483			21-Jun-21	22-May-24	21-Jun-21 A	09-Jul-24	46	-33	0
SUM15	[LoE] CC_B Lyric Theatre - MEP 1st to Final Fix (Excl. TH SYS done by SVE)	718			22-Jun-21	04-Nov-24	22-Jun-21 A	13-Mar-25	-67	-104	0
SUM11	[LoE] CC_B Lyric Theatre - Superstructure RC Structural Concrete	301			02-Jul-21	22-Jul-23	02-Jul-21 A	09-Nov-23	-34	-80	0
SUM22	[LoE] CC_C - HoR Development (P32-1, P29-1, P31-EVA)	483			03-Aug-21	17-Apr-24	03-Aug-21 A	09-Jul-24	46	-58	0
SUM31	[LoE] CC_I Carriageway 3B - ABWF Works	240			12-Aug-21	01-Apr-23	12-Aug-21 A	29-Jul-23	343	-94	0
SUM42	[LoE] CC_E - DCS Outside of Cofferdam A Works (Connect DIA1,600 & Remove Temp O'fall)	331			08-Sep-21	29-Sep-23	08-Sep-21 A	14-Dec-23	-42	-60	-5
SUM32	[LoE] CC_I Carriageway 3B - MEP Works (1st Fix to Final Fix)	209			22-Mar-22	13-Feb-23	15-Sep-21 A	21-Jun-23	173	-104	-5
SUM40	[LoE] CC_N Lifts & Escalators	457			14-Dec-21	02-Feb-24	14-Dec-21 A	26-Apr-24	27	-62	0
SUM41	[LoE] CC_B Lyric Theatre - Structural Steel by CSD	363			04-Mar-22	20-Oct-23	11-Mar-22 A	24-Jan-24	-60	-78	0
SUM17	[LoE] CC_B Lyric Theatre - TH Systems (by SVE) Incl. T&C, Precom. & Commissioning	725			30-Aug-22	25-Nov-24	17-Oct-22	03-Apr-25	-67	-104	0
SUM26	[LoE] CC_F - Mods to Existing Pump Cell Civil & MEP Works (Excl. Options 2 Add. Pumps)	150			01-Mar-22	26-Sep-22	17-Oct-22	25-Apr-23	53	-162	-14
SUM12	[LoE] CC_B Lyric Theatre - EWS Weather Tight Type	269			25-Jun-22	09-Sep-23	05-Dec-22	01-Dec-23	6	-63	0
SUM20	[LoE] CC_C - LT Promenade & Pocket Square Bridge	520			04-Aug-22	31-Jul-24	31-Dec-22	02-Dec-24	-63	-93	-22
SUM13	[LoE] CC_B Lyric Theatre - EWS Non-Weather Tight Type 4.1 & 4.3	286			23-Mar-23	25-Mar-24	14-Jun-23	03-Jul-24	23	-70	0
SUM29	[LoE] CC_G Extended Basement - T&C	243			03-Jan-23	02-Feb-24	24-Jun-23	22-Apr-24	-17	-58	0
SUM33	[LoE] CC_I Underpass 3B & Associated Area - T&C	164			13-Apr-23	25-Oct-23	02-Aug-23	22-Feb-24	30	-94	0
SUM39	[LoE] CC_K - Water Main at Promenade	143			24-May-23	08-Jan-24	27-Oct-23	27-Apr-24	-65	-83	-22
SUM16	[LoE] CC_B Lyric Theatre - T&C (Excluding Non-FSD ELV & Electrical)	131			12-Dec-23	11-Jun-24	13-Apr-24	17-Sep-24	-22	-83	0
SUM18	[LoE] CC_B Lyric Theatre, EB, C'Way 3B - Stat. Insp. & Approval (from Form 314/501 to BD OP)	98			17-May-24	10-Sep-24	19-Sep-24	16-Jan-25	-104	-104	0
SUM38	[LoE] CC_J - M+ Day 2 FS Changeover in 3A SZ_1, Connections to M+, Integrated T&C	51			29-Jul-24	26-Sep-24	30-Nov-24	05-Feb-25	-104	-104	0
SUM34	[LoE] CC_J Carriageway 3A - Stat. Insp. & Approvals (from Form 314A to BA14)	56			02-Sep-24	08-Nov-24	08-Jan-25	18-Mar-25	-104	-104	0

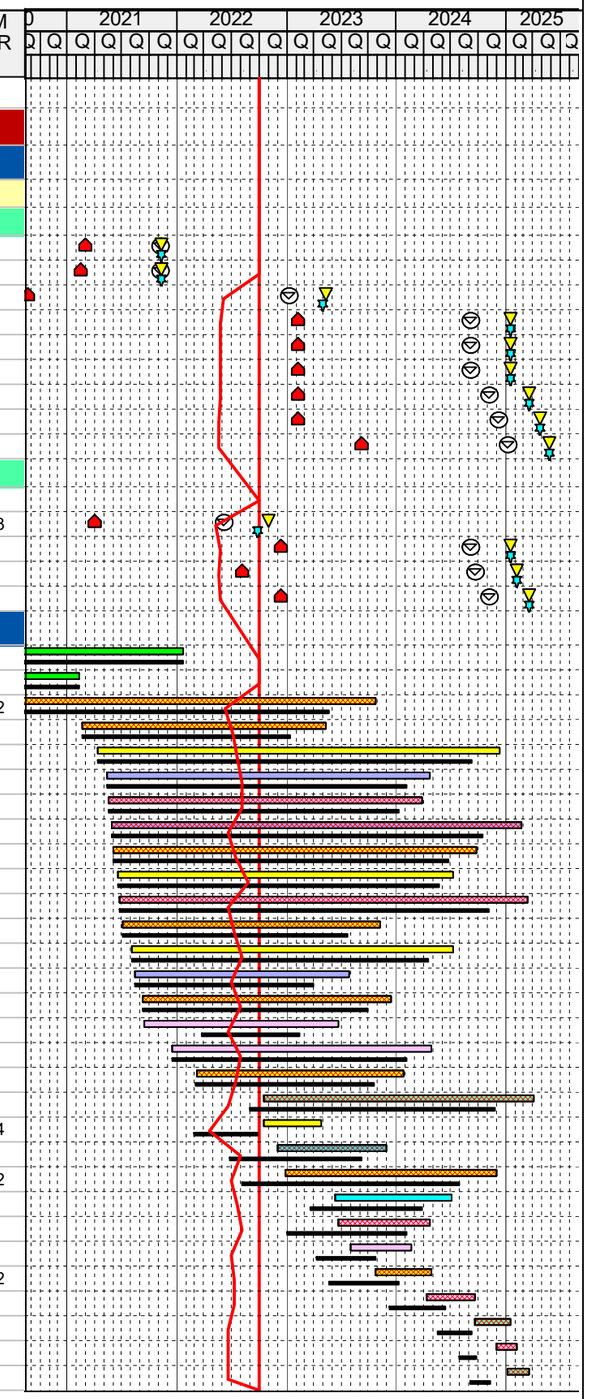

Gammon

Base Line ACT
Rev_0 KD
Base Line MS
Milestone
Current - Other Works
Current - Struct Works
Current - MEP Works
Current - ABWF Works
Current - Facade Works
Critical Works

L2 CMWP_R02_07 - IFA on 27Apr22 - ***LIVE*
(24th UPD; DD = 30Sep2022)**

Date	Revision	Checked	Approved
11-Oct-22	CMWP Rev_2_07 - 24th Update DD 30Sep22	NS	IH
