TASK filter: L2 UPD: Level 1 Prg .

ID	Activity	RD	BL_Rev_00 Finish	BL_Rev_02 Start	BL_Rev_02 Finish	Start	Finish	LoE SUMM TF (approx)	BL_R2 VAR	LM VAR
*L2 CMWP_R02_09 - IFA on 27Apr22 - ***LIVE*** (26th UPD; DD = 30Nov2022)*										
GENERAL & PRELIMINARIES										
Contract Significant Dates										
Commencement & Completion Dates - CMWP_Rev_01										
Section Keydates										
KD05A	Complete Required Pedestrian Access Corridor and Floor Finishes at AURW	0	28-Feb-21		12-Nov-21		12-Nov-21 A		0	0
KD05B	Complete Required Pedestrian Access Corridor & associated top slab at Avenue Level [if instructed]	0	14-Feb-21		12-Nov-21		12-Nov-21 A		0	0
KD05	PC for HO of the Remaining Works for M+ Promenade South	0	24-Aug-20		13-Jan-23		02-Jun-23*	-140	-140	-21
KD08	PC for HO Loc ICT/Risers Rms to APC for ICT Sys Instn Wrks	0	10-Feb-23		10-Sep-24		16-Jan-25*	-128	-128	0
KD10	PC for HO of ASDA, Lyric Theatre Promenade South to Authority	0	10-Feb-23		10-Sep-24		16-Jan-25*	-128	-128	0
KD09	PC for HO of RDE areas for Tenancy Fit-out Wrks	0	10-Feb-23		10-Sep-24		16-Jan-25*	-128	-128	0
KD11	PC for HO of Extended Basement for HO to Authority & HO of Carriageway to Relevant Govt Authority	0	10-Feb-23		12-Nov-24		21-Mar-25*	-129	-129	0
KD07	PRACTICAL COMPLETION for C'Way 3A (M+ Day 2 Works)	0	10-Feb-23		09-Dec-24		22-Apr-25*	-102	-134	0
KD13	PRACTICAL COMPLETION for Lyric Theatre, EB & C'Way 3B (Incl. Provisional PPE License)	0	08-Sep-23		10-Jan-25		23-May-25*	-133	-133	0
Stage Keydates										
KD01	Compl Dsgn Coor/Subm and obtn NNO for L1 Contr Bsmt constn wrks	0	20-Jul-19		20-Jul-19		20-Jul-19 A		0	0
KD06	PC for Fountain Related Plantroom(s) (allow access to Project Contractor)	0	01-Apr-21		07-Jun-22		22-Sep-22 A		-106	0
KD03	OBTAIN OP for Lyric Theatre & Extended Basement	0	12-Dec-22		10-Sep-24		16-Jan-25*	-128	-128	0
KD14	Complete U/G road and the associated plantrooms at Zone 3A&3B Integrated Basement	0	04-Aug-22		26-Sep-24		05-Feb-25*	-132	-132	0
KD02	Obtain BA14 Acknowledge from BD for M+ Day2 A&A Works	0	12-Dec-22		08-Nov-24		18-Mar-25*	-130	-130	0
CMWP - Summary Program - Level 1										
SUM10	[LoE] CC_B Lyric Theatre - Substructure RC Structural Concrete	0		06-May-20	22-Jan-22	06-May-20 A	22-Jan-22 A		0	0
SUM30	[LoE] CC_H - Vibration Isolation Spring System Remaining as of 30Apr2020 (AS=30Sep19)	0		09-May-20	10-Feb-21	09-May-20 A	10-Feb-21 A		0	0
SUM25	[LoE] CC_E - DCS Cofferdam A Works & Obtain BA14	281		23-Jun-20	23-May-23	23-Jun-20 A	12-Dec-23	-86	-151	7
SUM24	[LoE] CC_D - Remaining Works for M+ Promenade South	137		18-Feb-21	13-Jan-23	18-Feb-21 A	02-Jun-23	-102	-102	-15
SUM21	[LoE] CC_C - LT EVA1 & EVA2	562		12-Apr-21	09-Sep-24	12-Apr-21 A	23-Dec-24	117	-82	7
SUM27	[LoE] CC_G Extended Basement - ABWF Works (Incl. Deferred Areas Under Deck)	431		15-May-21	02-Feb-24	15-May-21 A	27-May-24	128	-86	-15
SUM28	[LoE] CC_G Extended Basement - MEP 1st Fix to Final Fix (Incl. Deferred Areas Under Deck)	413		17-May-21	12-Jan-24	17-May-21 A	04-May-24	-45	-86	-15
SUM14	[LoE] CC_B Lyric Theatre - ABWF Work Including Theatres (Exd. Punch List Works)	650		28-May-21	14-Oct-24	28-May-21 A	20-Feb-25	-31	-104	0
SUM35	[LoE] CC_J - M+ Day 2 Works (excl. connections to M+ and SZ_1 FS Changeover)	539		03-Jun-21	25-Jun-24	03-Jun-21 A	04-Oct-24	-63	-84	0
SUM23	[LoE] CC_C - Artist SQ. Bridge (ASB_1/2/3; ASB_3; P31_2; P34_2; AS_1/2; ASB-6/P31 EVA)	463		21-Jun-21	22-May-24	21-Jun-21 A	16-Aug-24	18	-61	-15
SUM15	[LoE] CC_B Lyric Theatre - MEP 1st to Final Fix (Excl. TH SYS done by SVE)	668		22-Jun-21	04-Nov-24	22-Jun-21 A	13-Mar-25	-67	-104	0
SUM11	[LoE] CC_B Lyric Theatre - Superstructure RC Structural Concrete	253		02-Jul-21	22-Jul-23	02-Jul-21 A	09-Nov-23	-34	-80	0
SUM22	[LoE] CC_C - HoR Development (P32-1, P29-1, P31-EVA)	463		03-Aug-21	17-Apr-24	03-Aug-21 A	16-Aug-24	18	-86	-15
SUM31	[LoE] CC_I Carriageway 3B - ABWF Works	234		12-Aug-21	01-Apr-23	12-Aug-21 A	19-Sep-23	299	-138	-30
SUM42	[LoE] CC_E - DCS Outside of Cofferdam A Works (Connect DIA1,600 & Remove Temp O'fall)	182		08-Sep-21	29-Sep-23	08-Sep-21 A	04-Aug-23	13	41	-2
SUM32	[LoE] CC_I Carriageway 3B - MEP Works (1st Fix to Final Fix)	215		22-Mar-22	13-Feb-23	15-Sep-21 A	28-Aug-23	117	-160	-38
SUM40	[LoE] CC_N Lifts & Escalators	434		14-Dec-21	02-Feb-24	14-Dec-21 A	30-May-24	0	-89	-12
SUM41	[LoE] CC_B Lyric Theatre - Structural Steel by CSD	315		04-Mar-22	20-Oct-23	11-Mar-22 A	24-Jan-24	-60	-78	0
SUM26	[LoE] CC_F - Mods to Existing Pump Cell Civil & MEP Works (Excl. Options 2 Add. Pumps)	138		01-Mar-22	26-Sep-22	12-Oct-22 A	03-Jun-23	148	-189	-21
SUM17	[LoE] CC_B Lyric Theatre - TH Systems (by SVE) Incl. T&C, Precom. & Commissioning	686		30-Aug-22	25-Nov-24	28-Nov-22 A	03-Apr-25	-67	-104	0
SUM12	[LoE] CC_B Lyric Theatre - EWS Weather Tight Type	277		25-Jun-22	09-Sep-23	03-Dec-22	09-Dec-23	-1	-70	0
SUM20	[LoE] CC_C - LT Promenade & Pocket Square Bridge	488		04-Aug-22	31-Jul-24	08-Mar-23	23-Dec-24	-81	-111	7
SUM29	[LoE] CC_G Extended Basement - T&C	245		03-Jan-23	02-Feb-24	26-Jul-23	27-May-24	-45	-86	-15
SUM13	[LoE] CC_B Lyric Theatre - EWS Non-Weather Tight Type 4.1 & 4.3	257		23-Mar-23	25-Mar-24	01-Aug-23	10-Jul-24	18	-75	0
SUM33	[LoE] CC_I Underpass 3B & Associated Area - T&C	108		13-Apr-23	25-Oct-23	11-Nov-23	26-Mar-24	2	-122	-28
SUM39	[LoE] CC_K - Water Main at Promenade	143		24-May-23	08-Jan-24	13-Dec-23	22-Jun-24	-86	-123	7
SUM16	[LoE] CC_B Lyric Theatre - T&C (Excluding Non-FSD ELV & Electrical)	145		12-Dec-23	11-Jun-24	13-Apr-24	05-Oct-24	-36	-97	0
SUM18	[LoE] CC_B Lyric Theatre, EB, C'Way 3B - Stat. Insp. & Approval (from Form 314/501 to BD OP)	98		17-May-24	10-Sep-24	19-Sep-24	16-Jan-25	-104	-104	0
SUM38	[LoE] CC_J - M+ Day 2 FS Changeover in 3A SZ_1, Connections to M+, Integrated T&C	51		29-Jul-24	26-Sep-24	30-Nov-24	05-Feb-25	-104	-104	0
SUM34	[LoE] CC_J Carriageway 3A - Stat. Insp. & Approvals (from Form 314A to BA14)	56		02-Sep-24	08-Nov-24	08-Jan-25	18-Mar-25	-104	-104	0

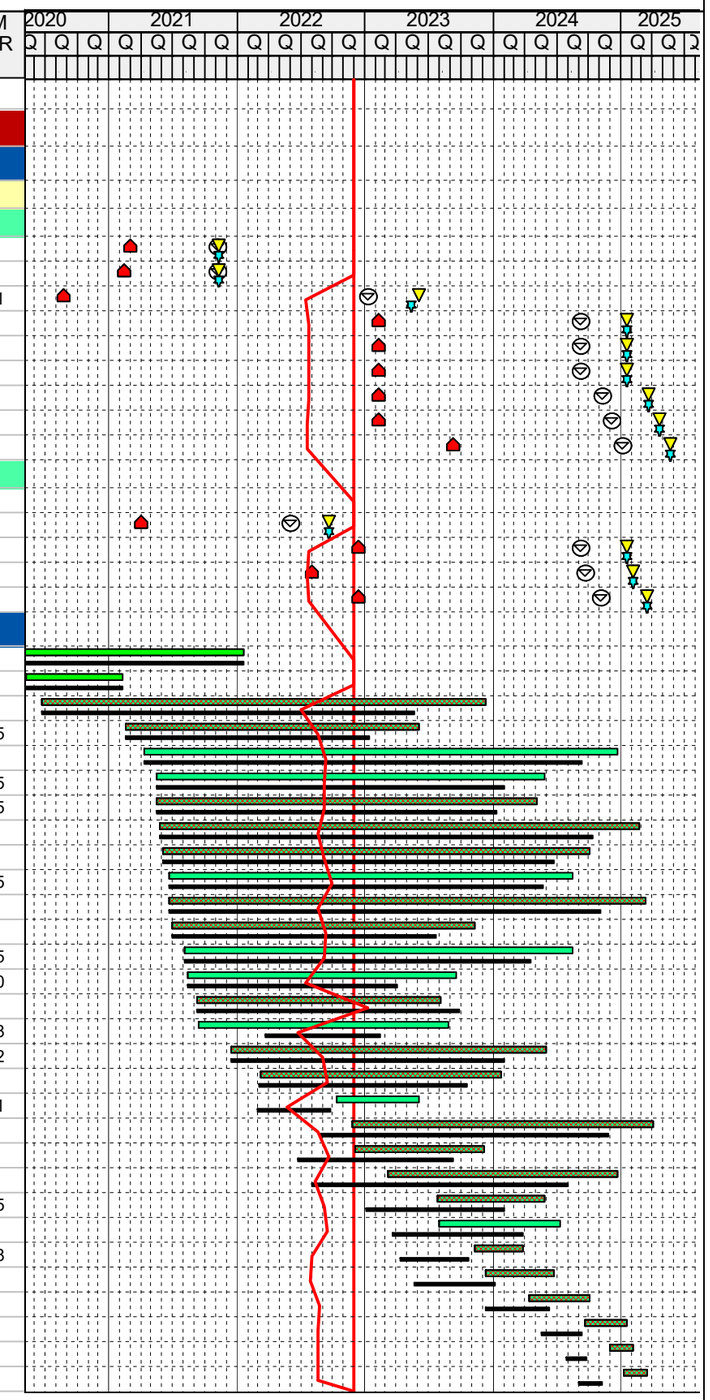

Base Line ACT
Rev_0 KD
Base Line MS
Milestone
Current - Other Works
Current - Struct Works
Current - MEP Works
Current - ABWF Works
Current - Facade Works
Critical Works

L2 CMWP_R02_09 - IFA on 27Apr22 - ***LIVE*
(26th UPD; DD = 30Nov2022)**

Date	Revision	Checked	Approved
08-Dec-22	CMWP Rev_2_09 - 26th Update DD 30Nov22	NS	IH
