TASK filter: L2 UPD: Level 1 Summary (after compres.).

ID	Activity	RD	BL1 Finish	R_1 BL Start	R_1 BL Finish	CURR Start	CURR Finish	LoE SUMM TF (approx, not for use)	R_0 BL VAR	R_1 BL VAR
	L2 CMWP_R01_17 Approved 29Sep20 - 17th Update DD=31 Jan 2022									
	GENERAL & PRELIMINARIES									
	Contract Significant Dates									
	Commencement & Completion Dates - CMWP_Rev_01									
	Section Keydates									
KD05A	Complete Required Pedestrian Access Corridor and Floor Finishes at AURW	0	12-Nov-21		13-May-22		12-Nov-21 A		0	183
KD05B	Complete Required Pedestrian Access Corridor & associated top slab at Avenue Level [if instructed]	0	12-Nov-21		13-May-22		12-Nov-21 A		0	183
KD05	PC for HO of Landscape Area at Avenue & Pedestrian level between P31 & P34 [if instructed]	0	03-Sep-22		13-May-22		05-Oct-22*	-145	-32	-145
KD05	PC for HO of the Remaining Works for M+ Promenade South	0	07-Nov-22		21-Sep-21		13-Jan-23*	-478	-67	-479
KD08	PC for HO Loc ICT/Risers Rms to APC for ICT Sys Instn Wrks	0	10-Sep-24		30-Oct-23		10-Sep-24*	-316	0	-316
KD10	PC for HO of ASDA, Lyric Theatre Promenade South to Authority	0	10-Sep-24		30-Oct-23		10-Sep-24*	-316	0	-316
KD09	PC for HO of RDE areas for Tenancy Fit-out Wrks	0	10-Sep-24		30-Oct-23		10-Sep-24*	-316	0	-316
KD11	PC for HO of Extended Basement for HO to Authority & HO of Carriageway to Relevant Govt Authority	0	12-Nov-24		30-Dec-23		12-Nov-24*	-318	0	-318
KD07	PRACTICAL COMPLETION for C'Way 3A (M+ Day 2 Works)	0	09-Dec-24		27-Jan-24		09-Dec-24*	-317	0	-317
KD13	PRACTICAL COMPLETION for Lyric Theatre, Extended Basement & C'Way 3B (Excl. PPE License)	0	09-Dec-24		27-Jan-24		09-Dec-24*	-317	0	-317
	Stage Keydates									
KD01	Compl Dsgn Coor/Subm and obtn NNO for L1 Contr Bsmt constn wrks	0	20-Jul-19		20-Jul-19		20-Jul-19 A		0	0
KD06	PC for Fountain Related Plantroom(s) (allow access to Project Contractor)	0	07-Jun-22		30-Apr-22		07-Jun-22*	-38	0	-38
KD03	OBTAIN OP for Lyric Theatre & Extended Basement	0	10-Sep-24		30-Oct-23		10-Sep-24*	-316	0	-316
KD14	Complete U/G road and the associated plantrooms at Zone 3A&3B Integrated Basement	0	26-Sep-24		14-Nov-23		26-Sep-24*	-317	0	-317
KD02	Obtain BA14 Acknowledge from BD for M+ Day2 A&A Works	0	08-Nov-24		27-Dec-23		08-Nov-24*	-317	0	-317
	CMWP_Rev_01 - Summary Program - Level 1									
SUM10	[LoE] CC_B Lyric Theatre - Substructure RC Structural Concrete	0	22-Jan-22	02-May-20	24-May-21	06-May-20 A	22-Jan-22 A		1	-182
SUM30	[LoE] CC_H - Vibration Isolation Spring System Remaining as of 30Apr2020 (AS=30Sep19)	0	10-Feb-21	02-May-20	29-Dec-20	09-May-20 A	10-Feb-21 A		0	-35
SUM25	[LoE] CC_E - DCS Cofferdam A Works & Obtain BA14	323	06-Jun-23	22-Jun-20	25-Apr-22	23-Jun-20 A	12-Apr-23	-160	39	-262
SUM24	[LoE] CC_D - Remaining Works for M+ Promenade South	257	07-Nov-22	07-Nov-20	21-Sep-21	18-Feb-21 A	13-Jan-23	-361	-55	-361
SUM21	[LoE] CC_C - LT EVA1 & EVA2	702	09-Sep-24	27-Oct-20	09-Oct-23	12-Apr-21 A	09-Sep-24	365	0	-252
SUM27	[LoE] CC_G Extended Basement - ABWF Works (Incl. Deferred Areas Under Deck)	596	17-Feb-24	24-Nov-20	17-Mar-23	15-May-21 A	17-Feb-24	-47	0	-269
SUM28	[LoE] CC_G Extended Basement - MEP 1st Fix to Final Fix (Incl. Deferred Areas Under Deck)	578	20-Jan-24	04-Feb-21	24-Feb-23	17-May-21 A	20-Jan-24	-220	0	-269
SUM14	[LoE] CC_B Lyric Theatre - ABWF Work Including Theatres (Excl. Punch List Works)	789	02-Oct-24	24-Nov-20	01-Nov-23	28-May-21 A	12-Oct-24	-205	-8	-277
SUM35	[LoE] CC_J - M+ Day 2 Works (excl. connections to M+ and SZ_1 FS Changeover)	699	25-Jun-24	23-Mar-21	03-Aug-23	03-Jun-21 A	25-Jun-24	-233	0	-261
SUM23	[LoE] CC_C - Artist SQ. Bridge (ASB_1/2/3; ASB_3; P31_2; P34_2; AS_1/2; ASB-6/P31 EVA)	631	01-Jun-24	11-Feb-21	27-Oct-23	21-Jun-21 A	01-Jun-24	436	0	-167
SUM11	[LoE] CC_B Lyric Theatre - Superstructure RC Structural Concrete	388	12-Jul-23	08-Mar-21	26-Jul-22	02-Jul-21 A	12-Jul-23	-216	0	-262
SUM22	[LoE] CC_C - HoR Development (P32-1, P29-1, P31-EVA)	606	27-Apr-24	02-Nov-22	27-Oct-23	03-Aug-21 A	27-Apr-24	-140	0	-142
SUM31	[LoE] CC_I Carriageway 3B - ABWF Works	340	17-Mar-23	24-Nov-20	27-Oct-22	12-Aug-21 A	01-Apr-23	183	-13	-125
SUM42	[LoE] CC_E - DCS Outside of Cofferdam A Works (Connect DIA1,600 & Remove Temp O'fall)	461	20-Sep-23	11-Jul-22	08-Oct-22	08-Sep-21 A	24-Oct-23	-223	-22	-283
SUM40	[LoE] CC_N Lifts & Escalators	597	19-Feb-24	23-Aug-21	28-Apr-23	14-Dec-21 A	19-Feb-24	-173	0	-238
SUM26	[LoE] CC_F - Mods to Existing Pump Cell Civil & MEP Works (Excl. Options 2 Add. Pumps)	153	26-Sep-22	30-Nov-20	31-Aug-21	01-Mar-22	26-Sep-22	-12	0	-290
SUM15	[LoE] CC_B Lyric Theatre - MEP 1st to Final Fix (Excl. TH SYS, TH Non-FSD in Walls, etc.)	645	16-May-2	20-Mar-21	30-May-23	04-Mar-22	16-May-24	-198	0	-282
SUM32	[LoE] CC_I Carriageway 3B - MEP Works (1st Fix to Final Fix)	278	28-Jan-23	14-May-21	02-Sep-22	04-Mar-22	13-Feb-23	23	-13	-129
SUM41	[LoE] CC_B Lyric Theatre - Structural Steel by CSD	438	20-Oct-23	05-Jun-21	01-Nov-22	04-Mar-22	20-Oct-23	-216	0	-262
SUM20	[LoE] CC_C - LT Promenade & Pocket Square Bridge	597	23-Jul-24	08-May-21	07-Aug-23	10-Jun-22	21-Aug-24	-223	-22	-283
SUM12	[LoE] CC_B Lyric Theatre - EWS Weather Tight Type	320	09-Sep-23	03-Nov-21	30-Sep-22	06-Jul-22	09-Sep-23	-66	0	-257
SUM29	[LoE] CC_G Extended Basement - T&C	369	17-Feb-24	13-May-22	17-Mar-23	11-Nov-22	17-Feb-24	-220	0	-269
SUM17	[LoE] CC_B Lyric Theatre - Theatre Specialist Systems Incl. T&C, Precom. & Commissioning	551	09-Dec-24	21-Dec-21	27-Jan-24	14-Jan-23	29-Nov-24	-246	8	-246
SUM13	[LoE] CC_B Lyric Theatre - EWS Non-Weather Tight Type 4.1 & 4.3	271	25-Mar-24	27-May-22	29-Apr-23	27-Mar-23	25-Mar-24	-145	0	-247
SUM33	[LoE] CC_I Underpass 3B & Associated Area - T&C	159	12-Oct-23	08-Jul-22	12-Nov-22	30-Mar-23	12-Oct-23	-120	0	-267
SUM39	[LoE] CC_K - Water Main at Promenade	216	30-Dec-23	26-Apr-22	12-Jan-23	13-Apr-23	26-Jan-24	-223	-22	-283
SUM16	[LoE] CC_B Lyric Theatre - T&C (Excluding Non-FSD ELV & Electrical)	126	16-May-2	07-Jan-23	04-Jul-23	05-Dec-23	16-May-24	-254	0	-254
SUM18	[LoE] CC_B Lyric Theatre, EB, C'Way 3B - Stat. Insp. & Approval (from Form 314/501 to BD OP)	98	10-Sep-24	05-Jul-23	30-Oct-23	17-May-24	10-Sep-24	-254	0	-254
SUM38	[LoE] CC_J - M+ Day 2 FS Changeover in 3A SZ_1, Connections to M+, Integrated T&C	51	26-Sep-24	19-Jul-23	14-Nov-23	29-Jul-24	26-Sep-24	-254	0	-254
SUM34	[LoE] CC_J Carriageway 3A - Stat. Insp. & Approvals (from Form 314A to BA14)	56	08-Nov-24	20-Oct-23	27-Dec-23	02-Sep-24	08-Nov-24	-254	0	-254

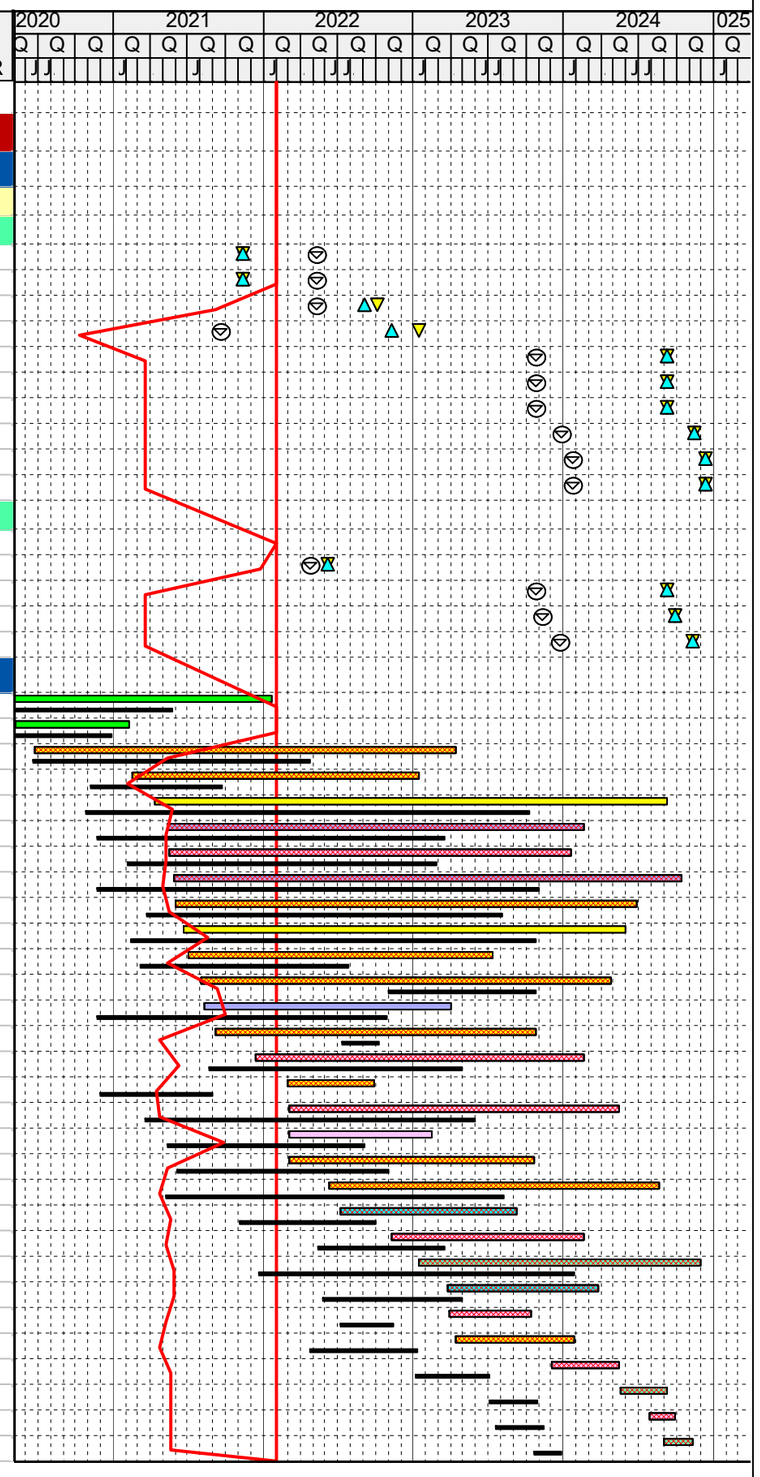

Gammon

Base Line ACT
Base Line MS
Milestone
Current - Other Works
Current - Struct Works
Current - MEP Works
Current - ABWF Works
Current - Facade Works
Critical Works
Actual

L2 CMWP_R01_17 Approved 29Sep20 - 17th Update DD=31 Jan 2022

Date	Revision	Checked	Approved
14-Feb-22	CMWP Rev_1_17 - 17th Update DD 31Jan22	NS	IH
